

Office
District I - (575) 393-6161
1625 N. French Dr., Hobbs, NM 88240
District II - (575) 748-1283
811 S. First St., Artesia, NM 88210
District III - (505) 334-6178
1000 Rio Brazos Rd., Aztec, NM 87410
District IV - (505) 476-3460
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals and Natural Resources

Form C-103
Revised July 18, 2013

OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

WELL API NO. 30-025-08820
5. Indicate Type of Lease STATE [X] FEE []
6. State Oil & Gas Lease No. B015060009
7. Lease Name or Unit Agreement Name State 157 B
8. Well Number 001
9. OGRID Number 181109
10. Pool name or Wildcat [33820] JALMAT; TAN-YATES-7 RVRS

SUNDRY NOTICES AND REPORTS ON WELLS
(DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)
1. Type of Well: Oil Well [X] Gas Well [] Other []
2. Name of Operator Cameron Oil & Gas, Inc.
3. Address of Operator P.O. Box 1089, Eunice, NM 88231
4. Well Location Unit Letter C : 330 feet from the North line and 2310 feet from the West line
Section 7 Township 22-S Range 36-E NMPM County Lea
11. Elevation (Show whether DR, RKB, RT, GR, etc.) 3603' G.R.

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:
PERFORM REMEDIAL WORK [] PLUG AND ABANDON []
TEMPORARILY ABANDON [] CHANGE PLANS []
PULL OR ALTER CASING [] MULTIPLE COMPL []
DOWNHOLE COMMINGLE []
CLOSED-LOOP SYSTEM []
OTHER: []
SUBSEQUENT REPORT OF:
REMEDIAL WORK [] ALTERING CASING []
COMMENCE DRILLING OPNS. [] P AND A [X]
CASING/CEMENT JOB [] PNR []
OTHER []

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

PLUG AND ABANDON PROCEDURE - ORDERED P&A'D BY STATE LAND OFFICE

MIRU Pulling unit. Remove horsehead, install BOP & pull rods - tag bottom w/ tubing (~3650') and ready mud & cement crew. (Note: CIBP @ 3685' w/ 35' cement cap set in 1975.)

Load hole w/ 9.5# MLF and spot cement as follows:

Spot 45 sx 3648 feet to 3312 feet;
Perf 4 squeeze holes @ 1700 feet (top of salt) - attempted squeeze - could not.
Spot 35 sx 1754 feet to 1537 feet - TAGGED;
Perf squeeze holdes @300 feet - attempt sqz, could not.
Spot 70 sx 350 feet to Surface.
Install P&A Marker, remove all equipment and junk, cut anchors, level and clean location
Notify NMOCD for final P&A release inspection.

Spud Date: 10/11/1937 Rig Release Date: 12/15/2021

NOTE: FULL PROCEDURE AND WELLBORE DIAGRAM ATTACHED.

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE [Signature] TITLE Agent/consultant DATE 12/23/2021

Type or print name For State Use Only E-mail address: ben@sosconsulting.us PHONE: 903-488-9850

APPROVED BY: [Signature] TITLE Compliance Officer A DATE 2/2/22
Conditions of Approval (if any): 575-263-6633

Cameron Oil Company

State 157 B #1, 30-025-08820, Well Plugging

Pursuant to NM State Land Office directive, the well was plugged and abandoned as follows:

11/22/2021 – Move in/ rig up plugging equipment to location. Dug out around wellhead to 6' couldn't find surface head. Rigged up equipment. Shut down.

11/29/2021 - POH laying down rods. Installed stripper head. Tagged bottom with tubing at 3648' POH with tubing. RIH with testing tubing. Tested oh. left tubing at 3642'; Shut down.

11/30/2021 - Spot 45 sx of cement at 3642'. POH with tubing. Shut down.

12/01/2021 - Tagged cement at 3312'. RIH with tubing mixed 9.5# MLF to cover between all plugs. POH with tubing. Perforated at 1700'. Attempted to pump into perforations could not pump into perms. Left tubing at 1754'; Shut down.

12/02/2021 - Mixed and pumped 35 sx cement at 1754'. POH with tubing. WOC 4 hours. Tag cement at 1537'. Perforated at 300'. Attempted to pump into perms hole in 7" casing 2' down from wellhead. RIH with tubing to 350". Mixed and pumped 70 sx of cement filling 7" casing to surface. Rig down/ move out.

12/15/2021 - Installed P&A Marker, removed all equipment and junk, cut anchors, leveled and cleaned location Notify NMOCD for final P&A release inspection




P&A SCHEMATIC - SUBSEQUENT
State 157 B Well No.1

API 30-025-08820

330' FNL & 2310' FWL, SEC. 7-T22S-R36E
 LEA COUNTY, NEW MEXICO

Jalmt; TnsI-Yts-7 Rs (33820)

Spud Date: 11/10/1937
 P&A Date: 12/15/2021

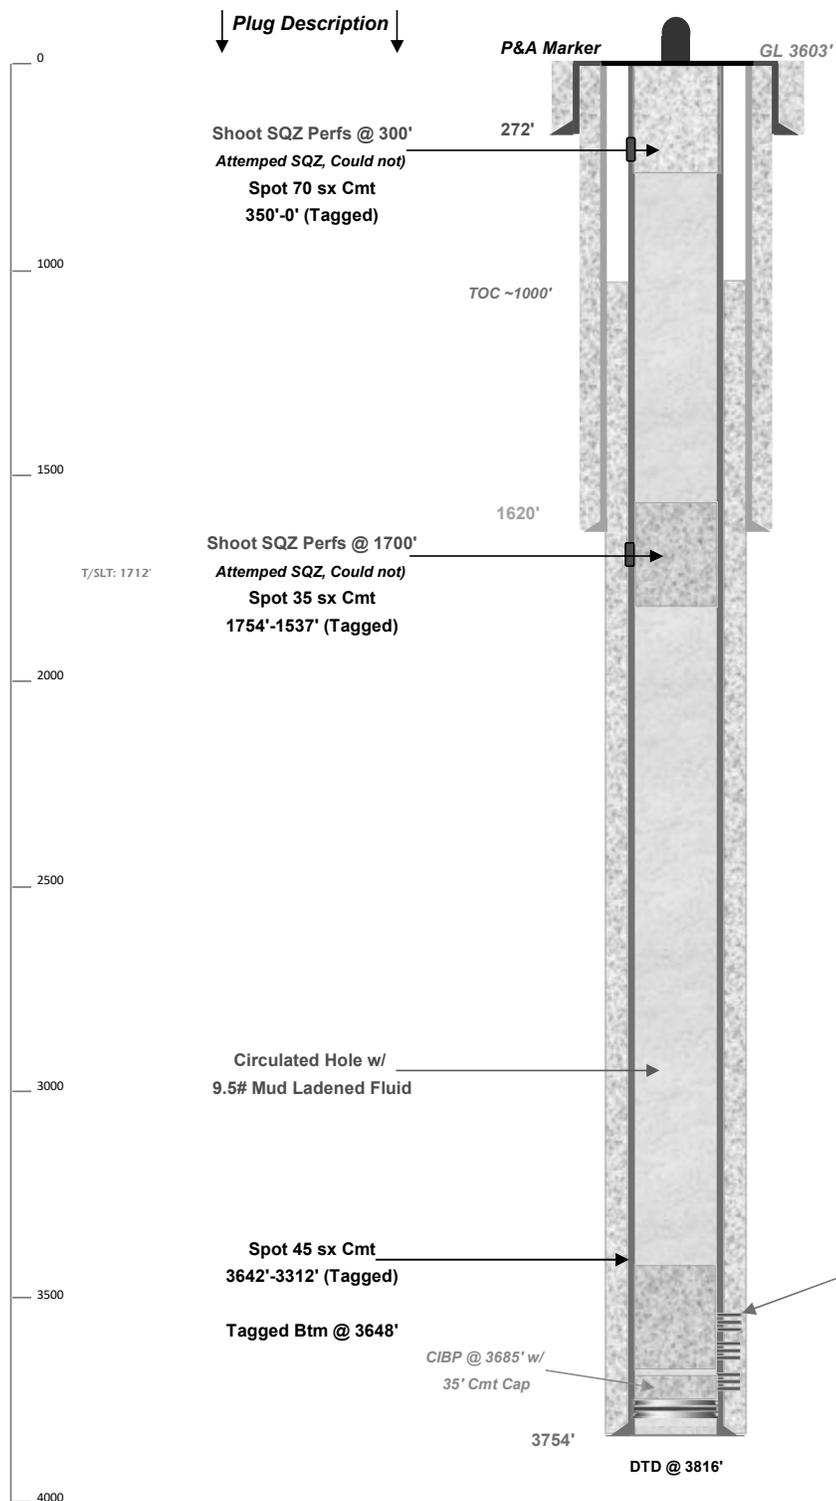

Surface Casing
 13.0" Csg. (16.0" Hole) @ 272'
 200 sx - 40 sx Circulated to Surface

Intermediate Casing
 9.625" Csg. (12.0" Hole) @ 1620'
 400 sx - Circulated to Surface

PLUG AND ABANDON PROCEDURE
ORDERED P&A'D BY STATE LAND OFFICE

MIRU Pulling unit. Remove horsehead, install BOP & pull rods – tag bottom w/ tubing (~3650') and ready mud & cement crew. (Note: CIBP @ 3685' w/ 35' cement cap set in 1975.)

RIH and tagged bottom @ 3648'.
Load hole w/ 9.5# MLF and spotted cement as follows:

- Spot 45 sx 3642 feet to 3312 feet;
- Perf 4 squeeze holes @ 1700 feet (top of salt) – attempted squeeze - could not.
- Spot 35 sx 1754 feet to 1537 feet - TAGGED;
- Spot 70 sx 350 feet to Surface.

Install P&A Marker, remove all equipment and junk, cut anchors, level and clean location.

Notify NMOCD for final P&A release inspection.

Production Casing
 7.0", 17.0# J-55 Csg. (8.75" Hole) @ 3754'
 250 sx - TOC @ 1000' by Calc.

Drawn by: Ben Stone, Rvs'd 12/23/2021



Cameron Oil Company

State 157 B #1, 30-025-08820, Well Plugging

Pursuant to NM State Land Office directive, the well was plugged and abandoned as follows:

11/22/2021 – Move in/ rig up plugging equipment to location. Dug out around wellhead to 6' couldn't find surface head. Rigged up equipment. Shut down.

11/29/2021 - POH laying down rods. Installed stripper head. Tagged bottom with tubing at 3648' POH with tubing. RIH with testing tubing. Tested oh. left tubing at 3642'; Shut down.

11/30/2021 - Spot 45 sx of cement at 3642'. POH with tubing. Shut down.

12/01/2021 - Tagged cement at 3312'. RIH with tubing mixed 9.5# MLF to cover between all plugs. POH with tubing. Perforated at 1700'. Attempted to pump into perforations could not pump into perfs. Left tubing at 1754'; Shut down.

12/02/2021 - Mixed and pumped 35 sx cement at 1754'. POH with tubing. WOC 4 hours. Tag cement at 1537'. Perforated at 300'. Attempted to pump into perfs hole in 7" casing 2' down from wellhead. RIH with tubing to 350". Mixed and pumped 70 sx of cement filling 7" casing to surface. Rig down/ move out.

12/15/2021 - Installed P&A Marker, removed all equipment and junk, cut anchors, leveled and cleaned location Notify NMOCD for final P&A release inspection




P&A SCHEMATIC - SUBSEQUENT State 157 B Well No.1

API 30-025-08820

330' FNL & 2310' FWL, SEC. 7-T22S-R36E
LEA COUNTY, NEW MEXICO

Jalmat; TnsI-Yts-7 Rs (33820)

Spud Date: 11/10/1937
P&A Date: 12/15/2021

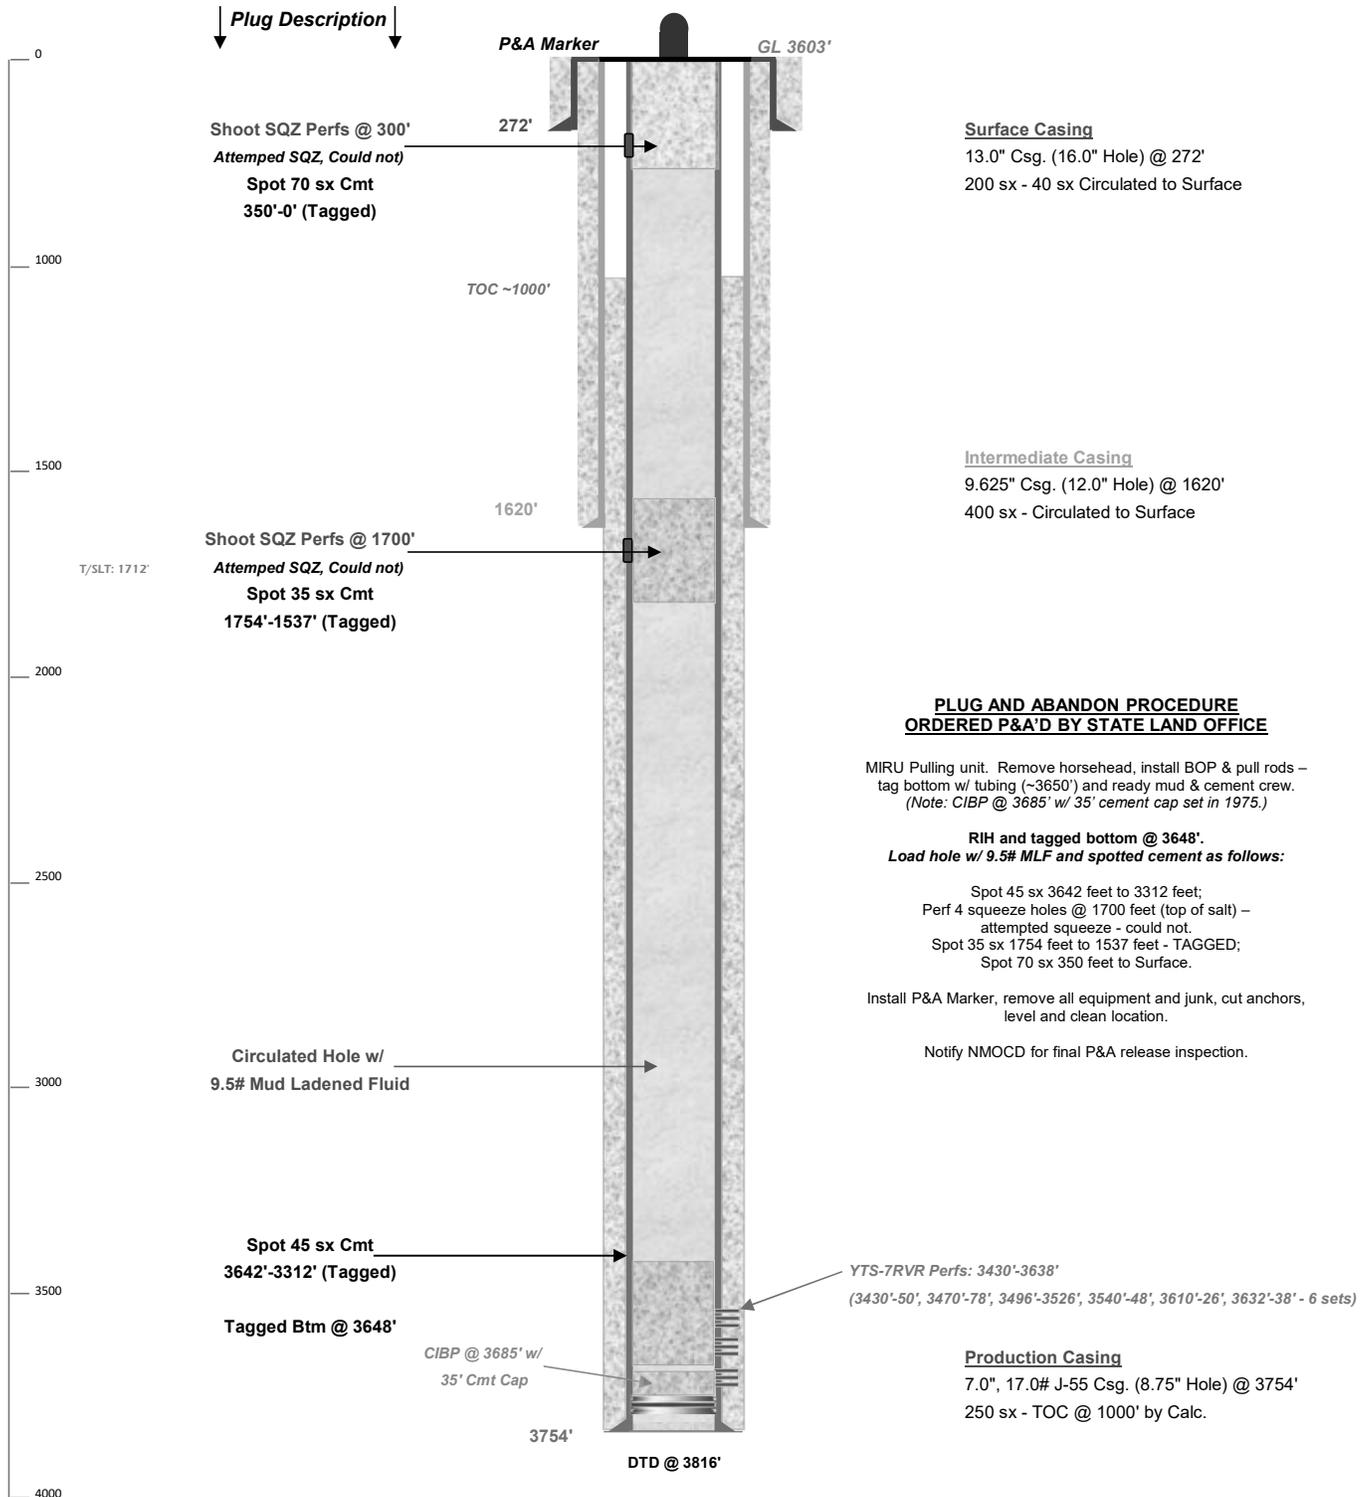

Drawn by: Ben Stone, Rvs'd 12/23/2021



District I
 1625 N. French Dr., Hobbs, NM 88240
 Phone:(575) 393-6161 Fax:(575) 393-0720
District II
 811 S. First St., Artesia, NM 88210
 Phone:(575) 748-1283 Fax:(575) 748-9720
District III
 1000 Rio Brazos Rd., Aztec, NM 87410
 Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
 1220 S. St Francis Dr., Santa Fe, NM 87505
 Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS
 Action 68686

CONDITIONS

Operator: CAMERON OIL & GAS INC P.O. Box 1089 Eunice, NM 88231	OGRID: 181109 Action Number: 68686 Action Type: [C-103] Sub. Plugging (C-103P)
---	--

CONDITIONS

Created By	Condition	Condition Date
kfortner	Need C103Q with pic of Marker	2/2/2022
