

District I

1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

Form C-101
August 1, 2011

Permit 306976

APPLICATION FOR PERMIT TO DRILL, RE-ENTER, DEEPEN, PLUGBACK, OR ADD A ZONE

1. Operator Name and Address CENTENNIAL RESOURCE PRODUCTION, LLC 1001 17th Street, Suite 1800 Denver, CO 80202		2. OGRID Number 372165
		3. API Number 30-025-49745
4. Property Code 322320	5. Property Name AIRSTREAM 24 STATE COM	6. Well No. 302H

7. Surface Location

UL - Lot M	Section 13	Township 22S	Range 34E	Lot Idn M	Feet From 400	N/S Line S	Feet From 1270	E/W Line W	County Lea
---------------	---------------	-----------------	--------------	--------------	------------------	---------------	-------------------	---------------	---------------

8. Proposed Bottom Hole Location

UL - Lot E	Section 25	Township 22S	Range 34E	Lot Idn E	Feet From 2535	N/S Line N	Feet From 1254	E/W Line W	County Lea
---------------	---------------	-----------------	--------------	--------------	-------------------	---------------	-------------------	---------------	---------------

9. Pool Information

OJO CHISO;BONE SPRING, SOUTH	97293
------------------------------	-------

Additional Well Information

11. Work Type New Well	12. Well Type OIL	13. Cable/Rotary	14. Lease Type State	15. Ground Level Elevation 3497
16. Multiple N	17. Proposed Depth 17210	18. Formation 1st Bone Spring Sand	19. Contractor	20. Spud Date 6/1/2022
Depth to Ground water		Distance from nearest fresh water well		Distance to nearest surface water

☒ We will be using a closed-loop system in lieu of lined pits

21. Proposed Casing and Cement Program

Type	Hole Size	Casing Size	Casing Weight/ft	Setting Depth	Sacks of Cement	Estimated TOC
Surf	17.5	13.375	54.4	1825	1553	0
Int1	12.25	9.625	40	5850	1457	0
Prod	8.5	5.5	20	17210	1864	9216
Prod	8.75	5.5	20	9959	771	0

Casing/Cement Program: Additional Comments

--

22. Proposed Blowout Prevention Program

Type	Working Pressure	Test Pressure	Manufacturer
Pipe	10000	5000	CAMERON

23. I hereby certify that the information given above is true and complete to the best of my knowledge and belief. I further certify I have complied with 19.15.14.9 (A) NMAC ☒ and/or 19.15.14.9 (B) NMAC ☒ if applicable.		OIL CONSERVATION DIVISION	
Signature:			
Printed Name:	Electronically filed by Sarah Ferreyros	Approved By:	Paul F Kautz
Title:	Regulatory Lead	Title:	Geologist
Email Address:	Sarah.Ferreyros@cdevinc.com	Approved Date:	2/9/2022
Date:	2/8/2022	Phone:	720-499-1454
		Expiration Date: 2/9/2024	
Conditions of Approval Attached			

District I

1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

Form C-102

August 1, 2011

Permit 306976

WELL LOCATION AND ACREAGE DEDICATION PLAT

1. API Number 30-025-49745	2. Pool Code 97293	3. Pool Name OJO CHISO;BONE SPRING, SOUTH
4. Property Code 322320	5. Property Name AIRSTREAM 24 STATE COM	6. Well No. 302H
7. OGRID No. 372165	8. Operator Name CENTENNIAL RESOURCE PRODUCTION, LLC	9. Elevation 3497

10. Surface Location

UL - Lot M	Section 13	Township 22S	Range 34E	Lot Idn M	Feet From 400	N/S Line S	Feet From 1270	E/W Line W	County Lea
---------------	---------------	-----------------	--------------	--------------	------------------	---------------	-------------------	---------------	---------------

11. Bottom Hole Location If Different From Surface

UL - Lot E	Section 25	Township 22S	Range 34E	Lot Idn E	Feet From 2535	N/S Line N	Feet From 1254	E/W Line W	County Lea
12. Dedicated Acres 480.00	13. Joint or Infill		14. Consolidation Code				15. Order No.		

NO ALLOWABLE WILL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN CONSOLIDATED OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION

	OPERATOR CERTIFICATION <i>I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location(s) or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.</i> E-Signed By: Sarah Ferreyros Title: Regulatory Lead Date: 2/8/2022
	SURVEYOR CERTIFICATION <i>I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.</i> Surveyed By: Paul Buchele Date of Survey: 12/9/2021 Certificate Number: 23782

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

Form APD Comments

Permit 306976

PERMIT COMMENTS

Operator Name and Address: CENTENNIAL RESOURCE PRODUCTION, LLC [372165] 1001 17th Street, Suite 1800 Denver, CO 80202		API Number: 30-025-49745
		Well: AIRSTREAM 24 STATE COM #302H
Created By	Comment	Comment Date
mtwele	Spudder rig will preset surface casing	2/8/2022
mtwele	Drilling 8.75-hole size for the curve and 8.5-hole size for the lateral for the 5.5 production casing string.	2/8/2022

District I

1625 N. French Dr., Hobbs, NM 88240
 Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
 Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
 Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
 Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

Form APD Conditions

Permit 306976

PERMIT CONDITIONS OF APPROVAL

Operator Name and Address: CENTENNIAL RESOURCE PRODUCTION, LLC [372165] 1001 17th Street, Suite 1800 Denver, CO 80202	API Number: 30-025-49745
	Well: AIRSTREAM 24 STATE COM #302H

OCD Reviewer	Condition
pkautz	Notify OCD 24 hours prior to casing & cement
pkautz	Will require a File As Drilled C-102 and a Directional Survey with the C-104
pkautz	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string
pkautz	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system
pkautz	The Operator is to notify NMOCD by sundry (Form C-103) within ten (10) days of the well being spud

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number	² Pool Code 97293	³ Pool Name Ojo Chiso; Bone Spring, South
⁴ Property Code 322320	⁵ Property Name AIRSTREAM 24 STATE COM	⁶ Well Number #302H
⁷ OGRID No. 372165	⁸ Operator Name CENTENNIAL RESOURCE PRODUCTION, LLC	⁹ Elevation 3497.8'


¹⁰ Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
M	13	22S	34E		400	SOUTH	1270	WEST	LEA

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
E	25	22S	34E		2535	NORTH	1254	WEST	LEA
¹² Dedicated Acres 480.00	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.						

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

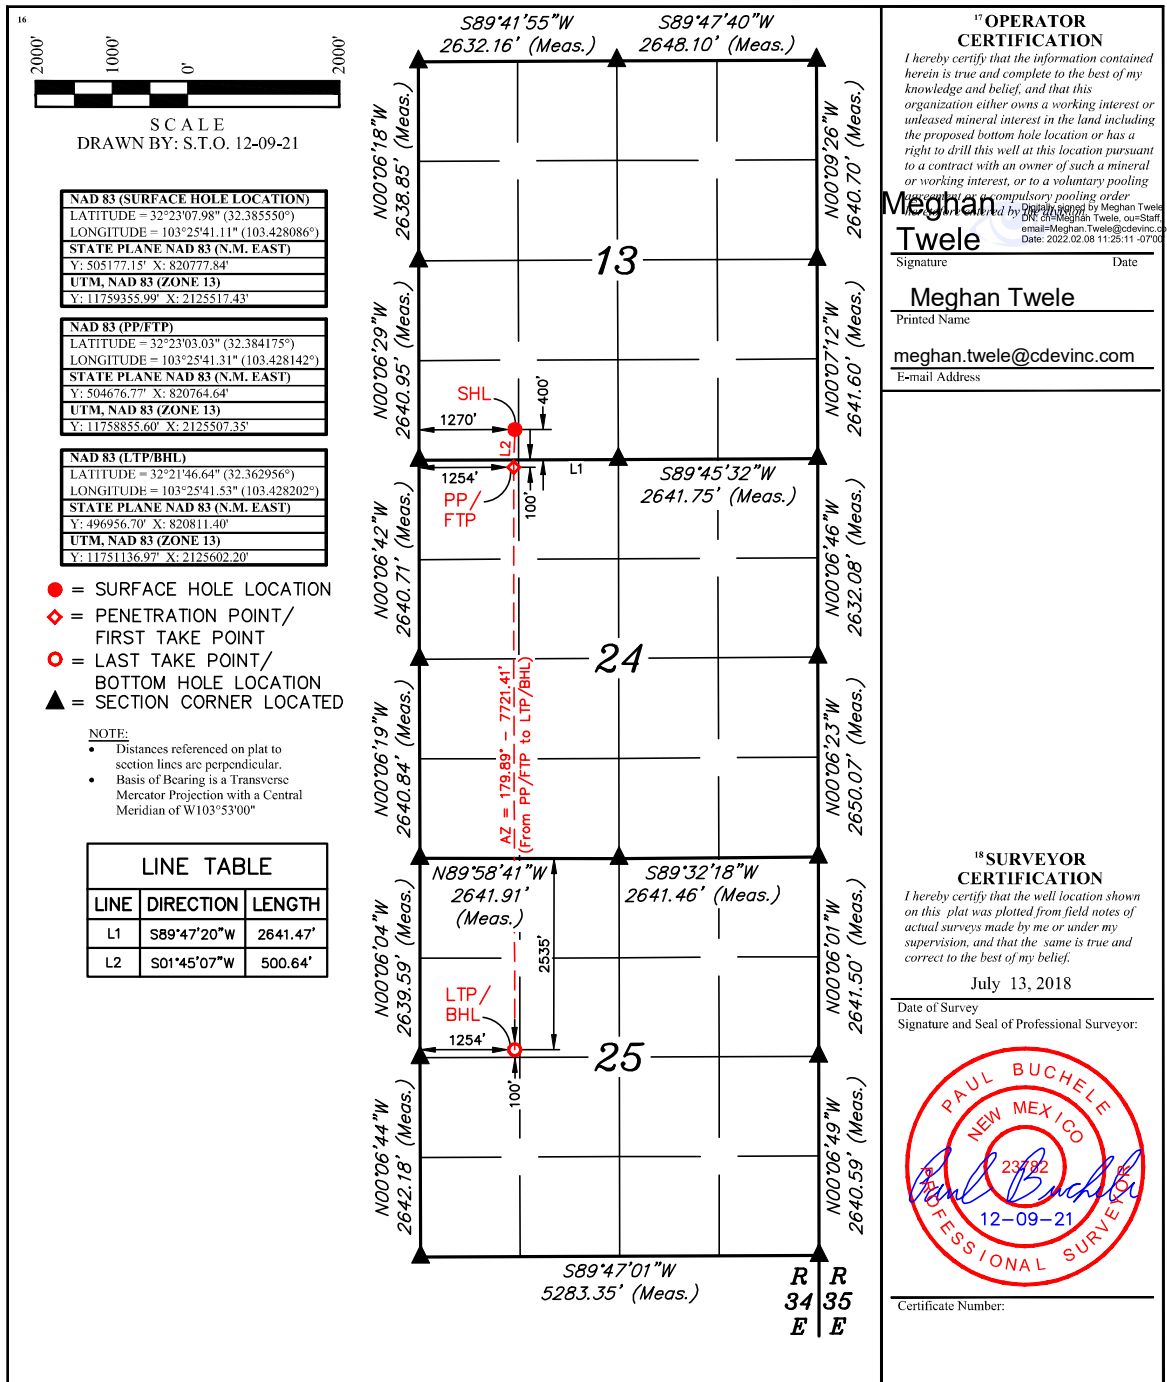

State of New Mexico
Energy, Minerals and Natural Resources Department

Submit Electronically
Via E-permitting

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description

Effective May 25, 2021

I. Operator: Centennial Resource Prod, LLC **OGRID:** 372165 **Date:** 01 / 03 / 2023

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
Airstream 24 State Com 301H		M-13-22S-34E	400 FSL&1240FWL	3400 BBL/D	4080 BBL/D	18,700 BBL/D
Airstream 24 State Com 302H		M-13-22S-34E	400 FSL&1240FWL	3400 BBL/D	4080 BBL/D	18,700 BBL/D

IV. Central Delivery Point Name: Airstream CDP [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Airstream 24 State Com 301H		02/09/2023	02/17/2023	06/10/2023	06/29/2023	06/29/2023
Airstream 24 State Com 302H		02/24/2023	03/04/2023	06/10/2023	06/29/2023	06/29/2023

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:


(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

Page 8

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature: 
Printed Name: Stewart MacCallum
Title: Director of Marketing
E-mail Address: Stewart.MacCallum@cdevinc.com
Date: 1/12/2022
Phone: (720) 499-1458
OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form)
Approved By:
Title:
Approval Date:
Conditions of Approval:

Centennial Resource Production, LLC (372165)

Natural Gas Management Plan Descriptions**VI. Separation Equipment:**

Centennial utilizes a production forecast from our Reservoir Engineering team to appropriately size each permanent, 3-phase separator and heater treater utilized for production operations. Our goal is to maintain 5 minutes of retention time in the test vessel and 20 minutes in the heater treater at peak production rates. The gas produced is routed from the separator to the gas sales line.

VII. Operational Practices:*Drilling*

During Centennial's drilling operations it is uncommon for venting or flaring to occur. If flaring is needed due to safety concerns, gas will be routed to a flare and volumes will be estimated.

Flowback

During completion/recompletion flowback operations, after separation flowback begins and as soon as it is technically feasible, Centennial routes gas through a permanent separator and the controlled facility where the gas is either sold or flared through a high-pressure flare if needed.

Production

Per 19.15.27.8.D, Centennial's facilities are designed to minimize waste. Our produced gas will only be vented or flared in an emergency or malfunction situation, except as allowed for normal operations noted in 19.15.27.8.D(2) & (4). All gas that is flared is metered. All gas that may be vented will be estimated.

Performance Standards

Centennial utilizes a production forecast from our Reservoir Engineering team to appropriately size each permanent, 3-phase separator and heater treater utilized for production operations.

All of Centennial's permanent storage tanks associated with production operations which are routed to a flare or control device are equipped with an automatic gauging system.

All of Centennial's flare stacks, both currently installed and for future installation, are:

- 1) Appropriately sized and designed to ensure proper combustion efficiency.
- 2) Equipped with an automatic ignitor or continuous pilot.
- 3) Anchored and located at least 100 feet from the well and storage tanks.

Centennial's field operations and HSE teams have implemented an AVO inspection schedule that adheres to the requirements of 19.15.27.8.E(5).

All of our operations and facilities are designed to minimize waste. We routinely employ the following methods and practices:

- Closed-loop systems
- Enclosed and properly sized tanks

Centennial Resource Production, LLC (372165)

- Vapor recovery units to maximize recovery of low-pressure gas streams and potential unauthorized emissions
- Low-emitting or electric engines whenever practical
- Combustors and flare stacks in the event of a malfunction or emergency
- Routine facility inspections to identify leaking components, functioning control devices, such as flares and combustors, and repair / replacement of malfunctioning components where applicable

Measurement or estimation

Centennial measures or estimates the volumes of natural gas vented, flared and/or beneficially used for all of our drilling, completing and producing wells. We utilize accepted industry standards and methodology which can be independently verified. Annual GOR testing is completed on our wells and will be submitted as required by the OCD. None of our equipment is designed to allow diversion around metering elements except during inspection, maintenance and repair operations.

VIII. Best Management Practices:

Centennial utilizes the following BMPs to minimize venting during active and planned maintenance activities:


- Use a closed-loop process wherever possible during planned maintenance activities, such as blowdowns, liquid removal, and work over operations.
- Employ low-emitting or electric engines for equipment, such as compressors
- Adhere to a strict preventative maintenance program which includes routine facility inspections, identification of component malfunctions, and repairing or replacing components such as hatches, seals, valves, etc. where applicable
- Utilize vapor recovery units (VRU's) to maximize recovery of volumes of low-pressure gas streams and potential unauthorized emissions
- Route low pressure gas and emissions streams to a combustion device to prevent venting where necessary



Project: Lea County, NM (NAD83 - UTM Zone 13)
Site: Airstream 24 State Com
Well: 302H
Wellbore: OH
Design: Plan 1 01-12-22
Rig: TBD



Azimuths to True North
Magnetic North: 6.38°
Magnetic Field
Strength: 47747.7nT
Dip Angle: 60.03°
Date: 3/12/2022
Model: MVHD

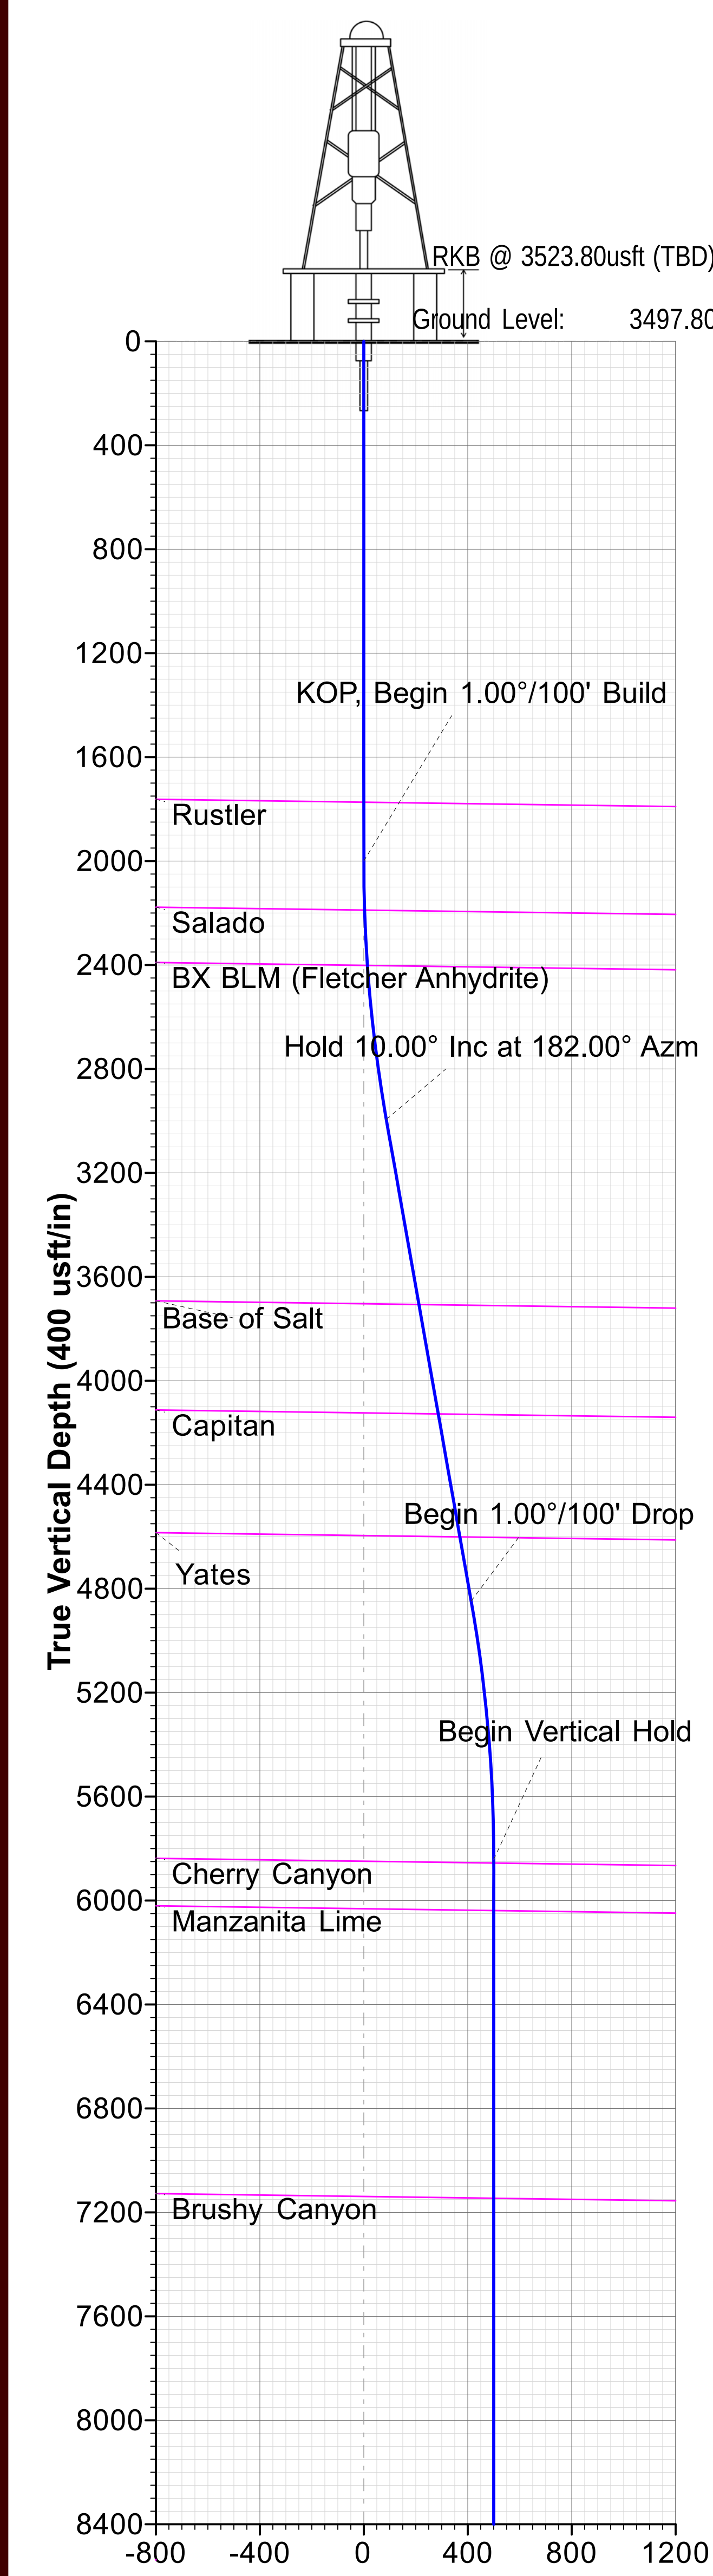

WELL DETAILS									
		Ground Level: 3497.80		Latitude		Longitude			
+N/-S		+E/-W		Northing		Easting		Latitude	
0.00		0.00		11759355.99		2125517.43		32° 23' 7.981220 N	
								103° 25' 41.108694 W	




Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSect	Target	Annotation
1	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		
2	2000.00	0.00	0.00	2000.00	0.00	0.00	0.00	0.00	0.00		KOP, Begin 1.00°/100' Build
3	2999.65	10.00	182.00	2994.59	-86.93	-3.03	1.00	182.00	86.94		Hold 10.00° Inc at 182.00° Azm
4	4881.04	10.00	182.00	4847.41	-413.32	-14.41	0.00	0.00	413.38		Begin 1.00°/100' Drop
5	5880.69	0.00	0.00	5842.00	-500.25	-17.44	1.00	180.00	500.32		Begin Vertical Hold
6	9215.63	0.00	0.00	9176.94	-500.25	-17.44	0.00	0.00	500.32		KOP2, Begin 12.00°/100' Build
7	9958.97	89.20	180.14	9654.36	-971.05	-18.57	12.00	180.14	971.12		LP, Hold 89.20° Inc at 180.14° Azm
8	17209.09	89.20	180.14	9755.59	-8220.45	-36.05	0.00	0.00	8220.53	BHL - Airstream 24 State Com 302H	TD at 17209.09

DESIGN TARGET DETAILS							
Name	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
FTP - Airstream 24 State Com 302H	9647.79	-500.25	-17.44	11758855.60	2125507.35	32° 23' 3.031259 N	103° 25' 41.312008 W
BHL - Airstream 24 State Com 302H	9755.59	-8220.45	-36.05	11751136.97	2125602.20	32° 21' 46.640446 N	103° 25' 41.528388 W

Map System: Universal Transverse Mercator (US Survey Feet)
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone Name: Zone 13N (108 W to 102 W)
Local Origin: Well 302H, True North
Latitude: 32° 23' 7.981220 N
Longitude: 103° 25' 41.108694 W
Grid East: 2125517.43
Grid North: 11759355.99
Scale Factor: 1.000
Geomagnetic Model: MVHD
Sample Date: 12-Mar-22
Magnetic Declination: 6.38°
Dip Angle from Horizontal: 60.03°
Magnetic Field Strength: 47747.70764837nT
To convert a Magnetic Direction to a Grid Direction, Add 5.54°
To convert a Magnetic Direction to a True Direction, Add 6.38° East
To convert a True Direction to a Grid Direction, Subtract 0.84°

FORMATION TOP DETAILS		
TVDPath	MDPath	Formation
1773.80	1773.80	Rustler
2188.84	2188.88	Salado
2402.00	2402.33	BX BLM (Fletcher Anhydrite)
3706.77	3722.81	Base of Salt
4127.80	4150.34	Capitan
4600.97	4630.79	Yates
5855.79	5894.48	Cherry Canyon
6038.79	6077.48	Manzanita Lime
7145.79	7184.48	Brushy Canyon
8553.79	8592.48	Bone Spring Lime
8689.79	8728.48	Avalon Shale
9643.01	9861.08	First Bone Spring Sand

LEGEND	
503H, OH / 65238, Plan 1 08-12-19 V0	
502H, OH, Surveys V0	
501H, OH, Surveys V0	
501H, OH / 69001, Plan 3 01-11-22 V0	
501H, OH / 69001, Surveys (H&P 296) V0	
301H, OH, Plan 1 01-12-22 V0	
503H, OH / 69003, Plan 2 01-10-22 V0	
503H, OH / 69003, Surveys (H&P 296) V0	
502H, OH / 69002, Plan 3 01-11-22 V0	
502H, OH / 69002, Surveys (H&P 296) V0	
Plan 1 01-12-22	

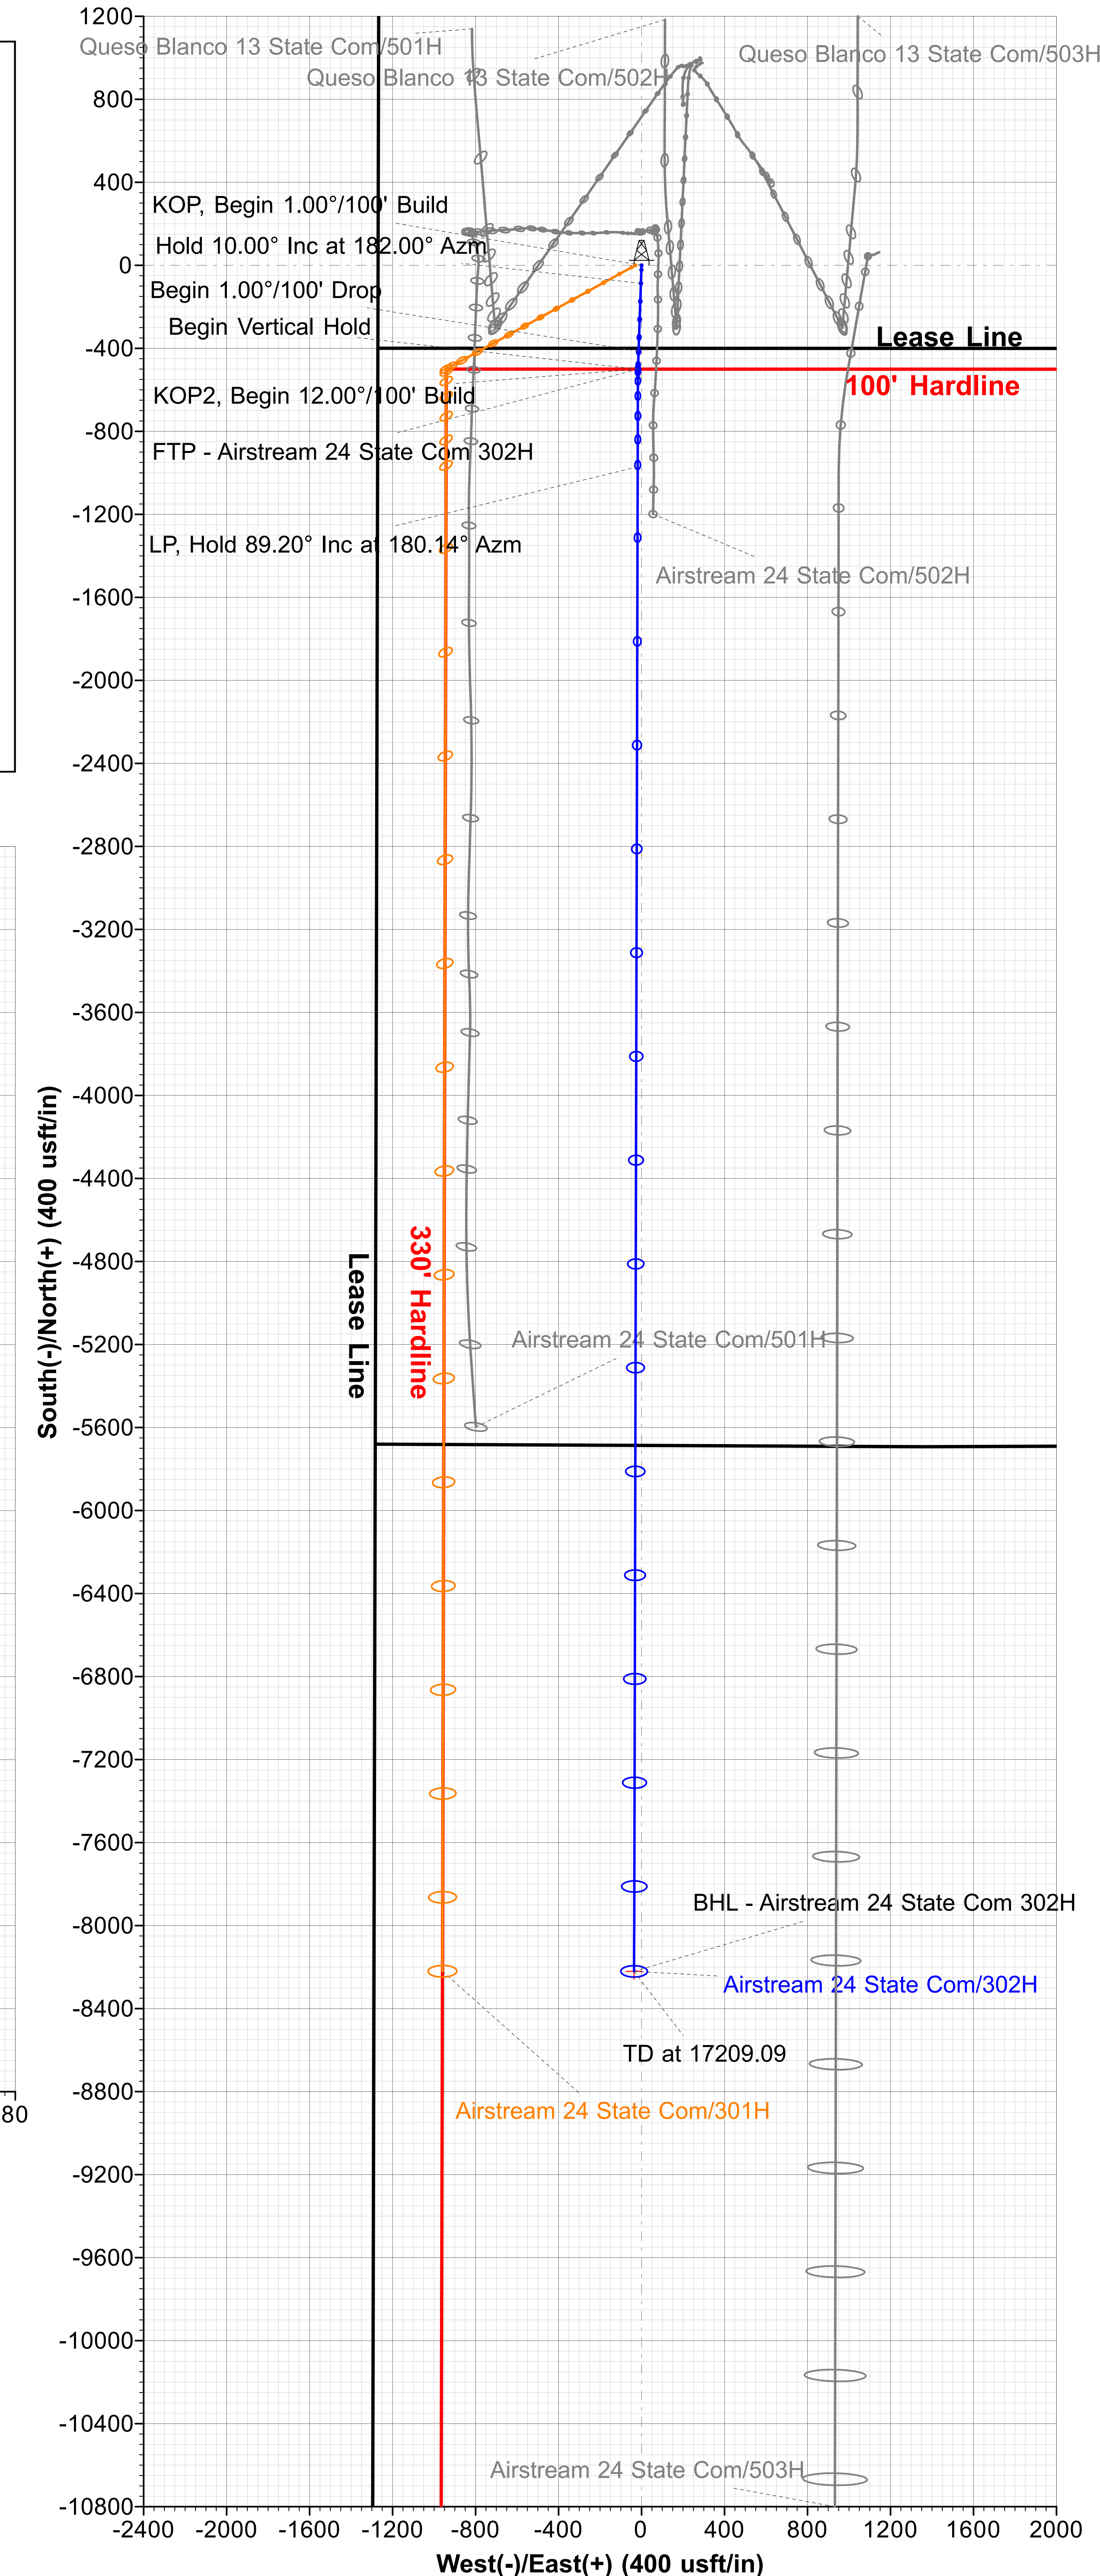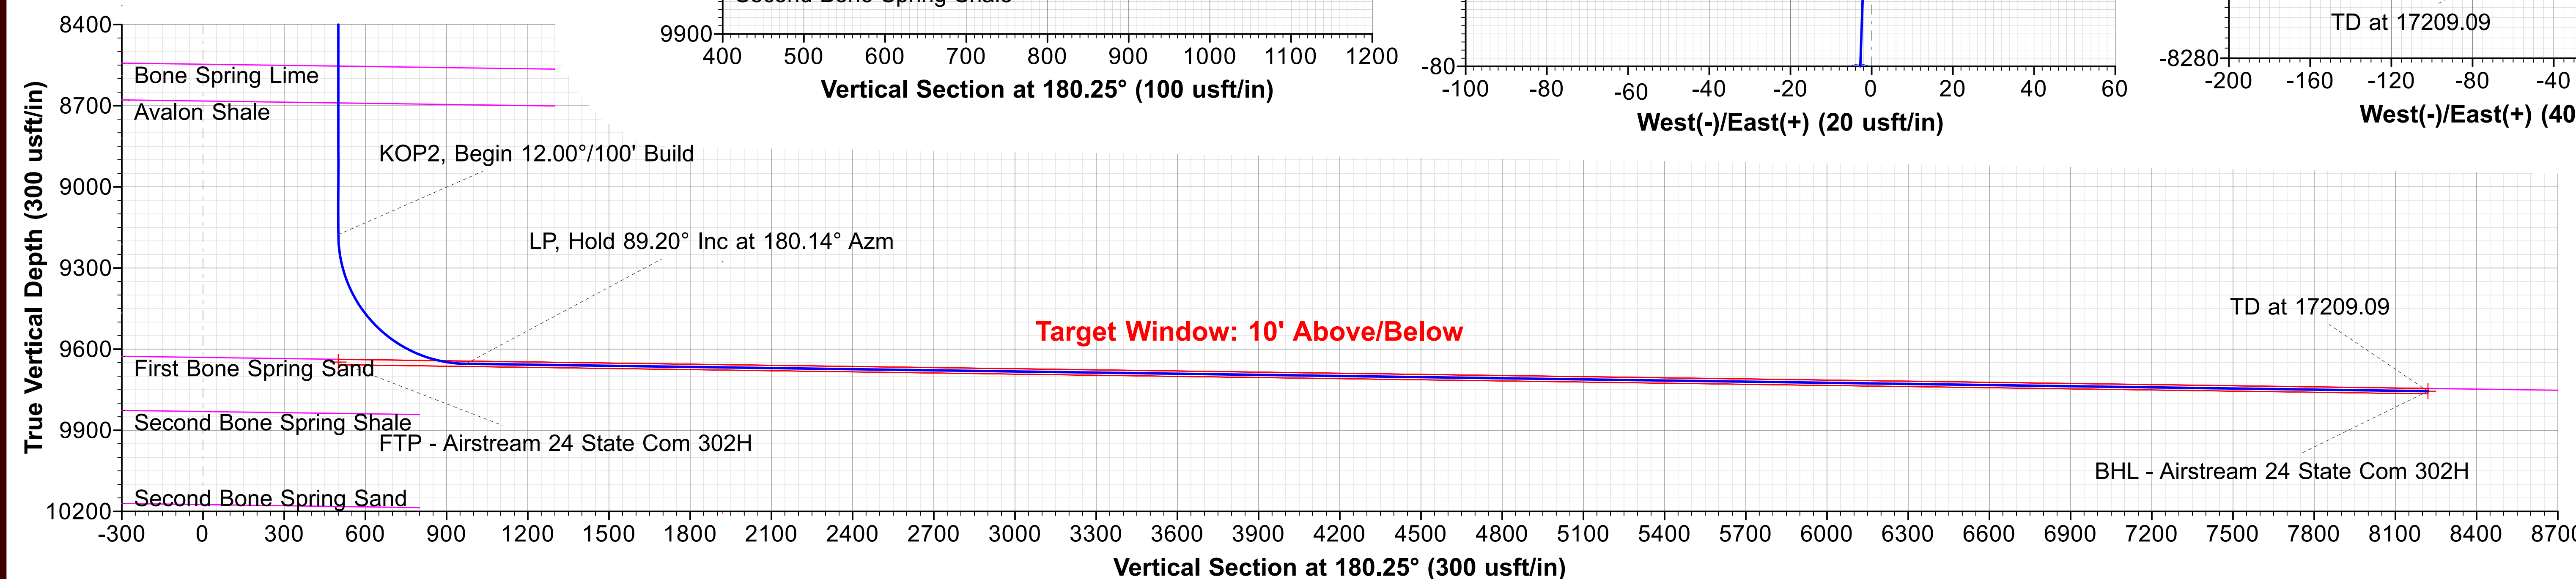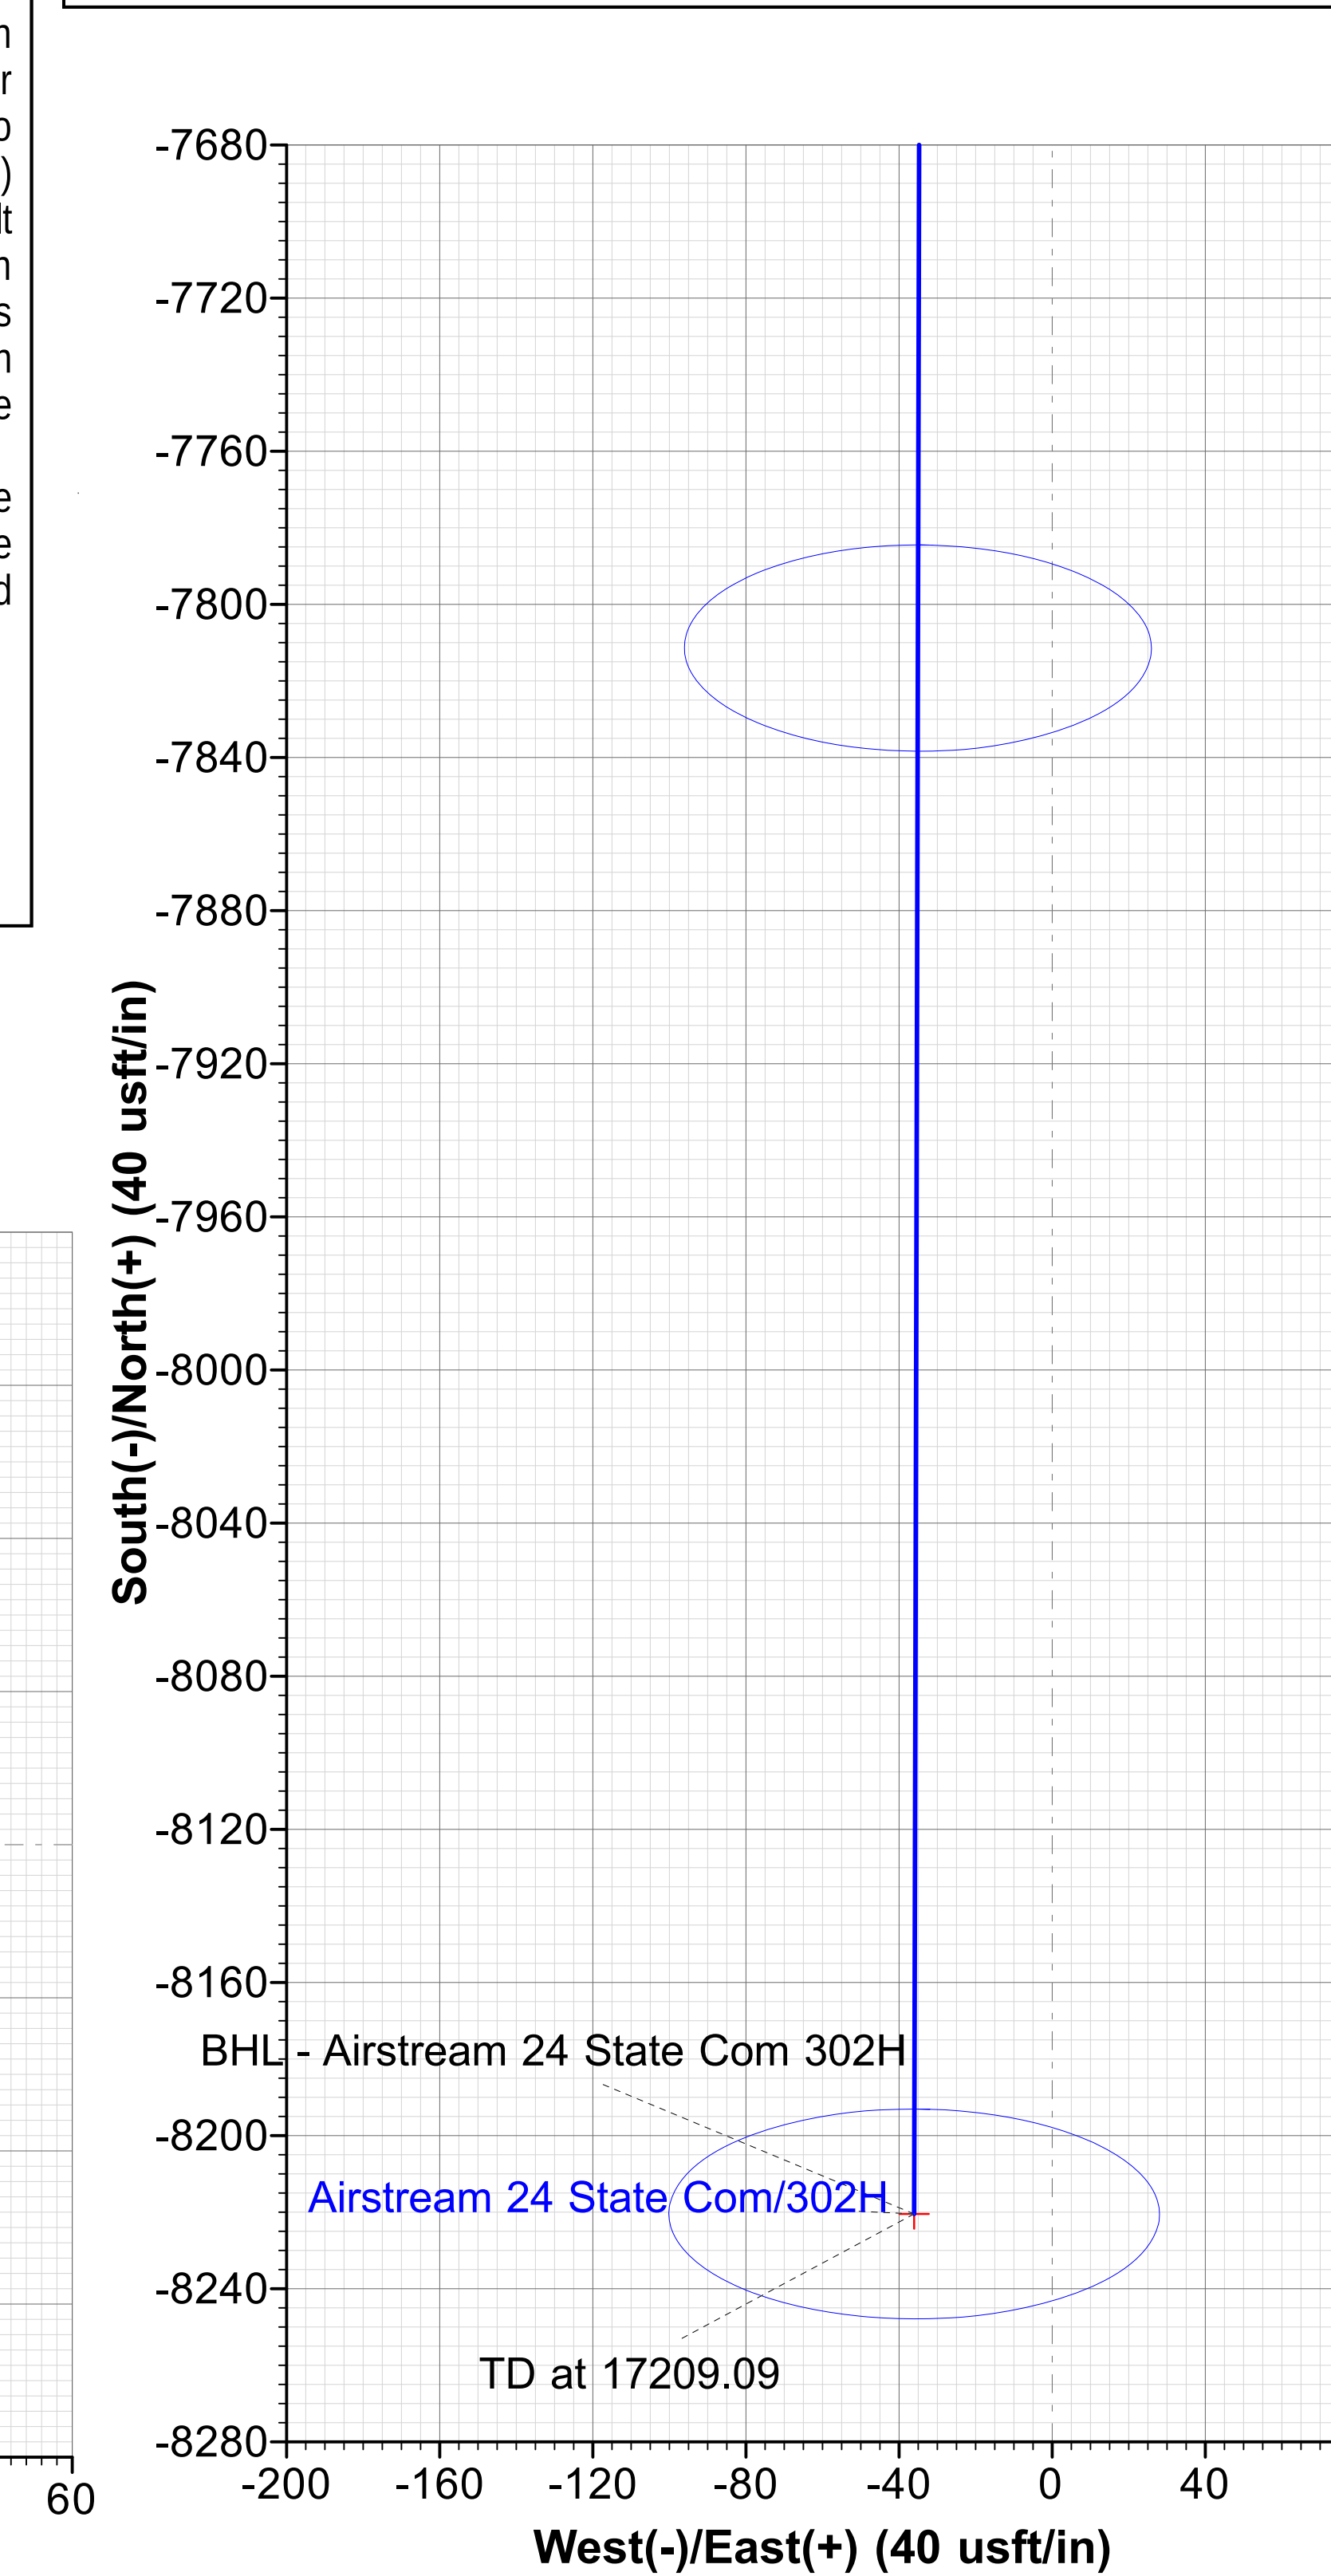



Centennial Resources Development, Inc.

**Lea County, NM (NAD83 - UTM Zone 13)
Airstream 24 State Com
302H**

OH

Plan: Plan 1 01-12-22

Standard Planning Report

12 January, 2022





Planning Report



Database:	USA Compass	Local Co-ordinate Reference:	Well 302H
Company:	Centennial Resources Development, Inc.	TVD Reference:	RKB @ 3523.80usft (TBD)
Project:	Lea County, NM (NAD83 - UTM Zone 13)	MD Reference:	RKB @ 3523.80usft (TBD)
Site:	Airstream 24 State Com	North Reference:	True
Well:	302H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 1 01-12-22		

Project	Lea County, NM (NAD83 - UTM Zone 13)		
Map System:	Universal Transverse Mercator (US Survey Fee	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	Zone 13N (108 W to 102 W)		Using geodetic scale factor

Site	Airstream 24 State Com		
Site Position:		Northing:	11,759,575.83 usft
From:	Map	Easting:	2,126,944.14 usft
Position Uncertainty:	1.00 usft	Slot Radius:	13-3/16 "
		Latitude:	32° 23' 9.948753 N
		Longitude:	103° 25' 24.433178 W

Well	302H		
Well Position	+N/-S	-198.81 usft	Northing: 11,759,355.99 usft
	+E/-W	-1,429.98 usft	Easting: 2,125,517.43 usft
Position Uncertainty	1.00 usft	Wellhead Elevation:	Latitude: 32° 23' 7.981220 N
			Longitude: 103° 25' 41.108694 W
			Ground Level: 3,497.80 usft

Wellbore	OH		
Magnetics	Model Name	Sample Date	Declination (°)
	MVHD	3/12/2022	6.38
			Dip Angle (°) 60.03
			Field Strength (nT) 47,747.70764837

Design	Plan 1 01-12-22		
Audit Notes:			
Version:	Phase:	PLAN	Tie On Depth: 0.00
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)
	0.00	0.00	0.00
			Direction (°) 180.25

Plan Survey Tool Program	Date	1/12/2022		
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks
1	0.00	17,209.09	Plan 1 01-12-22 (OH)	MWD+IFR1+MS
				OWSG MWD + IFR1 + Mult

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,000.00	0.00	0.00	2,000.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,999.65	10.00	182.00	2,994.59	-86.93	-3.03	1.00	1.00	0.00	182.00	
4,881.04	10.00	182.00	4,847.41	-413.32	-14.41	0.00	0.00	0.00	0.00	
5,880.69	0.00	0.00	5,842.00	-500.25	-17.44	1.00	-1.00	0.00	180.00	
9,215.63	0.00	0.00	9,176.94	-500.25	-17.44	0.00	0.00	0.00	0.00	
9,958.97	89.20	180.14	9,654.36	-971.05	-18.57	12.00	12.00	0.00	180.14	
17,209.09	89.20	180.14	9,755.59	-8,220.45	-36.05	0.00	0.00	0.00	0.00	BHL - Airstream 24



Planning Report



Database:	USA Compass	Local Co-ordinate Reference:	Well 302H
Company:	Centennial Resources Development, Inc.	TVD Reference:	RKB @ 3523.80usft (TBD)
Project:	Lea County, NM (NAD83 - UTM Zone 13)	MD Reference:	RKB @ 3523.80usft (TBD)
Site:	Airstream 24 State Com	North Reference:	True
Well:	302H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 1 01-12-22		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
1,773.80	0.00	0.00	1,773.80	0.00	0.00	0.00	0.00	0.00	0.00
Rustler									
2,000.00	0.00	0.00	2,000.00	0.00	0.00	0.00	0.00	0.00	0.00
KOP, Begin 1.00°/100' Build									
2,100.00	1.00	182.00	2,099.99	-0.87	-0.03	0.87	1.00	1.00	0.00
2,188.88	1.89	182.00	2,188.84	-3.11	-0.11	3.11	1.00	1.00	0.00
Salado									
2,200.00	2.00	182.00	2,199.96	-3.49	-0.12	3.49	1.00	1.00	0.00
2,300.00	3.00	182.00	2,299.86	-7.85	-0.27	7.85	1.00	1.00	0.00
2,400.00	4.00	182.00	2,399.68	-13.95	-0.49	13.95	1.00	1.00	0.00
2,402.33	4.02	182.00	2,402.00	-14.11	-0.49	14.11	1.00	1.00	0.00
BX BLM (Fletcher Anhydrite)									
2,500.00	5.00	182.00	2,499.37	-21.79	-0.76	21.79	1.00	1.00	0.00
2,600.00	6.00	182.00	2,598.90	-31.37	-1.09	31.37	1.00	1.00	0.00
2,700.00	7.00	182.00	2,698.26	-42.68	-1.49	42.69	1.00	1.00	0.00
2,800.00	8.00	182.00	2,797.40	-55.73	-1.94	55.73	1.00	1.00	0.00
2,900.00	9.00	182.00	2,896.30	-70.50	-2.46	70.51	1.00	1.00	0.00
2,999.65	10.00	182.00	2,994.59	-86.93	-3.03	86.94	1.00	1.00	0.00
Hold 10.00° Inc at 182.00° Azm									
3,000.00	10.00	182.00	2,994.93	-86.99	-3.03	87.00	0.00	0.00	0.00
3,100.00	10.00	182.00	3,093.41	-104.34	-3.64	104.36	0.00	0.00	0.00
3,200.00	10.00	182.00	3,191.89	-121.69	-4.24	121.71	0.00	0.00	0.00
3,300.00	10.00	182.00	3,290.38	-139.04	-4.85	139.06	0.00	0.00	0.00
3,400.00	10.00	182.00	3,388.86	-156.39	-5.45	156.41	0.00	0.00	0.00
3,500.00	10.00	182.00	3,487.34	-173.73	-6.06	173.76	0.00	0.00	0.00
3,600.00	10.00	182.00	3,585.82	-191.08	-6.66	191.11	0.00	0.00	0.00
3,700.00	10.00	182.00	3,684.30	-208.43	-7.26	208.46	0.00	0.00	0.00
3,722.81	10.00	182.00	3,706.77	-212.39	-7.40	212.42	0.00	0.00	0.00
Base of Salt									
3,800.00	10.00	182.00	3,782.79	-225.78	-7.87	225.81	0.00	0.00	0.00
3,900.00	10.00	182.00	3,881.27	-243.13	-8.47	243.16	0.00	0.00	0.00
4,000.00	10.00	182.00	3,979.75	-260.48	-9.08	260.51	0.00	0.00	0.00
4,100.00	10.00	182.00	4,078.23	-277.82	-9.68	277.86	0.00	0.00	0.00
4,150.34	10.00	182.00	4,127.80	-286.56	-9.99	286.60	0.00	0.00	0.00
Capitan									
4,200.00	10.00	182.00	4,176.71	-295.17	-10.29	295.21	0.00	0.00	0.00
4,300.00	10.00	182.00	4,275.19	-312.52	-10.89	312.57	0.00	0.00	0.00
4,400.00	10.00	182.00	4,373.68	-329.87	-11.50	329.92	0.00	0.00	0.00
4,500.00	10.00	182.00	4,472.16	-347.22	-12.10	347.27	0.00	0.00	0.00
4,600.00	10.00	182.00	4,570.64	-364.57	-12.71	364.62	0.00	0.00	0.00
4,630.79	10.00	182.00	4,600.97	-369.91	-12.89	369.96	0.00	0.00	0.00
Yates									
4,700.00	10.00	182.00	4,669.12	-381.91	-13.31	381.97	0.00	0.00	0.00
4,800.00	10.00	182.00	4,767.60	-399.26	-13.92	399.32	0.00	0.00	0.00
4,881.04	10.00	182.00	4,847.41	-413.32	-14.41	413.38	0.00	0.00	0.00
Begin 1.00°/100' Drop									
4,900.00	9.81	182.00	4,866.09	-416.58	-14.52	416.64	1.00	-1.00	0.00
5,000.00	8.81	182.00	4,964.77	-432.74	-15.08	432.80	1.00	-1.00	0.00
5,100.00	7.81	182.00	5,063.72	-447.18	-15.59	447.24	1.00	-1.00	0.00
5,200.00	6.81	182.00	5,162.91	-459.89	-16.03	459.96	1.00	-1.00	0.00
5,300.00	5.81	182.00	5,262.30	-470.87	-16.41	470.94	1.00	-1.00	0.00
5,400.00	4.81	182.00	5,361.87	-480.11	-16.73	480.18	1.00	-1.00	0.00



Planning Report



Database:	USA Compass	Local Co-ordinate Reference:	Well 302H
Company:	Centennial Resources Development, Inc.	TVD Reference:	RKB @ 3523.80usft (TBD)
Project:	Lea County, NM (NAD83 - UTM Zone 13)	MD Reference:	RKB @ 3523.80usft (TBD)
Site:	Airstream 24 State Com	North Reference:	True
Well:	302H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 1 01-12-22		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
5,500.00	3.81	182.00	5,461.59	-487.62	-17.00	487.69	1.00	-1.00	0.00
5,600.00	2.81	182.00	5,561.42	-493.38	-17.20	493.45	1.00	-1.00	0.00
5,700.00	1.81	182.00	5,661.34	-497.41	-17.34	497.48	1.00	-1.00	0.00
5,800.00	0.81	182.00	5,761.31	-499.69	-17.42	499.76	1.00	-1.00	0.00
5,880.69	0.00	0.00	5,842.00	-500.25	-17.44	500.32	1.00	-1.00	0.00
Begin Vertical Hold									
5,894.48	0.00	0.00	5,855.79	-500.25	-17.44	500.32	0.00	0.00	0.00
Cherry Canyon									
6,077.48	0.00	0.00	6,038.79	-500.25	-17.44	500.32	0.00	0.00	0.00
Manzanita Lime									
7,184.48	0.00	0.00	7,145.79	-500.25	-17.44	500.32	0.00	0.00	0.00
Brushy Canyon									
8,592.48	0.00	0.00	8,553.79	-500.25	-17.44	500.32	0.00	0.00	0.00
Bone Spring Lime									
8,728.48	0.00	0.00	8,689.79	-500.25	-17.44	500.32	0.00	0.00	0.00
Avalon Shale									
9,215.63	0.00	0.00	9,176.94	-500.25	-17.44	500.32	0.00	0.00	0.00
KOP2, Begin 12.00°/100' Build									
9,300.00	10.12	180.14	9,260.87	-507.69	-17.45	507.76	12.00	12.00	0.00
9,400.00	22.12	180.14	9,356.76	-535.41	-17.52	535.48	12.00	12.00	0.00
9,500.00	34.12	180.14	9,444.79	-582.46	-17.63	582.53	12.00	12.00	0.00
9,600.00	46.12	180.14	9,521.12	-646.79	-17.79	646.86	12.00	12.00	0.00
9,700.00	58.12	180.14	9,582.40	-725.58	-17.98	725.65	12.00	12.00	0.00
9,800.00	70.12	180.14	9,625.96	-815.39	-18.20	815.46	12.00	12.00	0.00
9,861.08	77.45	180.14	9,643.01	-874.00	-18.34	874.07	12.00	12.00	0.00
First Bone Spring Sand									
9,900.00	82.12	180.14	9,649.90	-912.29	-18.43	912.36	12.00	12.00	0.00
9,958.97	89.20	180.14	9,654.36	-971.05	-18.57	971.12	12.00	12.00	0.00
LP, Hold 89.20° Inc at 180.14° Azm									
10,000.00	89.20	180.14	9,654.93	-1,012.08	-18.67	1,012.15	0.00	0.00	0.00
10,100.00	89.20	180.14	9,656.33	-1,112.07	-18.91	1,112.14	0.00	0.00	0.00
10,200.00	89.20	180.14	9,657.73	-1,212.06	-19.15	1,212.13	0.00	0.00	0.00
10,300.00	89.20	180.14	9,659.12	-1,312.05	-19.39	1,312.12	0.00	0.00	0.00
10,400.00	89.20	180.14	9,660.52	-1,412.04	-19.63	1,412.11	0.00	0.00	0.00
10,500.00	89.20	180.14	9,661.91	-1,512.03	-19.87	1,512.10	0.00	0.00	0.00
10,600.00	89.20	180.14	9,663.31	-1,612.02	-20.12	1,612.09	0.00	0.00	0.00
10,700.00	89.20	180.14	9,664.71	-1,712.01	-20.36	1,712.08	0.00	0.00	0.00
10,800.00	89.20	180.14	9,666.10	-1,812.00	-20.60	1,812.07	0.00	0.00	0.00
10,900.00	89.20	180.14	9,667.50	-1,911.99	-20.84	1,912.06	0.00	0.00	0.00
11,000.00	89.20	180.14	9,668.90	-2,011.98	-21.08	2,012.05	0.00	0.00	0.00
11,100.00	89.20	180.14	9,670.29	-2,111.97	-21.32	2,112.04	0.00	0.00	0.00
11,200.00	89.20	180.14	9,671.69	-2,211.96	-21.56	2,212.03	0.00	0.00	0.00
11,300.00	89.20	180.14	9,673.08	-2,311.95	-21.80	2,312.02	0.00	0.00	0.00
11,400.00	89.20	180.14	9,674.48	-2,411.94	-22.04	2,412.01	0.00	0.00	0.00
11,500.00	89.20	180.14	9,675.88	-2,511.93	-22.29	2,512.00	0.00	0.00	0.00
11,600.00	89.20	180.14	9,677.27	-2,611.92	-22.53	2,611.99	0.00	0.00	0.00
11,700.00	89.20	180.14	9,678.67	-2,711.91	-22.77	2,711.98	0.00	0.00	0.00
11,800.00	89.20	180.14	9,680.07	-2,811.90	-23.01	2,811.97	0.00	0.00	0.00
11,900.00	89.20	180.14	9,681.46	-2,911.89	-23.25	2,911.96	0.00	0.00	0.00
12,000.00	89.20	180.14	9,682.86	-3,011.88	-23.49	3,011.95	0.00	0.00	0.00
12,100.00	89.20	180.14	9,684.25	-3,111.87	-23.73	3,111.94	0.00	0.00	0.00
12,200.00	89.20	180.14	9,685.65	-3,211.86	-23.97	3,211.93	0.00	0.00	0.00
12,300.00	89.20	180.14	9,687.05	-3,311.85	-24.21	3,311.92	0.00	0.00	0.00



Planning Report



Database:	USA Compass	Local Co-ordinate Reference:	Well 302H
Company:	Centennial Resources Development, Inc.	TVD Reference:	RKB @ 3523.80usft (TBD)
Project:	Lea County, NM (NAD83 - UTM Zone 13)	MD Reference:	RKB @ 3523.80usft (TBD)
Site:	Airstream 24 State Com	North Reference:	True
Well:	302H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 1 01-12-22		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
12,400.00	89.20	180.14	9,688.44	-3,411.84	-24.45	3,411.91	0.00	0.00	0.00	
12,500.00	89.20	180.14	9,689.84	-3,511.83	-24.70	3,511.90	0.00	0.00	0.00	
12,600.00	89.20	180.14	9,691.23	-3,611.82	-24.94	3,611.89	0.00	0.00	0.00	
12,700.00	89.20	180.14	9,692.63	-3,711.81	-25.18	3,711.88	0.00	0.00	0.00	
12,800.00	89.20	180.14	9,694.03	-3,811.80	-25.42	3,811.87	0.00	0.00	0.00	
12,900.00	89.20	180.14	9,695.42	-3,911.79	-25.66	3,911.86	0.00	0.00	0.00	
13,000.00	89.20	180.14	9,696.82	-4,011.78	-25.90	4,011.85	0.00	0.00	0.00	
13,100.00	89.20	180.14	9,698.22	-4,111.77	-26.14	4,111.84	0.00	0.00	0.00	
13,200.00	89.20	180.14	9,699.61	-4,211.76	-26.38	4,211.83	0.00	0.00	0.00	
13,300.00	89.20	180.14	9,701.01	-4,311.75	-26.62	4,311.82	0.00	0.00	0.00	
13,400.00	89.20	180.14	9,702.40	-4,411.74	-26.86	4,411.81	0.00	0.00	0.00	
13,500.00	89.20	180.14	9,703.80	-4,511.73	-27.11	4,511.80	0.00	0.00	0.00	
13,600.00	89.20	180.14	9,705.20	-4,611.72	-27.35	4,611.79	0.00	0.00	0.00	
13,700.00	89.20	180.14	9,706.59	-4,711.71	-27.59	4,711.78	0.00	0.00	0.00	
13,800.00	89.20	180.14	9,707.99	-4,811.70	-27.83	4,811.77	0.00	0.00	0.00	
13,900.00	89.20	180.14	9,709.39	-4,911.69	-28.07	4,911.76	0.00	0.00	0.00	
14,000.00	89.20	180.14	9,710.78	-5,011.68	-28.31	5,011.75	0.00	0.00	0.00	
14,100.00	89.20	180.14	9,712.18	-5,111.67	-28.55	5,111.74	0.00	0.00	0.00	
14,200.00	89.20	180.14	9,713.57	-5,211.66	-28.79	5,211.73	0.00	0.00	0.00	
14,300.00	89.20	180.14	9,714.97	-5,311.65	-29.03	5,311.72	0.00	0.00	0.00	
14,400.00	89.20	180.14	9,716.37	-5,411.64	-29.28	5,411.71	0.00	0.00	0.00	
14,500.00	89.20	180.14	9,717.76	-5,511.63	-29.52	5,511.70	0.00	0.00	0.00	
14,600.00	89.20	180.14	9,719.16	-5,611.62	-29.76	5,611.69	0.00	0.00	0.00	
14,700.00	89.20	180.14	9,720.56	-5,711.61	-30.00	5,711.69	0.00	0.00	0.00	
14,800.00	89.20	180.14	9,721.95	-5,811.60	-30.24	5,811.68	0.00	0.00	0.00	
14,900.00	89.20	180.14	9,723.35	-5,911.59	-30.48	5,911.67	0.00	0.00	0.00	
15,000.00	89.20	180.14	9,724.74	-6,011.58	-30.72	6,011.66	0.00	0.00	0.00	
15,100.00	89.20	180.14	9,726.14	-6,111.57	-30.96	6,111.65	0.00	0.00	0.00	
15,200.00	89.20	180.14	9,727.54	-6,211.56	-31.20	6,211.64	0.00	0.00	0.00	
15,300.00	89.20	180.14	9,728.93	-6,311.55	-31.44	6,311.63	0.00	0.00	0.00	
15,400.00	89.20	180.14	9,730.33	-6,411.54	-31.69	6,411.62	0.00	0.00	0.00	
15,500.00	89.20	180.14	9,731.73	-6,511.53	-31.93	6,511.61	0.00	0.00	0.00	
15,600.00	89.20	180.14	9,733.12	-6,611.52	-32.17	6,611.60	0.00	0.00	0.00	
15,700.00	89.20	180.14	9,734.52	-6,711.51	-32.41	6,711.59	0.00	0.00	0.00	
15,800.00	89.20	180.14	9,735.91	-6,811.50	-32.65	6,811.58	0.00	0.00	0.00	
15,900.00	89.20	180.14	9,737.31	-6,911.49	-32.89	6,911.57	0.00	0.00	0.00	
16,000.00	89.20	180.14	9,738.71	-7,011.48	-33.13	7,011.56	0.00	0.00	0.00	
16,100.00	89.20	180.14	9,740.10	-7,111.47	-33.37	7,111.55	0.00	0.00	0.00	
16,200.00	89.20	180.14	9,741.50	-7,211.46	-33.61	7,211.54	0.00	0.00	0.00	
16,300.00	89.20	180.14	9,742.89	-7,311.45	-33.85	7,311.53	0.00	0.00	0.00	
16,400.00	89.20	180.14	9,744.29	-7,411.44	-34.10	7,411.52	0.00	0.00	0.00	
16,500.00	89.20	180.14	9,745.69	-7,511.43	-34.34	7,511.51	0.00	0.00	0.00	
16,600.00	89.20	180.14	9,747.08	-7,611.42	-34.58	7,611.50	0.00	0.00	0.00	
16,700.00	89.20	180.14	9,748.48	-7,711.41	-34.82	7,711.49	0.00	0.00	0.00	
16,800.00	89.20	180.14	9,749.88	-7,811.40	-35.06	7,811.48	0.00	0.00	0.00	
16,900.00	89.20	180.14	9,751.27	-7,911.39	-35.30	7,911.47	0.00	0.00	0.00	
17,000.00	89.20	180.14	9,752.67	-8,011.38	-35.54	8,011.46	0.00	0.00	0.00	
17,100.00	89.20	180.14	9,754.06	-8,111.37	-35.78	8,111.45	0.00	0.00	0.00	
17,200.00	89.20	180.14	9,755.46	-8,211.36	-36.02	8,211.44	0.00	0.00	0.00	
17,209.09	89.20	180.14	9,755.59	-8,220.45	-36.05	8,220.53	0.00	0.00	0.00	
TD at 17209.09										



Planning Report



Database:	USA Compass	Local Co-ordinate Reference:	Well 302H
Company:	Centennial Resources Development, Inc.	TVD Reference:	RKB @ 3523.80usft (TBD)
Project:	Lea County, NM (NAD83 - UTM Zone 13)	MD Reference:	RKB @ 3523.80usft (TBD)
Site:	Airstream 24 State Com	North Reference:	True
Well:	302H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 1 01-12-22		

Design Targets

Target Name

- hit/miss target	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
- Shape									
FTP - Airstream 24 St	0.00	0.00	9,647.79	-500.25	-17.44	11,758,855.60	2,125,507.35	32° 23' 3.031259 N	3° 25' 41.312008 W
- plan misses target center by 193.69usft at 9600.00usft MD (9521.12 TVD, -646.79 N, -17.79 E)									
- Point									
BHL - Airstream 24 St	0.80	180.14	9,755.59	-8,220.45	-36.05	11,751,136.97	2,125,602.20	32° 21' 46.640446 N	3° 25' 41.528388 W
- plan hits target center									
- Rectangle (sides W0.00 H7,720.97 D20.00)									

Formations

Measured Depth (usft)	Vertical Depth (usft)	Name	Lithology	Dip (°)	Dip Direction (°)
1,773.80	1,773.80	Rustler		0.80	180.25
2,188.88	2,188.84	Salado		0.80	180.25
2,402.33	2,402.00	BX BLM (Fletcher Anhydrite)		0.80	180.25
3,722.81	3,706.77	Base of Salt		0.80	180.25
4,150.34	4,127.80	Capitan		0.80	180.25
4,630.79	4,600.97	Yates		0.80	180.25
5,894.48	5,855.79	Cherry Canyon		0.80	180.25
6,077.48	6,038.79	Manzanita Lime		0.80	180.25
7,184.48	7,145.79	Brushy Canyon		0.80	180.25
8,592.48	8,553.79	Bone Spring Lime		0.80	180.25
8,728.48	8,689.79	Avalon Shale		0.80	180.25
9,861.08	9,643.01	First Bone Spring Sand		0.80	180.25

Plan Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
2,000.00	2,000.00	0.00	0.00	KOP, Begin 1.00°/100' Build
2,999.65	2,994.59	-86.93	-3.03	Hold 10.00° Inc at 182.00° Azm
4,881.04	4,847.41	-413.32	-14.41	Begin 1.00°/100' Drop
5,880.69	5,842.00	-500.25	-17.44	Begin Vertical Hold
9,215.63	9,176.94	-500.25	-17.44	KOP2, Begin 12.00°/100' Build
9,958.97	9,654.36	-971.05	-18.57	LP, Hold 89.20° Inc at 180.14° Azm
17,209.09	9,755.59	-8,220.45	-36.05	TD at 17209.09

Intent ☐ As Drilled ☐

API #		
Operator Name:	Property Name:	Well Number

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

First Take Point (FTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Is this well the defining well for the Horizontal Spacing Unit? ☐Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018
