

Form 3160-3
(June 2015)UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 20185. Lease Serial No.
NMNM111416

6. If Indian, Allottee or Tribe Name

7. If Unit or CA Agreement, Name and No.

8. Lease Name and Well No.

SATURNINUS FED COM 1510
231H1a. Type of work: ☒ DRILL ☐ REENTER
1b. Type of Well: ☐ Oil Well ☒ Gas Well ☐ Other
1c. Type of Completion: ☐ Hydraulic Fracturing ☒ Single Zone ☐ Multiple Zone2. Name of Operator
NOVO OIL AND GAS NORTHERN DELAWARE LLC9. API Well No.
30-015-493093a. Address
1001 West Wilshire Boulevard Suite 206, Oklahoma City, OK 73102
3b. Phone No. (include area code)
(405) 404-041410. Field and Pool, or Exploratory
PURPLE SAGE WOLFACMP GAS4. Location of Well (Report location clearly and in accordance with any State requirements. *)
At surface SESW / 784 FSL / 2170 FWL / LAT 32.2999871 / LONG -103.9741642
At proposed prod. zone NWSW / 2510 FSL / 330 FWL / LAT 32.3193586 / LONG -103.980138611. Sec., T. R. M. or Blk. and Survey or Area
SEC 15/T23S/R29E/NMP14. Distance in miles and direction from nearest town or post office*
7 miles12. County or Parish
EDDY13. State
NM15. Distance from proposed*
location to nearest
property or lease line, ft.
(Also to nearest drig. unit line, if any)
784 feet

16. No of acres in lease

17. Spacing Unit dedicated to this well
480.018. Distance from proposed location*
to nearest well, drilling, completed,
applied for, on this lease, ft.
20 feet19. Proposed Depth
11104 feet / 19293 feet20. BLM/BIA Bond No. in file
FED: NMB00153621. Elevations (Show whether DF, KDB, RT, GL, etc.)
2979 feet22. Approximate date work will start*
12/01/202023. Estimated duration
90 days

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|---|---|
| 1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification.
6. Such other site specific information and/or plans as may be requested by the BLM. |
|---|---|

25. Signature
(Electronic Submission)Name (Printed/Typed)
BRIAN WOOD / Ph: (405) 404-0414Date
10/07/2020Title
PresidentApproved by (Signature)
(Electronic Submission)Name (Printed/Typed)
Cody Layton / Ph: (575) 234-5959Date
02/22/2022Title
Assistant Field Manager Lands & MineralsOffice
Carlsbad Field Office

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)



DISTRICT I
1625 N. French Dr., Hobbs, N.M. 88240
Phone: (575) 393-6161 Fax: (575) 393-0720

DISTRICT II
811 S. First St., Artesia, N.M. 88210
Phone: (575) 748-1283 Fax: (575) 748-9720

DISTRICT III
1000 Rio Brazos Rd., Aztec, N.M. 87410
Phone: (505) 334-6178 Fax: (505) 334-6170

DISTRICT IV
1220 S. St. Francis Dr., Santa Fe, N.M. 87505
Phone: (505) 476-3480 Fax: (505) 476-3482

State of New Mexico
Energy, Minerals & Natural Resources Department

OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, N.M. 87505

Form C-102

Revised August 1, 2011

Submit one copy to appropriate
District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-015- 49309	² Pool Code 98220	³ Pool Name PURPLE SAGE; WOLFCAMP
⁴ Property Code 332441	⁵ Property Name Saturninus Fed Com 1510	
⁶ OGRID No. 372920	⁷ Operator Name Novo Oil & Gas Northern Delaware, LLC	⁸ Well Number 231H
		⁹ Elevation 2979

¹⁰ Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
N	15	23 S	29 E		784	South	2170	West	Eddy

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
L	10	23 S	29 E		2510	South	330	West	Eddy

¹² Dedicated Acres 480	¹³ Joint or Infill	¹⁴ Consolidation Code C	¹⁵ Order No.
---	-------------------------------	--	-------------------------

NO ALLOWABLE WILL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN CONSOLIDATED
OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION

16

BOTTOM HOLE LOCATION
NAD 83 NMSPC ZONE 3001
Y= 480094.72 N
X= 650442.77 E
LAT.= 32.3193586° N
LONG.= 103.9801386° W

LAST TAKE POINT
NAD 83 NMSPC ZONE 3001
2310' FSL, 330' FWL
SEC. 10, T23S, R29E
Y= 479894.73 N
X= 650445.28 E
LAT.= 32.3188088° N
LONG.= 103.9801326° W

FIRST TAKE POINT
NAD 83 NMSPC ZONE 3001
330' FSL, 330' FWL
SEC. 15, T23S, R29E
Y= 472597.57 N
X= 650471.18 E
LAT.= 32.2987501° N
LONG.= 103.9801266° W

SURFACE LOCATION
NAD 83 NMSPC ZONE 3001
Y= 473053.71 N
X= 652311.92 E
LAT.= 32.2999871° N
LONG.= 103.9741642° W

CORNER COORDINATES TABLE
NAD 83 NMSPC ZONE 3001

A - Y= 482904.46 N, X= 650077.43 E
B - Y= 482903.50 N, X= 652733.86 E
C - Y= 480244.34 N, X= 650110.86 E
D - Y= 477584.21 N, X= 650144.28 E
E - Y= 477588.69 N, X= 652779.36 E
F - Y= 474927.64 N, X= 650143.57 E
G - Y= 472267.13 N, X= 650140.84 E
H - Y= 472270.67 N, X= 652791.98 E

CORNER COORDINATES TABLE
NAD 83 NMSPC ZONE 3001

A - LAT.=32.3270854° N, LONG.=103.9812913° W
B - LAT.=32.3270584° N, LONG.=103.9726914° W
C - LAT.=32.3197729° N, LONG.=103.9812114° W
D - LAT.=32.3124604° N, LONG.=103.9811315° W
E - LAT.=32.3124486° N, LONG.=103.9726020° W
F - LAT.=32.3051580° N, LONG.=103.9811621° W
G - LAT.=32.2978447° N, LONG.=103.9811992° W
H - LAT.=32.2978302° N, LONG.=103.9726191° W

17 OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Cory Walk **10-01-2021**
Signature Date
Cory Walk
Printed Name
cory@permitswest.com
E-mail Address

18 SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

08/25/21
Date of Survey
Signature and Seal of Professional Surveyor
MAHALL W. LINDEEN
NEW MEXICO
17078
9-16-21
PROFESSIONAL SURVEYOR
17078
Certificate Number

State of New Mexico
Energy, Minerals and Natural Resources Department

Submit Electronically
Via E-permitting

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description

Effective May 25, 2021

I. Operator: _Novo Oil & Gas Northern Delaware, LLC_____ **OGRID:** ___372920_____ **Date:** __2__/_11__/_22_____

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water
Saturninus Fed Com 1510 131H	30-015-xxxxx	N-15-23S-29E	784' FSL & 2,150 FWL	700	5200	2300
Saturninus Fed Com 1510 132H	30-015-xxxxx	N-15-23S-29E	784' FSL & 2,270 FWL	700	5200	2300
Saturninus Fed Com 1510 211H	30-015-xxxxx	N-15-23S-29E	784' FSL & 2,190 FWL	700	5200	2300
Saturninus Fed Com 1510 212H	30-015-xxxxx	N-15-23S-29E	784' FSL & 1,955 FWL	700	5200	2300
Saturninus Fed Com 1510 222H	30-015-xxxxx	N-15-23S-29E	784' FSL & 2,230 FWL	700	5200	2300
Saturninus Fed Com 1510 231H	30-015-xxxxx	N-15-23S-29E	784' FSL & 2,170 FWL	700	5200	2300
Saturninus Fed Com 1510 232H	30-015-xxxxx	N-15-23S-29E	784' FSL & 2,210 FWL	700	5200	2300
Saturninus Fed Com 1510 235H	30-015-xxxxx	N-15-23S-29E	784' FSL & 2,250 FWL	700	5200	2300
Saturninus Fed Com 1510 241H	30-015-xxxxx	N-15-23S-29E	784' FSL & 2,915 FWL	700	5200	2300
Saturninus Fed Com 1510 242H	30-015-xxxxx	N-15-23S-29E	784' FSL & 2,935 FWL	700	5200	2300
Saturninus Fed Com 1510 245H	30-015-xxxxx	N-15-23S-29E	784' FSL & 1,975 FWL	700	5200	2300

IV. Central Delivery Point Name: _CTB Name: Saturninus CTB_____ [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Saturninus Fed Com 1510 131H	30-015-xxxxx	3/1/2022	3/15/2022	9/20/2022	10/1/2022	10/1/2022
Saturninus Fed Com 1510 132H	30-015-xxxxx	3/4/2022	3/31/2022	9/20/2022	10/1/2022	10/1/2022
Saturninus Fed Com 1510 211H	30-015-xxxxx	3/7/2022	4/17/2022	9/20/2022	10/1/2022	10/1/2022
Saturninus Fed Com 1510 212H	30-015-xxxxx	3/10/2022	5/1/2022	9/20/2022	10/1/2022	10/1/2022
Saturninus Fed Com 1510 222H	30-015-xxxxx	3/13/2022	5/18/2022	9/20/2022	10/1/2022	10/1/2022
Saturninus Fed Com 1510 231H	30-015-xxxxx	3/15/2022	5/31/2022	9/20/2022	10/1/2022	10/1/2022
Saturninus Fed Com 1510 232H	30-015-xxxxx	3/18/2022	6/14/2022	9/20/2022	10/1/2022	10/1/2022
Saturninus Fed Com 1510 235H	30-015-xxxxx	3/21/2022	6/30/2022	9/20/2022	10/1/2022	10/1/2022
Saturninus Fed Com 1510 241H	30-015-xxxxx	3/23/2022	7/15/2022	9/20/2022	10/1/2022	10/1/2022
Saturninus Fed Com 1510 242H	30-015-xxxxx	3/26/2022	7/31/2022	9/20/2022	10/1/2022	10/1/2022
Saturninus Fed Com 1510 245H	30-015-xxxxx	3/30/2022	8/15/2022	9/20/2022	10/1/2022	10/1/2022

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 2 – Enhanced Plan **EFFECTIVE APRIL 1, 2022**

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☐ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☒ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature:	
Printed Name:	Justin Carter
Title:	Landman
E-mail Address:	jcarler@novuog.com
Date:	2/11/2022
Phone:	405 286-3375

OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form)	
Approved By:	
Title:	
Approval Date:	
Conditions of Approval:	

APPENDIX A



Separation Equipment

Novo Oil & Gas Northern Delaware, LLC (Novo) has pulled representative pressurized samples from wells in the same producing formation. Novo has utilized these samples in process simulations to determine the amount of gas anticipated in each stage of the process and utilized this information with a safety factor to size the equipment listed below:

- Separation equipment will be set as follows:
 - Individual 3 Phase separators will be set for each individual well.
 - The separators will be sized based on the anticipated volume of the well and the pressure of the lines utilized for oil, gas, and water takeaway.
 - Individual Heater treaters will be set for each individual well.
 - The heater treaters are sized based on the anticipated combined volume of oil and water predicted to come from the initial 3 phase separator.
 - Oil will be separated from the water and water will be sent to its respective tanks
 - The combined oil and natural gas stream is routed to the Vapor Recovery Tower.
 - The oil and water tanks utilize a closed vent capture system to ensure all breathing, working and flashing losses are routed to the Vapor Recovery Tower (VRT) and Vapor Recovery Unit (VRU)
 - The Vapor Recovery Tower has been sized, based on the anticipated volume of gas from the heater treater and oil and water tanks. A VRU is then utilized to push the recovered gas into the sales pipeline.
 - The VRU will be sized based on the anticipated gas volume and the gas pressure for the line utilized for takeaway.

All equipment has been sized based on the modeled projected need and a safety factor of at least 10%. This is ensuring that the capture of methane gas and VOC will minimize flaring below 50mcf/d per facility.



Operational Practices

19.15.27.8 (A) Venting and Flaring of Natural Gas

Novo Oil & Gas Northern Delaware, LLC (Novo) understands the requirements of NMAC 19.15.27.8 which states that the venting and flaring of natural gas during drilling, completion or production that constitutes waste as defined in 19.15.2 are prohibited.

19.15.27.8 (B) Venting and flaring during drilling operations

1. Novo shall capture or combust natural gas if technically feasible during drilling operations using best industry practices.
2. A flare stack with a 100 percent capacity for expected volumes will be set on location of the CTB at least 100 feet from the nearest surface hole location, well heads, and storage tanks.
3. In the event of an emergency, Novo will vent natural gas in order to avoid substantial impact. Novo shall report the vented or flared gas to the NMOCD.

19.15.27.8 (C) Venting and flaring during completion or recompletion

During completion operations, Novo utilizes the following:

1. Novo facilities are built and ready from day 1 of flowback
2. Individual well test separators will be set to properly separate gas and liquids. Temporary test separator will be utilized initially to process volumes. In addition, separators will be tied into flowback tanks which will be tied into the gas processing equipment for sales down a pipeline. See **Appendix A** for details on Separation Equipment used by Novo.
3. Should the facility not yet be capable of processing gas, or the gas does not meet quality standards, then storage tanks will be set that are tied into gas busters or a temporary flare to manage all natural gas. This flare would meet the following requirements:
 - a) An appropriately sized flare stack with an automatic igniter
 - b) Novo analyzes the natural gas samples twice per week

- c) Novo routes the natural gas into a gathering pipeline as soon as the pipeline specifications are met
- d) Novo provides the NMOCD with pipeline specifications and natural gas data.

19.15.27.8 (D) Venting and flaring during production operations.

Novo will not vent or flare natural gas except under the following circumstances:

1. During an emergency or malfunction
2. To unload or clean-up liquid holdup in a well to atmospheric pressure, provided
 - a) Novo does not vent after the well achieves a stabilized rate and pressure
 - b) Novo will remain present on-site during liquids unloaded by manual purging and takes all reasonable actions to achieve a stabilized rate and pressure at the earliest practical time
 - c) Novo will optimize the system to minimize natural gas venting on any well equipped with a plunger lift or auto control system
 - d) Best management practices will be used during downhole well maintenance.
3. During the first year of production from an exploratory well provided
 - a) Novo receives approval from the NMOCD
 - b) Novo remains in compliance with NM gas capture requirements
 - c) Novo submits an updated C-129 from to the NMOCD.
4. During the following activities unless prohibited
 - a) Gauging or sampling a storage tank or low-pressure production vessel
 - b) Loading out liquids from a storage tank
 - c) Repair and maintenance
 - d) Normal operation of a gas-activated pneumatic controller or pump
 - e) Normal operation of a storage tank but not including venting from a thief hatch
 - f) Normal operation of dehydration units
 - g) Normal operations of compressors, compressor engines, turbines, valves, flanges, and connectors
 - h) During a bradenhead, packer leakage test, or production test lasting less than 24 hours
 - i) When natural gas does not meet the gathering pipeline specifications
 - j) Commissioning of pipelines, equipment, or facilities only for as long as necessary to purge introduced impurities.

In order to comply with these laws, see **Appendix B** for details on Novo Venting and Flaring.

19.15.27.8 (E) Performance standards

1. Novo has utilized process simulations with a safety factor to design all separation and storage equipment. The equipment is routed to a vapor recovery system and utilizes as a flare as back up for periods of startup, shutdown, maintenance or malfunction of the VRU system.
2. Novo will install a flare that designed to handle the full volume of vapors from the facility in case of VRU failure and it is designed with an auto-ignition system.
3. Flare stacks will be appropriately sized and designed to ensure proper combustion efficiency
 - a) Flare stacks installed or replaced will be equipped with an automatic ignitor or continuous pilot
 - b) Previously installed flare stacks will be retrofitted with an automatic ignitor, continuous pilot , or technology that alerts Novo of flare malfunction within 18 months after May 25, 2021.
 - c) Flare stacks replaced after May 25, 2021 will be equipped with an automatic ignitor or continuous pilot if located at a well or facility with an average daily production of 60,000 cubic feet of natural gas or less.
 - d) Flare stacks will be located at least 100 feet from well and storage tanks and securely anchored
4. Novo will conduct an AVO inspection on all components for leaks and defects at least weekly.
5. Novo will make and keep records of AVO inspections available to the NMOCD for at least 5 years.
6. Novo may use a remote or automated monitoring technology to detect leaks and releases in lieu of AVO inspections with prior NMOCD approval.
7. Facilities will be designed to minimize waste.
8. Novo will resolve emergencies as promptly as possible.

19.15.27.8 (F) Measurement or estimation of vented and flared natural gas

1. Novo will have meters on both the low pressure and high pressure sides of the flares and the volumes are recorded in the SCADA system.
2. Novo will install equipment to measure the volume of flared natural gas that has an average daily production of 60,000 cubic feet or greater of natural gas.
3. Novo's measuring equipment will conform to an industry standards.
4. The measurement system is designed such that it cannot be bypassed except for inspections and servicing the meters.
5. Novo will estimate the volume of vented or flared natural gas using a methodology that can be independently verified if metering is not practicable due to low flow rate or pressure.

6. Novo will estimate the volume of vented and flared natural gas based on the results of an annual GOR test for wells that do not require measuring equipment reported on form C-116.
7. Novo will install measuring equipment whenever the NMOCD determines that metering is necessary.

APPENDIX A



Separation Equipment

Novo Oil & Gas Northern Delaware, LLC (Novo) has pulled representative pressurized samples from wells in the same producing formation. Novo has utilized these samples in process simulations to determine the amount of gas anticipated in each stage of the process and utilized this information with a safety factor to size the equipment listed below:

- Separation equipment will be set as follows:
 - Individual 3 Phase separators will be set for each individual well.
 - The separators will be sized based on the anticipated volume of the well and the pressure of the lines utilized for oil, gas, and water takeaway.
 - Individual Heater treaters will be set for each individual well.
 - The heater treaters are sized based on the anticipated combined volume of oil and water predicted to come from the initial 3 phase separator.
 - Oil will be separated from the water and water will be sent to its respective tanks
 - The combined oil and natural gas stream is routed to the Vapor Recovery Tower.
 - The oil and water tanks utilize a closed vent capture system to ensure all breathing, working and flashing losses are routed to the Vapor Recovery Tower (VRT) and Vapor Recovery Unit (VRU)
 - The Vapor Recovery Tower has been sized, based on the anticipated volume of gas from the heater treater and oil and water tanks. A VRU is then utilized to push the recovered gas into the sales pipeline.
 - The VRU will be sized based on the anticipated gas volume and the gas pressure for the line utilized for takeaway.

All equipment has been sized based on the modeled projected need and a safety factor of at least 10%. This is ensuring that the capture of methane gas and VOC will minimize flaring below 50mcf/d per facility.

APPENDIX B



Venting and Flaring

Novo Oil & Gas Northern Delaware, LLC (Novo) has a natural gas system available prior to startup of completion operations. Novo utilizes a VRU system and sells all gas except during periods of startup, shutdown, maintenance, or malfunction for the gas capturing equipment, including the VRT, VRU, storage tanks, and pipelines.

Currently, Novo utilizes the following from list A-I of Section 3 for its operations to minimize flaring:

- a) Novo Oil & Gas utilizes Natural Gas (NG) powered generators to power it's leases where grid power isn't available.
- b) When electrical grid power is unavailable, NG generators will be used for major equipment onsite.
- c) Novo Oil & Gas compression in service will be NG powered.
- d) Should liquids removal – such as dehydration – be required, units will be powered by NG.

Additionally, Novo Oil & Gas will only flare gas during the following times:

- Scheduled maintenance for gas capturing equipment including:
 - VRT
 - VRU
 - Storage tanks
 - Pipelines
- Emergency flaring



Best Management Practices

Novo Oil & Gas Northern Delaware, LLC (Novo) utilizes the following best management practices to minimize venting during active and planned maintenance.

Novo has a closed vent capture system to route emissions from the heater treater, tanks and vapor recovery to the VRU with a flare for backup. The system is designed such that if the VRU is taken out of service for any reason, the vapors will be routed to the flare for combustion.

Novo will isolate and attempt to route all vapors to the VRU or flare prior to opening any lines for maintenance to minimize venting from the equipment. Not limited to:



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Drilling Plan Data Report

02/12/2022

APD ID: 10400062621

Submission Date: 10/07/2020

Highlighted data
reflects the most
recent changes

Operator Name: NOVO OIL AND GAS NORTHERN DELAWARE LLC

Well Name: SATURNINUS FED COM 1510

Well Number: 231H

[Show Final Text](#)

Well Type: CONVENTIONAL GAS WELL

Well Work Type: Drill

Section 1 - Geologic Formations

Formation ID	Formation Name	Elevation	True Vertical Depth	Measured Depth	Lithologies	Mineral Resources	Producing Formation
889221	QUATERNARY	2979	0	0	OTHER : None	USEABLE WATER	N
889222	RUSTLER ANHYDRITE	2674	305	305	ANHYDRITE	NONE	N
889223	SALADO	2415	564	574	SALT	NONE	N
889225	LAMAR	-46	3025	3045	LIMESTONE	NONE	N
889226	BELL CANYON	-46	3025	3055	SANDSTONE	NATURAL GAS, OIL	N
889227	CHERRY CANYON	-1096	4075	4115	SANDSTONE	NATURAL GAS, OIL	N
890547	BRUSHY CANYON	-2571	5550	5600	SANDSTONE	NATURAL GAS, OIL	N
889228	BONE SPRING	-3751	6730	6790	LIMESTONE	NATURAL GAS, OIL	N
889229	AVALON SAND	-4421	7400	7470	SHALE	NATURAL GAS, OIL	N
889230	BONE SPRING 1ST	-4751	7730	7810	SANDSTONE	NATURAL GAS, OIL	N
889231	BONE SPRING 2ND	-5046	8025	8115	OTHER : Carbonate	NATURAL GAS, OIL	N
889232	BONE SPRING 2ND	-5551	8530	8630	SANDSTONE	NATURAL GAS, OIL	N
889233	BONE SPRING 3RD	-5856	8835	8945	OTHER : Carbonate	NATURAL GAS, OIL	N
889220	WOLFCAMP	-7001	9980	10100	OTHER : XY Carbonate	NATURAL GAS, OIL	N
889264	WOLFCAMP	-7151	10130	10260	OTHER : A	NATURAL GAS, OIL	N
889265	WOLFCAMP	-7421	10400	10540	OTHER : B	NATURAL GAS, OIL	Y
7648781	WOLFCAMP	-8071	11050	11200	OTHER : B Flow Unit	NATURAL GAS, OIL	N
7648782	WOLFCAMP	-8181	11160	11160	OTHER : C	NATURAL GAS, OIL	N

Operator Name: NOVO OIL AND GAS NORTHERN DELAWARE LLC**Well Name:** SATURNINUS FED COM 1510**Well Number:** 231H**Section 2 - Blowout Prevention****Pressure Rating (PSI):** 5M**Rating Depth:** 12000

Equipment: A 13.625" 5M Blowout Preventer system will be installed on a multi-bowl (speed head) wellhead with a 13.625" flanged casing spool. Top flange of casing spool will be set in a cellar below ground level. BOP system will consist of a single pipe ram on the bottom, mud cross, double pipe ram with blind rams on bottom and pipe rams on top, and annular preventer. Blowout preventer will be installed on top of the 13.375" surface casing and will remain installed to TD of the well. Wellhead, blowout preventer, and choke manifold diagram are included.

Requesting Variance? YES

Variance request: Variance is requested to use a co-flex hose between the BOP system and choke manifold. A typical co-flex pressure test certificate is attached. An equipment specific co-flex pressure test certificate will be on site when testing the BOP.

Testing Procedure: All casing strings will be tested in accordance with Onshore Order 2 III.B.1.h. The BOP system will be isolated with a test plug and tested by an independent tester to 250 psi low and 5,000 psi high for 10 minutes. The Surface Casing will be pressure tested to 250 psi low and 1500 psi high. Intermediate Casing will be pressure tested to 250 psi low and (.22 psi x Shoe TVD, which is equivalent to 2305.16 psi) high for 30 minutes

Choke Diagram Attachment:

Choke_5M_20211004085442.pdf

BOP Diagram Attachment:

BOP_5M_20211004085451.pdf

Section 3 - Casing

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE	17.5	13.375	NEW	API	N	0	385	0	385	2979	2594	385	J-55	54.5	BUTT	1.125	1.125	DRY	1.6	DRY	1.6
2	OTHER	12.25	10.75	NEW	API	N	0	3325	0	3325	2968	-346	3325	J-55	40.5	BUTT	1.125	1.125	DRY	1.6	DRY	1.6
3	INTERMEDIATE	9.875	8.625	NEW	NON API	N	0	10628	0	10478	2968	-7499	10628	OTHER	32	OTHER - Talon HTQ	1.125	1.125	DRY	1.6	DRY	1.6
4	PRODUCTION	7.875	5.5	NEW	NON API	N	0	19293	0	11104	2968	-8125	19293	OTHER	20	OTHER - DW/C-1S Plus	1.125	1.125	DRY	1.6	DRY	1.6

Operator Name: NOVO OIL AND GAS NORTHERN DELAWARE LLC**Well Name:** SATURNINUS FED COM 1510**Well Number:** 231H**Casing Attachments**

Casing ID: 1 **String Type:** SURFACE**Inspection Document:****Spec Document:****Tapered String Spec:****Casing Design Assumptions and Worksheet(s):**Casing_Design_Assumptions_20200930131839.pdf

Casing ID: 2 **String Type:** OTHER - Salt**Inspection Document:****Spec Document:****Tapered String Spec:****Casing Design Assumptions and Worksheet(s):**

10.750in_SC_BTC_20200930131859.pdf

Casing_Design_Assumptions_20200930131903.pdf

Casing ID: 3 **String Type:** INTERMEDIATE**Inspection Document:****Spec Document:**

8.625_P110HP_TALON_HTQ_Casing_Spec_20211004085612.pdf

Tapered String Spec:**Casing Design Assumptions and Worksheet(s):**Casing_Design_Assumptions_20200930131931.pdf

Operator Name: NOVO OIL AND GAS NORTHERN DELAWARE LLC**Well Name:** SATURNINUS FED COM 1510**Well Number:** 231H**Casing Attachments****Casing ID:** 4 **String Type:** PRODUCTION**Inspection Document:****Spec Document:**

5.5in_P_110_EC_20200930131955.pdf

Tapered String Spec:**Casing Design Assumptions and Worksheet(s):**

Casing_Design_Assumptions_20200930132005.pdf

Section 4 - Cement

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
SURFACE	Lead		0	0	0	0	0	0	0	None	None
SURFACE	Tail		0	385	330	1.62	13.8	535	100	Class C	Gel + accelerator + LCM
PRODUCTION	Lead		0	0	0	0	0	0	0	None	None
PRODUCTION	Tail		8478	19293	1354	1.59	13.2	2153	20	Class H	Fluid loss + retarder + LCM
OTHER	Lead		0	2575	440	2.42	12	1128	125	Class C	2% Gypsum, 2% SMS
OTHER	Tail		2575	3325	110	1.82	13.2	200	70	Class C	2% Gypsum, 2% SMS
INTERMEDIATE	Lead		0	9478	708	3.58	10	2535	100	Class C or H	Fluid loss + retarder + LCM, possibly beads for compressive strength
INTERMEDIATE	Tail		9478	10628	130	1.39	13.8	181	50	Class C or H	Fluid loss + retarder + LCM

Operator Name: NOVO OIL AND GAS NORTHERN DELAWARE LLC**Well Name:** SATURNINUS FED COM 1510**Well Number:** 231H**Section 5 - Circulating Medium****Mud System Type:** Closed**Will an air or gas system be Used?** NO**Description of the equipment for the circulating system in accordance with Onshore Order #2:****Diagram of the equipment for the circulating system in accordance with Onshore Order #2:****Describe what will be on location to control well or mitigate other conditions:** All necessary mud products (barite, bentonite, LCM) to control weight and fluid loss will be on site at all times. Mud program may change due to hole conditions.**Describe the mud monitoring system utilized:** An electronic PVT mud system will monitor flow rate, pump pressure, stroke rate, and volume.**Circulating Medium Table**

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
0	385	OTHER : Water Based Spud Mud	8.3	8.3							
385	3325	OTHER : Brine	9.8	10.2							
3325	10628	OTHER : WBM/Cut Brine	8.8	9.6							
10628	19293	OIL-BASED MUD	11	12.5							

Operator Name: NOVO OIL AND GAS NORTHERN DELAWARE LLC**Well Name:** SATURNINUS FED COM 1510**Well Number:** 231H

Section 6 - Test, Logging, Coring

List of production tests including testing procedures, equipment and safety measures:

A 2-person mud logging program will be used from 3000' to TD. GR log will be acquired by MWD tools from the intermediate casing to TD.

List of open and cased hole logs run in the well:

MUD LOG/GEOLOGICAL LITHOLOGY LOG, GAMMA RAY LOG,

Coring operation description for the well:

No core or drill stem test is planned.

Section 7 - Pressure

Anticipated Bottom Hole Pressure: 5679**Anticipated Surface Pressure:** 3236**Anticipated Bottom Hole Temperature(F):** 215**Anticipated abnormal pressures, temperatures, or potential geologic hazards?** NO**Describe:****Contingency Plans geohazards description:****Contingency Plans geohazards attachment:****Hydrogen Sulfide drilling operations plan required?** YES**Hydrogen sulfide drilling operations plan:**

Saturninus_PadV_H2S_Plan_v2_20211004090152.pdf

Section 8 - Other Information

Proposed horizontal/directional/multi-lateral plan submission:

Saturninus_231H_Horizontal_Plan_v2_20211004090233.pdf

Other proposed operations facets description:**Other proposed operations facets attachment:**

CoFlex_Certs_20200930132245.pdf

Speedhead_Specs_20200930132333.pdf


Saturninus_231H_Drill_Plan_v2_20211004090306.pdf

Saturninus_231H_Anticollision_Report_v2_20211004090331.pdf

Alternative_Casing_Spec_Request_20211004090348.pdf




Other Variance attachment:

Casing_Cement_Variance_20211004090400.pdf

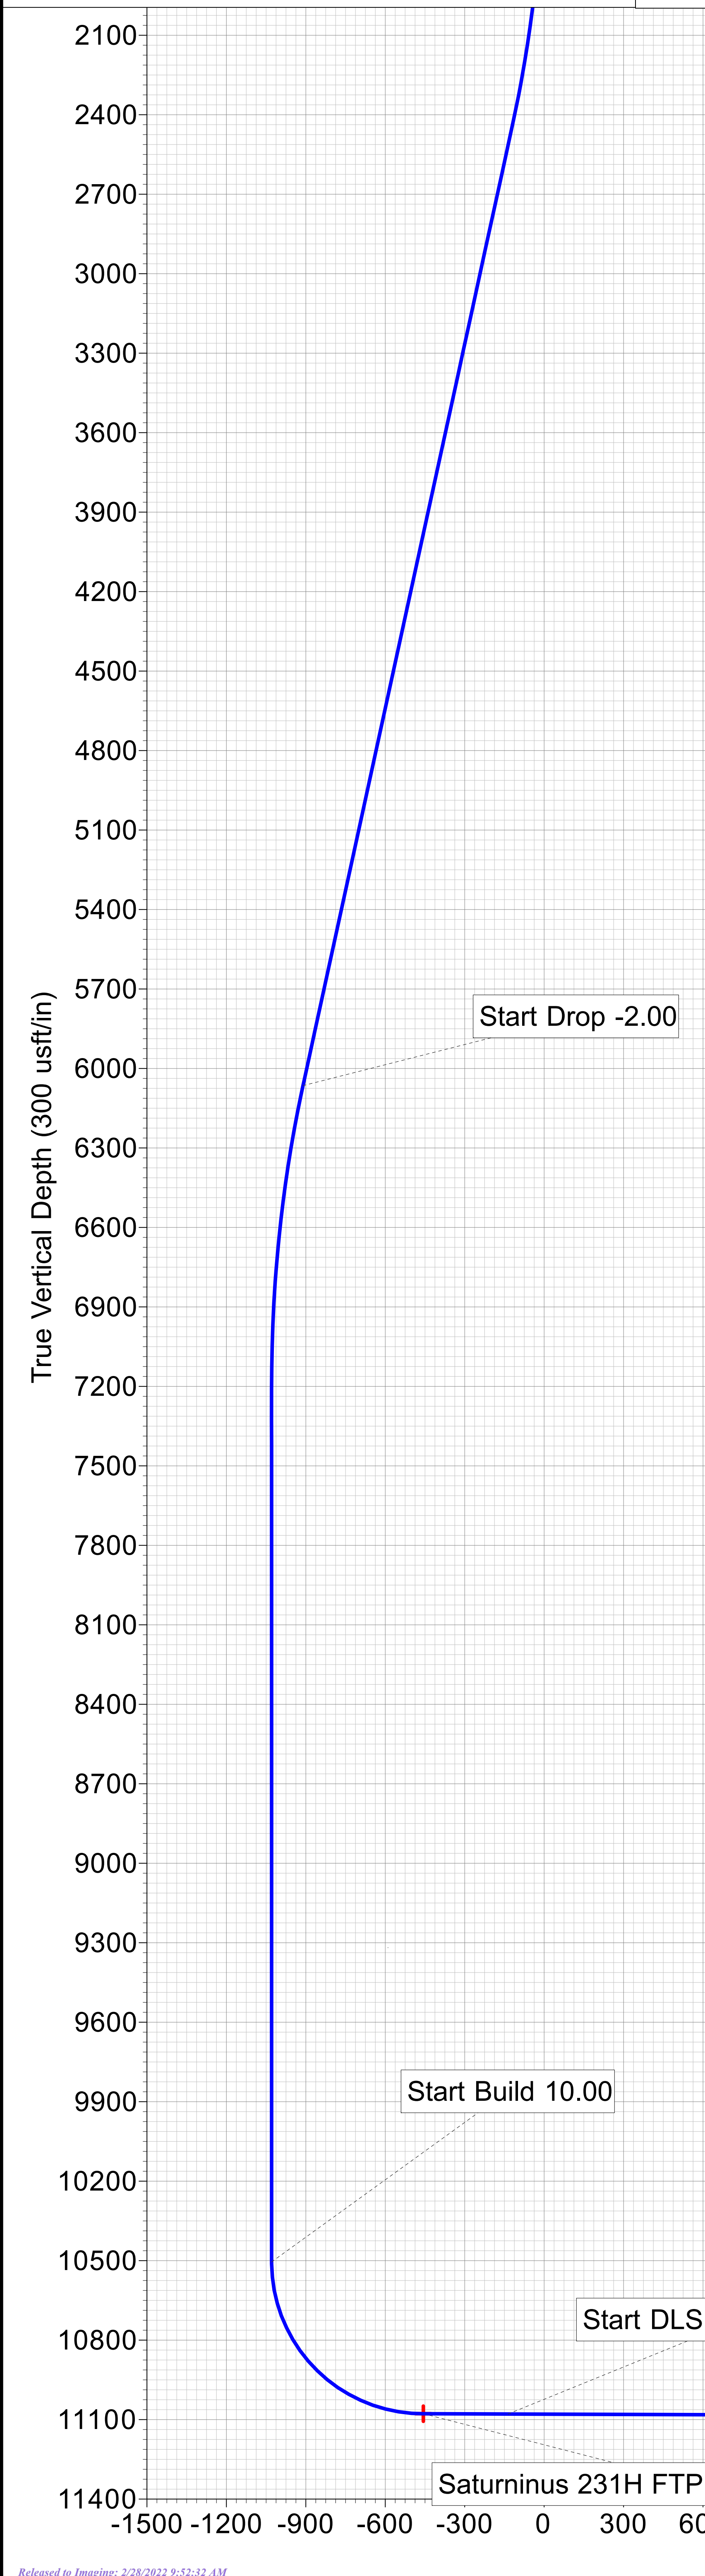

WELL DETAILS: Saturninus Fed Com 1510 231H Plan 1						
GL Elev (ft).: Ground Level: 2979.00						
+N/-S 0.00	+E/-W 0.00	Northing 473053.71	Easting 652311.92	Latitude 32.299987	Longitude -103.974164	
SECTION DETAILS						
MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg TFace VSect
0.00	0.00	0.00	0.00	0.00	0.00	0.00 0.00 0.00
1300.00	0.00	0.00	1300.00	0.00	0.00	0.00 0.00 0.00
2467.11	23.34	239.63	2435.09	-118.56	-202.29	2.00 239.63 -118.56
6420.49	23.34	239.63	6064.91	-910.58	-1553.71	0.00 0.00 -910.58
7587.60	0.00	0.00	7200.00	-1029.14	-1756.00	2.00 180.00 -1029.14
10892.65	0.00	0.00	10505.05	-1029.14	-1756.00	0.00 0.00 -1029.14
11790.65	89.80	355.00	11078.00	-460.35	-1805.76	10.00 355.00 -460.35
12115.65	89.80	355.00	11079.14	-136.59	-1834.09	0.00 0.00 -136.59
12355.67	89.80	359.80	11079.98	103.10	-1844.97	2.00 90.01 103.10
19293.66	89.80	359.80	11104.18	7041.01	-1869.15	0.00 0.00 7041.01

Project: EDDY CO., NM (NAD83)
Site: SEC 15-T23S-R29E
Well: Saturninus Fed Com 1510 231H
Wellbore: Wellbore #1
Design: Plan 1

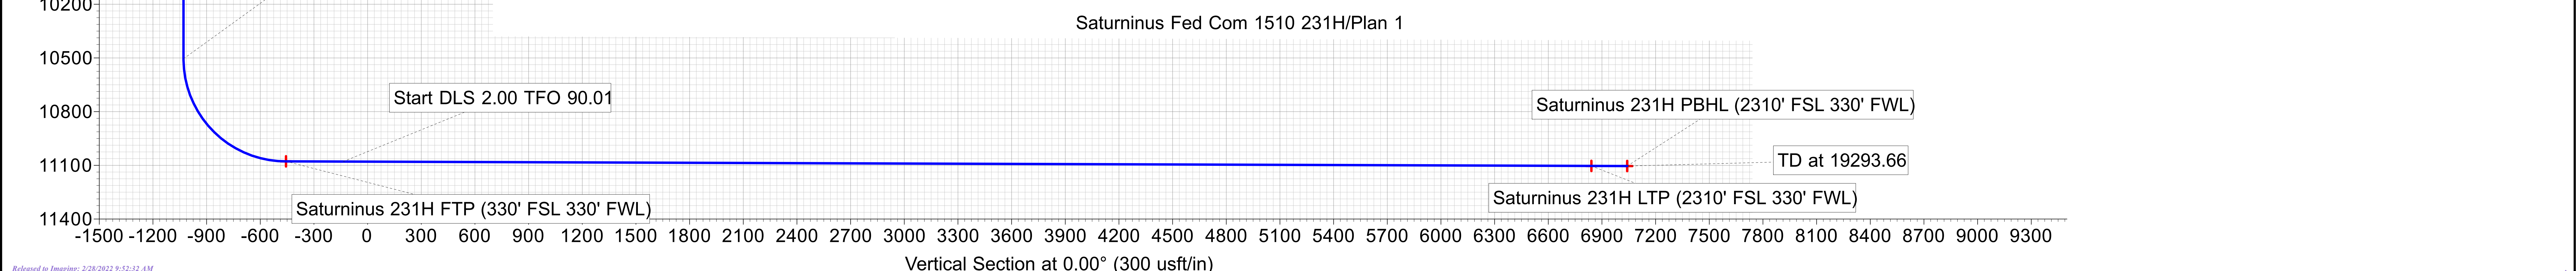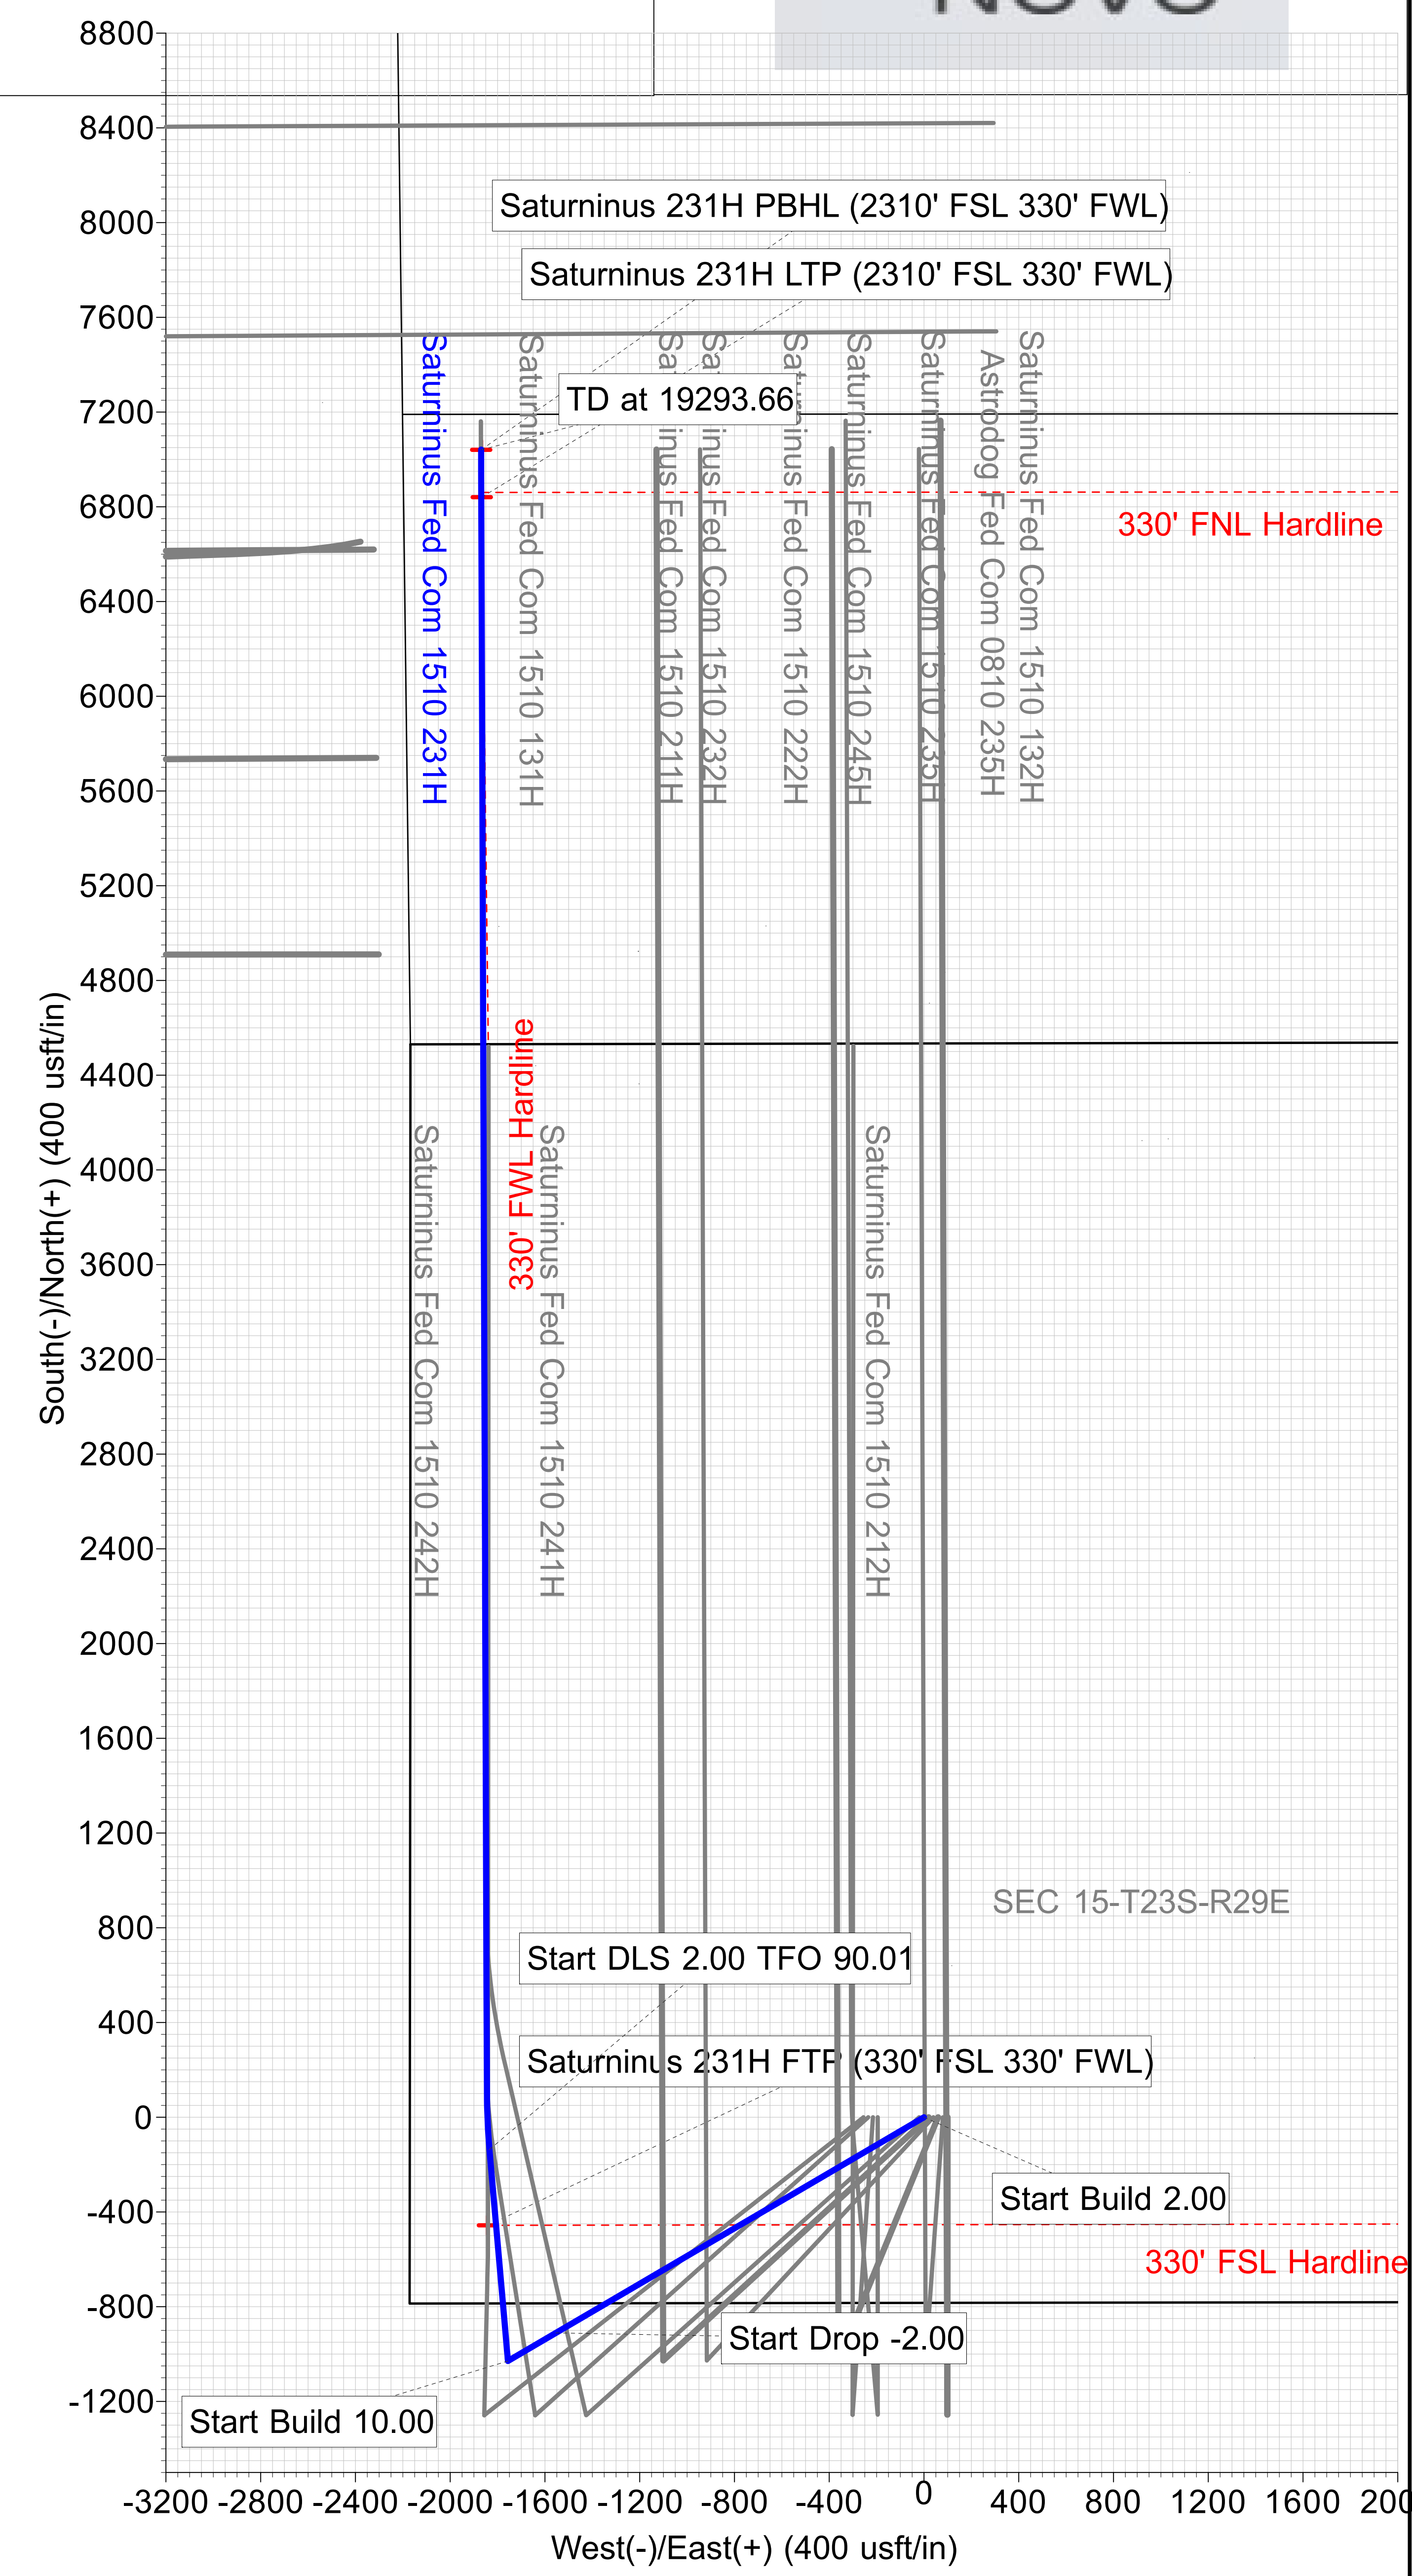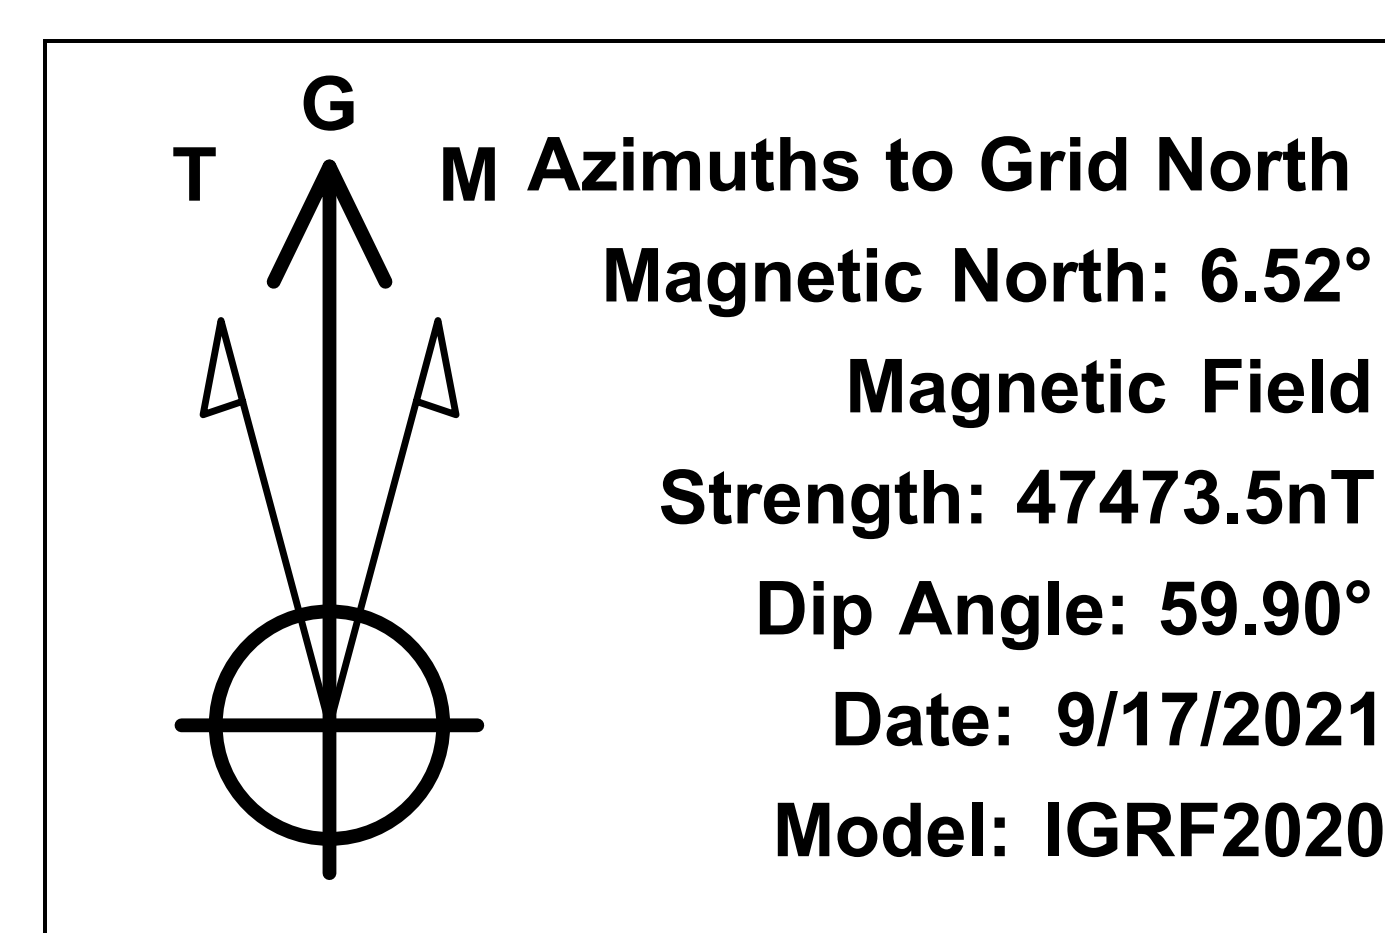



NOVO Oil & Gas

EDDY CO., NM (NAD83)

SEC 15-T23S-R29E

Saturninus Fed Com 1510 231H

Wellbore #1

Plan: Plan 1

Standard Planning Report

21 September, 2021





SB Directional Services

Planning Report



Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Saturninus Fed Com 1510 231H
Company:	NOVO Oil & Gas	TVD Reference:	RKB 25' + GL 2979' @ 3004.00usft
Project:	EDDY CO., NM (NAD83)	MD Reference:	RKB 25' + GL 2979' @ 3004.00usft
Site:	SEC 15-T23S-R29E	North Reference:	Grid
Well:	Saturninus Fed Com 1510 231H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Plan 1		

Project	EDDY CO., NM (NAD83)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site		SEC 15-T23S-R29E				
Site Position:		Northing:	473,053.76	usft	Latitude:	32.299990
From:	Map	Easting:	652,056.71	usft	Longitude:	-103.974990
Position Uncertainty:		0.00	usft	Slot Radius:	13-3/16	"

Well	Saturninus Fed Com 1510 231H					
Well Position	+N/-S	0.00 usft	Northing:	473,053.71 usft	Latitude:	32.299987
	+E/-W	0.00 usft	Easting:	652,311.92 usft	Longitude:	-103.974164
Position Uncertainty		0.00 usft	Wellhead Elevation:	2,979.00 usft	Ground Level:	2,979.00 usft
Grid Convergence:		0.19 °				

Wellbore	Wellbore #1				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	9/17/2021	6.71	59.90	47,473.54498847

Design	Plan 1				
Audit Notes:					
Version:	Phase:	PLAN	Tie On Depth:	0.00	
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)	
	0.00	0.00	0.00	0.00	

Plan Survey Tool Program	Date	9/21/2021			
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks	
1	0.00	19,293.66 Plan 1 (Wellbore #1)	MWD		
			MWD - Standard		



SB Directional Services

Planning Report




Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Saturninus Fed Com 1510 231H
Company:	NOVO Oil & Gas	TVD Reference:	RKB 25' + GL 2979' @ 3004.00usft
Project:	EDDY CO., NM (NAD83)	MD Reference:	RKB 25' + GL 2979' @ 3004.00usft
Site:	SEC 15-T23S-R29E	North Reference:	Grid
Well:	Saturninus Fed Com 1510 231H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Plan 1		

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,300.00	0.00	0.00	1,300.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,467.11	23.34	239.63	2,435.09	-118.56	-202.29	2.00	2.00	0.00	239.63	
6,420.49	23.34	239.63	6,064.91	-910.58	-1,553.71	0.00	0.00	0.00	0.00	
7,587.60	0.00	0.01	7,200.00	-1,029.14	-1,756.00	2.00	-2.00	0.00	180.00	
10,892.65	0.00	0.01	10,505.05	-1,029.14	-1,756.00	0.00	0.00	0.00	0.01	
11,790.65	89.80	355.00	11,078.00	-460.35	-1,805.76	10.00	10.00	0.00	355.00	
12,115.65	89.80	355.00	11,079.14	-136.59	-1,834.09	0.00	0.00	0.00	0.00	
12,355.67	89.80	359.80	11,079.98	103.10	-1,844.97	2.00	0.00	2.00	90.01	
19,293.66	89.80	359.80	11,104.18	7,041.01	-1,869.15	0.00	0.00	0.00	0.00	Saturninus 231H PBI-



SB Directional Services

Planning Report



Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Saturninus Fed Com 1510 231H
Company:	NOVO Oil & Gas	TVD Reference:	RKB 25' + GL 2979' @ 3004.00usft
Project:	EDDY CO., NM (NAD83)	MD Reference:	RKB 25' + GL 2979' @ 3004.00usft
Site:	SEC 15-T23S-R29E	North Reference:	Grid
Well:	Saturninus Fed Com 1510 231H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Plan 1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
100.00	0.00	0.00	100.00	0.00	0.00	0.00	0.00	0.00	0.00
200.00	0.00	0.00	200.00	0.00	0.00	0.00	0.00	0.00	0.00
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00	0.00
500.00	0.00	0.00	500.00	0.00	0.00	0.00	0.00	0.00	0.00
600.00	0.00	0.00	600.00	0.00	0.00	0.00	0.00	0.00	0.00
700.00	0.00	0.00	700.00	0.00	0.00	0.00	0.00	0.00	0.00
800.00	0.00	0.00	800.00	0.00	0.00	0.00	0.00	0.00	0.00
900.00	0.00	0.00	900.00	0.00	0.00	0.00	0.00	0.00	0.00
1,000.00	0.00	0.00	1,000.00	0.00	0.00	0.00	0.00	0.00	0.00
1,100.00	0.00	0.00	1,100.00	0.00	0.00	0.00	0.00	0.00	0.00
1,200.00	0.00	0.00	1,200.00	0.00	0.00	0.00	0.00	0.00	0.00
1,300.00	0.00	0.00	1,300.00	0.00	0.00	0.00	0.00	0.00	0.00
1,400.00	2.00	239.63	1,399.98	-0.88	-1.51	-0.88	2.00	2.00	0.00
1,500.00	4.00	239.63	1,499.84	-3.53	-6.02	-3.53	2.00	2.00	0.00
1,600.00	6.00	239.63	1,599.45	-7.94	-13.54	-7.94	2.00	2.00	0.00
1,700.00	8.00	239.63	1,698.70	-14.10	-24.05	-14.10	2.00	2.00	0.00
1,800.00	10.00	239.63	1,797.47	-22.01	-37.55	-22.01	2.00	2.00	0.00
1,900.00	12.00	239.63	1,895.62	-31.65	-54.01	-31.65	2.00	2.00	0.00
2,000.00	14.00	239.63	1,993.06	-43.03	-73.42	-43.03	2.00	2.00	0.00
2,100.00	16.00	239.63	2,089.64	-56.11	-95.75	-56.11	2.00	2.00	0.00
2,200.00	18.00	239.63	2,185.27	-70.90	-120.97	-70.90	2.00	2.00	0.00
2,300.00	20.00	239.63	2,279.82	-87.36	-149.06	-87.36	2.00	2.00	0.00
2,400.00	22.00	239.63	2,373.17	-105.48	-179.97	-105.48	2.00	2.00	0.00
2,467.11	23.34	239.63	2,435.09	-118.56	-202.29	-118.56	2.00	2.00	0.00
2,500.00	23.34	239.63	2,465.29	-125.14	-213.53	-125.14	0.00	0.00	0.00
2,600.00	23.34	239.63	2,557.11	-145.18	-247.72	-145.18	0.00	0.00	0.00
2,700.00	23.34	239.63	2,648.92	-165.21	-281.90	-165.21	0.00	0.00	0.00
2,800.00	23.34	239.63	2,740.74	-185.25	-316.08	-185.25	0.00	0.00	0.00
2,900.00	23.34	239.63	2,832.55	-205.28	-350.27	-205.28	0.00	0.00	0.00
3,000.00	23.34	239.63	2,924.37	-225.32	-384.45	-225.32	0.00	0.00	0.00
3,100.00	23.34	239.63	3,016.18	-245.35	-418.64	-245.35	0.00	0.00	0.00
3,200.00	23.34	239.63	3,108.00	-265.38	-452.82	-265.38	0.00	0.00	0.00
3,300.00	23.34	239.63	3,199.81	-285.42	-487.00	-285.42	0.00	0.00	0.00
3,400.00	23.34	239.63	3,291.63	-305.45	-521.19	-305.45	0.00	0.00	0.00
3,500.00	23.34	239.63	3,383.45	-325.49	-555.37	-325.49	0.00	0.00	0.00
3,600.00	23.34	239.63	3,475.26	-345.52	-589.56	-345.52	0.00	0.00	0.00
3,700.00	23.34	239.63	3,567.08	-365.56	-623.74	-365.56	0.00	0.00	0.00
3,800.00	23.34	239.63	3,658.89	-385.59	-657.92	-385.59	0.00	0.00	0.00
3,900.00	23.34	239.63	3,750.71	-405.62	-692.11	-405.62	0.00	0.00	0.00
4,000.00	23.34	239.63	3,842.52	-425.66	-726.29	-425.66	0.00	0.00	0.00
4,100.00	23.34	239.63	3,934.34	-445.69	-760.48	-445.69	0.00	0.00	0.00
4,200.00	23.34	239.63	4,026.15	-465.73	-794.66	-465.73	0.00	0.00	0.00
4,300.00	23.34	239.63	4,117.97	-485.76	-828.84	-485.76	0.00	0.00	0.00
4,400.00	23.34	239.63	4,209.78	-505.79	-863.03	-505.79	0.00	0.00	0.00
4,500.00	23.34	239.63	4,301.60	-525.83	-897.21	-525.83	0.00	0.00	0.00
4,600.00	23.34	239.63	4,393.42	-545.86	-931.40	-545.86	0.00	0.00	0.00
4,700.00	23.34	239.63	4,485.23	-565.90	-965.58	-565.90	0.00	0.00	0.00
4,800.00	23.34	239.63	4,577.05	-585.93	-999.76	-585.93	0.00	0.00	0.00
4,900.00	23.34	239.63	4,668.86	-605.97	-1,033.95	-605.97	0.00	0.00	0.00
5,000.00	23.34	239.63	4,760.68	-626.00	-1,068.13	-626.00	0.00	0.00	0.00
5,100.00	23.34	239.63	4,852.49	-646.03	-1,102.32	-646.03	0.00	0.00	0.00
5,200.00	23.34	239.63	4,944.31	-666.07	-1,136.50	-666.07	0.00	0.00	0.00



SB Directional Services

Planning Report



Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Saturninus Fed Com 1510 231H
Company:	NOVO Oil & Gas	TVD Reference:	RKB 25' + GL 2979' @ 3004.00usft
Project:	EDDY CO., NM (NAD83)	MD Reference:	RKB 25' + GL 2979' @ 3004.00usft
Site:	SEC 15-T23S-R29E	North Reference:	Grid
Well:	Saturninus Fed Com 1510 231H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Plan 1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
5,300.00	23.34	239.63	5,036.12	-686.10	-1,170.68	-686.10	0.00	0.00	0.00
5,400.00	23.34	239.63	5,127.94	-706.14	-1,204.87	-706.14	0.00	0.00	0.00
5,500.00	23.34	239.63	5,219.75	-726.17	-1,239.05	-726.17	0.00	0.00	0.00
5,600.00	23.34	239.63	5,311.57	-746.21	-1,273.24	-746.21	0.00	0.00	0.00
5,700.00	23.34	239.63	5,403.39	-766.24	-1,307.42	-766.24	0.00	0.00	0.00
5,800.00	23.34	239.63	5,495.20	-786.27	-1,341.60	-786.27	0.00	0.00	0.00
5,900.00	23.34	239.63	5,587.02	-806.31	-1,375.79	-806.31	0.00	0.00	0.00
6,000.00	23.34	239.63	5,678.83	-826.34	-1,409.97	-826.34	0.00	0.00	0.00
6,100.00	23.34	239.63	5,770.65	-846.38	-1,444.16	-846.38	0.00	0.00	0.00
6,200.00	23.34	239.63	5,862.46	-866.41	-1,478.34	-866.41	0.00	0.00	0.00
6,300.00	23.34	239.63	5,954.28	-886.45	-1,512.52	-886.45	0.00	0.00	0.00
6,400.00	23.34	239.63	6,046.09	-906.48	-1,546.71	-906.48	0.00	0.00	0.00
6,420.49	23.34	239.63	6,064.91	-910.58	-1,553.71	-910.58	0.00	0.00	0.00
6,500.00	21.75	239.63	6,138.34	-926.00	-1,580.01	-926.00	2.00	-2.00	0.00
6,600.00	19.75	239.63	6,231.84	-943.91	-1,610.58	-943.91	2.00	-2.00	0.00
6,700.00	17.75	239.63	6,326.53	-960.17	-1,638.32	-960.17	2.00	-2.00	0.00
6,800.00	15.75	239.63	6,422.28	-974.74	-1,663.18	-974.74	2.00	-2.00	0.00
6,900.00	13.75	239.63	6,518.98	-987.62	-1,685.15	-987.62	2.00	-2.00	0.00
7,000.00	11.75	239.63	6,616.51	-998.78	-1,704.19	-998.78	2.00	-2.00	0.00
7,100.00	9.75	239.63	6,714.75	-1,008.21	-1,720.29	-1,008.21	2.00	-2.00	0.00
7,200.00	7.75	239.63	6,813.58	-1,015.90	-1,733.41	-1,015.90	2.00	-2.00	0.00
7,300.00	5.75	239.63	6,912.88	-1,021.85	-1,743.56	-1,021.85	2.00	-2.00	0.00
7,400.00	3.75	239.63	7,012.53	-1,026.04	-1,750.70	-1,026.04	2.00	-2.00	0.00
7,500.00	1.75	239.63	7,112.41	-1,028.46	-1,754.84	-1,028.46	2.00	-2.00	0.00
7,587.60	0.00	0.01	7,200.00	-1,029.14	-1,756.00	-1,029.14	2.00	-2.00	0.00
7,600.00	0.00	0.00	7,212.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
7,700.00	0.00	0.00	7,312.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
7,800.00	0.00	0.00	7,412.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
7,900.00	0.00	0.00	7,512.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
8,000.00	0.00	0.00	7,612.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
8,100.00	0.00	0.00	7,712.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
8,200.00	0.00	0.00	7,812.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
8,300.00	0.00	0.00	7,912.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
8,400.00	0.00	0.00	8,012.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
8,500.00	0.00	0.00	8,112.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
8,600.00	0.00	0.00	8,212.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
8,700.00	0.00	0.00	8,312.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
8,800.00	0.00	0.00	8,412.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
8,900.00	0.00	0.00	8,512.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
9,000.00	0.00	0.00	8,612.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
9,100.00	0.00	0.00	8,712.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
9,200.00	0.00	0.00	8,812.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
9,300.00	0.00	0.00	8,912.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
9,400.00	0.00	0.00	9,012.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
9,500.00	0.00	0.00	9,112.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
9,600.00	0.00	0.00	9,212.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
9,700.00	0.00	0.00	9,312.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
9,800.00	0.00	0.00	9,412.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
9,900.00	0.00	0.00	9,512.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
10,000.00	0.00	0.00	9,612.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
10,100.00	0.00	0.00	9,712.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
10,200.00	0.00	0.00	9,812.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
10,300.00	0.00	0.00	9,912.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
10,400.00	0.00	0.00	10,012.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00



SB Directional Services

Planning Report




Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Saturninus Fed Com 1510 231H
Company:	NOVO Oil & Gas	TVD Reference:	RKB 25' + GL 2979' @ 3004.00usft
Project:	EDDY CO., NM (NAD83)	MD Reference:	RKB 25' + GL 2979' @ 3004.00usft
Site:	SEC 15-T23S-R29E	North Reference:	Grid
Well:	Saturninus Fed Com 1510 231H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Plan 1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
10,500.00	0.00	0.00	10,112.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
10,600.00	0.00	0.00	10,212.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
10,700.00	0.00	0.00	10,312.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
10,800.00	0.00	0.00	10,412.40	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
10,892.65	0.00	0.01	10,505.05	-1,029.14	-1,756.00	-1,029.14	0.00	0.00	0.00
10,900.00	0.73	355.00	10,512.40	-1,029.09	-1,756.00	-1,029.09	10.00	10.00	0.00
10,950.00	5.73	355.00	10,562.30	-1,026.28	-1,756.25	-1,026.28	10.00	10.00	0.00
11,000.00	10.73	355.00	10,611.77	-1,019.15	-1,756.87	-1,019.15	10.00	10.00	0.00
11,050.00	15.73	355.00	10,660.43	-1,007.75	-1,757.87	-1,007.75	10.00	10.00	0.00
11,100.00	20.73	355.00	10,707.90	-992.17	-1,759.23	-992.17	10.00	10.00	0.00
11,150.00	25.73	355.00	10,753.83	-972.53	-1,760.95	-972.53	10.00	10.00	0.00
11,200.00	30.73	355.00	10,797.87	-948.97	-1,763.01	-948.97	10.00	10.00	0.00
11,250.00	35.73	355.00	10,839.68	-921.68	-1,765.40	-921.68	10.00	10.00	0.00
11,300.00	40.73	355.00	10,878.94	-890.86	-1,768.10	-890.86	10.00	10.00	0.00
11,350.00	45.73	355.00	10,915.36	-856.75	-1,771.08	-856.75	10.00	10.00	0.00
11,400.00	50.73	355.00	10,948.65	-819.61	-1,774.33	-819.61	10.00	10.00	0.00
11,450.00	55.73	355.00	10,978.57	-779.72	-1,777.82	-779.72	10.00	10.00	0.00
11,500.00	60.73	355.00	11,004.88	-737.39	-1,781.53	-737.39	10.00	10.00	0.00
11,550.00	65.73	355.00	11,027.39	-692.93	-1,785.41	-692.93	10.00	10.00	0.00
11,600.00	70.73	355.00	11,045.92	-646.68	-1,789.46	-646.68	10.00	10.00	0.00
11,650.00	75.73	355.00	11,060.34	-599.01	-1,793.63	-599.01	10.00	10.00	0.00
11,700.00	80.73	355.00	11,070.53	-550.26	-1,797.90	-550.26	10.00	10.00	0.00
11,750.00	85.73	355.00	11,076.42	-500.81	-1,802.22	-500.81	10.00	10.00	0.00
11,790.65	89.80	355.00	11,078.00	-460.35	-1,805.76	-460.35	10.00	10.00	0.00
11,800.00	89.80	355.00	11,078.04	-451.04	-1,806.58	-451.04	0.00	0.00	0.00
11,900.00	89.80	355.00	11,078.39	-351.42	-1,815.29	-351.42	0.00	0.00	0.00
12,000.00	89.80	355.00	11,078.74	-251.80	-1,824.01	-251.80	0.00	0.00	0.00
12,100.00	89.80	355.00	11,079.08	-152.18	-1,832.72	-152.18	0.00	0.00	0.00
12,115.65	89.80	355.00	11,079.14	-136.59	-1,834.09	-136.59	0.00	0.00	0.00
12,200.00	89.80	356.69	11,079.43	-52.47	-1,840.20	-52.47	2.00	0.00	2.00
12,300.00	89.80	358.69	11,079.78	47.44	-1,844.24	47.44	2.00	0.00	2.00
12,355.67	89.80	359.80	11,079.98	103.10	-1,844.97	103.10	2.00	0.00	2.00
12,400.00	89.80	359.80	11,080.13	147.44	-1,845.13	147.44	0.00	0.00	0.00
12,500.00	89.80	359.80	11,080.48	247.44	-1,845.47	247.44	0.00	0.00	0.00
12,600.00	89.80	359.80	11,080.83	347.43	-1,845.82	347.43	0.00	0.00	0.00
12,700.00	89.80	359.80	11,081.18	447.43	-1,846.17	447.43	0.00	0.00	0.00
12,800.00	89.80	359.80	11,081.53	547.43	-1,846.52	547.43	0.00	0.00	0.00
12,900.00	89.80	359.80	11,081.88	647.43	-1,846.87	647.43	0.00	0.00	0.00
13,000.00	89.80	359.80	11,082.22	747.43	-1,847.22	747.43	0.00	0.00	0.00
13,100.00	89.80	359.80	11,082.57	847.43	-1,847.57	847.43	0.00	0.00	0.00
13,200.00	89.80	359.80	11,082.92	947.43	-1,847.91	947.43	0.00	0.00	0.00
13,300.00	89.80	359.80	11,083.27	1,047.43	-1,848.26	1,047.43	0.00	0.00	0.00
13,400.00	89.80	359.80	11,083.62	1,147.42	-1,848.61	1,147.42	0.00	0.00	0.00
13,500.00	89.80	359.80	11,083.97	1,247.42	-1,848.96	1,247.42	0.00	0.00	0.00
13,600.00	89.80	359.80	11,084.32	1,347.42	-1,849.31	1,347.42	0.00	0.00	0.00
13,700.00	89.80	359.80	11,084.67	1,447.42	-1,849.66	1,447.42	0.00	0.00	0.00
13,800.00	89.80	359.80	11,085.02	1,547.42	-1,850.01	1,547.42	0.00	0.00	0.00
13,900.00	89.80	359.80	11,085.36	1,647.42	-1,850.35	1,647.42	0.00	0.00	0.00
14,000.00	89.80	359.80	11,085.71	1,747.42	-1,850.70	1,747.42	0.00	0.00	0.00
14,100.00	89.80	359.80	11,086.06	1,847.42	-1,851.05	1,847.42	0.00	0.00	0.00
14,200.00	89.80	359.80	11,086.41	1,947.41	-1,851.40	1,947.41	0.00	0.00	0.00
14,300.00	89.80	359.80	11,086.76	2,047.41	-1,851.75	2,047.41	0.00	0.00	0.00
14,400.00	89.80	359.80	11,087.11	2,147.41	-1,852.10	2,147.41	0.00	0.00	0.00
14,500.00	89.80	359.80	11,087.46	2,247.41	-1,852.44	2,247.41	0.00	0.00	0.00



SB Directional Services

Planning Report



Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Saturninus Fed Com 1510 231H
Company:	NOVO Oil & Gas	TVD Reference:	RKB 25' + GL 2979' @ 3004.00usft
Project:	EDDY CO., NM (NAD83)	MD Reference:	RKB 25' + GL 2979' @ 3004.00usft
Site:	SEC 15-T23S-R29E	North Reference:	Grid
Well:	Saturninus Fed Com 1510 231H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Plan 1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
14,600.00	89.80	359.80	11,087.81	2,347.41	-1,852.79	2,347.41	0.00	0.00	0.00	
14,700.00	89.80	359.80	11,088.16	2,447.41	-1,853.14	2,447.41	0.00	0.00	0.00	
14,800.00	89.80	359.80	11,088.50	2,547.41	-1,853.49	2,547.41	0.00	0.00	0.00	
14,900.00	89.80	359.80	11,088.85	2,647.41	-1,853.84	2,647.41	0.00	0.00	0.00	
15,000.00	89.80	359.80	11,089.20	2,747.40	-1,854.19	2,747.40	0.00	0.00	0.00	
15,100.00	89.80	359.80	11,089.55	2,847.40	-1,854.54	2,847.40	0.00	0.00	0.00	
15,200.00	89.80	359.80	11,089.90	2,947.40	-1,854.88	2,947.40	0.00	0.00	0.00	
15,300.00	89.80	359.80	11,090.25	3,047.40	-1,855.23	3,047.40	0.00	0.00	0.00	
15,400.00	89.80	359.80	11,090.60	3,147.40	-1,855.58	3,147.40	0.00	0.00	0.00	
15,500.00	89.80	359.80	11,090.95	3,247.40	-1,855.93	3,247.40	0.00	0.00	0.00	
15,600.00	89.80	359.80	11,091.29	3,347.40	-1,856.28	3,347.40	0.00	0.00	0.00	
15,700.00	89.80	359.80	11,091.64	3,447.40	-1,856.63	3,447.40	0.00	0.00	0.00	
15,800.00	89.80	359.80	11,091.99	3,547.39	-1,856.97	3,547.39	0.00	0.00	0.00	
15,900.00	89.80	359.80	11,092.34	3,647.39	-1,857.32	3,647.39	0.00	0.00	0.00	
16,000.00	89.80	359.80	11,092.69	3,747.39	-1,857.67	3,747.39	0.00	0.00	0.00	
16,100.00	89.80	359.80	11,093.04	3,847.39	-1,858.02	3,847.39	0.00	0.00	0.00	
16,200.00	89.80	359.80	11,093.39	3,947.39	-1,858.37	3,947.39	0.00	0.00	0.00	
16,300.00	89.80	359.80	11,093.74	4,047.39	-1,858.72	4,047.39	0.00	0.00	0.00	
16,400.00	89.80	359.80	11,094.09	4,147.39	-1,859.07	4,147.39	0.00	0.00	0.00	
16,500.00	89.80	359.80	11,094.43	4,247.39	-1,859.41	4,247.39	0.00	0.00	0.00	
16,600.00	89.80	359.80	11,094.78	4,347.39	-1,859.76	4,347.39	0.00	0.00	0.00	
16,700.00	89.80	359.80	11,095.13	4,447.38	-1,860.11	4,447.38	0.00	0.00	0.00	
16,800.00	89.80	359.80	11,095.48	4,547.38	-1,860.46	4,547.38	0.00	0.00	0.00	
16,900.00	89.80	359.80	11,095.83	4,647.38	-1,860.81	4,647.38	0.00	0.00	0.00	
17,000.00	89.80	359.80	11,096.18	4,747.38	-1,861.16	4,747.38	0.00	0.00	0.00	
17,100.00	89.80	359.80	11,096.53	4,847.38	-1,861.51	4,847.38	0.00	0.00	0.00	
17,200.00	89.80	359.80	11,096.88	4,947.38	-1,861.85	4,947.38	0.00	0.00	0.00	
17,300.00	89.80	359.80	11,097.23	5,047.38	-1,862.20	5,047.38	0.00	0.00	0.00	
17,400.00	89.80	359.80	11,097.57	5,147.38	-1,862.55	5,147.38	0.00	0.00	0.00	
17,500.00	89.80	359.80	11,097.92	5,247.37	-1,862.90	5,247.37	0.00	0.00	0.00	
17,600.00	89.80	359.80	11,098.27	5,347.37	-1,863.25	5,347.37	0.00	0.00	0.00	
17,700.00	89.80	359.80	11,098.62	5,447.37	-1,863.60	5,447.37	0.00	0.00	0.00	
17,800.00	89.80	359.80	11,098.97	5,547.37	-1,863.94	5,547.37	0.00	0.00	0.00	
17,900.00	89.80	359.80	11,099.32	5,647.37	-1,864.29	5,647.37	0.00	0.00	0.00	
18,000.00	89.80	359.80	11,099.67	5,747.37	-1,864.64	5,747.37	0.00	0.00	0.00	
18,100.00	89.80	359.80	11,100.02	5,847.37	-1,864.99	5,847.37	0.00	0.00	0.00	
18,200.00	89.80	359.80	11,100.37	5,947.37	-1,865.34	5,947.37	0.00	0.00	0.00	
18,300.00	89.80	359.80	11,100.71	6,047.36	-1,865.69	6,047.36	0.00	0.00	0.00	
18,400.00	89.80	359.80	11,101.06	6,147.36	-1,866.04	6,147.36	0.00	0.00	0.00	
18,500.00	89.80	359.80	11,101.41	6,247.36	-1,866.38	6,247.36	0.00	0.00	0.00	
18,600.00	89.80	359.80	11,101.76	6,347.36	-1,866.73	6,347.36	0.00	0.00	0.00	
18,700.00	89.80	359.80	11,102.11	6,447.36	-1,867.08	6,447.36	0.00	0.00	0.00	
18,800.00	89.80	359.80	11,102.46	6,547.36	-1,867.43	6,547.36	0.00	0.00	0.00	
18,900.00	89.80	359.80	11,102.81	6,647.36	-1,867.78	6,647.36	0.00	0.00	0.00	
19,000.00	89.80	359.80	11,103.16	6,747.36	-1,868.13	6,747.36	0.00	0.00	0.00	
19,100.00	89.80	359.80	11,103.50	6,847.35	-1,868.48	6,847.35	0.00	0.00	0.00	
19,200.00	89.80	359.80	11,103.85	6,947.35	-1,868.82	6,947.35	0.00	0.00	0.00	
19,293.66	89.80	359.80	11,104.18	7,041.01	-1,869.15	7,041.01	0.00	0.00	0.00	



SB Directional Services

Planning Report



Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Saturninus Fed Com 1510 231H
Company:	NOVO Oil & Gas	TVD Reference:	RKB 25' + GL 2979' @ 3004.00usft
Project:	EDDY CO., NM (NAD83)	MD Reference:	RKB 25' + GL 2979' @ 3004.00usft
Site:	SEC 15-T23S-R29E	North Reference:	Grid
Well:	Saturninus Fed Com 1510 231H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Plan 1		

Design Targets									
Target Name - hit/miss target - Shape	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
Saturninus 231H FTP (3 - plan misses target center by 34.48usft at 11797.90usft MD (11078.03 TVD, -453.14 N, -1806.39 E) - Point	0.00	0.01	11,078.00	-456.14	-1,840.74	472,597.57	650,471.18	32.298750	-103.980127
Saturninus 231H LTP (2: - plan misses target center by 1.81usft at 19093.66usft MD (11103.48 TVD, 6841.01 N, -1868.45 E) - Point	0.00	0.00	11,103.48	6,841.02	-1,866.64	479,894.73	650,445.28	32.318809	-103.980133
Saturninus 231H PBHL (- plan hits target center - Point	0.00	0.00	11,104.18	7,041.01	-1,869.15	480,094.72	650,442.77	32.319359	-103.980139

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	NOVO OIL AND GAS LLC
LEASE NO.:	NMNM111416
WELL NAME & NO.:	SATURNINUS FED COM 1510 231H
SURFACE HOLE FOOTAGE:	784'/S & 2170'/W
BOTTOM HOLE FOOTAGE:	2510'/S & 330'/W
LOCATION:	Section 15, T.23 S., R.29 E., NMPM
COUNTY:	Eddy County, New Mexico

COA

H2S	☐ Yes	☒ No	
Potash	☒ None	☐ Secretary	☐ R-111-P
Cave/Karst Potential	☐ Low	☒ Medium	☐ High
Cave/Karst Potential	☐ Critical		
Variance	☐ None	☒ Flex Hose	☐ Other
Wellhead	☐ Conventional	☒ Multibowl	☐ Both
Other	☐ 4 String Area	☐ Capitan Reef	☐ WIPP
Other	☒ Fluid Filled	☐ Cement Squeeze	☐ Pilot Hole
Special Requirements	☐ Water Disposal	☒ COM	☐ Unit

A. HYDROGEN SULFIDE

Hydrogen Sulfide (H2S) monitors shall be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.

B. CASING

1. The **13-3/8** inch surface casing shall be set at approximately **385 feet** (a minimum of 70 feet (Eddy County) into the Rustler Anhydrite and above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8**

- hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
- c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The **10-3/4** inch Intermediate casing shall be set at **2900 feet**. The minimum required fill of cement behind the **10-3/4** inch intermediate casing is:

Option 1 (Single Stage):

- Cement to surface. If cement does not circulate see B.1.a, c-d above.
Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.
- ❖ In Medium Cave/Karst Areas if cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface.

Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.

3. The minimum required fill of cement behind the **8-5/8** inch production casing is:

Option 1 (Single Stage):

- Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.

4. The minimum required fill of cement behind the **5-1/2** inch production liner is:
- Cement should tie-back **100 feet** into the previous casing. Operator shall provide method of verification.

PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'
2. **BOP REQUIREMENTS.**

Option 1

- a. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **2000 (2M)** psi.
- b. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the intermediate casing shoe shall be **10,000 (10M)** psi.

Option 2

3. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi. . **Variance is approved to use a 5000 (5M) Annular which shall be tested to 5000 (5M) psi.**
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
 - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

C. SPECIAL REQUIREMENT (S)**Communitization Agreement**

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Eddy County

Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
(575) 361-2822

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)
393-3612

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig

- Notify the BLM when moving in and removing the Spudder Rig.
 - Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
 3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.

4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.

- b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.
 - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
- a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the plug. However, **no tests** shall commence until the cement has had a minimum of 24 hours setup time, except the casing pressure test can be initiated immediately after bumping the plug (only applies to single stage cement jobs).
 - c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to Onshore Order 2 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
 - d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall

have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.

- e. The results of the test shall be reported to the appropriate BLM office.
- f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

RI11202021



H₂S Drilling Operations Plan

- a. All personnel will be trained in H₂S working conditions as required by Onshore Order 6 before drilling out of the surface casing.
- b. Two briefing areas will be established. Each will be at least 150' from the wellhead, perpendicular from one another, and easily entered and exited. See H₂S page 5 for more details.
- c. H₂S Safety Equipment/Systems:
 - i. Well Control Equipment
 - Flare line will be $\geq 150'$ from the wellhead and ignited by a pilot light.
 - Beware of SO₂ created by flaring.
 - Choke manifold will include a remotely operated choke.
 - Mud gas separator
 - ii. Protective Equipment for Essential Personnel
 - Every person on site will be required to wear a personal H₂S and SO₂ monitor at all times while on site. Monitors will not be worn on hard hats. Monitors will be worn on the front of the chest.
 - One self-contained breathing apparatus (SCBA) 30-minute rescue pack will be at each briefing area. Two 30-minute SCBA packs will be stored in the safety trailer.
 - Four work/escape packs will be on the rig floor. Each pack will have a long enough hose to allow unimpaired work activity.
 - Four emergency escape packs will be in the doghouse for emergency evacuation.
 - Hand signals will be used when wearing protective breathing apparatus.
 - Stokes litter or stretcher
 - Two full OSHA compliant body harnesses
 - A 100-foot long x 5/8" OSHA compliant rope
 - One 20-pound ABC fire extinguisher

iii. H₂S Detection & Monitoring Equipment

- Every person on site will be required to wear a personal H₂S and SO₂ monitor at all times while on site. Monitors will not be worn on hard hats. Monitors will be worn on the front of the chest.
- A stationary detector with three sensors will be in the doghouse.
- Sensors will be installed on the rig floor, bell nipple, and at the end of the flow line or where drilling fluids are discharged.
- Visual alarm will be triggered at 10 ppm.
- Audible alarm will be triggered at 10 ppm.
- Calibration will occur at least every 30 days. Gas sample tubes will be kept in the safety trailer.

iv. Visual Warning System

- Color-coded H₂S condition sign will be set at the entrance to the pad.
- Color-coded condition flag will be installed to indicate current H₂S conditions.
- Two wind socks will be installed that will be visible from all sides.

v. Mud Program

- A water based mud with a pH of ≥ 10 will be maintained to control corrosion, H₂S gas returns to the surface, and minimize sulfide stress cracking and embrittlement.
- Drilling mud containing H₂S gas will be degassed at an optimum location for the rig configuration.
- This gas will be piped into the flare system.
- Enough mud additives will be on location to scavenge and/or neutralize H₂S where formation pressures are unknown.

vi. Metallurgy

- All equipment that has the potential to be exposed to H₂S will be suitable for H₂S service.
- Equipment that will meet these metallurgical standards include the drill string, casing, wellhead, BOP assembly, casing head and spool, rotating head, kill lines, choke, choke manifold and lines, valves, mud-gas separators, DST tools, test units, tubing, flanges, and other related equipment (elastomer packings and seals).

vii. Communication from well site

- Cell phones and/or two-way radios will be used to communicate from the well site.

- d. A remote-controlled choke, mud-gas separator, and a rotating head will be installed before drilling or testing any formation expected to contain H₂S.

Company Personnel to be Notified

Kurt Shipley, Vice-President - Operations Office: (405) 609-1596

Local & County Agencies

Loving Fire Department 911 or (575) 745-3600

Eddy County Sheriff (Carlsbad) 911 (575) 887-7551

Eddy County Emergency Management (Carlsbad) (575) 887-9511

Carlsbad Medical Center Hospital (575) 887-4100

Eddy County South Road Department (Carlsbad) (575) 885-4835

State Agencies

NM State Police (Carlsbad) (575) 885-3138

NM Oil Conservation (Artesia) (575) 748-1283

NM Oil Conservation (Santa Fe) (505) 476-3440

NM Dept. of Transportation (Roswell) (575) 637-7201

Federal Agencies

BLM Carlsbad Field Office (575) 234-5972

National Response Center (800) 424-8802

US EPA Region 6 (Dallas) (800) 887-6063

(214) 665-6444

Residents within 3/4 mile

none

Air Evacuation

Med Flight Air Ambulance (Albuquerque) (800) 842-4431

Lifeguard (Albuquerque) (888) 866-7256

Veterinarians

Desert Willow Veterinary Services (Carlsbad) (575) 885-3399

Animal Care Center (Carlsbad) (575) 885-5352

NOVO OIL & GAS NORTHERN DELAWARE, LLC
SATURNINUS PAD V
SE 1/4 SW 1/4 OF SEC. 15, T-23-S, R-29-E, N.M.P.M.
EDDY COUNTY, N.M.

*Before digging
call for utility
line location!*

highest ground
at Northeast

SE 1/4
SW 1/4
BUREAU OF
OF LAND
MANAGEMENT

flare >150' from wellhead
flare line straight

windsocks on rig floor
& at mud tanks

secondary briefing area
>150' from wellhead
& exit route

PRIMARY safety briefing
area >150' from wellhead
& exit route

warning sign
& windsock

prevailing wind
from South


OVERALL DIMENSIONS: 715' X 495' = 7.491 ACRES

	WELL FLAG	NAD 83
1	241H WELL FLAG 784' FSL, 1915' FWL	LAT.=32.2999896' N LONG.=103.9749902' W
2	242H WELL FLAG 784' FSL, 1935' FWL	LAT.=32.2999897' N LONG.=103.9749253' W
3	212H WELL FLAG 784' FSL, 1955' FWL	LAT.=32.2999894' N LONG.=103.9748607' W
4	245H WELL FLAG 784' FSL, 1975' FWL	LAT.=32.2999892' N LONG.=103.9747958' W

	WELL FLAG	NAD 83
5	131H WELL FLAG 784' FSL, 2150' FWL	LAT.=32.2999875' N LONG.=103.9742292' W
6	231H WELL FLAG 784' FSL, 2170' FWL	LAT.=32.2999871' N LONG.=103.9741642' W
7	211H WELL FLAG 784' FSL, 2190' FWL	LAT.=32.2999873' N LONG.=103.9740998' W
8	232H WELL FLAG 784' FSL, 2210' FWL	LAT.=32.2999870' N LONG.=103.9740350' W
9	222H WELL FLAG 784' FSL, 2230' FWL	LAT.=32.2999869' N LONG.=103.9739706' W
10	235H WELL FLAG 784' FSL, 2250' FWL	LAT.=32.2999863' N LONG.=103.9739055' W
11	132H WELL FLAG 784' FSL, 2270' FWL	LAT.=32.2999863' N LONG.=103.9738410' W

- Notes:**
- 1. All Bearings, distances and coordinates are based upon the New Mexico State Plane Coordinate System, East Zone, NAD 83, in U.S. survey feet.
 - 2. Contractor shall contact "One-Call" for location of any marked or unmarked buried pipelines or cables on pad and/or access road at least two (2) working days prior to construction.
 - 3. United Field Services Inc. is not liable for underground utilities or pipelines.

I, MARSHALL W. LINDEEN, NEW MEXICO PROFESSIONAL SURVEYOR NO. 17078, DO HEREBY CERTIFY THAT THIS SURVEY PLAT AND THE ACTUAL SURVEY ON THE GROUND UPON WHICH IT IS BASED WERE PERFORMED BY ME OR UNDER MY DIRECT SUPERVISION; THAT I AM RESPONSIBLE FOR THIS SURVEY; THAT THIS SURVEY MEETS THE MINIMUM STANDARDS FOR SURVEYING IN NEW MEXICO; AND THAT IT IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF. I FURTHER CERTIFY THAT THIS SURVEY IS NOT A LAND DIVISION OR SUBDIVISION AS DEFINED IN THE NEW MEXICO SUBDIVISION ACT.



NOVO OIL & GAS NORTHERN DELAWARE, LLC

SURVEYED: 08/13/21 & 08/25/21	REV./BY: 09/01/21	APP. BY: M.W.L.
DRAWN BY: C.B.	DATE DRAWN: 08/27/21	FILE NAME: 11565-PAD



P.O. BOX 3651
FARMINGTON, NM 87499
OFFICE: (505) 334-0408

Marshall W. Lindeen
MARSHALL W. LINDEEN P.S. #17078
9-15-21
DATE

Section 15, Township 23S, Range 29E
Eddy County, New Mexico

 Well Pad Location

1:27,000

0 0.25 0.5 1


Miles




NAD 1983 New Mexico State Plane East
FIPS 3001 Feet



Prepared by Permits West, Inc., October 1, 2021
for Novo Oil & Gas Northern Delaware, LLC

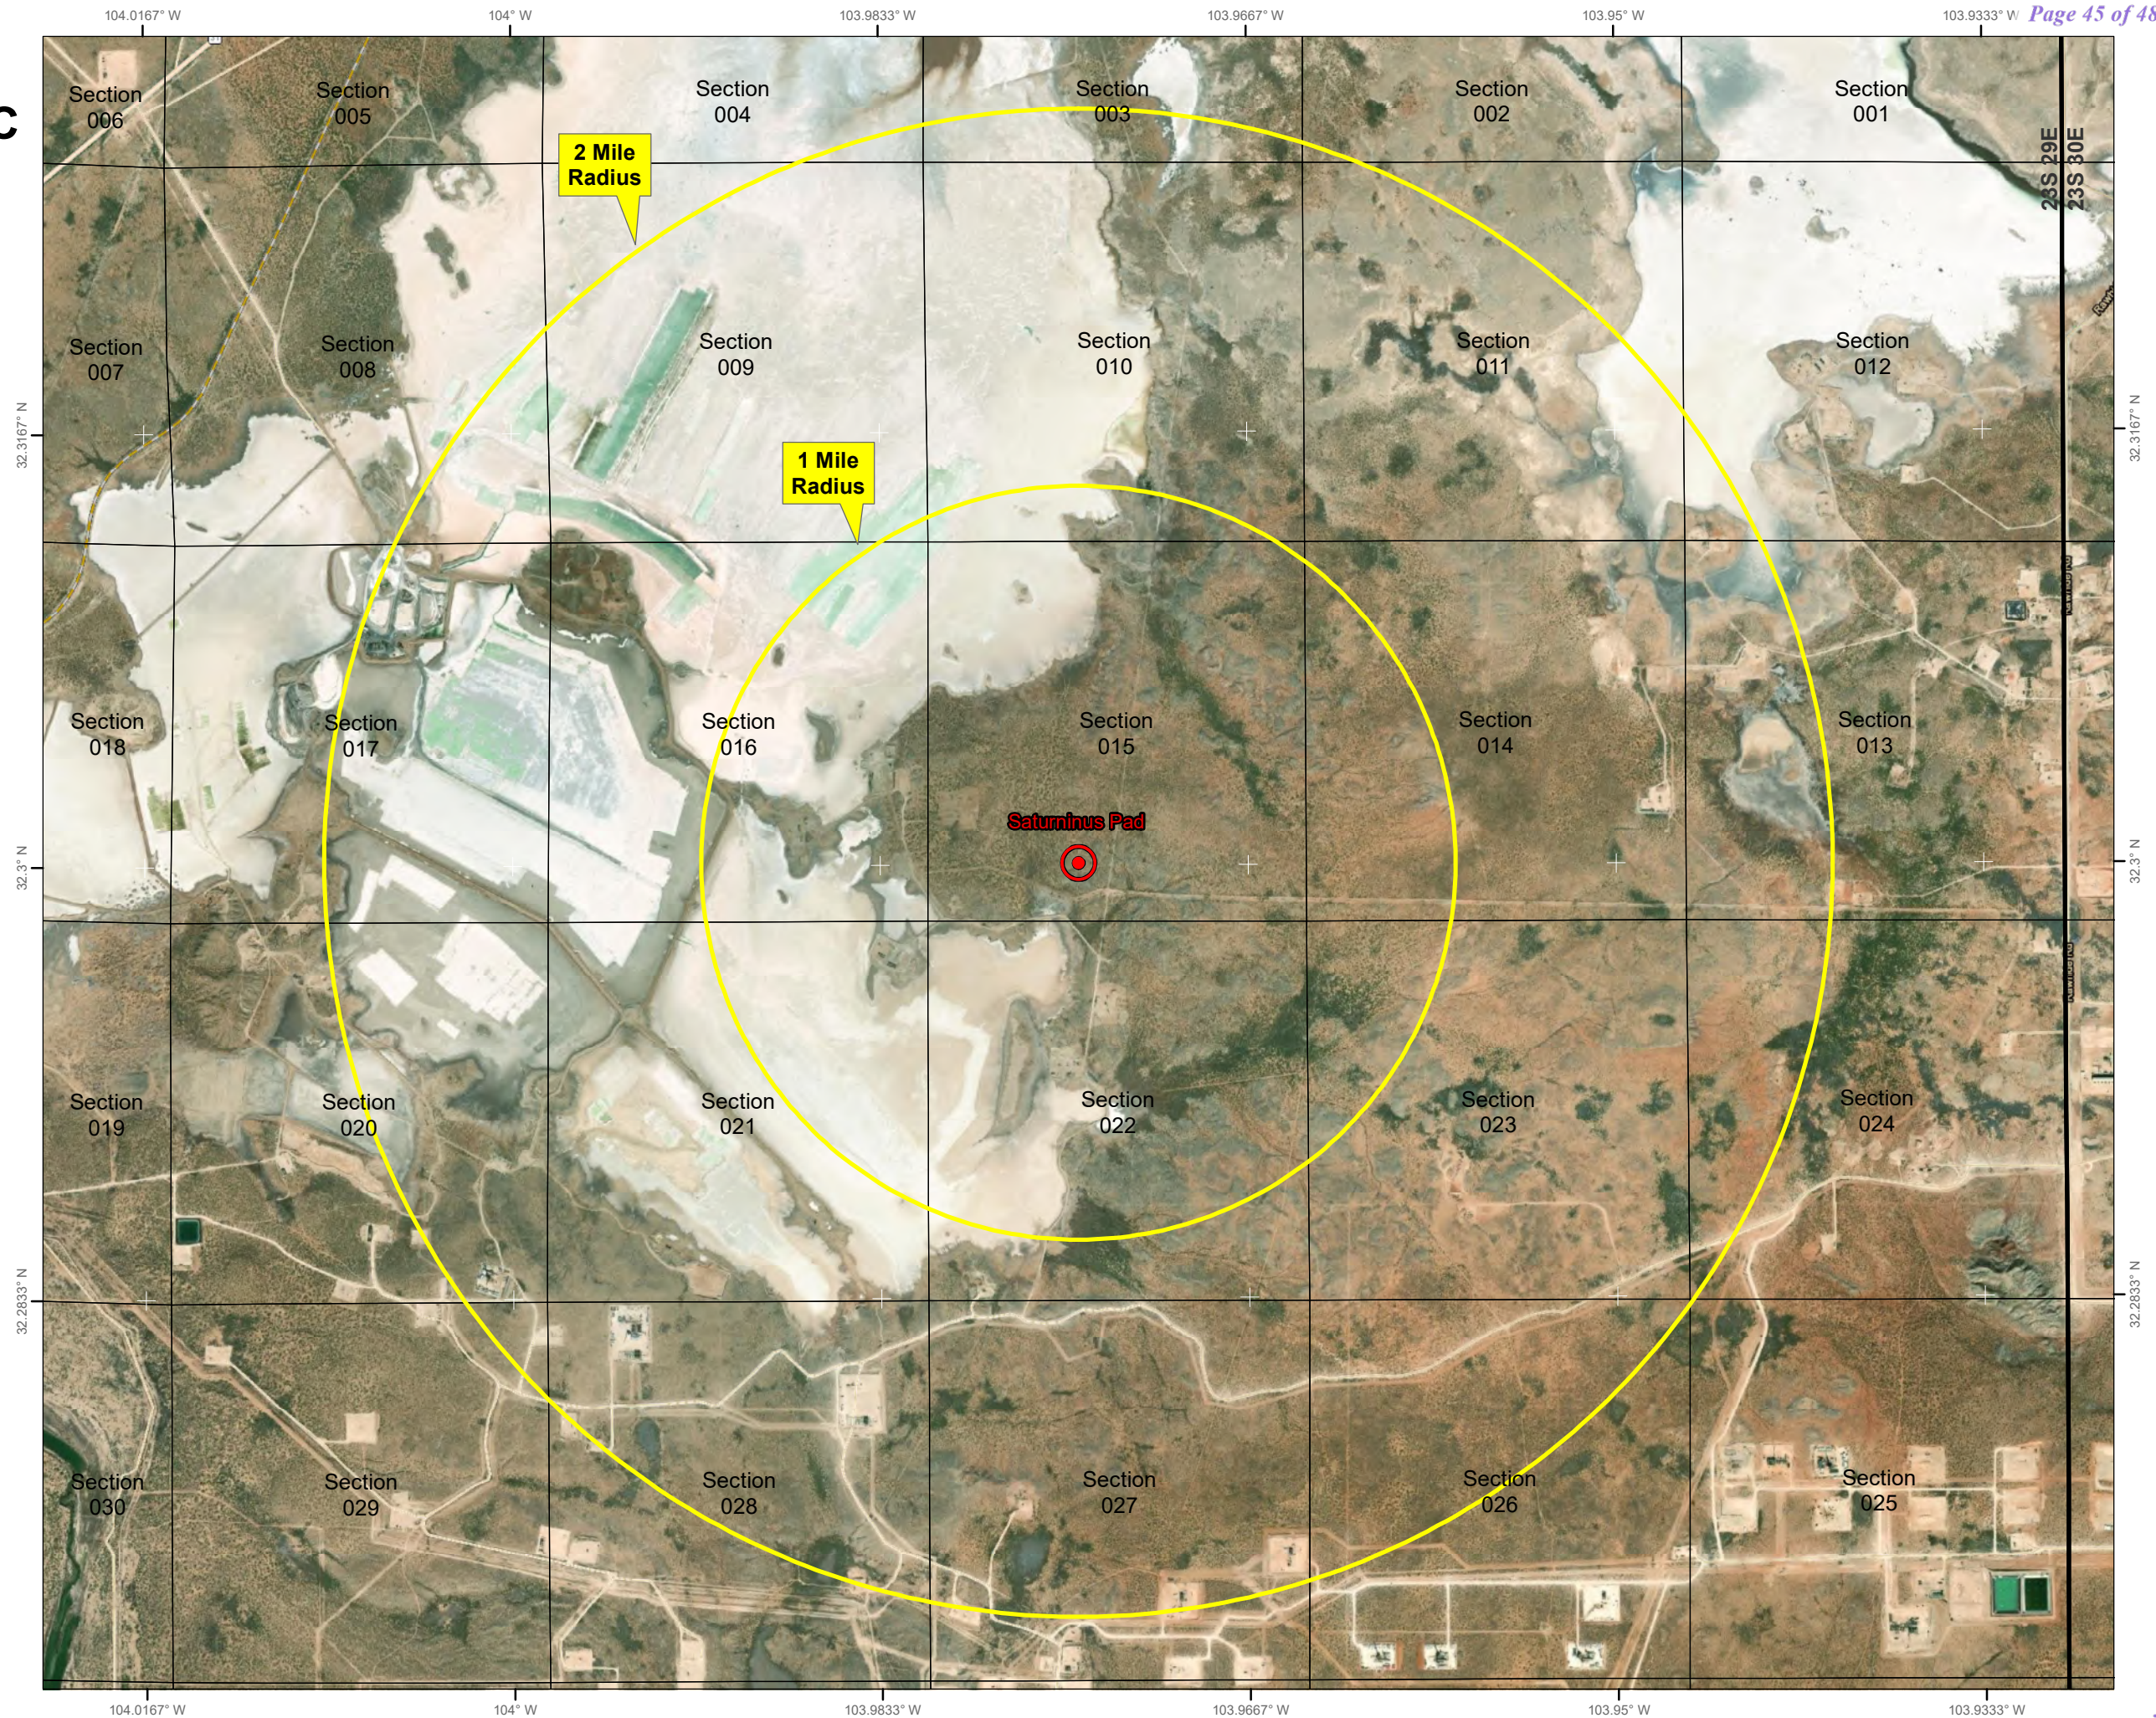

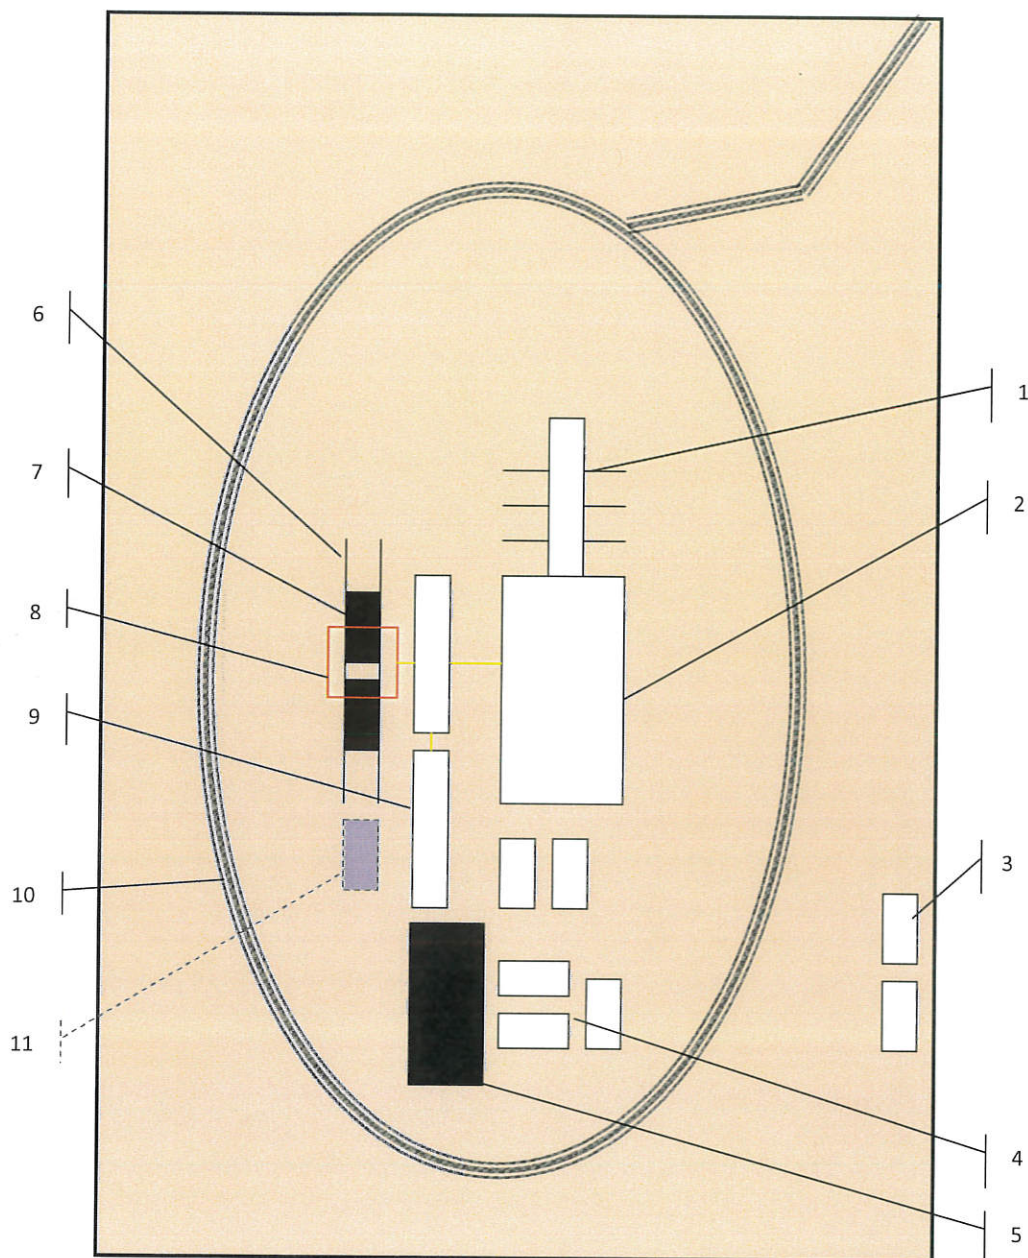

Schematic Closed Loop Drilling Rig*

1. Pipe Rack
2. Drill Rig
3. House Trailers/ Offices
4. Generator/Fuel/Storage
5. Overflow-Frac Tank
6. Skids
7. Roll Offs
8. Hopper or Centrifuge
9. Mud Tanks
10. Loop Drive
11. Generator (only for use with centrifuge)

*Not drawn to scale: Closed loop system requires at least 30 feet beyond mud tanks. Ideally 60 feet would be available

PERMITS WEST, INC.
 PROVIDING PERMITS for LAND USERS
 37Verano Loop, Santa Fe, New Mexico 87508 (505) 466-8120




Above: Centrifugal Closed Loop System



Closed Loop Drilling System: Mud tanks to right (1)
 Hopper in air to settle out solids (2)
 Water return pipe (3)
 Shaker between hopper and mud tanks (4)
 Roll offs on skids (5)

Flow Chart for Drilling Fluids and Solids

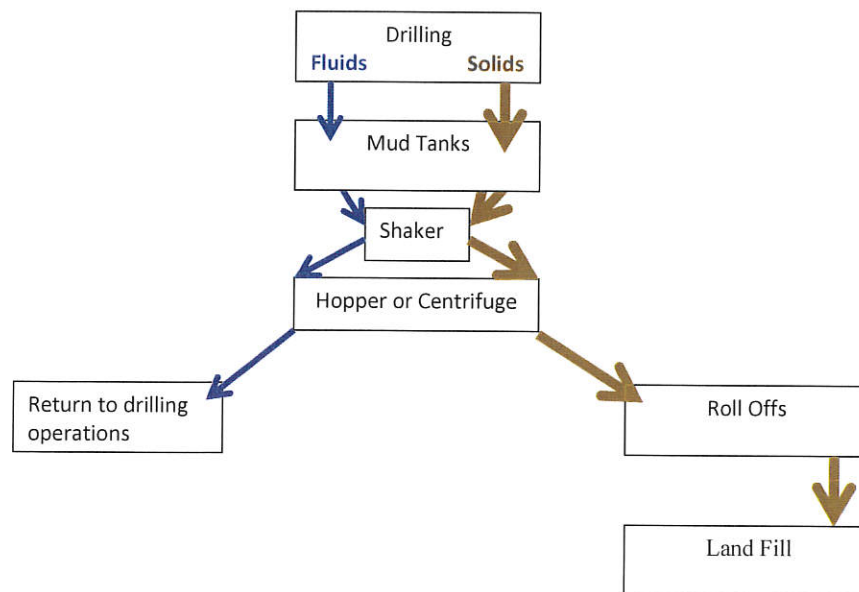

Photos Courtesy of Gandy Corporation Oil
 Field Service

PERMITS WEST, INC.
 PROVIDING PERMITS for LAND USERS
 37Verano Loop, Santa Fe, New Mexico 87508 (505) 466-8120

District I

1625 N. French Dr., Hobbs, NM 88240
 Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
 Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
 Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
 Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 83581

CONDITIONS

Operator: NOVO OIL & GAS NORTHERN DELAWARE, LLC 1001 West Wilshire Blvd Oklahoma City, OK 73116	OGRID: 372920
	Action Number: 83581
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

CONDITIONS

Created By	Condition	Condition Date
kpickford	Notify OCD 24 hours prior to casing & cement	2/28/2022
kpickford	Will require a File As Drilled C-102 and a Directional Survey with the C-104	2/28/2022
kpickford	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string	2/28/2022
kpickford	Cement is required to circulate on both surface and intermediate1 strings of casing	2/28/2022
kpickford	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system	2/28/2022
