

Office  
 District I – (575) 393-6161  
 1625 N. French Dr., Hobbs, NM 88240  
 District II – (575) 748-1283  
 811 S. First St., Artesia, NM 88210  
 District III – (505) 334-6178  
 1000 Rio Brazos Rd., Aztec, NM 87410  
 District IV – (505) 476-3460  
 1220 S. St. Francis Dr., Santa Fe, NM  
 87505

State of New Mexico  
 Energy, Minerals and Natural Resources

Form C-103  
 Revised July 18, 2013

OIL CONSERVATION DIVISION  
 1220 South St. Francis Dr.  
 Santa Fe, NM 87505

WELL API NO. 30-025-28787
5. Indicate Type of Lease STATE <input checked="" type="checkbox"/> FEE <input type="checkbox"/>
6. State Oil & Gas Lease No. E-3633
7. Lease Name or Unit Agreement Name Anderson Ranch 10 State
8. Well Number 001
9. OGRID Number 155471
10. Pool name or Wildcat Anderson Ranch Wolfcamp

SUNDRY NOTICES AND REPORTS ON WELLS (DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)	
1. Type of Well: Oil Well <input checked="" type="checkbox"/> Gas Well <input type="checkbox"/> Other <input type="checkbox"/>	
2. Name of Operator Grand Banks Energy Company	
3. Address of Operator 10 Desta Drive, Suite 300-E Midland, Texas 79705	
4. Well Location Unit Letter <u>A</u> : <u>660</u> feet from the <u>N</u> line and <u>660</u> feet from the <u>W</u> line Section <u>10</u> Township <u>16S</u> Range <u>32E</u> NMPM County <u>Lea</u>	
11. Elevation (Show whether DR, RKB, RT, GR, etc.) 4317.2 GR	

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:		SUBSEQUENT REPORT OF:	
PERFORM REMEDIAL WORK <input type="checkbox"/>	PLUG AND ABANDON <input type="checkbox"/>	REMEDIAL WORK <input type="checkbox"/>	ALTERING CASING <input type="checkbox"/>
TEMPORARILY ABANDON <input type="checkbox"/>	CHANGE PLANS <input type="checkbox"/>	COMMENCE DRILLING OPNS. <input type="checkbox"/>	<b>P AND A</b> <input checked="" type="checkbox"/> PNR
PULL OR ALTER CASING <input type="checkbox"/>	MULTIPLE COMPL <input type="checkbox"/>	CASING/CEMENT JOB <input type="checkbox"/>	
DOWNHOLE COMMINGLE <input type="checkbox"/>			
CLOSED-LOOP SYSTEM <input type="checkbox"/>			
OTHER: <input type="checkbox"/>		OTHER: <input type="checkbox"/>	

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

6/29/2022: Moved om rog amd equipment to location.  
 6/30/2022: Set large matting board and rigged up. Unseated the pump and laid down rods until end of the day.  
 7/05/2022: Finished laying rods. Dug out intermediate head and plumbed to the steel pit. Installed the BOP and released the anchor. POOH with tubing. Anchor at 249 joints. Total 298 joints of 2 7/8" tubing.  
 7/06/2022: Made guage ring run due to anchor being set 1400' above where the CIBP was to be set. Set 5.5" CIBO @ 8900'. RIH with tubing and tagged CIBP. Circulated MLF and tested casing. Good to 500#. Shut down due to thunderstorm.  
 7/07/2022: Spot 25 sx Class C on top of CIBP. TOC at 8680'. Spot 25 sx Class H across DV tool from 7535'. TOC at 7321'. Spot 25 sx Class C from 6525'. Perforated casing at 4250'. Set packer and pressured up to 500# and held. POOH with packer and spot 25 sx cement across perfs from 4304'. POOH and SION.  
 7/08/2022: Tagged cement at 4062'. Spot 25 sx cement with CaCL from 1112'. Tagged at 865'. Perforated at 550'. Squeezed with 50 sx cement with CaCl. Good circulation from intermediate head. Tagged at 394'. Circulated cement from surface from 270' with 30 sx. Shut down  
 7/11/2022: Rigged down, dug out cellar and removed the wellhead. Filled up all three strings of casing with 15 sx cement. Installed standard marker, removed the anchors and cleaned the pit. Hauled 130 bbls to SWD and 50 bbls to land fill and jetted out.

Spud Date:

Rig Release Date:

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE Socorro Hendry TITLE Regulatory Analyst DATE 07/13/2022

Type or print name Socorro Hendry E-mail address: shendry@cambridgmgmt.com PHONE: 432-620-9181

For State Use Only

APPROVED BY: Kerry Fortner TITLE Compliance Officer A DATE 7/14/22  
 Conditions of Apprc : .....

**Plugging Report  
Anderson Ranch 10 State #1  
API 30-025-28787**

6/29/2022      Moved in rig and equipment to location.

6/30/2022      Set large matting board and rigged up. Unseated the pump and laid down rods until end of the day.

7/5/2022      Finished laying rods. Dug out intermediate head and plumbed to the steel pit. Installed the BOP and released the anchor. POOH with tubing. Anchor at 249 joints. Total 298 joints of 2 7/8" tubing.

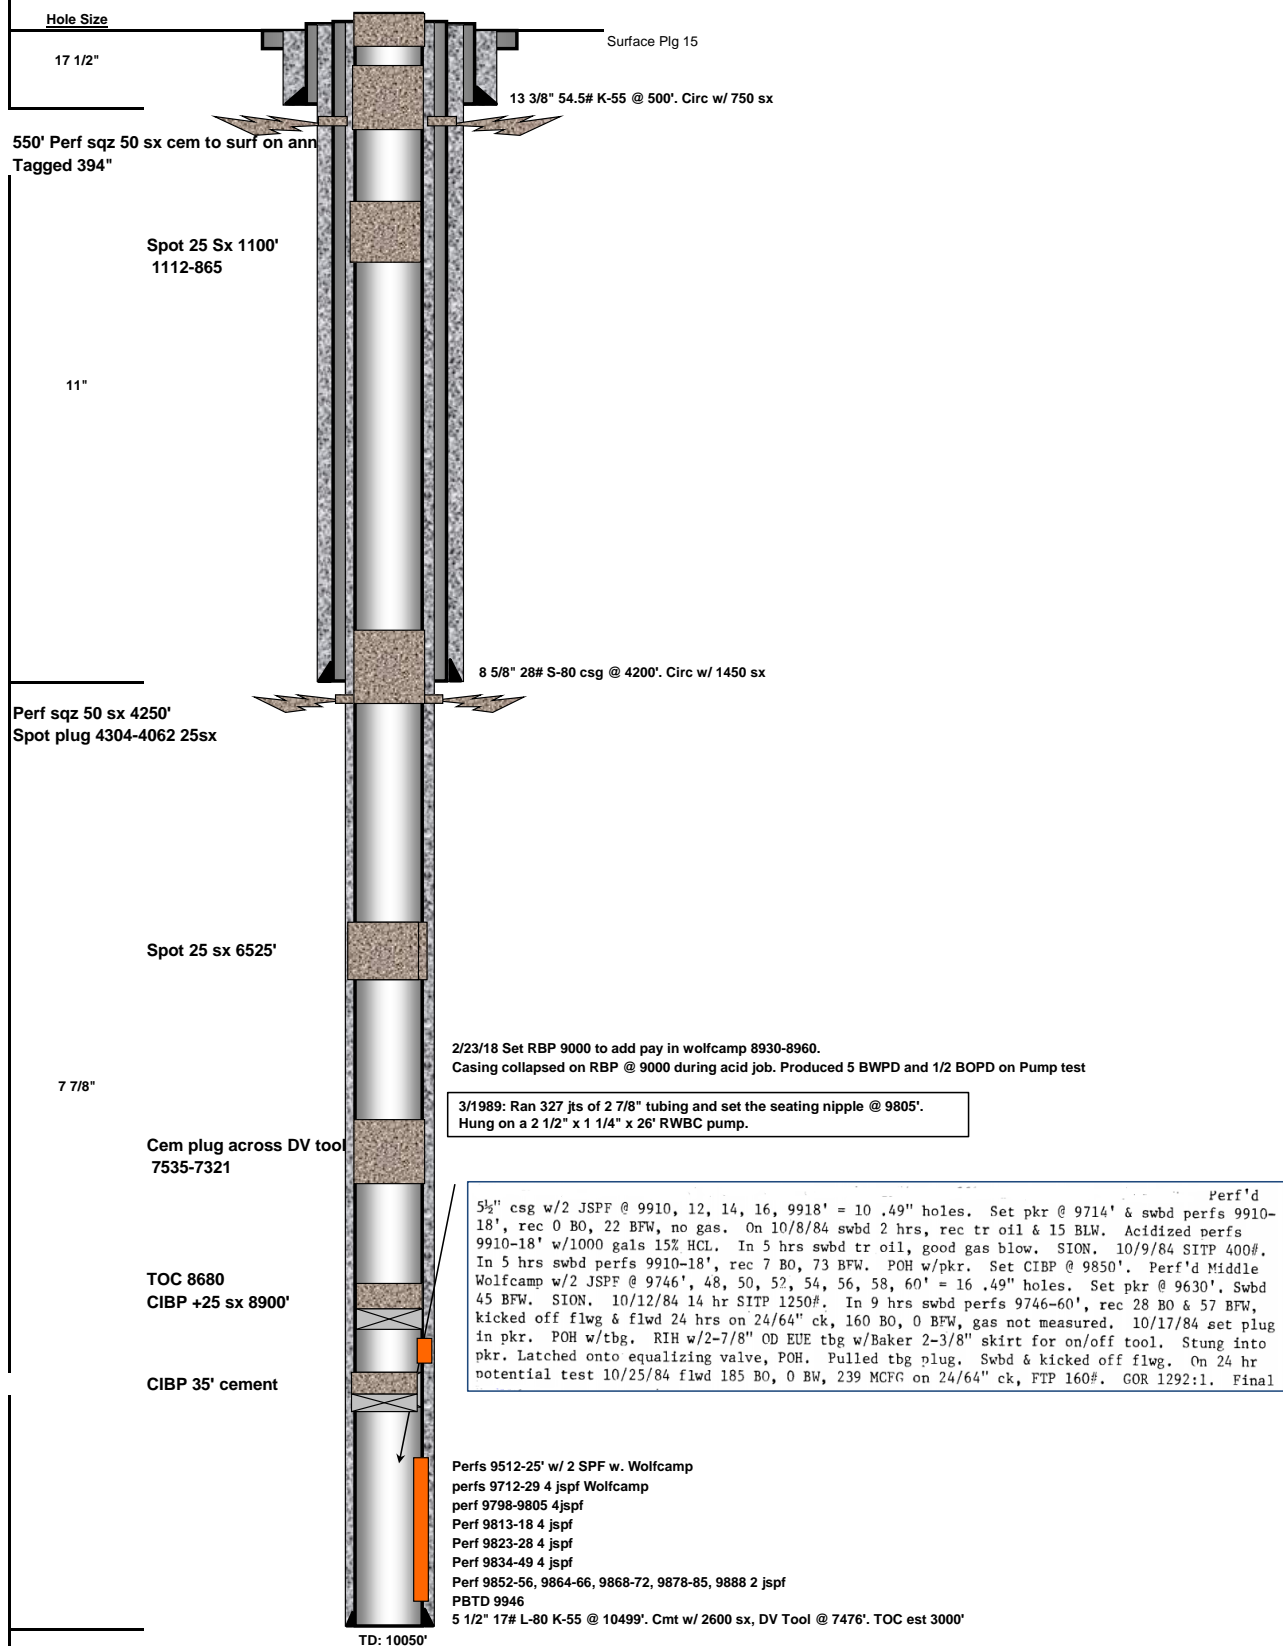
7/6/2022      Made gauge ring run due to anchor being set 1400' above where the CIBP was to be set. Set 5.5" CIBP at 8900'. RIH with tubing and tagged CIBP. Circulated MLF and tested casing. Good to 500#. Shut down due to thunderstorm.

7/7/2022      Spot 25 sx Class H on top of CIBP. TOC at 8680'. Spot 25 sx Class H across DV tool from 7535'. TOC at 7321'. Spot 25 sx Class C from 6525'. Perforated casing at 4250'. Set packer and pressured up to 500# and held. POOH with packer and spot 25 sx cement across perms from 4304'. POOH and SION.

7/8/2022      Tagged cement at 4062'. Spot 25 sx cement with CaCl from 1112'. Tagged at 865'. Perforated at 550'. Squeezed with 50 sx cement with CaCl. Good circulation from intermediate head. Tagged at 394'. Circulated cement from surface from 270' with 30 sx. Shut down.

7/11/2022      Rigged down, dug out cellar, and removed the wellhead. Filled up all three strings of casing with 15 sx cement. Installed standard marker, removed the anchors, and cleaned the pit. Hauled 130 bbls to SWD and 50 bbls to land fill and jetted out.

**Grand Banks Energy**  
**Wellbore Diagram Proposed P & A**

[illegible]

**District I**  
1625 N. French Dr., Hobbs, NM 88240  
Phone:(575) 393-6161 Fax:(575) 393-0720  
**District II**  
811 S. First St., Artesia, NM 88210  
Phone:(575) 748-1283 Fax:(575) 748-9720  
**District III**  
1000 Rio Brazos Rd., Aztec, NM 87410  
Phone:(505) 334-6178 Fax:(505) 334-6170  
**District IV**  
1220 S. St Francis Dr., Santa Fe, NM 87505  
Phone:(505) 476-3470 Fax:(505) 476-3462

**State of New Mexico**  
**Energy, Minerals and Natural Resources**  
**Oil Conservation Division**  
**1220 S. St Francis Dr.**  
**Santa Fe, NM 87505**

COMMENTS

Action 125042

COMMENTS

Operator: GRAND BANKS ENERGY CO 10 Desta Drive Midland, TX 79705	OGRID: 155471
	Action Number: 125042
	Action Type: [C-103] Sub. Plugging (C-103P)

COMMENTS

Created By	Comment	Comment Date
plmartinez	DATA ENTRY PM	7/18/2022

**District I**

1625 N. French Dr., Hobbs, NM 88240  
Phone:(575) 393-6161 Fax:(575) 393-0720

**District II**

811 S. First St., Artesia, NM 88210  
Phone:(575) 748-1283 Fax:(575) 748-9720

**District III**

1000 Rio Brazos Rd., Aztec, NM 87410  
Phone:(505) 334-6178 Fax:(505) 334-6170

**District IV**

1220 S. St Francis Dr., Santa Fe, NM 87505  
Phone:(505) 476-3470 Fax:(505) 476-3462

**State of New Mexico**  
**Energy, Minerals and Natural Resources**  
**Oil Conservation Division**  
**1220 S. St Francis Dr.**  
**Santa Fe, NM 87505**

CONDITIONS

Action 125042

## CONDITIONS

Operator: GRAND BANKS ENERGY CO 10 Desta Drive Midland, TX 79705	OGRID: 155471
	Action Number: 125042
	Action Type: [C-103] Sub. Plugging (C-103P)

## CONDITIONS

Created By	Condition	Condition Date
kfortner	Need C103Q and marker pics to release	7/14/2022
