

Well Name: PF FED COM	Well Location: T26S / R35E / SEC 1 / TR A / 32.078996 / -103.316231	County or Parish/State: LEA / NM
Well Number: 805H	Type of Well: OIL WELL	Allottee or Tribe Name:
Lease Number: NMNM117126	Unit or CA Name:	Unit or CA Number:
US Well Number: 3002549860	Well Status: Drilling Well	Operator: FRANKLIN MOUNTAIN ENERGY LLC

Notice of Intent

Sundry ID: 2672203

Type of Submission: Notice of Intent

Type of Action: APD Change

Date Sundry Submitted: 05/17/2022

Time Sundry Submitted: 02:52

Date proposed operation will begin: 05/30/2022

Procedure Description: Franklin Mountain Energy, LLC (FME), Operator, respectfully requests approval to make the following changes to the proposed drilling plan for the above referenced well: BHL Change: FME requests approval to change the BHL for this well to 150' FSL 960' FEL Sec 12 26S 35E SHL remains the same. Please see attached Plan #2, revised 14-point plan, geo prog and C-102.

NOI Attachments

Procedure Description

- C_102_PF_Fed_Com_805H_20220701114012.pdf
- FME_Federal_14_Point_Plan_PF_805_updated_psi_20220601093730.pdf
- FM__Paul_Foster_Fed_Com_805H__Plan_2_WP_RPT_20220517145202.pdf
- PF_Fed_Com_805H_GEOPROG_FINAL_20220517145202.pdf

Well Name: PF FED COM	Well Location: T26S / R35E / SEC 1 / TR A / 32.078996 / -103.316231	County or Parish/State: LEA / NM
Well Number: 805H	Type of Well: OIL WELL	Allottee or Tribe Name:
Lease Number: NMNM117126	Unit or CA Name:	Unit or CA Number:
US Well Number: 3002549860	Well Status: Drilling Well	Operator: FRANKLIN MOUNTAIN ENERGY LLC

Operator

I certify that the foregoing is true and correct. Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction. Electronic submission of Sundry Notices through this system satisfies regulations requiring a

Operator Electronic Signature: RACHAEL OVERBEY
Signed on: JUL 01, 2022 11:40 AM
Name: FRANKLIN MOUNTAIN ENERGY LLC
Title: Director – Operations Planning and Regulatory
Street Address: 2401 E 2nd Avenue, Suite 300
City: Denver **State:** CO
Phone: (720) 414-7868
Email address: roverbey@fmellc.com

Field

Representative Name:
Street Address:
City: **State:** **Zip:**
Phone:
Email address:

BLM Point of Contact

BLM POC Name: CHRISTOPHER WALLS
BLM POC Phone: 5752342234
Disposition: Approved
Signature: Chris Walls
BLM POC Title: Petroleum Engineer
BLM POC Email Address: cwalls@blm.gov
Disposition Date: 08/01/2022

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office

☒ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-025-49860	² Pool Code 98288	³ Pool Name WC-025 G-09 S253536D; UPR WOLFCAMP
⁴ Property Code 332687	⁵ Property Name PAUL FOSTER FED COM	⁶ Well Number 805H
⁷ OGRID No. 373910	⁸ Operator Name FRANKLIN MOUNTAIN ENERGY LLC	⁹ Elevation 3031.8'


¹⁰ Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
A	1	26S	35E		210	NORTH	1087	EAST	LEA

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
P	12	26S	35E		150	SOUTH	960	EAST	LEA
¹² Dedicated Acres 640	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.						

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

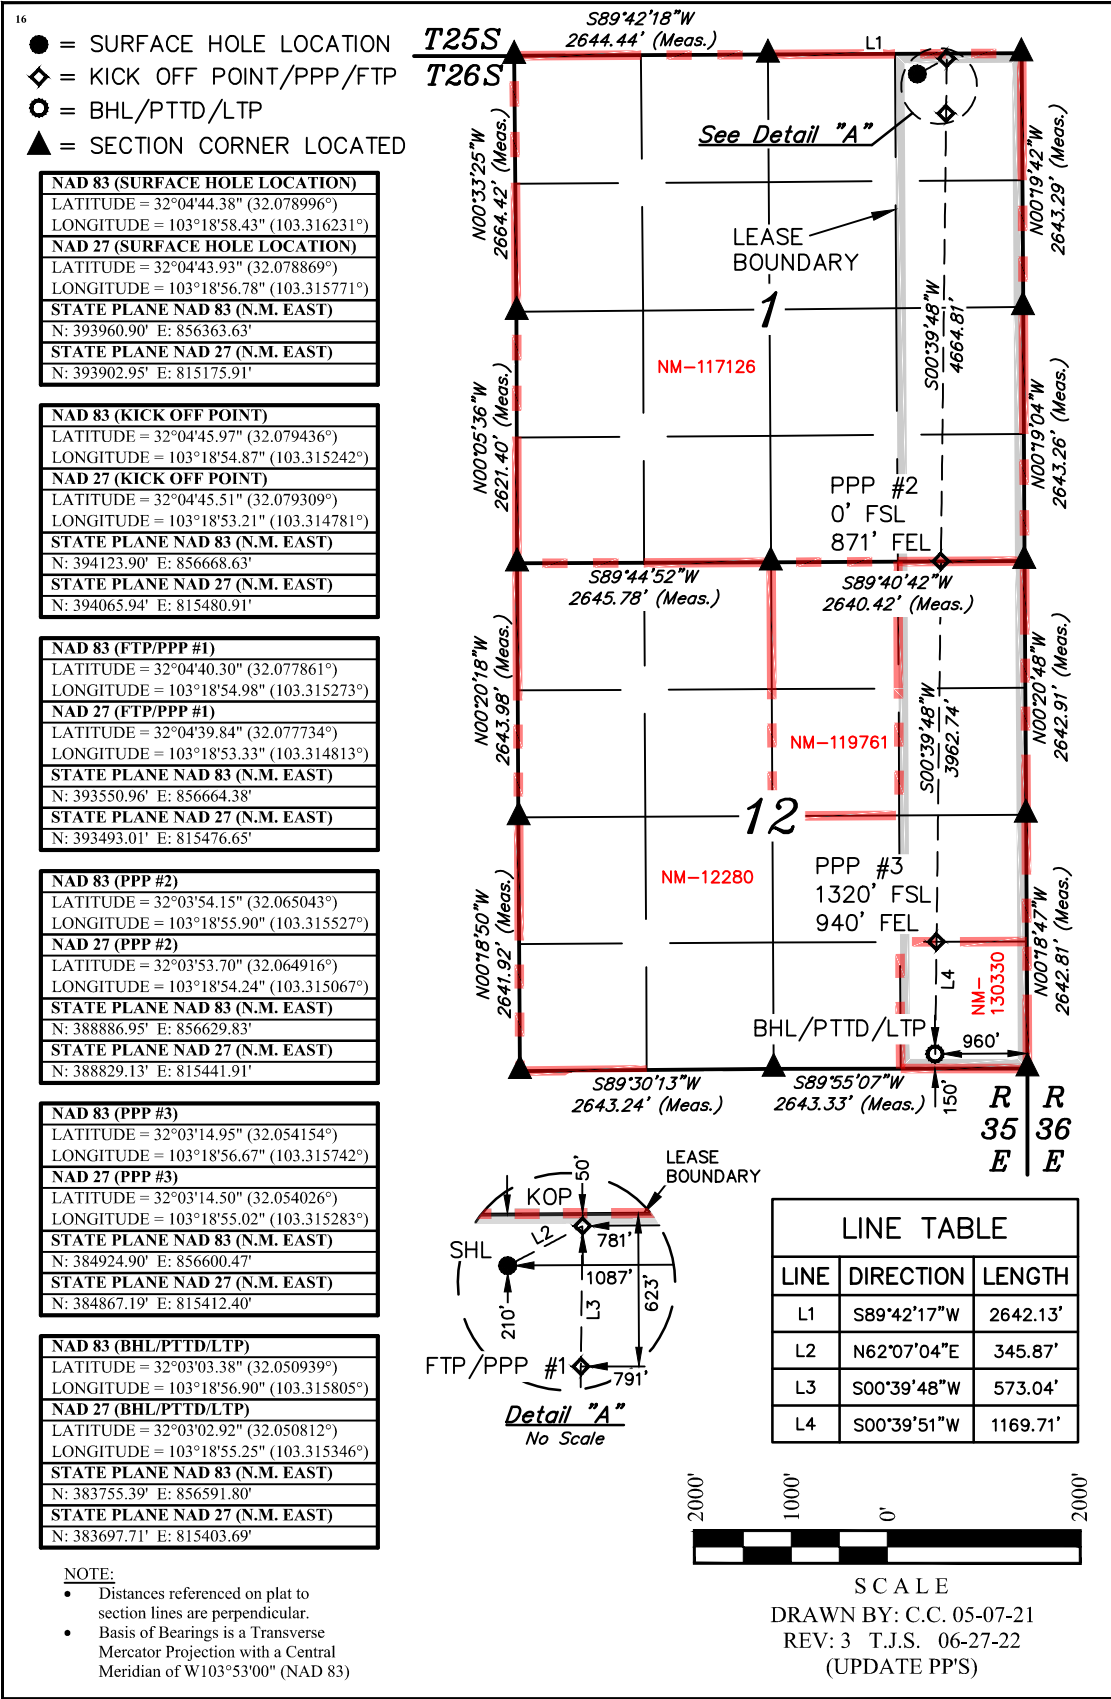

¹⁷ OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Signature: *Rachael Overbey* Date: 7/1/2022

Printed Name: Rachael Overbey

E-mail Address: roverbey@fmellc.com

¹⁸ SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

April 28, 2021

Date of Survey

Signature and Seal of Professional Surveyor:

Paul Buchele

PAUL BUCHELE
NEW MEXICO
23782
06-27-22
PROFESSIONAL SURVEYOR

Certificate Number:

Released to Imaging: 8/3/2022 1:29:19 PM

Franklin Mountain Energy

Project: Lea County, NM (NAD83)
Site: PF Fed Com
Well: Paul Foster Fed Com 805H
Wellbore: OH
Design: Plan #2



Azimuths to Grid North
True North: -0.54°
Magnetic North: 5.86°
Magnetic Field
Strength: 47427.4nT
Dip Angle: 59.80°
Date: 7/16/2021
Model: IGRF2020





PROJECT DETAILS: Lea County, NM (NAD83)
Geodetic System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone: New Mexico Eastern Zone

DESIGN TARGET DETAILS

Name	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
LP P2 (PF Fed Com 805H)	12299.00	-409.94	300.76	393551.08	856664.49	32.0778615	-103.3152726
PBHL P2 (PF Fed Com 805H)	12299.00	-10205.81	228.19	383755.22	856591.93	32.0509390	-103.3158050
SHL (PF Fed Com 805H)	0.00	0.00	0.00	393961.02	856363.73	32.0789960	-103.3162310

SECTION DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSec	Annotation
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
2200.00	0.00	0.00	2200.00	0.00	0.00	0.00	0.00	0.00	Start Build 1.50
2483.86	4.26	61.88	2483.60	4.97	9.30	1.50	61.88	-4.76	Start 4373.88 hold at 2483.86 MD
6857.74	4.26	61.88	6845.40	158.03	295.70	0.00	0.00	-151.38	Start Drop -1.50
7141.59	0.00	0.00	7129.00	163.00	305.00	1.50	180.00	-156.14	Start 4597.04 hold at 7141.59 MD
11738.64	0.00	0.00	11726.04	163.00	305.00	0.00	0.00	-156.14	Start Build 10.00
12638.64	90.00	180.42	12299.00	-409.94	300.76	10.00	180.42	416.56	Start 9796.14 hold at 12638.64 MD
22434.77	90.00	180.42	12299.00	-10205.81	228.19	0.00	0.00	0208.36	TD at 22434.77

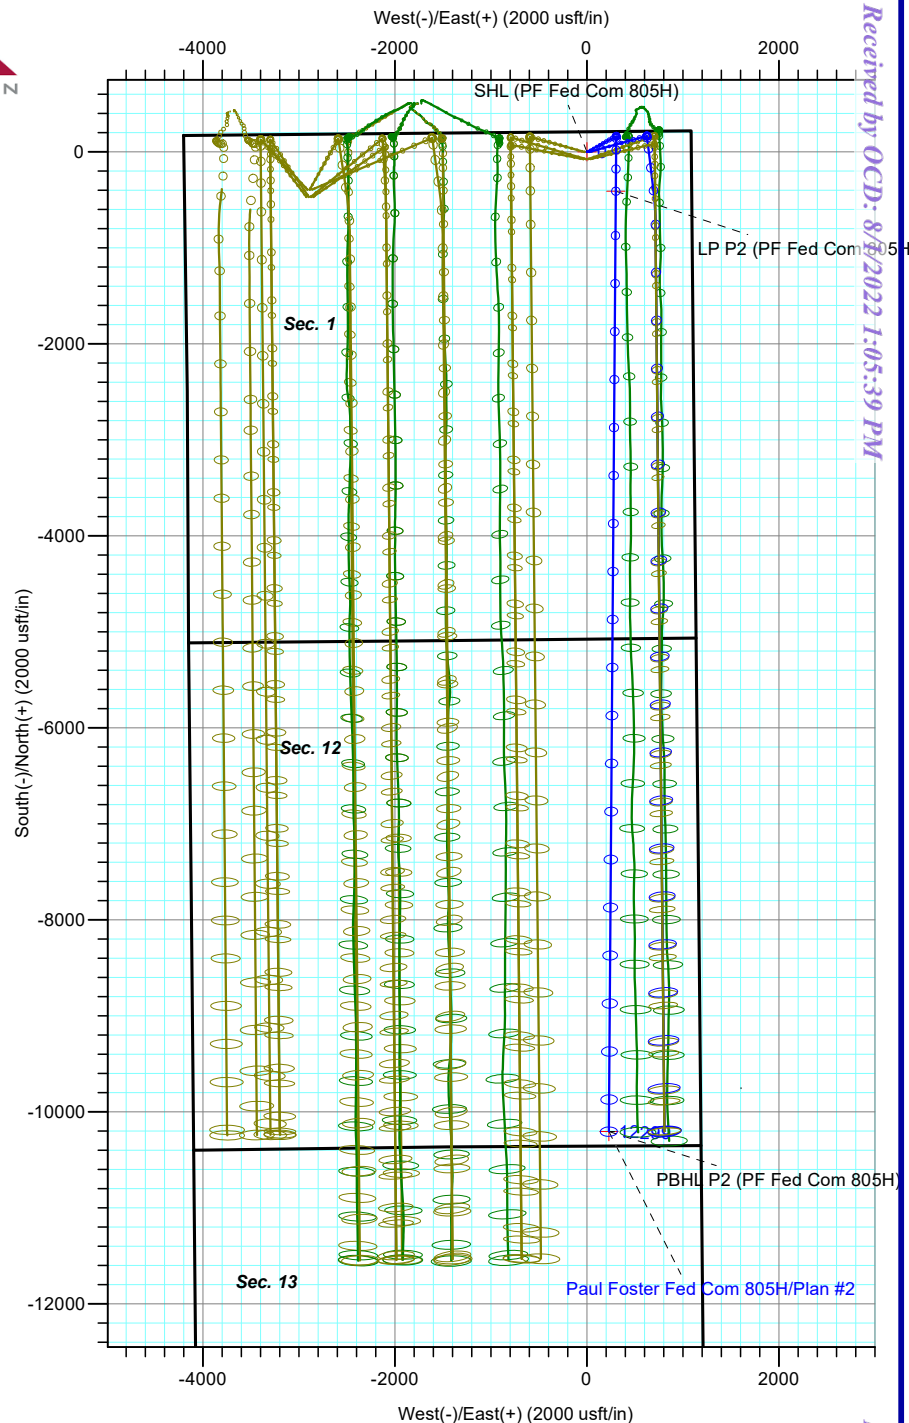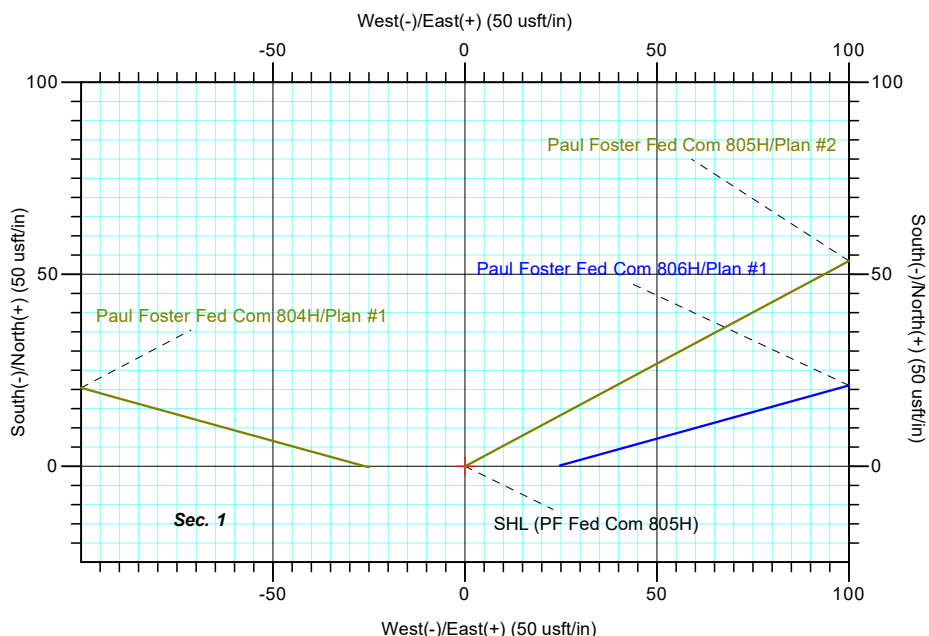

TOTAL DIRECTIONAL SERVICES LLC
671 Academy Ct, Windsor, CO 80550
Phone: (970) 460-9402


Plan: Plan #2 (Paul Foster Fed Com 805H/OH)
PF Fed Com
Created By: RDW
Date: 15:09, May 16 2022
Approved: _____
Date: _____

Received by OCD: 8/3/2022 1:05:39 PM

Page 4 of 22

Franklin Mountain Energy

Project: Lea County, NM (NAD83)
Site: PF Fed Com
Well: Paul Foster Fed Com 805H
Wellbore: OH
Design: Plan #2




Azimuths to Grid North
True North: -0.54°
Magnetic North: 5.86°

Magnetic Field
Strength: 47427.4nT
Dip Angle: 59.80°
Date: 7/16/2021
Model: IGRF2020

PROJECT DETAILS: Lea County, NM (NAD83)

Geodetic System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone: New Mexico Eastern Zone


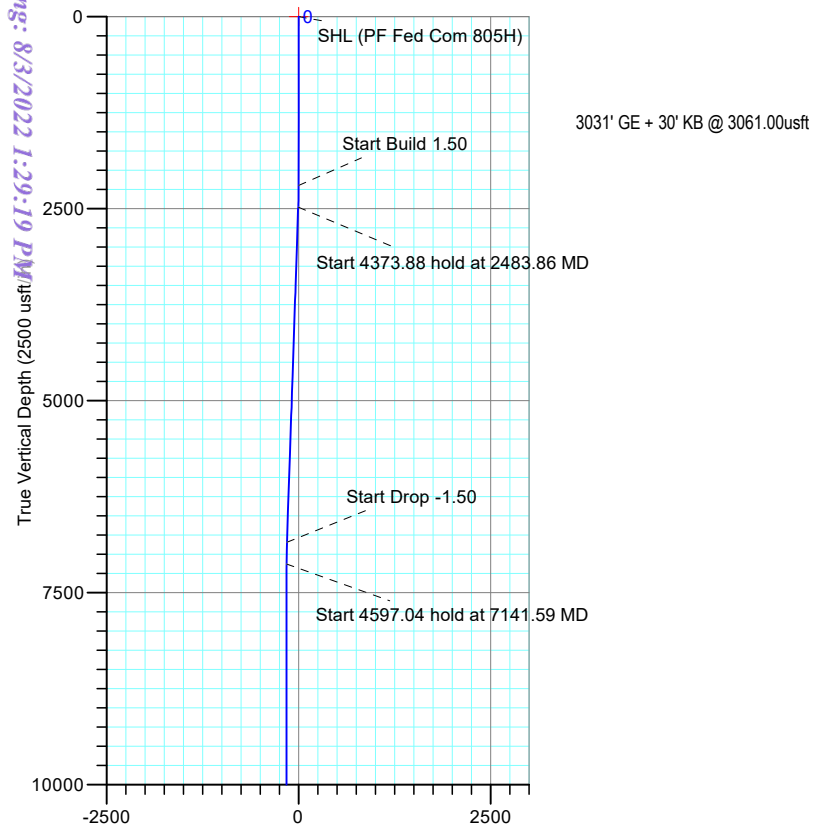


SECTION DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	Vsect	Annotation
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
2200.00	0.00	0.00	2200.00	0.00	0.00	0.00	0.00	0.00	Start Build 1.50
2483.86	4.26	61.88	2483.60	4.97	9.30	1.50	61.88	-4.76	Start 4373.88 hold at 2483.86 MD
6857.74	4.26	61.88	6845.40	158.03	295.70	0.00	0.00	-151.38	Start Drop -1.50
7141.59	0.00	0.00	7129.00	163.00	305.00	1.50	180.00	-156.14	Start 4597.04 hold at 7141.59 MD
11738.64	0.00	0.00	11726.04	163.00	305.00	0.00	0.00	-156.14	Start Build 10.00
12638.64	90.00	180.42	12299.00	-409.94	300.76	10.00	180.42	416.56	Start 9796.14 hold at 12638.64 MD
22434.77	90.00	180.42	22299.00	10205.81	228.19	0.00	0.00	10208.36	TD at 22434.77

DESIGN TARGET DETAILS

Name	TVD	+N/-S	+E/-W	Latitude	Longitude
LP P2 (PF Fed Com 805H)	12299.00	-409.94	300.76	32.0778615	-103.3152726
PBHL P2 (PF Fed Com 805H)	12299.00	10205.81	228.19	32.0509390	-103.3158050
SHL (PF Fed Com 805H)	0.00	0.00	0.00	32.0789960	-103.3162310

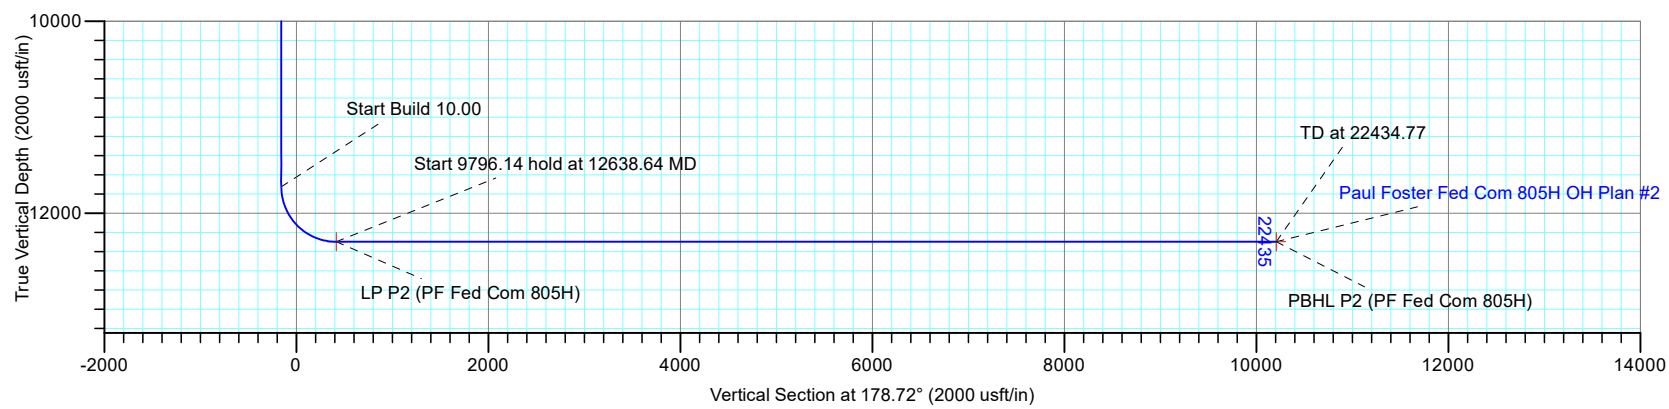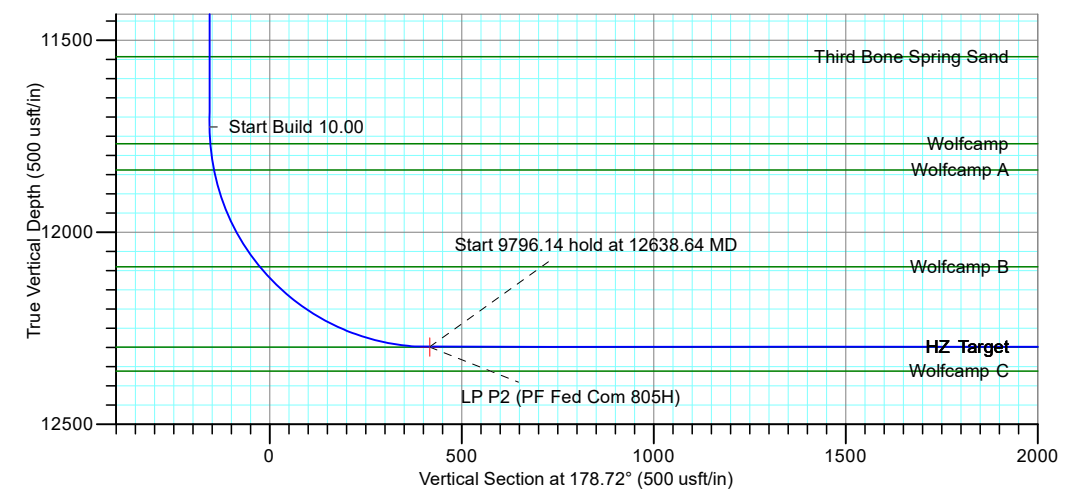

TOTAL DIRECTIONAL SERVICES LLC
671 Academy Ct, Windsor, CO 80550
Phone: (970) 460-9402

Plan: Plan #2 (Paul Foster Fed Com 805H/OH)
PF Fed Com
Created By: RDW
Date: 15:11, May 16 2022
Approved: _____
Date: _____



Franklin Mountain Energy

Lea County, NM (NAD83)

PF Fed Com

Paul Foster Fed Com 805H

OH

Plan: Plan #2

Standard Planning Report

16 May, 2022





Planning Report



Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Paul Foster Fed Com 805H
Company:	Franklin Mountain Energy	TVD Reference:	3031' GE + 30' KB @ 3061.00usft
Project:	Lea County, NM (NAD83)	MD Reference:	3031' GE + 30' KB @ 3061.00usft
Site:	PF Fed Com	North Reference:	Grid
Well:	Paul Foster Fed Com 805H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #2		

Project	Lea County, NM (NAD83)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	PF Fed Com		
Site Position:		Northing:	393,493.72 usft
From:	Lat/Long	Easting:	853,440.15 usft
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16 "
		Latitude:	32.0777870
		Longitude:	-103.3256830

Well	Paul Foster Fed Com 805H		
Well Position	+N/-S	0.00 usft	Northing: 393,961.02 usft
	+E/-W	0.00 usft	Easting: 856,363.73 usft
Position Uncertainty	0.00 usft	Wellhead Elevation:	usft
Grid Convergence:	0.54 °	Ground Level:	3,031.00 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	7/16/2021	6.41	59.80	47,427.41136823

Design	Plan #2				
Audit Notes:					
Version:	Phase:	PLAN	Tie On Depth:	0.00	
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)	
	0.00	0.00	0.00	178.72	

Plan Survey Tool Program	Date	5/16/2022			
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks	
1	0.00	22,434.77 Plan #2 (OH)	OWSG (Rev2) MWD+IFR1		
			OWSG MWD + IFR1 + Mult		

Plan Sections											
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target	
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		
2,200.00	0.00	0.00	2,200.00	0.00	0.00	0.00	0.00	0.00	0.00		
2,483.86	4.26	61.88	2,483.60	4.97	9.30	1.50	1.50	0.00	61.88		
6,857.74	4.26	61.88	6,845.40	158.03	295.70	0.00	0.00	0.00	0.00		
7,141.59	0.00	0.00	7,129.00	163.00	305.00	1.50	-1.50	0.00	180.00		
11,738.64	0.00	0.00	11,726.04	163.00	305.00	0.00	0.00	0.00	0.00		
12,638.64	90.00	180.42	12,299.00	-409.94	300.76	10.00	10.00	0.00	180.42		
22,434.77	90.00	180.42	12,299.00	-10,205.81	228.19	0.00	0.00	0.00	0.00	PBHL P2 (PF Fed C	



Planning Report



Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Paul Foster Fed Com 805H
Company:	Franklin Mountain Energy	TVD Reference:	3031' GE + 30' KB @ 3061.00usft
Project:	Lea County, NM (NAD83)	MD Reference:	3031' GE + 30' KB @ 3061.00usft
Site:	PF Fed Com	North Reference:	Grid
Well:	Paul Foster Fed Com 805H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
30.00	0.00	0.00	30.00	0.00	0.00	0.00	0.00	0.00	0.00
Cenozoic Alluvium (surface)									
100.00	0.00	0.00	100.00	0.00	0.00	0.00	0.00	0.00	0.00
200.00	0.00	0.00	200.00	0.00	0.00	0.00	0.00	0.00	0.00
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00
388.00	0.00	0.00	388.00	0.00	0.00	0.00	0.00	0.00	0.00
Rustler									
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00	0.00
500.00	0.00	0.00	500.00	0.00	0.00	0.00	0.00	0.00	0.00
600.00	0.00	0.00	600.00	0.00	0.00	0.00	0.00	0.00	0.00
700.00	0.00	0.00	700.00	0.00	0.00	0.00	0.00	0.00	0.00
800.00	0.00	0.00	800.00	0.00	0.00	0.00	0.00	0.00	0.00
900.00	0.00	0.00	900.00	0.00	0.00	0.00	0.00	0.00	0.00
1,000.00	0.00	0.00	1,000.00	0.00	0.00	0.00	0.00	0.00	0.00
1,100.00	0.00	0.00	1,100.00	0.00	0.00	0.00	0.00	0.00	0.00
1,200.00	0.00	0.00	1,200.00	0.00	0.00	0.00	0.00	0.00	0.00
1,300.00	0.00	0.00	1,300.00	0.00	0.00	0.00	0.00	0.00	0.00
1,400.00	0.00	0.00	1,400.00	0.00	0.00	0.00	0.00	0.00	0.00
1,500.00	0.00	0.00	1,500.00	0.00	0.00	0.00	0.00	0.00	0.00
1,600.00	0.00	0.00	1,600.00	0.00	0.00	0.00	0.00	0.00	0.00
1,700.00	0.00	0.00	1,700.00	0.00	0.00	0.00	0.00	0.00	0.00
1,800.00	0.00	0.00	1,800.00	0.00	0.00	0.00	0.00	0.00	0.00
1,879.00	0.00	0.00	1,879.00	0.00	0.00	0.00	0.00	0.00	0.00
Salado									
1,900.00	0.00	0.00	1,900.00	0.00	0.00	0.00	0.00	0.00	0.00
2,000.00	0.00	0.00	2,000.00	0.00	0.00	0.00	0.00	0.00	0.00
2,100.00	0.00	0.00	2,100.00	0.00	0.00	0.00	0.00	0.00	0.00
2,200.00	0.00	0.00	2,200.00	0.00	0.00	0.00	0.00	0.00	0.00
Start Build 1.50									
2,300.00	1.50	61.88	2,299.99	0.62	1.15	-0.59	1.50	1.50	0.00
2,400.00	3.00	61.88	2,399.91	2.47	4.62	-2.36	1.50	1.50	0.00
2,483.86	4.26	61.88	2,483.60	4.97	9.30	-4.76	1.50	1.50	0.00
Start 4373.88 hold at 2483.86 MD									
2,500.00	4.26	61.88	2,499.69	5.53	10.35	-5.30	0.00	0.00	0.00
2,600.00	4.26	61.88	2,599.42	9.03	16.90	-8.65	0.00	0.00	0.00
2,700.00	4.26	61.88	2,699.14	12.53	23.45	-12.01	0.00	0.00	0.00
2,800.00	4.26	61.88	2,798.87	16.03	30.00	-15.36	0.00	0.00	0.00
2,900.00	4.26	61.88	2,898.59	19.53	36.55	-18.71	0.00	0.00	0.00
3,000.00	4.26	61.88	2,998.31	23.03	43.10	-22.06	0.00	0.00	0.00
3,062.86	4.26	61.88	3,061.00	25.23	47.21	-24.17	0.00	0.00	0.00
Potential Losses - Capitan									
3,094.95	4.26	61.88	3,093.00	26.35	49.31	-25.24	0.00	0.00	0.00
Base Salt									
3,100.00	4.26	61.88	3,098.04	26.53	49.64	-25.41	0.00	0.00	0.00
3,200.00	4.26	61.88	3,197.76	30.03	56.19	-28.77	0.00	0.00	0.00
3,300.00	4.26	61.88	3,297.49	33.53	62.74	-32.12	0.00	0.00	0.00
3,400.00	4.26	61.88	3,397.21	37.03	69.29	-35.47	0.00	0.00	0.00
3,500.00	4.26	61.88	3,496.93	40.53	75.84	-38.82	0.00	0.00	0.00
3,600.00	4.26	61.88	3,596.66	44.03	82.38	-42.18	0.00	0.00	0.00
3,700.00	4.26	61.88	3,696.38	47.53	88.93	-45.53	0.00	0.00	0.00
3,800.00	4.26	61.88	3,796.11	51.03	95.48	-48.88	0.00	0.00	0.00
3,900.00	4.26	61.88	3,895.83	54.53	102.03	-52.23	0.00	0.00	0.00



Planning Report



Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Paul Foster Fed Com 805H
Company:	Franklin Mountain Energy	TVD Reference:	3031' GE + 30' KB @ 3061.00usft
Project:	Lea County, NM (NAD83)	MD Reference:	3031' GE + 30' KB @ 3061.00usft
Site:	PF Fed Com	North Reference:	Grid
Well:	Paul Foster Fed Com 805H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
4,000.00	4.26	61.88	3,995.55	58.03	108.58	-55.58	0.00	0.00	0.00
4,100.00	4.26	61.88	4,095.28	61.53	115.12	-58.94	0.00	0.00	0.00
4,200.00	4.26	61.88	4,195.00	65.02	121.67	-62.29	0.00	0.00	0.00
4,300.00	4.26	61.88	4,294.73	68.52	128.22	-65.64	0.00	0.00	0.00
4,400.00	4.26	61.88	4,394.45	72.02	134.77	-68.99	0.00	0.00	0.00
4,500.00	4.26	61.88	4,494.17	75.52	141.32	-72.35	0.00	0.00	0.00
4,600.00	4.26	61.88	4,593.90	79.02	147.86	-75.70	0.00	0.00	0.00
4,700.00	4.26	61.88	4,693.62	82.52	154.41	-79.05	0.00	0.00	0.00
4,800.00	4.26	61.88	4,793.35	86.02	160.96	-82.40	0.00	0.00	0.00
4,900.00	4.26	61.88	4,893.07	89.52	167.51	-85.75	0.00	0.00	0.00
4,940.04	4.26	61.88	4,933.00	90.92	170.13	-87.10	0.00	0.00	0.00
Lamar									
5,000.00	4.26	61.88	4,992.79	93.02	174.06	-89.11	0.00	0.00	0.00
5,029.29	4.26	61.88	5,022.00	94.05	175.97	-90.09	0.00	0.00	0.00
Bell Canyon									
5,100.00	4.26	61.88	5,092.52	96.52	180.60	-92.46	0.00	0.00	0.00
5,200.00	4.26	61.88	5,192.24	100.02	187.15	-95.81	0.00	0.00	0.00
5,300.00	4.26	61.88	5,291.97	103.52	193.70	-99.16	0.00	0.00	0.00
5,400.00	4.26	61.88	5,391.69	107.02	200.25	-102.52	0.00	0.00	0.00
5,500.00	4.26	61.88	5,491.41	110.52	206.80	-105.87	0.00	0.00	0.00
5,600.00	4.26	61.88	5,591.14	114.02	213.34	-109.22	0.00	0.00	0.00
5,700.00	4.26	61.88	5,690.86	117.52	219.89	-112.57	0.00	0.00	0.00
5,800.00	4.26	61.88	5,790.59	121.02	226.44	-115.92	0.00	0.00	0.00
5,859.58	4.26	61.88	5,850.00	123.10	230.34	-117.92	0.00	0.00	0.00
Cherry Canyon									
5,900.00	4.26	61.88	5,890.31	124.52	232.99	-119.28	0.00	0.00	0.00
6,000.00	4.26	61.88	5,990.03	128.01	239.54	-122.63	0.00	0.00	0.00
6,100.00	4.26	61.88	6,089.76	131.51	246.09	-125.98	0.00	0.00	0.00
6,200.00	4.26	61.88	6,189.48	135.01	252.63	-129.33	0.00	0.00	0.00
6,300.00	4.26	61.88	6,289.21	138.51	259.18	-132.68	0.00	0.00	0.00
6,400.00	4.26	61.88	6,388.93	142.01	265.73	-136.04	0.00	0.00	0.00
6,500.00	4.26	61.88	6,488.65	145.51	272.28	-139.39	0.00	0.00	0.00
6,600.00	4.26	61.88	6,588.38	149.01	278.83	-142.74	0.00	0.00	0.00
6,700.00	4.26	61.88	6,688.10	152.51	285.37	-146.09	0.00	0.00	0.00
6,800.00	4.26	61.88	6,787.83	156.01	291.92	-149.45	0.00	0.00	0.00
6,857.74	4.26	61.88	6,845.40	158.03	295.70	-151.38	0.00	0.00	0.00
Start Drop -1.50									
6,900.00	3.62	61.88	6,887.57	159.40	298.26	-152.69	1.50	-1.50	0.00
7,000.00	2.12	61.88	6,987.44	161.76	302.69	-154.96	1.50	-1.50	0.00
7,100.00	0.62	61.88	7,087.41	162.89	304.80	-156.04	1.50	-1.50	0.00
7,141.59	0.00	0.00	7,129.00	163.00	305.00	-156.14	1.50	-1.50	0.00
Start 4597.04 hold at 7141.59 MD									
7,200.00	0.00	0.00	7,187.41	163.00	305.00	-156.14	0.00	0.00	0.00
7,300.00	0.00	0.00	7,287.41	163.00	305.00	-156.14	0.00	0.00	0.00
7,310.59	0.00	0.00	7,298.00	163.00	305.00	-156.14	0.00	0.00	0.00
Brushy Canyon									
7,400.00	0.00	0.00	7,387.41	163.00	305.00	-156.14	0.00	0.00	0.00
7,500.00	0.00	0.00	7,487.41	163.00	305.00	-156.14	0.00	0.00	0.00
7,600.00	0.00	0.00	7,587.41	163.00	305.00	-156.14	0.00	0.00	0.00
7,700.00	0.00	0.00	7,687.41	163.00	305.00	-156.14	0.00	0.00	0.00
7,800.00	0.00	0.00	7,787.41	163.00	305.00	-156.14	0.00	0.00	0.00
7,900.00	0.00	0.00	7,887.41	163.00	305.00	-156.14	0.00	0.00	0.00
8,000.00	0.00	0.00	7,987.41	163.00	305.00	-156.14	0.00	0.00	0.00



Planning Report



Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Paul Foster Fed Com 805H
Company:	Franklin Mountain Energy	TVD Reference:	3031' GE + 30' KB @ 3061.00usft
Project:	Lea County, NM (NAD83)	MD Reference:	3031' GE + 30' KB @ 3061.00usft
Site:	PF Fed Com	North Reference:	Grid
Well:	Paul Foster Fed Com 805H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
8,100.00	0.00	0.00	8,087.41	163.00	305.00	-156.14	0.00	0.00	0.00
8,200.00	0.00	0.00	8,187.41	163.00	305.00	-156.14	0.00	0.00	0.00
8,300.00	0.00	0.00	8,287.41	163.00	305.00	-156.14	0.00	0.00	0.00
8,400.00	0.00	0.00	8,387.41	163.00	305.00	-156.14	0.00	0.00	0.00
8,500.00	0.00	0.00	8,487.41	163.00	305.00	-156.14	0.00	0.00	0.00
8,503.59	0.00	0.00	8,491.00	163.00	305.00	-156.14	0.00	0.00	0.00
Bone Spring Lime									
8,557.59	0.00	0.00	8,545.00	163.00	305.00	-156.14	0.00	0.00	0.00
Avalon									
8,600.00	0.00	0.00	8,587.41	163.00	305.00	-156.14	0.00	0.00	0.00
8,700.00	0.00	0.00	8,687.41	163.00	305.00	-156.14	0.00	0.00	0.00
8,703.59	0.00	0.00	8,691.00	163.00	305.00	-156.14	0.00	0.00	0.00
Chert Zone									
8,800.00	0.00	0.00	8,787.41	163.00	305.00	-156.14	0.00	0.00	0.00
8,900.00	0.00	0.00	8,887.41	163.00	305.00	-156.14	0.00	0.00	0.00
9,000.00	0.00	0.00	8,987.41	163.00	305.00	-156.14	0.00	0.00	0.00
9,100.00	0.00	0.00	9,087.41	163.00	305.00	-156.14	0.00	0.00	0.00
9,200.00	0.00	0.00	9,187.41	163.00	305.00	-156.14	0.00	0.00	0.00
9,300.00	0.00	0.00	9,287.41	163.00	305.00	-156.14	0.00	0.00	0.00
9,400.00	0.00	0.00	9,387.41	163.00	305.00	-156.14	0.00	0.00	0.00
9,500.00	0.00	0.00	9,487.41	163.00	305.00	-156.14	0.00	0.00	0.00
9,600.00	0.00	0.00	9,587.41	163.00	305.00	-156.14	0.00	0.00	0.00
9,700.00	0.00	0.00	9,687.41	163.00	305.00	-156.14	0.00	0.00	0.00
9,800.00	0.00	0.00	9,787.41	163.00	305.00	-156.14	0.00	0.00	0.00
9,840.59	0.00	0.00	9,828.00	163.00	305.00	-156.14	0.00	0.00	0.00
First Bone Spring Sand									
9,900.00	0.00	0.00	9,887.41	163.00	305.00	-156.14	0.00	0.00	0.00
9,904.59	0.00	0.00	9,892.00	163.00	305.00	-156.14	0.00	0.00	0.00
Second Bone Spring Carbonates									
10,000.00	0.00	0.00	9,987.41	163.00	305.00	-156.14	0.00	0.00	0.00
10,100.00	0.00	0.00	10,087.41	163.00	305.00	-156.14	0.00	0.00	0.00
10,200.00	0.00	0.00	10,187.41	163.00	305.00	-156.14	0.00	0.00	0.00
10,261.59	0.00	0.00	10,249.00	163.00	305.00	-156.14	0.00	0.00	0.00
Second Bone Spring Sand									
10,300.00	0.00	0.00	10,287.41	163.00	305.00	-156.14	0.00	0.00	0.00
10,400.00	0.00	0.00	10,387.41	163.00	305.00	-156.14	0.00	0.00	0.00
10,500.00	0.00	0.00	10,487.41	163.00	305.00	-156.14	0.00	0.00	0.00
10,600.00	0.00	0.00	10,587.41	163.00	305.00	-156.14	0.00	0.00	0.00
10,700.00	0.00	0.00	10,687.41	163.00	305.00	-156.14	0.00	0.00	0.00
10,800.00	0.00	0.00	10,787.41	163.00	305.00	-156.14	0.00	0.00	0.00
10,854.59	0.00	0.00	10,842.00	163.00	305.00	-156.14	0.00	0.00	0.00
Third Bone Spring Carbonates									
10,900.00	0.00	0.00	10,887.41	163.00	305.00	-156.14	0.00	0.00	0.00
11,000.00	0.00	0.00	10,987.41	163.00	305.00	-156.14	0.00	0.00	0.00
11,100.00	0.00	0.00	11,087.41	163.00	305.00	-156.14	0.00	0.00	0.00
11,200.00	0.00	0.00	11,187.41	163.00	305.00	-156.14	0.00	0.00	0.00
11,300.00	0.00	0.00	11,287.41	163.00	305.00	-156.14	0.00	0.00	0.00
11,400.00	0.00	0.00	11,387.41	163.00	305.00	-156.14	0.00	0.00	0.00
11,500.00	0.00	0.00	11,487.41	163.00	305.00	-156.14	0.00	0.00	0.00
11,555.59	0.00	0.00	11,543.00	163.00	305.00	-156.14	0.00	0.00	0.00
Third Bone Spring Sand									
11,600.00	0.00	0.00	11,587.41	163.00	305.00	-156.14	0.00	0.00	0.00
11,700.00	0.00	0.00	11,687.41	163.00	305.00	-156.14	0.00	0.00	0.00



Planning Report



Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Paul Foster Fed Com 805H
Company:	Franklin Mountain Energy	TVD Reference:	3031' GE + 30' KB @ 3061.00usft
Project:	Lea County, NM (NAD83)	MD Reference:	3031' GE + 30' KB @ 3061.00usft
Site:	PF Fed Com	North Reference:	Grid
Well:	Paul Foster Fed Com 805H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
11,738.64	0.00	0.00	11,726.04	163.00	305.00	-156.14	0.00	0.00	0.00
Start Build 10.00									
11,750.00	1.14	180.42	11,737.41	162.89	305.00	-156.03	10.00	10.00	0.00
11,782.64	4.40	180.42	11,770.00	161.31	304.99	-154.45	10.00	10.00	0.00
Wolfcamp									
11,800.00	6.14	180.42	11,787.29	159.72	304.98	-152.86	10.00	10.00	0.00
11,850.00	11.14	180.42	11,836.71	152.21	304.92	-145.36	10.00	10.00	0.00
11,851.32	11.27	180.42	11,838.00	151.96	304.92	-145.10	10.00	10.00	0.00
Wolfcamp A									
11,900.00	16.14	180.42	11,885.28	140.43	304.83	-133.58	10.00	10.00	0.00
11,950.00	21.14	180.42	11,932.64	124.46	304.71	-117.61	10.00	10.00	0.00
12,000.00	26.14	180.42	11,978.44	104.42	304.57	-97.58	10.00	10.00	0.00
12,050.00	31.14	180.42	12,022.31	80.46	304.39	-73.64	10.00	10.00	0.00
12,100.00	36.14	180.42	12,063.92	52.78	304.18	-45.96	10.00	10.00	0.00
12,133.00	39.44	180.42	12,090.00	32.56	304.03	-25.75	10.00	10.00	0.00
Wolfcamp B									
12,150.00	41.14	180.42	12,102.96	21.57	303.95	-14.77	10.00	10.00	0.00
12,200.00	46.14	180.42	12,139.14	-12.93	303.70	19.71	10.00	10.00	0.00
12,250.00	51.14	180.42	12,172.17	-50.44	303.42	57.21	10.00	10.00	0.00
12,300.00	56.14	180.42	12,201.81	-90.69	303.12	97.44	10.00	10.00	0.00
12,350.00	61.14	180.42	12,227.82	-133.37	302.80	140.10	10.00	10.00	0.00
12,400.00	66.14	180.42	12,250.02	-178.15	302.47	184.87	10.00	10.00	0.00
12,450.00	71.14	180.42	12,268.23	-224.70	302.13	231.40	10.00	10.00	0.00
12,500.00	76.14	180.42	12,282.31	-272.66	301.77	279.34	10.00	10.00	0.00
12,550.00	81.14	180.42	12,292.16	-321.66	301.41	328.32	10.00	10.00	0.00
12,600.00	86.14	180.42	12,297.70	-371.34	301.04	377.97	10.00	10.00	0.00
12,638.64	90.00	180.42	12,299.00	-409.94	300.76	416.56	10.00	10.00	0.00
Start 9796.14 hold at 12638.64 MD - HZ Target									
12,700.00	90.00	180.42	12,299.00	-471.30	300.30	477.90	0.00	0.00	0.00
12,800.00	90.00	180.42	12,299.00	-571.30	299.56	577.85	0.00	0.00	0.00
12,900.00	90.00	180.42	12,299.00	-671.30	298.82	677.81	0.00	0.00	0.00
13,000.00	90.00	180.42	12,299.00	-771.30	298.08	777.77	0.00	0.00	0.00
13,100.00	90.00	180.42	12,299.00	-871.29	297.34	877.72	0.00	0.00	0.00
13,200.00	90.00	180.42	12,299.00	-971.29	296.60	977.68	0.00	0.00	0.00
13,300.00	90.00	180.42	12,299.00	-1,071.29	295.86	1,077.63	0.00	0.00	0.00
13,400.00	90.00	180.42	12,299.00	-1,171.28	295.12	1,177.59	0.00	0.00	0.00
13,500.00	90.00	180.42	12,299.00	-1,271.28	294.38	1,277.54	0.00	0.00	0.00
13,600.00	90.00	180.42	12,299.00	-1,371.28	293.63	1,377.50	0.00	0.00	0.00
13,700.00	90.00	180.42	12,299.00	-1,471.28	292.89	1,477.46	0.00	0.00	0.00
13,800.00	90.00	180.42	12,299.00	-1,571.27	292.15	1,577.41	0.00	0.00	0.00
13,900.00	90.00	180.42	12,299.00	-1,671.27	291.41	1,677.37	0.00	0.00	0.00
14,000.00	90.00	180.42	12,299.00	-1,771.27	290.67	1,777.32	0.00	0.00	0.00
14,100.00	90.00	180.42	12,299.00	-1,871.27	289.93	1,877.28	0.00	0.00	0.00
14,200.00	90.00	180.42	12,299.00	-1,971.26	289.19	1,977.23	0.00	0.00	0.00
14,300.00	90.00	180.42	12,299.00	-2,071.26	288.45	2,077.19	0.00	0.00	0.00
14,400.00	90.00	180.42	12,299.00	-2,171.26	287.71	2,177.15	0.00	0.00	0.00
14,500.00	90.00	180.42	12,299.00	-2,271.25	286.97	2,277.10	0.00	0.00	0.00
14,600.00	90.00	180.42	12,299.00	-2,371.25	286.23	2,377.06	0.00	0.00	0.00
14,700.00	90.00	180.42	12,299.00	-2,471.25	285.49	2,477.01	0.00	0.00	0.00
14,800.00	90.00	180.42	12,299.00	-2,571.25	284.75	2,576.97	0.00	0.00	0.00
14,900.00	90.00	180.42	12,299.00	-2,671.24	284.01	2,676.92	0.00	0.00	0.00
15,000.00	90.00	180.42	12,299.00	-2,771.24	283.26	2,776.88	0.00	0.00	0.00
15,100.00	90.00	180.42	12,299.00	-2,871.24	282.52	2,876.84	0.00	0.00	0.00



Planning Report



Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Paul Foster Fed Com 805H
Company:	Franklin Mountain Energy	TVD Reference:	3031' GE + 30' KB @ 3061.00usft
Project:	Lea County, NM (NAD83)	MD Reference:	3031' GE + 30' KB @ 3061.00usft
Site:	PF Fed Com	North Reference:	Grid
Well:	Paul Foster Fed Com 805H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
15,200.00	90.00	180.42	12,299.00	-2,971.24	281.78	2,976.79	0.00	0.00	0.00
15,300.00	90.00	180.42	12,299.00	-3,071.23	281.04	3,076.75	0.00	0.00	0.00
15,400.00	90.00	180.42	12,299.00	-3,171.23	280.30	3,176.70	0.00	0.00	0.00
15,500.00	90.00	180.42	12,299.00	-3,271.23	279.56	3,276.66	0.00	0.00	0.00
15,600.00	90.00	180.42	12,299.00	-3,371.22	278.82	3,376.61	0.00	0.00	0.00
15,700.00	90.00	180.42	12,299.00	-3,471.22	278.08	3,476.57	0.00	0.00	0.00
15,800.00	90.00	180.42	12,299.00	-3,571.22	277.34	3,576.53	0.00	0.00	0.00
15,900.00	90.00	180.42	12,299.00	-3,671.22	276.60	3,676.48	0.00	0.00	0.00
16,000.00	90.00	180.42	12,299.00	-3,771.21	275.86	3,776.44	0.00	0.00	0.00
16,100.00	90.00	180.42	12,299.00	-3,871.21	275.12	3,876.39	0.00	0.00	0.00
16,200.00	90.00	180.42	12,299.00	-3,971.21	274.38	3,976.35	0.00	0.00	0.00
16,300.00	90.00	180.42	12,299.00	-4,071.21	273.64	4,076.30	0.00	0.00	0.00
16,400.00	90.00	180.42	12,299.00	-4,171.20	272.89	4,176.26	0.00	0.00	0.00
16,500.00	90.00	180.42	12,299.00	-4,271.20	272.15	4,276.22	0.00	0.00	0.00
16,600.00	90.00	180.42	12,299.00	-4,371.20	271.41	4,376.17	0.00	0.00	0.00
16,700.00	90.00	180.42	12,299.00	-4,471.19	270.67	4,476.13	0.00	0.00	0.00
16,800.00	90.00	180.42	12,299.00	-4,571.19	269.93	4,576.08	0.00	0.00	0.00
16,900.00	90.00	180.42	12,299.00	-4,671.19	269.19	4,676.04	0.00	0.00	0.00
17,000.00	90.00	180.42	12,299.00	-4,771.19	268.45	4,775.99	0.00	0.00	0.00
17,100.00	90.00	180.42	12,299.00	-4,871.18	267.71	4,875.95	0.00	0.00	0.00
17,200.00	90.00	180.42	12,299.00	-4,971.18	266.97	4,975.91	0.00	0.00	0.00
17,300.00	90.00	180.42	12,299.00	-5,071.18	266.23	5,075.86	0.00	0.00	0.00
17,400.00	90.00	180.42	12,299.00	-5,171.18	265.49	5,175.82	0.00	0.00	0.00
17,500.00	90.00	180.42	12,299.00	-5,271.17	264.75	5,275.77	0.00	0.00	0.00
17,600.00	90.00	180.42	12,299.00	-5,371.17	264.01	5,375.73	0.00	0.00	0.00
17,700.00	90.00	180.42	12,299.00	-5,471.17	263.27	5,475.68	0.00	0.00	0.00
17,800.00	90.00	180.42	12,299.00	-5,571.16	262.52	5,575.64	0.00	0.00	0.00
17,900.00	90.00	180.42	12,299.00	-5,671.16	261.78	5,675.60	0.00	0.00	0.00
18,000.00	90.00	180.42	12,299.00	-5,771.16	261.04	5,775.55	0.00	0.00	0.00
18,100.00	90.00	180.42	12,299.00	-5,871.16	260.30	5,875.51	0.00	0.00	0.00
18,200.00	90.00	180.42	12,299.00	-5,971.15	259.56	5,975.46	0.00	0.00	0.00
18,300.00	90.00	180.42	12,299.00	-6,071.15	258.82	6,075.42	0.00	0.00	0.00
18,400.00	90.00	180.42	12,299.00	-6,171.15	258.08	6,175.37	0.00	0.00	0.00
18,500.00	90.00	180.42	12,299.00	-6,271.15	257.34	6,275.33	0.00	0.00	0.00
18,600.00	90.00	180.42	12,299.00	-6,371.14	256.60	6,375.29	0.00	0.00	0.00
18,700.00	90.00	180.42	12,299.00	-6,471.14	255.86	6,475.24	0.00	0.00	0.00
18,800.00	90.00	180.42	12,299.00	-6,571.14	255.12	6,575.20	0.00	0.00	0.00
18,900.00	90.00	180.42	12,299.00	-6,671.13	254.38	6,675.15	0.00	0.00	0.00
19,000.00	90.00	180.42	12,299.00	-6,771.13	253.64	6,775.11	0.00	0.00	0.00
19,100.00	90.00	180.42	12,299.00	-6,871.13	252.89	6,875.06	0.00	0.00	0.00
19,200.00	90.00	180.42	12,299.00	-6,971.13	252.15	6,975.02	0.00	0.00	0.00
19,300.00	90.00	180.42	12,299.00	-7,071.12	251.41	7,074.98	0.00	0.00	0.00
19,400.00	90.00	180.42	12,299.00	-7,171.12	250.67	7,174.93	0.00	0.00	0.00
19,500.00	90.00	180.42	12,299.00	-7,271.12	249.93	7,274.89	0.00	0.00	0.00
19,600.00	90.00	180.42	12,299.00	-7,371.11	249.19	7,374.84	0.00	0.00	0.00
19,700.00	90.00	180.42	12,299.00	-7,471.11	248.45	7,474.80	0.00	0.00	0.00
19,800.00	90.00	180.42	12,299.00	-7,571.11	247.71	7,574.75	0.00	0.00	0.00
19,900.00	90.00	180.42	12,299.00	-7,671.11	246.97	7,674.71	0.00	0.00	0.00
20,000.00	90.00	180.42	12,299.00	-7,771.10	246.23	7,774.67	0.00	0.00	0.00
20,100.00	90.00	180.42	12,299.00	-7,871.10	245.49	7,874.62	0.00	0.00	0.00
20,200.00	90.00	180.42	12,299.00	-7,971.10	244.75	7,974.58	0.00	0.00	0.00
20,300.00	90.00	180.42	12,299.00	-8,071.10	244.01	8,074.53	0.00	0.00	0.00
20,400.00	90.00	180.42	12,299.00	-8,171.09	243.27	8,174.49	0.00	0.00	0.00
20,500.00	90.00	180.42	12,299.00	-8,271.09	242.52	8,274.44	0.00	0.00	0.00



Planning Report



Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Paul Foster Fed Com 805H
Company:	Franklin Mountain Energy	TVD Reference:	3031' GE + 30' KB @ 3061.00usft
Project:	Lea County, NM (NAD83)	MD Reference:	3031' GE + 30' KB @ 3061.00usft
Site:	PF Fed Com	North Reference:	Grid
Well:	Paul Foster Fed Com 805H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #2		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
20,600.00	90.00	180.42	12,299.00	-8,371.09	241.78	8,374.40	0.00	0.00	0.00	
20,700.00	90.00	180.42	12,299.00	-8,471.08	241.04	8,474.36	0.00	0.00	0.00	
20,800.00	90.00	180.42	12,299.00	-8,571.08	240.30	8,574.31	0.00	0.00	0.00	
20,900.00	90.00	180.42	12,299.00	-8,671.08	239.56	8,674.27	0.00	0.00	0.00	
21,000.00	90.00	180.42	12,299.00	-8,771.08	238.82	8,774.22	0.00	0.00	0.00	
21,100.00	90.00	180.42	12,299.00	-8,871.07	238.08	8,874.18	0.00	0.00	0.00	
21,200.00	90.00	180.42	12,299.00	-8,971.07	237.34	8,974.13	0.00	0.00	0.00	
21,300.00	90.00	180.42	12,299.00	-9,071.07	236.60	9,074.09	0.00	0.00	0.00	
21,400.00	90.00	180.42	12,299.00	-9,171.07	235.86	9,174.05	0.00	0.00	0.00	
21,500.00	90.00	180.42	12,299.00	-9,271.06	235.12	9,274.00	0.00	0.00	0.00	
21,600.00	90.00	180.42	12,299.00	-9,371.06	234.38	9,373.96	0.00	0.00	0.00	
21,700.00	90.00	180.42	12,299.00	-9,471.06	233.64	9,473.91	0.00	0.00	0.00	
21,800.00	90.00	180.42	12,299.00	-9,571.05	232.90	9,573.87	0.00	0.00	0.00	
21,900.00	90.00	180.42	12,299.00	-9,671.05	232.15	9,673.82	0.00	0.00	0.00	
22,000.00	90.00	180.42	12,299.00	-9,771.05	231.41	9,773.78	0.00	0.00	0.00	
22,100.00	90.00	180.42	12,299.00	-9,871.05	230.67	9,873.74	0.00	0.00	0.00	
22,200.00	90.00	180.42	12,299.00	-9,971.04	229.93	9,973.69	0.00	0.00	0.00	
22,300.00	90.00	180.42	12,299.00	-10,071.04	229.19	10,073.65	0.00	0.00	0.00	
22,400.00	90.00	180.42	12,299.00	-10,171.04	228.45	10,173.60	0.00	0.00	0.00	
22,434.77	90.00	180.42	12,299.00	-10,205.81	228.19	10,208.36	0.00	0.00	0.00	
TD at 22434.77										

Design Targets										
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude	
SHL (PF Fed Com 80: - hit/miss target - Shape	0.00	0.00	0.00	0.00	0.00	393,961.02	856,363.73	32.0789960	-103.3162310	
LP P2 (PF Fed Com 8: - plan hits target center - Point	0.00	0.01	12,299.00	-409.94	300.76	393,551.08	856,664.49	32.0778615	-103.3152726	
PBHL P2 (PF Fed Com 8: - plan hits target center - Point	0.00	0.00	12,299.00	-10,205.81	228.19	383,755.21	856,591.93	32.0509390	-103.3158050	



Planning Report



Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Paul Foster Fed Com 805H
Company:	Franklin Mountain Energy	TVD Reference:	3031' GE + 30' KB @ 3061.00usft
Project:	Lea County, NM (NAD83)	MD Reference:	3031' GE + 30' KB @ 3061.00usft
Site:	PF Fed Com	North Reference:	Grid
Well:	Paul Foster Fed Com 805H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #2		

Formations

Measured Depth (usft)	Vertical Depth (usft)	Name	Lithology	Dip (°)	Dip Direction (°)
30.00	30.00	Cenozoic Alluvium (surface)			
388.00	388.00	Rustler			
1,879.00	1,879.00	Salado			
3,062.86	3,061.00	Potential Losses			
3,062.86	3,061.00	Capitan			
3,094.95	3,093.00	Base Salt			
4,940.04	4,933.00	Lamar			
5,029.29	5,022.00	Bell Canyon			
5,859.58	5,850.00	Cherry Canyon			
7,310.59	7,298.00	Brushy Canyon			
8,503.59	8,491.00	Bone Spring Lime			
8,557.59	8,545.00	Avalon			
8,703.59	8,691.00	*Chert Zone*			
9,840.59	9,828.00	First Bone Spring Sand			
9,904.59	9,892.00	Second Bone Spring Carbonates			
10,261.59	10,249.00	Second Bone Spring Sand			
10,854.59	10,842.00	Third Bone Spring Carbonates			
11,555.59	11,543.00	Third Bone Spring Sand			
11,782.64	11,770.00	Wolfcamp			
11,851.32	11,838.00	Wolfcamp A			
12,133.00	12,090.00	Wolfcamp B			
12,638.64	12,299.00	HZ Target			

Plan Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
2,200.00	2,200.00	0.00	0.00	Start Build 1.50
2,483.86	2,483.60	4.97	9.30	Start 4373.88 hold at 2483.86 MD
6,857.74	6,845.40	158.03	295.70	Start Drop -1.50
7,141.59	7,129.00	163.00	305.00	Start 4597.04 hold at 7141.59 MD
11,738.64	11,726.04	163.00	305.00	Start Build 10.00
12,638.64	12,299.00	-409.94	300.76	Start 9796.14 hold at 12638.64 MD
22,434.77	12,299.00	-10,205.81	228.19	TD at 22434.77



PF Fed Com 805H

1. Geologic name of surface location: Permian
2. Estimated tops of important geological markers:

Formations	PROG SS	PROG TVD	Picked TVD	delta	Potential/Issues
Cenozoic Alluvium (surface)	3,031'	30'	30'	0	Sand/Gravels/unconsolidated
Rustler	2,673'	388'			Carbonates
Salado	1,182'	1,879'			Salt, Carbonate & Clastics
Base Salt	-32'	3,093'			Shaley Carbonate & Shale
Potential Losses		3,061'			
Capitan		3,061'			Carbonate & Clastics
Lamar	-1,872'	4,933'			Carbonate & Clastics
Bell Canyon	-1,961'	5,022'			Sandstone - oil/gas/water
Cherry Canyon	-2,789'	5,850'			Sandstone - oil/gas/water
Brushy Canyon	-4,237'	7,298'			Sand/carb/shales - oil/gas/water
Bone Spring Lime	-5,430'	8,491'			Shale/Carbonates - oil/gas
Avalon	-5,484'	8,545'			Shale/Carbonates - oil/gas
Chert Zone	-5,630'	8,691'			Carbonate/Chert
First Bone Spring Sand	-6,767'	9,828'			Sandstone - oil/gas/water
Second Bone Spring Carbonates	-6,831'	9,892'			Shale/Carbonates - oil/gas
Second Bone Spring Sand	-7,188'	10,249'			Sandstone - oil/gas/water
Third Bone Spring Carbonates	-7,781'	10,842'			Shale/Carbonates - oil/gas
Third Bone Spring Sand	-8,482'	11,543'			Sandstone - oil/gas/water
Wolfcamp	-8,709'	11,770'			Overpressure shale/sand- Oil/Gas
Wolfcamp A	-8,777'	11,838'			Overpressure Shale - Oil/Gas
Wolfcamp B	-9,029'	12,090'			Overpressure Shale - Oil/Gas
HZ Target	-9,238'	12,299'			Overpressure Shale - Oil/Gas
Wolfcamp C	-9,301'	12,362'			Overpressure Shale - Oil/Gas

3. Estimated depth of anticipated fresh water, oil or gas:

Upper Permian Sands	0- 400'	Fresh Water
Delaware Sands	5,022'	Oil
Bone Spring	9,828'	Oil
Wolfcamp	11,770'	Oil

No other formations are expected to give up oil, gas or fresh water in measurable quantities. Surface freshwater sands will be protected by setting 13 3/8" casing at 1,300' and circulating cement back to surface.

4. Casing Program:

All casing strings will be run new. Safety factors calculated assuming the well is vertical.

Casing string	Weight	Grade	Burst	Collapse	Tension	Conn	Length	API design factor			
								Burst	Collapse	Tension	Coupling
Surface 13 3/8"	54.5	J-55	2730	1130	853	BTC 909	1300	1.18	1.67	4.99	5.32
Intermediate 9 5/8"	40	HCL-80	7430	4230	916	BTC 1042	4970	1.82	1.82	3.07	3.49
Intermediate 7 5/8"	29.7	HCP-110	8280	7150	827	Liberty 558	11650	1.14	1.31	1.85	1.25
Long string 5 1/2"	23	P-110	14520	14520	729	Eagle 606 TVD	22434 12299	1.32	1.38	1.18	0.98 1.58



7 5/8" casing will be set at 11,650' MD/11,637' TVD at 0° Inc. Stress calculations on 5 1/2" casing performed assuming 22,434' depth. Actual max vertical depth is 12,299'.

Cementing Program:

Cementing Stage tool can be placed in the 1st Intermediate string as a contingency to ensure required TOC to surface.

String Type	Hole Size	Casing Size	Setting Depth	Sacks	Type of cmt	Lead Yield ft ³ /sk	Water gal/sk	TOC ft	Sacks	Type of cmt	Tail Yield ft ³ /sk	Water gal/sk	TOC	Excess
Surf	17.5	13.375	1300	795	Extenda Cem, 12.8 ppg Class C, 3lb/sk Kol-Seal	1.747	9.06	0	334	Tail, 14.8 ppg, Class C,	1.349	6.51	1000	100%
					0.125pps Poly-E-Flake					1% CaCl ₂ , 0.125pps Celo-Flake				
Int1	12.25	9.625	4970	1442	Lead, 12.8 ppg, Class C 5% Salt,	1.79	9.74	0	154	Tail, 14.8 ppg, Class C,	1.33	6.37	4670	100%
					0.125 pps Poly-E-Flake, 3lb/sk Kol-Seal					0.1% HR 800 .125 pps Poly-E-Flake				
Int2	8.75	7.625	11650	359	Lite Fill, 9.5 ppg, Class C 3lb/sk	2.13	5.97	3970	94	NeoCem 14.8 ppg, Class C	1.33	6.29	10650	50%
					Bridgemaker Gel, 5%					0.25 pps Cello-Flake, 2% CaCl ₂				
Prod	6.75	5.5	22434	879	Salt, 5pps LCM, 0.25pps Cello-Flake									
					Tail, 14.5 ppg, Gas Migration Control	1.34	6.22	10650						20%

5. Minimum Specifications for Pressure Control:

The minimum blowout preventer equipment (BOPE) shown in Exhibit #1 will consist of a single ram, mud cross and double ram-type (10,000 psi WP) preventer and an annular preventer (5,000-psi WP). Both units will be hydraulically operated, and the ram-type will be equipped with blind rams on bottom and 4 1/2" x 7" variable pipe rams on top. All BOPE will be tested in accordance with Onshore Oil & Gas order No. 2.

Before drilling out of the surface casing, the ram-type BOP and accessory equipment will be tested to 5,000/250 psig and the annular preventer to 5,000/250 psig. The surface casing will be tested to 1500 psi for 30 minutes.

Before drilling out of the second intermediate casing, the ram-type BOP and accessory equipment will be tested to 10,000/250 psig and the annular preventer to 5,000/250 psig. The second intermediate casing will be tested to a minimum of .22 psi/ft for 30 minutes prior to drillout.

Pipe rams will be operationally checked each 24-hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets.

A hydraulically operated choke will be installed prior to drilling out of the intermediate casing shoe.



6. Types and characteristics of the proposed mud system:

During this procedure we plan to use a Closed-Loop System and haul contents to the required disposal. The applicable depths and properties of the drilling fluid systems are as follows.

Depth	Type	Weight (ppg)	Viscosity	Water Loss
0 – 1,300'	Fresh - Gel	8.6-8.8	28-34	N/c
1,300' – 11,650'	Brine	8.8-10.2	28-34	N/c
11,650' – 22,434' Lateral	Oil Base	10.0-12.0	58-68	3 - 6

The highest mud weight needed to balance formation is expected to be 11-12 ppg. In order to maintain hole stability, mud weights up to 13 ppg may be utilized.

An electronic pit volume totalizer (PVT) will be utilized on the circulating system, to monitor pit volume, flow rate, pump pressure and stroke rate.

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept at the wellsite at all times.

7. Auxiliary well control and monitoring equipment:

(A) A kelly cock will be kept in the drill string at all times.

(B) A full opening drill pipe-stabbing valve (inside BOP) with proper drill pipe connections will be on the rig floor at all times.

(C) H₂S monitoring and detection equipment will be utilized from surface casing point to TD.

(D) A wear bushing will be installed in the wellhead prior to drilling out of the surface casing.

8. Logging, testing and coring program:

GR–CCL–CNL Will be run in cased hole during completions phase of operations.

Open-hole logs are not planned for this well.

9. Abnormal conditions, pressures, temperatures and potential hazards:

The estimated bottom-hole temperature at 12,299' TVD (deepest point of the well) is 195F with an estimated maximum bottom-hole pressure (BHP) at the same point of 8,314 psig (based on 13 ppg MW). Hydrogen sulfate may be present in the area. All necessary precautions will be taken before drilling operations commence. See Hydrogen Sulfide Plan below:

10. Hydrogen Sulfide Plan:

A. All personnel shall receive proper awareness H₂S training.

B. Briefing Area: two perpendicular areas will be designated by signs and readily accessible.

C. Required Emergency Equipment

a. Well Control Equipment

i. Flare line 150' from wellhead to be ignited by auto ignition sparking system.

ii. Choke manifold with a remotely operated hydraulic choke.

iii. Mud/gas separator

b. Protective equipment for essential personnel

i. Breathing Apparatus

1. Rescue packs (SCBA) – 1 unit shall be placed at each briefing area, 2 shall be stored in a safety trailer on site.

2. Work/Escapes packs – 4 packs shall be stored on the rig floor with sufficient air hose not to restrict work activity



3. Emergency Escape Packs – 4 packs shall be stored in the doghouse for emergency evacuation.
- ii. Auxiliary Rescue Equipment
 1. Stretcher
 2. Two OSHA full body harnesses
 3. 100 feet of 5/8 inches OSHA approved rope
 4. 1-20# class ABC fire extinguisher
- c. H2S Detection and Monitoring Equipment
 - i. A stationary detector with three sensors will be placed in the doghouse if equipped, set to visually alarm at 10 ppm and audible at 14 ppm. The detector will be calibrated a minimum of every 30 days or as needed. The sensors will be placed in the following places:
 1. Rig Floor
 2. Below Rig Floor / Near BOPs
 3. End of flow line or where well bore fluid is being discharged (near shakers)
 - ii. If H2S is encountered, measured values and formations will be provided to the BLM.
- d. Visual Warning Systems
 - i. One color code condition sign will be placed at the entrance to the site reflecting the possible conditions at the site.
 - ii. A colored condition flag will be on display, reflecting the current condition at the site at the time.
 - iii. Two windsocks will be placed in strategic locations, visible from all angles.
- e. Mud Program
 - i. The Mud program will be designed to minimize the volume of H2S circulated to surface. The operator will have the necessary mud products to minimize hazards while drilling in H2S bearing zones.
- f. Metallurgy
 - i. All drill strings, casings, tubing, wellhead, blowout preventer, drilling spool, kill lines, choke manifold and lines, and valves shall be suitable for H2S service at the anticipated operating pressures to prevent sour sulfide stress cracking.
- g. Communication
 - i. Communication will be via cell phones and walkie talkies on location.

Franklin Mountain Energy has conducted a review of offset operated wells to determine if an H2S contingency plan is required for the proposed well. Based on concentrations of offset wells, proximity to main roads, and distance to populated areas, the radius of exposure created by a potential release was determined to be minimal and low enough to not necessitate an H2S contingency plan. This will be reevaluated during wellbore construction if H2S is observed and after the well is on production.

11. Anticipated starting date and duration of operations:

The drilling operations on the well should be finished in approximately one month. However, in order to minimize disturbance in the area and to improve efficiency Franklin Mountain is planning to drill all the wells on the pad prior to commence completion operations. To even further reduce the time heavy machinery is used the “batch drilling” method may be used. A batch drilling sequence sundry will be submitted for BLM approval prior to spud. A drilling rig with walking/skidding capabilities will be used.

**12. Disposal/environmental concerns:**

- (A) Drilled cuttings will be hauled to and disposed of in a state-certified disposal site.
- (B) Non-hazardous waste mud/cement from the drilling process will also be hauled to and disposed of in a state-certified disposal site.
- (C) Garbage will be hauled to the Pecos City Landfill.
- (D) Sewage (grey water) will be hauled to the Carlsbad City Landfill

13. Wellhead:

A multi-bowl wellhead system will be utilized.

After running the 13 3/8" surface casing, a 13-5/8" BOP/BOPE system with a minimum working pressure of 10,000 psi will be installed on the wellhead system and will be pressure tested to 250 psi low followed by a 5,000 psi pressure test. This pressure test will be repeated at least every 21 days, as per Onshore Order No. 2

The minimum working pressure of the BOP and related BOPE required for drilling below the surface casing shoe shall be 5,000 psi.

After running the 2nd intermediate casing, and before drilling out, the wellhead, BOP, and related equipment will be tested to 10,000/250 psig.

The multi-bowl wellhead will be installed by vendor's representative(s). A copy of the installation instructions for the Cactus Multi-Bowl WH system has been sent to the BLM office in Carlsbad.

The wellhead will be installed by a third party welder while being monitored by WH vendor's representative.

All BOP equipment will be tested utilizing a conventional test plug. Not a cup or J-packer type.

A solid steel body pack-off will be utilized after running and cementing the intermediate casing strings. After installation of the first intermediate string the pack-off and lower flanges will be pressure tested to 5000 psi. After installation of the second intermediate string, the pack-off and upper flange will be pressure tested to 10,000 psi.

Both the surface and intermediate casing strings will be tested as per Onshore Order No. 2 to at least 0.22 psi/ft or 1500 psi, whichever is greater.

14. Additional variance requests**A. Casing.**

In order to minimize potential environmental and technical hazards, this well is planned with two intermediate strings of casing.

1. Variance is requested to wave the centralizer requirements for the 7 5/8" casing due to the tight clearance with 9 5/8" string.
2. Variance is requested to wave/reduce the centralizer requirements for the 5 1/2" casing due to the tight clearance with 6 3/4" hole and 5 1/2" casing due to tight clearances.

FRANKLIN MOUNTAIN ENERGY



Geologic Prognosis

Well Name	PF Fed Com 805H
Operator	Franklin Mountain Energy, LLC
Project Area	PF Unit
Well Type	10,000' Wolfcamp B Lateral
API	
Rig	

State	NM	County	Lea						
SHL	Township	26S/35E	Section	1	1,087'	FEL	210'	FNL	
BHL	Township	26S/35E	Section	12	960'	FEL	150'	FSL	
Surface Latitude	NAD 83		32.078996						
Surface Longitude	NAD 83		103.316231						
Bottom Hole Latitude	NAD 83		32.050939						
Bottom Hole Longitude	NAD 83		103.315805						
Ground Level	3,031'	Rig KB	30'	KB	3,061'				

Formations	PROG SS	PROG TVD	Picked TVD	delta	Potential/Issues
Cenozoic Alluvium (surface)	3,031'	30'	30'	0	Sand/Gravels/unconsolidated
Rustler	2,673'	388'			Carbonates
Salado	1,182'	1,879'			Salt, Carbonate & Clastics
Base Salt	-32'	3,093'			Shaley Carbonate & Shale
Potential Losses		3,061'			
Capitan		3,061'			Carbonate & Clastics
Lamar	-1,872'	4,933'			Carbonate & Clastics
Bell Canyon	-1,961'	5,022'			Sandstone - oil/gas/water
Cherry Canyon	-2,789'	5,850'			Sandstone - oil/gas/water
Brushy Canyon	-4,237'	7,298'			Sand/carb/shales - oil/gas/water
Bone Spring Lime	-5,430'	8,491'			Shale/Carbonates - oil/gas
Avalon	-5,484'	8,545'			Shale/Carbonates - oil/gas
Chert Zone	-5,630'	8,691'			Carbonate/Chert
First Bone Spring Sand	-6,767'	9,828'			Sandstone - oil/gas/water
Second Bone Spring Carbonates	-6,831'	9,892'			Shale/Carbonates - oil/gas
Second Bone Spring Sand	-7,188'	10,249'			Sandstone - oil/gas/water
Third Bone Spring Carbonates	-7,781'	10,842'			Shale/Carbonates - oil/gas
Third Bone Spring Sand	-8,482'	11,543'			Sandstone - oil/gas/water
Wolfcamp	-8,709'	11,770'			Overpressure shale/sand- Oil/Gas
Wolfcamp A	-8,777'	11,838'			Overpressure Shale - Oil/Gas
Wolfcamp B	-9,029'	12,090'			Overpressure Shale - Oil/Gas
HZ Target	-9,238'	12,299'			Overpressure Shale - Oil/Gas
Wolfcamp C	-9,301'	12,362'			Overpressure Shale - Oil/Gas

Target interval is expected to have an average apparent dip of 0.0 degrees down along the lateral based on the Wolfcamp B structure

Target window tolerance is set at +/- 15'

Target Line: 12299' KBTVD @ 0' VS w/ 90.0° inc.

Offset Log: Talco Unit 001 (300252674700)

Updated 5/12/22

FME Geologist	Ellen Wilcox	ewilcox@fmellc.com
Office		Cell 585-880-1737

FME Geologist	Ben Kessel		bkessel@fmellc.com	
	Office	720-414-7868	Cell	303.868.9946
FME Engineer				
Electric Logs	From		To	
Open-Hole	n/a			
MWD/LWD	MWD GR		Int. 1 Csg. Point	TD
Mud Log:				
Start logging at drill out of surface casing				
Sampling:	10' samples in vertical and through curve, 30' samples in lateral			
Samples:	1 set dry samples at footage frequency noted above			
Mud Gas:	Continuous			
Daily Contact:	Email distribution of mud log/daily report at 7:30am and 4:30 pm CST			
Daily Mud Log Email Distribution List				
Final Mud Log Distribution				
	Ben Kessel (bkessel@fmellc.com)		email	
Cuttings/Samples Shipment Information				

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 130229

CONDITIONS

Operator: Franklin Mountain Energy LLC 44 Cook Street Denver, CO 80206	OGRID: 373910
	Action Number: 130229
	Action Type: [C-103] NOI Change of Plans (C-103A)

CONDITIONS

Created By	Condition	Condition Date
pkautz	None	8/3/2022
