

Form 3160-5
(June 2019)UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENTFORM APPROVED
OMB No. 1004-0137
Expires: October 31, 2021**SUNDRY NOTICES AND REPORTS ON WELLS**
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.5. Lease Serial No. **NOG13121863**6. If Indian, Allottee or Tribe Name
EASTERN NAVAJO***SUBMIT IN TRIPLICATE - Other instructions on page 2***

1. Type of Well

☒ Oil Well ☐ Gas Well ☐ Other2. Name of Operator
ENDURING RESOURCES LLC3a. Address **1050 17TH STREET SUITE 2500, DENVER, CO** 3b. Phone No. (include area code)
(303) 573-12224. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SEC 23/T23N/R09W/NMP7. If Unit of CA/Agreement, Name and/or No.
NMNM135216A8. Well Name and No. **W LYBROOK UNIT/726H**9. API Well No. **3004538266**

10. Field and Pool or Exploratory Area

11. Country or Parish, State
SAN JUAN/NM**12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA**

TYPE OF SUBMISSION	TYPE OF ACTION				
☐ Notice of Intent	☐ Acidize	☐ Deepen	☐ Production (Start/Resume)	☐ Water Shut-Off	
☒ Subsequent Report	☐ Alter Casing	☐ Hydraulic Fracturing	☐ Reclamation	☐ Well Integrity	
☐ Final Abandonment Notice	☐ Casing Repair	☐ New Construction	☐ Recomplete	☒ Other	
	☐ Change Plans	☐ Plug and Abandon	☐ Temporarily Abandon		
	☐ Convert to Injection	☐ Plug Back	☐ Water Disposal		

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has detennined that the site is ready for final inspection.)

Enduring Resources performed a drillout and initial gas lift installation. An updated well schematic is attached.

EOT: 5083 MD

Packer: 5009 MD

GLVs: 2113, 2705, 3231, 3787, 4343 MD

Orifice Valve: 4968 MD

Job Start: 04.11.2022

Job End: 04.12.2022

14. I hereby certify that the foregoing is true and correct. Name (Printed/Typed)
HEATHER HUNTINGTON / Ph: (505) 636-9751Title **Permitting Technician**

Signature

Date

05/04/2022**THE SPACE FOR FEDERAL OR STATE OFFICE USE**

Approved by

KENNETH G RENNICK / Ph: (505) 564-7742 / AcceptedTitle **Petroleum Engineer**Date **05/13/2022**

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office **FARMINGTON**

Title 18 U.S.C Section 1001 and Title 43 U.S.C Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)




Enduring Resources IV - Production WBD

Well Name: W LYBROOK UNIT 726H

NOTE: Well schematic is drawn vertically due to space constraints on the report. Please reference the directional surveys as needed.

API/UWI 30-045-38266	Surface Legal Location (Unit M) Section 23, Twp 23N, Rng 09W,...	Field Name CHACO	License #	State/Province NEW MEXICO	Well Configuration Type Horizontal
Original KB Elevation (ft) 6,775.00	KB-Tubing Head Distance (ft)	Spud Date 12/13/2021 11:30	Rig Release Date	PBTD (All) (ftKB)	Total Depth All (TVD) (ftKB) Sidetrack 1 - 4,731.9

Horizontal, Sidetrack 1, 4/28/2022 2:10:43 PM

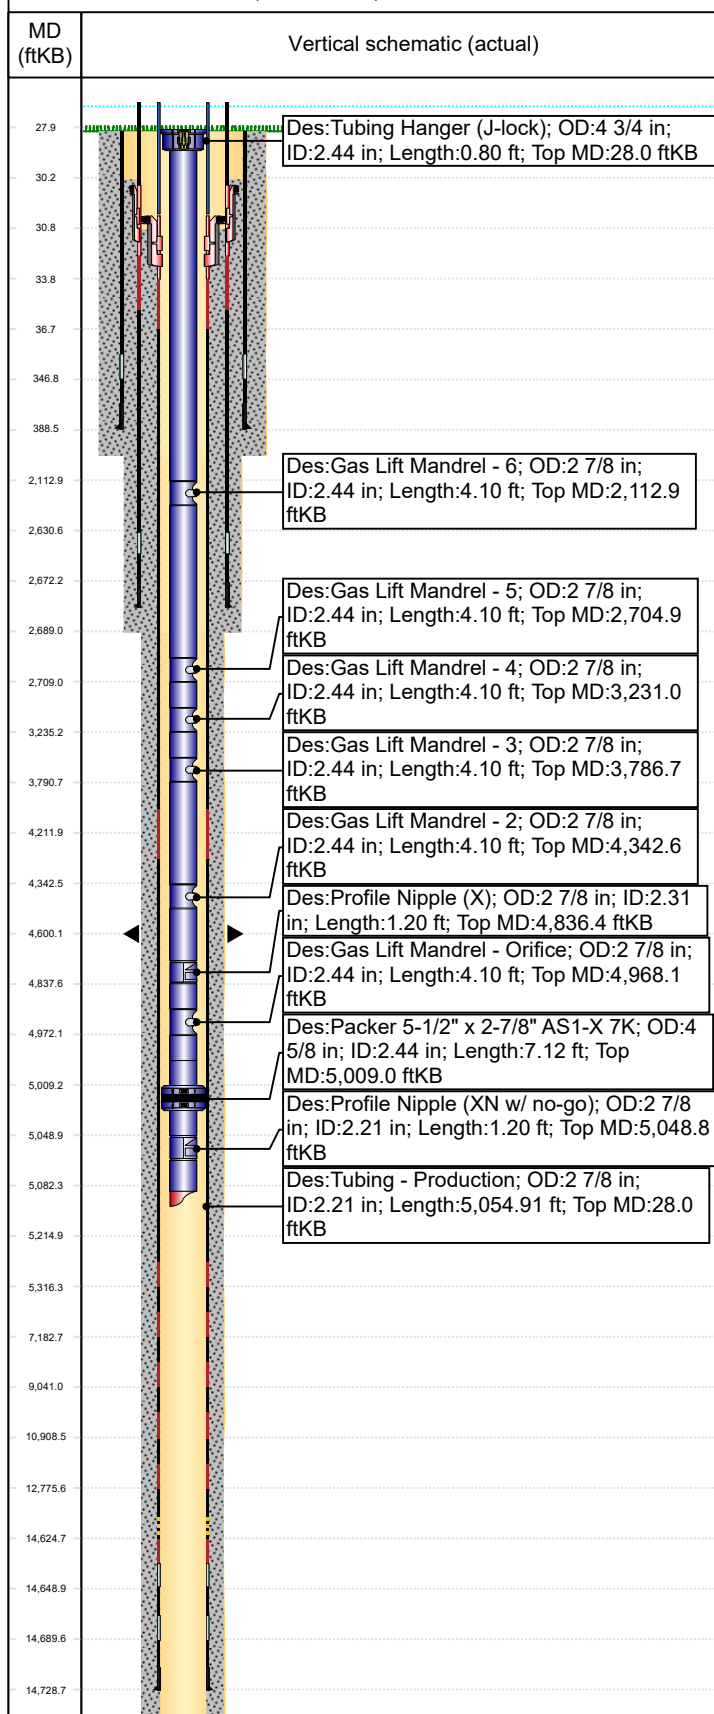

Wellbore Sections

Section Des	Size (in)	Act Top (ftKB)	Act Top (TVD) (ftKB)	Act Btm (ftKB)	Act Btm (TVD) (ftKB)
Production	8 1/2	4,600.0	4,335.4	14,739.0	4,731.9

Rod Strings

Rod Description	Run Date	String Length (ft)	Set Depth (ftKB)
Item Des	Jts	OD (in)	Len (ft)
		Top (ftKB)	Btm (ftKB)

Tubing - Production set at 5,082.9ftKB on 4/11/2022 12:00

Tubing Description	Run Date	String Length (ft)	Set Depth (ftKB)
Tubing - Production	4/11/2022	5,054.91	5,082.9
Item Des	Jts	Grade	Wt (lb/ft)
		OD (in)	ID (in)
		Len (ft)	Top (ftKB)
			Btm (ftKB)
Tubing Hanger (J-lock)	1		
Tubing	64	L-80	6.50
Gas Lift Mandrel - 6	1		
Tubing	18	L-80	6.50
Gas Lift Mandrel - 5	1		
Tubing	16	L-80	6.50
Gas Lift Mandrel - 4	1		
Tubing	17	L-80	6.50
Gas Lift Mandrel - 3	1		
Tubing	17	L-80	6.50
Gas Lift Mandrel - 2	1		
Tubing	15	L-80	6.50
Profile Nipple (X)	1		
Tubing	4	L-80	6.50
Gas Lift Mandrel - Orifice	1		
Tubing	1	L-80	6.50
Tubing (pup jt)	1	L-80	6.50
Packer 5-1/2" x 2-7/8" AS1-X 7K	1		
Tubing	1	L-80	6.50
Profile Nipple (XN w/ no-go)	1		
Tubing	1	L-80	6.50
Mule Shoe w/ pump-out plug (1556 psi shear)			

Surface, 388.3ftKB

OD (in) 13 3/8	Wt/Len (lb/ft) 54.50	String Grade J-55	Top Connection Buttress Thread	Top (ftKB) 28.0	Set Depth (ftKB) 388.3
Item Des		Jts	Len (ft)	Top (ftKB)	Btm (ftKB)
Casing Joints		8	317.09	28.0	345.1
Float Collar		1	1.62	345.1	346.7
Casing Joints		1	39.73	346.7	386.5
Float Shoe		1	1.84	386.5	388.3

Intermediate, 2,674.0ftKB

OD (in)	Wt/Len (lb/ft)	String Grade	Top Connection	Top (ftKB)	Set Depth (ftKB)
9 5/8	36.00	J-55	LT&C	-5.7	2,674.0
Item Des		Jts	Len (ft)	Top (ftKB)	Btm (ftKB)
Casing Joints		0	0.00	-5.7	-5.7




Enduring Resources IV - Production WBD

Well Name: W LYBROOK UNIT 726H

NOTE: Well schematic is drawn vertically due to space constraints on the report. Please reference the directional surveys as needed.

API/UWI 30-045-38266	Surface Legal Location (Unit M) Section 23, Twp 23N, Rng 09W,...	Field Name CHACO	License #	State/Province NEW MEXICO	Well Configuration Type Horizontal
Original KB Elevation (ft) 6,775.00	KB-Tubing Head Distance (ft)	Spud Date 12/13/2021 11:30	Rig Release Date	PBTD (All) (ftKB)	Total Depth All (TVD) (ftKB) Sidetrack 1 - 4,731.9

Horizontal, Sidetrack 1, 4/28/2022 2:10:45 PM

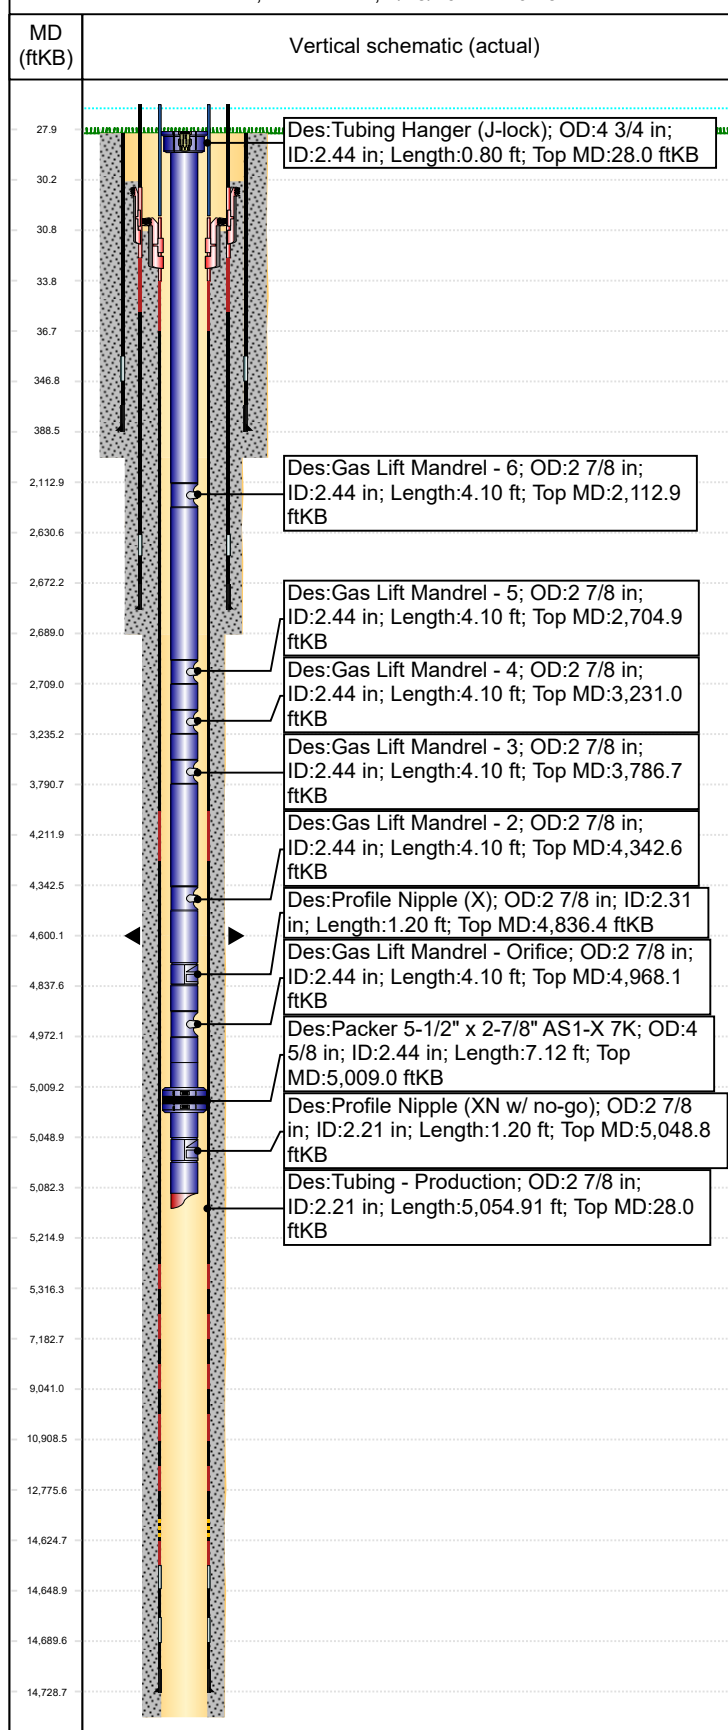

Item Des	Jts	Len (ft)	Top (ftKB)	Btm (ftKB)
Landing Joint	1	36.00	-5.7	30.3
Casing Hanger	1	3.20	30.3	33.5
Casing Pup Joint	1	3.00	33.5	36.5
Casing Joints	65	2,594.25	36.5	2,630.7
Float Collar	1	1.35	2,630.7	2,632.1
Casing Joints	1	40.30	2,632.1	2,672.4
Float Shoe	1	1.62	2,672.4	2,674.0

Production, 14,728.8ftKB

OD (in) 5 1/2	Wt/Len (lb/ft) 17.00	String Grade P-110	Top Connection LT&C	Top (ftKB) -5.6	Set Depth (ftKB) 14,728.8	
Item Des			Jts	Len (ft)	Top (ftKB)	Btm (ftKB)
Marker Joint			0	0.00	-5.6	-5.6
Casing Joints			0	0.00	-5.6	-5.6
Landing Joint			1	36.25	-5.6	30.6
Casing Hanger			1	3.20	30.6	33.8
Casing Pup Joint			1	3.00	33.8	36.8
Casing Joints			106	4,173.13	36.8	4,210.0
Air Lock			1	1.92	4,210.0	4,211.9
Marker Joint			1	23.06	4,211.9	4,235.0
Casing Joints			27	1,059.13	4,235.0	5,294.1
Marker Joint			1	22.10	5,294.1	5,316.2
Casing Joints			46	1,844.26	5,316.2	7,160.5
Marker Joint			1	22.40	7,160.5	7,182.9
Casing Joints			46	1,835.39	7,182.9	9,018.2
Marker Joint			1	22.80	9,018.2	9,041.0
Casing Joints			46	1,845.25	9,041.0	10,886.3
Marker Joint			1	22.29	10,886.3	10,908.6
Casing Joints			47	1,845.81	10,908.6	12,754.4
Marker Joint			1	21.11	12,754.4	12,775.5
Casing Joints			47	1,844.18	12,775.5	14,619.7
Toe Sleeve			1	5.10	14,619.7	14,624.8
Marker Joint			1	22.12	14,624.8	14,646.9
Float Collar			1	1.92	14,646.9	14,648.8
Casing Joints			1	38.98	14,648.8	14,687.8
Float Collar			1	1.92	14,687.8	14,689.7
Casing Joints			1	37.45	14,689.7	14,727.2
Float Shoe			1	1.63	14,727.2	14,728.8

Cement

Description	Cementing Start Date	Cementing End Date
Surface Casing Cement	12/18/2021	12/16/2021
Comment PJSM , Test Lines , Pumped 10 bbl's FW Spacer , 10 bbls Sapp Spacer , 10 bbls FW Spacer , 86.6 bbls Type iii Cement , 350 sks , @ 14.6 ppg , Dropped Plug , Displaced with 49 bbls water , Bumped Plug Bled Back 1/2 bbl , Float Held , 39 bbls Cement Back To Surface , Rig Down Cementer's , (Rig Released @ 19:00 hrs on 12/16/2021		
Description	Cementing Start Date	Cementing End Date
Intermediate Casing Cement	1/30/2022	1/30/2022
Comment Cement Online as follows: PJSM with Drake Energy Services. Pressure tested lines to 3,000 psi. Pumped 10 bbls FW, 20 bbls D-Mud Breaker, & 10 bbls of FW. Pumped Lead Cement: 194 bbls (503 sx) 90:10 Poz:Type III at 12.5 ppg, 2.14 ft3/sk, 12.05 gal H2O/sk. Pumped Tail Cement: 33 bbls (136 sx) Type III Blend at 14.6 ppg, 1.38 ft3/sk, 6.64 gal H2O/sk. Dropped plug & began displacement. Displaced with 200.2 bbls FW. FCP at 770 psi Bumped Plug at 1,332 psi. Maintained returns throughout job. Calculated 40 bbls to surface and got 30 bbls of good cement to surface. Top of Lead to surface and top of tail at 2,502 ft MD. (Cement 16:37 Hour's To 19:07 Hour's on -1/30/2022)		




Enduring Resources IV - Production WBD

Well Name: **W LYBROOK UNIT 726H**

NOTE: Well schematic is drawn vertically due to space constraints on the report. Please reference the directional surveys as needed.

API/UWI 30-045-38266	Surface Legal Location (Unit M) Section 23, Twp 23N, Rng 09W,...	Field Name CHACO	License #	State/Province NEW MEXICO	Well Configuration Type Horizontal
Original KB Elevation (ft) 6,775.00	KB-Tubing Head Distance (ft)	Spud Date 12/13/2021 11:30	Rig Release Date	PBTD (All) (ftKB)	Total Depth All (TVD) (ftKB) Sidetrack 1 - 4,731.9

Horizontal, Sidetrack 1, 4/28/2022 2:10:46 PM

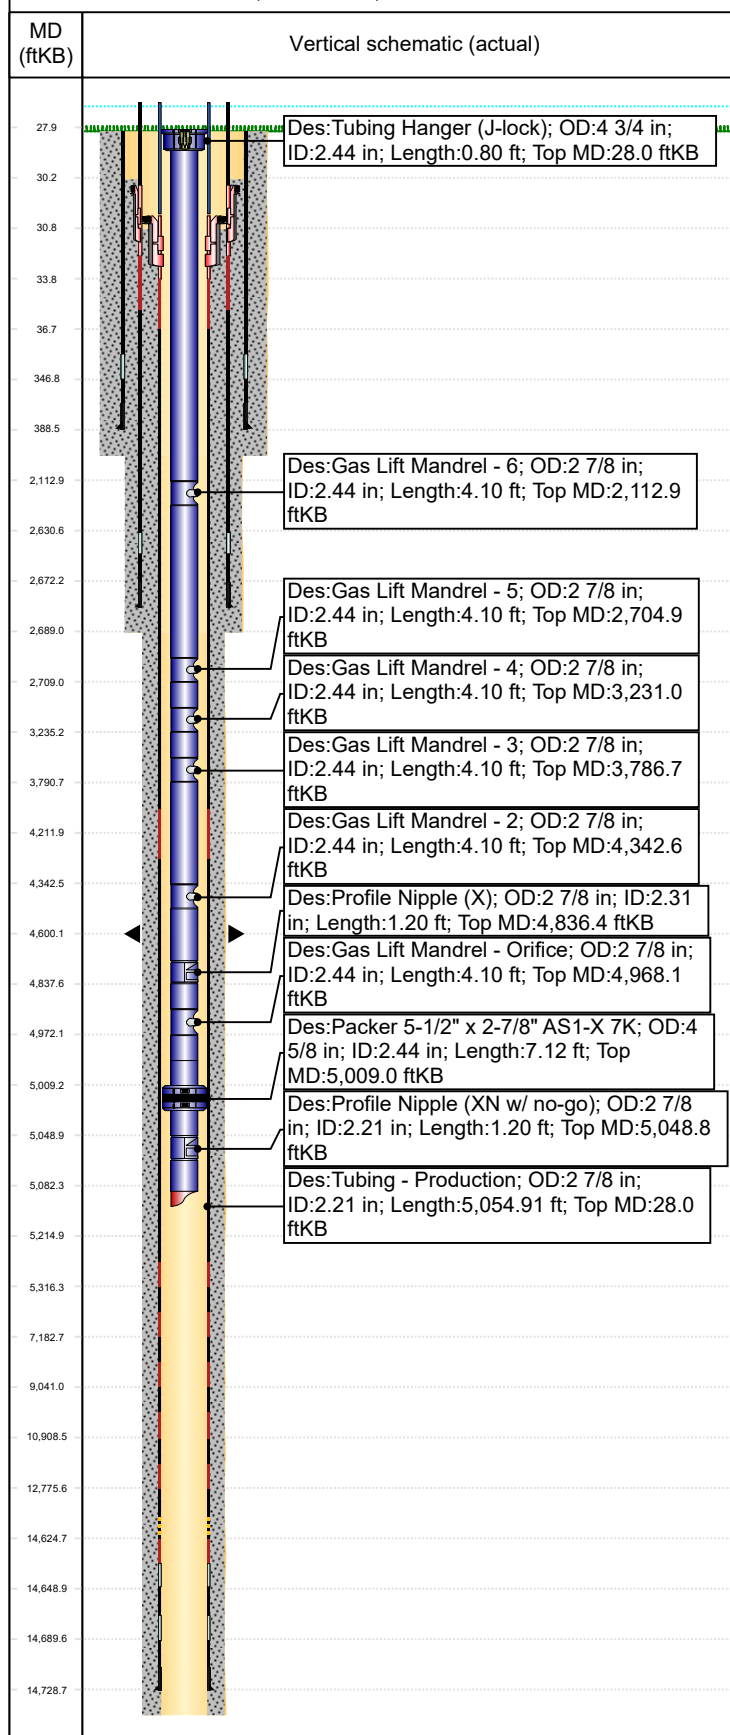

Cement

Description Production Casing Cement	Cementing Start Date 3/7/2022	Cementing End Date 3/8/2022
Comment Cement Summary: PJSM with American Cementing. Pressure tested lines to 5000 psi. Pumped 60 bbls Intraguard Star @ 11.0 ppg. Pumped Lead Cement: 247 bbls (472 sx) ASTM Type I/II at 12.4 ppg, 2.39 ft3/sk, 13.3 gal H2O/sk. Pumped Tail Cement: 471 bbls (1557 sx) Class G Cement at 13.3 ppg, 1.58 ft3/sk, 7.57 gal H2O/sk. Washed lines, dropped plug & began displacement. Displaced with 340.5 bbls FW with cement retarder in 1st 50 bbls. FCP at 2,060 psi and plug bumped at 4.0 bpm to 3,120 psi. Bled back 3.5 Bbls and floats held. Top of Tail: Calculated 3,696 ft MD. Tof of Lead: surface Cement Back 40 BBL Cement in place at 04:45 on 3/8/2022		

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

COMMENTS

Action 113099

COMMENTS

Operator: ENDURING RESOURCES, LLC 6300 S Syracuse Way, Suite 525 Centennial, CO 80111	OGRID: 372286
	Action Number: 113099
	Action Type: [C-103] Sub. Workover (C-103R)

COMMENTS

Created By	Comment	Comment Date
jagarcia	Accepted, John Garcia, Petroleum Engineer	11/7/2022

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 113099

CONDITIONS

Operator: ENDURING RESOURCES, LLC 6300 S Syracuse Way, Suite 525 Centennial, CO 80111	OGRID: 372286
	Action Number: 113099
	Action Type: [C-103] Sub. Workover (C-103R)

CONDITIONS

Created By	Condition	Condition Date
jagarcia	None	11/7/2022
