

I. REQUEST FOR ALLOWABLE MINERAL AUTHORIZATION TO TRANSPORT

¹ Operator name and Address EOG RESOURCES INC PO BOX 2267 MIDLAND, TEXAS 79702		² OGRID Number 7377
		³ Reason for Filing Code/ Effective Date NW 12/12/2021
⁴ API Number 30 - 025-48837	⁵ Pool Name WC025 G08 S253235G; LOWER BONE SPRING	
		⁶ Pool Code 97903
⁷ Property Code 330803	⁸ Property Name JEFE 29 FEDERAL COM	
		⁹ Well Number 502H

II. ¹⁰ Surface Location

Ul or lot no. L	Section 29	Township 25S	Range 32E	Lot Idn	Feet from the 2128'	North/South Line SOUTH	Feet from the 595'	East/West line WEST	County LEA
--------------------	---------------	-----------------	--------------	---------	------------------------	---------------------------	-----------------------	------------------------	---------------

¹¹ Bottom Hole Location

UL or lot no. M	Section 32	Township 25S	Range 32E	Lot Idn	Feet from the 111'	North/South line SOUTH	Feet from the 1130'	East/West line WEST	County LEA
¹² Lse Code	¹³ Producing Method Code FLOWING	¹⁴ Gas Connection Date	¹⁵ C-129 Permit Number		¹⁶ C-129 Effective Date		¹⁷ C-129 Expiration Date		

III. Oil and Gas Transporters

¹⁸ Transporter OGRID	¹⁹ Transporter Name and Address	²⁰ O/G/W
372812	EOGRM	OIL
151618	ENTERPRISE FIELD SERVICES	GAS
298751	REGENCY FIELD SERVICES	GAS
36785	DCP MIDSTREAM	GAS

IV. Well Completion Data

²¹ Spud Date 07/18/2021	²² Ready Date 12/12/2021	²³ TD 17,896'	²⁴ PBDT 17,874'	²⁵ Perforations 10,530 - 17,874'	²⁶ DHC, MC
²⁷ Hole Size		²⁸ Casing & Tubing Size		²⁹ Depth Set	³⁰ Sacks Cement
16"		13 3/8"		1148'	670 SXS CL C/CIRC
12 1/4"		9 5/8"		4425'	1290 SXS CL C&H/CIRC
8 1/2"		6"		17,881'	2230 SXS CL H TOC 1100' CBL

V. Well Test Data

³¹ Date New Oil 12/12/2021	³² Gas Delivery Date 12/12/2021	³³ Test Date 12/23/2021	³⁴ Test Length 24 HRS	³⁵ Tbg. Pressure	³⁶ Csg. Pressure 919
³⁷ Choke Size 128	³⁸ Oil 3276	³⁹ Water 7017	⁴⁰ Gas 6448		⁴¹ Test Method
⁴² I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief. Signature: Kay Maddox			OIL CONSERVATION DIVISION		
Printed name: Kay Maddox			Approved by: <i>PATRICIA MARTINEZ</i>		
Title: SENIOR REGULATORY SPECIALIST			Title: <i>PETROLEUM SPECIALIST</i>		
E-mail Address: kay_maddox@eogresources.com			Approval Date: <i>11/30/2022</i>		
Date: 01/06/2022		Phone: 432-638-8475			

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources
Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

FORM C-102

Revised August 1, 2011

Submit one copy to appropriate

District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-025-48837	² Pool Code 97903	³ Pool Name WC025 G08 S253235G; LOWER BONE SPRING
⁴ Property Code 330803	⁵ Property Name JEFE 29 FED COM	⁶ Well Number 502H
⁷ OGRID No. 7377	⁸ Operator Name EOG RESOURCES, INC.	⁹ Elevation 3360'

¹⁰Surface Location


UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
L	29	25-S	32-E	-	2128'	SOUTH	595'	WEST	LEA

¹¹Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
M	32	25-S	32-E	-	111'	SOUTH	1130'	WEST	LEA

¹² Dedicated Acres 480.00	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.
--	-------------------------------	----------------------------------	-------------------------

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

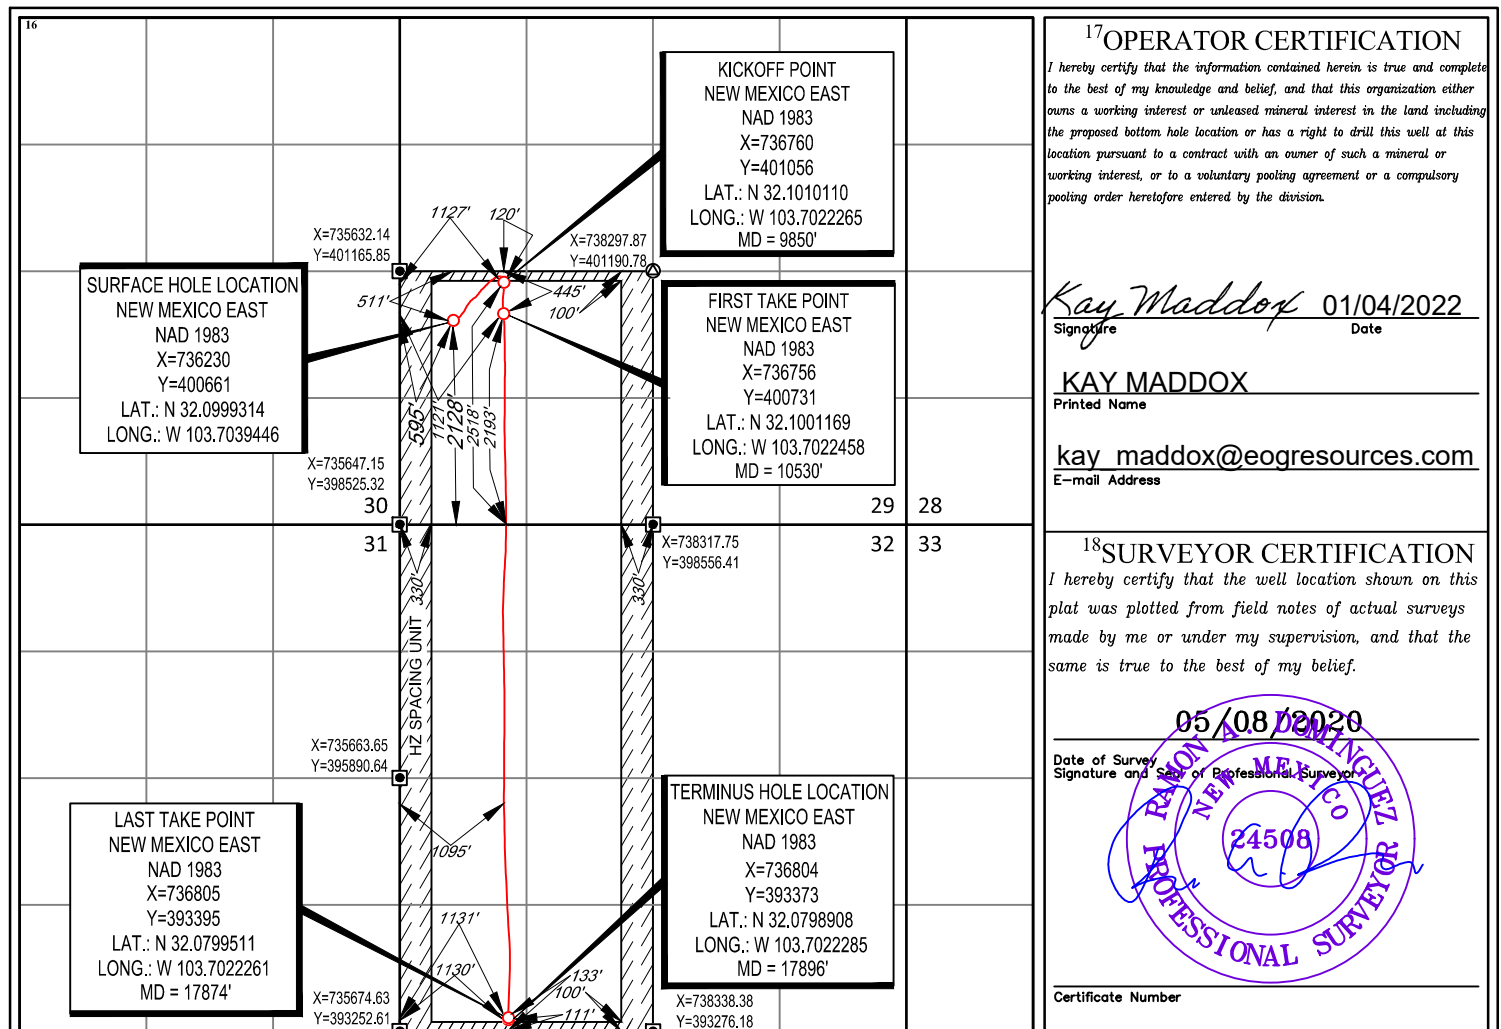



Midland

Lea County, NM (NAD 83 NME)

Jefe 29 Fed Com

#502H

OH

Design: OH

Final PVA

23 August, 2021



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #502H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 25' @ 3385.0usft
Site:	Jefe 29 Fed Com	MD Reference:	kb = 25' @ 3385.0usft
Well:	#502H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Project	Lea County, NM (NAD 83 NME)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Jefe 29 Fed Com		
Site Position:		Northing:	400,660.00 usft
From:	Map	Easting:	736,197.00 usft
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "
		Latitude:	32° 5' 59.750 N
		Longitude:	103° 42' 14.588 W
		Grid Convergence:	0.33 °

Well		#502H				
Well Position	+N/-S	0.0 usft	Northing:	400,661.00 usft	Latitude:	32° 5' 59.758 N
	+E/-W	0.0 usft	Easting:	736,230.00 usft	Longitude:	103° 42' 14.204 W
Position Uncertainty	0.0 usft		Wellhead Elevation:	usft	Ground Level:	3,360.0 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	7/15/2020	6.70	59.80	47,502.63840906

Design	OH			
Audit Notes:				
Version:	1.0	Phase:	ACTUAL	Tie On Depth: 0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0	0.0	0.0	175.58

Survey Program	Date	8/23/2021		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description
199.0	17,896.0	Pro MWD #1 (OH)	EOG MWD+IFR1	MWD + IFR1



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #502H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 25' @ 3385.0usft
Site:	Jefe 29 Fed Com	MD Reference:	kb = 25' @ 3385.0usft
Well:	#502H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.0	0.0	
199.0	0.35	156.70	199.0	-0.6	0.2	0.18	0.18	0.00	-0.6	0.0	
289.0	0.40	124.00	289.0	-1.0	0.6	0.24	0.06	-36.33	-1.1	-0.5	
381.0	0.25	119.43	381.0	-1.3	1.1	0.17	-0.16	-4.97	-1.5	-0.6	
470.0	0.83	124.44	470.0	-1.7	1.8	0.65	0.65	5.63	-2.4	-0.4	
560.0	1.54	123.56	560.0	-2.8	3.3	0.79	0.79	-0.98	-4.3	-0.5	
651.0	2.50	83.49	650.9	-3.2	6.3	1.82	1.05	-44.03	-5.9	-3.9	
788.0	2.37	44.55	787.8	-0.9	11.2	1.19	-0.09	-28.42	-7.3	-8.6	
832.0	2.86	30.84	831.8	0.7	12.4	1.80	1.11	-31.16	-7.0	-10.3	
923.0	3.30	36.46	922.6	4.8	15.2	0.59	0.48	6.18	-12.9	-9.4	
1,014.0	3.65	45.87	1,013.5	8.9	18.8	0.73	0.38	10.34	-19.7	-6.7	
1,086.0	4.39	51.41	1,085.3	12.2	22.6	1.16	1.03	7.69	-25.3	-4.6	
1,282.0	5.27	61.07	1,280.6	21.3	36.3	0.61	0.45	4.93	-42.1	1.0	
1,371.0	5.58	59.49	1,369.2	25.4	43.6	0.39	0.35	-1.78	-50.5	-0.2	
1,462.0	5.71	59.40	1,459.7	30.0	51.4	0.14	0.14	-0.10	-59.5	-0.3	
1,552.0	5.32	58.70	1,549.3	34.4	58.8	0.44	-0.43	-0.78	-68.1	-1.1	
1,643.0	4.39	60.28	1,640.0	38.4	65.4	1.03	-1.02	1.74	-75.8	0.9	
1,734.0	3.91	61.60	1,730.8	41.6	71.2	0.54	-0.53	1.45	-82.4	2.7	
1,824.0	3.74	49.12	1,820.6	44.9	76.1	0.94	-0.19	-13.87	-86.9	-15.8	
1,915.0	7.38	32.77	1,911.1	51.8	81.5	4.32	4.00	-17.97	-87.5	-40.8	
2,005.0	4.22	34.71	2,000.7	59.4	86.5	3.52	-3.51	2.16	-98.0	-37.4	
2,097.0	3.87	31.81	2,092.4	64.8	90.1	0.44	-0.38	-3.15	-101.1	-41.9	
2,187.0	3.78	35.59	2,182.2	69.8	93.4	0.30	-0.10	4.20	-105.2	-33.9	
2,278.0	3.87	37.43	2,273.0	74.7	97.0	0.17	0.10	2.02	-105.0	-29.0	
2,369.0	3.78	37.61	2,363.8	79.5	100.7	0.10	-0.10	0.20	-100.8	-26.7	
2,460.0	3.78	33.65	2,454.6	84.4	104.2	0.29	0.00	-4.35	-91.7	-30.3	
2,550.0	3.78	75.58	2,544.4	87.6	108.7	3.00	0.00	46.59	-81.1	33.7	



Final PVA

Company: Midland
Project: Lea County, NM (NAD 83 NME)
Site: Jefe 29 Fed Com
Well: #502H
Wellbore: OH
Design: OH

Local Co-ordinate Reference: Well #502H
TVD Reference: kb = 25' @ 3385.0usft
MD Reference: kb = 25' @ 3385.0usft
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
2,640.0	3.65	30.58	2,634.3	90.8	113.0	3.16	-0.14	-50.00	-72.7	-30.8	
2,731.0	6.15	27.68	2,724.9	97.6	116.8	2.76	2.75	-3.19	-65.3	-29.3	
2,822.0	5.93	26.53	2,815.4	106.1	121.1	0.28	-0.24	-1.26	-60.8	-25.4	
2,912.0	5.32	25.65	2,905.0	114.0	125.0	0.68	-0.68	-0.98	-56.0	-20.8	
3,003.0	7.03	26.27	2,995.5	122.8	129.3	1.88	1.88	0.68	-52.6	-14.7	
3,093.0	6.46	28.38	3,084.8	132.2	134.2	0.69	-0.63	2.34	-50.2	-7.7	
3,184.0	6.02	27.50	3,175.3	141.0	138.8	0.49	-0.48	-0.97	-46.4	-3.5	
3,274.0	5.89	27.59	3,264.8	149.2	143.1	0.14	-0.14	0.10	-42.4	1.7	
3,364.0	6.28	33.65	3,354.3	157.4	148.0	0.83	0.43	6.73	-37.6	10.2	
3,455.0	7.78	37.43	3,444.6	166.5	154.5	1.72	1.65	4.15	-33.8	15.7	
3,545.0	7.16	37.61	3,533.9	175.7	161.6	0.69	-0.69	0.20	-31.4	18.5	
3,636.0	6.59	35.41	3,624.2	184.5	168.1	0.69	-0.63	-2.42	-28.8	20.3	
3,726.0	6.42	35.23	3,713.6	192.8	174.0	0.19	-0.19	-0.20	-25.1	23.4	
3,817.0	5.98	41.56	3,804.1	200.5	180.1	0.89	-0.48	6.96	-17.8	28.3	
3,907.0	6.06	46.48	3,893.6	207.3	186.6	0.58	0.09	5.47	-10.5	30.6	
3,998.0	6.90	44.20	3,984.0	214.5	193.9	0.97	0.92	-2.51	-7.5	31.0	
4,088.0	6.50	50.44	4,073.4	221.6	201.6	0.92	-0.44	6.93	-0.3	31.7	
4,178.0	6.20	55.45	4,162.8	227.6	209.5	0.70	-0.33	5.57	6.8	30.3	
4,269.0	5.45	63.27	4,253.4	232.4	217.5	1.20	-0.82	8.59	15.6	26.0	
4,359.0	6.81	54.57	4,342.9	237.4	225.6	1.83	1.51	-9.67	16.2	25.9	
4,478.0	5.67	53.95	4,461.2	244.9	236.1	0.96	-0.96	-0.52	21.8	24.2	
4,569.0	6.77	40.24	4,551.6	251.7	243.2	2.02	1.21	-15.07	20.1	29.6	
4,660.0	6.59	38.05	4,642.0	259.9	249.9	0.34	-0.20	-2.41	22.7	32.7	
4,751.0	6.24	35.50	4,732.4	268.0	256.0	0.50	-0.38	-2.80	25.2	36.7	
4,842.0	9.84	40.16	4,822.5	278.0	263.9	4.02	3.96	5.12	29.7	37.0	
4,932.0	8.57	38.31	4,911.4	289.1	273.0	1.45	-1.41	-2.06	28.2	40.1	
5,023.0	7.65	36.29	5,001.5	299.3	280.8	1.06	-1.01	-2.22	28.0	43.9	



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #502H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 25' @ 3385.0usft
Site:	Jefe 29 Fed Com	MD Reference:	kb = 25' @ 3385.0usft
Well:	#502H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
5,114.0	7.12	33.65	5,091.7	308.9	287.5	0.69	-0.58	-2.90	28.3	48.5	
5,204.0	10.06	49.30	5,180.7	318.7	296.6	4.14	3.27	17.39	41.3	40.5	
5,295.0	9.49	42.27	5,270.4	329.4	307.6	1.45	-0.63	-7.73	35.1	45.7	
5,385.0	8.31	47.27	5,359.3	339.3	317.4	1.57	-1.31	5.56	39.2	43.4	
5,476.0	7.21	46.04	5,449.5	347.7	326.3	1.22	-1.21	-1.35	40.5	44.7	
5,567.0	6.20	43.41	5,539.8	355.3	333.8	1.16	-1.11	-2.89	42.2	47.5	
5,657.0	6.15	36.55	5,629.3	362.7	340.0	0.82	-0.06	-7.62	40.6	54.5	
5,748.0	9.49	48.77	5,719.5	371.5	348.6	4.08	3.67	13.43	53.4	45.7	
5,839.0	9.18	44.55	5,809.3	381.7	359.3	0.83	-0.34	-4.64	49.6	49.8	
5,929.0	9.14	41.30	5,898.1	392.2	369.1	0.58	-0.04	-3.61	46.6	53.9	
6,020.0	10.28	50.88	5,987.8	402.7	380.1	2.17	1.25	10.53	54.0	46.1	
6,110.0	10.72	54.66	6,076.3	412.6	393.2	0.91	0.49	4.20	54.6	41.4	
6,201.0	9.36	54.04	6,165.9	421.9	406.1	1.50	-1.49	-0.68	52.7	40.5	
6,292.0	8.70	51.49	6,255.8	430.5	417.5	0.85	-0.73	-2.80	51.0	41.6	
6,383.0	8.17	50.00	6,345.8	438.9	427.8	0.63	-0.58	-1.64	51.0	42.3	
6,473.0	8.48	67.84	6,434.9	445.5	438.9	2.88	0.34	19.82	61.4	22.3	
6,564.0	7.73	68.81	6,525.0	450.3	450.8	0.84	-0.82	1.07	59.0	17.6	
6,655.0	7.95	70.39	6,615.1	454.6	462.4	0.34	0.24	1.74	54.2	13.2	
6,746.0	7.69	72.41	6,705.3	458.6	474.1	0.42	-0.29	2.22	46.7	9.5	
6,837.0	6.15	78.74	6,795.6	461.4	484.7	1.89	-1.69	6.96	38.2	3.9	
6,927.0	5.63	105.19	6,885.1	461.1	493.7	3.04	-0.58	29.39	27.2	-11.4	
7,018.0	5.93	110.21	6,975.7	458.3	502.4	0.65	0.33	5.52	17.0	-13.4	
7,109.0	4.22	114.16	7,066.3	455.4	509.9	1.92	-1.88	4.34	8.0	-14.2	
7,200.0	3.21	129.01	7,157.1	452.4	514.9	1.52	-1.11	16.32	-1.7	-14.9	
7,290.0	3.56	171.29	7,247.0	448.0	517.3	2.74	0.39	46.98	-15.9	-8.2	
7,381.0	2.59	167.33	7,337.8	443.2	518.2	1.09	-1.07	-4.35	-20.2	-9.5	
7,471.0	1.23	150.81	7,427.8	440.4	519.1	1.61	-1.51	-18.36	-19.6	-15.4	



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #502H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 25' @ 3385.0usft
Site:	Jefe 29 Fed Com	MD Reference:	kb = 25' @ 3385.0usft
Well:	#502H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
7,562.0	1.49	160.04	7,518.8	438.4	520.0	0.37	0.29	10.14	-23.9	-11.9	
7,652.0	1.76	168.48	7,608.7	436.0	520.7	0.40	0.30	9.38	-28.0	-8.1	
7,743.0	0.40	123.92	7,699.7	434.4	521.2	1.65	-1.49	-48.97	-15.6	-26.4	
7,833.0	0.44	107.74	7,789.7	434.2	521.8	0.14	0.04	-17.98	-8.3	-29.7	
7,924.0	0.70	119.70	7,880.7	433.8	522.6	0.31	0.29	13.14	-15.1	-27.3	
8,014.0	0.88	121.46	7,970.7	433.1	523.7	0.20	0.20	1.96	-17.2	-26.8	
8,105.0	1.10	150.63	8,061.7	432.0	524.7	0.60	0.24	32.05	-29.6	-14.7	
8,195.0	1.19	169.79	8,151.7	430.3	525.3	0.43	0.10	21.29	-34.5	-3.9	
8,286.0	1.05	171.82	8,242.7	428.6	525.6	0.16	-0.15	2.23	-36.4	-2.6	
8,376.0	1.10	180.78	8,332.6	426.9	525.7	0.19	0.06	9.96	-38.1	3.2	
8,467.0	1.19	191.15	8,423.6	425.1	525.5	0.25	0.10	11.40	-38.7	10.2	
8,557.0	1.27	203.19	8,513.6	423.3	524.9	0.30	0.09	13.38	-37.6	18.2	
8,648.0	0.92	208.12	8,604.6	421.7	524.2	0.40	-0.38	5.42	-37.6	21.5	
8,738.0	0.88	233.43	8,694.6	420.7	523.3	0.44	-0.04	28.12	-26.2	35.8	
8,829.0	0.70	269.55	8,785.6	420.2	522.2	0.57	-0.20	39.69	-1.2	44.8	
8,919.0	0.66	297.50	8,875.6	420.5	521.2	0.37	-0.04	31.06	18.9	40.3	
9,010.0	0.26	141.67	8,966.6	420.5	520.8	0.99	-0.44	-171.24	-33.5	-29.3	
9,100.0	1.05	133.06	9,056.5	419.8	521.6	0.88	0.88	-9.57	-29.8	-34.0	
9,190.0	2.02	137.98	9,146.5	418.1	523.2	1.09	1.08	5.47	-35.0	-31.3	
9,280.1	2.24	155.75	9,236.6	415.3	525.0	0.77	0.24	19.73	-46.1	-18.6	
HL Crossing, MD:9280.1', TVD:9236.6', N/S:415.3', E/W:525.0', INC:2.24											
9,281.0	2.24	155.91	9,237.5	415.3	525.0	0.77	0.35	17.51	-46.2	-18.5	
9,372.0	2.24	160.65	9,328.4	412.0	526.3	0.20	0.00	5.21	-51.1	-14.4	
9,462.0	2.50	164.79	9,418.3	408.4	527.4	0.35	0.29	4.60	-55.8	-10.6	
9,553.0	1.93	158.10	9,509.2	405.1	528.5	0.69	-0.63	-7.35	-57.7	-17.2	
9,643.0	2.07	166.81	9,599.2	402.1	529.5	0.37	0.16	9.68	-62.7	-8.1	
9,734.0	1.67	178.58	9,690.1	399.2	529.9	0.61	-0.44	12.93	-66.0	5.2	



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #502H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 25' @ 3385.0usft
Site:	Jefe 29 Fed Com	MD Reference:	kb = 25' @ 3385.0usft
Well:	#502H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
9,824.0	1.45	184.56	9,780.1	396.7	529.8	0.30	-0.24	6.64	-66.1	12.1	
9,850.0	2.43	193.43	9,806.1	395.9	529.7	3.94	3.77	34.10	-61.8	21.5	
KOP (MD=9850.0')											
9,914.0	4.92	199.85	9,870.0	391.9	528.4	3.94	3.89	10.04	-51.9	24.1	
10,005.0	10.11	180.96	9,960.2	380.3	526.9	6.24	5.70	-20.76	-38.1	4.4	
10,096.0	14.99	173.57	10,049.0	360.6	528.1	5.63	5.36	-8.12	-13.2	3.6	
10,186.0	25.36	180.08	10,133.3	329.7	529.4	11.77	11.52	7.23	14.0	5.8	
10,231.0	29.40	184.65	10,173.3	309.0	528.5	10.11	8.98	10.16	27.1	3.2	
10,277.0	33.18	186.85	10,212.6	285.2	526.1	8.58	8.22	4.78	40.3	-1.1	
10,322.0	42.19	186.41	10,248.2	257.9	522.9	20.03	20.02	-0.98	51.4	-4.8	
10,367.0	53.44	183.24	10,278.3	224.8	520.2	25.53	25.00	-7.04	58.1	-6.0	
10,412.0	65.35	179.73	10,301.2	186.1	519.3	27.30	26.47	-7.80	58.9	-5.2	
10,447.0	74.84	177.35	10,313.1	153.3	520.1	27.86	27.11	-6.80	55.1	-3.6	
10,479.0	83.14	176.12	10,319.2	121.9	521.9	26.21	25.94	-3.84	48.4	-1.8	
10,570.0	87.28	175.68	10,326.8	31.5	528.4	4.57	4.55	-0.48	28.2	3.6	
10,660.0	88.15	177.26	10,330.4	-58.2	533.9	2.00	0.97	1.76	17.5	8.2	
10,751.0	91.36	179.11	10,330.8	-149.2	536.8	4.07	3.53	2.03	15.8	10.6	
10,842.0	93.21	179.72	10,327.2	-240.1	537.8	2.14	2.03	0.67	12.2	11.0	
10,932.0	94.70	179.29	10,321.0	-329.9	538.5	1.72	1.66	-0.48	6.0	11.3	
11,022.0	95.93	178.41	10,312.6	-419.5	540.3	1.68	1.37	-0.98	-2.3	12.7	
11,042.0	93.52	178.58	10,311.0	-439.4	540.9	12.08	-12.05	0.85	-4.0	13.1	
11,072.0	91.93	179.73	10,309.5	-469.4	541.3	6.54	-5.30	3.83	-5.4	13.4	
11,113.0	92.02	179.64	10,308.1	-510.3	541.5	0.31	0.22	-0.22	-6.8	13.4	
11,160.0	89.47	182.01	10,307.5	-557.3	540.8	7.41	-5.43	5.04	-7.4	12.5	
11,203.0	86.97	180.52	10,308.9	-600.3	539.9	6.77	-5.81	-3.47	-6.1	11.3	
11,249.0	86.31	180.34	10,311.6	-646.2	539.6	1.49	-1.43	-0.39	-3.4	10.7	
11,294.0	85.91	180.17	10,314.6	-691.1	539.4	0.97	-0.89	-0.38	-0.3	10.3	



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #502H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 25' @ 3385.0usft
Site:	Jefe 29 Fed Com	MD Reference:	kb = 25' @ 3385.0usft
Well:	#502H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
11,384.0	87.10	180.34	10,320.1	-780.9	539.0	1.34	1.32	0.19	5.1	9.4
11,474.0	88.46	180.60	10,323.6	-870.8	538.2	1.54	1.51	0.29	8.6	8.2
11,565.0	90.88	180.52	10,324.1	-961.8	537.3	2.66	2.66	-0.09	9.1	6.8
11,654.0	91.58	180.34	10,322.2	-1,050.8	536.7	0.81	0.79	-0.20	7.2	5.7
11,744.0	91.80	179.64	10,319.5	-1,140.8	536.7	0.81	0.24	-0.78	4.6	5.2
11,834.0	92.15	179.02	10,316.4	-1,230.7	537.7	0.79	0.39	-0.69	1.5	5.8
11,925.0	92.50	178.14	10,312.7	-1,321.6	540.0	1.04	0.38	-0.97	-2.2	7.6
12,015.0	89.91	178.93	10,310.9	-1,411.6	542.3	3.01	-2.88	0.88	-4.1	9.4
12,106.0	89.82	179.11	10,311.1	-1,502.5	543.8	0.22	-0.10	0.20	-3.9	10.5
12,197.0	87.54	178.06	10,313.2	-1,593.5	546.1	2.76	-2.51	-1.15	-1.8	12.2
12,287.0	86.13	178.32	10,318.1	-1,683.3	548.9	1.59	-1.57	0.29	3.1	14.6
12,378.0	91.45	179.81	10,320.1	-1,774.2	550.4	6.07	5.85	1.64	5.1	15.6
12,468.0	92.55	179.99	10,316.9	-1,864.2	550.6	1.24	1.22	0.20	1.9	15.3
12,558.0	92.11	179.11	10,313.3	-1,954.1	551.3	1.09	-0.49	-0.98	-1.7	15.5
12,649.0	91.58	179.81	10,310.3	-2,045.0	552.1	0.96	-0.58	0.77	-4.6	15.9
12,739.0	91.23	180.43	10,308.1	-2,135.0	551.9	0.79	-0.39	0.69	-6.9	15.2
12,829.0	87.41	180.34	10,309.2	-2,225.0	551.3	4.25	-4.24	-0.10	-5.8	14.1
12,920.0	88.86	181.04	10,312.1	-2,315.9	550.2	1.77	1.59	0.77	-2.8	12.6
12,979.0	83.23	182.27	10,316.2	-2,374.7	548.5	9.77	-9.54	2.08	1.3	10.5
13,010.0	83.14	182.27	10,319.9	-2,405.5	547.3	0.29	-0.29	0.00	4.9	9.2
13,100.0	84.07	183.59	10,329.9	-2,494.8	542.7	1.79	1.03	1.47	14.9	4.1
13,190.0	87.41	183.07	10,336.6	-2,584.4	537.5	3.76	3.71	-0.58	21.6	-1.6
13,210.0	90.40	182.80	10,337.0	-2,604.4	536.5	15.01	14.95	-1.35	22.0	-2.7
13,281.0	90.79	182.80	10,336.2	-2,675.3	533.0	0.55	0.55	0.00	21.3	-6.5
13,340.0	90.48	182.54	10,335.6	-2,734.2	530.3	0.69	-0.53	-0.44	20.6	-9.6
13,372.0	90.22	182.54	10,335.4	-2,766.2	528.9	0.81	-0.81	0.00	20.4	-11.2
13,463.0	92.37	182.80	10,333.3	-2,857.1	524.6	2.38	2.36	0.29	18.4	-15.9



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #502H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 25' @ 3385.0usft
Site:	Jefe 29 Fed Com	MD Reference:	kb = 25' @ 3385.0usft
Well:	#502H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
13,554.0	92.37	181.84	10,329.6	-2,947.9	521.0	1.05	0.00	-1.05	14.6	-20.0	
13,644.0	92.55	179.99	10,325.7	-3,037.8	519.5	2.06	0.20	-2.06	10.7	-22.0	
13,734.0	90.04	178.41	10,323.7	-3,127.8	520.8	3.30	-2.79	-1.76	8.7	-21.2	
13,825.0	91.63	178.85	10,322.4	-3,218.7	523.0	1.81	1.75	0.48	7.4	-19.5	
13,916.0	91.63	179.02	10,319.8	-3,309.7	524.6	0.19	0.00	0.19	4.8	-18.3	
14,007.0	90.26	178.67	10,318.3	-3,400.6	526.5	1.55	-1.51	-0.38	3.3	-16.9	
14,097.0	90.35	179.20	10,317.8	-3,490.6	528.1	0.60	0.10	0.59	2.8	-15.7	
14,188.0	89.96	178.93	10,317.5	-3,581.6	529.6	0.52	-0.43	-0.30	2.6	-14.7	
14,278.0	89.34	178.76	10,318.1	-3,671.6	531.4	0.71	-0.69	-0.19	3.1	-13.4	
14,369.0	88.20	178.76	10,320.0	-3,762.5	533.4	1.25	-1.25	0.00	5.1	-11.9	
14,459.0	87.63	178.76	10,323.3	-3,852.5	535.4	0.63	-0.63	0.00	8.3	-10.4	
14,550.0	91.32	180.52	10,324.2	-3,943.4	535.9	4.49	4.05	1.93	9.2	-10.3	
14,641.0	89.38	180.34	10,323.6	-4,034.4	535.3	2.14	-2.13	-0.20	8.6	-11.5	
14,732.0	92.11	180.43	10,322.4	-4,125.4	534.6	3.00	3.00	0.10	7.4	-12.6	
14,823.0	91.89	179.64	10,319.2	-4,216.4	534.6	0.90	-0.24	-0.87	4.3	-13.1	
14,914.0	92.59	180.60	10,315.7	-4,307.3	534.4	1.30	0.77	1.05	0.7	-13.8	
15,005.0	92.15	180.25	10,311.9	-4,398.2	533.7	0.62	-0.48	-0.38	-3.1	-14.9	
15,096.0	92.02	179.99	10,308.6	-4,489.1	533.5	0.32	-0.14	-0.29	-6.4	-15.6	
15,186.0	90.44	180.43	10,306.7	-4,579.1	533.2	1.82	-1.76	0.49	-8.3	-16.4	
15,277.0	90.35	180.43	10,306.0	-4,670.1	532.5	0.10	-0.10	0.00	-8.9	-17.6	
15,368.0	88.68	180.43	10,306.8	-4,761.1	531.8	1.84	-1.84	0.00	-8.2	-18.7	
15,458.0	88.77	180.60	10,308.8	-4,851.1	531.0	0.21	0.10	0.19	-6.2	-20.0	
15,549.0	88.81	181.04	10,310.7	-4,942.0	529.7	0.49	0.04	0.48	-4.3	-21.8	
15,640.0	88.73	178.93	10,312.7	-5,033.0	529.7	2.32	-0.09	-2.32	-2.3	-22.3	
15,730.0	89.17	178.58	10,314.3	-5,123.0	531.7	0.62	0.49	-0.39	-0.6	-20.8	
15,821.0	89.47	178.76	10,315.4	-5,214.0	533.8	0.38	0.33	0.20	0.4	-19.1	
15,912.0	89.17	178.85	10,316.5	-5,304.9	535.7	0.34	-0.33	0.10	1.5	-17.7	



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #502H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 25' @ 3385.0usft
Site:	Jefe 29 Fed Com	MD Reference:	kb = 25' @ 3385.0usft
Well:	#502H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
16,003.0	88.68	178.93	10,318.2	-5,395.9	537.5	0.55	-0.54	0.09	3.2	-16.4	
16,093.0	88.81	178.41	10,320.2	-5,485.8	539.6	0.60	0.14	-0.58	5.2	-14.8	
16,183.0	88.73	178.06	10,322.1	-5,575.8	542.3	0.40	-0.09	-0.39	7.1	-12.5	
16,274.0	89.08	177.88	10,323.9	-5,666.7	545.6	0.43	0.38	-0.20	8.9	-9.8	
16,365.0	87.50	176.74	10,326.6	-5,757.6	549.8	2.14	-1.74	-1.25	11.6	-6.0	
16,455.0	89.69	177.18	10,328.8	-5,847.4	554.6	2.48	2.43	0.49	13.8	-1.7	
16,546.0	90.31	177.26	10,328.8	-5,938.3	559.0	0.69	0.68	0.09	13.8	2.2	
16,636.0	91.41	177.79	10,327.4	-6,028.2	562.9	1.36	1.22	0.59	12.4	5.6	
16,727.0	91.98	177.71	10,324.7	-6,119.1	566.5	0.63	0.63	-0.09	9.7	8.7	
16,818.0	91.89	177.09	10,321.7	-6,209.9	570.6	0.69	-0.10	-0.68	6.7	12.4	
16,909.0	91.58	176.74	10,318.9	-6,300.8	575.5	0.51	-0.34	-0.38	3.9	16.8	
17,000.0	90.00	175.24	10,317.7	-6,391.5	581.9	2.39	-1.74	-1.65	2.7	22.7	
17,091.0	90.70	176.21	10,317.1	-6,482.3	588.6	1.31	0.77	1.07	2.1	29.0	
17,181.0	92.29	178.76	10,314.7	-6,572.1	592.6	3.34	1.77	2.83	-0.2	32.5	
17,272.0	91.23	179.73	10,312.0	-6,663.1	593.8	1.58	-1.16	1.07	-3.0	33.2	
17,362.0	91.32	181.31	10,310.0	-6,753.1	593.0	1.76	0.10	1.76	-5.1	31.9	
17,453.0	89.25	181.92	10,309.5	-6,844.0	590.4	2.37	-2.27	0.67	-5.5	28.8	
17,543.0	90.13	182.27	10,310.0	-6,934.0	587.1	1.05	0.98	0.39	-5.0	25.1	
17,634.0	90.00	182.98	10,309.9	-7,024.9	582.9	0.79	-0.14	0.78	-5.1	20.4	
17,725.0	86.44	181.84	10,312.7	-7,115.7	579.1	4.11	-3.91	-1.25	-2.3	16.1	
17,816.0	86.40	181.66	10,318.4	-7,206.5	576.3	0.20	-0.04	-0.20	3.4	12.9	
Final MWD Survey (MD=17816.0')											
17,896.0	86.40	181.66	10,323.4	-7,286.3	574.0	0.00	0.00	0.00	8.4	10.1	
Final Projection to Bit (MD=17896.0')											



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #502H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 25' @ 3385.0usft
Site:	Jefe 29 Fed Com	MD Reference:	kb = 25' @ 3385.0usft
Well:	#502H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Design Annotations					
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates			
		+N/-S (usft)	+E/-W (usft)	Comment	
9,280.1	9,236.6	415.3	525.0	HL Crossing, MD:9280.1', TVD:9236.6', N/S:415.3', E/W:525.0', INC:2.24	
9,850.0	9,806.1	395.9	529.7	KOP (MD=9850.0')	
17,816.0	10,318.4	-7,206.5	576.3	Final MWD Survey (MD=17816.0')	
17,896.0	10,323.4	-7,286.3	574.0	Final Projection to Bit (MD=17896.0')	

Checked By: _____ Approved By: _____ Date: _____

I CERTIFY THIS SURVEY TO BE TRUE AND CORRECT TO THE BEST OF MY BELIEF AND KNOWLEDGE
KAY MADDOX 01/03/2022

Intent ☐ As Drilled ☐

API #		
Operator Name:	Property Name:	Well Number

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude			NAD	

First Take Point (FTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude			NAD	

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude			NAD	

Is this well the defining well for the Horizontal Spacing Unit? ☐Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018

Submit To Appropriate District Office Two Copies <u>District I</u> 1625 N. French Dr., Hobbs, NM 88240 <u>District II</u> 811 S. First St., Artesia, NM 88210 <u>District III</u> 1000 Rio Brazos Rd., Aztec, NM 87410 <u>District IV</u> 1220 S. St. Francis Dr., Santa Fe, NM 87505		State of New Mexico Energy, Minerals and Natural Resources Oil Conservation Division 1220 South St. Francis Dr. Santa Fe, NM 87505			Form C-105 Revised August 1, 2011					
WELL COMPLETION OR RECOMPLETION REPORT AND LOG										
4. Reason for filing: ☒ COMPLETION REPORT (Fill in boxes #1 through #31 for State and Fee wells only) ☐ C-144 CLOSURE ATTACHMENT (Fill in boxes #1 through #9, #15 Date Rig Released and #32 and/or #33; attach this and the plat to the C-144 closure report in accordance with 19.15.17.13.K NMAC)								5. Lease Name or Unit Agreement Name JEFE 29 FEDERAL COM		
								6. Well Number: 502H		
7. Type of Completion: ☒ NEW WELL ☐ WORKOVER ☐ DEEPENING ☐ PLUGBACK ☐ DIFFERENT RESERVOIR ☐ OTHER _____										
8. Name of Operator EOG RESOURCES INC						9. OGRID 7377				
10. Address of Operator PO BOX 2267 MIDLAND, TEXAS 79702						11. Pool name or Wildcat WC025 G08 S253235G; LOWER BONE SPRING				
12. Location	Unit Ltr	Section	Township	Range	Lot	Feet from the	N/S Line	Feet from the	E/W Line	County
Surface:	L	29	25S	32E		2128	SOUTH	595	WEST	LEA
BH:	M	32	25S	32E		111	SOUTH	1130	WEST	LEA
13. Date Spudded 07/18/2021	14. Date T.D. Reached 08/14/2021		15. Date Rig Released 08/15/2021			16. Date Completed (Ready to Produce) 12/12/2021		17. Elevations (DF and RKB, RT, GR, etc.) 3360' GL		
18. Total Measured Depth of Well MD 17,896' TVD 10,323'			19. Plug Back Measured Depth MD 17,874' TVD 10,323'			20. Was Directional Survey Made? YES		21. Type Electric and Other Logs Run None		
22. Producing Interval(s), of this completion - Top, Bottom, Name BONE SPRING 10,530 - 17,874'										
23. CASING RECORD (Report all strings set in well)										
CASING SIZE		WEIGHT LB./FT.		DEPTH SET		HOLE SIZE		CEMENTING RECORD		AMOUNT PULLED
13 3/8"		54.5# J-55		1,148'		16"		670 CL C/CIRC		
9 5/8"		40# HCL 80		4,425'		12 1/4"		1290 CL C & H/CIRC		
6"		24.5# ECP 110		17,881'		8 1/2"		2230 CL H TOC 1100' CB		
24. LINER RECORD						25. TUBING RECORD				
SIZE	TOP	BOTTOM	SACKS CEMENT	SCREEN		SIZE	DEPTH SET	PACKER SET		
26. Perforation record (interval, size, and number) 10,530 - 17,874' 3 1/8", 1500 holes						27. ACID, SHOT, FRACTURE, CEMENT, SQUEEZE, ETC.				
						DEPTH INTERVAL		AMOUNT AND KIND MATERIAL USED		
						10,530 - 17,874'		FRAC W/18,202,725 lbs proppant, 285,403 bbls load fld		
28. PRODUCTION										
Date First Production 12/12/2021		Production Method (<i>Flowing, gas lift, pumping - Size and type pump</i>) Flowing				Well Status (<i>Prod. or Shut-in</i>) Producing				
Date of Test 12/23/2021	Hours Tested 24	Choke Size 128	Prod'n For Test Period	Oil - Bbl 3276	Gas - MCF 6448	Water - Bbl. 7017	Gas - Oil Ratio 1968			
Flow Tubing Press.	Casing Pressure 919	Calculated 24-Hour Rate	Oil - Bbl.	Gas - MCF	Water - Bbl.	Oil Gravity - API - (<i>Corr.</i>) 46				
29. Disposition of Gas (<i>Sold, used for fuel, vented, etc.</i>) SOLD								30. Test Witnessed By		
31. List Attachments C-102, C-104, Directional Survey, H spacing										
32. If a temporary pit was used at the well, attach a plat with the location of the temporary pit.										
33. If an on-site burial was used at the well, report the exact location of the on-site burial:										
Latitude _____				Longitude _____				NAD 1927 1983		
<i>I hereby certify that the information shown on both sides of this form is true and complete to the best of my knowledge and belief</i>										
Signature Kay Maddox			Name Kay Maddox			Title Senior Regulatory Specialist			Date 01/05/2022	
E-mail Address kay_maddox@eogresources.com										

This form is to be filed with the appropriate District Office of the Division not later than 20 days after the completion of any newly-drilled or deepened well and not later than 60 days after completion of closure. When submitted as a completion report, this shall be accompanied by one copy of all electrical and radio-activity logs run on the well and a summary of all special tests conducted, including drill stem tests. All depths reported shall be measured depths. In the case of directionally drilled wells, true vertical depths shall also be reported. For multiple completions, items 11, 12 and 26-31 shall be reported for each zone.

Southeastern New Mexico			Northwestern New Mexico				
T. Anhy	Rustler	1036'	T. Canyon	Brushy	6811'	T. Ojo Alamo	T. Penn A "
T. Salt		1118'	T. Strawn			T. Kirtland	T. Penn. "B"
B. Salt		4305'	T. Atoka			T. Fruitland	T. Penn. "C"
T. Yates			T. Miss			T. Pictured Cliffs	T. Penn. "D"
T. 7 Rivers			T. Devonian			T. Cliff House	T. Leadville
T. Queen			T. Silurian			T. Menefee	T. Madison
T. Grayburg			T. Montoya			T. Point Lookout	T. Elbert
T. San Andres			T. Simpson			T. Mancos	T. McCracken
T. Glorieta			T. McKee			T. Gallup	T. Ignacio Otzte
T. Paddock			T. Ellenburger			Base Greenhorn	T. Granite
T. Blinebry			T. Gr. Wash			T. Dakota	
T. Tubb			T. Delaware Sand			T. Morrison	
T. Drinkard			T. Bone Springs			T. Todilto	
T. Abo			T. 1st BS Sand	9544'		T. Entrada	
T. Wolfcamp			T. 2nd BS Sand	10,159'		T. Wingate	
T. Penn			T.			T. Chinle	
T. Cisco (Bough C)			T.			T. Permian	

No. 1, from.....to.....
No. 2, from.....to.....
No. 3, from.....to.....
No. 4, from.....to.....

Include data on rate of water inflow and elevation to which water rose in hole.

No. 1, from.....to.....feet.....
 No. 2, from.....to.....feet.....
 No. 3, from.....to.....feet.....

From	To	Thickness In Feet	Lithology

From	To	Thickness In Feet	Lithology

District I

1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

ACKNOWLEDGMENTS

Action 70890

ACKNOWLEDGMENTS

Operator: EOG RESOURCES INC P.O. Box 2267 Midland, TX 79702	OGRID: 7377
	Action Number: 70890
	Action Type: [C-104] Completion Packet (C-104C)

ACKNOWLEDGMENTS

☒	I hereby certify that the required Water Use Report has been, or will be, submitted for this wells completion.
☒	I hereby certify that the required FracFocus disclosure has been, or will be, submitted for this wells completion.

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720

District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720

District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170

District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 70890

CONDITIONS

Operator: EOG RESOURCES INC P.O. Box 2267 Midland, TX 79702	OGRID: 7377
	Action Number: 70890
	Action Type: [C-104] Completion Packet (C-104C)

CONDITIONS

Created By	Condition	Condition Date
plmartinez	None	11/30/2022
