

Form 3160-3  
(June 2015)

FORM APPROVED  
OMB No. 1004-0137  
Expires: January 31, 2018

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT  
**APPLICATION FOR PERMIT TO DRILL OR REENTER**

1a. Type of work:  DRILL  REENTER  
1b. Type of Well:  Oil Well  Gas Well  Other  
1c. Type of Completion:  Hydraulic Fracturing  Single Zone  Multiple Zone

5. Lease Serial No.

6. If Indian, Allottee or Tribe Name

7. If Unit or CA Agreement, Name and No.

8. Lease Name and Well No.

[334072]

2. Name of Operator

[372098]

9. API Well No.

30-025-51535

3a. Address

3b. Phone No. (include area code)

10. Field and Pool, or Exploratory  
XXXXXXXXXXXXXXXXXX

[17645]

4. Location of Well (Report location clearly and in accordance with any State requirements. \*)

At surface

At proposed prod. zone

11. Sec., T. R. M. or Blk. and Survey or Area

14. Distance in miles and direction from nearest town or post office\*

12. County or Parish

13. State

15. Distance from proposed\* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)

16. No of acres in lease

17. Spacing Unit dedicated to this well

18. Distance from proposed location\* to nearest well, drilling, completed, applied for, on this lease, ft.

19. Proposed Depth

20. BLM/BIA Bond No. in file

21. Elevations (Show whether DF, KDB, RT, GL, etc.)

22. Approximate date work will start\*

23. Estimated duration

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- 1. Well plat certified by a registered surveyor.
- 2. A Drilling Plan.
- 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).

- 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- 5. Operator certification.
- 6. Such other site specific information and/or plans as may be requested by the BLM.

25. Signature

Name (Printed/Typed)

Date

Title

Approved by (Signature)

Name (Printed/Typed)

Date

Title

Office

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.  
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

NGMP Rec 05/23/2023

SL



KZ  
05/31/2023

(Continued on page 2)

\*(Instructions on page 2)

State of New Mexico  
Energy, Minerals and Natural Resources Department

Submit Electronically  
Via E-permitting

Oil Conservation Division  
1220 South St. Francis Dr.  
Santa Fe, NM 87505

### NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

#### Section 1 – Plan Description Effective May 25, 2021

**I. Operator:** MARATHON OIL PERMIAN, LLC. **OGRID:** 372098 **Date:** 03 / 23 / 2023

**II. Type:**  Original  Amendment due to  19.15.27.9.D(6)(a) NMAC  19.15.27.9.D(6)(b) NMAC  Other.

If Other, please describe: \_\_\_\_\_

**III. Well(s):** Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
COLIBRI 10 TB FEDERAL 5H		O-10-23S-32E	393 FSL 1587 FEL	1800	2600	5400
COLIBRI 10 TB FEDERAL 7H		O-10-23S-32E	393 FSL 1527 FEL	1800	2600	5400
COLIBRI 10 WA FEDERAL 10H		O-10-23S-32E	392 FSL 1437 FEL	1400	2400	4100
COLIBRI 10 WA FEDERL 8H		O-10-23S-32E	392 FSL 1497 FEL	1400	2400	4100

**IV. Central Delivery Point Name:** COLIBRI 10 FED COM CTB [See 19.15.27.9(D)(1) NMAC]

**V. Anticipated Schedule:** Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
COLIBRI 10 TB FEDERAL 5H		7/1/2023	9/6/2023	10/1/2023	12/1/2023	12/1/2023
COLIBRI 10 TB FEDERAL 7H		6/28/2023	8/15/2023	10/1/2023	12/1/2023	12/1/2023
COLIBRI 10 WA FEDERAL 10H		6/26/2023	7/23/2023	10/1/2023	12/1/2023	12/1/2023
COLIBRI 10 WA FEDERL 8H		7/3/2023	9/1/2023	10/1/2023	12/1/2023	12/1/2023

**VI. Separation Equipment:**  Attach a complete description of how Operator will size separation equipment to optimize gas capture.

**VII. Operational Practices:**  Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

**VIII. Best Management Practices:**  Attach a complete description of Operator’s best management practices to minimize venting during active and planned maintenance.

**Section 2 – Enhanced Plan**  
**EFFECTIVE APRIL 1, 2022**

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

**IX. Anticipated Natural Gas Production:**

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

**X. Natural Gas Gathering System (NGGS):**

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

**XI. Map.**  Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

**XII. Line Capacity.** The natural gas gathering system  will  will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

**XIII. Line Pressure.** Operator  does  does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

Attach Operator’s plan to manage production in response to the increased line pressure.

**XIV. Confidentiality:**  Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

### **Section 3 - Certifications**

**Effective May 25, 2021**

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

***If Operator checks this box, Operator will select one of the following:***

**Well Shut-In.**  Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

**Venting and Flaring Plan.**  Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

### **Section 4 - Notices**

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature:



Printed Name:

Adrian Covarrubias

Title:

Adv. Regulatory Compliance Representative

E-mail Address:

acovarrubias@marathonoil.com

Date:

03/23/2023

Phone:

713-296-3368

**OIL CONSERVATION DIVISION**  
**(Only applicable when submitted as a standalone form)**

Approved By:

Title:

Approval Date:

Conditions of Approval:

**APPENDIX**

## Section 1 - Parts VI, VII, and VIII

**VI. Separation Equipment:**  Attach a complete description of how Operator will size separation equipment to optimize gas capture.

- Separation equipment is sized to allow for retention time and velocity to adequately separate oil, gas, and water at anticipated peak rates.
- All central tank battery equipment is designed to efficiently capture the remaining gas from the liquid phase.
- Valves and meters are designed to service without flow interruption or venting of gas.

**VII. Operational Practices:**  Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

- ◆ **19.15.27.8 (A) – Venting and Flaring Of Natural Gas**
  - Marathon Oil Permian’s field operations are designed with the goal of minimizing flaring and preventing venting of natural gas. If capturing the gas is not possible then the gas is combusted/flared using properly sized flares or combustors in accordance with state air permit rules.
- ◆ **19.15.27.8 (B) – Venting and Flaring During Drilling Operations**
  - A properly-sized flare stack will be located at a minimum 100’ from the nearest surface hole location on the pad.
  - All natural gas produced during drilling operations will be flared. Venting will only occur if there is an equipment malfunction and/or to avoid risk of an immediate and substantial adverse impact on safety, public health, or the environment.
- ◆ **19.15.27.8 (C) – Venting and Flaring During Completion or Recompletion Operations**
  - During all phases of flowback, wells will flow through a sand separator, or other appropriate flowback separation equipment, and the well stream will be directed to a central tank battery (CTB) through properly sized flowlines.
  - The CTB will have properly sized separation equipment for maximum anticipated flow rates.
  - Multiple stages of separation will be used to separate gas from liquids. All gas will be routed to a sales outlet. Fluids will be routed to tanks equipped with a closed loop system that will recover any residual gas from the tanks and route such gas to a sales outlet.
- ◆ **19.15.27.8 (D) – Venting and Flaring During Production Operations**
  - During production, the well stream will be routed to the CTB where multiple stages of separation will separate gas from liquids. All gas will be routed to a sales outlet. Fluids will be routed to tanks equipped with a closed loop system that will recover any residual gas from the tanks and route such gas to a sales outlet, minimizing tank emissions.
  - Flares are equipped with auto-ignition systems and continuous pilot operations.
  - Automatic gauging equipment is installed on all tanks.
- ◆ **19.15.27.8 (E) – Performance Standards**
  - Production equipment will be designed to handle maximum anticipated rates and pressure.
  - Automatic gauging equipment is installed on all tanks to minimize venting.
  - All flared gas will be combusted in a flare stack that is properly sized and designed to ensure proper combustion.
  - Flares are equipped with continuous pilots and auto-ignitors along with remote monitoring of the pilot status.
  - Weekly AVOs and monthly LDAR inspections will be performed on all wells and facilities that produce more than 60 MCFD.
  - Gas/H<sub>2</sub>S detectors will be installed throughout the facilities and wellheads to detect leaks and enable timely repairs.

◆ **19.15.27.8 (F) – Measurement or Estimation of Vented and Flared Natural Gas**

- All high pressure flared gas is measured by equipment conforming to API 14.10.
- No meter bypasses are installed.
- When metering is not practical due to low pressure/low rate, the vented or flared volume will be estimated through flare flow curves with the assistance of air emissions consultants, as necessary.

**VIII. Best Management Practices:**  Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

- Marathon Oil Permian will use best management practices to vent as minimally as possible during well intervention operations and downhole well maintenance.
- All natural gas is routed into the gas gathering system and directed to one of Marathon Oil Permian's multiple gas sales outlets.
- All venting events will be recorded and all start-up, shutdown, maintenance logs will be kept for control equipment.
- All control equipment will be maintained to provide highest run-time possible.
- All procedures are drafted to keep venting and flaring to the absolute minimum.

# **Marathon Oil Corporation**

**Lea County, NM**

**Colibri 10**

**Colibri 10 WA Federal 10H**

**Wellbore #1**

**Plan: Preliminary Plan #1**

## **Standard Planning Report - Geographic**

**11 November, 2020**

Planning Report - Geographic

<b>Database:</b>	EDM 5000.15 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Colibri 10 WA Federal 10H
<b>Company:</b>	Marathon Oil Corporation	<b>TVD Reference:</b>	KB Elev Est. @ 3732.00usft
<b>Project:</b>	Lea County, NM	<b>MD Reference:</b>	KB Elev Est. @ 3732.00usft
<b>Site:</b>	Colibri 10	<b>North Reference:</b>	Grid
<b>Well:</b>	Colibri 10 WA Federal 10H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Preliminary Plan #1		

<b>Project</b>	Lea County, NM		
<b>Map System:</b>	US State Plane 1927 (Exact solution)	<b>System Datum:</b>	Mean Sea Level
<b>Geo Datum:</b>	NAD 1927 (NADCON CONUS)		
<b>Map Zone:</b>	New Mexico East 3001		

<b>Site</b>	Colibri 10				
<b>Site Position:</b>	<b>Northing:</b>	478,199.33 usft	<b>Latitude:</b>	32.31288268	
<b>From:</b> Map	<b>Easting:</b>	708,447.44 usft	<b>Longitude:</b>	-103.65861624	
<b>Position Uncertainty:</b>	0.00 usft	<b>Slot Radius:</b>	13-3/16 "	<b>Grid Convergence:</b>	0.36 °

<b>Well</b>	Colibri 10 WA Federal 10H					
<b>Well Position</b>	<b>+N/-S</b>	0.00 usft	<b>Northing:</b>	478,199.33 usft	<b>Latitude:</b>	32.31288009
	<b>+E/-W</b>	0.00 usft	<b>Easting:</b>	708,597.44 usft	<b>Longitude:</b>	-103.65813073
<b>Position Uncertainty</b>	0.00 usft		<b>Wellhead Elevation:</b>		<b>Ground Level:</b>	3,707.00 usft

<b>Wellbore</b>	Wellbore #1				
<b>Magnetics</b>	<b>Model Name</b>	<b>Sample Date</b>	<b>Declination (°)</b>	<b>Dip Angle (°)</b>	<b>Field Strength (nT)</b>
	IGRF2020	11/10/2020	6.66	59.99	47,597.52131997

<b>Design</b>	Preliminary Plan #1			
<b>Audit Notes:</b>				
<b>Version:</b>	<b>Phase:</b>	PLAN	<b>Tie On Depth:</b>	0.00
<b>Vertical Section:</b>	<b>Depth From (TVD) (usft)</b>	<b>+N/-S (usft)</b>	<b>+E/-W (usft)</b>	<b>Direction (°)</b>
	0.00	0.00	0.00	359.62

<b>Plan Survey Tool Program</b>	<b>Date</b>	11/11/2020		
<b>Depth From (usft)</b>	<b>Depth To (usft)</b>	<b>Survey (Wellbore)</b>	<b>Tool Name</b>	<b>Remarks</b>
1	0.00	17,396.07 Preliminary Plan #1 (Wellbore #1)	MWD+IFR1 OWSG MWD + IFR1	

<b>Plan Sections</b>										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,500.00	0.00	0.00	1,500.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,000.00	2.50	104.29	1,999.84	-2.69	10.57	0.50	0.50	0.00	104.29	
2,999.51	10.00	104.29	2,992.71	-29.52	115.91	0.75	0.75	0.00	0.00	
8,695.45	10.00	104.29	8,602.17	-273.55	1,074.05	0.00	0.00	0.00	0.00	
9,095.30	0.00	0.00	9,000.00	-282.14	1,107.77	2.50	-2.50	0.00	180.00	VP (Colibri 10 WA Fed
12,047.84	0.00	0.00	11,952.54	-282.14	1,107.77	0.00	0.00	0.00	0.00	
12,797.84	90.00	359.62	12,430.00	195.31	1,104.60	12.00	12.00	0.00	359.62	
17,396.07	90.00	359.62	12,430.00	4,793.45	1,074.10	0.00	0.00	0.00	0.00	PBHL-10' (Colibri 10 \

Planning Report - Geographic

<b>Database:</b>	EDM 5000.15 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Colibri 10 WA Federal 10H
<b>Company:</b>	Marathon Oil Corporation	<b>TVD Reference:</b>	KB Elev Est. @ 3732.00usft
<b>Project:</b>	Lea County, NM	<b>MD Reference:</b>	KB Elev Est. @ 3732.00usft
<b>Site:</b>	Colibri 10	<b>North Reference:</b>	Grid
<b>Well:</b>	Colibri 10 WA Federal 10H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Preliminary Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Map Northing (usft)	Map Easting (usft)	Latitude	Longitude	
0.00	0.00	0.00	0.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
100.00	0.00	0.00	100.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
200.00	0.00	0.00	200.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
300.00	0.00	0.00	300.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
400.00	0.00	0.00	400.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
500.00	0.00	0.00	500.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
600.00	0.00	0.00	600.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
700.00	0.00	0.00	700.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
800.00	0.00	0.00	800.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
900.00	0.00	0.00	900.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
1,000.00	0.00	0.00	1,000.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
1,100.00	0.00	0.00	1,100.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
1,171.00	0.00	0.00	1,171.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
<b>Rustler</b>										
1,200.00	0.00	0.00	1,200.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
1,300.00	0.00	0.00	1,300.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
1,400.00	0.00	0.00	1,400.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
1,500.00	0.00	0.00	1,500.00	0.00	0.00	478,199.33	708,597.44	32.31288009	-103.65813073	
<b>KOP - Build @ 0.5°/100'</b>										
1,600.00	0.50	104.29	1,600.00	-0.11	0.42	478,199.22	708,597.86	32.31287978	-103.65812937	
1,646.00	0.73	104.29	1,646.00	-0.23	0.90	478,199.10	708,598.34	32.31287944	-103.65812782	
<b>Salado</b>										
1,700.00	1.00	104.29	1,699.99	-0.43	1.69	478,198.90	708,599.13	32.31287887	-103.65812527	
1,800.00	1.50	104.29	1,799.97	-0.97	3.81	478,198.36	708,601.24	32.31287736	-103.65811844	
1,900.00	2.00	104.29	1,899.92	-1.72	6.76	478,197.61	708,604.20	32.31287523	-103.65810888	
2,000.00	2.50	104.29	1,999.84	-2.69	10.57	478,196.64	708,608.01	32.31287250	-103.65809658	
<b>Continue Build 0.75°/100'</b>										
2,100.00	3.25	104.29	2,099.71	-3.93	15.43	478,195.40	708,612.87	32.31286902	-103.65808087	
2,200.00	4.00	104.29	2,199.51	-5.49	21.56	478,193.84	708,618.99	32.31286462	-103.65806108	
2,300.00	4.75	104.29	2,299.22	-7.37	28.95	478,191.96	708,626.38	32.31285932	-103.65803719	
2,400.00	5.50	104.29	2,398.82	-9.58	37.61	478,189.75	708,635.04	32.31285311	-103.65800921	
2,500.00	6.25	104.29	2,498.30	-12.10	47.52	478,187.23	708,644.96	32.31284599	-103.65797716	
2,600.00	7.00	104.29	2,597.63	-14.95	58.70	478,184.38	708,656.14	32.31283797	-103.65794103	
2,700.00	7.75	104.29	2,696.80	-18.12	71.14	478,181.21	708,668.58	32.31282905	-103.65790084	
2,800.00	8.50	104.29	2,795.79	-21.61	84.84	478,177.72	708,682.28	32.31281922	-103.65785658	
2,900.00	9.25	104.29	2,894.60	-25.42	99.79	478,173.91	708,697.23	32.31280850	-103.65780826	
2,999.51	10.00	104.29	2,992.71	-29.52	115.91	478,169.81	708,713.35	32.31279693	-103.65775617	
<b>EOB - Hold @ 10.00 INC, 104.29 AZI</b>										
3,000.00	10.00	104.29	2,993.19	-29.54	115.99	478,169.79	708,713.43	32.31279687	-103.65775591	
3,100.00	10.00	104.29	3,091.67	-33.83	132.81	478,165.50	708,730.25	32.31278480	-103.65770155	
3,200.00	10.00	104.29	3,190.15	-38.11	149.64	478,161.22	708,747.07	32.31277274	-103.65764719	
3,300.00	10.00	104.29	3,288.63	-42.40	166.46	478,156.94	708,763.89	32.31276067	-103.65759283	
3,400.00	10.00	104.29	3,387.12	-46.68	183.28	478,152.65	708,780.71	32.31274860	-103.65753847	
3,500.00	10.00	104.29	3,485.60	-50.96	200.10	478,148.37	708,797.54	32.31273653	-103.65748412	
3,569.46	10.00	104.29	3,554.00	-53.94	211.78	478,145.39	708,809.22	32.31272815	-103.65744636	
<b>Castile</b>										
3,600.00	10.00	104.29	3,584.08	-55.25	216.92	478,144.08	708,814.36	32.31272446	-103.65742976	
3,700.00	10.00	104.29	3,682.56	-59.53	233.74	478,139.80	708,831.18	32.31271240	-103.65737540	
3,800.00	10.00	104.29	3,781.04	-63.82	250.56	478,135.51	708,848.00	32.31270033	-103.65732104	
3,900.00	10.00	104.29	3,879.53	-68.10	267.39	478,131.23	708,864.82	32.31268826	-103.65726668	
4,000.00	10.00	104.29	3,978.01	-72.39	284.21	478,126.95	708,881.64	32.31267619	-103.65721232	
4,100.00	10.00	104.29	4,076.49	-76.67	301.03	478,122.66	708,898.47	32.31266412	-103.65715797	
4,200.00	10.00	104.29	4,174.97	-80.95	317.85	478,118.38	708,915.29	32.31265206	-103.65710361	
4,300.00	10.00	104.29	4,273.45	-85.24	334.67	478,114.09	708,932.11	32.31263999	-103.65704925	

Planning Report - Geographic

<b>Database:</b>	EDM 5000.15 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Colibri 10 WA Federal 10H
<b>Company:</b>	Marathon Oil Corporation	<b>TVD Reference:</b>	KB Elev Est. @ 3732.00usft
<b>Project:</b>	Lea County, NM	<b>MD Reference:</b>	KB Elev Est. @ 3732.00usft
<b>Site:</b>	Colibri 10	<b>North Reference:</b>	Grid
<b>Well:</b>	Colibri 10 WA Federal 10H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Preliminary Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Map Northing (usft)	Map Easting (usft)	Latitude	Longitude	
4,400.00	10.00	104.29	4,371.93	-89.52	351.49	478,109.81	708,948.93	32.31262792	-103.65699489	
4,500.00	10.00	104.29	4,470.42	-93.81	368.32	478,105.52	708,965.75	32.31261585	-103.65694053	
4,600.00	10.00	104.29	4,568.90	-98.09	385.14	478,101.24	708,982.57	32.31260378	-103.65688617	
4,700.00	10.00	104.29	4,667.38	-102.38	401.96	478,096.96	708,999.39	32.31259171	-103.65683182	
4,800.00	10.00	104.29	4,765.86	-106.66	418.78	478,092.67	709,016.22	32.31257964	-103.65677746	
4,900.00	10.00	104.29	4,864.34	-110.94	435.60	478,088.39	709,033.04	32.31256758	-103.65672310	
4,928.08	10.00	104.29	4,892.00	-112.15	440.33	478,087.18	709,037.76	32.31256419	-103.65670784	
<b>Lamar/Base of Salt</b>										
4,980.88	10.00	104.29	4,944.00	-114.41	449.21	478,084.92	709,046.64	32.31255782	-103.65667913	
<b>Bell Canyon</b>										
5,000.00	10.00	104.29	4,962.83	-115.23	452.42	478,084.10	709,049.86	32.31255551	-103.65666874	
5,100.00	10.00	104.29	5,061.31	-119.51	469.24	478,079.82	709,066.68	32.31254344	-103.65661438	
5,200.00	10.00	104.29	5,159.79	-123.80	486.07	478,075.53	709,083.50	32.31253137	-103.65656003	
5,300.00	10.00	104.29	5,258.27	-128.08	502.89	478,071.25	709,100.32	32.31251930	-103.65650567	
5,400.00	10.00	104.29	5,356.75	-132.37	519.71	478,066.96	709,117.15	32.31250723	-103.65645131	
5,500.00	10.00	104.29	5,455.24	-136.65	536.53	478,062.68	709,133.97	32.31249517	-103.65639695	
5,600.00	10.00	104.29	5,553.72	-140.93	553.35	478,058.40	709,150.79	32.31248310	-103.65634259	
5,700.00	10.00	104.29	5,652.20	-145.22	570.17	478,054.11	709,167.61	32.31247103	-103.65628824	
5,800.00	10.00	104.29	5,750.68	-149.50	587.00	478,049.83	709,184.43	32.31245896	-103.65623388	
5,900.00	10.00	104.29	5,849.16	-153.79	603.82	478,045.54	709,201.25	32.31244689	-103.65617952	
6,000.00	10.00	104.29	5,947.64	-158.07	620.64	478,041.26	709,218.07	32.31243482	-103.65612516	
6,100.00	10.00	104.29	6,046.13	-162.36	637.46	478,036.97	709,234.90	32.31242275	-103.65607080	
6,120.18	10.00	104.29	6,066.00	-163.22	640.85	478,036.11	709,238.29	32.31242032	-103.65605984	
<b>Cherry Canyon</b>										
6,200.00	10.00	104.29	6,144.61	-166.64	654.28	478,032.69	709,251.72	32.31241068	-103.65601645	
6,300.00	10.00	104.29	6,243.09	-170.92	671.10	478,028.41	709,268.54	32.31239862	-103.65596209	
6,400.00	10.00	104.29	6,341.57	-175.21	687.92	478,024.12	709,285.36	32.31238655	-103.65590773	
6,500.00	10.00	104.29	6,440.05	-179.49	704.75	478,019.84	709,302.18	32.31237448	-103.65585337	
6,600.00	10.00	104.29	6,538.54	-183.78	721.57	478,015.55	709,319.00	32.31236241	-103.65579902	
6,700.00	10.00	104.29	6,637.02	-188.06	738.39	478,011.27	709,335.82	32.31235034	-103.65574466	
6,800.00	10.00	104.29	6,735.50	-192.35	755.21	478,006.98	709,352.65	32.31233827	-103.65569030	
6,900.00	10.00	104.29	6,833.98	-196.63	772.03	478,002.70	709,369.47	32.31232620	-103.65563594	
7,000.00	10.00	104.29	6,932.46	-200.91	788.85	477,998.42	709,386.29	32.31231413	-103.65558158	
7,100.00	10.00	104.29	7,030.95	-205.20	805.68	477,994.13	709,403.11	32.31230207	-103.65552723	
7,200.00	10.00	104.29	7,129.43	-209.48	822.50	477,989.85	709,419.93	32.31229000	-103.65547287	
7,220.89	10.00	104.29	7,150.00	-210.38	826.01	477,988.95	709,423.45	32.31228748	-103.65546151	
<b>Brushy Canyon</b>										
7,300.00	10.00	104.29	7,227.91	-213.77	839.32	477,985.56	709,436.75	32.31227793	-103.65541851	
7,400.00	10.00	104.29	7,326.39	-218.05	856.14	477,981.28	709,453.58	32.31226586	-103.65536415	
7,500.00	10.00	104.29	7,424.87	-222.34	872.96	477,976.99	709,470.40	32.31225379	-103.65530980	
7,600.00	10.00	104.29	7,523.35	-226.62	889.78	477,972.71	709,487.22	32.31224172	-103.65525544	
7,700.00	10.00	104.29	7,621.84	-230.90	906.60	477,968.43	709,504.04	32.31222965	-103.65520108	
7,800.00	10.00	104.29	7,720.32	-235.19	923.43	477,964.14	709,520.86	32.31221758	-103.65514672	
7,900.00	10.00	104.29	7,818.80	-239.47	940.25	477,959.86	709,537.68	32.31220551	-103.65509236	
8,000.00	10.00	104.29	7,917.28	-243.76	957.07	477,955.57	709,554.50	32.31219344	-103.65503801	
8,100.00	10.00	104.29	8,015.76	-248.04	973.89	477,951.29	709,571.33	32.31218137	-103.65498365	
8,200.00	10.00	104.29	8,114.25	-252.33	990.71	477,947.00	709,588.15	32.31216931	-103.65492929	
8,300.00	10.00	104.29	8,212.73	-256.61	1,007.53	477,942.72	709,604.97	32.31215724	-103.65487493	
8,400.00	10.00	104.29	8,311.21	-260.89	1,024.36	477,938.44	709,621.79	32.31214517	-103.65482058	
8,500.00	10.00	104.29	8,409.69	-265.18	1,041.18	477,934.15	709,638.61	32.31213310	-103.65476622	
8,600.00	10.00	104.29	8,508.17	-269.46	1,058.00	477,929.87	709,655.43	32.31212103	-103.65471186	
8,695.45	10.00	104.29	8,602.17	-273.55	1,074.05	477,925.78	709,671.49	32.31210951	-103.65465998	
<b>Start Drop @ 2.5°/100'</b>										
8,700.00	9.88	104.29	8,606.66	-273.75	1,074.82	477,925.58	709,672.25	32.31210896	-103.65465752	

Planning Report - Geographic

<b>Database:</b>	EDM 5000.15 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Colibri 10 WA Federal 10H
<b>Company:</b>	Marathon Oil Corporation	<b>TVD Reference:</b>	KB Elev Est. @ 3732.00usft
<b>Project:</b>	Lea County, NM	<b>MD Reference:</b>	KB Elev Est. @ 3732.00usft
<b>Site:</b>	Colibri 10	<b>North Reference:</b>	Grid
<b>Well:</b>	Colibri 10 WA Federal 10H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Preliminary Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Map Northing (usft)	Map Easting (usft)	Latitude	Longitude	
8,800.00	7.38	104.29	8,705.52	-277.45	1,089.36	477,921.88	709,686.80	32.31209853	-103.65461052	
8,803.51	7.29	104.29	8,709.00	-277.56	1,089.79	477,921.77	709,687.23	32.31209822	-103.65460911	
<b>Bone Spring</b>										
8,900.00	4.88	104.29	8,804.94	-280.09	1,099.71	477,919.24	709,697.15	32.31209110	-103.65457707	
9,000.00	2.38	104.29	8,904.73	-281.65	1,105.85	477,917.68	709,703.29	32.31208670	-103.65455723	
9,095.30	0.00	0.00	9,000.00	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
<b>EOD - Hold @ 0.00 INC, 0.00 AZI - VP (Colibri 10 WA Federal 10H)</b>										
9,100.00	0.00	0.00	9,004.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
9,200.00	0.00	0.00	9,104.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
9,300.00	0.00	0.00	9,204.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
9,400.00	0.00	0.00	9,304.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
9,500.00	0.00	0.00	9,404.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
9,600.00	0.00	0.00	9,504.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
9,700.00	0.00	0.00	9,604.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
9,800.00	0.00	0.00	9,704.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
9,900.00	0.00	0.00	9,804.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
9,985.30	0.00	0.00	9,890.00	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
<b>1st Bone Spring Sand</b>										
10,000.00	0.00	0.00	9,904.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
10,100.00	0.00	0.00	10,004.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
10,200.00	0.00	0.00	10,104.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
10,300.00	0.00	0.00	10,204.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
10,400.00	0.00	0.00	10,304.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
10,500.00	0.00	0.00	10,404.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
10,600.00	0.00	0.00	10,504.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
10,656.30	0.00	0.00	10,561.00	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
<b>2nd Bone Spring Sand</b>										
10,700.00	0.00	0.00	10,604.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
10,800.00	0.00	0.00	10,704.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
10,900.00	0.00	0.00	10,804.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
11,000.00	0.00	0.00	10,904.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
11,100.00	0.00	0.00	11,004.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
11,200.00	0.00	0.00	11,104.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
11,300.00	0.00	0.00	11,204.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
11,400.00	0.00	0.00	11,304.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
11,500.00	0.00	0.00	11,404.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
11,600.00	0.00	0.00	11,504.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
11,700.00	0.00	0.00	11,604.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
11,800.00	0.00	0.00	11,704.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
11,900.00	0.00	0.00	11,804.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
11,934.30	0.00	0.00	11,839.00	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
<b>3rd Bone Spring Sand</b>										
12,000.00	0.00	0.00	11,904.70	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
12,047.84	0.00	0.00	11,952.54	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
<b>Start Build @ 12°/100'</b>										
12,100.00	6.26	359.62	12,004.60	-279.29	1,107.75	477,920.04	709,705.19	32.31209314	-103.65455103	
12,200.00	18.26	359.62	12,102.14	-258.10	1,107.61	477,941.23	709,705.05	32.31215141	-103.65455105	
12,228.59	21.69	359.62	12,129.00	-248.33	1,107.55	477,951.00	709,704.98	32.31217825	-103.65455106	
<b>Wolfcamp</b>										
12,248.12	24.03	359.62	12,147.00	-240.74	1,107.50	477,958.59	709,704.93	32.31219911	-103.65455107	
<b>Wolfcamp X Sand</b>										
12,300.00	30.26	359.62	12,193.14	-217.09	1,107.34	477,982.24	709,704.77	32.31226414	-103.65455109	

Planning Report - Geographic

<b>Database:</b>	EDM 5000.15 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Colibri 10 WA Federal 10H
<b>Company:</b>	Marathon Oil Corporation	<b>TVD Reference:</b>	KB Elev Est. @ 3732.00usft
<b>Project:</b>	Lea County, NM	<b>MD Reference:</b>	KB Elev Est. @ 3732.00usft
<b>Site:</b>	Colibri 10	<b>North Reference:</b>	Grid
<b>Well:</b>	Colibri 10 WA Federal 10H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Preliminary Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Map Northing (usft)	Map Easting (usft)	Latitude	Longitude	
12,399.15	42.16	359.62	12,273.00	-158.62	1,106.95	478,040.71	709,704.39	32.31242486	-103.65455115	
<b>Wolfcamp Y Sand</b>										
12,400.00	42.26	359.62	12,273.63	-158.05	1,106.95	478,041.28	709,704.38	32.31242642	-103.65455115	
12,411.54	43.64	359.62	12,282.07	-150.19	1,106.89	478,049.14	709,704.33	32.31244803	-103.65455116	
<b>FTP (Colibri 10 WA Federal 10H)</b>										
12,500.00	54.26	359.62	12,340.08	-83.57	1,106.45	478,115.76	709,703.89	32.31263115	-103.65455122	
12,508.53	55.28	359.62	12,345.00	-76.61	1,106.41	478,122.72	709,703.84	32.31265031	-103.65455123	
<b>Wolfcamp A</b>										
12,600.00	66.26	359.62	12,389.60	3.09	1,105.88	478,202.43	709,703.31	32.31286939	-103.65455131	
12,700.00	78.26	359.62	12,420.01	98.16	1,105.25	478,297.49	709,702.68	32.31313073	-103.65455140	
12,797.84	90.00	359.62	12,430.00	195.31	1,104.60	478,394.65	709,702.04	32.31339778	-103.65455149	
<b>Landing Point - 12797.84 MD, 12430.00 TVD, 90.00 INC, 359.62 AZI - Target Centerline: 12430' KBTVD @ 0° VS, 90°</b>										
12,800.00	90.00	359.62	12,430.00	197.48	1,104.59	478,396.81	709,702.02	32.31340373	-103.65455150	
12,900.00	90.00	359.62	12,430.00	297.48	1,103.92	478,496.81	709,701.36	32.31367861	-103.65455159	
13,000.00	90.00	359.62	12,430.00	397.47	1,103.26	478,596.80	709,700.70	32.31395349	-103.65455169	
13,100.00	90.00	359.62	12,430.00	497.47	1,102.60	478,696.80	709,700.03	32.31422837	-103.65455179	
13,200.00	90.00	359.62	12,430.00	597.47	1,101.93	478,796.80	709,699.37	32.31450326	-103.65455189	
13,300.00	90.00	359.62	12,430.00	697.47	1,101.27	478,896.80	709,698.71	32.31477814	-103.65455198	
13,400.00	90.00	359.62	12,430.00	797.46	1,100.61	478,996.80	709,698.04	32.31505302	-103.65455208	
13,500.00	90.00	359.62	12,430.00	897.46	1,099.94	479,096.79	709,697.38	32.31532790	-103.65455218	
13,600.00	90.00	359.62	12,430.00	997.46	1,099.28	479,196.79	709,696.72	32.31560278	-103.65455228	
13,700.00	90.00	359.62	12,430.00	1,097.46	1,098.62	479,296.79	709,696.05	32.31587766	-103.65455237	
13,800.00	90.00	359.62	12,430.00	1,197.46	1,097.95	479,396.79	709,695.39	32.31615255	-103.65455247	
13,900.00	90.00	359.62	12,430.00	1,297.45	1,097.29	479,496.78	709,694.73	32.31642743	-103.65455257	
14,000.00	90.00	359.62	12,430.00	1,397.45	1,096.63	479,596.78	709,694.06	32.31670231	-103.65455266	
14,100.00	90.00	359.62	12,430.00	1,497.45	1,095.96	479,696.78	709,693.40	32.31697719	-103.65455276	
14,200.00	90.00	359.62	12,430.00	1,597.45	1,095.30	479,796.78	709,692.74	32.31725207	-103.65455286	
14,300.00	90.00	359.62	12,430.00	1,697.45	1,094.64	479,896.78	709,692.07	32.31752695	-103.65455296	
14,400.00	90.00	359.62	12,430.00	1,797.44	1,093.97	479,996.77	709,691.41	32.31780184	-103.65455305	
14,500.00	90.00	359.62	12,430.00	1,897.44	1,093.31	480,096.77	709,690.75	32.31807672	-103.65455315	
14,600.00	90.00	359.62	12,430.00	1,997.44	1,092.65	480,196.77	709,690.08	32.31835160	-103.65455325	
14,700.00	90.00	359.62	12,430.00	2,097.44	1,091.98	480,296.77	709,689.42	32.31862648	-103.65455335	
14,800.00	90.00	359.62	12,430.00	2,197.43	1,091.32	480,396.76	709,688.76	32.31890136	-103.65455344	
14,900.00	90.00	359.62	12,430.00	2,297.43	1,090.66	480,496.76	709,688.09	32.31917624	-103.65455354	
15,000.00	90.00	359.62	12,430.00	2,397.43	1,089.99	480,596.76	709,687.43	32.31945112	-103.65455364	
15,100.00	90.00	359.62	12,430.00	2,497.43	1,089.33	480,696.76	709,686.77	32.31972601	-103.65455373	
15,200.00	90.00	359.62	12,430.00	2,597.43	1,088.67	480,796.76	709,686.10	32.32000089	-103.65455383	
15,300.00	90.00	359.62	12,430.00	2,697.42	1,088.00	480,896.75	709,685.44	32.32027577	-103.65455393	
15,400.00	90.00	359.62	12,430.00	2,797.42	1,087.34	480,996.75	709,684.77	32.32055065	-103.65455403	
15,500.00	90.00	359.62	12,430.00	2,897.42	1,086.68	481,096.75	709,684.11	32.32082553	-103.65455412	
15,600.00	90.00	359.62	12,430.00	2,997.42	1,086.01	481,196.75	709,683.45	32.32110041	-103.65455422	
15,700.00	90.00	359.62	12,430.00	3,097.41	1,085.35	481,296.75	709,682.78	32.32137530	-103.65455432	
15,800.00	90.00	359.62	12,430.00	3,197.41	1,084.69	481,396.74	709,682.12	32.32165018	-103.65455441	
15,900.00	90.00	359.62	12,430.00	3,297.41	1,084.02	481,496.74	709,681.46	32.32192506	-103.65455451	
16,000.00	90.00	359.62	12,430.00	3,397.41	1,083.36	481,596.74	709,680.79	32.32219994	-103.65455461	
16,100.00	90.00	359.62	12,430.00	3,497.41	1,082.69	481,696.74	709,680.13	32.32247482	-103.65455471	
16,200.00	90.00	359.62	12,430.00	3,597.40	1,082.03	481,796.73	709,679.47	32.32274970	-103.65455480	
16,300.00	90.00	359.62	12,430.00	3,697.40	1,081.37	481,896.73	709,678.80	32.32302458	-103.65455490	
16,400.00	90.00	359.62	12,430.00	3,797.40	1,080.70	481,996.73	709,678.14	32.32329946	-103.65455500	
16,500.00	90.00	359.62	12,430.00	3,897.40	1,080.04	482,096.73	709,677.48	32.32357435	-103.65455509	
16,600.00	90.00	359.62	12,430.00	3,997.39	1,079.38	482,196.73	709,676.81	32.32384923	-103.65455519	
16,700.00	90.00	359.62	12,430.00	4,097.39	1,078.71	482,296.72	709,676.15	32.32412411	-103.65455529	
16,800.00	90.00	359.62	12,430.00	4,197.39	1,078.05	482,396.72	709,675.49	32.32439899	-103.65455538	
16,900.00	90.00	359.62	12,430.00	4,297.39	1,077.39	482,496.72	709,674.82	32.32467387	-103.65455548	

Planning Report - Geographic

<b>Database:</b>	EDM 5000.15 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Colibri 10 WA Federal 10H
<b>Company:</b>	Marathon Oil Corporation	<b>TVD Reference:</b>	KB Elev Est. @ 3732.00usft
<b>Project:</b>	Lea County, NM	<b>MD Reference:</b>	KB Elev Est. @ 3732.00usft
<b>Site:</b>	Colibri 10	<b>North Reference:</b>	Grid
<b>Well:</b>	Colibri 10 WA Federal 10H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Preliminary Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Map Northing (usft)	Map Easting (usft)	Latitude	Longitude	
17,000.00	90.00	359.62	12,430.00	4,397.39	1,076.72	482,596.72	709,674.16	32.32494875	-103.65455558	
17,100.00	90.00	359.62	12,430.00	4,497.38	1,076.06	482,696.71	709,673.50	32.32522363	-103.65455568	
17,200.00	90.00	359.62	12,430.00	4,597.38	1,075.40	482,796.71	709,672.83	32.32549851	-103.65455577	
17,300.00	90.00	359.62	12,430.00	4,697.38	1,074.73	482,896.71	709,672.17	32.32577340	-103.65455587	
17,396.07	90.00	359.62	12,430.00	4,793.45	1,074.10	482,992.78	709,671.53	32.32603747	-103.65455596	
<b>TD - 17396.07 MD, 12430.00 TVD - PBHL-10' (Colibri 10 WA Federal 10H) - PBHL (Colibri 10 WA Federal 10H)</b>										

Design Targets										
Target Name - hit/miss target - Shape	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude	
VP (Colibri 10 WA Feder - plan hits target center - Point	0.00	0.00	9,000.00	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
PBHL-10' (Colibri 10 WA - plan hits target center - Point	0.00	0.00	12,430.00	4,793.45	1,074.10	482,992.78	709,671.53	32.32603747	-103.65455596	
FTP (Colibri 10 WA Feder - plan misses target center by 198.23usft at 12411.53usft MD (12282.07 TVD, -150.19 N, 1106.89 E) - Point	0.00	0.00	12,430.00	-282.14	1,107.77	477,917.19	709,705.21	32.31208532	-103.65455103	
PBHL (Colibri 10 WA Feder - plan misses target center by 10.00usft at 17396.07usft MD (12430.00 TVD, 4793.45 N, 1074.10 E) - Point	0.00	0.00	12,430.00	4,803.45	1,074.03	483,002.78	709,671.47	32.32606497	-103.65455597	

Formations						
Measured Depth (usft)	Vertical Depth (usft)	Name	Lithology	Dip (°)	Dip Direction (°)	
1,171.00	1,171.00	Rustler		0.00	359.62	
1,646.00	1,646.00	Salado		0.00	359.62	
3,569.46	3,554.00	Castile		0.00	359.62	
4,928.08	4,892.00	Lamar/Base of Salt		0.00	359.62	
4,980.88	4,944.00	Bell Canyon		0.00	359.62	
6,120.18	6,066.00	Cherry Canyon		0.00	359.62	
7,220.89	7,150.00	Brushy Canyon		0.00	359.62	
8,803.51	8,709.00	Bone Spring		0.00	359.62	
9,985.30	9,890.00	1st Bone Spring Sand		0.00	359.62	
10,656.30	10,561.00	2nd Bone Spring Sand		0.00	359.62	
11,934.30	11,839.00	3rd Bone Spring Sand		0.00	359.62	
12,228.59	12,129.00	Wolfcamp		0.00	359.62	
12,248.12	12,147.00	Wolfcamp X Sand		0.00	359.62	
12,399.15	12,273.00	Wolfcamp Y Sand		0.00	359.62	
12,508.53	12,345.00	Wolfcamp A		0.00	359.62	
12,797.84	12,430.00	Target Centerline: 12430' KBTVD @ 0' \		0.00	359.62	

Planning Report - Geographic

<b>Database:</b>	EDM 5000.15 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Colibri 10 WA Federal 10H
<b>Company:</b>	Marathon Oil Corporation	<b>TVD Reference:</b>	KB Elev Est. @ 3732.00usft
<b>Project:</b>	Lea County, NM	<b>MD Reference:</b>	KB Elev Est. @ 3732.00usft
<b>Site:</b>	Colibri 10	<b>North Reference:</b>	Grid
<b>Well:</b>	Colibri 10 WA Federal 10H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Preliminary Plan #1		

Plan Annotations					
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment	
		+N/-S (usft)	+E/-W (usft)		
1,500.00	1,500.00	0.00	0.00	KOP - Build @ 0.5°/100'	
2,000.00	1,999.84	-2.69	10.57	Continue Build 0.75°/100'	
2,999.51	2,992.71	-29.52	115.91	EOB - Hold @ 10.00 INC, 104.29 AZI	
8,695.45	8,602.17	-273.55	1,074.05	Start Drop @ 2.5°/100'	
9,095.30	9,000.00	-282.14	1,107.77	EOD - Hold @ 0.00 INC, 0.00 AZI	
12,047.84	11,952.54	-282.14	1,107.77	Start Build @ 12°/100'	
12,797.84	12,430.00	195.31	1,104.60	Landing Point - 12797.84 MD, 12430.00 TVD, 90.00 INC, 359.62 AZI	
17,396.07	12,430.00	4,793.45	1,074.10	TD - 17396.07 MD, 12430.00 TVD	



**Marathon Oil Corporation**  
**Well Name: Colibri 10 WA Federal 10H**  
**Project: Lea County, NM**  
**Wellbore: Wellbore #1**  
**Plan: Preliminary Plan #1**




Map System: US State Plane 1927 (Exact solution)  
 Datum: NAD 1927 (NADCON CONUS)  
 Ellipsoid: Clarke 1866  
 Zone Name: New Mexico East 3001

Latitude: 32.31288009  
 Longitude: -103.65813073  
 Grid East: 708597.44  
 Grid North: 478199.33  
 Scale Factor: 1.000

Geomagnetic Model: IGRF2020  
 Sample Date: 10-Nov-20  
 Magnetic Declination: 6.66°  
 Dip Angle from Horizontal: 59.99°  
 Magnetic Field Strength: 47597.52131997nT

To convert a Magnetic Direction to a Grid Direction, Add 6.30°

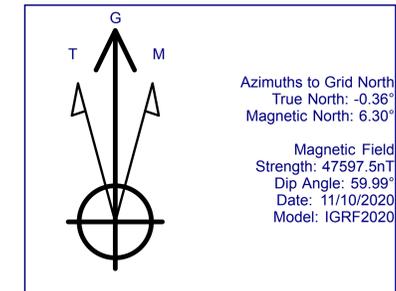



Well Planning: Chris Thomas  
 11:13, November 11 2020

SURFACE LOCATION		Ground Elevation:	3707.00	KB Elev Est. @	3732.00usft
+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
0.00	0.00	478199.33	708597.44	32.31288009	-103.65813073

TARGET LOCATIONS					
Name	TVD	+N/-S	+E/-W	Northing	Easting
VP (Colibri 10 WA Federal 10H)	9000.00	-282.14	1107.77	477917.19	709705.21
FTP (Colibri 10 WA Federal 10H)	12430.00	-282.14	1107.77	477917.19	709705.21
PBHL (Colibri 10 WA Federal 10H)	12430.00	4803.45	1074.03	483002.78	709671.47
PBHL-10' (Colibri 10 WA Federal 10H)	12430.00	4793.45	1074.10	482992.78	709671.54

Well Offset Distances			
Slot Name	+N/-S	+E/-W	
Colibri 10 TB Federal 5H	0.00	-150.00	
Colibri 10 TB Federal 7H	0.00	-90.00	
Colibri 10 TB Federal 9H	0.05	-29.96	
Colibri 10 WA Federal 10H	0.00	0.00	
Colibri 10 WA Federal 6H	0.00	-120.00	
Colibri 10 WA Federal 8H	0.00	-60.00	

SECTION DETAILS:										
Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VFace	Annotation
1	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	KOP - Build @ 0.5°/100'
2	1500.00	0.00	0.00	1500.00	0.00	0.00	0.00	0.00	0.00	Continue Build 0.75°/100'
3	2000.00	2.50	104.29	1999.84	-2.69	10.57	0.50	104.29	-2.76	EOB - Hold @ 10.00 INC, 104.29 AZI
4	2999.51	10.00	104.29	2992.71	-29.52	115.91	0.75	0.00	-30.29	Start Drop @ 2.5°/100'
5	8695.45	10.00	104.29	8602.17	-273.55	1074.05	0.00	0.00	-280.67	EOD - Hold @ 0.00 INC, 0.00 AZI
6	9095.30	0.00	0.00	9000.00	-282.14	1107.77	2.50	180.00	-289.48	Start Build @ 12°/100'
7	12047.84	0.00	0.00	11952.54	-282.14	1107.77	0.00	0.00	-289.48	Landing Point - 12797.84 MD, 12430.00 TVD, 90.00 INC, 359.62 AZI
8	12797.84	90.00	359.62	12430.00	195.31	1104.60	12.00	359.62	187.98	TD - 17396.07 MD, 12430.00 TVD
9	17396.07	90.00	359.62	12430.00	4793.45	1074.10	0.00	0.00	4786.22	

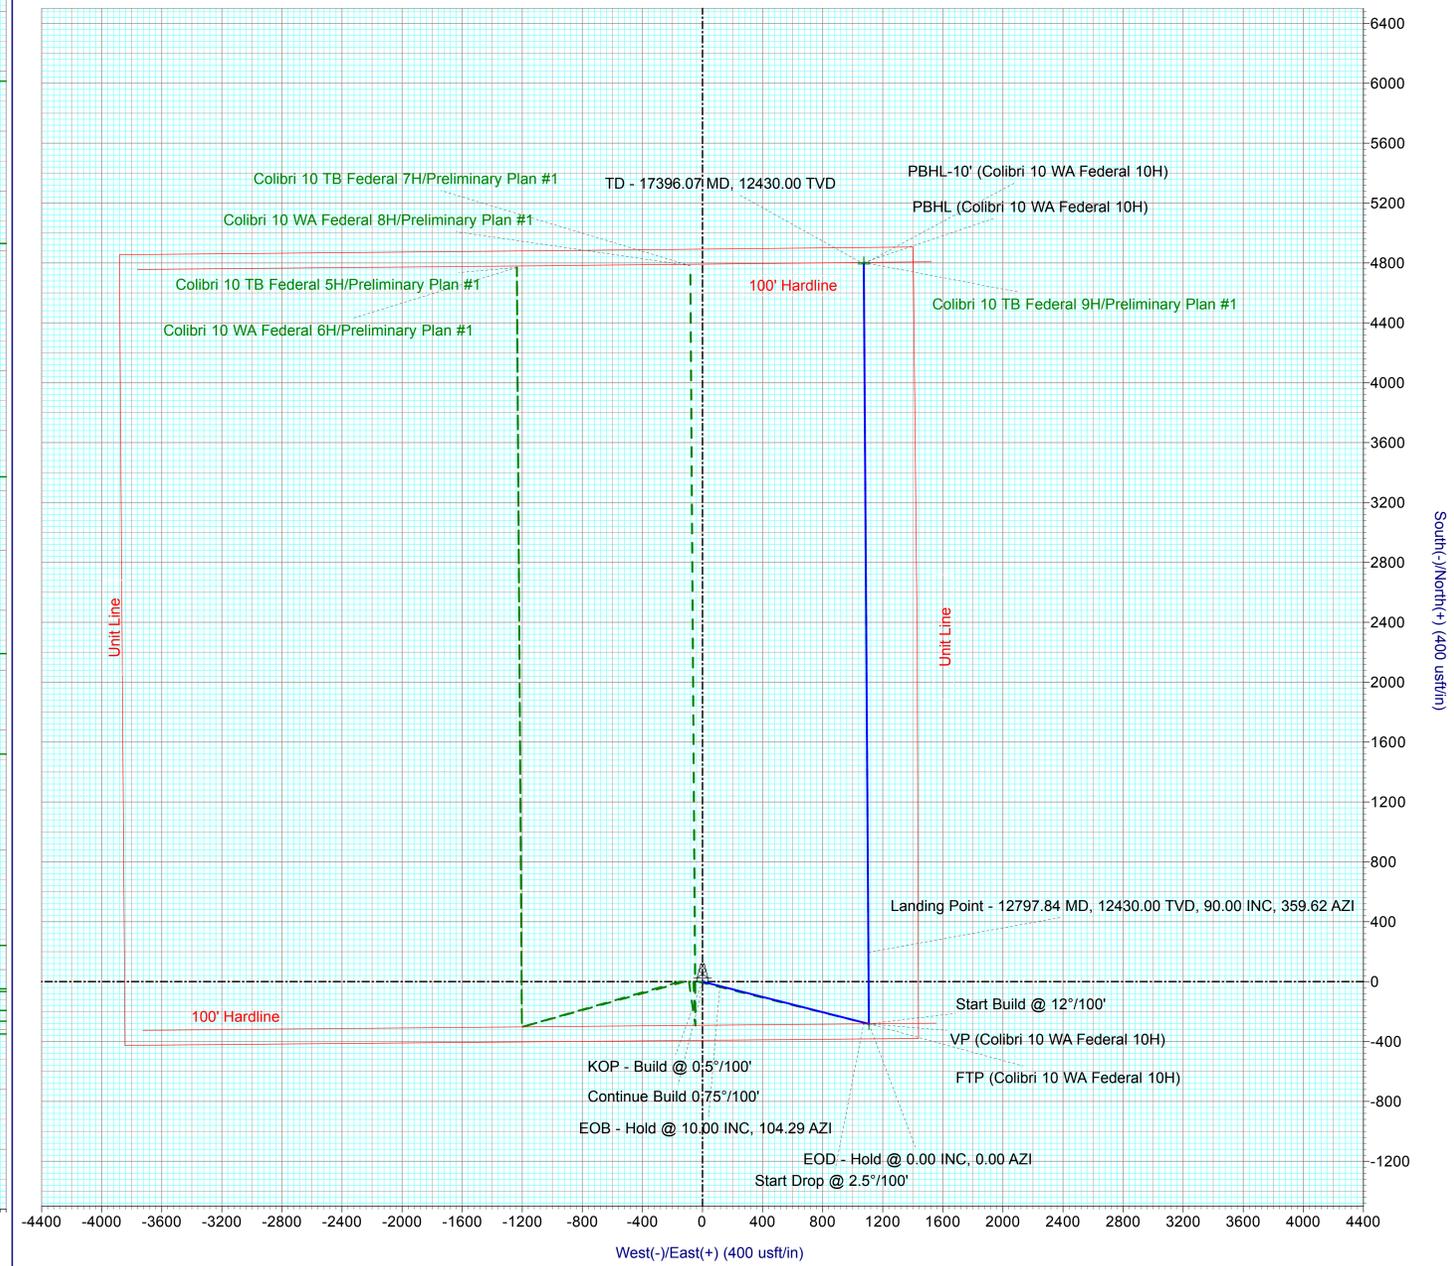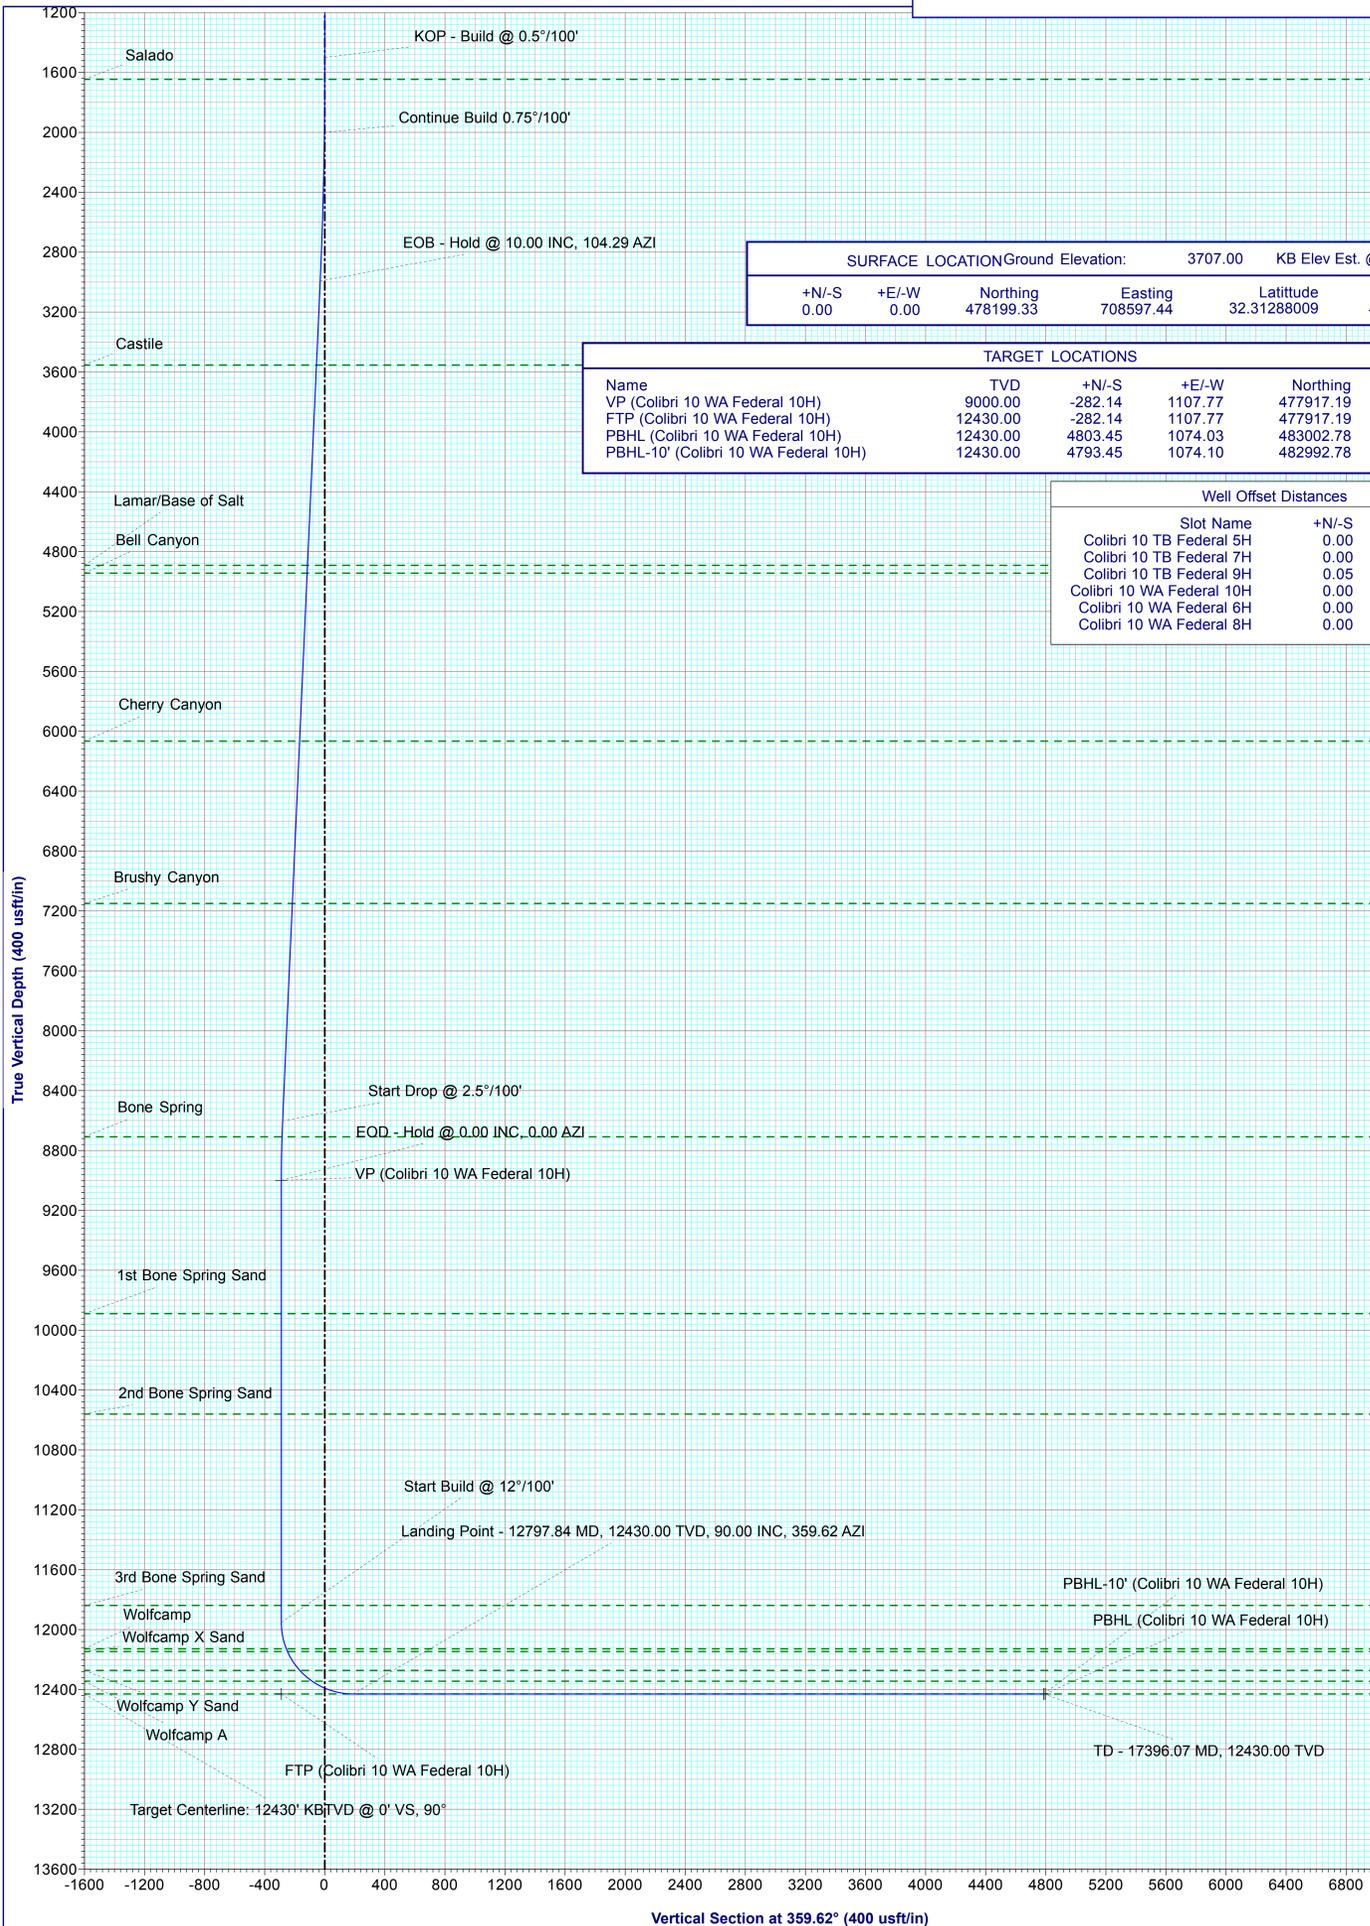

MARATHON OIL PERMIAN, LLC.  
**DRILLING AND OPERATIONS PLAN**



WELL NAME & NUMBER:

**COLIBRI 10 WA FEDERAL 10H**

LOCATION:

SECTION **10** TOWNSHIP **23S** RANGE **32E**  
 LEA COUNTY, **NEW MEXICO**

**Section 1: GEOLOGICAL FORMATIONS**

Name of Surface Formation: Permian  
 Elevation: 3707 feet

**Estimated Tops of Important Geological Markers:**

Formation	TVD (ft)	MD (ft)	Elevation (ft SS)	Lithologies	Mineral Resources	Producing Formation?
Rustler	1171	1198	2171	Anhydrite	Brine	No
Salado	1646	1673	1720	Salt/Anhydrite	Brine	No
Castile	3554	3581	-354	Salt/Anhydrite	Brine	No
Base of Salt (BX)	4892	4919	-2121	Salt/Anhydrite	Brine	No
Lamar	4892	4919	-2121	Sandstone/Shale	None	No
Bell Canyon	4944	4971	-2146	Sandstone	Oil	No
Cherry Canyon	6066	6093	-3446	Sandstone	Oil	No
Brushy Canyon	7150	7177	-4609	Sandstone	Oil	No
Bone Spring Lime	8709	8736	-6055	Limestone	None	No
Upper Avalon Shale	8709	8736	-6093	Shale	Oil	Yes
1st Bone Spring Sand	9890	9917	-7390	Sandstone	Oil	Yes
2nd Bone Spring Carbonate	9890	9917	-7593	Limestone/Shale	None	No
2nd Bone Spring Sand	10561	10588	-7904	Sandstone	Oil	Yes
3rd Bone Spring Carbonate	11839	11866	-8373	Limestone	Oil	No
3rd Bone Spring Sand	11839	11866	-8964	Sandstone	Oil	Yes
Wolfcamp	12129	12156	-9368	Sandstone/Shale/Carbonates	Natural Gas / Oil	Yes
Wolfcamp A	12345	12372	-9493	Sandstone/Shale/Carbonates	Natural Gas / Oil	Yes
Wolfcamp B	12622	12649	-9822	Sandstone/Shale/Carbonates	Natural Gas / Oil	No
Wolfcamp C	12835	12862	-10140	Sandstone/Shale/Carbonates	Natural Gas / Oil	No
Wolfcamp D	12978	13005	-10531	Sandstone/Shale/Carbonates	Natural Gas / Oil	No

**Section 2: BLOWOUT PREVENTER TESTING PROCEDURE**

Pressure Rating (PSI): 10M  
 Rating Depth: 10000  
 Equipment: 13 5/8 BOP Annular (5,000 psi WP) and BOP Stack (10,000 psi WP) will be installed and tested before drilling all holes.

Requesting Variance? Yes  
 Variance Request: A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart.

Testing Procedure: BOP/BOPE will be tested to 250 psi low and a high of 100% WP for the Annular and 5,000psi for the BOP Stacking before drilling 12.25" intermediate hole, 10,000psi for the BOP Stacking before drilling the 8.75" production hole. Testing will be conducted by an independent service company per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the Equipment Description above. If the system is upgraded all the components installed will be functional and tested.  
 Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock, full opening safety valve / inside BOP and choke lines and choke manifold. See attached schematics.  
 Formation integrity test will be performed per Onshore Order #2. On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i. A multibowl wellhead is being used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested. See attached schematic.



**Section 5: CIRCULATING MEDIUM**

**Mud System Type:** Closed  
**Will an air or gas system be used?** No

**Describe what will be on location to control well or mitigate other conditions:**  
 The necessary mud products for additional weight and fluid loss control will be on location at all times.

**Describe the mud monitoring system utilized:**  
 Losses or gains in the mud system will be monitored visually/manually as well as with an electronic PVT.

**Circulating Medium Table:**

Top Depth	Bottom Depth	Mud Type	Min. Weight (ppg)	Max Weight (ppg)
0	1268	Water Based Mud	8.4	8.8
1268	11947	Brine or Oil Based Mud	9.2	10.2
11947	17396	Oil Based Mud	10.5	12.5

**Section 6: TESTING, LOGGING, CORING**

**List of production tests including testing procedures, equipment and safety measures:**  
 GR from TD to surface (horizontal well - vertical portion of hole)

**List of open and cased hole logs run in the well:**  
 GR while drilling from Intermediate casing shoe to TD.

**Coring operation description for the well:**  
 Run gamma-ray (GR) and corrected neutron log (CNL) or analogous to surface for future development of the area, one per shared well pad not to exceed 200' radial distance.

**Section 7: ANTICIPATED PRESSURE**

**Anticipated Bottom Hole Pressure:** 8080 PSI  
**Anticipated Bottom Hole Temperature:** 195 °F  
**Anticipated Abnormal Pressure?** No  
**Anticipated Abnormal Temperature?** No

**Potential Hazards:**  
 H2S detection equipment will be in operation after drilling out the surface casing shoe until the production casing has been cemented. Breathing equipment will be on location from drilling out the surface shoe until production casing is cemented. If H2S is encountered the operator will comply with Onshore Order #6. Adequate flare lines will be installed off the mud/gas separator where gas may be flared safely. All personnel will be familiar with all aspects of safe operation of equipment being used to drill this well. See attached H2S Contingency Plan.

**Section 8: OTHER INFORMATION**

**Auxiliary Well Control and Monitoring Equipment:**  
 A Kelly cock will be in the drill string at all times. A full opening drill pipe stabbing valve having the appropriate connections will be on the rig floor unobstructed and readily accessible at all times.  
 Hydrogen Sulfide detection equipment will be in operation after drilling out the surface casing shoe until the production casing is cemented. Breathing equipment will be on location upon drilling the surface casing shoe until total depth is reached. If Hydrogen Sulfide is encountered, measured amounts and formations will be reported to the BLM.

**Anticipated Starting Date and Duration of Operations:**  
 Road and location construction will begin after the BLM has approved the APD. Anticipated spud date will be as soon as possible after BLM approval and as soon as a rig will be available. Move in operations and drilling is expected to take 30 days.

## PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

<b>OPERATOR'S NAME:</b>	<b>Marathon</b>
<b>LEASE NO.:</b>	<b>NMNM85939</b>
<b>LOCATION:</b>	Section 10, T.23 S., R.32 E., NMPPM
<b>COUNTY:</b>	Lea County, New Mexico

<b>WELL NAME &amp; NO.:</b>	Colibri 10 WA Fed 10H
<b>SURFACE HOLE FOOTAGE:</b>	392'/S & 1437'/E
<b>BOTTOM HOLE FOOTAGE:</b>	100'/N & 330'/E

COA

H2S	<input type="radio"/> Yes	<input checked="" type="radio"/> No	
Potash	<input checked="" type="radio"/> None	<input type="radio"/> Secretary	<input type="radio"/> R-111-P
Cave/Karst Potential	<input checked="" type="radio"/> Low	<input type="radio"/> Medium	<input type="radio"/> High
Cave/Karst Potential	<input type="radio"/> Critical		
Variance	<input type="radio"/> None	<input checked="" type="radio"/> Flex Hose	<input type="radio"/> Other
Wellhead	<input type="radio"/> Conventional	<input checked="" type="radio"/> Multibowl	<input type="radio"/> Both
Other	<input type="checkbox"/> 4 String Area	<input type="checkbox"/> Capitan Reef	<input type="checkbox"/> WIPP
Other	<input checked="" type="checkbox"/> Fluid Filled	<input type="checkbox"/> Cement Squeeze	<input type="checkbox"/> Pilot Hole
Special Requirements	<input type="checkbox"/> Water Disposal	<input type="checkbox"/> COM	<input type="checkbox"/> Unit

### A. HYDROGEN SULFIDE

Hydrogen Sulfide (H2S) monitors shall be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.

### B. CASING

1. The **13-3/8** inch surface casing shall be set at approximately **1371**feet (a minimum of **25 feet (Lea County)** into the Rustler Anhydrite and above the salt) and cemented to the surface. **Excess calculates to 21%. Additional cement maybe required.**
  - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
  - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8**

- hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
- c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
  - d. If cement falls back, remedial cementing will be done prior to drilling out that string.

**Intermediate casing must be kept 50% fluid filled to meet BLM minimum collapse requirement.**

2. The minimum required fill of cement behind the **9-5/8** inch intermediate casing is:
  - Cement to surface. If cement does not circulate see B.1.a, c-d above. **Wait on cement (WOC) time for a primary cement job is to include the tail cement slurry due to cave/karst.**

**Operator is approved to use DV Tool. Operator shall contact BLM before proceeding with DV Tool operation.**

3. The minimum required fill of cement behind the **5-1/2** inch production casing is:
  - Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

### **C. PRESSURE CONTROL**

1. **Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).**
2. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **10,000 (10M) psi. Variance is approved to use a 5000 (5M) Annular which shall be tested to 5000 (5M) psi.**
  - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
  - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
  - c. Manufacturer representative shall install the test plug for the initial BOP test.
  - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
  - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

## GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

Eddy County  
Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,  
(575) 361-2822

Lea County  
Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)  
689-5981

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
  - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
  - b. When the operator proposes to set surface casing with Spudder Rig
    - Notify the BLM when moving in and removing the Spudder Rig.
    - Notify the BLM when moving in the 2<sup>nd</sup> Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
    - BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.

3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.

7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
  - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
  - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
  - c. Manufacturer representative shall install the test plug for the initial BOP test.
  - d. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.
  - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.

- a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
- b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the plug. However, **no tests** shall commence until the cement has had a minimum of 24 hours setup time, except the casing pressure test can be initiated immediately after bumping the plug (only applies to single stage cement jobs).
- c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to Onshore Order 2 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
- d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- e. The results of the test shall be reported to the appropriate BLM office.
- f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500

feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

**ZS091922**



**District I**  
 1625 N. French Dr., Hobbs, NM 88240  
 Phone:(575) 393-6161 Fax:(575) 393-0720  
**District II**  
 811 S. First St., Artesia, NM 88210  
 Phone:(575) 748-1283 Fax:(575) 748-9720  
**District III**  
 1000 Rio Brazos Rd., Aztec, NM 87410  
 Phone:(505) 334-6178 Fax:(505) 334-6170  
**District IV**  
 1220 S. St Francis Dr., Santa Fe, NM 87505  
 Phone:(505) 476-3470 Fax:(505) 476-3462

**State of New Mexico**  
**Energy, Minerals and Natural Resources**  
**Oil Conservation Division**  
**1220 S. St Francis Dr.**  
**Santa Fe, NM 87505**

CONDITIONS

Action 219835

**CONDITIONS**

Operator: MARATHON OIL PERMIAN LLC 990 Town & Country Blvd. Houston, TX 77024	OGRID: 372098
	Action Number: 219835
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

**CONDITIONS**

Created By	Condition	Condition Date
pkautz	Will require a File As Drilled C-102 and a Directional Survey with the C-104	5/31/2023
pkautz	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string	5/31/2023
pkautz	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system	5/31/2023
pkautz	Cement is required to circulate on both surface and intermediate1 strings of casing	5/31/2023
