

I. REQUEST FOR ALLOWABLE MINERAL AUTHORIZATION TO TRANSPORT

¹ Operator name and Address EOG RESOURCES INC PO BOX 2267 MIDLAND, TEXAS 79702		² OGRID Number 7377
		³ Reason for Filing Code/ Effective Date NW 10/25/2021
⁴ API Number 30 - 025-47133	⁵ Pool Name TRISTE DRAW; BONE SPRING	⁶ Pool Code 96603
⁷ Property Code 328120	⁸ Property Name PEGASUS 3 FEDERAL COM	⁹ Well Number 504H

II. ¹⁰ Surface Location

Ul or lot no. O	Section 03	Township 24S	Range 32E	Lot Idn	Feet from the 611'	North/South Line SOUTH	Feet from the 2003'	East/West line EAST	County LEA
--------------------	---------------	-----------------	--------------	---------	-----------------------	---------------------------	------------------------	------------------------	---------------

¹¹ Bottom Hole Location

UL or lot no. B	Section 34	Township 23S	Range 32E	Lot Idn	Feet from the 111'	North/South line NORTH	Feet from the 1618'	East/West line EAST	County LEA
¹² Lse Code	¹³ Producing Method Code FLOWING	¹⁴ Gas Connection Date	¹⁵ C-129 Permit Number		¹⁶ C-129 Effective Date		¹⁷ C-129 Expiration Date		

III. Oil and Gas Transporters

¹⁸ Transporter OGRID	¹⁹ Transporter Name and Address	²⁰ O/G/W
372812	EOGRM	OIL
151618	ENTERPRISE FIELD SERVICES	GAS
298751	REGENCY FIELD SERVICES	GAS
36785	DCP MIDSTREAM	GAS

IV. Well Completion Data

²¹ Spud Date 3/27/2021	²² Ready Date 10/25/2021	²³ TD 21,173'	²⁴ PBTD 21,151"	²⁵ Perforations 11,027 - 21,151'	²⁶ DHC, MC
²⁷ Hole Size		²⁸ Casing & Tubing Size	²⁹ Depth Set		³⁰ Sacks Cement
17 1/2"		13 3/8"	1248'		1070 SXS CL C/CIRC
12 1/4"		9 5/8"	4823'		1365 SXS CL C TOC 500' TS
8 1/2"		5 1/2"	21,195'		3580 SXS CL H TOC 554' CBL

V. Well Test Data

³¹ Date New Oil 10/25/2021	³² Gas Delivery Date 10/25/2021	³³ Test Date 11/04/2021	³⁴ Test Length 24 HRS	³⁵ Tbg. Pressure	³⁶ Csg. Pressure 800
³⁷ Choke Size 64	³⁸ Oil 4050	³⁹ Water 9044	⁴⁰ Gas 5655		⁴¹ Test Method
⁴² I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief. Signature: Kay Maddox			OIL CONSERVATION DIVISION		
Printed name: Kay Maddox			Approved by: PATRICIA MARTINEZ		
Title: SENIOR REGULATORY SPECIALIST			Title: PETROLEUM SPECIALIST		
E-mail Address: kay_maddox@eogresources.com			Approval Date: 10/17/2023		
Date: 11/16/2021		Phone: 432-638-8475			

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources
Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

FORM C-102

Revised August 1, 2011

Submit one copy to appropriate

District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-025-47133		² Pool Code 96603		³ Pool Name TRISTE DRAW; BONE SPRING	
⁴ Property Code 328120		⁵ Property Name PEGASUS 3 FED COM			⁶ Well Number 504H
⁷ OGRID No. 7377		⁸ Operator Name EOG RESOURCES, INC.			⁹ Elevation 3645'

¹⁰Surface Location


UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
0	3	24-S	32-E	-	611'	SOUTH	2003'	EAST	LEA

¹¹Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
B	34	23-S	32-E	-	111'	NORTH	1618'	EAST	LEA

¹² Dedicated Acres 639.39	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.
---	-------------------------------	----------------------------------	-------------------------

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

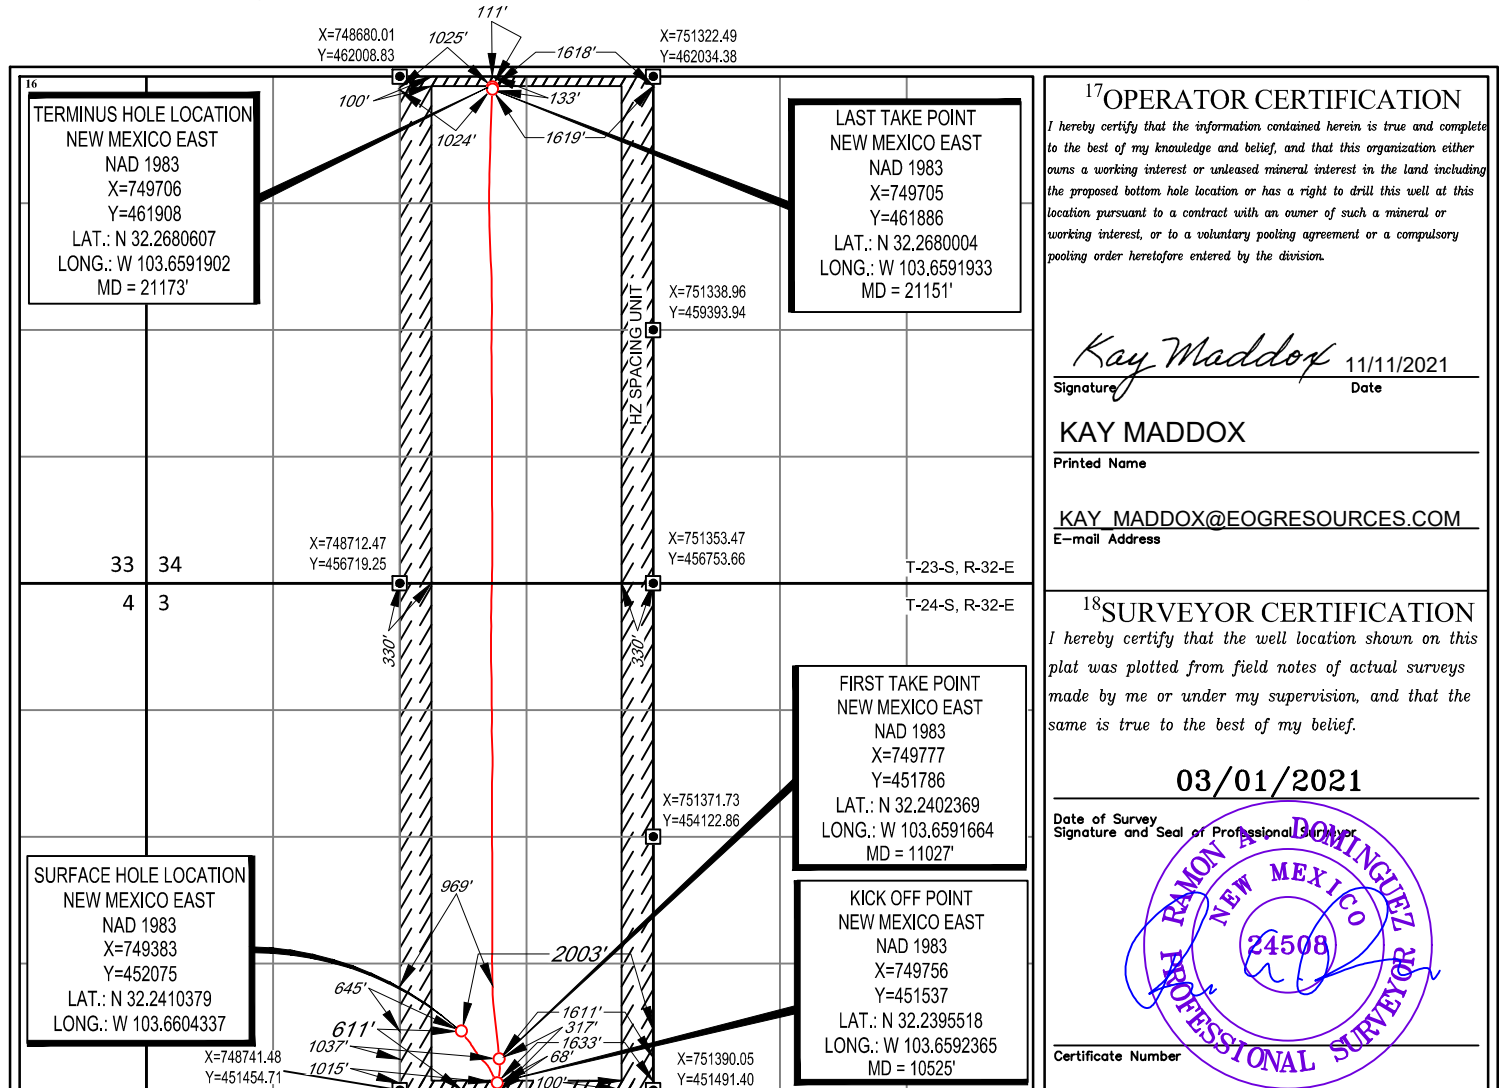



Lea County, NM (NAD 83 NME)

Pegasus 3 Fed Com #504H


OH

PROJECT DETAILS: Lea County, NM (NAD 83 NME)










Geodetic System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone: New Mexico Eastern Zone
System Datum: Mean Sea Level

WELL DETAILS: #504H

KB = 25 @ 3670.0usft
Northing 452075.00 Easting 749383.00 Latitude 32° 14' 27.738 N Longitude 103° 39' 37.560 W

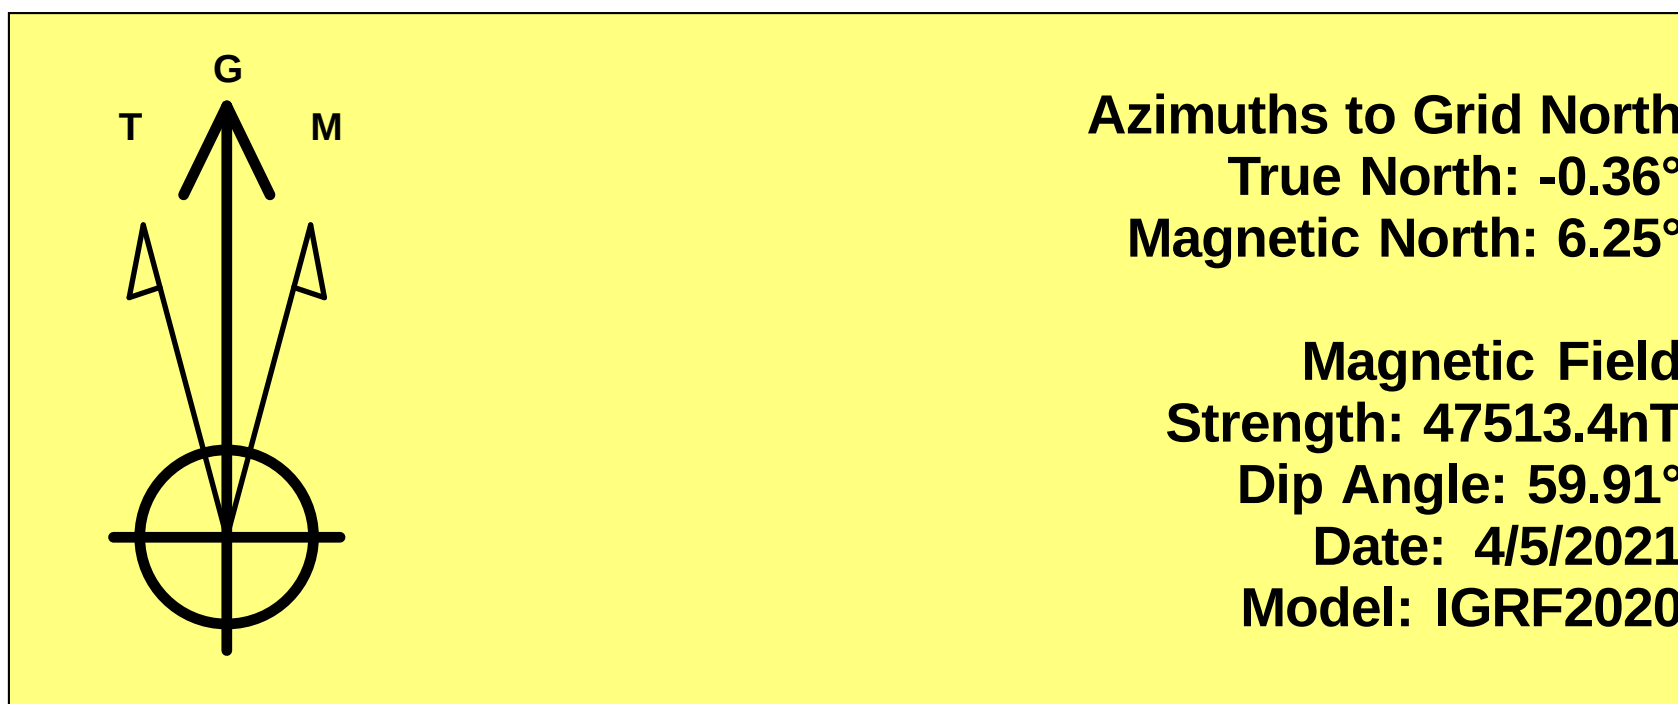

To convert a Magnetic Direction to a Grid Direction, Add 6.25°
To convert a Magnetic Direction to a True Direction, Add 6.61° East
To convert a True Direction to a Grid Direction, Subtract 0.36°

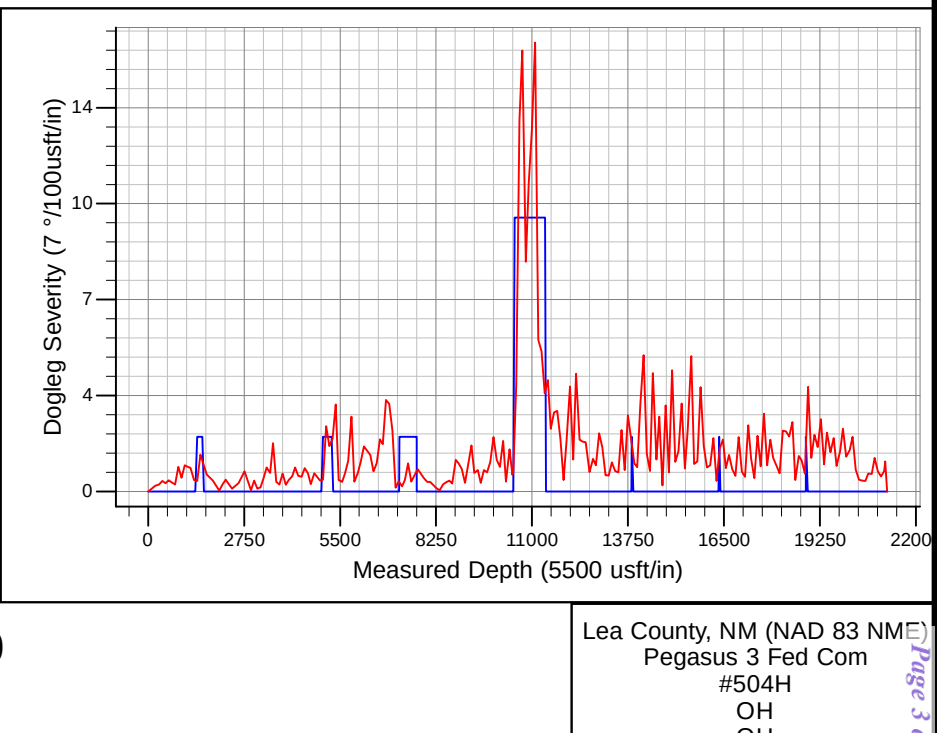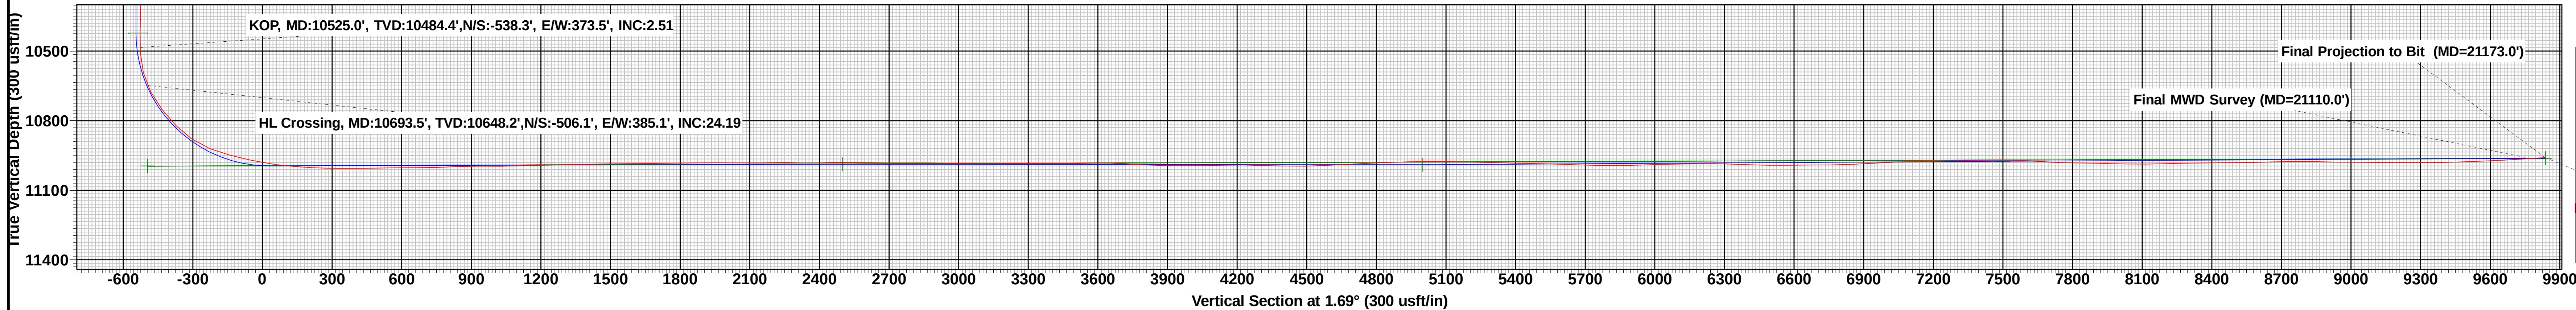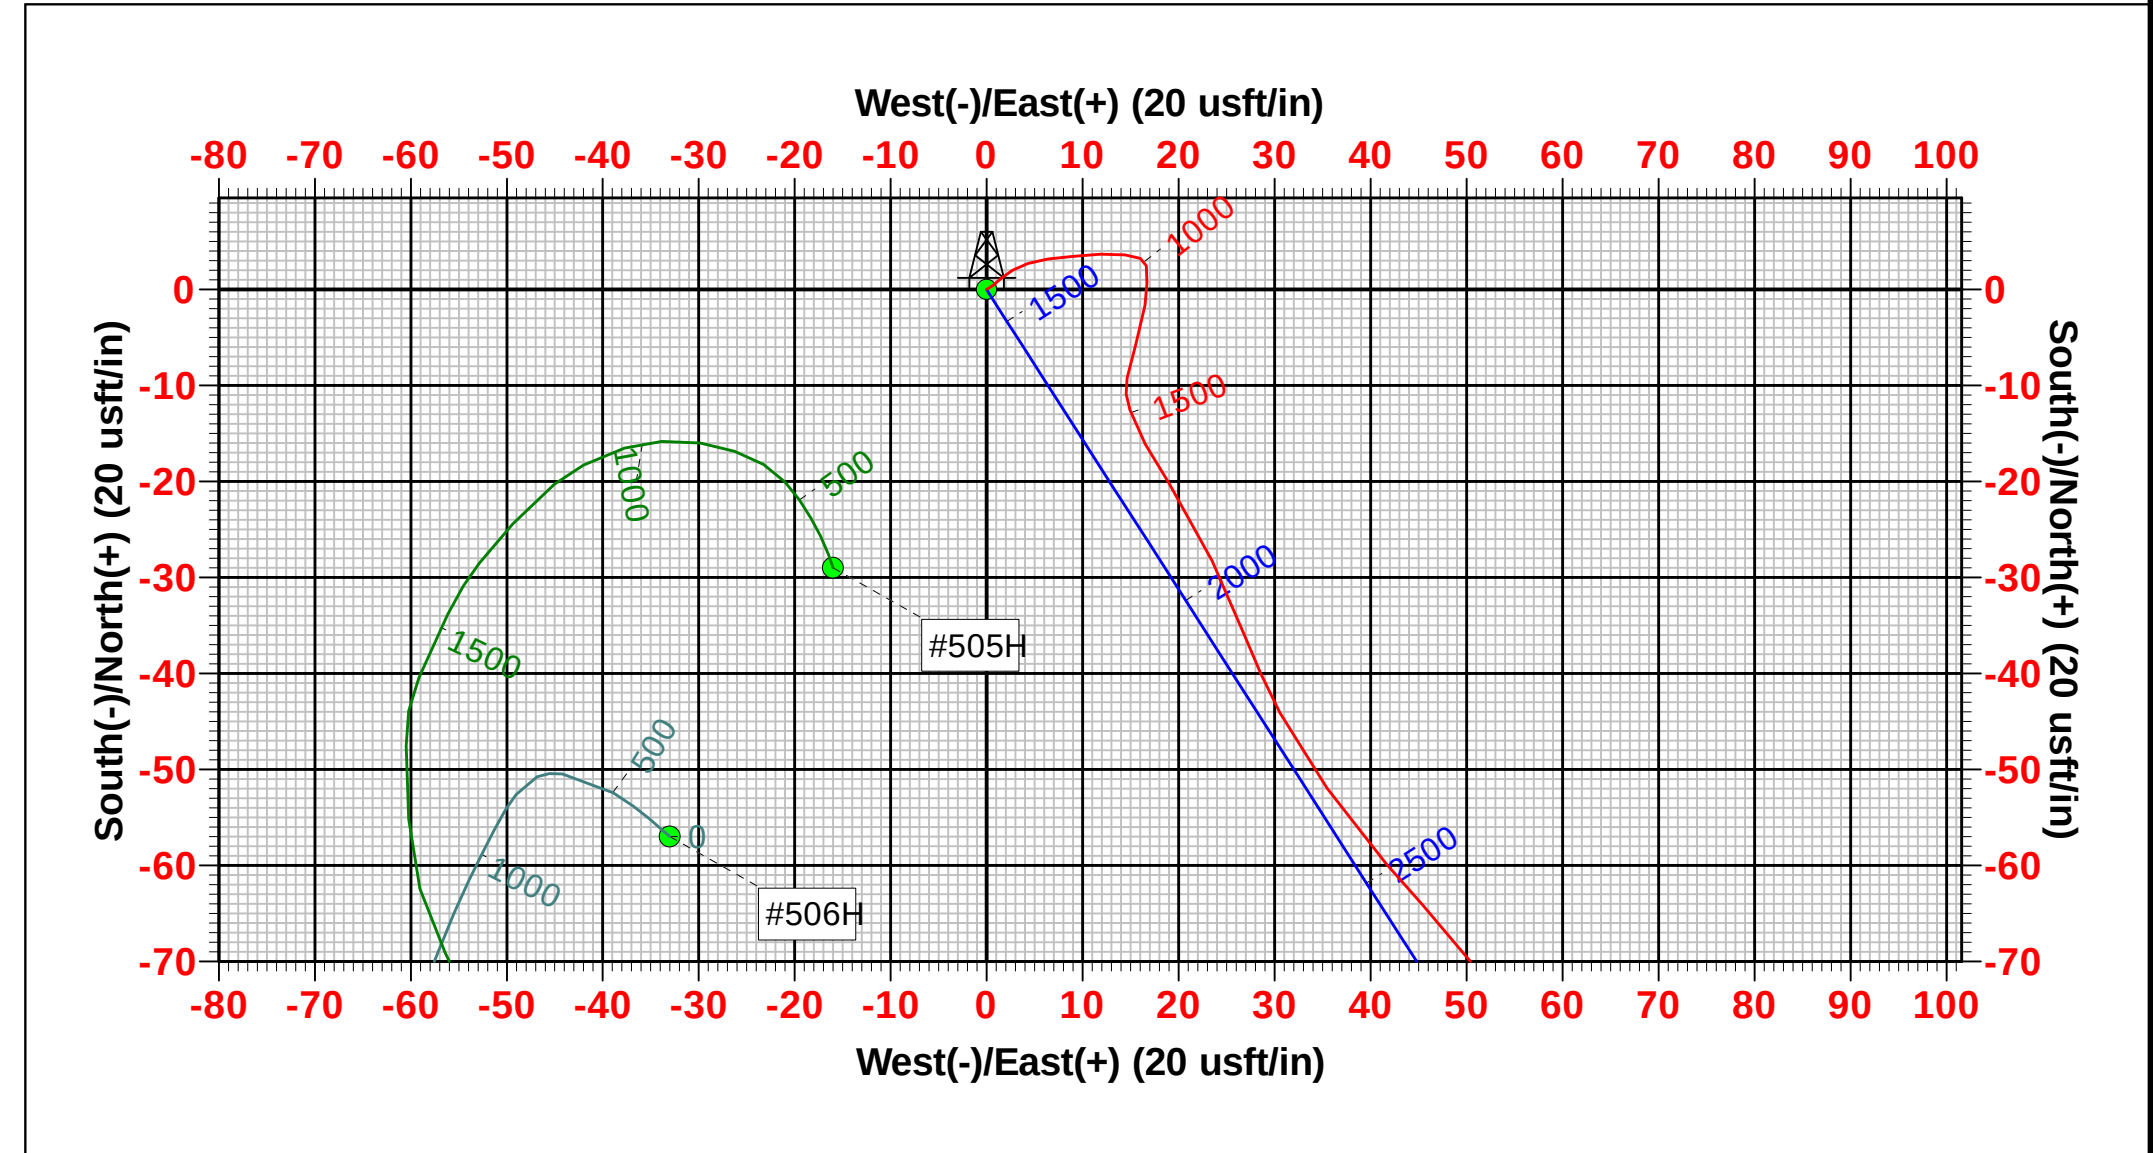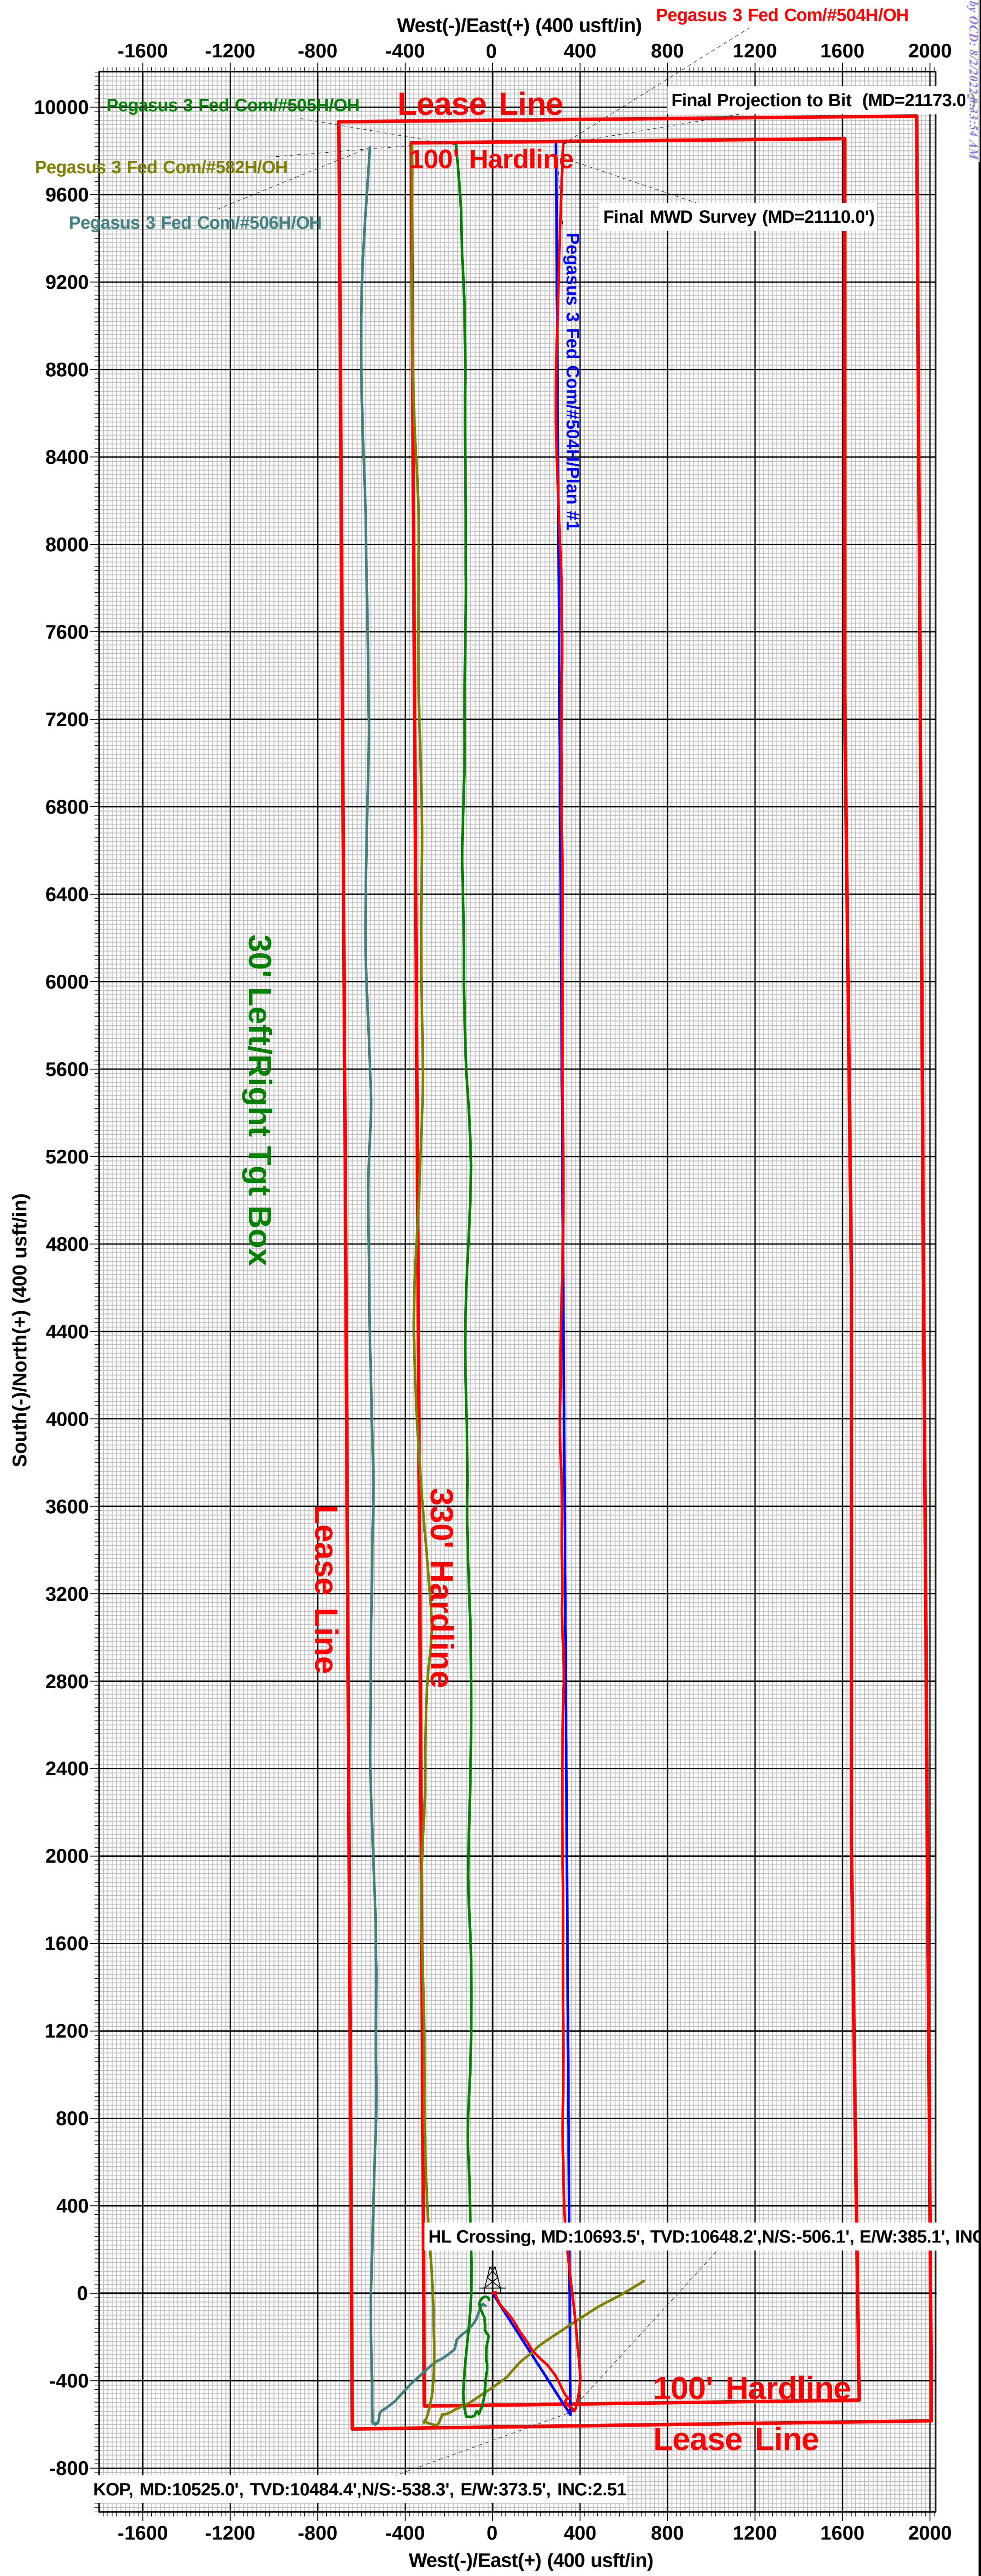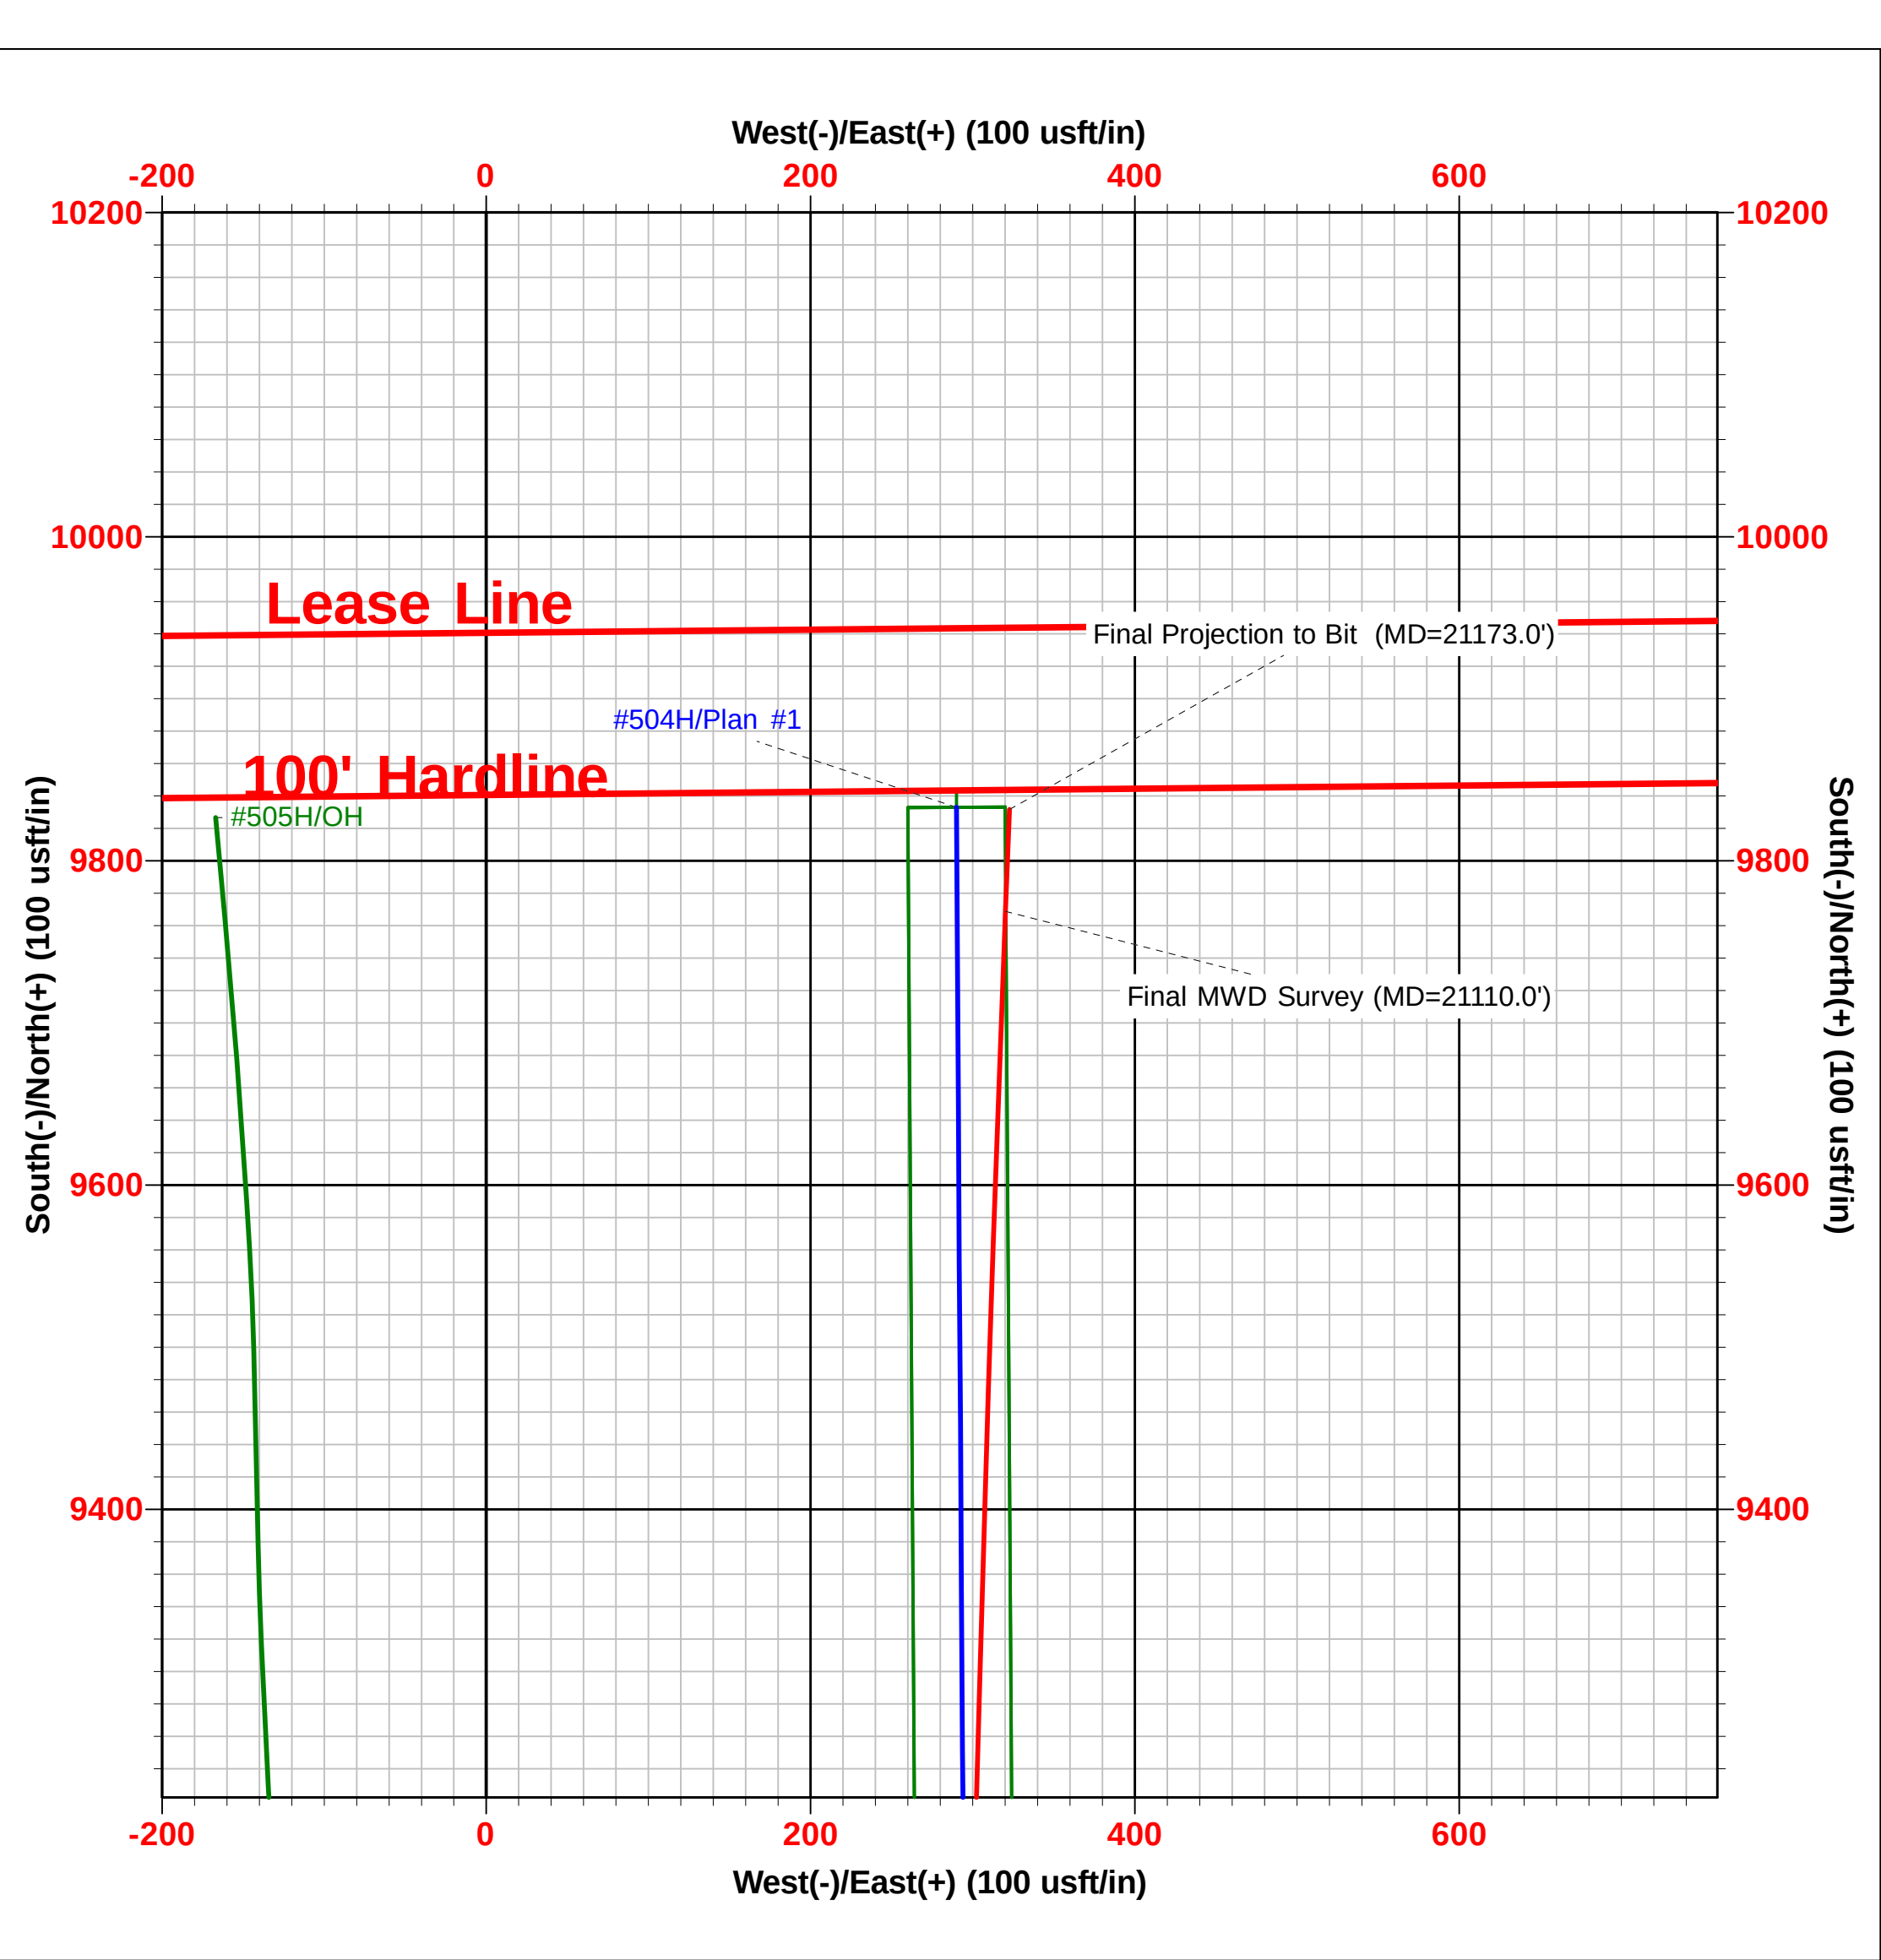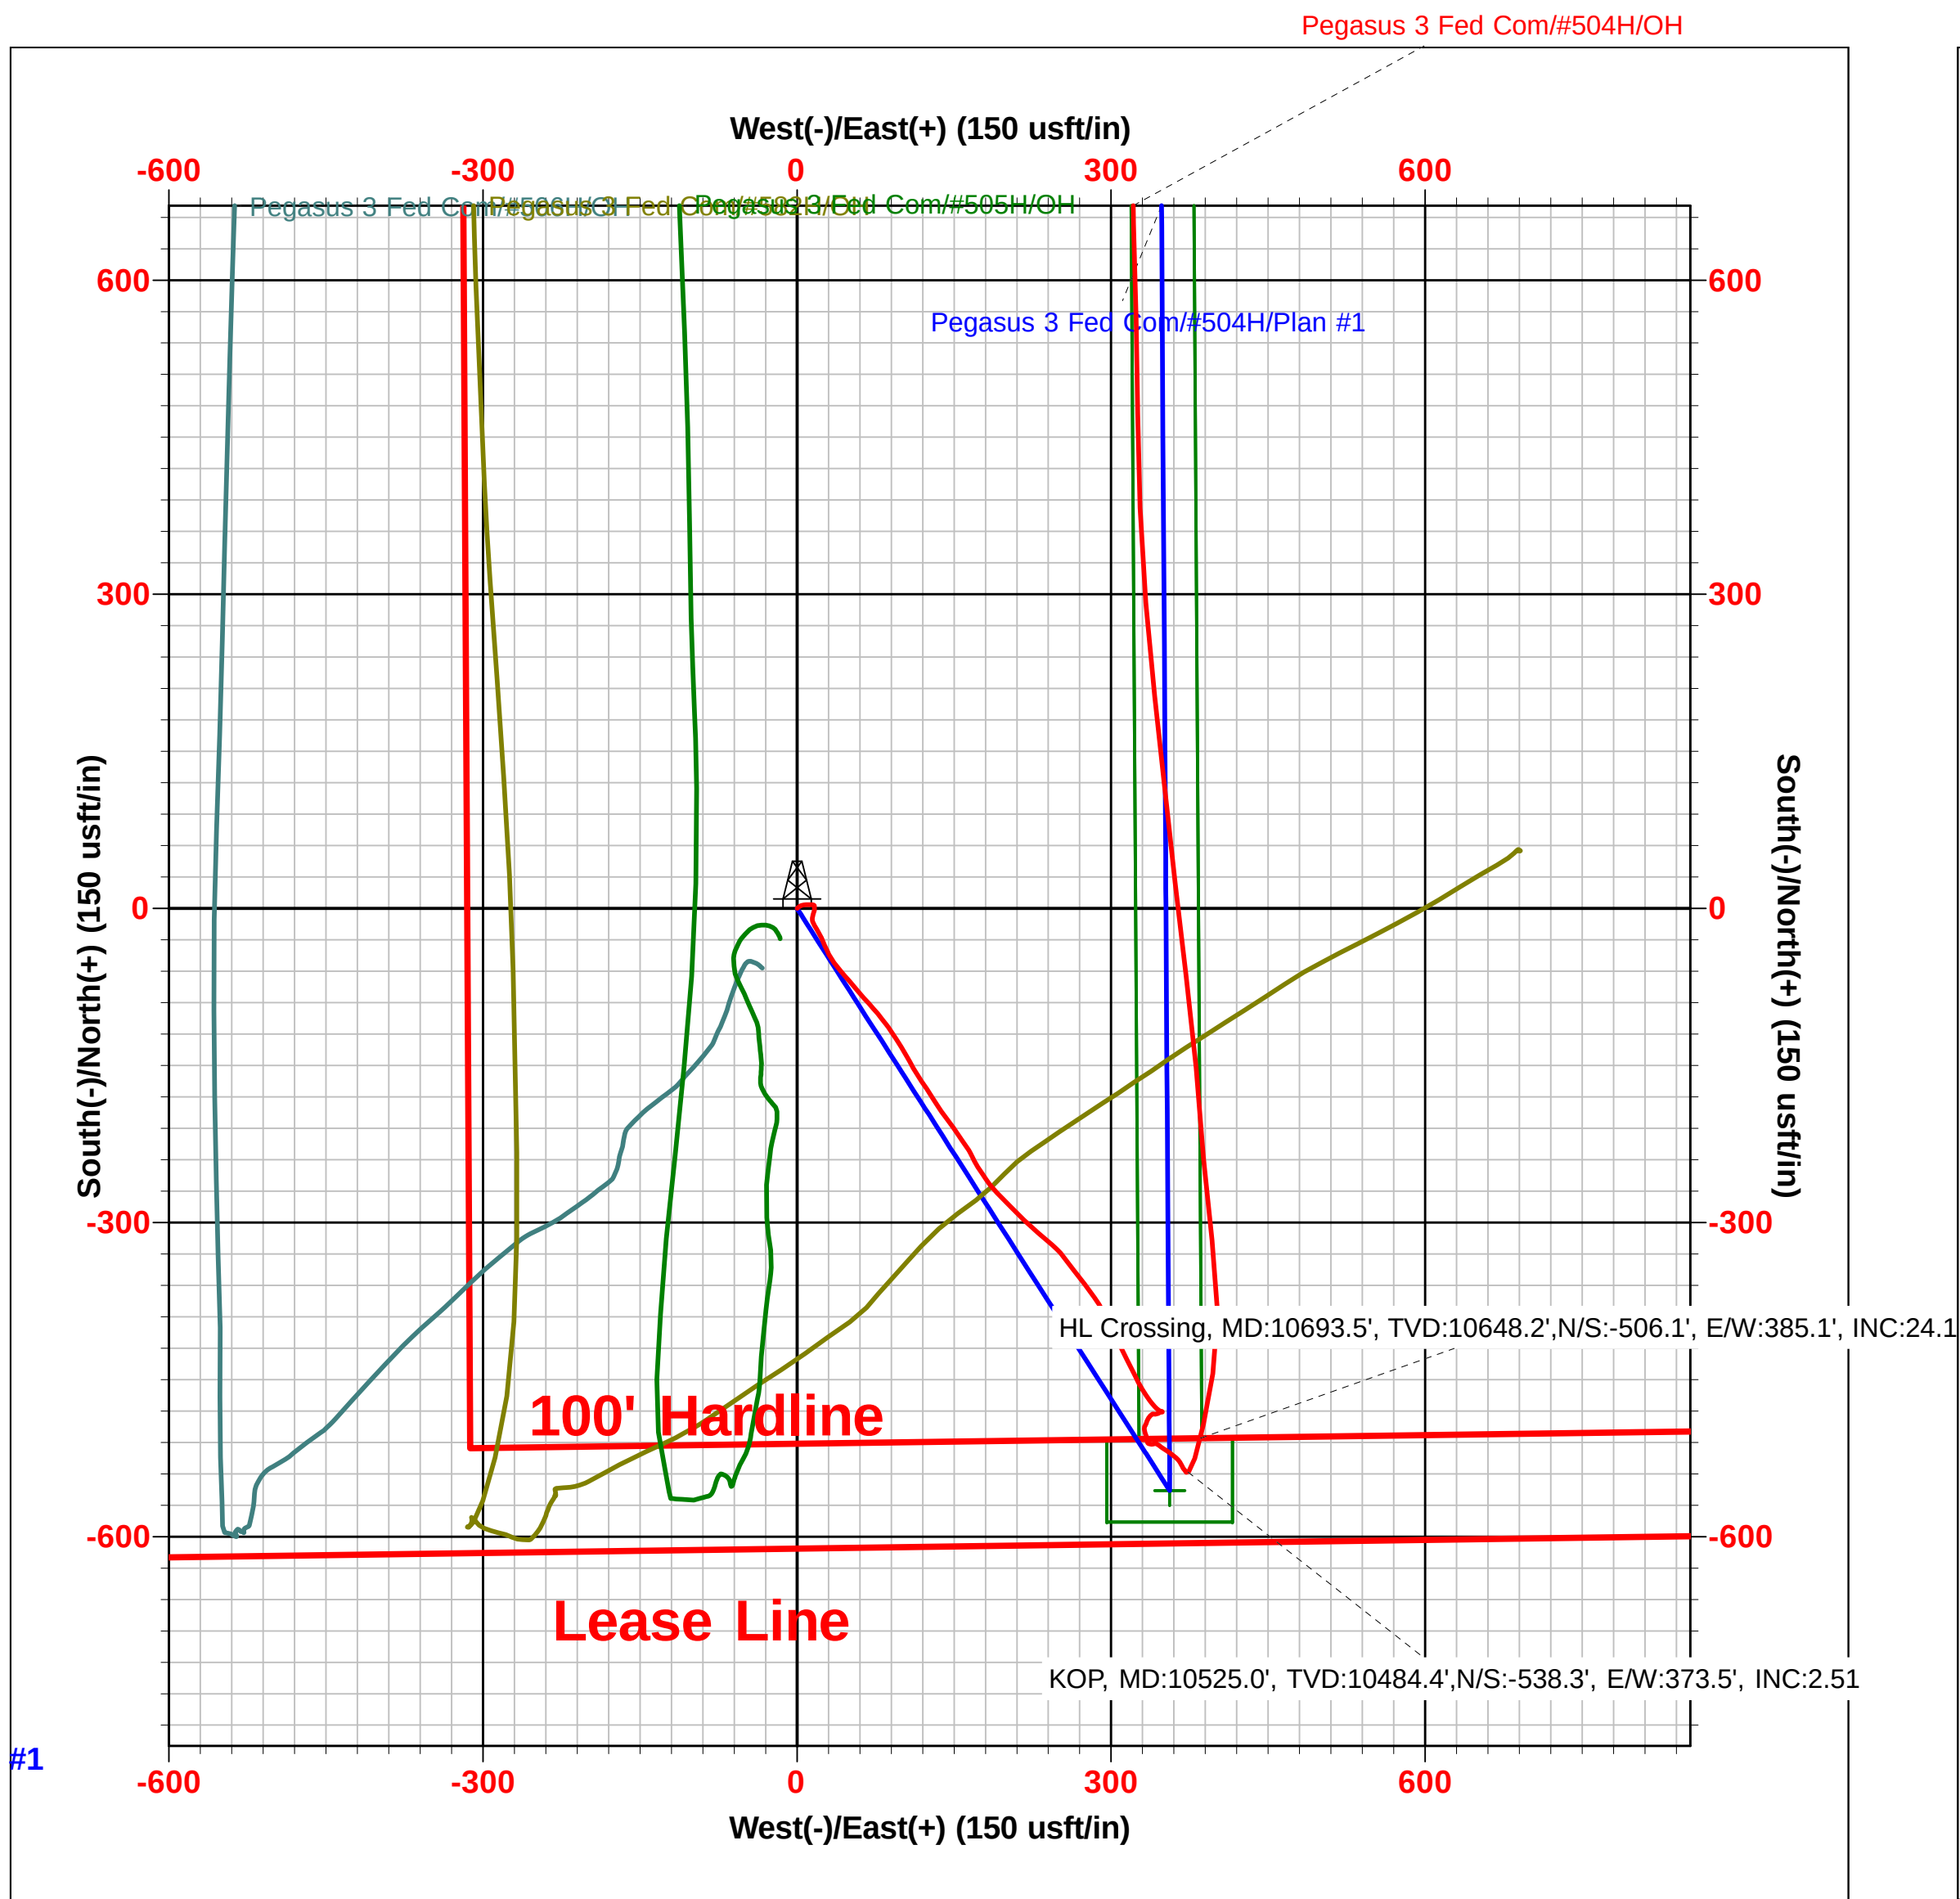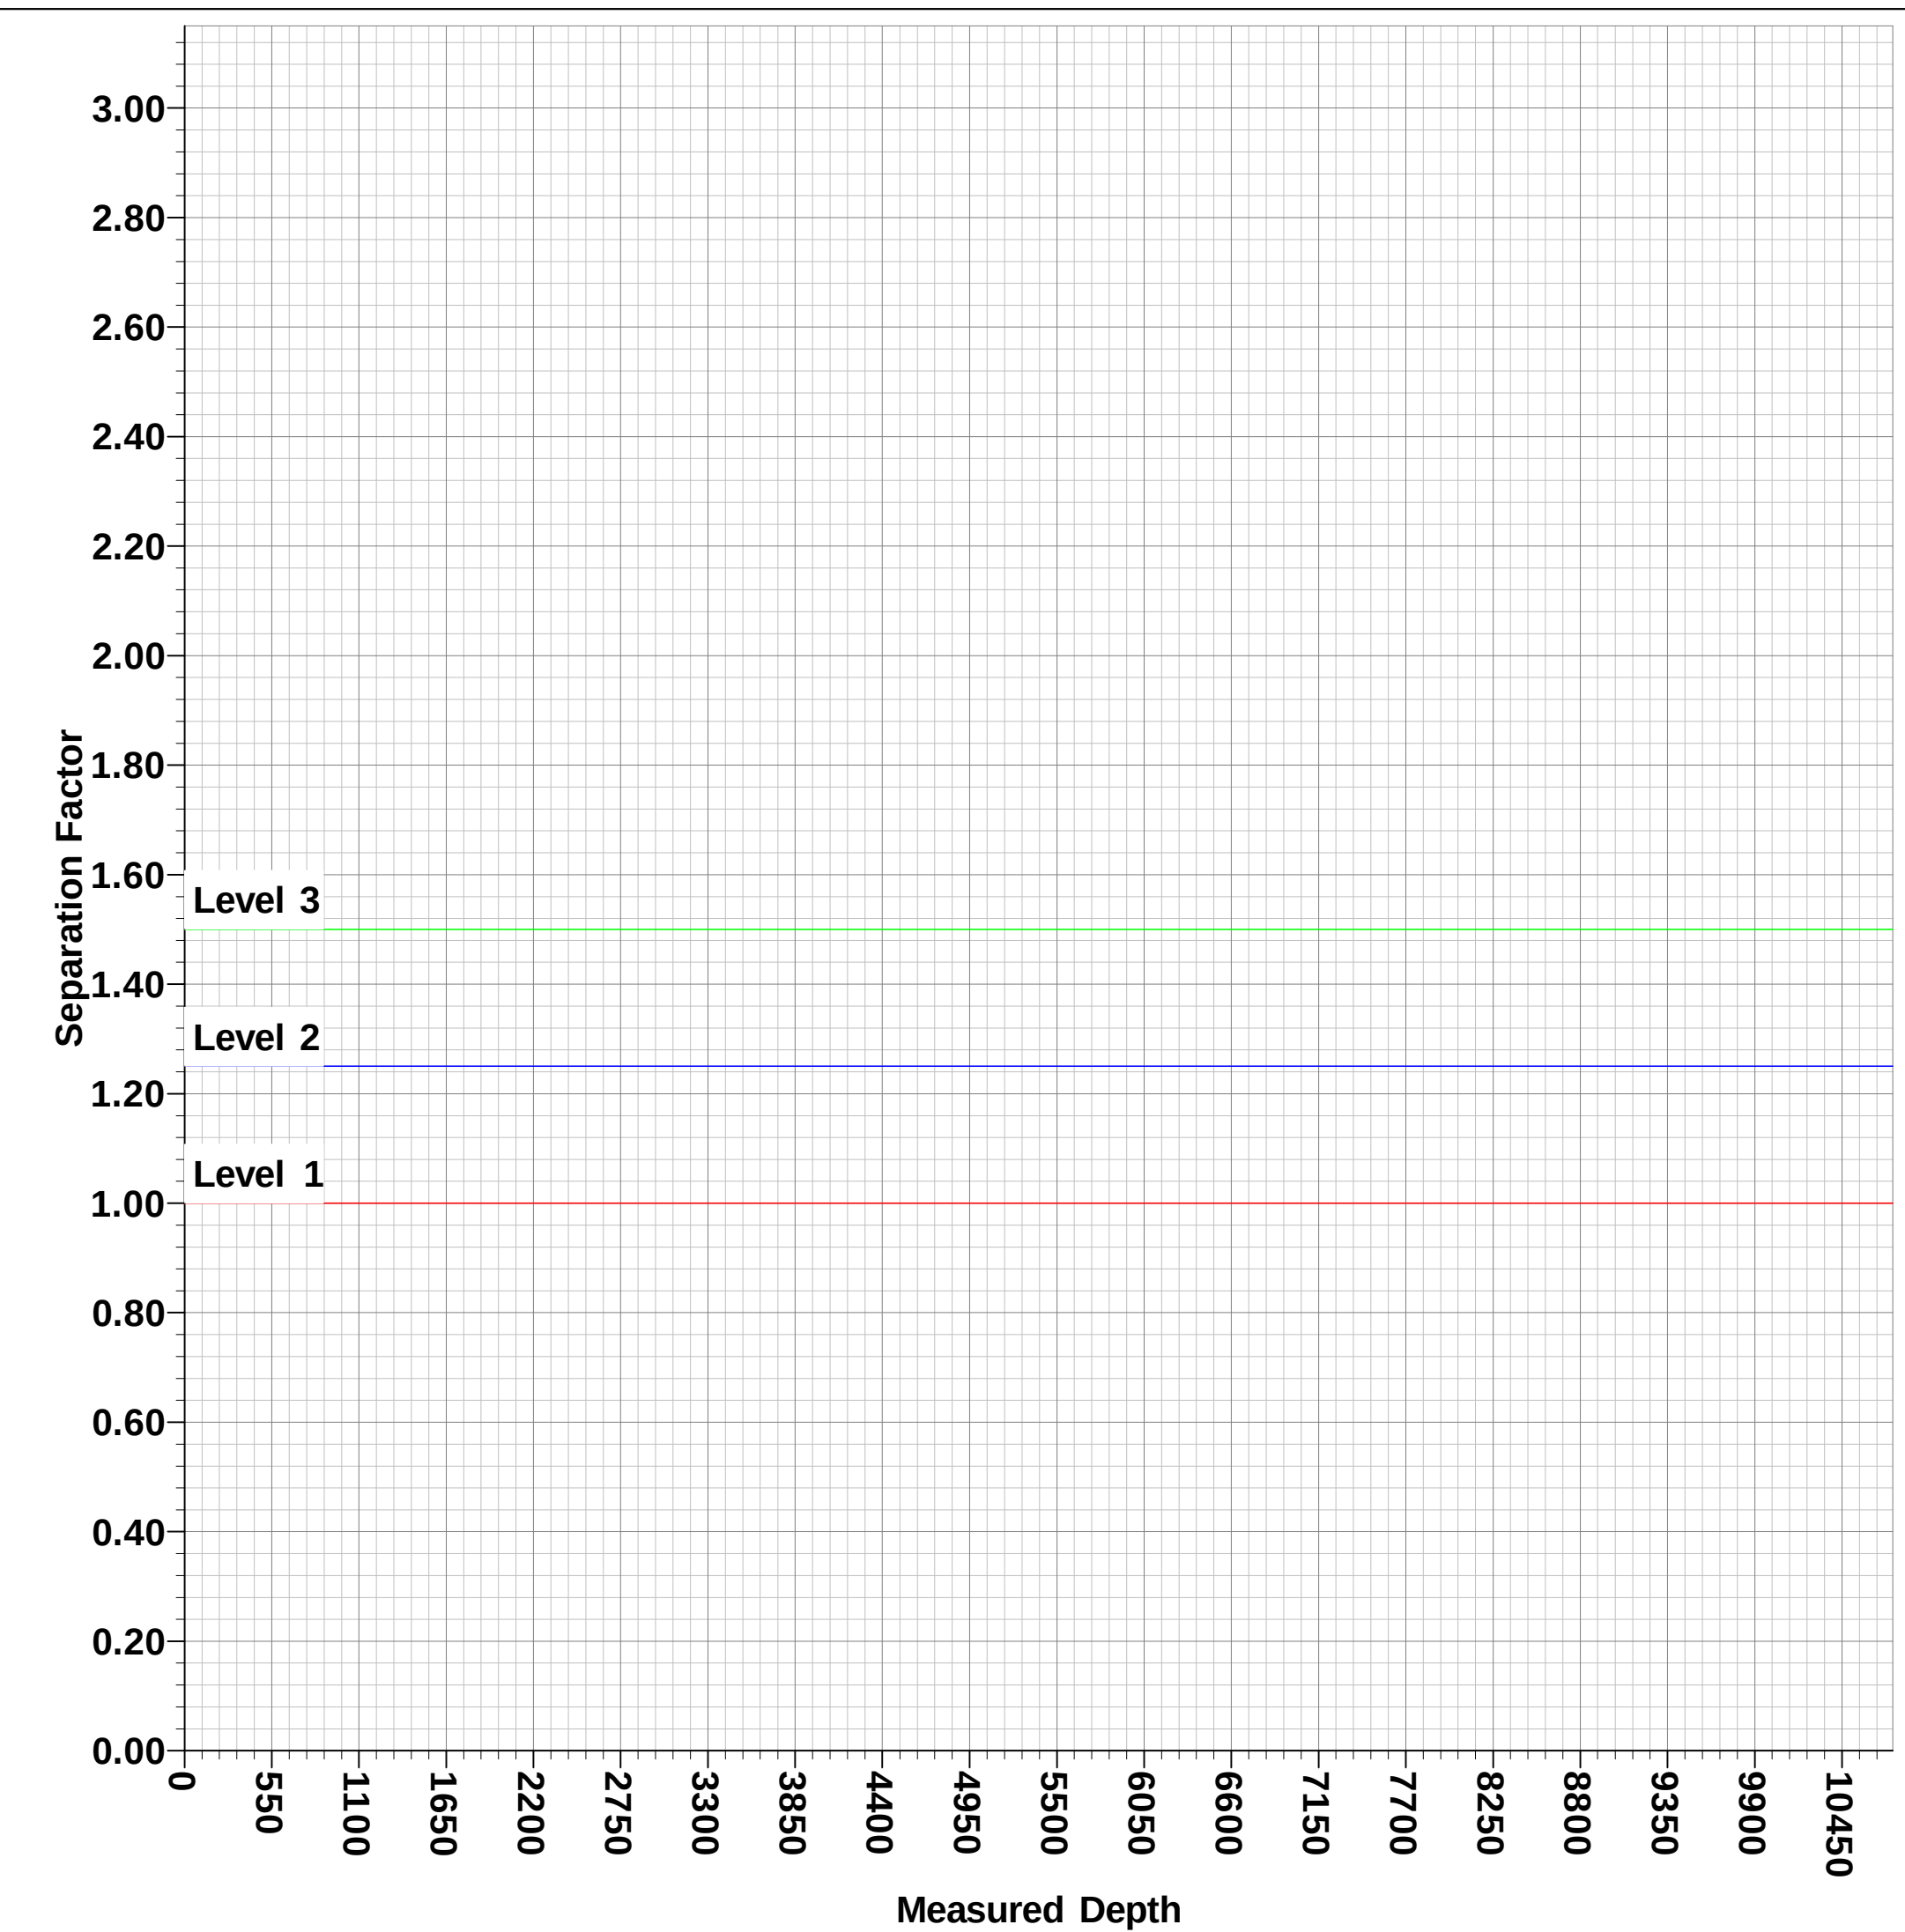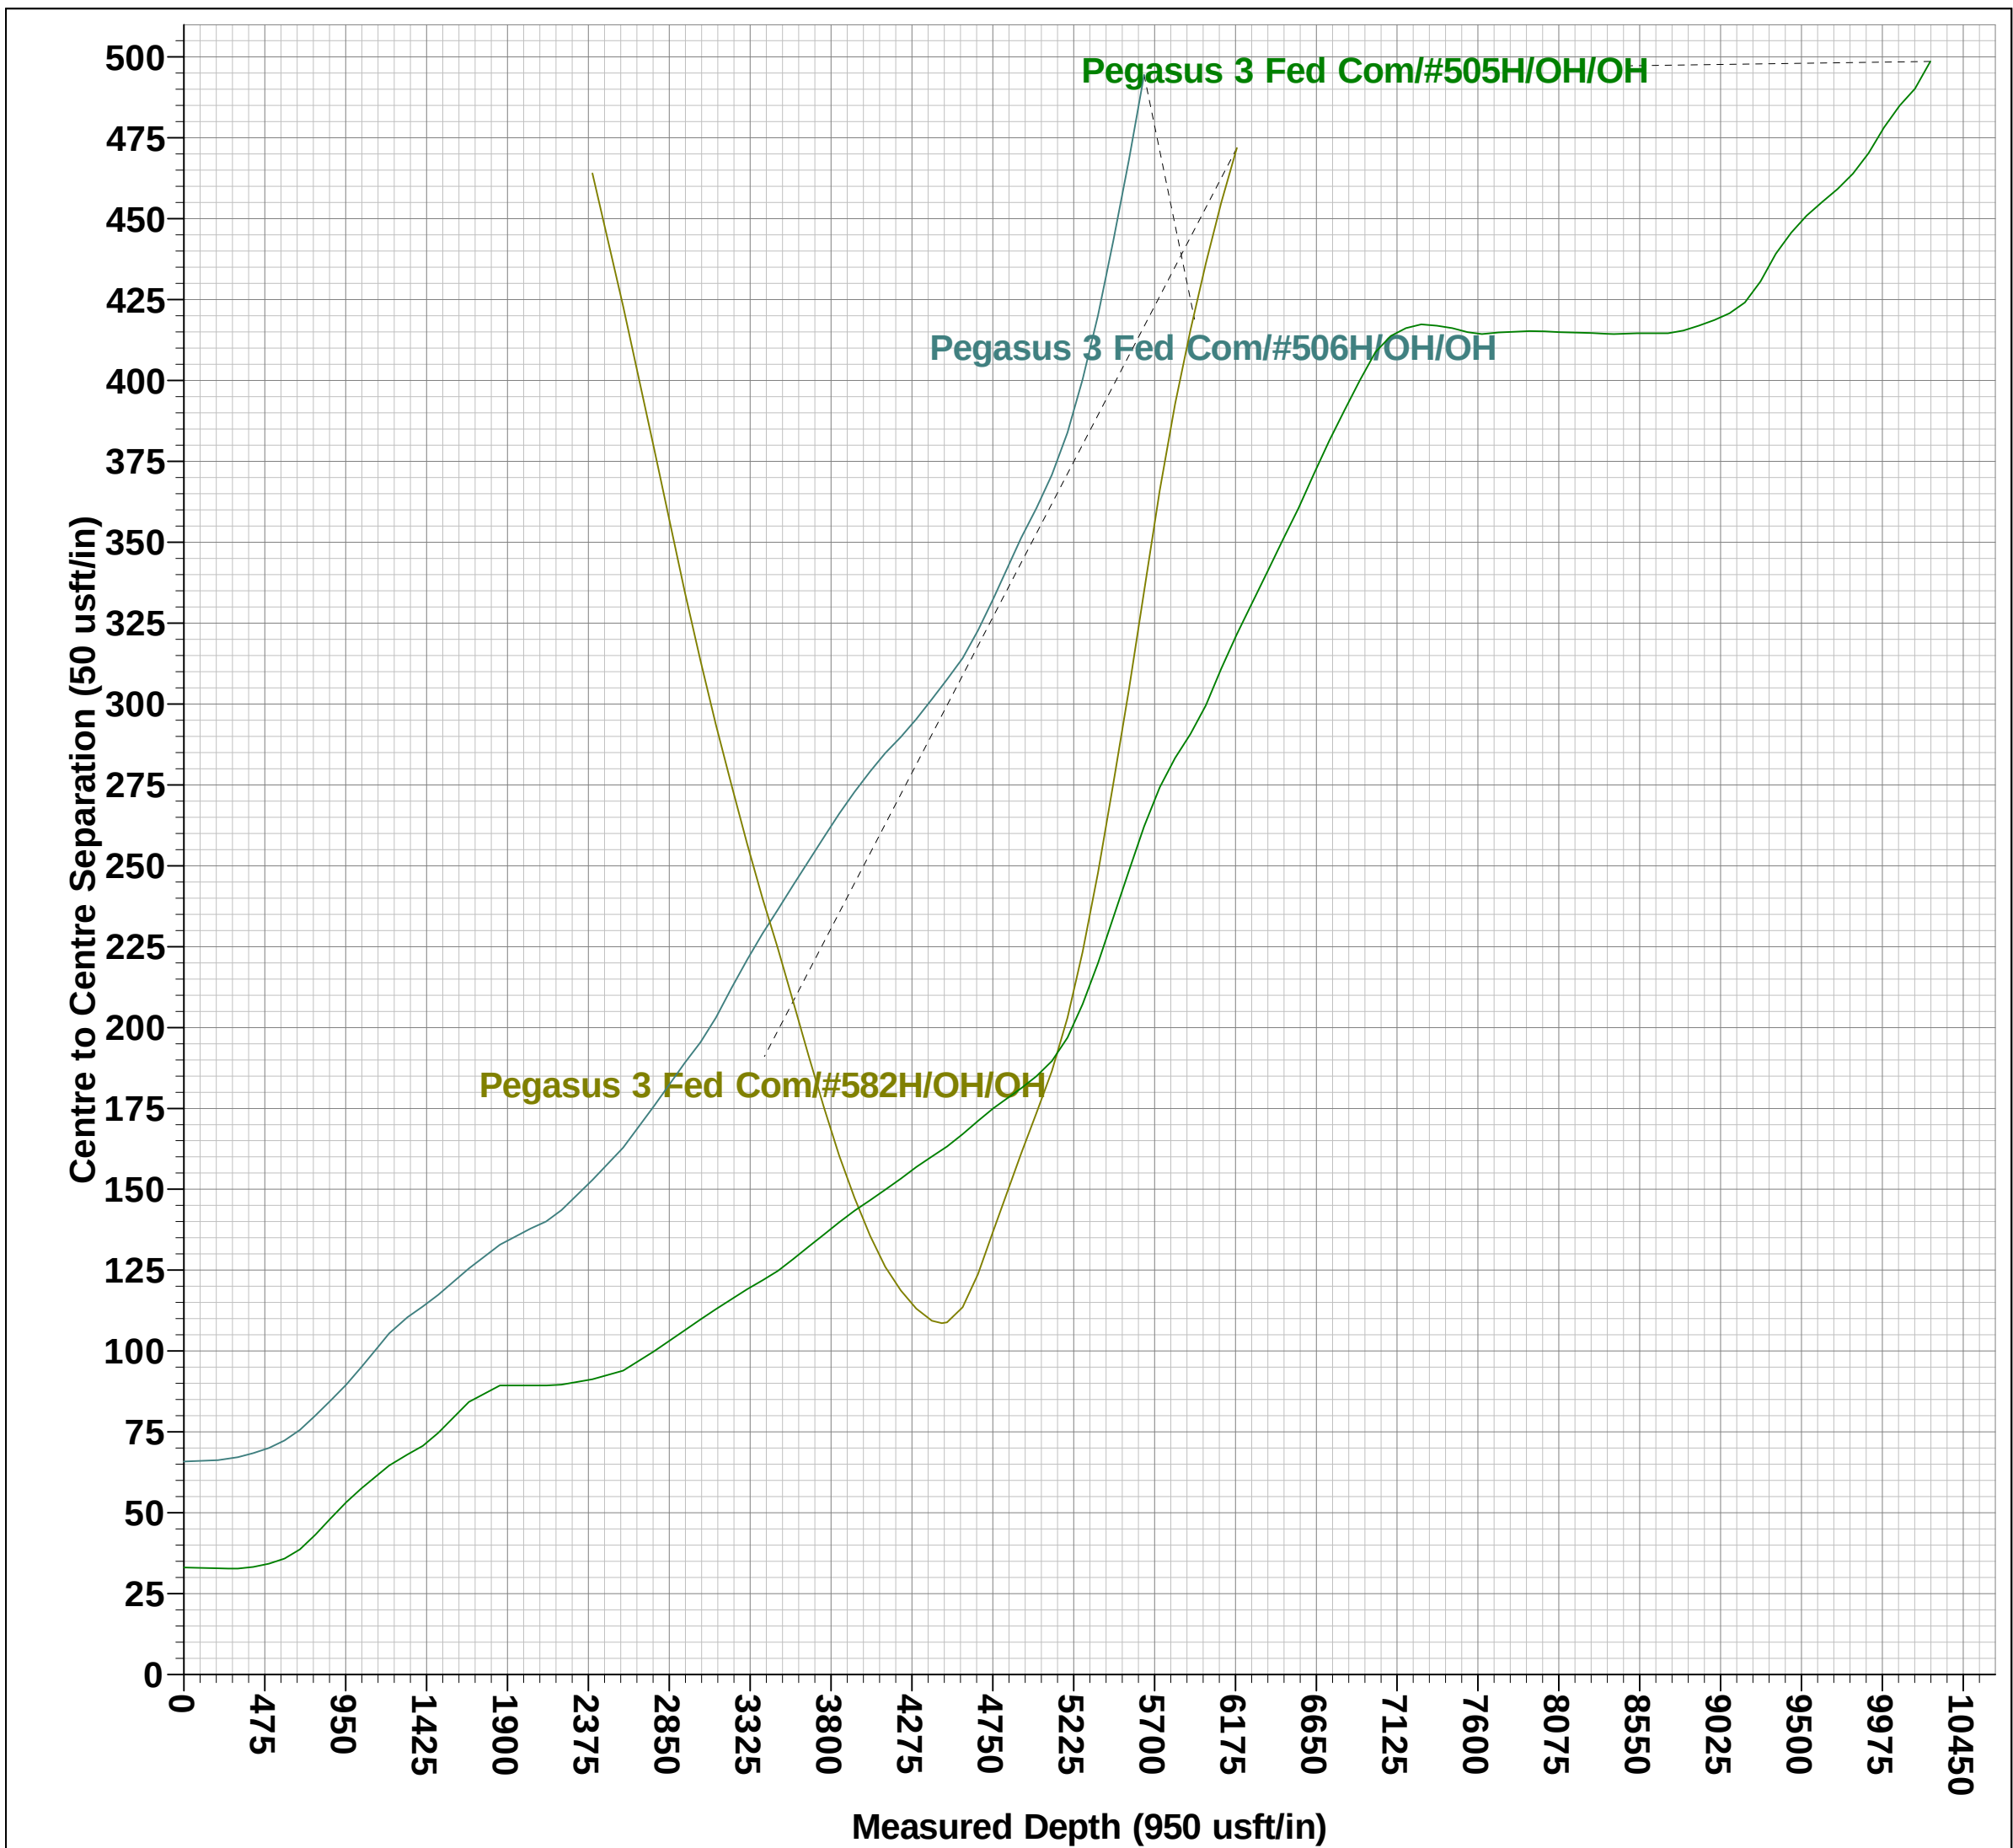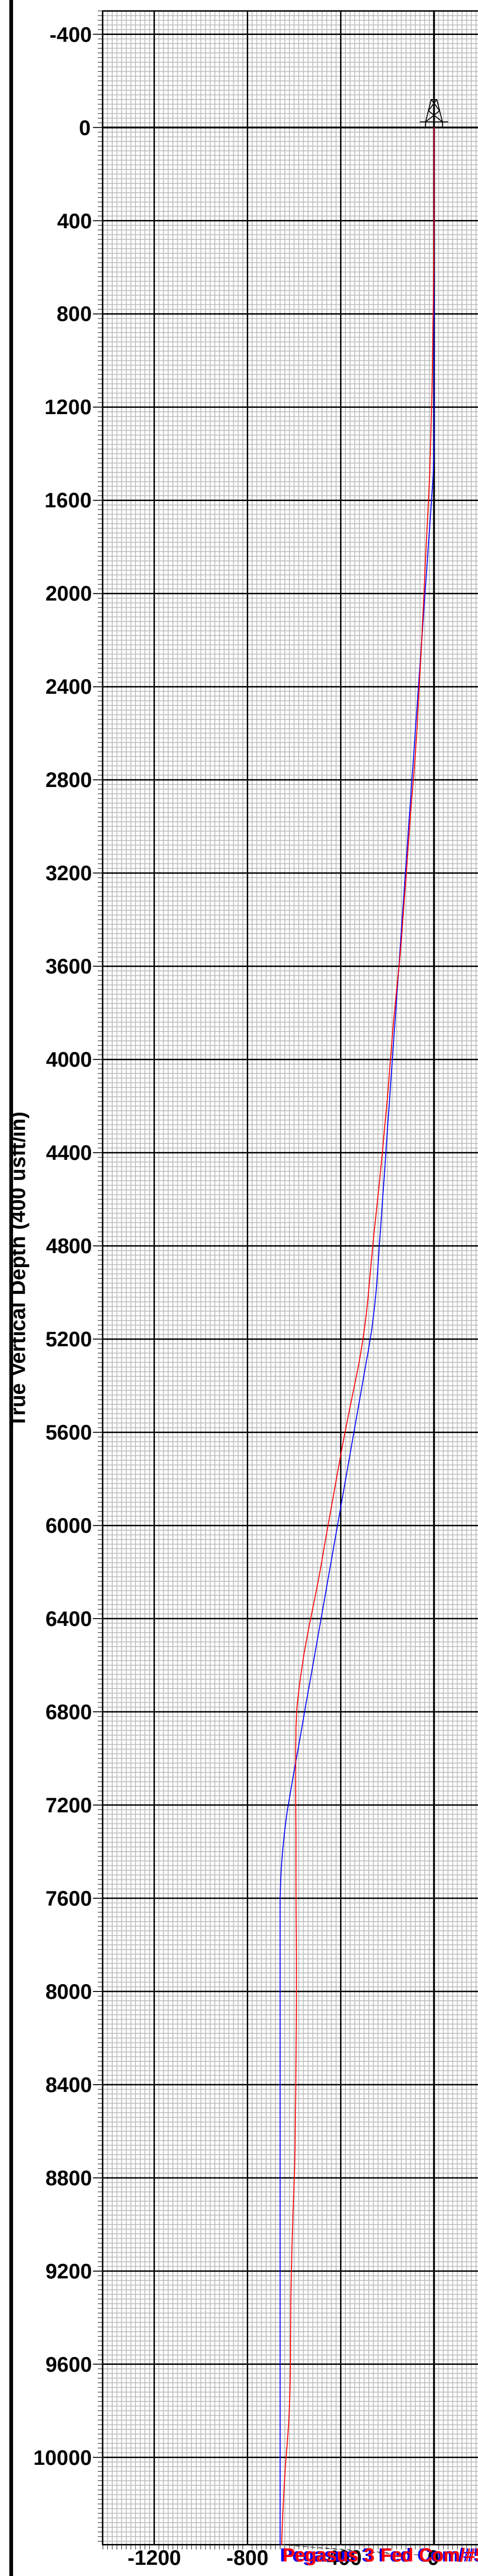



EOG Resources - Midland

Lea County, NM (NAD 83 NME)

Pegasus 3 Fed Com

#504H

OH

Design: OH

Final PVA

14 May, 2021



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #504H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3670.0usft
Site:	Pegasus 3 Fed Com	MD Reference:	KB = 25 @ 3670.0usft
Well:	#504H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Project	Lea County, NM (NAD 83 NME)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Pegasus 3 Fed Com		
Site Position:		Northing:	451,857.00 usft
From:	Map	Easting:	747,693.00 usft
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "
		Latitude:	32° 14' 25.685 N
		Longitude:	103° 39' 57.253 W
		Grid Convergence:	0.36 °

Well		#504H				
Well Position	+N/-S	0.0 usft	Northing:	452,075.00 usft	Latitude:	32° 14' 27.738 N
	+E/-W	0.0 usft	Easting:	749,383.00 usft	Longitude:	103° 39' 37.560 W
Position Uncertainty		0.0 usft	Wellhead Elevation:	usft	Ground Level:	3,645.0 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	4/5/2021	6.61	59.91	47,513.42192817

Design	OH				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)	
	0.0	0.0	0.0	1.69	

Survey Program	Date	5/14/2021			
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
200.0	21,173.0	SDI MWD #1 (OH)	EOG MWD+IFR1	MWD + IFR1	



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #504H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3670.0usft
Site:	Pegasus 3 Fed Com	MD Reference:	KB = 25 @ 3670.0usft
Well:	#504H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.0	0.0	
200.0	0.44	56.08	200.0	0.4	0.6	0.22	0.22	0.00	-0.8	0.0	
316.0	0.74	47.28	316.0	1.2	1.6	0.27	0.26	-7.59	-1.9	-0.2	
407.0	1.05	58.71	407.0	2.0	2.7	0.39	0.34	12.56	-3.4	0.3	
498.0	1.16	72.18	498.0	2.7	4.3	0.31	0.12	14.80	-4.9	1.3	
591.0	1.47	82.12	590.9	3.2	6.4	0.41	0.33	10.69	-6.7	2.3	
681.0	1.76	85.19	680.9	3.5	8.9	0.34	0.32	3.41	-9.1	2.7	
772.0	1.99	86.67	771.9	3.7	11.9	0.26	0.25	1.63	-12.1	3.0	
862.0	1.25	98.98	861.8	3.6	14.4	0.90	-0.82	13.68	-13.6	5.8	
953.0	0.81	107.56	952.8	3.3	16.0	0.51	-0.48	9.43	-14.3	7.9	
1,043.0	0.74	175.41	1,042.8	2.5	16.6	0.96	-0.08	75.39	1.1	16.8	
1,134.0	1.56	179.92	1,133.8	0.7	16.7	0.91	0.90	4.96	0.6	16.7	
1,205.0	2.12	188.10	1,204.7	-1.6	16.5	0.87	0.79	11.52	0.7	16.6	
1,312.0	2.42	197.04	1,311.7	-5.7	15.6	0.43	0.28	8.36	-0.9	16.6	
1,403.0	2.14	191.62	1,402.6	-9.2	14.7	0.39	-0.31	-5.96	-5.7	15.9	
1,493.0	2.27	159.96	1,492.5	-12.5	14.9	1.34	0.14	-35.18	-13.4	8.9	
1,674.0	3.20	146.24	1,673.3	-20.1	19.0	0.62	0.51	-7.58	-11.6	4.9	
1,856.0	2.70	156.71	1,855.1	-28.3	23.5	0.40	-0.27	5.75	-7.3	5.8	
2,036.0	2.63	156.13	2,034.9	-35.9	26.8	0.04	-0.04	-0.32	-3.3	3.8	
2,127.0	2.86	157.80	2,125.8	-40.0	28.5	0.27	0.25	1.84	-1.3	2.8	
2,218.0	2.90	149.80	2,216.7	-44.0	30.5	0.44	0.04	-8.79	0.1	2.0	
2,399.0	3.00	146.36	2,397.4	-52.0	35.5	0.11	0.06	-1.90	3.3	1.9	
2,580.0	3.32	137.89	2,578.1	-59.8	41.6	0.31	0.18	-4.68	5.5	3.8	
2,761.0	4.64	140.16	2,758.7	-69.3	49.8	0.73	0.73	1.25	5.7	5.3	
2,943.0	4.56	139.27	2,940.1	-80.4	59.3	0.06	-0.04	-0.49	3.5	7.1	
3,034.0	4.20	138.33	3,030.9	-85.7	63.8	0.40	-0.40	-1.03	2.7	8.1	
3,125.0	4.16	137.02	3,121.6	-90.6	68.3	0.11	-0.04	-1.44	2.2	9.2	



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #504H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3670.0usft
Site:	Pegasus 3 Fed Com	MD Reference:	KB = 25 @ 3670.0usft
Well:	#504H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
3,216.0	4.06	138.40	3,212.4	-95.4	72.7	0.15	-0.11	1.52	2.1	10.2
3,307.0	4.52	139.95	3,303.1	-100.5	77.1	0.52	0.51	1.70	1.9	11.1
3,398.0	3.79	144.36	3,393.9	-105.7	81.2	0.88	-0.80	4.85	2.5	11.5
3,488.0	4.36	141.25	3,483.7	-110.8	85.1	0.68	0.63	-3.46	1.7	12.1
3,579.0	5.93	145.03	3,574.3	-117.4	89.9	1.76	1.73	4.15	0.7	12.5
3,669.0	5.78	147.74	3,663.8	-125.0	95.0	0.35	-0.17	3.01	-1.6	12.6
3,759.0	5.55	148.58	3,753.4	-132.6	99.7	0.27	-0.26	0.93	-4.0	12.6
3,849.0	4.97	150.06	3,843.0	-139.6	103.9	0.66	-0.64	1.64	-5.7	12.5
3,939.0	4.75	150.91	3,932.7	-146.3	107.7	0.26	-0.24	0.94	-6.9	12.2
4,030.0	4.37	151.44	4,023.4	-152.6	111.2	0.42	-0.42	0.58	-7.7	11.9
4,120.0	4.67	146.22	4,113.1	-158.7	114.8	0.57	0.33	-5.80	-9.5	11.0
4,211.0	5.45	148.32	4,203.8	-165.4	119.2	0.88	0.86	2.31	-10.8	11.3
4,301.0	5.14	143.71	4,293.4	-172.3	123.8	0.58	-0.34	-5.12	-13.7	10.5
4,392.0	4.93	148.90	4,384.0	-179.0	128.2	0.55	-0.23	5.70	-14.3	11.9
4,482.0	5.69	147.41	4,473.6	-186.0	132.6	0.86	0.84	-1.66	-16.7	11.4
4,573.0	6.25	145.06	4,564.1	-193.9	137.9	0.67	0.62	-2.58	-20.3	10.8
4,663.0	6.25	142.79	4,653.6	-201.8	143.7	0.27	0.00	-2.52	-24.2	10.3
4,754.0	5.67	144.47	4,744.1	-209.4	149.3	0.67	-0.64	1.85	-27.0	11.5
4,918.0	5.05	146.89	4,907.4	-222.0	157.9	0.40	-0.38	1.48	-30.4	13.0
5,008.0	5.17	142.62	4,997.0	-228.6	162.5	0.44	0.13	-4.74	-32.6	11.0
5,098.0	6.83	155.76	5,086.5	-236.7	167.2	2.38	1.84	14.60	-29.4	17.6
5,189.0	7.98	148.15	5,176.8	-247.0	172.8	1.66	1.26	-8.36	-30.9	12.7
5,279.0	9.67	145.59	5,265.7	-258.5	180.3	1.93	1.88	-2.84	-30.4	11.5
5,369.0	11.96	136.38	5,354.1	-271.5	191.0	3.18	2.54	-10.23	-33.3	8.4
5,459.0	11.64	135.34	5,442.2	-284.7	203.9	0.43	-0.36	-1.16	-36.6	10.9
5,550.0	11.75	133.83	5,531.3	-297.7	217.0	0.36	0.12	-1.66	-40.0	13.4
5,640.0	11.69	130.87	5,619.5	-310.0	230.5	0.67	-0.07	-3.29	-44.0	15.3



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #504H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3670.0usft
Site:	Pegasus 3 Fed Com	MD Reference:	KB = 25 @ 3670.0usft
Well:	#504H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
5,731.0	10.68	130.18	5,708.7	-321.5	243.9	1.12	-1.11	-0.76	-46.7	19.3
5,821.0	10.19	143.57	5,797.2	-333.2	255.0	2.74	-0.54	14.88	-41.6	32.4
5,912.0	10.10	141.72	5,886.8	-346.0	264.7	0.37	-0.10	-2.03	-42.9	32.4
6,002.0	10.69	142.70	5,975.3	-358.8	274.7	0.68	0.66	1.09	-43.0	34.5
6,093.0	9.73	144.10	6,064.9	-371.8	284.3	1.09	-1.05	1.54	-42.6	36.6
6,184.0	9.51	153.01	6,154.6	-384.7	292.2	1.65	-0.24	9.79	-35.9	42.3
6,365.0	11.92	153.76	6,332.5	-414.8	307.3	1.33	1.33	0.41	-37.8	39.5
6,455.0	11.26	153.60	6,420.6	-431.0	315.3	0.73	-0.73	-0.18	-40.5	37.7
6,546.0	10.31	153.78	6,510.0	-446.3	322.8	1.04	-1.04	0.20	-41.7	36.1
6,636.0	8.78	149.12	6,598.8	-459.4	329.9	1.90	-1.70	-5.18	-43.7	31.5
6,726.0	7.46	143.21	6,687.9	-470.0	337.0	1.73	-1.47	-6.57	-43.7	27.3
6,817.0	4.56	134.06	6,778.4	-477.2	343.1	3.35	-3.19	-10.05	-41.5	22.8
6,907.0	2.12	105.57	6,868.2	-480.1	347.3	3.20	-2.71	-31.66	-40.4	9.1
6,998.0	0.21	168.17	6,959.2	-480.8	348.9	2.23	-2.10	68.79	3.2	35.9
7,088.0	0.11	202.56	7,049.2	-481.0	348.9	0.15	-0.11	38.21	31.4	15.2
7,178.0	0.30	307.32	7,139.2	-480.9	348.7	0.38	0.21	116.40	-8.0	-39.6
7,268.0	0.47	298.95	7,229.2	-480.6	348.2	0.20	0.19	-9.30	-15.6	-47.4
7,359.0	0.21	244.51	7,320.2	-480.5	347.7	0.43	-0.29	-59.82	27.6	-52.6
7,449.0	1.14	234.67	7,410.2	-481.1	346.8	1.04	1.03	-10.93	35.5	-56.2
7,540.0	1.46	230.72	7,501.1	-482.3	345.2	0.36	0.35	-4.34	37.9	-60.0
7,721.0	0.94	303.61	7,682.1	-483.0	342.2	0.82	-0.29	40.27	-51.9	-53.2
7,902.0	0.78	242.60	7,863.1	-482.7	339.8	0.49	-0.09	-33.71	19.4	-72.5
7,992.0	1.09	236.56	7,953.1	-483.5	338.6	0.36	0.34	-6.71	25.4	-70.1
8,083.0	0.89	222.04	8,044.1	-484.5	337.4	0.35	-0.22	-15.96	40.6	-61.7
8,264.0	0.99	208.75	8,225.1	-486.9	335.7	0.13	0.06	-7.34	50.8	-51.0
8,354.0	0.99	211.76	8,315.0	-488.2	334.9	0.06	0.00	3.34	46.5	-53.6
8,445.0	1.04	198.31	8,406.0	-489.7	334.2	0.27	0.05	-14.78	56.1	-41.5



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #504H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3670.0usft
Site:	Pegasus 3 Fed Com	MD Reference:	KB = 25 @ 3670.0usft
Well:	#504H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
8,535.0	1.35	197.04	8,496.0	-491.5	333.7	0.35	0.34	-1.41	55.1	-40.3
8,626.0	1.07	208.94	8,587.0	-493.3	333.0	0.41	-0.31	13.08	43.8	-50.5
8,716.0	1.34	206.99	8,677.0	-494.9	332.1	0.30	0.30	-2.17	43.6	-49.0
8,807.0	1.92	175.28	8,767.9	-497.4	331.7	1.15	0.64	-34.85	60.4	-19.4
8,897.0	2.65	160.75	8,857.9	-500.9	332.5	1.03	0.81	-16.14	59.8	-4.0
8,988.0	1.91	163.69	8,948.8	-504.3	333.6	0.82	-0.81	3.23	55.9	-6.9
9,078.0	2.08	170.37	9,038.7	-507.4	334.3	0.32	0.19	7.42	51.6	-13.2
9,168.0	1.17	169.19	9,128.7	-509.9	334.8	1.01	-1.01	-1.31	49.3	-12.2
9,259.0	1.77	110.19	9,219.7	-511.3	336.3	1.69	0.66	-64.84	33.9	35.2
9,349.0	1.45	91.05	9,309.6	-511.8	338.7	0.69	-0.36	-21.27	18.1	43.9
9,440.0	0.87	69.24	9,400.6	-511.5	340.5	0.79	-0.64	-23.97	-1.3	47.1
9,531.0	1.07	81.49	9,491.6	-511.2	342.0	0.32	0.22	13.46	7.2	46.4
9,622.0	0.51	117.23	9,582.6	-511.2	343.2	0.79	-0.62	39.27	31.9	34.0
9,712.0	1.15	118.54	9,672.6	-511.8	344.3	0.71	0.71	1.46	31.3	33.2
9,803.0	2.10	128.39	9,763.5	-513.3	346.5	1.08	1.04	10.82	34.0	27.5
9,894.0	3.89	122.87	9,854.4	-516.0	350.4	1.99	1.97	-6.07	26.4	30.5
9,985.0	4.93	125.62	9,945.1	-520.0	356.1	1.17	1.14	3.02	20.8	29.4
10,077.0	4.32	132.66	10,036.8	-524.6	361.9	0.90	-0.66	7.65	16.9	27.1
10,167.0	2.92	147.28	10,126.7	-528.9	365.6	1.85	-1.56	16.24	17.6	22.8
10,257.0	3.16	151.59	10,216.5	-533.0	368.0	0.37	0.27	4.79	14.5	21.6
10,347.0	1.82	142.47	10,306.5	-536.3	370.1	1.55	-1.49	-10.13	7.0	23.2
10,437.0	1.27	144.96	10,396.4	-538.2	371.5	0.62	-0.61	2.77	5.6	22.9
10,458.0	1.24	137.70	10,417.4	-538.6	371.8	0.77	-0.14	-34.57	2.2	23.4
10,525.0	2.51	56.31	10,484.4	-538.3	373.5	3.92	1.90	-121.47	-22.5	2.0
KOP, MD:10525.0', TVD:10484.4', N/S: -538.3', E/W:373.5', INC:2.51										
10,544.0	3.19	50.05	10,503.4	-537.7	374.3	3.92	3.57	-32.96	-21.9	-2.4
10,634.0	14.78	18.70	10,592.1	-525.2	379.9	13.52	12.88	-34.83	-12.0	-21.4



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #504H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3670.0usft
Site:	Pegasus 3 Fed Com	MD Reference:	KB = 25 @ 3670.0usft
Well:	#504H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
10,693.5	24.19	13.21	10,648.2	-506.1	385.1	16.09	15.81	-9.22	-9.2	-28.1	
HL Crossing, MD:10693.5', TVD:10648.2', N/S:-506.1', E/W:385.1', INC:24.19											
10,724.0	29.05	11.73	10,675.4	-492.8	388.1	16.09	15.94	-4.86	-9.5	-31.3	
10,815.0	36.59	9.53	10,751.9	-444.3	397.1	8.39	8.29	-2.42	-11.4	-40.6	
10,905.0	44.68	0.14	10,820.2	-386.1	401.6	11.25	8.99	-10.43	-6.5	-46.6	
10,996.0	55.08	352.16	10,878.8	-316.9	396.6	13.23	11.43	-8.77	-3.9	-42.5	
11,086.0	69.50	355.63	10,920.5	-237.9	388.3	16.38	16.02	3.86	-12.1	-34.6	
11,177.0	74.51	355.09	10,948.6	-151.6	381.3	5.53	5.51	-0.59	-19.4	-28.3	
11,267.0	78.41	352.56	10,969.7	-64.6	371.8	5.12	4.33	-2.81	-18.8	-19.3	
11,358.0	81.41	353.88	10,985.6	24.3	361.3	3.59	3.30	1.45	-9.2	-9.1	
11,448.0	85.06	353.60	10,996.2	113.1	351.5	4.07	4.06	-0.31	1.5	0.2	
11,538.0	87.11	353.82	11,002.4	202.4	341.7	2.29	2.28	0.24	7.9	9.5	
11,628.0	89.26	355.29	11,005.2	291.9	333.2	2.89	2.39	1.63	11.1	17.4	
11,719.0	90.34	357.75	11,005.6	382.7	327.6	2.95	1.19	2.70	11.6	22.4	
11,809.0	91.04	359.34	11,004.5	472.7	325.4	1.93	0.78	1.77	10.8	24.1	
11,899.0	90.91	358.98	11,002.9	562.7	324.0	0.43	-0.14	-0.40	9.5	24.9	
11,990.0	89.60	357.95	11,002.5	653.6	321.6	1.83	-1.44	-1.13	9.4	26.7	
12,080.0	91.78	0.63	11,001.4	743.6	320.5	3.84	2.42	2.98	8.5	27.3	
12,172.0	92.85	0.49	10,997.7	835.5	321.4	1.17	1.16	-0.15	5.1	25.8	
12,263.0	88.96	0.89	10,996.3	926.5	322.5	4.30	-4.27	0.44	3.9	24.1	
12,354.0	90.60	0.36	10,996.6	1,017.5	323.5	1.89	1.80	-0.58	4.5	22.5	
12,445.0	92.25	0.19	10,994.4	1,108.5	323.9	1.82	1.81	-0.19	2.5	21.5	
12,536.0	90.84	359.34	10,991.9	1,199.4	323.5	1.81	-1.55	-0.93	0.3	21.3	
12,650.0	91.65	359.45	10,989.5	1,313.4	322.3	0.72	0.71	0.10	-1.9	21.8	
12,740.0	90.64	359.82	10,987.7	1,403.4	321.8	1.20	-1.12	0.41	-3.4	21.8	
12,831.0	91.44	0.17	10,986.0	1,494.3	321.7	0.96	0.88	0.38	-4.8	21.2	
12,922.0	89.50	0.18	10,985.3	1,585.3	322.0	2.13	-2.13	0.01	-5.3	20.4	



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #504H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3670.0usft
Site:	Pegasus 3 Fed Com	MD Reference:	KB = 25 @ 3670.0usft
Well:	#504H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
13,013.0	90.97	0.24	10,984.9	1,676.3	322.4	1.62	1.62	0.07	-5.4	19.5	
13,104.0	91.07	359.70	10,983.3	1,767.3	322.3	0.60	0.11	-0.59	-6.8	18.9	
13,195.0	90.54	359.63	10,982.0	1,858.3	321.8	0.59	-0.58	-0.08	-7.8	18.9	
13,287.0	89.60	359.33	10,981.9	1,950.3	320.9	1.07	-1.02	-0.33	-7.7	19.1	
13,377.0	90.27	359.22	10,982.0	2,040.3	319.8	0.75	0.74	-0.12	-7.3	19.7	
13,468.0	89.70	359.52	10,982.0	2,131.3	318.8	0.71	-0.63	0.33	-7.0	20.1	
13,559.0	91.68	0.02	10,980.9	2,222.3	318.4	2.24	2.18	0.55	-7.9	19.9	
13,649.0	90.97	0.10	10,978.8	2,312.3	318.5	0.79	-0.79	0.09	-9.7	19.2	
13,740.0	88.46	0.49	10,979.3	2,403.2	319.0	2.79	-2.76	0.43	-9.0	18.2	
13,830.0	90.27	0.63	10,980.3	2,493.2	319.9	2.02	2.01	0.16	-7.7	16.7	
13,921.0	89.33	0.54	10,980.6	2,584.2	320.8	1.04	-1.03	-0.10	-7.5	15.2	
14,011.0	88.76	1.11	10,982.1	2,674.2	322.1	0.90	-0.63	0.63	-6.0	13.4	
14,102.0	91.24	2.65	10,982.1	2,765.1	325.1	3.21	2.73	1.69	-6.1	9.8	
14,193.0	88.89	358.78	10,982.0	2,856.1	326.2	4.98	-2.58	-4.25	-6.3	8.1	
14,283.0	88.62	357.56	10,983.9	2,946.0	323.4	1.39	-0.30	-1.36	-4.4	10.4	
14,374.0	89.13	357.10	10,985.7	3,036.9	319.1	0.75	0.56	-0.51	-2.7	14.1	
14,464.0	90.27	0.82	10,986.2	3,126.9	317.5	4.32	1.27	4.13	-2.3	15.1	
14,555.0	91.31	0.55	10,984.9	3,217.9	318.6	1.18	1.14	-0.30	-3.6	13.5	
14,646.0	89.23	359.17	10,984.5	3,308.9	318.3	2.74	-2.29	-1.52	-4.1	13.1	
14,736.0	89.26	358.97	10,985.7	3,398.8	316.9	0.22	0.03	-0.22	-3.0	14.0	
14,827.0	91.51	0.74	10,985.1	3,489.8	316.7	3.15	2.47	1.95	-3.7	13.6	
14,918.0	90.97	0.39	10,983.1	3,580.8	317.6	0.71	-0.59	-0.38	-5.7	12.2	
15,010.0	87.28	358.66	10,984.5	3,672.8	316.8	4.43	-4.01	-1.88	-4.4	12.3	
15,101.0	86.98	357.71	10,989.1	3,763.6	313.9	1.09	-0.33	-1.04	0.0	14.6	
15,192.0	88.32	357.67	10,992.8	3,854.5	310.2	1.47	1.47	-0.04	3.7	17.7	
15,283.0	89.77	0.21	10,994.3	3,945.4	308.6	3.21	1.59	2.79	5.2	18.8	
15,375.0	90.54	0.33	10,994.1	4,037.4	309.0	0.85	0.84	0.13	4.8	17.8	



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #504H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3670.0usft
Site:	Pegasus 3 Fed Com	MD Reference:	KB = 25 @ 3670.0usft
Well:	#504H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
15,466.0	92.32	1.40	10,991.8	4,128.4	310.4	2.28	1.96	1.18	2.5	15.9	
15,556.0	88.26	359.60	10,991.4	4,218.4	311.2	4.93	-4.51	-2.00	2.0	14.5	
15,647.0	88.93	0.23	10,993.6	4,309.3	311.0	1.01	0.74	0.69	4.1	14.1	
15,738.0	88.22	0.94	10,995.8	4,400.3	312.0	1.10	-0.78	0.78	6.3	12.6	
15,828.0	91.51	1.90	10,996.1	4,490.2	314.2	3.81	3.66	1.07	6.5	9.8	
15,919.0	93.02	1.76	10,992.5	4,581.1	317.1	1.67	1.66	-0.15	2.8	6.3	
16,010.0	92.52	1.13	10,988.1	4,672.0	319.4	0.88	-0.55	-0.69	-1.7	3.4	
16,100.0	93.36	0.92	10,983.4	4,761.9	321.0	0.96	0.93	-0.23	-6.4	1.2	
16,191.0	91.61	0.59	10,979.5	4,852.8	322.2	1.96	-1.92	-0.36	-10.4	-0.5	
16,283.0	91.28	0.72	10,977.2	4,944.7	323.2	0.39	-0.36	0.14	-12.8	-2.2	
16,374.0	90.23	359.73	10,976.0	5,035.7	323.6	1.59	-1.15	-1.09	-13.8	-3.1	
16,465.0	88.52	359.93	10,977.0	5,126.7	323.3	1.89	-1.88	0.22	-12.3	-3.4	
16,555.0	89.23	359.61	10,978.7	5,216.7	323.0	0.87	0.79	-0.36	-10.0	-3.6	
16,646.0	88.02	359.51	10,980.9	5,307.7	322.3	1.33	-1.33	-0.11	-7.2	-3.5	
16,736.0	88.76	359.58	10,983.5	5,397.6	321.5	0.83	0.82	0.08	-4.2	-3.4	
16,827.0	89.19	359.28	10,985.1	5,488.6	320.6	0.58	0.47	-0.33	-2.0	-3.0	
16,917.0	87.68	0.24	10,987.5	5,578.6	320.3	1.99	-1.68	1.07	1.0	-3.2	
17,008.0	88.26	359.92	10,990.8	5,669.5	320.4	0.73	0.64	-0.35	4.8	-3.9	
17,098.0	88.72	0.08	10,993.1	5,759.5	320.4	0.54	0.51	0.18	7.7	-4.5	
17,189.0	90.91	359.87	10,993.4	5,850.5	320.4	2.42	2.41	-0.23	8.5	-5.0	
17,279.0	91.98	359.71	10,991.2	5,940.4	320.0	1.20	1.19	-0.18	6.8	-5.3	
17,369.0	91.71	359.35	10,988.3	6,030.4	319.3	0.50	-0.30	-0.40	4.4	-5.1	
17,460.0	90.13	0.31	10,986.8	6,121.4	319.0	2.03	-1.74	1.05	3.5	-5.4	
17,550.0	90.97	0.24	10,985.9	6,211.4	319.4	0.94	0.93	-0.08	3.2	-6.4	
17,641.0	88.39	0.37	10,986.4	6,302.4	319.9	2.84	-2.84	0.14	4.3	-7.5	
17,731.0	87.68	359.87	10,989.5	6,392.3	320.1	0.96	-0.79	-0.56	7.9	-8.3	
17,822.0	89.40	359.81	10,991.9	6,483.3	319.9	1.89	1.89	-0.07	10.8	-8.6	



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #504H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3670.0usft
Site:	Pegasus 3 Fed Com	MD Reference:	KB = 25 @ 3670.0usft
Well:	#504H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
17,912.0	90.40	359.33	10,992.0	6,573.3	319.2	1.23	1.11	-0.53	11.5	-8.5
18,003.0	90.27	358.50	10,991.5	6,664.2	317.5	0.92	-0.14	-0.91	11.5	-7.3
18,093.0	90.74	358.88	10,990.7	6,754.2	315.4	0.67	0.52	0.42	11.2	-5.8
18,184.0	92.05	0.43	10,988.5	6,845.2	314.9	2.23	1.44	1.70	9.6	-5.9
18,274.0	94.03	0.32	10,983.7	6,935.0	315.4	2.20	2.20	-0.12	5.3	-7.0
18,365.0	92.62	359.15	10,978.4	7,025.9	315.0	2.01	-1.55	-1.29	0.6	-7.2
18,455.0	90.50	359.99	10,976.0	7,115.8	314.4	2.53	-2.36	0.93	-1.3	-7.1
18,545.0	90.57	0.37	10,975.1	7,205.8	314.6	0.43	0.08	0.42	-1.6	-7.9
18,636.0	91.75	0.50	10,973.3	7,296.8	315.3	1.30	1.30	0.14	-2.9	-9.2
18,726.0	90.94	1.12	10,971.2	7,386.8	316.6	1.13	-0.90	0.69	-4.5	-11.1
18,817.0	90.67	0.58	10,969.9	7,477.8	317.9	0.66	-0.30	-0.59	-5.2	-13.0
18,907.0	87.41	359.50	10,971.4	7,567.7	318.0	3.82	-3.62	-1.20	-3.2	-13.6
18,998.0	86.30	359.31	10,976.4	7,658.6	317.1	1.24	-1.22	-0.21	2.3	-13.3
19,088.0	88.15	359.14	10,980.8	7,748.5	315.9	2.06	2.06	-0.19	7.2	-12.6
19,179.0	89.63	359.13	10,982.5	7,839.5	314.5	1.63	1.63	-0.01	9.4	-11.8
19,270.0	87.95	357.41	10,984.4	7,930.4	311.7	2.64	-1.85	-1.89	11.9	-9.6
19,362.0	88.86	357.52	10,987.0	8,022.3	307.7	1.00	0.99	0.12	14.9	-6.2
19,453.0	90.77	357.97	10,987.3	8,113.2	304.1	2.16	2.10	0.49	15.7	-3.2
19,544.0	91.98	357.45	10,985.1	8,204.1	300.4	1.45	1.33	-0.57	14.1	-0.1
19,636.0	90.37	358.26	10,983.2	8,296.0	297.0	1.96	-1.75	0.88	12.7	2.8
19,727.0	91.21	358.42	10,982.0	8,386.9	294.4	0.94	0.92	0.18	11.9	4.8
19,818.0	90.17	357.58	10,980.9	8,477.9	291.2	1.47	-1.14	-0.92	11.3	7.4
19,910.0	90.87	359.57	10,980.0	8,569.8	288.9	2.29	0.76	2.16	11.0	9.1
20,001.0	91.75	0.33	10,978.0	8,660.8	288.8	1.28	0.97	0.84	9.4	8.6
20,092.0	90.47	0.84	10,976.2	8,751.8	289.8	1.51	-1.41	0.56	8.2	7.1
20,182.0	88.76	1.40	10,976.8	8,841.8	291.5	2.00	-1.90	0.62	9.3	4.8
20,272.0	89.26	1.92	10,978.4	8,931.7	294.1	0.80	0.56	0.58	11.3	1.6



EOG Resources

Final PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #504H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3670.0usft
Site:	Pegasus 3 Fed Com	MD Reference:	KB = 25 @ 3670.0usft
Well:	#504H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.14

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
20,363.0	89.60	1.71	10,979.3	9,022.7	297.0	0.44	0.37	-0.23	12.8	-1.9
20,453.0	89.60	1.35	10,979.9	9,112.6	299.4	0.40	0.00	-0.40	13.9	-4.8
20,544.0	89.63	1.71	10,980.5	9,203.6	301.8	0.40	0.03	0.40	15.0	-7.8
20,634.0	90.20	1.55	10,980.6	9,293.6	304.4	0.66	0.63	-0.18	15.6	-11.0
20,725.0	90.77	1.73	10,979.9	9,384.5	307.0	0.66	0.63	0.20	15.4	-14.1
20,815.0	91.88	1.80	10,977.8	9,474.5	309.8	1.24	1.23	0.08	13.8	-17.5
20,905.0	92.52	1.99	10,974.3	9,564.3	312.7	0.74	0.71	0.21	10.9	-21.0
20,996.0	93.02	2.06	10,969.9	9,655.2	316.0	0.55	0.55	0.08	7.0	-24.8
21,086.0	93.66	2.28	10,964.7	9,745.0	319.4	0.75	0.71	0.24	2.3	-28.8
21,110.0	93.90	2.17	10,963.1	9,768.9	320.3	1.10	1.00	-0.46	0.8	-29.9
Final MWD Survey (MD=21110.0')										
21,173.0	93.90	2.17	10,958.8	9,831.7	322.7	0.00	0.00	0.00	-3.1	-32.7
Final Projection to Bit (MD=21173.0')										

Design Annotations				
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
10,525.0	10,484.4	-538.3	373.5	KOP, MD:10525.0', TVD:10484.4', N/S:-538.3', E/W:373.5', INC:2.51
10,693.5	10,648.2	-506.1	385.1	HL Crossing, MD:10693.5', TVD:10648.2', N/S:-506.1', E/W:385.1', INC:24.19
21,110.0	10,963.1	9,768.9	320.3	Final MWD Survey (MD=21110.0')
21,173.0	10,958.8	9,831.7	322.7	Final Projection to Bit (MD=21173.0')

Checked By: _____ Approved By: _____ Date: _____

I CERTIFY THIS SURVEY TO BE TRUE AND CORRECT TO THE BEST OF MY BELIEF AND KNOWLEDGE
KAY MADDOX 11/11/2021

Intent ☐ As Drilled ☐

API #		
Operator Name:	Property Name:	Well Number

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

First Take Point (FTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Is this well the defining well for the Horizontal Spacing Unit? ☐Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018

Submit To Appropriate District Office Two Copies <u>District I</u> 1625 N. French Dr., Hobbs, NM 88240 <u>District II</u> 811 S. First St., Artesia, NM 88210 <u>District III</u> 1000 Rio Brazos Rd., Aztec, NM 87410 <u>District IV</u> 1220 S. St. Francis Dr., Santa Fe, NM 87505		State of New Mexico Energy, Minerals and Natural Resources Oil Conservation Division 1220 South St. Francis Dr. Santa Fe, NM 87505			Form C-105 Revised August 1, 2011													
WELL COMPLETION OR RECOMPLETION REPORT AND LOG																		
4. Reason for filing: ☒ COMPLETION REPORT (Fill in boxes #1 through #31 for State and Fee wells only) ☐ C-144 CLOSURE ATTACHMENT (Fill in boxes #1 through #9, #15 Date Rig Released and #32 and/or #33; attach this and the plat to the C-144 closure report in accordance with 19.15.17.13.K NMAC)								5. Lease Name or Unit Agreement Name PEGASUS 3 FED COM										
								6. Well Number: 504H										
7. Type of Completion: ☒ NEW WELL ☐ WORKOVER ☐ DEEPENING ☐ PLUGBACK ☐ DIFFERENT RESERVOIR ☐ OTHER _____																		
8. Name of Operator EOG RESOURCES INC							9. OGRID 7377											
10. Address of Operator PO BOX 2267 MIDLAND, TEXAS 79702							11. Pool name or Wildcat TRISTE DRAW; BONE SPRING (96603)											
12. Location	Unit Ltr	Section	Township	Range	Lot	Feet from the	N/S Line	Feet from the	E/W Line	County								
Surface:	O	03	24S	32E		611	SOUTH	2003	EAST	LEA								
BH:	B	34	23S	32E		111	NORTH	1618	EAST	LEA								
13. Date Spudded 03/27/2021	14. Date T.D. Reached 05/13/2021		15. Date Rig Released 05/15/2021			16. Date Completed (Ready to Produce) 10/25/2021		17. Elevations (DF and RKB, RT, GR, etc.) 3645' GL										
18. Total Measured Depth of Well MD 21,173' TVD 10,958'			19. Plug Back Measured Depth MD 21,151' TVD 10,958'			20. Was Directional Survey Made? YES		21. Type Electric and Other Logs Run None										
22. Producing Interval(s), of this completion - Top, Bottom, Name BONE SPRING 11,027 - 21,151'																		
23. CASING RECORD (Report all strings set in well)																		
CASING SIZE		WEIGHT LB./FT.		DEPTH SET		HOLE SIZE		CEMENTING RECORD		AMOUNT PULLED								
13 3/8"		54.5# J-55		1248'		17 1/2"		1070 SXS CL C/CIRC										
9 5/8"		40# ECP 110		4823'		12 1/4"		1365 SXS CL C TOC 500'		TS								
5 1/2"		20# ECP 110		21,195'		8 1/2"		3580 SXS CL H TOC 554'		CBL								
24. LINER RECORD						25. TUBING RECORD												
SIZE	TOP	BOTTOM	SACKS CEMENT	SCREEN		SIZE	DEPTH SET	PACKER SET										
26. Perforation record (interval, size, and number) 11,027 - 21,151' 3 1/8", 2854 holes						27. ACID, SHOT, FRACTURE, CEMENT, SQUEEZE, ETC. <table border="1" style="width:100%; border-collapse: collapse;"> <tr> <td>DEPTH INTERVAL</td> <td>AMOUNT AND KIND MATERIAL USED</td> </tr> <tr> <td>11,027 - 21,151'</td> <td>FRAC W/25,959,664 lbs proppant, 383,311 bbls load fld</td> </tr> <tr> <td> </td> <td> </td> </tr> <tr> <td> </td> <td> </td> </tr> </table>					DEPTH INTERVAL	AMOUNT AND KIND MATERIAL USED	11,027 - 21,151'	FRAC W/25,959,664 lbs proppant, 383,311 bbls load fld				
DEPTH INTERVAL	AMOUNT AND KIND MATERIAL USED																	
11,027 - 21,151'	FRAC W/25,959,664 lbs proppant, 383,311 bbls load fld																	
28. PRODUCTION																		
Date First Production 10/25/2021		Production Method (<i>Flowing, gas lift, pumping - Size and type pump</i>) Flowing				Well Status (<i>Prod. or Shut-in</i>) Producing												
Date of Test 11/04/2021	Hours Tested 24	Choke Size 64	Prod'n For Test Period	Oil - Bbl 4050	Gas - MCF 5655	Water - Bbl. 9044	Gas - Oil Ratio 1396											
Flow Tubing Press.	Casing Pressure 800	Calculated 24-Hour Rate	Oil - Bbl.	Gas - MCF	Water - Bbl.	Oil Gravity - API - (<i>Corr.</i>) 44												
29. Disposition of Gas (<i>Sold, used for fuel, vented, etc.</i>) SOLD								30. Test Witnessed By										
31. List Attachments C-102, C-104, C-103, Directional Survey, H spacing																		
32. If a temporary pit was used at the well, attach a plat with the location of the temporary pit.																		
33. If an on-site burial was used at the well, report the exact location of the on-site burial: Latitude _____ Longitude _____ NAD 1927 1983																		
I hereby certify that the information shown on both sides of this form is true and complete to the best of my knowledge and belief Signature Kay Maddox Name Kay Maddox Title Senior Regulatory Specialist Date 11/16/2021 E-mail Address kay_maddox@eogresources.com																		

This form is to be filed with the appropriate District Office of the Division not later than 20 days after the completion of any newly-drilled or deepened well and not later than 60 days after completion of closure. When submitted as a completion report, this shall be accompanied by one copy of all electrical and radio-activity logs run on the well and a summary of all special tests conducted, including drill stem tests. All depths reported shall be measured depths. In the case of directionally drilled wells, true vertical depths shall also be reported. For multiple completions, items 11, 12 and 26-31 shall be reported for each zone.

Southeastern New Mexico			Northwestern New Mexico			
T. Anhy	Rustler	1145'	T. Canyon	Brushy 7070'	T. Ojo Alamo	T. Penn A"
T. Salt		1449'	T. Strawn		T. Kirtland	T. Penn. "B"
B. Salt		4650'	T. Atoka		T. Fruitland	T. Penn. "C"
T. Yates			T. Miss		T. Pictured Cliffs	T. Penn. "D"
T. 7 Rivers			T. Devonian		T. Cliff House	T. Leadville
T. Queen			T. Silurian		T. Menefee	T. Madison
T. Grayburg			T. Montoya		T. Point Lookout	T. Elbert
T. San Andres			T. Simpson		T. Mancos	T. McCracken
T. Glorieta			T. McKee		T. Gallup	T. Ignacio Otzte
T. Paddock			T. Ellenburger		Base Greenhorn	T. Granite
T. Blinebry			T. Gr. Wash		T. Dakota	
T. Tubb			T. Delaware Sand		T. Morrison	
T. Drinkard			T. Bone Springs		T. Todilto	
T. Abo			T. 1st BS Sand	9884'	T. Entrada	
T. Wolfcamp			T. 2nd BS Sand	10,501'	T. Wingate	
T. Penn			T.		T. Chinle	
T. Cisco (Bough C)			T.		T. Permian	

No. 1, from.....to.....
No. 2, from.....to.....
No. 3, from.....to.....
No. 4, from.....to.....

Include data on rate of water inflow and elevation to which water rose in hole.

No. 1, from.....to.....feet.....
 No. 2, from.....to.....feet.....
 No. 3, from.....to.....feet.....

From	To	Thickness In Feet	Lithology

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

ACKNOWLEDGMENTS

Action 130503

ACKNOWLEDGMENTS

Operator: EOG RESOURCES INC P.O. Box 2267 Midland, TX 79702	OGRID: 7377
	Action Number: 130503
	Action Type: [C-104] Completion Packet (C-104C)

ACKNOWLEDGMENTS

☒	I hereby certify that the required Water Use Report has been, or will be, submitted for this wells completion.
☒	I hereby certify that the required FracFocus disclosure has been, or will be, submitted for this wells completion.

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 130503

CONDITIONS

Operator: EOG RESOURCES INC P.O. Box 2267 Midland, TX 79702	OGRID: 7377
	Action Number: 130503
	Action Type: [C-104] Completion Packet (C-104C)

CONDITIONS

Created By	Condition	Condition Date
plmartinez	File 3160-4 Completion Report within 10 days to NMOCD after BLM approval.	10/17/2023
