

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: ☐ DRILL ☐ REENTER 1b. Type of Well: ☐ Oil Well ☐ Gas Well ☐ Other 1c. Type of Completion: ☐ Hydraulic Fracturing ☐ Single Zone ☐ Multiple Zone		5. Lease Serial No. 6. If Indian, Allottee or Tribe Name 7. If Unit or CA Agreement, Name and No. 8. Lease Name and Well No.	
2. Name of Operator		9. API Well No. 30-015-54343	
3a. Address		3b. Phone No. (include area code) 10. Field and Pool, or Exploratory	
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		11. Sec., T. R. M. or Blk. and Survey or Area	
14. Distance in miles and direction from nearest town or post office*		12. County or Parish 13. State	
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)		16. No of acres in lease	
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.		17. Spacing Unit dedicated to this well	
19. Proposed Depth		20. BLM/BIA Bond No. in file	
21. Elevations (Show whether DF, KDB, RT, GL, etc.)		22. Approximate date work will start*	
23. Estimated duration		24. Attachments	
The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)			
1. Well plat certified by a registered surveyor. 2. A Drilling Plan. 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).		4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). 5. Operator certification. 6. Such other site specific information and/or plans as may be requested by the BLM.	
25. Signature		Name (Printed/Typed)	
Title		Date	
Approved by (Signature)		Name (Printed/Typed)	
Title		Date	
Office		Date	
Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon. Conditions of approval, if any, are attached.			
Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.			

APPROVED WITH CONDITIONS

(Continued on page 2)

*(Instructions on page 2)

Additional Operator Remarks

Location of Well

0. SHL: SESE / 390 FSL / 795 FEL / TWSP: 24S / RANGE: 29E / SECTION: 2 / LAT: 32.2405128 / LONG: -103.9492014 (TVD: 0 feet, MD: 0 feet)

PPP: SESE / 100 FSL / 440 FEL / TWSP: 24S / RANGE: 29E / SECTION: 2 / LAT: 32.2397188 / LONG: -103.948046 (TVD: 8672 feet, MD: 8713 feet)

BHL: NESE / 2620 FSL / 440 FEL / TWSP: 23S / RANGE: 29E / SECTION: 35 / LAT: 32.2611692 / LONG: -103.9481763 (TVD: 9045 feet, MD: 16699 feet)

BLM Point of Contact

Name: Candy Vigil

Title: LIE

Phone: (575) 234-5982

Email: cvigil@blm.gov

CONFIDENTIAL

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720

District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720

District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170

District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised August 1,
2011
Submit one copy to appropriate
District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-015-54343	² Pool Code [11520]	³ Pool Name CEDAR CANYON;BONE SPRING
⁴ Property Code 331701	⁵ Property Name TATER TOT 2-35 STATE FED COM	⁶ Well Number 236H
⁷ OGRID No. 6137	⁸ Operator Name DEVON ENERGY PRODUCTION COMPANY, L.P.	⁹ Elevation 3073.5

¹⁰ Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
P	2	24 S	29 E		390	SOUTH	795	EAST	EDDY

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
I	35	23 S	29 E		2620	SOUTH	440	EAST	EDDY

¹² Dedicated Acres	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.
479.2			

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

	¹⁷ OPERATOR CERTIFICATION I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division. <i>Jenny Harms</i> 4-7-2021 Signature Date JENNY HARMS Printed Name JENNY.HARMS@DVN.COM E-mail Address
	¹⁸ SURVEYOR CERTIFICATION I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief. MARCH 24, 2021 Date of Survey <i>Mon F. Jaramillo</i> Signature and Seal of Professional Surveyor Certificate Number: 12797

Intent ☒ As Drilled ☐

API #

Operator Name:	Property Name:	Well Number
DEVON ENERGY PRODUCTION CO., L.P.	TATER TOT 2-35 STATE FED COM	236H

Kick Off Point (KOP)

UL	Section 2	Township 24S	Range 29E	Lot	Feet 42 FSL	From N/S	Feet 440 FEL	From E/W	County EDDY
Latitude 32.23946448					Longitude -103.94804751			NAD 83	

First Take Point (FTP)

UL P	Section 2	Township 24S	Range 29E	Lot	Feet 100	From N/S SOUTH	Feet 440	From E/W EAST	County EDDY
Latitude 32.2397188					Longitude 103.9480460			NAD 83	

Last Take Point (LTP)

UL I	Section 35	Township 23S	Range 29E	Lot	Feet 2520	From N/S SOUTH	Feet 440	From E/W EAST	County EDDY
Latitude 32.2608944					Longitude 103.9481755			NAD 83	

Is this well the defining well for the Horizontal Spacing Unit?

☐ NO

Is this well an infill well?

☐ YES

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #

Operator Name:	Property Name:	Well Number

KZ 06/29/2018

State of New Mexico
Energy, Minerals and Natural Resources Department

Submit Electronically
Via E-permitting

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description

Effective May 25, 2021

I. Operator: DEVON ENERGY PRODUCTION COMPANY, LP **OGRID:** 6137 **Date:** 9 / 29 / 2021

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
See attachment.						

IV. Central Delivery Point Name: See attachment [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
See attachment						

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

[illegible]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow back Date	First Production Date
Tater Tot 2-35 State Fed Com 231H		9/4/2021	10/4/2021	2/1/2022	2/1/2022	2/1/2022
Tater Tot 2-35 State Fed Com 232H		9/19/2021	10/19/2021	2/16/2022	2/16/2022	2/16/2022
Tater Tot 2-35 State Fed Com 331H		4/20/2022	5/20/2022	9/17/2022	9/17/2022	9/17/2022
Tater Tot 2-35 State Fed Com 621H		5/24/2022	6/23/2022	10/21/2022	10/21/2022	10/21/2022
Tater Tot 2-35 State Fed Com 711H		5/5/2022	6/4/2022	10/2/2022	10/2/2022	10/2/2022
Tater Tot 2-35 State Fed Com 233H		9/28/2023	10/28/2023	2/25/2024	2/25/2024	2/25/2024
Tater Tot 2-35 State Fed Com 234H		9/13/2023	10/13/2023	2/10/2024	2/10/2024	2/10/2024
Tater Tot 2-35 State Fed Com 332H		5/21/2022	6/20/2022	10/18/2022	10/18/2022	10/18/2022
Tater Tot 2-35 State Fed Com 622H		6/5/2022	7/5/2022	11/2/2022	11/2/2022	11/2/2022
Tater Tot 2-35 State Fed Com 712H		6/21/2022	7/21/2022	11/18/2022	11/18/2022	11/18/2022
Tater Tot 2-35 State Fed Com 235H		10/2/2023	11/1/2023	2/29/2024	2/29/2024	2/29/2024
Tater Tot 2-35 State Fed Com 236H		9/17/2023	10/17/2023	2/14/2024	2/14/2024	2/14/2024
Tater Tot 2-35 State Fed Com 334H		6/6/2023	7/6/2023	11/3/2023	11/3/2023	11/3/2023
Tater Tot 2-35 State Fed Com 624H		6/22/2022	7/22/2022	11/19/2022	11/19/2022	11/19/2022

*Dates above are subject to change

Section 2 – Enhanced Plan

EFFECTIVE APRIL 1, 2022

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature:
Printed Name: Lindsey Miles
Title: Land Manager
E-mail Address:
Date:
Phone:
OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form)
Approved By:
Title:
Approval Date:
Conditions of Approval:



VI. Separation Equipment

Devon Energy Production Company, L.P. utilizes a "stage separation" process in which oil and gas separation is carried out through a series of separators operating at successively reduced pressures. Hydrocarbon liquids are produced into a high-pressure inlet separator, then carried through one or more lower pressure separation vessels before entering the storage tanks. The purpose of this separation process is to attain maximum recovery of liquid hydrocarbons from the fluids and allow maximum capture of produced gas into the sales pipeline. Devon utilizes a series of Low-Pressure Compression units to capture gas off the staged separation and send it to the sales pipeline. This process minimizes the amount of flash gas that enters the end-stage storage tanks that is subsequently vented or flared.



VII. Operational Practices

Devon Energy Production Company, L. P. will employ best management practices and control technologies to maximize the recovery and minimize waste of natural gas through venting and flaring.

- During drilling operations, Devon will utilize flares and/or combustors to capture and control natural gas, where technically feasible. If flaring is deemed technically in-feasible, Devon will employ best management practices to minimize or reduce venting to the extent possible.
- During completions operations, Devon will utilize Green Completion methods to capture gas produced during well completions that is otherwise vented or flared. If capture is technically in-feasible, flares and/or combustors will be used to capture and control flow back fluids entering into frac tanks during initial flowback. Upon indication of first measurable hydrocarbon volumes, Devon will turn operations to onsite separation vessels and flow to the gathering pipeline.
- During production operations, Devon will take every practical effort to minimize waste of natural gas through venting and flaring by:
 - Designing and constructing facilities in a manner consistent to achieve maximum capture and control of hydrocarbon liquids & produced gas
 - Utilizing a closed-loop capture system to collect and route produced gas to sales line via low pressure compression, or to a flare/combustor
 - Flaring in lieu of venting, where technically feasible
 - Utilizing auto-ignitors or continuous pilots, with thermocouples connected to Scada, to quickly detect and resolve issues related to malfunctioning flares/combustors
 - Employ the use of automatic tank gauging to minimize storage tank venting during loading events
 - Installing air-driven or electric-driven pneumatics & combustion engines, where technically feasible to minimize venting to the atmosphere
 - Confirm equipment is properly maintained and repaired through a preventative maintenance and repair program to ensure equipment meets all manufacturer specifications
 - Conduct and document AVO inspections on the frequency set forth in Part 27 to detect and repair any onsite leaks as quickly and efficiently as is feasible



VIII. Best Management Practices during Maintenance

Devon Energy Production Company, L.P. will utilize best management practices to minimize venting during active and planned maintenance activities. Devon is operating under guidance that production facilities permitted under NOI permits have no provisions to allow high pressure flaring and high pressure flaring is only allowed in disruption scenarios so long as the duration is less than eight hours. When technically feasible, flaring during maintenance activities will be utilized in lieu of venting to the atmosphere. Devon will work with third-party operators during scheduled maintenance of downstream pipeline or processing plants to address those events ahead of time to minimize venting. Actions considered include identifying alternative capture approaches or planning to temporarily reduce production or shut in the well to address these circumstances.

Tater Tot 2-35 State Fed Com 236H

1. Geologic Formations

TVD of target	9045	Pilot hole depth	N/A
MD at TD:	16699	Deepest expected fresh water	

Basin

Formation	Depth (TVD) from KB	Water/Mineral Bearing/Target Zone?	Hazards*
Rustler	260		
Salt	570		
Base of Salt	2995		
Delaware	3198		
Cherry Canyon	4075		
Brushy Canyon	5663		
1st Bone Spring Lime	6891		
Bone Spring 1st	7944		
Bone Spring 2nd	8672		
3rd Bone Spring Lime	9071		
Bone Spring 3rd	9869		
Wolfcamp	10216		

*H2S, water flows, loss of circulation, abnormal pressures, etc.

Tater Tot 2-35 State Fed Com 236H

2. Casing Program

Hole Size	Csg. Size	Wt (PPF)	Grade	Conn	Casing Interval		Casing Interval	
					From (MD)	To (MD)	From (TVD)	To (TVD)
17 1/2	13 3/8	48	H40	BTC	0	285	0	285
12 1/4	9 5/8	40	J-55	BTC	0	3095	0	3095
8 3/4	5 1/2	17	P110	BTC	0	16699	0	9045

- All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 IILB.1.h Must have table for contingency casing.

Tater Tot 2-35 State Fed Com 236H

3. Cementing Program (3-String Primary Design)

Casing	# Sks	TOC	Wt. (lb/gal)	Yld (ft ³ /sack)	Slurry Description
Surface	245	Surf	13.2	1.4	Lead: Class C Cement + additives
Int 1	320	Surf	9.0	3.3	Lead: Class C Cement + additives
	154	500' above shoe	13.2	1.4	Tail: Class H / C + additives
Int 1 Intermediate Squeeze	As Needed	Surf	9.0	3.3	Squeeze Lead: Class C Cement + additives
	320	Surf	9.0	3.3	Lead: Class C Cement + additives
	154	500' above shoe	13.2	1.4	Tail: Class H / C + additives
Production	504	500' tieback	9.0	3.3	Lead: Class H / C + additives
	1580	KOP	13.2	1.4	Tail: Class H / C + additives

If a DV tool is ran the depth(s) will be adjusted based on hole conditions and cement volumes will be adjusted proportionally. Slurry weights will be adjusted based on estimated fracture gradient of the formation. DV tool will be set a minimum of 50 feet below previous casing and a minimum of 200 feet above current shoe. If cement is not returned to surface during the primary cement job on the surface casing string, a planned top job will be conducted immediately after completion of the primary job.

Casing String	% Excess
Surface	50%
Intermediate	30%
Production	10%

Tater Tot 2-35 State Fed Com 236H

4. Pressure Control Equipment (Three String Design)

BOP installed and tested before drilling which hole?	Size?	Min. Required WP	Type	✓	Tested to:
Int 1	13-58"	5M	Annular	X	50% of rated working pressure
			Blind Ram	X	5M
			Pipe Ram		
			Double Ram	X	
			Other*		
Production	13-5/8"	5M	Annular	X	50% of rated working pressure
			Blind Ram	X	5M
			Pipe Ram		
			Double Ram	X	
			Other*		
			Annular (5M)		
			Blind Ram		
			Pipe Ram		
			Double Ram		
			Other*		

Tater Tot 2-35 State Fed Com 236H

5. Mud Program (Three String Design)

Section	Type	Weight (ppg)
Surface	FW Gel	8.5-9
Intermediate	Brine	10-10.5
Production	WBM	8.5-9

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times.

What will be used to monitor the loss or gain of fluid?	PVT/Pason/Visual Monitoring
---	-----------------------------

6. Logging and Testing Procedures

Logging, Coring and Testing	
X	Will run GR/CNL from TD to surface (horizontal well - vertical portion of hole). Stated logs run will be in the Completion Report and submitted to the BLM.
	No logs are planned based on well control or offset log information.
	Drill stem test? If yes, explain.
	Coring? If yes, explain.

Additional logs planned		Interval
	Resistivity	
	Density	
X	CBL	Production casing
X	Mud log	KOP to TD
	PEX	

7. Drilling Conditions

Condition	Specify what type and where?
BH pressure at deepest TVD	4233
Abnormal temperature	No

Mitigation measure for abnormal conditions. Describe. Lost circulation material/sweeps/mud scavengers.

Hydrogen Sulfide (H₂S) monitors will be installed prior to drilling out the surface shoe. If H₂S is detected in concentrations greater than 100 ppm, the operator will comply with the provisions of Onshore Oil and Gas Order #6. If Hydrogen Sulfide is encountered measured values and formations will be provided to the BLM.

N	H ₂ S is present
Y	H ₂ S plan attached.

Tater Tot 2-35 State Fed Com 236H

8. Other facets of operation

Is this a walking operation? Potentially

- 1 If operator elects, drilling rig will batch drill the surface holes and run/cement surface casing; walking the rig to next wells on the pad.
- 2 The drilling rig will then batch drill the intermediate sections and run/cement intermediate casing; the wellbore will be isolated with a blind flange and pressure gauge installed for monitoring the well before walking to the next well.
- 3 The drilling rig will then batch drill the production hole sections on the wells with OBM, run/cement production casing, and install TA caps or tubing heads for completions.

NOTE: During batch operations the drilling rig will be moved from well to well however, it will not be removed from the pad until all wells have production casing run/cemented.

Will be pre-setting casing? Potentially

- 1 Spudder rig will move in and batch drill surface hole.
 - a. Rig will utilize fresh water based mud to drill surface hole to TD. Solids control will be handled entirely on a closed loop basis.
- 2 After drilling the surface hole section, the spudder rig will run casing and cement following all of the applicable rules and regulations (OnShore Order 2, all COAs and NMOCD regulations).
- 3 The wellhead will be installed and tested once the surface casing is cut off and the WOC time has been reached.
- 4 A blind flange with the same pressure rating as the wellhead will be installed to seal the wellbore. Pressure will be monitored with a pressure gauge installed on the wellhead.
- 5 Spudder rig operations is expected to take 4-5 days per well on a multi-well pad.
- 6 The NMOCD will be contacted and notified 24 hours prior to commencing spudder rig operations.
- 7 Drilling operations will be performed with drilling rig. At that time an approved BOP stack will be nipped up and tested on the wellhead before drilling operations commences on each well.
 - a. The NMOCD will be contacted / notified 24 hours before the drilling rig moves back on to the pad with the pre-set surface casing.

Attachments

X Directional Plan
 Other, describe



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Drilling Plan Data Report

10/18/2023

APD ID: 10400088592

Submission Date: 10/26/2022

Highlighted data
reflects the most
recent changes

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: TATER TOT 2-35 STATE FED COM

Well Number: 236H

Well Type: OIL WELL

Well Work Type: Drill

[Show Final Text](#)

Section 1 - Geologic Formations

Formation ID	Formation Name	Elevation	True Vertical	Measured Depth	Lithologies	Mineral Resources	Producing Formatio
12317230	UNKNOWN	3093	0	0	OTHER : SURFACE	NONE	N
12317231	RUSTLER	2833	260	260	SANDSTONE	NONE	N
12317232	SALADO	2523	570	570	SALT	NONE	N
12317233	BASE OF SALT	98	2995	2995	ANHYDRITE	NATURAL GAS, OIL	N
12317234	BELL CANYON	-105	3198	3198	SANDSTONE	NATURAL GAS, OIL	N
12317235	CHERRY CANYON	-982	4075	4075	SANDSTONE	NATURAL GAS, OIL	N
12317236	BRUSHY CANYON	-2570	5663	5663	SANDSTONE	NATURAL GAS, OIL	N
12317243	BONE SPRING LIME	-3798	6891	6891	LIMESTONE	NATURAL GAS, OIL	N
12317237	BONE SPRING	-4851	7944	7944	SANDSTONE	NATURAL GAS, OIL	N
12317239	BONE SPRING 2ND	-5579	8672	8672	SANDSTONE	NATURAL GAS, OIL	Y
12317244	BONE SPRING LIME	-5978	9071	9071	LIMESTONE	NATURAL GAS, OIL	N
12317246	BONE SPRING 3RD	-6776	9869	9869	SANDSTONE, SHALE	NATURAL GAS, OIL	N
12317241	WOLFCAMP	-7123	10216	10216	SHALE	NATURAL GAS, OIL	N
12317242	STRAWN	-9106	12199	12199	LIMESTONE	NATURAL GAS, OIL	N

Section 2 - Blowout Prevention


Tater Tot 2-35 State Fed Com 236H



Well: Tater Tot 2-35 State Fed Com 236H
County: Eddy
Wellbore: Permit Plan
Design: Permit Plan #1

Geodetic System: US State Plane 1983
Datum: North American Datum 1927
Ellipsoid: Clarke 1866
Zone: 3001 - NM East (NAD83)

MD (ft)	INC (°)	AZI (°)	TVD (ft)	NS (ft)	EW (ft)	VS (ft)	DLS (°/100ft)	Comment
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	SHL
2000.00	0.00	140.00	2000.00	0.00	0.00	0.00	0.00	Start Tangent
2500.00	10.00	140.00	2497.47	-33.34	27.98	-32.24	2.00	Hold Tangent
4597.46	10.00	140.00	4563.06	-312.35	262.09	-302.01	0.00	Drop to Vertical
5097.46	0.00	140.00	5060.53	-345.69	290.07	-334.25	2.00	Hold Vertical
8508.98	0.00	0.00	8472.04	-345.69	290.07	-334.25	0.00	KOP
9408.98	90.00	0.00	9045.00	227.27	290.07	238.28	10.00	Landing Point
16698.99	90.00	0.00	9045.00	7517.28	290.07	7522.88	0.00	BHL

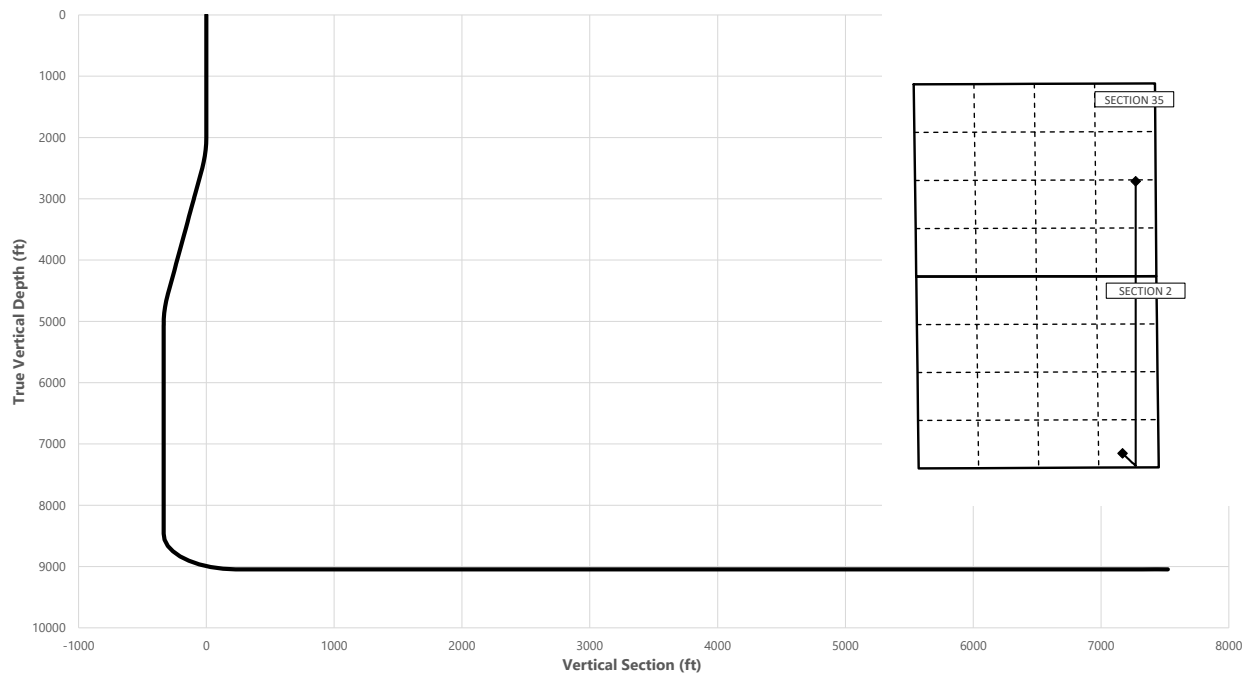

Key Depths	MD (ft)	TVD (ft)
Rustler	260.00	260.00
Salt	570.00	570.00
Base of Salt	3005.21	2995.00
Delaware	3211.34	3198.00
Cherry Canyon	4101.87	4075.00
Brushy Canyon	5699.93	5663.00
1st Bone Spring Lime	6927.93	6891.00
Bone Spring 1st	7980.93	7944.00
Bone Spring 2nd / Point of Penetrati	8713.23	8672.00
Exit	16618.99	9045.01
Bone Spring 3rd	#N/A	#N/A
Wolfcamp	#N/A	#N/A

SHL
KOP
Point of Penetration
Exit
BHL

MD (ft)	TVD (ft)	Lat (°)	Long (°)	Section Footages
0.00	0.00	32.2404	-103.9493	390' FSL, 795' FEL of Sec 2 in T24S, R29E
8508.98	8472.04	32.2395	-103.9484	42' FSL, 509' FEL of Sec 2 in T24S, R29E
8713.23	8672.00	32.2397	-103.9480	100' FSL, 440' FEL of Sec 2 in T24S, R29E
16618.99	9045.01	32.2609	-103.9482	2520' FSL, 440' FEL of Sec 35 in T24S, R29E
16698.99	9045.00	32.2611	-103.9483	2620' FSL, 440' FEL of Sec 35 in T24S, R29E

Tater Tot 2-35 State Fed Com 236H



Well: Tater Tot 2-35 State Fed Com 236H
County: Eddy
Wellbore: Permit Plan
Design: Permit Plan #1

Geodetic System: US State Plane 1983
Datum: North American Datum 1927
Ellipsoid: Clarke 1866
Zone: 3001 - NM East (NAD83)

MD (ft)	INC (°)	AZI (°)	TVD (ft)	NS (ft)	EW (ft)	VS (ft)	DLS (°/100ft)	Comment
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	SHL
100.00	0.00	140.00	100.00	0.00	0.00	0.00	0.00	
200.00	0.00	140.00	200.00	0.00	0.00	0.00	0.00	
260.00	0.00	140.00	260.00	0.00	0.00	0.00	0.00	Rustler
300.00	0.00	140.00	300.00	0.00	0.00	0.00	0.00	
400.00	0.00	140.00	400.00	0.00	0.00	0.00	0.00	
500.00	0.00	140.00	500.00	0.00	0.00	0.00	0.00	
570.00	0.00	140.00	570.00	0.00	0.00	0.00	0.00	Salt
600.00	0.00	140.00	600.00	0.00	0.00	0.00	0.00	
700.00	0.00	140.00	700.00	0.00	0.00	0.00	0.00	
800.00	0.00	140.00	800.00	0.00	0.00	0.00	0.00	
900.00	0.00	140.00	900.00	0.00	0.00	0.00	0.00	
1000.00	0.00	140.00	1000.00	0.00	0.00	0.00	0.00	
1100.00	0.00	140.00	1100.00	0.00	0.00	0.00	0.00	
1200.00	0.00	140.00	1200.00	0.00	0.00	0.00	0.00	
1300.00	0.00	140.00	1300.00	0.00	0.00	0.00	0.00	
1400.00	0.00	140.00	1400.00	0.00	0.00	0.00	0.00	
1500.00	0.00	140.00	1500.00	0.00	0.00	0.00	0.00	
1600.00	0.00	140.00	1600.00	0.00	0.00	0.00	0.00	
1700.00	0.00	140.00	1700.00	0.00	0.00	0.00	0.00	
1800.00	0.00	140.00	1800.00	0.00	0.00	0.00	0.00	
1900.00	0.00	140.00	1900.00	0.00	0.00	0.00	0.00	
2000.00	0.00	140.00	2000.00	0.00	0.00	0.00	0.00	Start Tangent
2100.00	2.00	140.00	2099.98	-1.34	1.12	-1.29	2.00	
2200.00	4.00	140.00	2199.84	-5.35	4.49	-5.17	2.00	
2300.00	6.00	140.00	2299.45	-12.02	10.09	-11.62	2.00	
2400.00	8.00	140.00	2398.70	-21.36	17.92	-20.65	2.00	
2500.00	10.00	140.00	2497.47	-33.34	27.98	-32.24	2.00	Hold Tangent
2600.00	10.00	140.00	2595.95	-46.64	39.14	-45.10	0.00	
2700.00	10.00	140.00	2694.43	-59.94	50.30	-57.96	0.00	
2800.00	10.00	140.00	2792.91	-73.25	61.46	-70.82	0.00	
2900.00	10.00	140.00	2891.39	-86.55	72.62	-83.68	0.00	
3000.00	10.00	140.00	2989.87	-99.85	83.79	-96.55	0.00	
3005.21	10.00	140.00	2995.00	-100.54	84.37	-97.22	0.00	Base of Salt
3100.00	10.00	140.00	3088.35	-113.15	94.95	-109.41	0.00	
3200.00	10.00	140.00	3186.83	-126.46	106.11	-122.27	0.00	
3211.34	10.00	140.00	3198.00	-127.96	107.38	-123.73	0.00	Delaware
3300.00	10.00	140.00	3285.31	-139.76	117.27	-135.13	0.00	
3400.00	10.00	140.00	3383.79	-153.06	128.43	-147.99	0.00	
3500.00	10.00	140.00	3482.27	-166.36	139.59	-160.86	0.00	
3600.00	10.00	140.00	3580.75	-179.66	150.76	-173.72	0.00	
3700.00	10.00	140.00	3679.23	-192.97	161.92	-186.58	0.00	
3800.00	10.00	140.00	3777.72	-206.27	173.08	-199.44	0.00	
3900.00	10.00	140.00	3876.20	-219.57	184.24	-212.30	0.00	
4000.00	10.00	140.00	3974.68	-232.87	195.40	-225.17	0.00	
4100.00	10.00	140.00	4073.16	-246.18	206.57	-238.03	0.00	
4101.87	10.00	140.00	4075.00	-246.42	206.78	-238.27	0.00	Cherry Canyon
4200.00	10.00	140.00	4171.64	-259.48	217.73	-250.89	0.00	
4300.00	10.00	140.00	4270.12	-272.78	228.89	-263.75	0.00	
4400.00	10.00	140.00	4368.60	-286.08	240.05	-276.61	0.00	
4500.00	10.00	140.00	4467.08	-299.38	251.21	-289.47	0.00	
4597.46	10.00	140.00	4563.06	-312.35	262.09	-302.01	0.00	Drop to Vertical
4600.00	9.95	140.00	4565.56	-312.69	262.37	-302.34	2.00	
4700.00	7.95	140.00	4664.34	-324.60	272.37	-313.86	2.00	
4800.00	5.95	140.00	4763.60	-333.87	280.15	-322.82	2.00	
4900.00	3.95	140.00	4863.22	-340.48	285.70	-329.21	2.00	
5000.00	1.95	140.00	4963.08	-344.42	289.00	-333.02	2.00	
5097.46	0.00	140.00	5060.53	-345.69	290.07	-334.25	2.00	Hold Vertical
5100.00	0.00	0.00	5063.07	-345.69	290.07	-334.25	0.00	
5200.00	0.00	0.00	5163.07	-345.69	290.07	-334.25	0.00	
5300.00	0.00	0.00	5263.07	-345.69	290.07	-334.25	0.00	
5400.00	0.00	0.00	5363.07	-345.69	290.07	-334.25	0.00	
5500.00	0.00	0.00	5463.07	-345.69	290.07	-334.25	0.00	
5600.00	0.00	0.00	5563.07	-345.69	290.07	-334.25	0.00	
5699.93	0.00	0.00	5663.00	-345.69	290.07	-334.25	0.00	Brushy Canyon
5700.00	0.00	0.00	5663.07	-345.69	290.07	-334.25	0.00	
5800.00	0.00	0.00	5763.07	-345.69	290.07	-334.25	0.00	
5900.00	0.00	0.00	5863.07	-345.69	290.07	-334.25	0.00	
6000.00	0.00	0.00	5963.07	-345.69	290.07	-334.25	0.00	
6100.00	0.00	0.00	6063.07	-345.69	290.07	-334.25	0.00	

Tater Tot 2-35 State Fed Com 236H



Well: Tater Tot 2-35 State Fed Com 236H
County: Eddy
Wellbore: Permit Plan
Design: Permit Plan #1

Geodetic System: US State Plane 1983
Datum: North American Datum 1927
Ellipsoid: Clarke 1866
Zone: 3001 - NM East (NAD83)

MD (ft)	INC (")	AZI (")	TVD (ft)	NS (ft)	EW (ft)	VS (ft)	DLS (°/100ft)	Comment
6200.00	0.00	0.00	6163.07	-345.69	290.07	-334.25	0.00	
6300.00	0.00	0.00	6263.07	-345.69	290.07	-334.25	0.00	
6400.00	0.00	0.00	6363.07	-345.69	290.07	-334.25	0.00	
6500.00	0.00	0.00	6463.07	-345.69	290.07	-334.25	0.00	
6600.00	0.00	0.00	6563.07	-345.69	290.07	-334.25	0.00	
6700.00	0.00	0.00	6663.07	-345.69	290.07	-334.25	0.00	
6800.00	0.00	0.00	6763.07	-345.69	290.07	-334.25	0.00	
6900.00	0.00	0.00	6863.07	-345.69	290.07	-334.25	0.00	
6927.93	0.00	0.00	6891.00	-345.69	290.07	-334.25	0.00	1st Bone Spring Lime
7000.00	0.00	0.00	6963.07	-345.69	290.07	-334.25	0.00	
7100.00	0.00	0.00	7063.07	-345.69	290.07	-334.25	0.00	
7200.00	0.00	0.00	7163.07	-345.69	290.07	-334.25	0.00	
7300.00	0.00	0.00	7263.07	-345.69	290.07	-334.25	0.00	
7400.00	0.00	0.00	7363.07	-345.69	290.07	-334.25	0.00	
7500.00	0.00	0.00	7463.07	-345.69	290.07	-334.25	0.00	
7600.00	0.00	0.00	7563.07	-345.69	290.07	-334.25	0.00	
7700.00	0.00	0.00	7663.07	-345.69	290.07	-334.25	0.00	
7800.00	0.00	0.00	7763.07	-345.69	290.07	-334.25	0.00	
7900.00	0.00	0.00	7863.07	-345.69	290.07	-334.25	0.00	
7980.93	0.00	0.00	7944.00	-345.69	290.07	-334.25	0.00	Bone Spring 1st
8000.00	0.00	0.00	7963.07	-345.69	290.07	-334.25	0.00	
8100.00	0.00	0.00	8063.07	-345.69	290.07	-334.25	0.00	
8200.00	0.00	0.00	8163.07	-345.69	290.07	-334.25	0.00	
8300.00	0.00	0.00	8263.07	-345.69	290.07	-334.25	0.00	
8400.00	0.00	0.00	8363.07	-345.69	290.07	-334.25	0.00	
8500.00	0.00	0.00	8463.07	-345.69	290.07	-334.25	0.00	
8508.98	0.00	0.00	8472.04	-345.69	290.07	-334.25	0.00	KOP
8600.00	9.10	0.00	8562.68	-338.47	290.07	-327.04	10.00	
8700.00	19.10	0.00	8659.55	-314.14	290.07	-302.72	10.00	
8713.23	20.43	0.00	8672.00	-309.67	290.07	-298.25	10.00	Bone Spring 2nd / Point of Penetration
8800.00	29.10	0.00	8750.71	-273.35	290.07	-261.97	10.00	
8900.00	39.10	0.00	8833.41	-217.36	290.07	-206.01	10.00	
9000.00	49.10	0.00	8905.13	-147.85	290.07	-136.56	10.00	
9100.00	59.10	0.00	8963.69	-66.95	290.07	-55.71	10.00	
9200.00	69.10	0.00	9007.31	22.89	290.07	34.06	10.00	
9300.00	79.10	0.00	9034.67	118.95	290.07	130.04	10.00	
9400.00	89.10	0.00	9044.93	218.29	290.07	229.31	10.00	
9408.98	90.00	0.00	9045.00	227.27	290.07	238.28	10.00	Landing Point
9500.00	90.00	0.00	9045.00	318.29	290.07	329.24	0.00	
9600.00	90.00	0.00	9045.00	418.29	290.07	429.17	0.00	
9700.00	90.00	0.00	9045.00	518.29	290.07	529.09	0.00	
9800.00	90.00	0.00	9045.00	618.29	290.07	629.02	0.00	
9900.00	90.00	0.00	9045.00	718.29	290.07	728.94	0.00	
10000.00	90.00	0.00	9045.00	818.29	290.07	828.87	0.00	
10100.00	90.00	0.00	9045.00	918.29	290.07	928.79	0.00	
10200.00	90.00	0.00	9045.00	1018.29	290.07	1028.72	0.00	
10300.00	90.00	0.00	9045.00	1118.29	290.07	1128.65	0.00	
10400.00	90.00	0.00	9045.00	1218.29	290.07	1228.57	0.00	
10500.00	90.00	0.00	9045.00	1318.29	290.07	1328.50	0.00	
10600.00	90.00	0.00	9045.00	1418.29	290.07	1428.42	0.00	
10700.00	90.00	0.00	9045.00	1518.29	290.07	1528.35	0.00	
10800.00	90.00	0.00	9045.00	1618.29	290.07	1628.27	0.00	
10900.00	90.00	0.00	9045.00	1718.29	290.07	1728.20	0.00	
11000.00	90.00	0.00	9045.00	1818.29	290.07	1828.12	0.00	
11100.00	90.00	0.00	9045.00	1918.29	290.07	1928.05	0.00	
11200.00	90.00	0.00	9045.00	2018.29	290.07	2027.98	0.00	
11300.00	90.00	0.00	9045.00	2118.29	290.07	2127.90	0.00	
11400.00	90.00	0.00	9045.00	2218.29	290.07	2227.83	0.00	
11500.00	90.00	0.00	9045.00	2318.29	290.07	2327.75	0.00	
11600.00	90.00	0.00	9045.00	2418.29	290.07	2427.68	0.00	
11700.00	90.00	0.00	9045.00	2518.29	290.07	2527.60	0.00	
11800.00	90.00	0.00	9045.00	2618.29	290.07	2627.53	0.00	
11900.00	90.00	0.00	9045.00	2718.29	290.07	2727.46	0.00	
12000.00	90.00	0.00	9045.00	2818.29	290.07	2827.38	0.00	
12100.00	90.00	0.00	9045.00	2918.29	290.07	2927.31	0.00	
12200.00	90.00	0.00	9045.00	3018.29	290.07	3027.23	0.00	
12300.00	90.00	0.00	9045.00	3118.29	290.07	3127.16	0.00	
12400.00	90.00	0.00	9045.00	3218.29	290.07	3227.08	0.00	
12500.00	90.00	0.00	9045.00	3318.29	290.07	3327.01	0.00	
12600.00	90.00	0.00	9045.00	3418.29	290.07	3426.93	0.00	

Tater Tot 2-35 State Fed Com 236H



Well: Tater Tot 2-35 State Fed Com 236H
County: Eddy
Wellbore: Permit Plan
Design: Permit Plan #1

Geodetic System: US State Plane 1983
Datum: North American Datum 1927
Ellipsoid: Clarke 1866
Zone: 3001 - NM East (NAD83)

MD	INC	AZI	TVD	NS	EW	VS	DLS	Comment
(ft)	(°)	(°)	(ft)	(ft)	(ft)	(ft)	(°/100ft)	
12700.00	90.00	0.00	9045.00	3518.29	290.07	3526.86	0.00	
12800.00	90.00	0.00	9045.00	3618.29	290.07	3626.79	0.00	
12900.00	90.00	0.00	9045.00	3718.29	290.07	3726.71	0.00	
13000.00	90.00	0.00	9045.00	3818.29	290.07	3826.64	0.00	
13100.00	90.00	0.00	9045.00	3918.29	290.07	3926.56	0.00	
13200.00	90.00	0.00	9045.01	4018.29	290.07	4026.49	0.00	
13300.00	90.00	0.00	9045.01	4118.29	290.07	4126.41	0.00	
13400.00	90.00	0.00	9045.01	4218.29	290.07	4226.34	0.00	
13500.00	90.00	0.00	9045.01	4318.29	290.07	4326.27	0.00	
13600.00	90.00	0.00	9045.01	4418.29	290.07	4426.19	0.00	
13700.00	90.00	0.00	9045.01	4518.29	290.07	4526.12	0.00	
13800.00	90.00	0.00	9045.01	4618.29	290.07	4626.04	0.00	
13900.00	90.00	0.00	9045.01	4718.29	290.07	4725.97	0.00	
14000.00	90.00	0.00	9045.01	4818.29	290.07	4825.89	0.00	
14100.00	90.00	0.00	9045.01	4918.29	290.07	4925.82	0.00	
14200.00	90.00	0.00	9045.01	5018.29	290.07	5025.74	0.00	
14300.00	90.00	0.00	9045.01	5118.29	290.07	5125.67	0.00	
14400.00	90.00	0.00	9045.01	5218.29	290.07	5225.60	0.00	
14500.00	90.00	0.00	9045.01	5318.29	290.07	5325.52	0.00	
14600.00	90.00	0.00	9045.01	5418.29	290.07	5425.45	0.00	
14700.00	90.00	0.00	9045.01	5518.29	290.07	5525.37	0.00	
14800.00	90.00	0.00	9045.01	5618.29	290.07	5625.30	0.00	
14900.00	90.00	0.00	9045.01	5718.29	290.07	5725.22	0.00	
15000.00	90.00	0.00	9045.01	5818.29	290.07	5825.15	0.00	
15100.00	90.00	0.00	9045.01	5918.29	290.07	5925.08	0.00	
15200.00	90.00	0.00	9045.01	6018.29	290.07	6025.00	0.00	
15300.00	90.00	0.00	9045.01	6118.29	290.07	6124.93	0.00	
15400.00	90.00	0.00	9045.01	6218.29	290.07	6224.85	0.00	
15500.00	90.00	0.00	9045.01	6318.29	290.07	6324.78	0.00	
15600.00	90.00	0.00	9045.01	6418.29	290.07	6424.70	0.00	
15700.00	90.00	0.00	9045.01	6518.29	290.07	6524.63	0.00	
15800.00	90.00	0.00	9045.01	6618.29	290.07	6624.55	0.00	
15900.00	90.00	0.00	9045.01	6718.29	290.07	6724.48	0.00	
16000.00	90.00	0.00	9045.01	6818.29	290.07	6824.41	0.00	
16100.00	90.00	0.00	9045.01	6918.29	290.07	6924.33	0.00	
16200.00	90.00	0.00	9045.01	7018.29	290.07	7024.26	0.00	
16300.00	90.00	0.00	9045.01	7118.29	290.07	7124.18	0.00	
16400.00	90.00	0.00	9045.01	7218.29	290.07	7224.11	0.00	
16500.00	90.00	0.00	9045.01	7318.29	290.07	7324.03	0.00	
16600.00	90.00	0.00	9045.01	7418.29	290.07	7423.96	0.00	
16618.99	90.00	0.00	9045.01	7437.28	290.07	7442.94	0.00	Exit
16698.99	90.00	0.00	9045.00	7517.28	290.07	7522.88	0.00	BHL



Well: Tater Tot 2-35 State Fed Com 236H
County: Eddy
Wellbore: Permit Plan
Design: Permit Plan #1

Geodetic System: US State Plane 1983
Datum: North American Datum 1927
Ellipsoid: Clarke 1866
Zone: 3001 - NM East (NAD83)

MD	INC	AZI	TVD	NS	EW	VS	DLS	Comment
(ft)	(°)	(°)	(ft)	(ft)	(ft)	(ft)	(°/100ft)	

Tater Tot 2-35 State Fed Com 236H

Well: Tater Tot 2-35 State Fed Com 236H
County: Eddy
Wellbore: Permit Plan
Design: Permit Plan #1

Geodetic System: US State Plane 1983
Datum: North American Datum 1927
Ellipsoid: Clarke 1866
Zone: 3001 - NM East (NAD83)

MD	INC	AZI	TVD	NS	EW	VS	DLS	Comment
(ft)	(°)	(°)	(ft)	(ft)	(ft)	(ft)	(°/100ft)	

A multibowl wellhead may be used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested.

Devon proposes using a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be 5000 (5M) psi.

- Wellhead will be installed by wellhead representatives.
- If the welding is performed by a third party, the wellhead representative will monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
- Wellhead representative will install the test plug for the initial BOP test.
- Wellhead company will install a solid steel body pack-off to completely isolate the lower head after cementing intermediate casing. After installation of the pack-off, the pack-off and the lower flange will be tested to 5M, as shown on the attached schematic. Everything above the pack-off will not have been altered whatsoever from the initial nipple up. Therefore the BOP components will not be retested at that time.
- If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head will be cut and top out operations will be conducted.
- Devon will pressure test all seals above and below the mandrel (but still above the casing) to full working pressure rating.
- Devon will test the casing to 0.22 psi/ft or 1500 psi, whichever is greater, as per Onshore Order #2.


After running the surface casing, a 13-5/8" BOP/BOPE system with a minimum rating of 5M will be installed on the wellhead system and will undergo a 250 psi low pressure test followed by a 5,000 psi high pressure test. The 5,000 psi high and 250 psi low test will cover testing requirements a maximum of 30 days, as per Onshore Order #2. If the well is not complete within 30 days of this BOP test, another full BOP test will be conducted, as per Onshore Order #2.


After running the intermediate casing with a mandrel hanger, the 13-5/8" BOP/BOPE system with a minimum rating of 5M will already be installed on the wellhead.

The pipe rams will be operated and checked each 24 hour period and each time the drill pipe is out of the hole. These tests will be logged in the daily driller's log. A 2" kill line and 3" choke line will be incorporated into the drilling spool below the ram BOP. In addition to the rams and annular preventer, additional BOP accessories include a kelly cock, floor safety valve, choke lines, and choke manifold rated at 5,000 psi WP.


Devon's proposed wellhead manufactures will be FMC Technologies, Cactus Wellhead, or Cameron.

13-5/8" 5M BOPE & Closed Loop Equipment Schematic

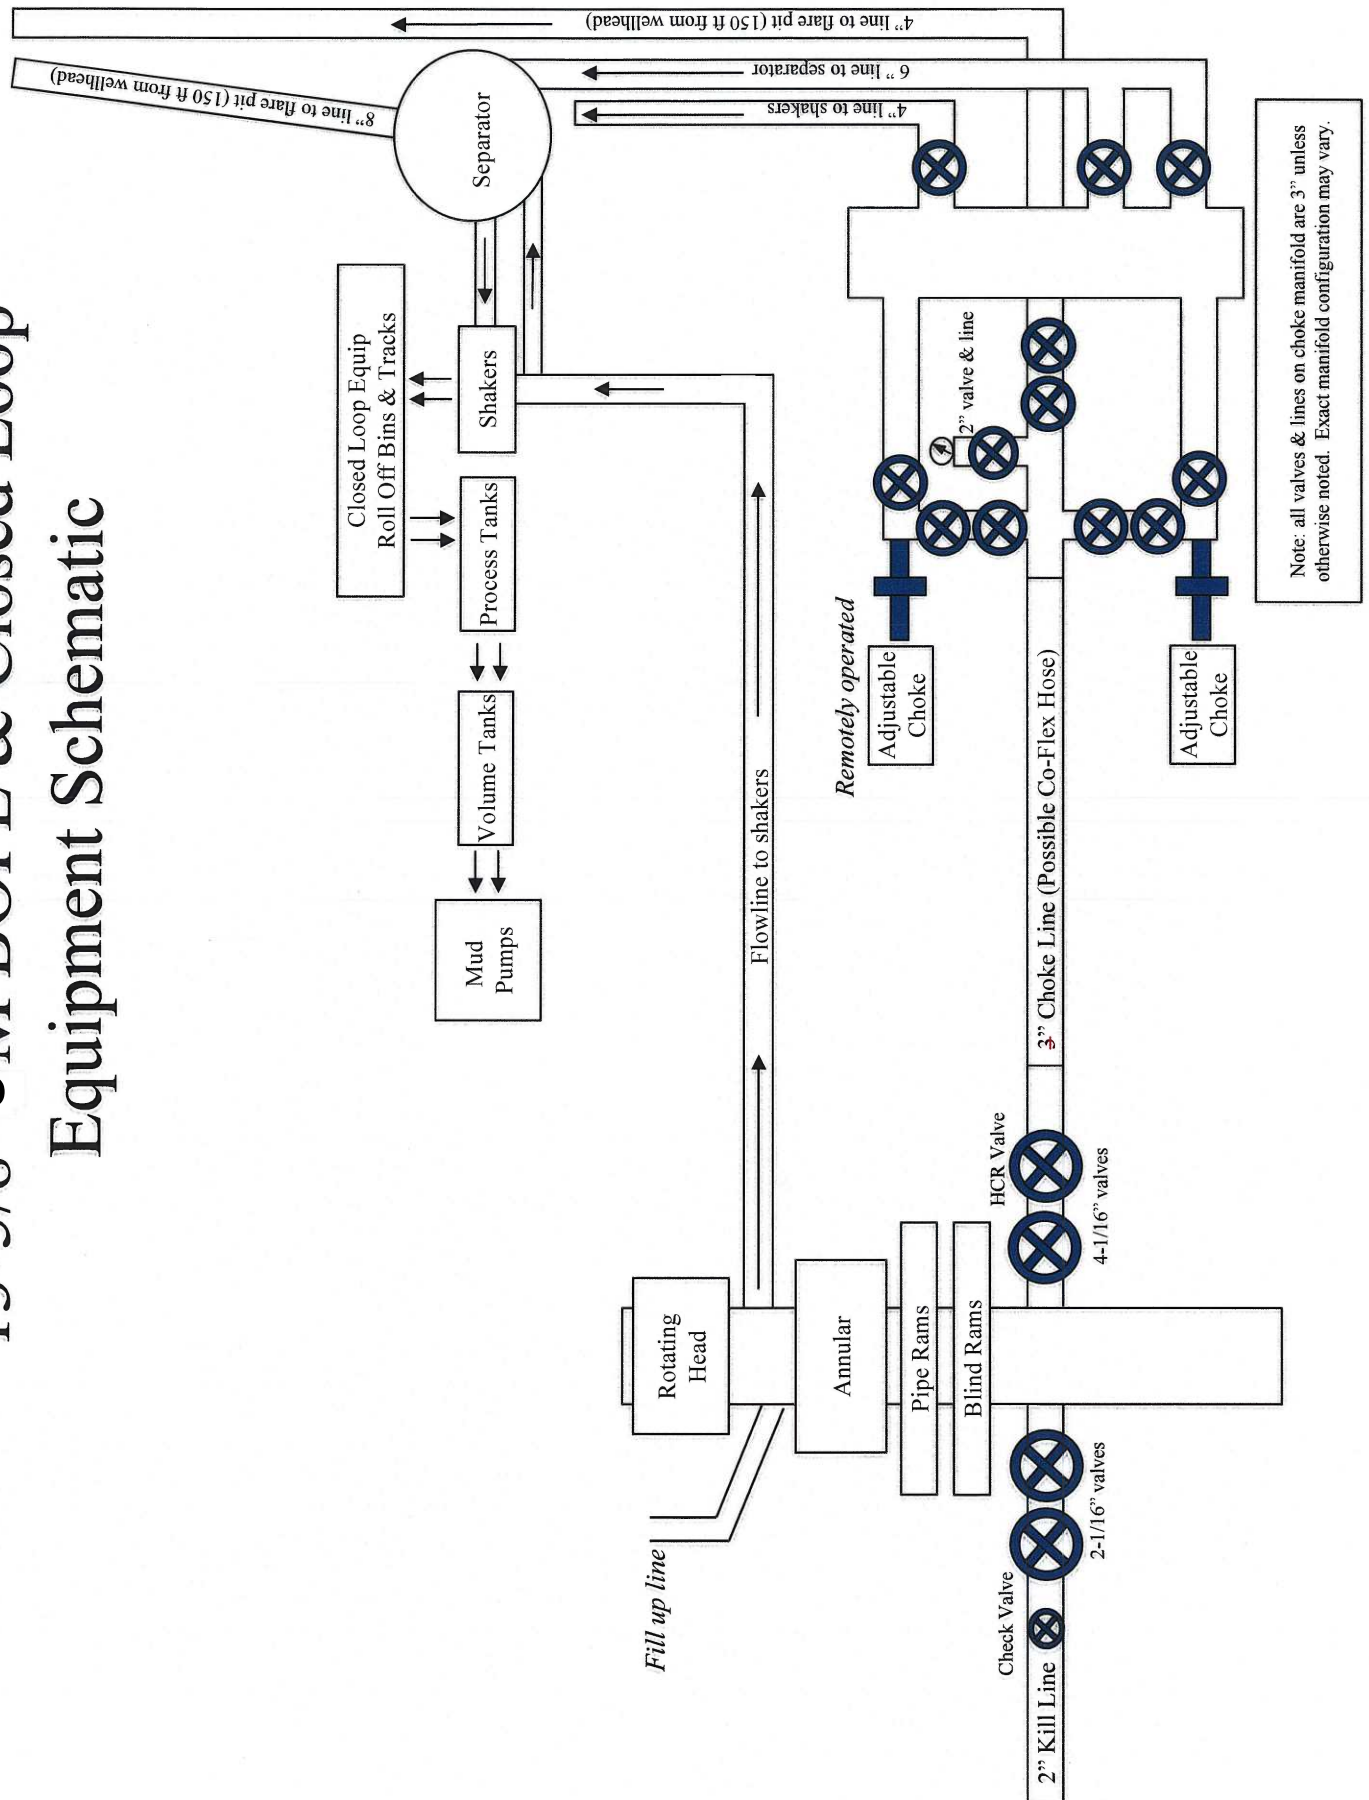

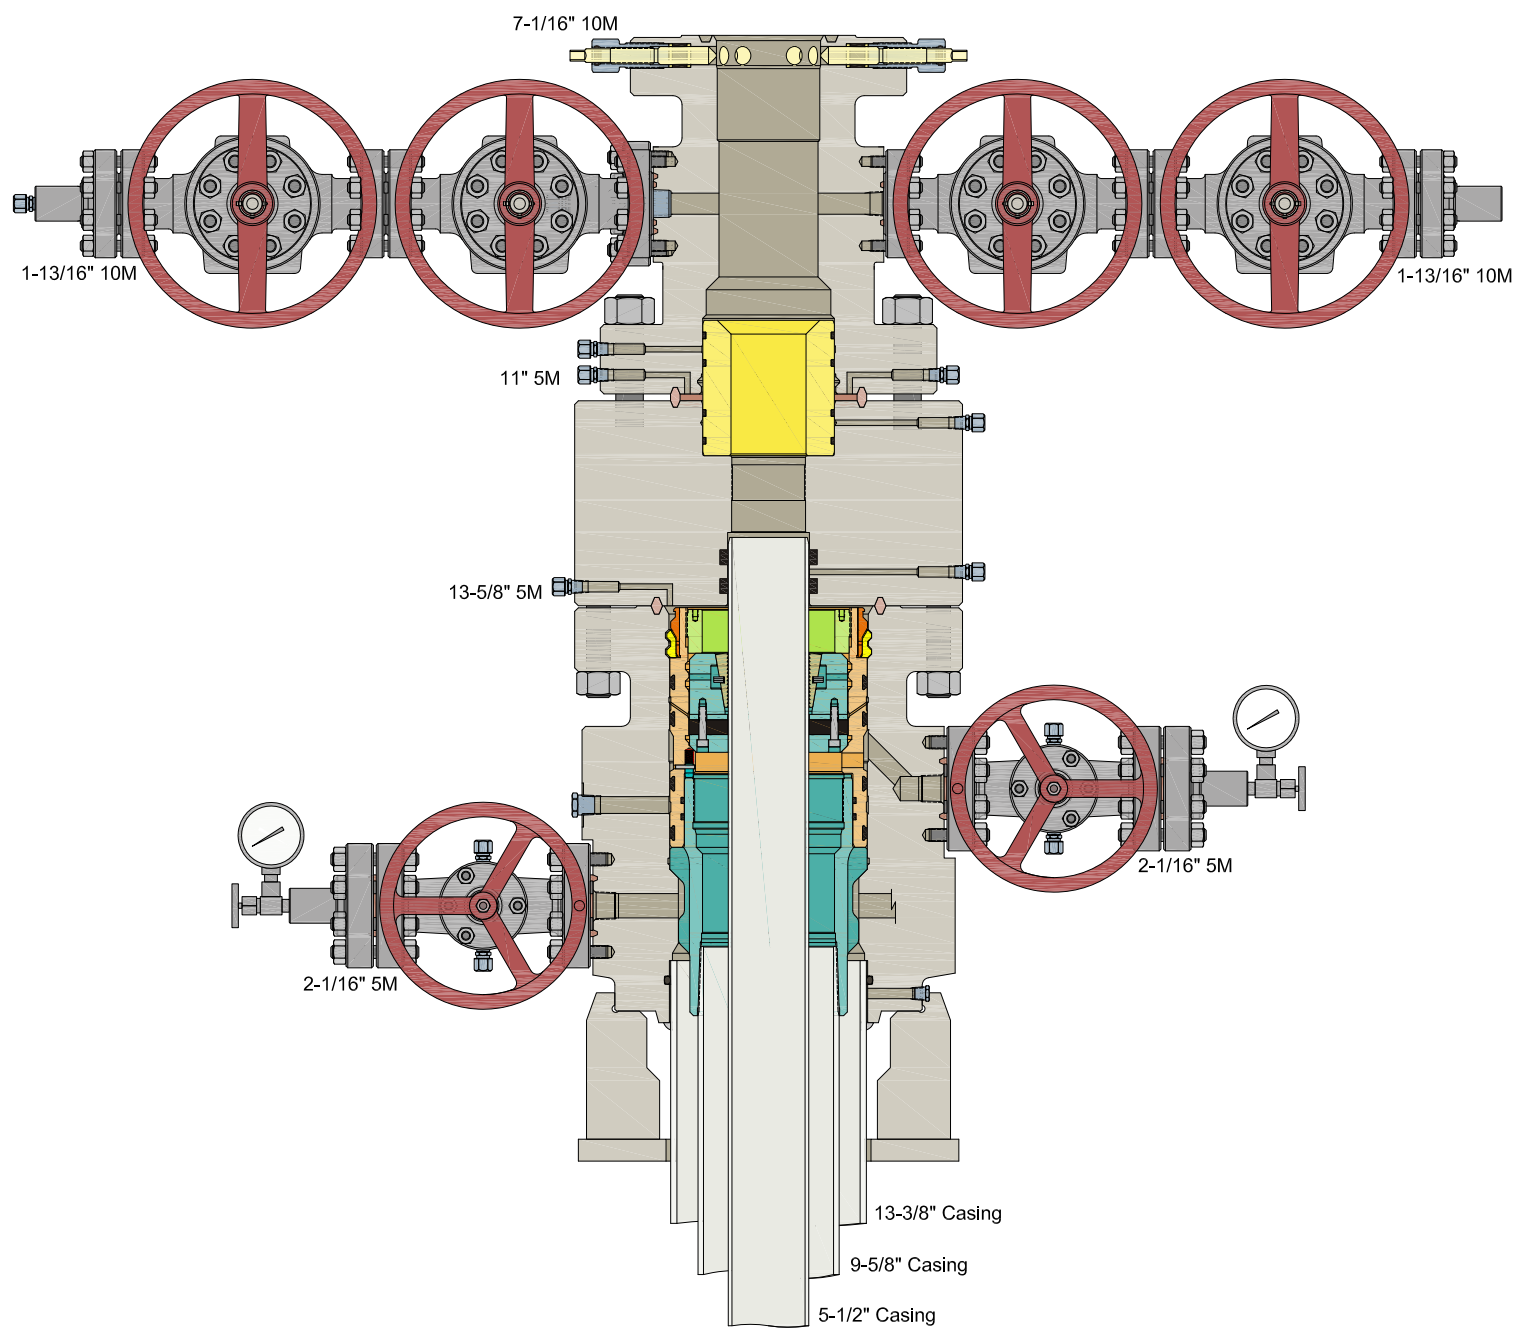

13-5/8" 5M BOPE & Closed Loop Equipment Schematic

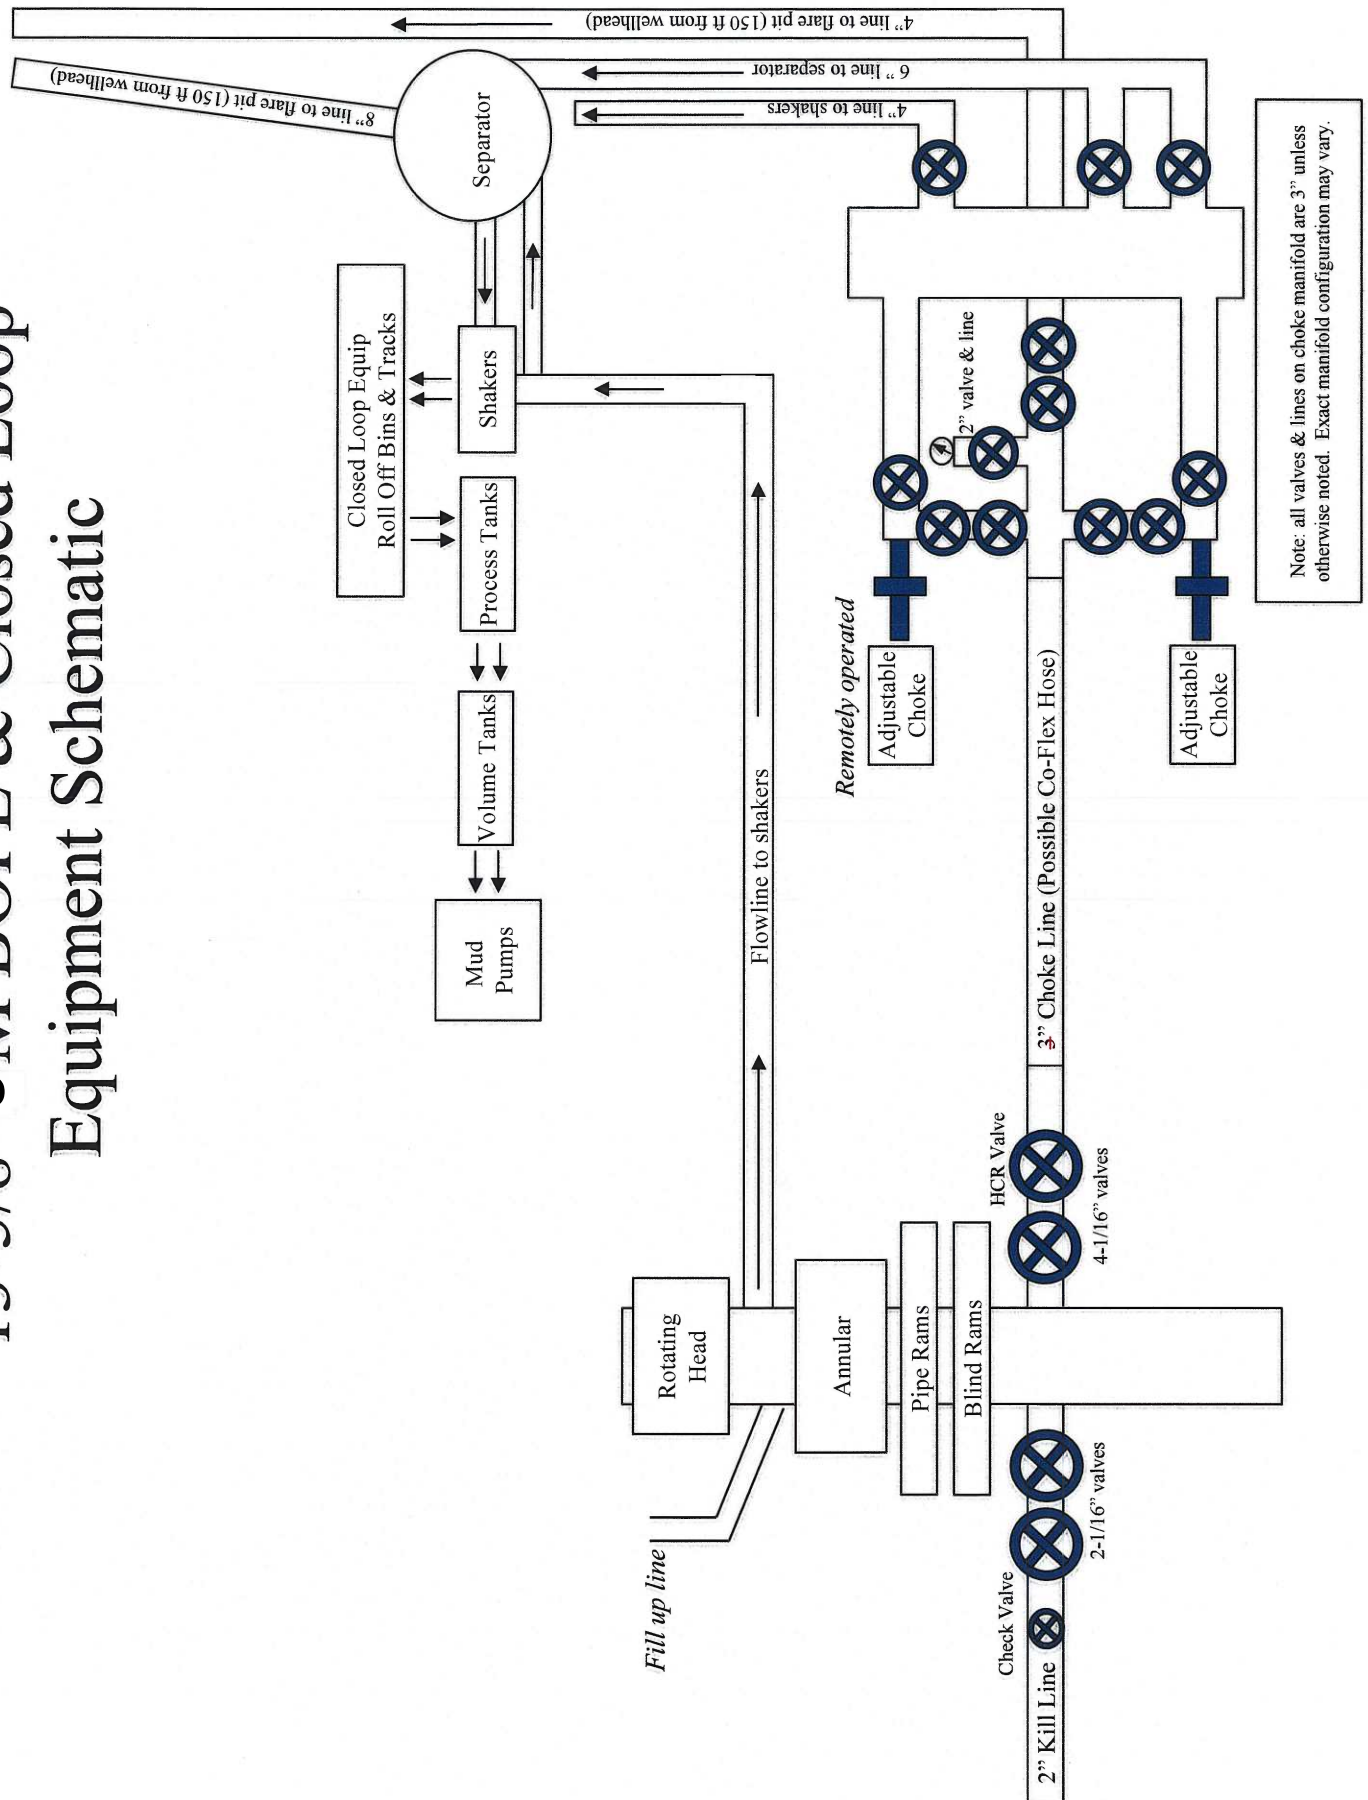

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	Devon Energy Production Company LP
LEASE NO.:	NMNM103604
LOCATION:	Section 2, T.24 S., R.29 E., NMPM
COUNTY:	Eddy County, New Mexico

WELL NAME & NO.:	Tater Tot 2-35 State Fed Com 236H
SURFACE HOLE FOOTAGE:	390'/S & 795'/E
BOTTOM HOLE FOOTAGE:	2620'/S & 440'/E
ATS/API ID:	ATS-23-838
APD ID:	10400088592
Sundry ID:	N/a

COA

H2S	No		
Potash	Secretary		
Cave/Karst Potential	Medium		
Cave/Karst Potential	☐ Critical		
Variance	☒ None	☒ Flex Hose	☒ Other
Wellhead	Conventional and Multibowl		
Other	☐ 4 String	Capitan Reef None	☐ WIPP
Other	Pilot Hole None	☐ Open Annulus	
Cementing	Contingency Squeeze Int 1	Echo-Meter None	Primary Cement Squeeze None
Special Requirements	☐ Water Disposal/Injection	☒ COM	☐ Unit
Special Requirements	☐ Batch Sundry		
Special Requirements Variance	☐ Break Testing	☐ Offline Cementing	☐ Casing Clearance

A. HYDROGEN SULFIDE

Hydrogen Sulfide (H₂S) monitors shall be installed prior to drilling out the surface shoe. If H₂S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet **43 CFR part 3170 Subpart 3176**, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.

B. CASING

1. The **13-3/8** inch surface casing shall be set at approximately **285 feet** (a minimum of **70 feet (Eddy County)** into the Rustler Anhydrite, above the salt, and below usable fresh water) and cemented to the surface. The surface hole shall be **17 1/2** inch in diameter.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **24 hours in the Potash Area** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The minimum required fill of cement behind the **9-5/8** inch intermediate casing is:

Option 1 (Single Stage):

- Cement to surface. If cement does not circulate see B.1.a, c-d above.
Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.

Option 2:

Operator has proposed a DV tool, the depth may be adjusted as long as the cement is changed proportionally. The DV tool may be cancelled if cement circulates to surface on the first stage.

- a. First stage to DV tool: Cement to circulate. If cement does not circulate off the DV tool, contact the appropriate BLM office before proceeding with second stage cement job.
- b. Second stage above DV tool:
 - Cement to surface. If cement does not circulate, contact the appropriate BLM office.
Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.

Operator has proposed to pump down 13-3/8" X 9-5/8" annulus after primary cementing stage. Operator must run a CBL from TD of the 9-5/8" casing to surface. Submit results to the BLM.

If cement does not tie-back into the previous casing shoe, a third stage remediation BH may be performed. The appropriate BLM office shall be notified.

- ❖ In Medium Cave/Karst Areas if cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface.
- ❖ In Secretary Potash Areas if cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface.

Production casing must be kept fluid filled to meet BLM minimum collapse requirement.

3. The minimum required fill of cement behind the 5-1/2 inch production casing is:
 - Cement should tie-back at least **500 feet** into previous casing string. Operator shall provide method of verification.
Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.
Cement excess is less than 25%, more cement is required if washout occurs. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.

C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'
- 2.

Option 1:

- a. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **3000 (3M)** psi.
- b. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the **9-5/8** inch intermediate casing shoe shall be **5000 (5M)** psi.

Option 2:

Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the **13-3/8** inch surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.

- a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
- b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
- c. Manufacturer representative shall install the test plug for the initial BOP test.
- d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
- e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

D. SPECIAL REQUIREMENT (S)

Communitization Agreement

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- The operator will submit an as-drilled survey well plat of the well completion, but are not limited to, those specified in **43 CFR part 3170 Subpart 3171**
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.

- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Eddy County

EMAIL or call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,

BLM_NM_CFO_DrillingNotifications@BLM.GOV

(575) 361-2822

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240,

(575) 689-5981

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - Notify the BLM when moving in and removing the Spudder Rig.
 - Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - BOP/BOPE test to be conducted per **43 CFR part 3170 Subpart 3172** as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a

digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.

8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in **43 CFR part 3170 Subpart 3172** and **API STD 53 Sec. 5.3**.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.
 - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after

installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead cement), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).

- b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the cement plug. The BOPE test can be initiated after bumping the cement plug with the casing valve open. (only applies to single stage cement jobs, prior to the cement setting up.)
- c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer and can be initiated immediately with the casing valve open. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to **43 CFR part 3170 Subpart 3172** with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
- d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- e. The results of the test shall be reported to the appropriate BLM office.
- f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per **43 CFR**

part 3170 Subpart 3172.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

LVO 9/27/2023



**Devon Energy Center
333 West Sheridan Avenue
Oklahoma City, Oklahoma 73102-5015**

Hydrogen Sulfide (H₂S) Contingency Plan

For



Tater Tot 2-35 State Fed Com 236H

**Sec-2 T-24S R-29E
390' FSL & 795' FEL
LAT. = 32.2405128' N (NAD83)
LONG = 103.9492014' W**

Eddy County NM

Tater Tot 2-35 State Fed Com 236H

This is an open drilling site. H₂S monitoring equipment and emergency response equipment will be used within 500' of zones known to contain H₂S, including warning signs, wind indicators and H₂S monitor.

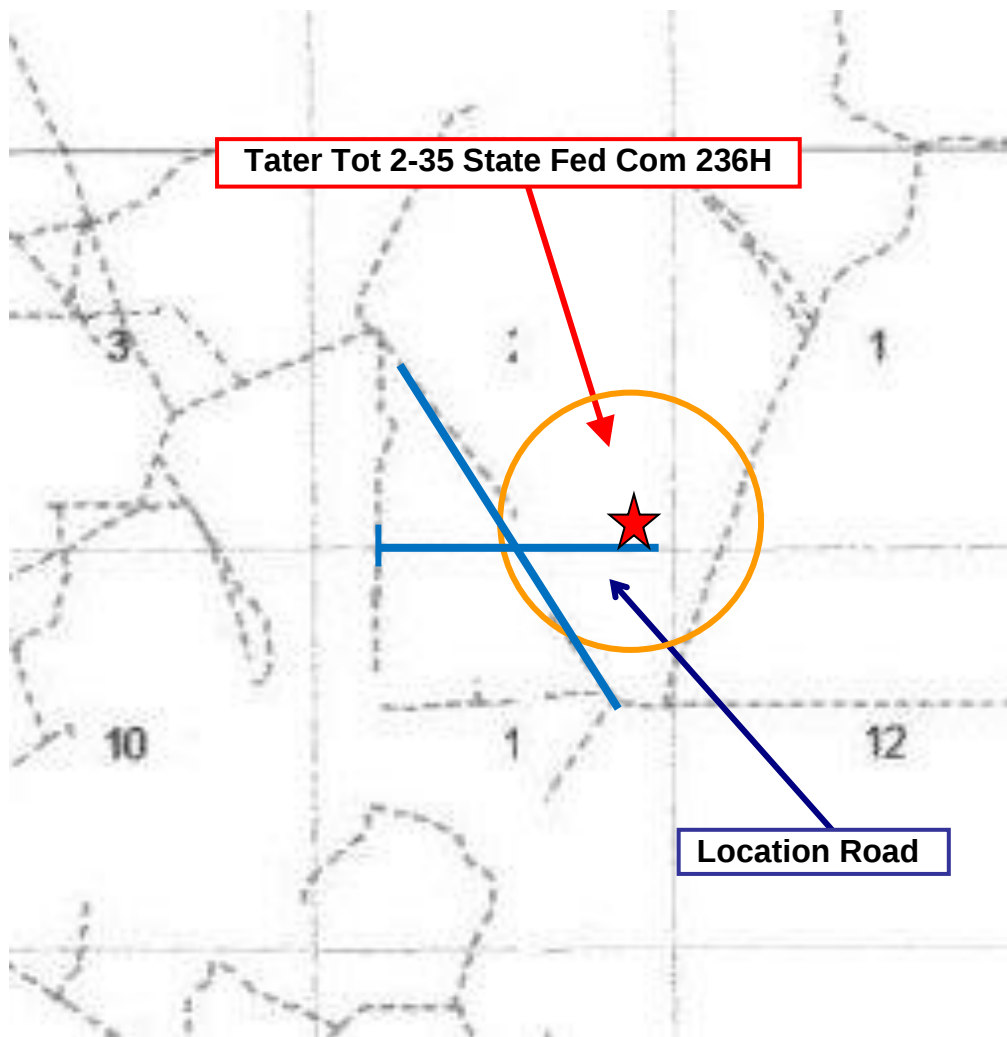

Assumed 100 ppm **ROE = 3000'** (Radius of Exposure)
100 ppm H₂S concentration shall trigger activation of this plan.

Escape

Crews shall escape upwind of escaping gas in the event of an emergency release of gas. Escape can be facilitated from the location entrance road. Crews should then block the entrance to the location from the lease road so as not to allow anyone traversing into a hazardous area. The blockade should be at a safe distance outside of the ROE. There are no homes or buildings in or near the ROE.

Assumed 100 ppm ROE = 3000'

100 ppm H₂S concentration shall trigger activation of this plan.

Emergency Procedures

In the event of a release of gas containing H₂S, the first responder(s) must

- Isolate the area and prevent entry by other persons into the 100 ppm ROE.
- Evacuate any public places encompassed by the 100 ppm ROE.
- Be equipped with H₂S monitors and air packs in order to control the release.
- Use the “buddy system” to ensure no injuries occur during the response
- Take precautions to avoid personal injury during this operation.
- Contact operator and/or local officials to aid in operation. See list of phone numbers attached.
- Have received training in the
 - Detection of H₂S, and
 - Measures for protection against the gas,
 - Equipment used for protection and emergency response.

Ignition of Gas Source

Should control of the well be considered lost and ignition considered, take care to protect against exposure to Sulfur Dioxide (SO₂). Intentional ignition must be coordinated with the NMOCD and local officials. Additionally the NM State Police may become involved. NM State Police shall be the Incident Command on scene of any major release. Take care to protect downwind whenever there is an ignition of the gas

Characteristics of H₂S and SO₂

Common Name	Chemical Formula	Specific Gravity	Threshold Limit	Hazardous Limit	Lethal Concentration
Hydrogen Sulfide	H ₂ S	1.189 Air = 1	10 ppm	100 ppm/hr	600 ppm
Sulfur Dioxide	SO ₂	2.21 Air = 1	2 ppm	N/A	1000 ppm

Contacting Authorities

Devon Energy Corp. personnel must liaison with local and state agencies to ensure a proper response to a major release. Additionally, the OCD must be notified of the release as soon as possible but no later than 4 hours. Agencies will ask for information such as type and volume of release, wind direction, location of release, etc. Be prepared with all information available. The following call list of essential and potential responders has been prepared for use during a release. Devon Energy Corp. Company response must be in coordination with the State of New Mexico's 'Hazardous Materials Emergency Response Plan' (HMER)

Hydrogen Sulfide Drilling Operation Plan

I. HYDROGEN SULFIDE (H₂S) TRAINING

All personnel, whether regularly assigned, contracted, or employed on an unscheduled basis, will receive training from a qualified instructor in the following areas prior to commencing drilling operations on this well:

1. The hazards and characteristics of hydrogen sulfide (H₂S)
2. The proper use and maintenance of personal protective equipment and life support systems.
3. The proper use of H₂S detectors, alarms, warning systems, briefing areas, evacuation procedures, and prevailing winds.
4. The proper techniques for first aid and rescue procedures.

In addition, supervisory personnel will be trained in the following areas:

1. The effects of H₂S metal components. If high tensile tubulars are to be used, personnel will be trained in their special maintenance requirements.
2. Corrective action and shut-in procedures when drilling or reworking a well and blowout prevention and well control procedures.
3. The contents and requirements of the H₂S Drilling Operations Plan and Public Protection Plan.

There will be an initial training session just prior to encountering a known or probable H₂S zone (within 3 days or 500 feet) and weekly H₂S and well control drills for all personnel in each crew. The initial training session shall include a review of the site specific H₂S Drilling Operations Plan and the Public Protection Plan.

II. HYDROGEN SULFIDE TRAINING

Note: All H₂S safety equipment and systems will be installed, tested, and operational when drilling reaches a depth of 500 feet above, or three days prior to penetrating the first zone containing or reasonably expected to contain H₂S.

1. Well Control Equipment

- A. Flare line
- B. Choke manifold – Remotely Operated
- C. Blind rams and pipe rams to accommodate all pipe sizes with properly sized closing unit
- D. Auxiliary equipment may include if applicable: annular preventer and rotating head.
- E. Mud/Gas Separator

2. Protective equipment for essential personnel:

30-minute SCBA units located at briefing areas, as indicated on well site diagram, with escape units available in the top doghouse. As it may be difficult to communicate audibly while wearing these units, hand signals shall be utilized.

3. H₂S detection and monitoring equipment:

Portable H₂S monitors positioned on location for best coverage and response. These units have warning lights which activate when H₂S levels reach 10 ppm and audible sirens which activate at 15 ppm. Sensor locations:

- Bell nipple
- Possum Belly/Shale shaker
- Rig floor
- Choke manifold
- Cellar

Visual warning systems:

- A. Wind direction indicators as shown on well site diagram
- B. Caution/ Danger signs shall be posted on roads providing direct access to locations. Signs will be painted a high visibility yellow with black lettering of sufficient size to be reasonable distance from the immediate location. Bilingual signs will be used when appropriate.

4. Mud program:

The mud program has been designed to minimize the volume of H₂S circulated to surface. Proper mud weight, safe drilling practices and the use of H₂S scavengers will minimize hazards when penetrating H₂S bearing zones.

5. Metallurgy:

- A. All drill strings, casings, tubing, wellhead, blowout preventer, drilling spool, kill lines, choke manifold lines, and valves shall be H₂S trim.
- B. All elastomers used for packing and seals shall be H₂S trim.

6. Communication:

- A. Company personnel have/use cellular telephones in the field.
- B. Land line (telephone) communications at Office

7. Well testing:



- A. Drill stem testing will be performed with a minimum number of personnel in the immediate vicinity, which are necessary to safety and adequately conduct the test. The drill stem testing will be conducted during daylight hours and formation fluids will not be flowed to the surface. All drill-stem-testing operations conducted in an H₂S environment will use the closed chamber method of testing.
- B. There will be no drill stem testing.

<u>Devon Energy Corp. Company Call List</u>		
Drilling Supervisor – Basin – Mark Kramer		405-823-4796
EHS Professional – Laura Wright		405-439-8129
<u>Agency Call List</u>		
<u>Lea County (575)</u>	Hobbs	
	Lea County Communication Authority	393-3981
	State Police	392-5588
	City Police	397-9265
	Sheriff's Office	393-2515
	Ambulance	911
	Fire Department	397-9308
	LEPC (Local Emergency Planning Committee)	393-2870
	NMOCD	393-6161
	US Bureau of Land Management	393-3612
<u>Eddy County (575)</u>	Carlsbad	
	State Police	885-3137
	City Police	885-2111
	Sheriff's Office	887-7551
	Ambulance	911
	Fire Department	885-3125
	LEPC (Local Emergency Planning Committee)	887-3798
	US Bureau of Land Management	887-6544
	NM Emergency Response Commission (Santa Fe)	(505) 476-9600
	24 HR	(505) 827-9126
	National Emergency Response Center	(800) 424-8802
	National Pollution Control Center: Direct	(703) 872-6000
	For Oil Spills	(800) 280-7118
	Emergency Services	
	Wild Well Control	(281) 784-4700
	Cudd Pressure Control	(915) 699-0139 (915) 563-3356
	Halliburton	(575) 746-2757
	B. J. Services	(575) 746-3569
<u>Give GPS position:</u>	Native Air – Emergency Helicopter – Hobbs (TX & NM)	(800) 642-7828
	Flight For Life - Lubbock, TX	(806) 743-9911
	Aerocare - Lubbock, TX	(806) 747-8923
	Med Flight Air Amb - Albuquerque, NM	(575) 842-4433
	Lifeguard Air Med Svc. Albuquerque, NM	(800) 222-1222
	Poison Control (24/7)	(575) 272-3115
	Oil & Gas Pipeline 24 Hour Service	(800) 364-4366
	NOAA – Website - www.nhc.noaa.gov	

Prepared in conjunction with
Dave Small



Devon Energy - Well Pad Rig Location Layout Safety Equipment Location

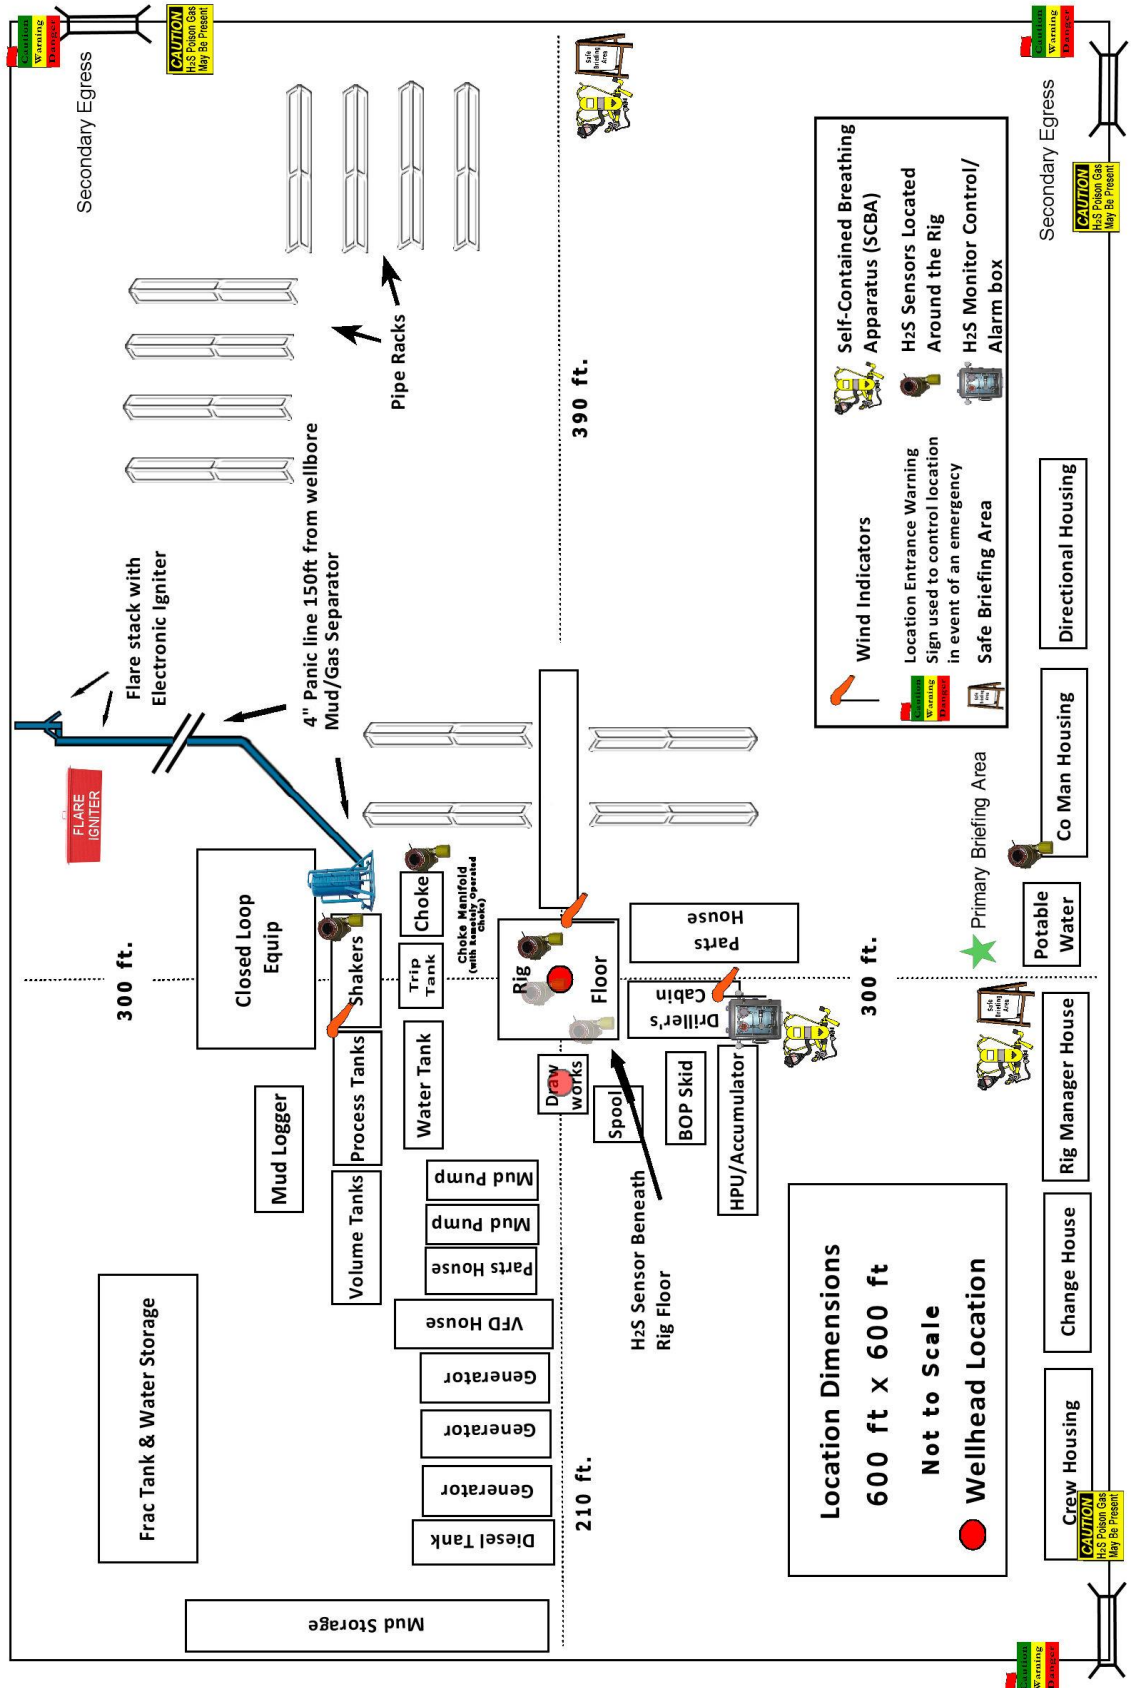

District I

1625 N. French Dr., Hobbs, NM 88240
 Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
 Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
 Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
 Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 277301

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 277301
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

CONDITIONS

Created By	Condition	Condition Date
ward.rikala	Notify OCD 24 hours prior to casing & cement	11/1/2023
ward.rikala	Will require a File As Drilled C-102 and a Directional Survey with the C-104	11/1/2023
ward.rikala	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string	11/1/2023
ward.rikala	Cement is required to circulate on both surface and intermediate1 strings of casing	11/1/2023
ward.rikala	If cement does not circulate on any string, a CBL is required for that string of casing	11/1/2023
ward.rikala	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system	11/1/2023
