

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

| | | |
|---|--|---|
| 1a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER 1b. Type of Well: <input type="checkbox"/> Oil Well <input checked="" type="checkbox"/> Gas Well <input type="checkbox"/> Other 1c. Type of Completion: <input type="checkbox"/> Hydraulic Fracturing <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone | | 5. Lease Serial No. NMNM15433 6. If Indian, Allottee or Tribe Name 7. If Unit or CA Agreement, Name and No. 8. Lease Name and Well No. CB AMILYN 10 3 FED COM P13 401H |
| 2. Name of Operator CHEVRON USA INCORPORATED | | 9. API Well No. 30-015-54556 |
| 3a. Address P O BOX 1635, HOUSTON, TX 77251 | 3b. Phone No. (include area code) (661) 654-7256 | 10. Field and Pool, or Exploratory PURPLE SAGE/(WOLFCAMP) GAS |
| 4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface NENW / 418 FNL / 1589 FWL / LAT 32.311543 / LONG -104.078774 At proposed prod. zone LOT 4 / 25 FNL / 330 FWL / LAT 32.341844 / LONG -104.082804 | | 11. Sec., T. R. M. or Blk. and Survey or Area SEC 15/T23S/R28E/NMP |
| 14. Distance in miles and direction from nearest town or post office* 2.1 miles | | 12. County or Parish EDDY |
| 15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 418 feet | 16. No of acres in lease | 17. Spacing Unit dedicated to this well 640.0 |
| 18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. 500 feet | 19. Proposed Depth 9562 feet / 20325 feet | 20. BLM/BIA Bond No. in file FED: |
| 21. Elevations (Show whether DF, KDB, RT, GL, etc.) 3000 feet | 22. Approximate date work will start* 11/23/2022 | 23. Estimated duration 147 days |
| 24. Attachments | | |

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|---|---|
| 1. Well plat certified by a registered surveyor. 2. A Drilling Plan. 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). 5. Operator certification. 6. Such other site specific information and/or plans as may be requested by the BLM. |
|---|---|

| | | |
|--|---|---------------------------|
| 25. Signature (Electronic Submission) | Name (Printed/Typed) CAROL ADLER / Ph: (432) 687-7866 | Date 07/06/2022 |
| Title Sr Regulatory Affairs Coordinator | | |
| Approved by (Signature) (Electronic Submission) | Name (Printed/Typed) CODY LAYTON / Ph: (575) 234-5959 | Date 11/28/2023 |
| Title Assistant Field Manager Lands & Minerals | | |
| Office Carlsbad Field Office | | |

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
 Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)



District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720

District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720

District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170

District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

| | | |
|--|--|---|
| ¹ API Number 30-015-54556 | ² Pool Code 98220 | ³ Pool Name PURPLE SAGE; WOLFCAMP (GAS) |
| ⁴ Property Code 335081 | ⁵ Property Name CB AMILYN 10 3 FED COM P13 | ⁶ Well Number 401H |
| ⁷ OGRID No. 4323 | ⁸ Operator Name CHEVRON U.S.A. INC. | ⁹ Elevation 3000' |

¹⁰ Surface Location

| UL or lot no. | Section | Township | Range | Lot Idn | Feet from the | North/South line | Feet from the | East/West line | County |
|---------------|---------|----------|-------------------|---------|---------------|------------------|---------------|----------------|--------|
| C | 15 | 23 SOUTH | 28 EAST, N.M.P.M. | | 418' | NORTH | 1589' | WEST | EDDY |

¹¹ Bottom Hole Location If Different From Surface

| UL or lot no. | Section | Township | Range | Lot Idn | Feet from the | North/South line | Feet from the | East/West line | County |
|---------------|---------|----------|-------------------|---------|---------------|------------------|---------------|----------------|--------|
| D | 3 | 23 SOUTH | 28 EAST, N.M.P.M. | | 25' | NORTH | 330' | WEST | EDDY |

| | | | |
|--------------------------------------|---|----------------------------------|-------------------------|
| ¹² Dedicated Acres 640 | ¹³ Joint or Infill INFILL | ¹⁴ Consolidation Code | ¹⁵ Order No. |
|--------------------------------------|---|----------------------------------|-------------------------|

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

| | | | | | | | | | | | | | | | | | | | | | | | | |
|---|---------------------------|---------------------------|---|---------------------------|---|---------------------------|---|---------------------------|---|---------------------------|---|---------------------------|---|---------------------------|---|---------------------------|---|---------------------------|---|---------------------------|---|---------------------------|--|---|
| <p>¹⁶</p> <p>PROPOSED LAST TAKE POINT X = 577,525' (NAD27 NM E) Y = 487,821' LAT. 32.340885° N (NAD27) LONG. 104.082317° W X = 618,707' (NAD83/86 NM E) Y = 487,880' LAT. 32.341006° N (NAD83/86) LONG. 104.082814° W</p> <p>PROPOSED MID POINT X = 577,487' (NAD27 NM E) Y = 482,777' LAT. 32.327020° N (NAD27) LONG. 104.082477° W X = 618,669' (NAD83/86 NM E) Y = 482,836' LAT. 32.327141° N (NAD83/86) LONG. 104.082974° W</p> <p>PROPOSED FIRST TAKE POINT X = 577,533' (NAD27 NM E) Y = 477,832' LAT. 32.313428° N (NAD27) LONG. 104.082366° W X = 618,715' (NAD83/86 NM E) Y = 477,892' LAT. 32.313549° N (NAD83/86) LONG. 104.082862° W</p> <p>PROPOSED BOTTOM HOLE LOCATION X = 577,527' (NAD27 NM E) Y = 488,126' LAT. 32.341724° N (NAD27) LONG. 104.082307° W X = 618,709' (NAD83/86 NM E) Y = 488,185' LAT. 32.341844° N (NAD83/86) LONG. 104.082804° W</p> <p>CORNER COORDINATES TABLE (NAD 27)</p> <table border="1"> <tr><td>A</td><td>-Y=488148.82, X=577197.00</td></tr> <tr><td>B</td><td>-Y=488156.72, X=578536.87</td></tr> <tr><td>C</td><td>-Y=488164.62, X=579876.75</td></tr> <tr><td>D</td><td>-Y=482771.59, X=577156.91</td></tr> <tr><td>E</td><td>-Y=482792.65, X=578487.26</td></tr> <tr><td>F</td><td>-Y=482813.72, X=579817.60</td></tr> <tr><td>G</td><td>-Y=477496.90, X=577205.98</td></tr> <tr><td>H</td><td>-Y=477519.13, X=578540.48</td></tr> <tr><td>I</td><td>-Y=477541.37, X=579874.98</td></tr> <tr><td>J</td><td>-Y=476168.14, X=577212.69</td></tr> <tr><td>K</td><td>-Y=476212.10, X=579878.70</td></tr> </table> <p>CB AMILYN 10 3 FED COM P13 401H WELL X = 578,797' (NAD27 NM E) Y = 477,106' LAT. 32.311422° N (NAD27) LONG. 104.078279° W X = 619,980' (NAD83/86 NM E) Y = 477,165' LAT. 32.311543° N (NAD83/86) LONG. 104.078774° W ELEV. +3000' (NAVD88)</p> | A | -Y=488148.82, X=577197.00 | B | -Y=488156.72, X=578536.87 | C | -Y=488164.62, X=579876.75 | D | -Y=482771.59, X=577156.91 | E | -Y=482792.65, X=578487.26 | F | -Y=482813.72, X=579817.60 | G | -Y=477496.90, X=577205.98 | H | -Y=477519.13, X=578540.48 | I | -Y=477541.37, X=579874.98 | J | -Y=476168.14, X=577212.69 | K | -Y=476212.10, X=579878.70 | | <p>¹⁷ OPERATOR CERTIFICATION I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.</p> <p><i>Carol Adler</i> 06/01/2022 Signature Date</p> <p>Carol Adler Printed Name</p> <p>caroladler@chevron.com E-mail Address</p> <p>¹⁸ SURVEYOR CERTIFICATION I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.</p> <p>Date of Survey Signature and Seal of Professional Surveyor: 23006 03/24/2022</p> <p><i>Robert L. Lastrapes</i> Certificate Number</p> |
| A | -Y=488148.82, X=577197.00 | | | | | | | | | | | | | | | | | | | | | | | |
| B | -Y=488156.72, X=578536.87 | | | | | | | | | | | | | | | | | | | | | | | |
| C | -Y=488164.62, X=579876.75 | | | | | | | | | | | | | | | | | | | | | | | |
| D | -Y=482771.59, X=577156.91 | | | | | | | | | | | | | | | | | | | | | | | |
| E | -Y=482792.65, X=578487.26 | | | | | | | | | | | | | | | | | | | | | | | |
| F | -Y=482813.72, X=579817.60 | | | | | | | | | | | | | | | | | | | | | | | |
| G | -Y=477496.90, X=577205.98 | | | | | | | | | | | | | | | | | | | | | | | |
| H | -Y=477519.13, X=578540.48 | | | | | | | | | | | | | | | | | | | | | | | |
| I | -Y=477541.37, X=579874.98 | | | | | | | | | | | | | | | | | | | | | | | |
| J | -Y=476168.14, X=577212.69 | | | | | | | | | | | | | | | | | | | | | | | |
| K | -Y=476212.10, X=579878.70 | | | | | | | | | | | | | | | | | | | | | | | |

State of New Mexico
Energy, Minerals and Natural Resources Department

Submit Electronically
Via E-permitting

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description

Effective May 25, 2021

I. Operator: Chevron USA **OGRID:** 4323 **Date:** 03 / 21 / 22

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

| Well Name | API | ULSTR | Footages | Anticipated Oil BBL/D | Anticipated Gas MCF/D | Anticipated Produced Water BBL/D |
|---------------------------------|----------------|-------------------------|---------------------|-----------------------|-----------------------|----------------------------------|
| CB AMILYN 10 3 FED COM P13 401H | <i>Pending</i> | UL:C, Sec 15, T23S-R28E | 418' FNL, 1589' FWL | 1314 BBL/D | 2831 MCF/D | 4478 BBL/D |
| CB AMILYN 10 3 FED COM P13 402H | <i>Pending</i> | UL:C, Sec 15, T23S-R28E | 418' FNL, 1614' FWL | 1314 BBL/D | 2831 MCF/D | 4478 BBL/D |
| CB AMILYN 10 3 FED COM P13 403H | <i>Pending</i> | UL:C, Sec 15, T23S-R28E | 418' FNL, 1639' FWL | 1314 BBL/D | 2831 MCF/D | 4478 BBL/D |

IV. Central Delivery Point Name: Culebra Bluff CTB Sec.15 [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

| Well Name | API | Spud Date | TD Reached Date | Completion Commencement Date | Initial Flow Back Date | First Production Date |
|---------------------------------|----------------|--------------|-----------------|------------------------------|------------------------|-----------------------|
| CB AMILYN 10 3 FED COM P13 401H | <i>Pending</i> | October 2023 | N/A | N/A | N/A | N/A |
| CB AMILYN 10 3 FED COM P13 402H | <i>Pending</i> | October 2023 | N/A | N/A | N/A | N/A |
| CB AMILYN 10 3 FED COM P13 403H | <i>Pending</i> | October 2023 | N/A | N/A | N/A | N/A |

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 2 – Enhanced Plan

EFFECTIVE APRIL 1, 2022

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☐ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

| Well | API | Anticipated Average Natural Gas Rate MCF/D | Anticipated Volume of Natural Gas for the First Year MCF |
|------|-----|--|--|
| | | | |
| | | | |

X. Natural Gas Gathering System (NGGS):

| Operator | System | ULSTR of Tie-in | Anticipated Gathering Start Date | Available Maximum Daily Capacity of System Segment Tie-in |
|----------|--------|-----------------|----------------------------------|---|
| | | | | |
| | | | | |

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

| |
|--|
| Signature: <i>Carol Adler</i> |
| Printed Name: Carol Adler |
| Title: Sr. Regulatory Affairs Coordinator |
| E-mail Address: caroladler@chevron.com |
| Date: 3/23/2022 |
| Phone: (432) 687-7148 |
| OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form) |
| Approved By: |
| Title: |
| Approval Date: |
| Conditions of Approval: |

Operator Name: CHEVRON USA INCORPORATED**Well Name:** CB AMILYN 10 3 FED COM P13**Well Number:** 401H

psi low / 5,000 psi high for 10 min each test against the connection that was broken when skidding the rig. Upon the first nipple up of the pad a full BOP test will be performed. A full BOP test will be completed prior to drilling the production lateral sections unless the BOP connection was not broken prior to drilling that hole section (example: drilling straight from production into production liner hole section). A break test will only be performed on operations where BLM documentation states a 5M or less BOP can be utilized. Chevron requests a variance to use a FMC Technologies UH-S Multibowl wellhead, which will be run through the rig floor on surface casing. BOPE will be nipped up and tested after cementing surface casing. Subsequent tests will be performed as needed, not to exceed 30 days. The field report from FMC Technologies and BOP test information will be provided in a subsequent report at the end of the well. Please see the attached wellhead schematic. An installation manual has been placed on file with the BLM office and remains unchanged from previous submittal. All tests performed by third party. Chevron requests to use high pressure flex hoses for all wells on the pad. Spec sheets attached to APD.

Testing Procedure: The stack will be tested as specified in the attached testing requirements. Batch drilling of the surface, production, and production liner will take place. Chevron proposes a digital BOP test method in lieu of the standard test chart. BOP test pressures and other documented tests will be recorded and documented via utilization of IPT SureTec Digital BOP Testing equipment and software. In the event the IPT system is unavailable, the standard test chart will be used. Test Test Time Test Pressure Criteria Additional Criteria Low Pressure Test 10 min 3 psi/min decline No visible leaks. Pressure shall not decrease below the intended test pressure. High Pressure Test 10 min 10 psi/min decline No visible leaks. Pressure shall not decrease below the intended test pressure. Pressure transducers are calibrated to the manufacturers specification. Each testing report will show information on the transducers including manufacturer, model, serial, and calibration date. IPT SureTec software will be used by knowledgeable personnel for BOP pressure testing. The software will be operated per IPT requirements and will not be used beyond the explicitly intended purpose.

Choke Diagram Attachment:

5K_BOPE_Choke_Schematic_Testing_Procedures_20220705104351.pdf

BLM_5M_Choke_Manifold_Diagram_20220705104810.pdf

BOP Diagram Attachment:

NM_Slim_Hole_Wellhead_6650_psi_UH_S_20220705104635.pdf

BLM_5M_Annular_10M_Rams_Stackup_and_Test_Plan_20220705104836.pdf

Section 3 - Casing

| Casing ID | String Type | Hole Size | Csg Size | Condition | Standard | Tapered String | Top Set MD | Bottom Set MD | Top Set TVD | Bottom Set TVD | Top Set MSL | Bottom Set MSL | Calculated casing length MD | Grade | Weight | Joint Type | Collapse SF | Burst SF | Joint SF Type | Joint SF | Body SF Type | Body SF |
|-----------|--------------|-----------|----------|-----------|----------|----------------|------------|---------------|-------------|----------------|-------------|----------------|-----------------------------|-------|--------|--------------|-------------|----------|---------------|----------|--------------|---------|
| 1 | SURFACE | 17.5 | 13.375 | NEW | API | N | 0 | 300 | 0 | 300 | 3000 | 2700 | 300 | J-55 | 54.5 | BUTT | 2.13 | 1.43 | BUOY | 2.09 | BUOY | 3.46 |
| 2 | INTERMEDIATE | 12.25 | 9.625 | NEW | API | N | 0 | 2604 | 0 | 2555 | 3000 | 445 | 2604 | L-80 | 40 | BUTT | 1.24 | 1.64 | BUOY | 3.16 | BUOY | 3.26 |
| 3 | INTERMEDIATE | 8.75 | 7.0 | NEW | API | N | 0 | 9033 | 0 | 8883 | 3000 | -5883 | 9033 | P-110 | 29 | OTHER - BLUE | 1.63 | 1.15 | BUOY | 2.3 | BUOY | 2.3 |
| 4 | PRODUCTION | 6.125 | 5.0 | NEW | API | N | 8733 | 9633 | 8483 | 9433 | -5483 | -6433 | 900 | P-110 | 18 | OTHER - W513 | 1.39 | 1.1 | BUOY | 1.63 | BUOY | 2.54 |

Operator Name: CHEVRON USA INCORPORATED

Well Name: CB AMILYN 10 3 FED COM P13

Well Number: 401H

| Casing ID | String Type | Hole Size | Csg Size | Condition | Standard | Tapered String | Top Set MD | Bottom Set MD | Top Set TVD | Bottom Set TVD | Top Set MSL | Bottom Set MSL | Calculated casing length MD | Grade | Weight | Joint Type | Collapse SF | Burst SF | Joint SF Type | Joint SF | Body SF Type | Body SF |
|-----------|-------------|-----------|----------|-----------|----------|----------------|------------|---------------|-------------|----------------|-------------|----------------|-----------------------------|-------|--------|--------------|-------------|----------|---------------|----------|--------------|---------|
| 5 | PRODUCTION | 6.125 | 4.5 | NEW | API | N | 9633 | 20325 | 9433 | 9562 | -6433 | -6562 | 10692 | P-110 | 11.6 | OTHER - W521 | 1.39 | 1.1 | BUOY | 1.63 | BUOY | 2.54 |

Casing Attachments

Casing ID: 1StringSURFACE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

13.375_casing_spec_sheet_20220705174824.pdf

Casing ID: 2StringINTERMEDIATE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

9.625_40.0lb_L80IC_BTC_20220705174926.pdf

Operator Name: CHEVRON USA INCORPORATED

Well Name: CB AMILYN 10 3 FED COM P13

Well Number: 401H

Casing Attachments

Casing ID: 3StringINTERMEDIATE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

7in_Blue_vs_BlueSD_20220705174800.pdf

Casing ID: 4StringPRODUCTION

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

5in_Tenaris_Collapse_13470_20220705175101.pdf

Casing ID: 5StringPRODUCTION

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

4.5_W521_Spec_Sheet_20220705175007.pdf

Section 4 - Cement

Operator Name: CHEVRON USA INCORPORATED**Well Name:** CB AMILYN 10 3 FED COM P13**Well Number:** 401H

| String Type | Lead/Tail | Stage Tool Depth | Top MD | Bottom MD | Quantity(sx) | Yield | Density | Cu Ft | Excess% | Cement type | Additives |
|--------------|-----------|------------------|--------|-----------|--------------|-------|---------|-------|---------|-------------|---|
| SURFACE | Lead | | 0 | 0 | 0 | 0 | 0 | 0 | 0 | NONE | NONE |
| SURFACE | Tail | | 0 | 300 | 196 | 1.33 | 14.8 | 261 | 25 | CLASS C | EXTENDER, ANTIFOAM, RETARDER, VISCOSIFER |
| INTERMEDIATE | Lead | | 0 | 1604 | 252 | 2.49 | 11.5 | 628 | 25 | CLASS C | EXTENDER, ANTIFOAM, RETARDER, VISCOSIFER |
| INTERMEDIATE | Tail | | 1604 | 2604 | 323 | 1.33 | 13.6 | 429 | 25 | CLASS C | EXTENDER, ANTIFOAM, RETARDER, VISCOSIFER |
| INTERMEDIATE | Lead | | 0 | 8033 | 651 | 2.2 | 11.5 | 1433 | 25 | CLASS C | EXTENDER, ANTIFOAM, RETARDER, VISCOSIFER |
| INTERMEDIATE | Tail | | 8033 | 9033 | 134 | 1.4 | 14.5 | 188 | 25 | CLASS C | EXTENDER, ANTIFOAM, RETARDER, VISCOSIFER |
| PRODUCTION | Lead | | 8833 | 2023 5 | 825 | 1.64 | 13.2 | 1353 | 25 | CLASS H | EXTENDER, ANTIFOAM, RETARDER, VISCOSIFER |

| | | | | | | | | | | | |
|------------|------|--|------|-----------|-----|------|------|------|----|---------|---|
| PRODUCTION | Lead | | 8833 | 2032 5 | 825 | 1.64 | 13.2 | 1353 | 25 | CLASS H | EXTENDER, ANTIFOAM, RETARDER, VISCOSIFER |
|------------|------|--|------|-----------|-----|------|------|------|----|---------|---|

Operator Name: CHEVRON USA INCORPORATED**Well Name:** CB AMILYN 10 3 FED COM P13**Well Number:** 401H**Section 5 - Circulating Medium****Mud System Type:** Closed**Will an air or gas system be Used?** NO**Description of the equipment for the circulating system in accordance with Onshore Order #2:****Diagram of the equipment for the circulating system in accordance with Onshore Order #2:**

Describe what will be on location to control well or mitigate other conditions: A weighting agent and lost circulating material (LCM) will be onsite to mitigate pressure or lost circulation as hole conditions dictate. Type If an open reserve pit is not approved by OCD, a closed system will be used consisting of above ground steel tanks and all wastes accumulated during drilling operations will be contained in a portable trash cage and removed from location and deposited in an approved sanitary landfill. If an open reserve pit is in place, pit construction, operation, and closure will follow all applicable rules and regulation. Sanitary wastes will be contained in a chemical porta-toilet and then hauled to an approved sanitary landfill. All fluids and cuttings will be disposed of in accordance with New Mexico Oil Conservation Division rules and regulations. And transporting of E&P waste will follow EPA regulations and accompanying manifests.

Describe the mud monitoring system utilized: A mud test shall be performed every 24 hours after mudding up to determine, as applicable: density, viscosity, gel strength, filtration, and pH. Visual mud monitoring equipment shall be in place to detect volume changes indicating loss or gain of circulating fluid volume. When abnormal pressures are anticipated -- a pit volume totalizer (PVT), stroke counter, and flow sensor will be used to detect volume changes indicating loss or gain of circulating fluid volume.

Circulating Medium Table

| Top Depth | Bottom Depth | Mud Type | Min Weight (lbs/gal) | Max Weight (lbs/gal) | Density (lbs/cu ft) | Gel Strength (lbs/100 sqft) | PH | Viscosity (CP) | Salinity (ppm) | Filtration (cc) | Additional Characteristics |
|-----------|--------------|-------------------|----------------------|----------------------|---------------------|-----------------------------|----|----------------|----------------|-----------------|--|
| 0 | 300 | SPUD MUD | 8.9 | 9.1 | | | | | | | FILTRATE: 15-25 |
| 300 | 2604 | SALT SATURATED | 8.9 | 10.5 | | | | | | | Saturated brine would be used through salt sections. FILTRATE: 15-25 |
| 2604 | 9033 | OTHER : WBM/BRINE | 8.7 | 9.6 | | | | | | | FILTRATE: 15-25 |
| 9033 | 2032 5 | OIL-BASED MUD | 9 | 12.2 | | | | | | | -Due to wellbore instability in the lateral, may exceed the MWweight window needed to maintain overburden stresses FILTRATE: 5-10 |

Operator Name: CHEVRON USA INCORPORATED**Well Name:** CB AMILYN 10 3 FED COM P13**Well Number:** 401H

Section 6 - Test, Logging, Coring

List of production tests including testing procedures, equipment and safety measures:

- A. PRODUCTION TESTS ARE NOT PLANNED
- B. LOGS RUN INCLUDE: GAMMA RAY LOG; DIRECTIONAL SURVEY
- C. CORING OPERATIONS ARE NOT PLANNED

List of open and cased hole logs run in the well:

GAMMA RAY LOG, DIRECTIONAL SURVEY,

Coring operation description for the well:

CORING OPERATIONS ARE NOT PLANNED

Section 7 - Pressure

Anticipated Bottom Hole Pressure: 6066**Anticipated Surface Pressure:** 3962**Anticipated Bottom Hole Temperature(F):** 165**Anticipated abnormal pressures, temperatures, or potential geologic hazards?** YES**Describe:**

Hydrogen sulfide gas is not anticipated: However the H2S Contingency plan is attached with this APD in the event that H2S is encountered

Contingency Plans geohazards description:

-Casing design accounts for pressure ramp.-Mud weighting agents available on location to increase drilling fluid density.-BOP, choke, and well control drills.-BOP functioned and pressure tested

Contingency Plans geohazards**Hydrogen Sulfide drilling operations plan required?** YES**Hydrogen sulfide drilling operations**

H2S_Contingency_Plan_20220705134236.pdf

Section 8 - Other Information

Proposed horizontal/directional/multi-lateral plan submission:

SpiderPlot_ChevronCBAmilynSec103Pad13_20220705135157.pdf

CB_AMILYN_10_3_FED_COM_13_401H_DP_20220705175745.pdf

DefPlan100ft_CBAmilyn103FedComP13401H_R0_20220705175757.pdf

Other proposed operations facets description:**Other proposed operations facets attachment:**

Culebra_Bluff_Pad_13_Gas_Management_Plan___NMOCD_20220705134934.pdf

Operational_Best_Management_Practices_20220705134855.pdf

Rig_Layout_20220411150452_20220705134949.pdf

Surface_Rig___20220705134956.pdf

Other Variance attachment:

Operator Name: CHEVRON USA INCORPORATED

Well Name: CB AMILYN 10 3 FED COM P13

Well Number: 401H



CB Amilyn 10 3 Fed Com P13 401H R0 mdv 29Mar22 Proposal Geodetic Report

(Def Plan)



Report Date: March 30, 2022 - 01:56 PM
Client: Chevron
Field: NM, Eddy County (NAD 27 EZ)
Structure / Slot: Chevron CB Amilyn Sec 10 3 Pad 13 / 401H
Well: CB Amilyn 10 3 Fed Com P13 401H
Borehole: CB Amilyn 10 3 Fed Com P13 401H
UWI / API#: Unknown / Unknown
Survey Name: CB Amilyn 10 3 Fed Com P13 401H R0 mdv 29Mar22
Survey Date: March 29, 2022
Tort / AHD / DDI / ERD Ratio: 120.920 ° / 12135.765 ft / 6.494 / 1.269
Coordinate Reference System: NAD27 New Mexico State Plane, Eastern Zone, US Feet
Location Lat / Long: N 32° 18' 41.12285", W 104° 4' 41.80677"
Location Grid N/E Y/X: N 477106.000 ftUS, E 578797.000 ftUS
CRS Grid Convergence Angle: 0.1363 °
Grid Scale Factor: 0.9999162
Version / Patch: 2.10.829.1

Survey / DLS Computation: Minimum Curvature / Lubinski
Vertical Section Azimuth: 359.970 ° (Grid North)
Vertical Section Origin: 0.000 ft, 0.000 ft
TVD Reference Datum: RKB = 28ft
TVD Reference Elevation: 3028.000 ft above MSL
Seabed / Ground Elevation: 3000.000 ft above MSL
Magnetic Declination: 6.840 °
Total Gravity Field Strength: 998.4789mgn (9.80665 Based)
Gravity Model: GARM
Total Magnetic Field Strength: 47609.058 nT
Magnetic Dip Angle: 59.969 °
Declination Date: March 29, 2022
Magnetic Declination Model: HDGM 2022
North Reference: Grid North
Grid Convergence Used: 0.1363 °
Total Corr Mag North->Grid North: 6.7041 °
Local Coord Referenced To: Well Head

| Comments | MD (ft) | Incl (°) | Azim Grid (°) | TVD (ft) | VSEC (ft) | NS (ft) | EW (ft) | DLS (°/100ft) | Northing (ftUS) | Easting (ftUS) | Latitude (N/S ° ' ") | Longitude (E/W ° ' ") |
|-------------------------|------------|-------------|------------------|-------------|--------------|------------|------------|------------------|--------------------|-------------------|-------------------------|--------------------------|
| Surface | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | N/A | 477106.00 | 578797.00 | N 32 18 41.12 W 104 | 4 41.81 |
| | 100.00 | 0.00 | 276.96 | 100.00 | 0.00 | 0.00 | 0.00 | 0.00 | 477106.00 | 578797.00 | N 32 18 41.12 W 104 | 4 41.81 |
| | 200.00 | 0.00 | 276.96 | 200.00 | 0.00 | 0.00 | 0.00 | 0.00 | 477106.00 | 578797.00 | N 32 18 41.12 W 104 | 4 41.81 |
| | 300.00 | 0.00 | 276.96 | 300.00 | 0.00 | 0.00 | 0.00 | 0.00 | 477106.00 | 578797.00 | N 32 18 41.12 W 104 | 4 41.81 |
| Salado (SLDO) | 328.00 | 0.00 | 276.96 | 328.00 | 0.00 | 0.00 | 0.00 | 0.00 | 477106.00 | 578797.00 | N 32 18 41.12 W 104 | 4 41.81 |
| | 400.00 | 0.00 | 276.96 | 400.00 | 0.00 | 0.00 | 0.00 | 0.00 | 477106.00 | 578797.00 | N 32 18 41.12 W 104 | 4 41.81 |
| Build 1.5"/100ft | 500.00 | 0.00 | 276.96 | 500.00 | 0.00 | 0.00 | 0.00 | 0.00 | 477106.00 | 578797.00 | N 32 18 41.12 W 104 | 4 41.81 |
| | 600.00 | 1.50 | 276.96 | 599.99 | 0.16 | 0.16 | -1.30 | 1.50 | 477106.16 | 578795.70 | N 32 18 41.12 W 104 | 4 41.82 |
| | 700.00 | 3.00 | 276.96 | 699.91 | 0.64 | 0.63 | -5.20 | 1.50 | 477106.63 | 578791.80 | N 32 18 41.13 W 104 | 4 41.87 |
| | 800.00 | 4.50 | 276.96 | 799.69 | 1.43 | 1.43 | -11.69 | 1.50 | 477107.43 | 578785.31 | N 32 18 41.14 W 104 | 4 41.94 |
| | 900.00 | 6.00 | 276.96 | 899.27 | 2.55 | 2.54 | -20.77 | 1.50 | 477108.54 | 578776.23 | N 32 18 41.15 W 104 | 4 42.05 |
| Castile (CSTL) | 953.06 | 6.80 | 276.96 | 952.00 | 3.27 | 3.25 | -26.64 | 1.50 | 477109.25 | 578770.36 | N 32 18 41.16 W 104 | 4 42.12 |
| | 1000.00 | 7.50 | 276.96 | 998.57 | 3.98 | 3.96 | -32.44 | 1.50 | 477109.96 | 578764.57 | N 32 18 41.16 W 104 | 4 42.18 |
| | 1100.00 | 9.00 | 276.96 | 1097.54 | 5.72 | 5.70 | -46.68 | 1.50 | 477111.70 | 578750.32 | N 32 18 41.18 W 104 | 4 42.35 |
| | 1200.00 | 10.50 | 276.96 | 1196.09 | 7.79 | 7.75 | -63.49 | 1.50 | 477113.75 | 578733.52 | N 32 18 41.20 W 104 | 4 42.55 |
| | 1300.00 | 12.00 | 276.96 | 1294.16 | 10.16 | 10.12 | -82.85 | 1.50 | 477116.12 | 578714.15 | N 32 18 41.22 W 104 | 4 42.77 |
| | 1400.00 | 13.50 | 276.96 | 1391.70 | 12.85 | 12.79 | -104.76 | 1.50 | 477118.79 | 578692.25 | N 32 18 41.25 W 104 | 4 43.03 |
| | 1500.00 | 15.00 | 276.96 | 1488.62 | 15.84 | 15.77 | -129.19 | 1.50 | 477121.77 | 578667.82 | N 32 18 41.28 W 104 | 4 43.31 |
| Hold | 1500.31 | 15.00 | 276.96 | 1488.91 | 15.85 | 15.78 | -129.27 | 1.50 | 477121.78 | 578667.74 | N 32 18 41.28 W 104 | 4 43.31 |
| | 1600.00 | 15.00 | 276.96 | 1585.21 | 18.99 | 18.91 | -154.89 | 0.00 | 477124.91 | 578642.12 | N 32 18 41.31 W 104 | 4 43.61 |
| | 1700.00 | 15.00 | 276.96 | 1681.80 | 22.15 | 22.05 | -180.59 | 0.00 | 477128.05 | 578616.42 | N 32 18 41.35 W 104 | 4 43.91 |
| | 1800.00 | 15.00 | 276.96 | 1778.39 | 25.30 | 25.19 | -206.29 | 0.00 | 477131.19 | 578590.73 | N 32 18 41.38 W 104 | 4 44.21 |
| | 1900.00 | 15.00 | 276.96 | 1874.98 | 28.45 | 28.33 | -231.99 | 0.00 | 477134.32 | 578565.03 | N 32 18 41.41 W 104 | 4 44.51 |
| | 2000.00 | 15.00 | 276.96 | 1971.57 | 31.60 | 31.46 | -257.69 | 0.00 | 477137.46 | 578539.33 | N 32 18 41.44 W 104 | 4 44.81 |
| | 2100.00 | 15.00 | 276.96 | 2068.16 | 34.75 | 34.60 | -283.39 | 0.00 | 477140.60 | 578513.64 | N 32 18 41.47 W 104 | 4 45.11 |
| | 2200.00 | 15.00 | 276.96 | 2164.75 | 37.90 | 37.74 | -309.09 | 0.00 | 477143.74 | 578487.94 | N 32 18 41.50 W 104 | 4 45.41 |
| | 2300.00 | 15.00 | 276.96 | 2261.34 | 41.05 | 40.88 | -334.78 | 0.00 | 477146.87 | 578462.24 | N 32 18 41.54 W 104 | 4 45.71 |
| | 2400.00 | 15.00 | 276.96 | 2357.93 | 44.20 | 44.02 | -360.48 | 0.00 | 477150.01 | 578436.55 | N 32 18 41.57 W 104 | 4 46.01 |
| | 2500.00 | 15.00 | 276.96 | 2454.52 | 47.36 | 47.15 | -386.18 | 0.00 | 477153.15 | 578410.85 | N 32 18 41.60 W 104 | 4 46.31 |
| | 2600.00 | 15.00 | 276.96 | 2551.11 | 50.51 | 50.29 | -411.88 | 0.00 | 477156.29 | 578385.15 | N 32 18 41.63 W 104 | 4 46.60 |
| Lamar (LMAR) | 2604.03 | 15.00 | 276.96 | 2555.00 | 50.63 | 50.42 | -412.92 | 0.00 | 477156.41 | 578384.12 | N 32 18 41.63 W 104 | 4 46.62 |
| Bell Canyon (BLCN) | 2647.51 | 15.00 | 276.96 | 2597.00 | 52.00 | 51.78 | -424.09 | 0.00 | 477157.78 | 578372.95 | N 32 18 41.65 W 104 | 4 46.75 |
| | 2700.00 | 15.00 | 276.96 | 2647.70 | 53.66 | 53.43 | -437.58 | 0.00 | 477159.42 | 578359.46 | N 32 18 41.66 W 104 | 4 46.90 |
| | 2800.00 | 15.00 | 276.96 | 2744.29 | 56.81 | 56.57 | -463.28 | 0.00 | 477162.56 | 578333.76 | N 32 18 41.69 W 104 | 4 47.20 |
| | 2900.00 | 15.00 | 276.96 | 2840.88 | 59.96 | 59.71 | -488.98 | 0.00 | 477165.70 | 578308.06 | N 32 18 41.73 W 104 | 4 47.50 |
| | 3000.00 | 15.00 | 276.96 | 2937.47 | 63.11 | 62.84 | -514.68 | 0.00 | 477168.84 | 578282.37 | N 32 18 41.76 W 104 | 4 47.80 |
| | 3100.00 | 15.00 | 276.96 | 3034.06 | 66.26 | 65.98 | -540.37 | 0.00 | 477171.98 | 578256.67 | N 32 18 41.79 W 104 | 4 48.10 |
| | 3200.00 | 15.00 | 276.96 | 3130.65 | 69.42 | 69.12 | -566.07 | 0.00 | 477175.11 | 578230.98 | N 32 18 41.82 W 104 | 4 48.40 |
| | 3300.00 | 15.00 | 276.96 | 3227.25 | 72.57 | 72.26 | -591.77 | 0.00 | 477178.25 | 578205.28 | N 32 18 41.85 W 104 | 4 48.70 |
| | 3400.00 | 15.00 | 276.96 | 3323.84 | 75.72 | 75.39 | -617.47 | 0.00 | 477181.39 | 578179.58 | N 32 18 41.88 W 104 | 4 49.00 |
| | 3500.00 | 15.00 | 276.96 | 3420.43 | 78.87 | 78.53 | -643.17 | 0.00 | 477184.53 | 578153.89 | N 32 18 41.92 W 104 | 4 49.30 |
| Cherry Canyon (CRCN) | 3514.05 | 15.00 | 276.96 | 3434.00 | 79.31 | 78.97 | -646.78 | 0.00 | 477184.97 | 578150.27 | N 32 18 41.92 W 104 | 4 49.34 |
| | 3600.00 | 15.00 | 276.96 | 3517.02 | 82.02 | 81.67 | -668.87 | 0.00 | 477187.66 | 578128.19 | N 32 18 41.95 W 104 | 4 49.60 |
| | 3700.00 | 15.00 | 276.96 | 3613.61 | 85.17 | 84.81 | -694.57 | 0.00 | 477190.80 | 578102.49 | N 32 18 41.98 W 104 | 4 49.90 |
| | 3800.00 | 15.00 | 276.96 | 3710.20 | 88.32 | 87.95 | -720.27 | 0.00 | 477193.94 | 578076.80 | N 32 18 42.01 W 104 | 4 50.20 |
| | 3900.00 | 15.00 | 276.96 | 3806.79 | 91.47 | 91.08 | -745.96 | 0.00 | 477197.08 | 578051.10 | N 32 18 42.04 W 104 | 4 50.50 |
| | 4000.00 | 15.00 | 276.96 | 3903.38 | 94.63 | 94.22 | -771.66 | 0.00 | 477200.21 | 578025.40 | N 32 18 42.07 W 104 | 4 50.80 |
| | 4100.00 | 15.00 | 276.96 | 3999.97 | 97.78 | 97.36 | -797.36 | 0.00 | 477203.35 | 577999.71 | N 32 18 42.10 W 104 | 4 51.09 |
| | 4200.00 | 15.00 | 276.96 | 4096.56 | 100.93 | 100.50 | -823.06 | 0.00 | 477206.49 | 577974.01 | N 32 18 42.14 W 104 | 4 51.39 |
| | 4300.00 | 15.00 | 276.96 | 4193.15 | 104.08 | 103.64 | -848.76 | 0.00 | 477209.63 | 577948.31 | N 32 18 42.17 W 104 | 4 51.69 |
| | 4400.00 | 15.00 | 276.96 | 4289.74 | 107.23 | 106.77 | -874.46 | 0.00 | 477212.76 | 577922.62 | N 32 18 42.20 W 104 | 4 51.99 |
| | 4500.00 | 15.00 | 276.96 | 4386.33 | 110.38 | 109.91 | -900.16 | 0.00 | 477215.90 | 577896.92 | N 32 18 42.23 W 104 | 4 52.29 |
| Brushy Canyon (BCN) | 4587.66 | 15.00 | 276.96 | 4471.00 | 113.15 | 112.66 | -922.68 | 0.00 | 477218.65 | 577874.39 | N 32 18 42.26 W 104 | 4 52.55 |
| | 4600.00 | 15.00 | 276.96 | 4482.92 | 113.53 | 113.05 | -925.86 | 0.00 | 477219.04 | 577871.22 | N 32 18 42.26 W 104 | 4 52.59 |
| | 4700.00 | 15.00 | 276.96 | 4579.51 | 116.69 | 116.19 | -951.55 | 0.00 | 477222.18 | 577845.53 | N 32 18 42.29 W 104 | 4 52.89 |
| | 4800.00 | 15.00 | 276.96 | 4676.10 | 119.84 | 119.32 | -977.25 | 0.00 | 477225.31 | 577819.83 | N 32 18 42.33 W 104 | 4 53.19 |
| Drop .75"/100ft | 4889.42 | 15.00 | 276.96 | 4762.48 | 122.65 | 122.13 | -1000.23 | 0.00 | 477228.12 | 577796.85 | N 32 18 42.35 W 104 | 4 53.46 |
| | 4900.00 | 14.93 | 276.96 | 4772.70 | 122.99 | 122.46 | -1002.95 | 0.75 | 477228.45 | 577794.14 | N 32 18 42.36 W 104 | 4 53.49 |
| | 5000.00 | 14.18 | 276.96 | 4869.49 | 126.05 | 125.51 | -1027.88 | 0.75 | 477231.50 | 577769.21 | N 32 18 42.39 W 104 | 4 53.78 |
| | 5100.00 | 13.43 | 276.96 | 4966.60 | 128.95 | 128.40 | -1051.56 | 0.75 | 477234.39 | 577745.53 | N 32 18 42.42 W 104 | 4 54.06 |
| | 5200.00 | 12.68 | 276.96 | 5064.02 | 131.70 | 131.13 | -1073.97 | 0.75 | 477237.12 | 577723.12 | N 32 18 42.45 W 104 | 4 54.32 |
| | 5300.00 | 11.93 | 276.96 | 5161.72 | 134.29 | 133.72 | -1095.12 | 0.75 | 477239.71 | 577701.97 | N 32 18 42.47 W 104 | 4 54.56 |
| | 5400.00 | 11.18 | 276.96 | 5259.69 | 136.73 | 136.14 | -1115.00 | 0.75 | 477242.13 | 577682.10 | N 32 18 42.50 W 104 | 4 54.79 |
| | 5500.00 | 10.43 | 276.96 | 5357.92 | 139.01 | 138.41 | -1133.60 | 0.75 | 477244.40 | 577663.50 | N 32 18 42.52 W 104 | 4 55.01 |
| | 5600.00 | 9.68 | 276.96 | 5456.39 | 141.13 | 140.53 | -1150.92 | 0.75 | 477246.52 | 577646.18 | N 32 18 42.54 W 104 | 4 55.21 |
| | 5700.00 | 8.93 | 276.96 | 5555.07 | 143.10 | 142.49 | -1166.96 | 0.75 | 477248.48 | 577630.14 | N 32 18 42.56 W 104 | 4 55.40 |
| | 5800.00 | 8.18 | 276.96 | 5653.96 | 144.91 | 144.29 | -1181.72 | 0.75 | 477250.28 | 577615.38 | N 32 18 42.58 W 104 | 4 55.57 |
| | 5900.00 | 7.43 | 276.96 | 5753.03 | 146.56 | 145.94 | -1195.19 | 0.75 | 477251.92 | 577601.91 | N 32 18 42.59 W 104 | 4 55.73 |
| | 6000.00 | 6.68 | 276.96 | 5852.28 | 148.06 | 147.42 | -1207.37 | 0.75 | 477253.41 | 577589.73 | N 32 18 42.61 W 104 | 4 55.87 |
| | 6100.00 | 5.93 | 276.96 | 5951.67 | 149.39 | 148.75 | -1218.27 | 0.75 | 477254.74 | 577578.84 | N 32 18 42.62 W 104 | 4 56.00 |
| | 6200.00 | 5.18 | 276.96 | 6051.20 | 150.57 | 149.93 | -1227.87 | 0.75 | 477255.91 | 577569.24 | N 32 18 42.64 W 104 | 4 56.11 |
| Bone Spring Lime (BSGL) | 6290.12 | 4.50 | 276.96 | 6141.00 | 151.49 | 150.85 | -1235.41 | 0.75 | 477256.83 | 577561.70 | N 32 18 42.64 W 104 | 4 56.20 |
| | 6300.00 | 4.43 | 276.96 | 61 | | | | | | | | |

| Comments | MD (ft) | Incl (°) | Azim Grid (°) | TVD (ft) | VSEC (ft) | NS (ft) | EW (ft) | DLS (°/100ft) | Northing (ftUS) | Easting (ftUS) | Latitude (N/S ° ' ") | Longitude (E/W ° ' ") |
|-----------------------------------|------------|-------------|------------------|-------------|--------------|------------|------------|------------------|--------------------|-------------------|-------------------------|--------------------------|
| Hold Vertical | 6890.04 | 0.00 | 276.96 | 6740.30 | 154.36 | 153.70 | -1258.78 | 0.75 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 6900.00 | 0.00 | 276.96 | 6750.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 7000.00 | 0.00 | 276.96 | 6850.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 7100.00 | 0.00 | 276.96 | 6950.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 7200.00 | 0.00 | 276.96 | 7050.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| First Bone Spring (FBS) | 7300.00 | 0.00 | 276.96 | 7150.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 7324.74 | 0.00 | 276.96 | 7175.00 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 7400.00 | 0.00 | 276.96 | 7250.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| First Bone Spring Shale (FBS_SH) | 7452.74 | 0.00 | 276.96 | 7303.00 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 7500.00 | 0.00 | 276.96 | 7350.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 7600.00 | 0.00 | 276.96 | 7450.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 7700.00 | 0.00 | 276.96 | 7550.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 7800.00 | 0.00 | 276.96 | 7650.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| Second Bone Spring Upper (SBU) | 7822.74 | 0.00 | 276.96 | 7673.00 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 7900.00 | 0.00 | 276.96 | 7750.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 8000.00 | 0.00 | 276.96 | 7850.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 8100.00 | 0.00 | 276.96 | 7950.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 8200.00 | 0.00 | 276.96 | 8050.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| Second Bone Spring Lower (SBL) | 8300.00 | 0.00 | 276.96 | 8150.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 8364.74 | 0.00 | 276.96 | 8215.00 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 8400.00 | 0.00 | 276.96 | 8250.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 8500.00 | 0.00 | 276.96 | 8350.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 8600.00 | 0.00 | 276.96 | 8450.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 8700.00 | 0.00 | 276.96 | 8550.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 8800.00 | 0.00 | 276.96 | 8650.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 8900.00 | 0.00 | 276.96 | 8750.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 9000.00 | 0.00 | 276.96 | 8850.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 9032.74 | 0.00 | 276.96 | 8883.00 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| Third Bone First Carbonate (TB1C) | 9100.00 | 0.00 | 276.96 | 8950.26 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| | 9130.04 | 0.00 | 276.96 | 8980.30 | 154.36 | 153.70 | -1258.78 | 0.00 | 477259.69 | 577538.33 | N 32 18 42.67 W 104 | 4 56.47 |
| Build 10"/100ft | 9200.00 | 7.00 | 359.47 | 9050.09 | 158.63 | 157.97 | -1258.82 | 10.00 | 477263.95 | 577538.29 | N 32 18 42.72 W 104 | 4 56.47 |
| | 9221.12 | 9.11 | 359.47 | 9071.00 | 161.58 | 160.92 | -1258.85 | 10.00 | 477266.91 | 577538.26 | N 32 18 42.74 W 104 | 4 56.47 |
| | 9300.00 | 17.00 | 359.47 | 9147.78 | 179.38 | 178.72 | -1259.01 | 10.00 | 477284.71 | 577538.10 | N 32 18 42.92 W 104 | 4 56.47 |
| | 9400.00 | 27.00 | 359.47 | 9240.39 | 216.79 | 216.13 | -1259.36 | 10.00 | 477322.11 | 577537.75 | N 32 18 43.29 W 104 | 4 56.47 |
| | 9500.00 | 37.00 | 359.47 | 9325.09 | 269.71 | 269.05 | -1259.85 | 10.00 | 477375.02 | 577537.26 | N 32 18 43.81 W 104 | 4 56.48 |
| | 9600.00 | 47.00 | 359.47 | 9399.31 | 336.53 | 335.87 | -1260.47 | 10.00 | 477441.84 | 577536.63 | N 32 18 44.48 W 104 | 4 56.48 |
| | 9611.40 | 48.14 | 359.47 | 9407.00 | 344.94 | 344.28 | -1260.55 | 10.00 | 477450.25 | 577536.56 | N 32 18 44.56 W 104 | 4 56.48 |
| Wolfcamp A | 9700.00 | 57.00 | 359.47 | 9460.80 | 415.22 | 414.56 | -1261.21 | 10.00 | 477520.53 | 577535.90 | N 32 18 45.25 W 104 | 4 56.49 |
| | 9800.00 | 67.00 | 359.47 | 9507.70 | 503.40 | 502.74 | -1262.03 | 10.00 | 477608.69 | 577535.08 | N 32 18 46.13 W 104 | 4 56.50 |
| | 9900.00 | 77.00 | 359.47 | 9538.57 | 598.38 | 597.72 | -1262.91 | 10.00 | 477703.67 | 577534.20 | N 32 18 47.07 W 104 | 4 56.51 |
| | 10000.00 | 87.00 | 359.47 | 9552.47 | 697.27 | 696.61 | -1263.83 | 10.00 | 477802.55 | 577533.28 | N 32 18 48.05 W 104 | 4 56.51 |
| | 10029.49 | 89.95 | 359.47 | 9553.26 | 726.75 | 726.08 | -1264.10 | 10.00 | 477832.02 | 577533.00 | N 32 18 48.34 W 104 | 4 56.52 |
| FIF CROSS Landline Point | 10100.00 | 89.95 | 359.47 | 9553.33 | 797.26 | 796.59 | -1264.76 | 0.00 | 477902.53 | 577532.35 | N 32 18 49.03 W 104 | 4 56.52 |
| | 10200.00 | 89.95 | 359.47 | 9553.42 | 897.25 | 896.59 | -1265.69 | 0.00 | 478002.51 | 577531.42 | N 32 18 50.02 W 104 | 4 56.53 |
| | 10300.00 | 89.95 | 359.47 | 9553.52 | 997.25 | 996.59 | -1266.62 | 0.00 | 478102.50 | 577530.49 | N 32 18 51.01 W 104 | 4 56.54 |
| | 10400.00 | 89.95 | 359.47 | 9553.61 | 1097.25 | 1096.58 | -1267.55 | 0.00 | 478202.49 | 577529.56 | N 32 18 52.00 W 104 | 4 56.55 |
| | 10500.00 | 89.95 | 359.47 | 9553.71 | 1197.24 | 1196.58 | -1268.48 | 0.00 | 478302.47 | 577528.63 | N 32 18 52.99 W 104 | 4 56.55 |
| | 10600.00 | 89.95 | 359.47 | 9553.80 | 1297.24 | 1296.57 | -1269.41 | 0.00 | 478402.46 | 577527.70 | N 32 18 53.98 W 104 | 4 56.56 |
| | 10700.00 | 89.95 | 359.47 | 9553.90 | 1397.23 | 1396.57 | -1270.34 | 0.00 | 478502.45 | 577526.77 | N 32 18 54.97 W 104 | 4 56.57 |
| | 10800.00 | 89.95 | 359.47 | 9554.00 | 1497.23 | 1496.56 | -1271.27 | 0.00 | 478602.44 | 577525.84 | N 32 18 55.96 W 104 | 4 56.58 |
| | 10900.00 | 89.95 | 359.47 | 9554.09 | 1597.23 | 1596.56 | -1272.20 | 0.00 | 478702.42 | 577524.91 | N 32 18 56.95 W 104 | 4 56.59 |
| | 11000.00 | 89.95 | 359.47 | 9554.19 | 1697.22 | 1696.56 | -1273.13 | 0.00 | 478802.41 | 577523.98 | N 32 18 57.94 W 104 | 4 56.59 |
| | 11100.00 | 89.95 | 359.47 | 9554.28 | 1797.22 | 1796.55 | -1274.06 | 0.00 | 478902.40 | 577523.05 | N 32 18 58.93 W 104 | 4 56.60 |
| | 11200.00 | 89.95 | 359.47 | 9554.38 | 1897.21 | 1896.55 | -1274.99 | 0.00 | 479002.38 | 577522.12 | N 32 18 59.92 W 104 | 4 56.61 |
| | 11300.00 | 89.95 | 359.47 | 9554.48 | 1997.21 | 1996.54 | -1275.92 | 0.00 | 479102.37 | 577521.19 | N 32 19 0.91 W 104 | 4 56.62 |
| | 11400.00 | 89.95 | 359.47 | 9554.57 | 2097.21 | 2096.54 | -1276.85 | 0.00 | 479202.36 | 577520.26 | N 32 19 1.90 W 104 | 4 56.63 |
| | 11500.00 | 89.95 | 359.47 | 9554.67 | 2197.20 | 2196.53 | -1277.78 | 0.00 | 479302.35 | 577519.32 | N 32 19 2.89 W 104 | 4 56.64 |
| | 11600.00 | 89.95 | 359.47 | 9554.76 | 2297.20 | 2296.53 | -1278.71 | 0.00 | 479402.33 | 577518.39 | N 32 19 3.88 W 104 | 4 56.64 |
| | 11700.00 | 89.95 | 359.47 | 9554.86 | 2397.19 | 2396.52 | -1279.65 | 0.00 | 479502.32 | 577517.46 | N 32 19 4.87 W 104 | 4 56.65 |
| | 11800.00 | 89.95 | 359.47 | 9554.96 | 2497.19 | 2496.52 | -1280.58 | 0.00 | 479602.31 | 577516.53 | N 32 19 5.86 W 104 | 4 56.66 |
| | 11900.00 | 89.95 | 359.47 | 9555.05 | 2597.19 | 2596.52 | -1281.51 | 0.00 | 479702.29 | 577515.60 | N 32 19 6.85 W 104 | 4 56.67 |
| | 12000.00 | 89.95 | 359.47 | 9555.15 | 2697.18 | 2696.51 | -1282.44 | 0.00 | 479802.28 | 577514.67 | N 32 19 7.84 W 104 | 4 56.68 |
| | 12100.00 | 89.95 | 359.47 | 9555.24 | 2797.18 | 2796.51 | -1283.37 | 0.00 | 479902.27 | 577513.74 | N 32 19 8.83 W 104 | 4 56.68 |
| | 12200.00 | 89.95 | 359.47 | 9555.34 | 2897.18 | 2896.50 | -1284.30 | 0.00 | 480002.25 | 577512.81 | N 32 19 9.81 W 104 | 4 56.69 |
| | 12300.00 | 89.95 | 359.47 | 9555.43 | 2997.17 | 2996.50 | -1285.2 | | | | | |

| Comments | MD (ft) | Incl (°) | Azim Grid (°) | TVD (ft) | VSEC (ft) | NS (ft) | EW (ft) | DLS (°/100ft) | Northing (ftUS) | Easting (ftUS) | Latitude (N/S ° ' ") | Longitude (E/W ° ' ") |
|-------------------------------------|------------|-------------|------------------|-------------|--------------|------------|------------|------------------|--------------------|-------------------|-------------------------|--------------------------|
| | 16400.00 | 89.95 | 0.43 | 9559.15 | 7097.02 | 7096.34 | -1299.76 | 0.00 | 484201.73 | 577497.36 | N 32 19 51.37 W 104 | 4 56.76 |
| | 16500.00 | 89.95 | 0.43 | 9559.23 | 7197.02 | 7196.34 | -1299.00 | 0.00 | 484301.72 | 577498.11 | N 32 19 52.36 W 104 | 4 56.75 |
| | 16600.00 | 89.95 | 0.43 | 9559.31 | 7297.01 | 7296.34 | -1298.25 | 0.00 | 484401.71 | 577498.87 | N 32 19 53.35 W 104 | 4 56.73 |
| | 16700.00 | 89.95 | 0.43 | 9559.39 | 7397.01 | 7396.33 | -1297.49 | 0.00 | 484501.70 | 577499.62 | N 32 19 54.34 W 104 | 4 56.72 |
| | 16800.00 | 89.95 | 0.43 | 9559.47 | 7497.01 | 7496.33 | -1296.73 | 0.00 | 484601.69 | 577500.38 | N 32 19 55.33 W 104 | 4 56.71 |
| | 16900.00 | 89.95 | 0.43 | 9559.55 | 7597.00 | 7596.33 | -1295.98 | 0.00 | 484701.68 | 577501.13 | N 32 19 56.32 W 104 | 4 56.70 |
| | 17000.00 | 89.95 | 0.43 | 9559.63 | 7697.00 | 7696.32 | -1295.22 | 0.00 | 484801.66 | 577501.89 | N 32 19 57.31 W 104 | 4 56.69 |
| | 17100.00 | 89.95 | 0.43 | 9559.71 | 7797.00 | 7796.32 | -1294.47 | 0.00 | 484901.65 | 577502.64 | N 32 19 58.30 W 104 | 4 56.68 |
| | 17200.00 | 89.95 | 0.43 | 9559.79 | 7896.99 | 7896.32 | -1293.71 | 0.00 | 485001.64 | 577503.40 | N 32 19 59.29 W 104 | 4 56.67 |
| | 17300.00 | 89.95 | 0.43 | 9559.88 | 7996.99 | 7996.32 | -1292.96 | 0.00 | 485101.63 | 577504.15 | N 32 20 0.28 W 104 | 4 56.65 |
| | 17400.00 | 89.95 | 0.43 | 9559.96 | 8096.99 | 8096.31 | -1292.20 | 0.00 | 485201.62 | 577504.91 | N 32 20 1.27 W 104 | 4 56.64 |
| | 17500.00 | 89.95 | 0.43 | 9560.04 | 8196.98 | 8196.31 | -1291.45 | 0.00 | 485301.61 | 577505.66 | N 32 20 2.26 W 104 | 4 56.63 |
| | 17600.00 | 89.95 | 0.43 | 9560.12 | 8296.98 | 8296.31 | -1290.69 | 0.00 | 485401.59 | 577506.42 | N 32 20 3.25 W 104 | 4 56.62 |
| | 17700.00 | 89.95 | 0.43 | 9560.20 | 8396.98 | 8396.30 | -1289.94 | 0.00 | 485501.58 | 577507.17 | N 32 20 4.24 W 104 | 4 56.61 |
| | 17800.00 | 89.95 | 0.43 | 9560.28 | 8496.97 | 8496.30 | -1289.18 | 0.00 | 485601.57 | 577507.93 | N 32 20 5.23 W 104 | 4 56.60 |
| | 17900.00 | 89.95 | 0.43 | 9560.36 | 8596.97 | 8596.30 | -1288.43 | 0.00 | 485701.56 | 577508.69 | N 32 20 6.22 W 104 | 4 56.58 |
| | 18000.00 | 89.95 | 0.43 | 9560.44 | 8696.97 | 8696.30 | -1287.67 | 0.00 | 485801.55 | 577509.44 | N 32 20 7.21 W 104 | 4 56.57 |
| | 18100.00 | 89.95 | 0.43 | 9560.52 | 8796.96 | 8796.29 | -1286.91 | 0.00 | 485901.54 | 577510.20 | N 32 20 8.19 W 104 | 4 56.56 |
| | 18200.00 | 89.95 | 0.43 | 9560.60 | 8896.96 | 8896.29 | -1286.16 | 0.00 | 486001.53 | 577510.95 | N 32 20 9.18 W 104 | 4 56.55 |
| | 18300.00 | 89.95 | 0.43 | 9560.68 | 8996.96 | 8996.29 | -1285.40 | 0.00 | 486101.51 | 577511.71 | N 32 20 10.17 W 104 | 4 56.54 |
| | 18400.00 | 89.95 | 0.43 | 9560.76 | 9096.96 | 9096.28 | -1284.65 | 0.00 | 486201.50 | 577512.46 | N 32 20 11.16 W 104 | 4 56.53 |
| | 18500.00 | 89.95 | 0.43 | 9560.84 | 9196.95 | 9196.28 | -1283.89 | 0.00 | 486301.49 | 577513.22 | N 32 20 12.15 W 104 | 4 56.52 |
| | 18600.00 | 89.95 | 0.43 | 9560.92 | 9296.95 | 9296.28 | -1283.14 | 0.00 | 486401.48 | 577513.97 | N 32 20 13.14 W 104 | 4 56.50 |
| | 18700.00 | 89.95 | 0.43 | 9561.00 | 9396.95 | 9396.27 | -1282.38 | 0.00 | 486501.47 | 577514.73 | N 32 20 14.13 W 104 | 4 56.49 |
| | 18800.00 | 89.95 | 0.43 | 9561.08 | 9496.94 | 9496.27 | -1281.63 | 0.00 | 486601.46 | 577515.48 | N 32 20 15.12 W 104 | 4 56.48 |
| | 18900.00 | 89.95 | 0.43 | 9561.16 | 9596.94 | 9596.27 | -1280.87 | 0.00 | 486701.45 | 577516.24 | N 32 20 16.11 W 104 | 4 56.47 |
| | 19000.00 | 89.95 | 0.43 | 9561.24 | 9696.94 | 9696.27 | -1280.12 | 0.00 | 486801.43 | 577516.99 | N 32 20 17.10 W 104 | 4 56.46 |
| | 19100.00 | 89.95 | 0.43 | 9561.32 | 9796.93 | 9796.26 | -1279.36 | 0.00 | 486901.42 | 577517.75 | N 32 20 18.09 W 104 | 4 56.45 |
| | 19200.00 | 89.95 | 0.43 | 9561.40 | 9896.93 | 9896.26 | -1278.60 | 0.00 | 487001.41 | 577518.50 | N 32 20 19.08 W 104 | 4 56.43 |
| | 19300.00 | 89.95 | 0.43 | 9561.49 | 9996.93 | 9996.26 | -1277.85 | 0.00 | 487101.40 | 577519.26 | N 32 20 20.07 W 104 | 4 56.42 |
| | 19400.00 | 89.95 | 0.43 | 9561.57 | 10096.92 | 10096.25 | -1277.09 | 0.00 | 487201.39 | 577520.02 | N 32 20 21.06 W 104 | 4 56.41 |
| | 19500.00 | 89.95 | 0.43 | 9561.65 | 10196.92 | 10196.25 | -1276.34 | 0.00 | 487301.38 | 577520.77 | N 32 20 22.05 W 104 | 4 56.40 |
| | 19600.00 | 89.95 | 0.43 | 9561.73 | 10296.92 | 10296.25 | -1275.58 | 0.00 | 487401.37 | 577521.53 | N 32 20 23.04 W 104 | 4 56.39 |
| | 19700.00 | 89.95 | 0.43 | 9561.81 | 10396.91 | 10396.25 | -1274.83 | 0.00 | 487501.35 | 577522.28 | N 32 20 24.03 W 104 | 4 56.38 |
| | 19800.00 | 89.95 | 0.43 | 9561.89 | 10496.91 | 10496.24 | -1274.07 | 0.00 | 487601.34 | 577523.04 | N 32 20 25.02 W 104 | 4 56.37 |
| | 19900.00 | 89.95 | 0.43 | 9561.97 | 10596.91 | 10596.24 | -1273.32 | 0.00 | 487701.33 | 577523.79 | N 32 20 26.01 W 104 | 4 56.35 |
| | 20000.00 | 89.95 | 0.43 | 9562.05 | 10696.90 | 10696.24 | -1272.56 | 0.00 | 487801.32 | 577524.55 | N 32 20 26.99 W 104 | 4 56.34 |
| LTP Cross | 20019.78 | 89.95 | 0.43 | 9562.06 | 10716.66 | 10716.00 | -1272.41 | 0.00 | 487821.08 | 577524.70 | N 32 20 27.19 W 104 | 4 56.34 |
| | 20100.00 | 89.95 | 0.43 | 9562.13 | 10796.90 | 10796.23 | -1271.81 | 0.00 | 487901.31 | 577525.30 | N 32 20 27.98 W 104 | 4 56.33 |
| | 20200.00 | 89.95 | 0.43 | 9562.21 | 10896.90 | 10896.23 | -1271.05 | 0.00 | 488001.30 | 577526.06 | N 32 20 28.97 W 104 | 4 56.32 |
| | 20300.00 | 89.95 | 0.43 | 9562.29 | 10996.89 | 10996.23 | -1270.30 | 0.00 | 488101.29 | 577526.81 | N 32 20 29.96 W 104 | 4 56.31 |
| CB Amilyn 10 3 Fed Com P13 401H BHL | 20324.72 | 89.95 | 0.43 | 9562.31 | 11021.61 | 11020.95 | -1270.11 | 0.00 | 488126.00 | 577527.00 | N 32 20 30.21 W 104 | 4 56.30 |

Survey Type: Def Plan

Survey Error Model: ISCWSA Rev 3 *** 3-D 97.071% Confidence 3.0000 sigma
Survey Program:

| Description | Part | MD From (ft) | MD To (ft) | EOU Freq (ft) | Hole Size (in) | Casing Diameter (in) | Expected Max Inclination (deg) | Survey Tool Type | Borehole / Survey |
|-------------|------|-----------------|---------------|------------------|-------------------|-------------------------|--------------------------------------|-------------------------------|--|
| | 1 | 0.000 | 28.000 | 1/100.000 | 30.000 | 30.000 | | B001Mb_MWD+HRGM-Depth Only | CB Amilyn 10 3 Fed Com P13 401H / CB Amilyn 10 3 Fed Com P13 401H R0 mdv 29Mar22 |
| | 1 | 28.000 | 20324.717 | 1/100.000 | 30.000 | 30.000 | | B001Mb_MWD+HRGM | CB Amilyn 10 3 Fed Com P13 401H / CB Amilyn 10 3 Fed Com |

...CB Amilyn 10 3 Fed Com P13 401H\CB Amilyn 10 3 Fed Com P13 401H R0 mdv 29Mar22

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

| | |
|------------------------------|-----------------------------------|
| OPERATOR'S NAME: | Chevron |
| LEASE NO.: | NMNM15433 |
| LOCATION: | Section 15, T.23 S, R.28 E., NMPM |
| COUNTY: | Eddy County, New Mexico |
| WELL NAME & NO.: | CB Amilyn 10 3 Fed Com P13 401H |
| SURFACE HOLE FOOTAGE: | 418'/N & 1589'/W |
| BOTTOM HOLE FOOTAGE: | 25'/N & 330'/W |

COA

| | | | |
|----------------------------------|--|---|--|
| H2S | <input checked="" type="radio"/> Yes | <input type="radio"/> No | |
| Potash | <input checked="" type="radio"/> None | <input type="radio"/> Secretary | <input type="radio"/> R-111-P |
| Cave/Karst Potential | <input type="radio"/> Low | <input checked="" type="radio"/> Medium | <input type="radio"/> High |
| Cave/Karst Potential | <input type="radio"/> Critical | | |
| Variance | <input type="radio"/> None | <input checked="" type="radio"/> Flex Hose | <input type="radio"/> Other |
| Wellhead | <input type="radio"/> Conventional | <input checked="" type="radio"/> Multibowl | <input type="radio"/> Both |
| Wellhead Variance | <input type="radio"/> Diverter | | |
| Other | <input type="checkbox"/> 4 String | <input type="checkbox"/> Capitan Reef | <input type="checkbox"/> WIPP |
| Other | <input type="checkbox"/> Fluid Filled | <input type="checkbox"/> Pilot Hole | <input type="checkbox"/> Open Annulus |
| Cementing | <input type="checkbox"/> Contingency Cement Squeeze | <input type="checkbox"/> EchoMeter | <input type="checkbox"/> Primary Cement Squeeze |
| Special Requirements | <input type="checkbox"/> Water Disposal | <input checked="" type="checkbox"/> COM | <input type="checkbox"/> Unit |
| Special Requirements | <input type="checkbox"/> Batch Sundry | | |
| Special Requirements Variance | <input checked="" type="checkbox"/> Break Testing | <input type="checkbox"/> Offline Cementing | <input type="checkbox"/> Casing Clearance |

A. HYDROGEN SULFIDE

A Hydrogen Sulfide (H2S) Drilling Plan shall be activated 500 feet prior to drilling into the **Delaware Group** formation. As a result, the Hydrogen Sulfide area must meet all requirements from **43 CFR 3176**, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, please provide measured values and formations to the BLM.

B. CASING

1. The **13-3/8** inch surface casing shall be set at approximately **300** feet (a minimum of **70 feet (Eddy County)** into the Rustler Anhydrite, above the salt, and below usable fresh water) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type of

temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.

- b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The minimum required fill of cement behind the **9-5/8** inch intermediate casing is:
 - Cement to surface. If cement does not circulate see B.1.a, c-d above.

Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst.

 - ❖ In Medium Cave/Karst Areas if cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface.
 3. The minimum required fill of cement behind the **7** inch production casing is:
 - Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst.
 4. The minimum required fill of cement behind the **5 x 4-1/2** inch production liner is:
 - Cement should tie-back **100 feet** into the previous casing. Operator shall provide method of verification.

C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).
2. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.

- c. Manufacturer representative shall install the test plug for the initial BOP test.
- d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
- e. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172 must be followed.

D. SPECIAL REQUIREMENT (S)

Communitization Agreement

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- The operator will submit an as-drilled survey well plat of the well completion, but are not limited to, those specified in **43 CFR 3171 and 3172**.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

(Note: For a minimum 5M BOPE or less (Utilizing a 10M BOPE system))

BOPE Break Testing Variance

- BOPE Break Testing is ONLY permitted for 5M BOPE or less. **(Annular preventer must be tested to a minimum of 70% of BOPE working pressure and shall be higher than the MASP)**
- BOPE Break Testing is NOT permitted to drilling the production hole section.
- Variance only pertains to the intermediate hole-sections and no deeper than the Bone Springs formation.
- While in transfer between wells, the BOPE shall be secured by the hydraulic carrier or cradle.
- Any well control event while drilling require notification to the BLM Petroleum Engineer **(575-706-2779)** prior to the commencement of any BOPE Break Testing operations.
- A full BOPE test is required prior to drilling the first deep intermediate hole section. If any subsequent hole interval is deeper than the first, a full BOPE test will be required. (200' TVD tolerance between intermediate shoes is allowable).
- The BLM is to be contacted **(575-361-2822 Eddy County)** 4 hours prior to BOPE tests.
- As a minimum, a full BOPE test shall be performed at 21-day intervals.

- In the event any repairs or replacement of the BOPE is required, the BOPE shall test as per must meet all requirements from **43 CFR 3172**.
- If in the event break testing is not utilized, then a full BOPE test would be conducted.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Eddy County

Email **or** call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220, BLM_NM_CFO_DrillingNotifications@BLM.GOV
(575) 361-2822

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240,
(575) 689-5981

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - Notify the BLM when moving in and removing the Spudder Rig.
 - Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - BOP/BOPE test to be conducted per **43 CFR part 3170 Subpart 3172** as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.

3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a

larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.

8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in **43 CFR part 3170 Subpart 3172** and **API STD 53 Sec. 5.3**.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. Whenever any seal subject to test pressure is broken, all the tests in **43 CFR part 3170 Subpart 3172** must be followed.
 - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.

5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead cement), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the cement plug. The BOPE test can be initiated after bumping the cement plug with the casing valve open. (only applies to single stage cement jobs, prior to the cement setting up.)
 - c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer and can be initiated immediately with the casing valve open. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to **43 CFR part 3170 Subpart 3172** with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
 - d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
 - e. The results of the test shall be reported to the appropriate BLM office.
 - f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.

- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per **43 CFR part 3170 Subpart 3172**.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

ZS 7/19/2023



H₂S Preparedness and Contingency Plan Summary

Training

MCBU Drilling and Completions H₂S training requirements are intended to define the minimum level of training required for employees, contractors and visitors to enter or perform work at MCBU Drilling and Completions locations that have known concentrations of H₂S.

Awareness Level

Employees and visitors to MCBU Drilling and Completions locations that have known concentrations of H₂S, who are not required to perform work in H₂S areas, will be provided with an awareness level of H₂S training prior to entering any H₂S areas. At a minimum, awareness level training will include:

1. Physical and chemical properties of H₂S
2. Health hazards of H₂S
3. Personal protective equipment
4. Information regarding potential sources of H₂S
5. Alarms and emergency evacuation procedures

Awareness level training will be developed and conducted by personnel who are qualified either by specific training, educational experience and/or work-related background.

Advanced Level H₂S Training

Employees and contractors required to work in areas that may contain H₂S will be provided with Advanced Level H₂S training prior to initial assignment. In addition to the Awareness Level requirements, Advanced Level H₂S training will include:

1. H₂S safe work practice procedures;
2. Emergency contingency plan procedures;
3. Methods to detect the presence or release of H₂S (e.g., alarms, monitoring equipment), including hands-on training with direct reading and personal monitoring H₂S equipment.
4. Basic overview of respiratory protective equipment suitable for use in H₂S environments. Note: Employees who work at sites that participate in the Chevron Respirator User program will require separate respirator training as required by the MCBU Respiratory Protection Program;
5. Basic overview of emergency rescue techniques, first aid, CPR and medical evaluation procedures. Employees who may be required to perform "standby" duties are required to receive additional first aid and CPR training, which is not covered in the Advanced Level H₂S training;
6. Proficiency examination covering all course material.

Advanced H₂S training courses will be instructed by personnel who have successfully completed an appropriate H₂S train-the-trainer development course (ANSI/ASSE Z390.1-2006) or who possess significant past experience through educational or work-related background.



H₂S Preparedness and Contingency Plan Summary

H₂S Training Certification

All employees and visitors will be issued an H₂S training certification card (or certificate) upon successful completion of the appropriate H₂S training course. Personnel working in an H₂S environment will carry a current H₂S training certification card as proof of having received the proper training on their person at all times.

Briefing Area

A minimum of two briefing areas will be established in locations that at least one area will be upwind from the well at all times. Upon recognition of an emergency situation, all personnel should assemble at the designated upwind briefing areas for instructions.

H₂S Equipment

Respiratory Protection

- a) Six 30 minute SCBAs – 2 at each briefing area and 2 in the Safety Trailer.
- b) Eight 5 minute EBAs – 5 in the dog house at the rig floor, 1 at the accumulator, 1 at the shale shakers and 1 at the mud pits.

Visual Warning System

- a) One color code sign, displaying all possible conditions, will be placed at the entrance to the location with a flag displaying the current condition.
- b) Two windsocks will be on location, one on the dog house and one on the Drill Site Manager's Trailer.

H₂S Detection and Monitoring System

- a) H₂S monitoring system (sensor head, warning light and siren) placed throughout rig.
 - Drilling Rig Locations: at a minimum, in the area of the Shale shaker, rig floor, and bell nipple.
 - Workover Rig Locations: at a minimum, in the area of the Cellar, rig floor and circulating tanks or shale shaker.



H₂S Preparedness and Contingency Plan Summary

Well Control Equipment

- a) Flare Line 150' from wellhead with igniter.
- b) Choke manifold with a remotely operated choke.
- c) Mud / gas separator

Mud Program

In the event of drilling, completions, workover and well servicing operations involving a hydrogen sulfide concentration of 100 ppm or greater the following shall be considered:


- 1. Use of a degasser
- 2. Use of a zinc based mud treatment
- 3. Increasing mud weight


Public Safety - Emergency Assistance

| <u>Agency</u> | <u>Telephone Number</u> |
|----------------------------------|-------------------------|
| Eddy County Sheriff's Department | 575-887-7551 |
| Carlsbad Fire Department | 575-885-3125 |
| Carlsbad Medical Center | 575-887-4100 |
| Eddy County Emergency Management | 575-885-3581 |
| Poison Control Center | 800-222-1222 |



H₂S Preparedness and Contingency Plan Summary

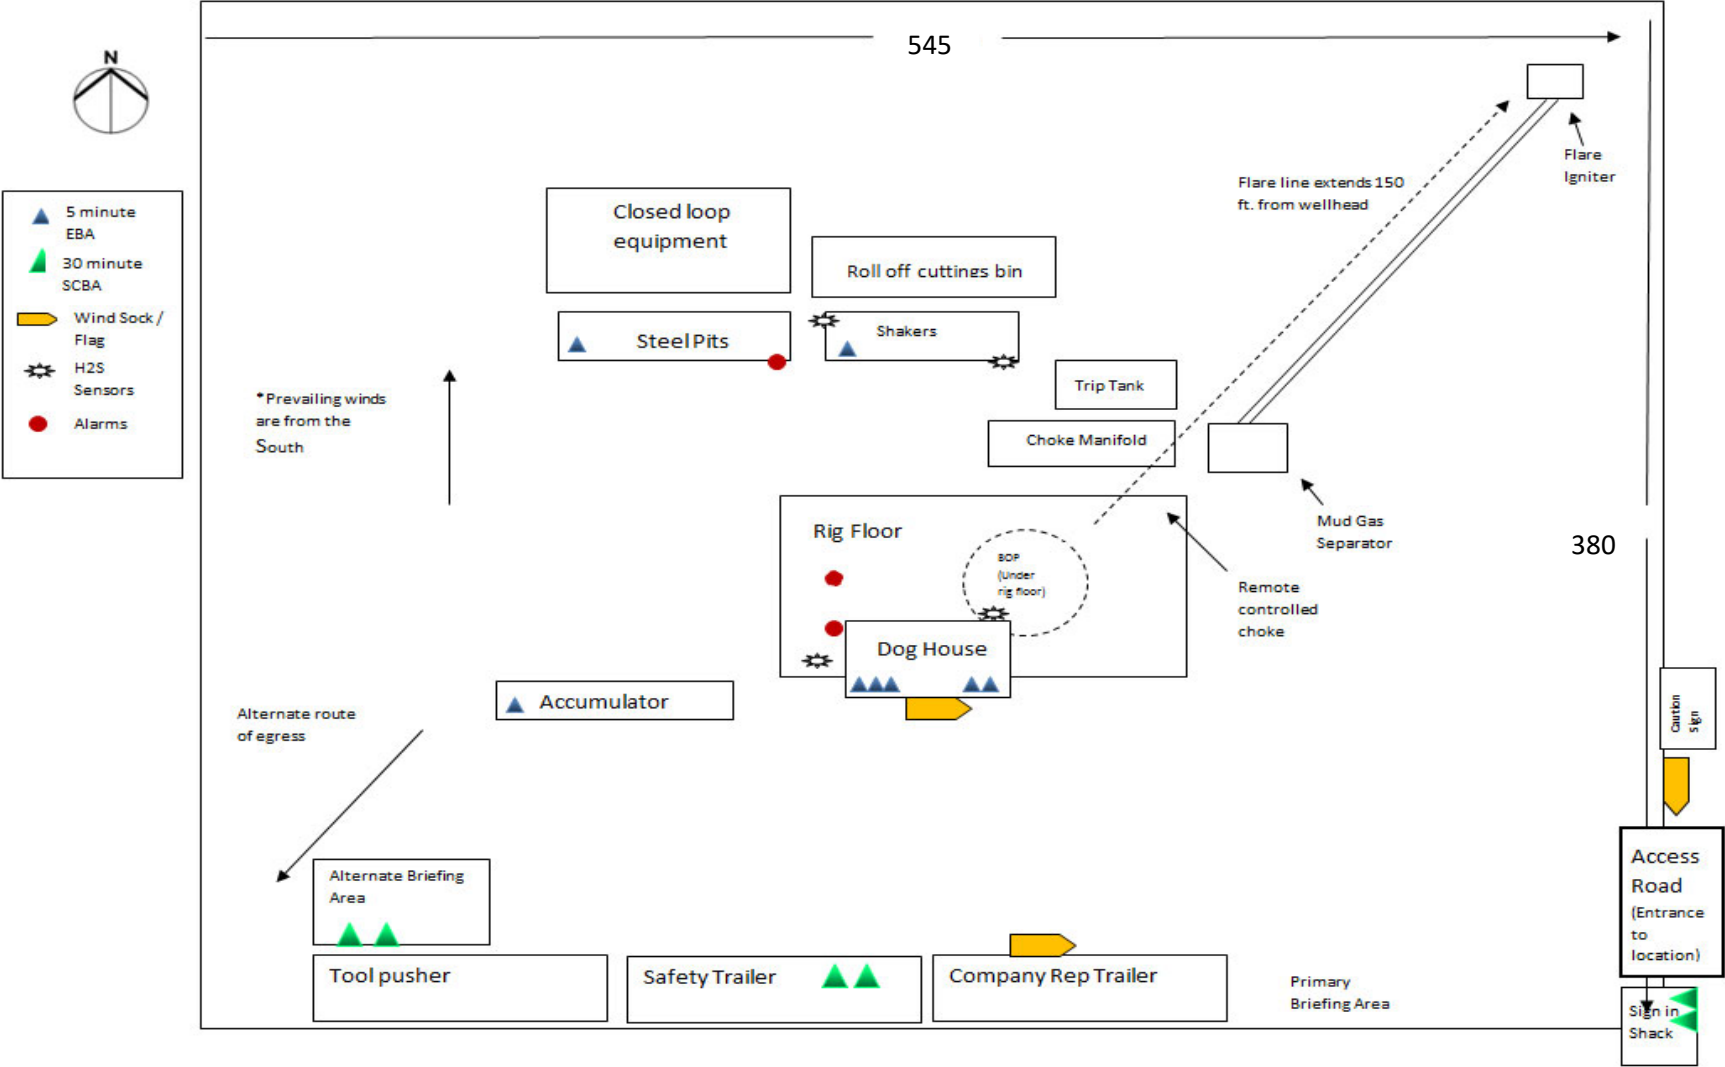

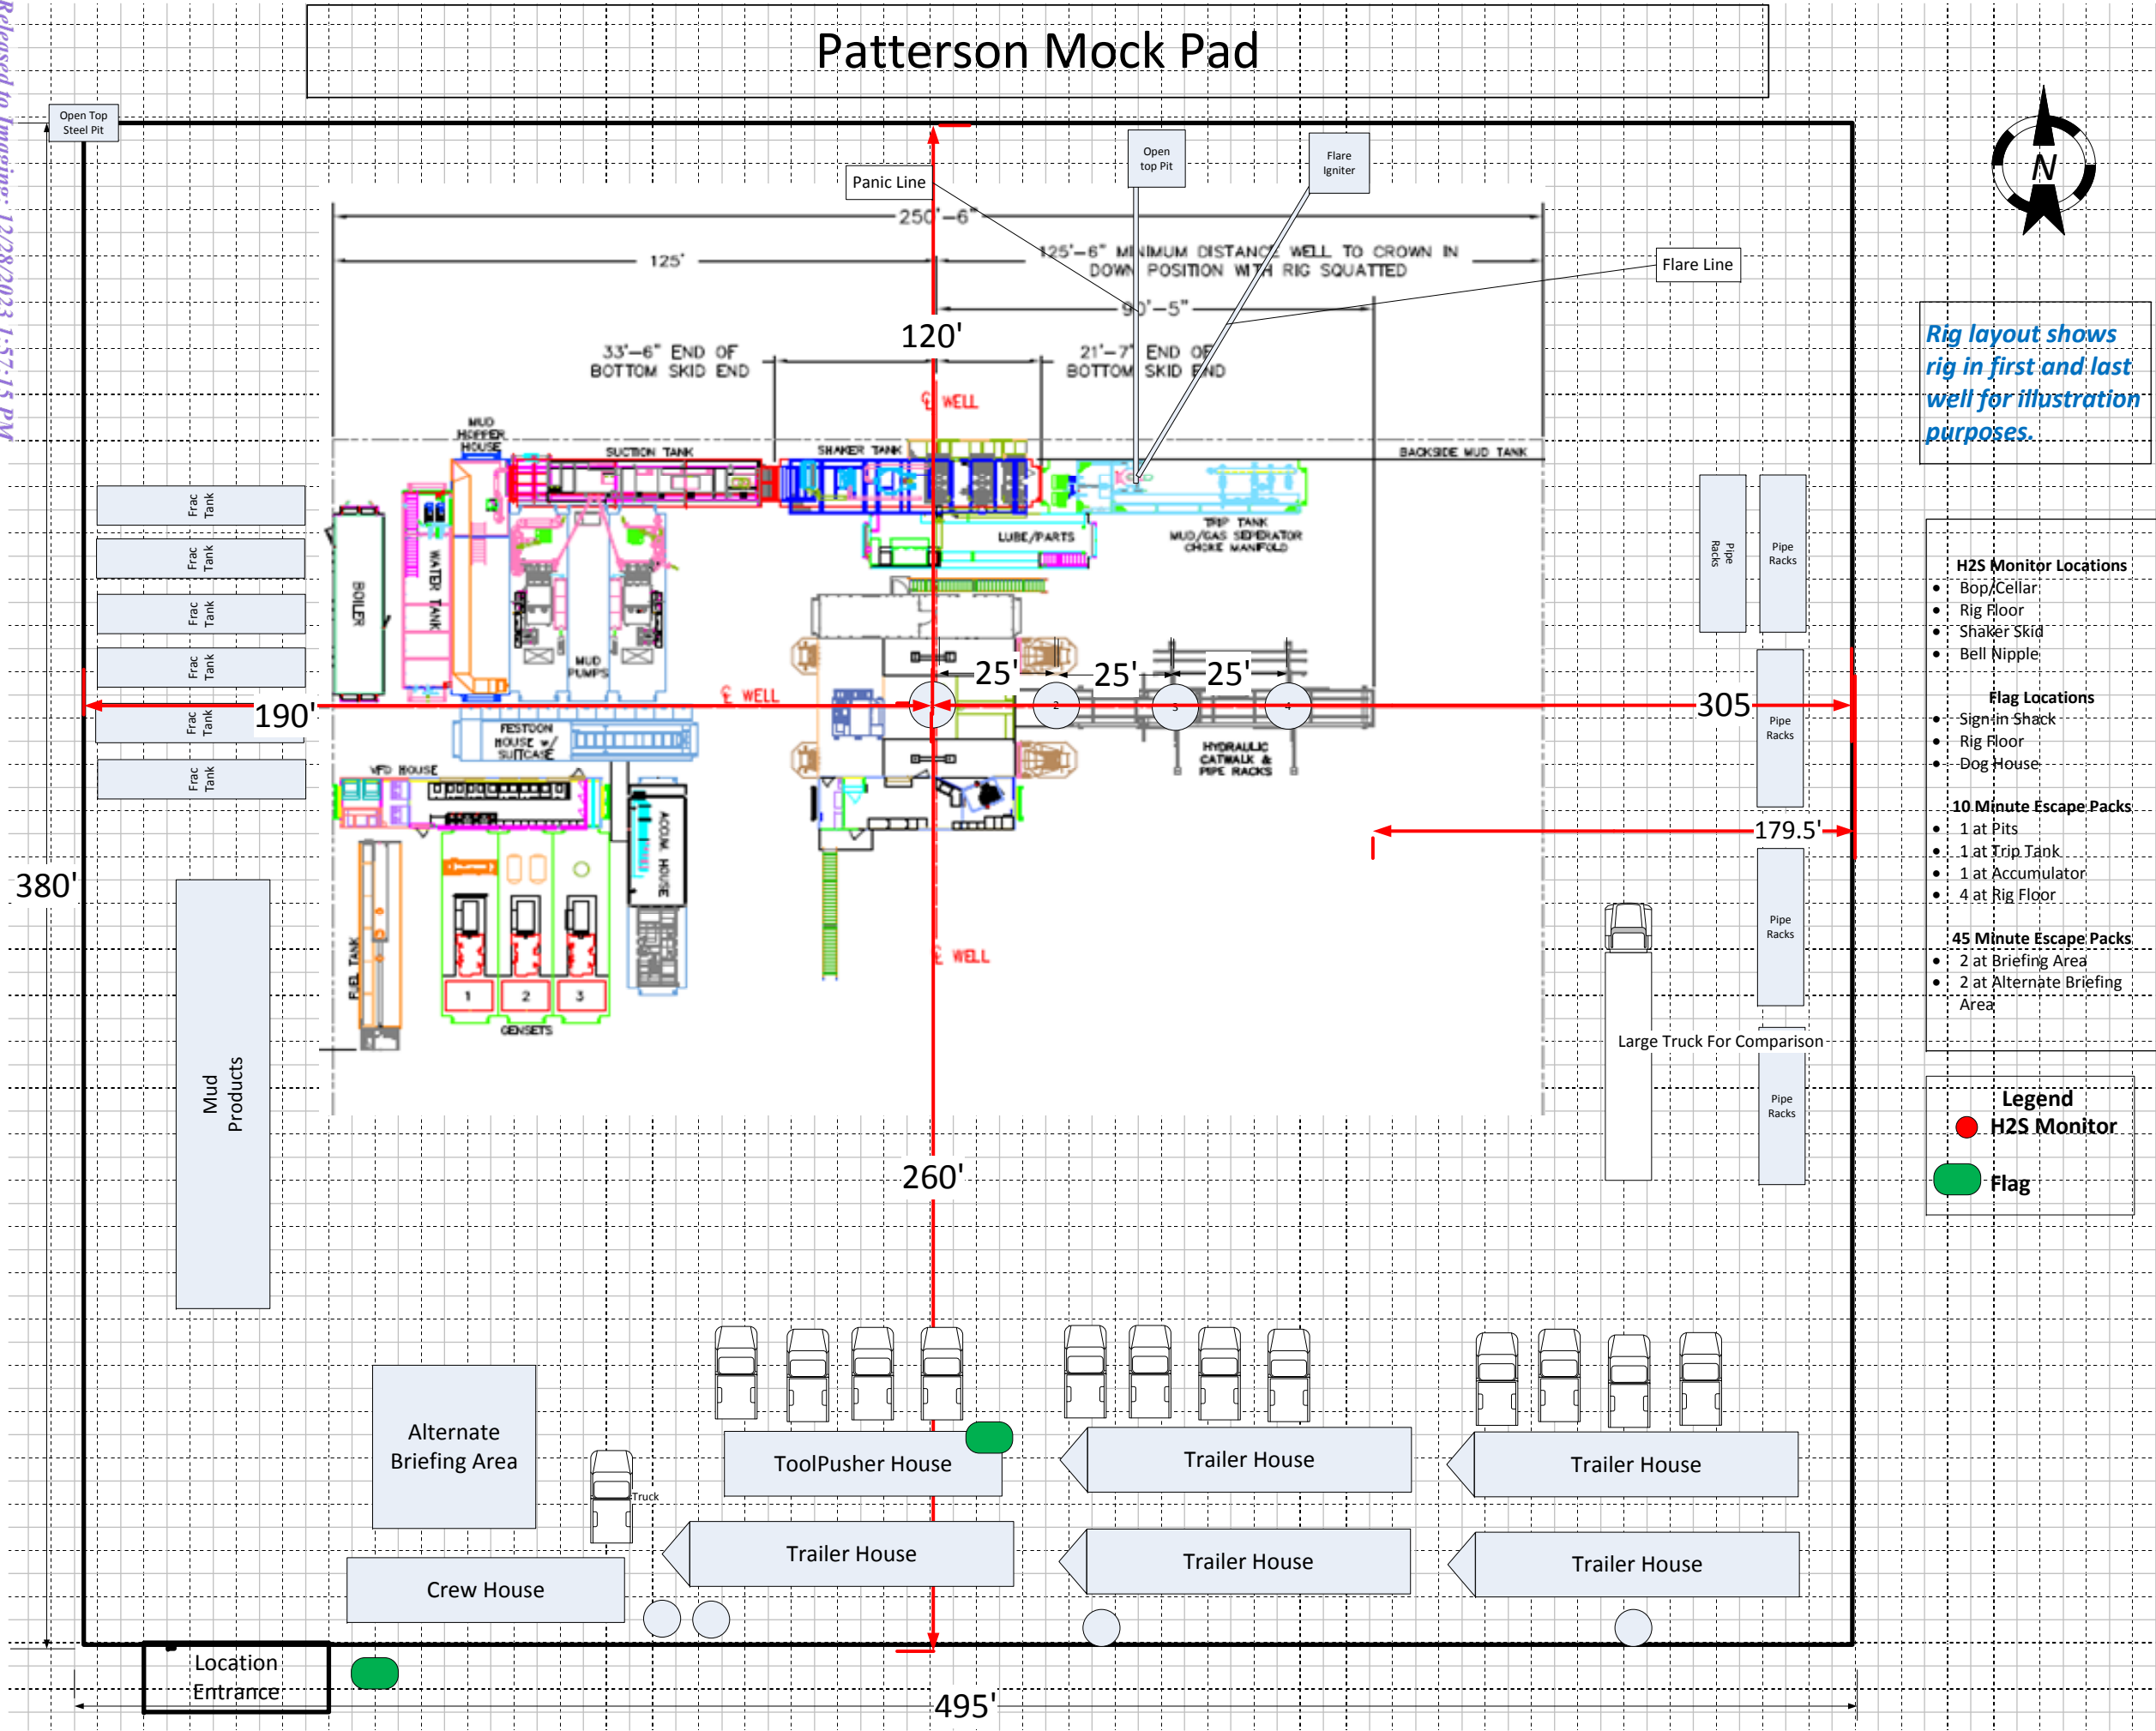

Intent ☐ As Drilled ☐

| | | |
|----------------|----------------|-------------|
| API # | | |
| Operator Name: | Property Name: | Well Number |

Kick Off Point (KOP)

| | | | | | | | | | |
|----------|---------|----------|-------|-----|-----------|----------|------|----------|--------|
| UL | Section | Township | Range | Lot | Feet | From N/S | Feet | From E/W | County |
| Latitude | | | | | Longitude | | | | NAD |

First Take Point (FTP)

| | | | | | | | | | |
|----------|---------|----------|-------|-----|-----------|----------|------|----------|--------|
| UL | Section | Township | Range | Lot | Feet | From N/S | Feet | From E/W | County |
| Latitude | | | | | Longitude | | | | NAD |

Last Take Point (LTP)

| | | | | | | | | | |
|----------|---------|----------|-------|-----|-----------|----------|------|----------|--------|
| UL | Section | Township | Range | Lot | Feet | From N/S | Feet | From E/W | County |
| Latitude | | | | | Longitude | | | | NAD |

Is this well the defining well for the Horizontal Spacing Unit? ☐Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

| | | |
|----------------|----------------|-------------|
| API # | | |
| Operator Name: | Property Name: | Well Number |



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Drilling Plan Data Report

11/29/2023

APD ID: 10400086546

Submission Date: 07/06/2022

Highlighted data
reflects the most
recent changes

Operator Name: CHEVRON USA INCORPORATED

Well Name: CB AMILYN 10 3 FED COM P13

Well Number: 401H

Well Type: CONVENTIONAL GAS WELL

Well Work Type: Drill

[Show Final Text](#)

Section 1 - Geologic Formations

| Formation ID | Formation Name | Elevation | True Vertical | Measured Depth | Lithologies | Mineral Resources | Producing Formatio |
|--------------|------------------|-----------|---------------|----------------|---------------------------------|-------------------|--------------------|
| 12520882 | SALADO | 0 | 328 | 328 | ANHYDRITE, SALT | NONE | N |
| 12520883 | CASTILE | -953 | 953 | 953 | ANHYDRITE, SALT | NONE | N |
| 12520884 | LAMAR | -2555 | 2555 | 2604 | LIMESTONE, SHALE | NONE | N |
| 12520885 | BELL CANYON | -2597 | 2597 | 2648 | LIMESTONE, SANDSTONE | NONE | N |
| 12520886 | CHERRY CANYON | -3434 | 3434 | 3514 | LIMESTONE, SANDSTONE, SILTSTONE | NONE | N |
| 12520887 | BRUSHY CANYON | -4471 | 4471 | 4588 | LIMESTONE, SANDSTONE, SHALE | NONE | N |
| 12520888 | BONE SPRING LIME | -6141 | 6141 | 6290 | SHALE, SILTSTONE | NONE | N |
| 12520889 | AVALON SAND | -6214 | 6214 | 6363 | SHALE | NONE | N |
| 12520890 | BONE SPRING 1ST | -7175 | 7175 | 7325 | SANDSTONE, SHALE | NONE | N |
| 12520891 | BONE SPRING 2ND | -7673 | 7673 | 7823 | SANDSTONE, SHALE | NATURAL GAS, OIL | N |
| 12520892 | BONE SPRING 3RD | -9071 | 9071 | 9221 | SANDSTONE, SHALE | NATURAL GAS, OIL | N |
| 12520893 | WOLFCAMP | -9407 | 9407 | 9611 | SANDSTONE, SHALE | NATURAL GAS, OIL | Y |

Section 2 - Blowout Prevention

Pressure Rating (PSI): 5M

Rating Depth: 9562

Equipment: Chevron will have a minimum of a 5,000 psi rig stack (see proposed schematic) for drill out below surface casing.

Requesting Variance? YES

Variance request: Chevron request to vary from the Onshore Order 2 where it states: "(A full BOP Test) shall be performed: when initially installed and whenever any seal subject to test pressure is broken." We propose to break test if able to finish the next hole section within 21 days of the previous full BOP test. No BOP components nor any break will ever surpass 21 days between testing. A break test will consist of a 250

BLOWOUT PREVENTOR SCHEMATIC

Minimum Requirements

OPERATION : Intermediate and Production Hole Sections

Minimum System Pressure Rating : 5,000 psi


| SIZE | PRESSURE | DESCRIPTION |
|-------|--------------------------------|-------------|
| A | N/A | Bell Nipple |
| B | 13 5/8" 5,000 psi | Annular |
| C | 13 5/8" 5,000 psi | Pipe Ram |
| D | 13 5/8" 5,000 psi | Blind Ram |
| E | 13 5/8" 5,000 psi | Mud Cross |
| F | | |
| DSA | As required for each hole size | |
| C-Sec | | |
| B-Sec | 13-5/8" 5K x 11" 5K | |
| A-Sec | 13-3/8" SOW x 13-5/8" 5K | |

Kill Line

| SIZE | PRESSURE | DESCRIPTION |
|------|-----------|-------------|
| 2" | 5,000 psi | Gate Valve |
| 2" | 5,000 psi | Gate Valve |
| 2" | 5,000 psi | Check Valve |
| | | |
| | | |

Choke Line

| SIZE | PRESSURE | DESCRIPTION |
|------|-----------|-------------|
| 3" | 5,000 psi | Gate Valve |
| 3" | 5,000 psi | HCR Valve |
| | | |
| | | |
| | | |

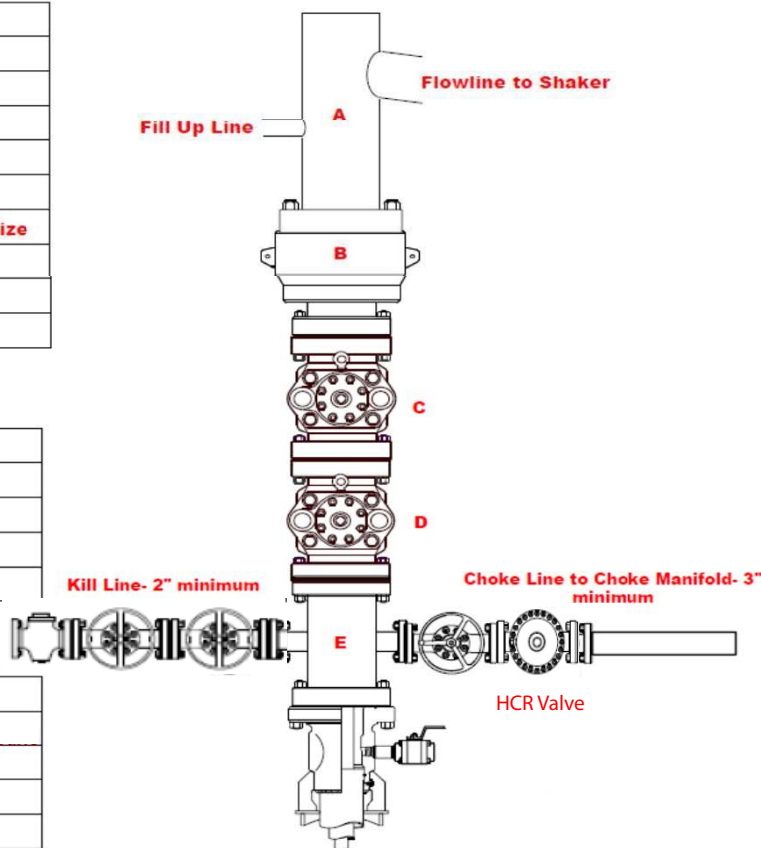

Installation Checklist

The following item must be verified and checked off prior to pressure testing of BOP equipment.

- ☐ The installed BOP equipment meets at least the minimum requirements (rating, type, size, configuration) as shown on this schematic. Components may be substituted for equivalent equipment rated to higher pressures. Additional components may be put into place as long as they meet or exceed the minimum pressure rating of the system.
- ☐ All valves on the kill line and choke line will be full opening and will allow straight through flow.
- ☐ The kill line and choke line will be straight unless turns use tee blocks or are targeted with running tress, and will be anchored to prevent whip and reduce vibration.
- ☐ Manual (hand wheels) or automatic locking devices will be installed on all ram preventers. Hand wheels will also be installed on all manual valves on the choke line and kill line.
- ☐ A valve will be installed in the closing line as close as possible to the annular preventer to act as a locking device. This valve will remain open unless accumulator is inoperative.
- ☐ Upper kelly cock valve with handle will be available on rig floor along with safety valve and subs to fit all drill string connections in use.

After Installation Checklist is complete, fill out the information below and email to Superintendent and Drilling Engineer

Wellname: _____

Representative: _____

Date: _____

CHOKE MANIFOLD SCHEMATIC


Minimum Requirements

OPERATION : Intermediate and Production Hole Sections

Minimum System
Pressure Rating : **5,000 psi**

Choke Manifold

| SIZE | PRESSURE | DESCRIPTION |
|------|-----------|-----------------------|
| 3" | 5,000 psi | Panic Line Valves |
| 2" | 5,000 psi | Valves on Choke Lines |
| | | |
| | | |
| | | |

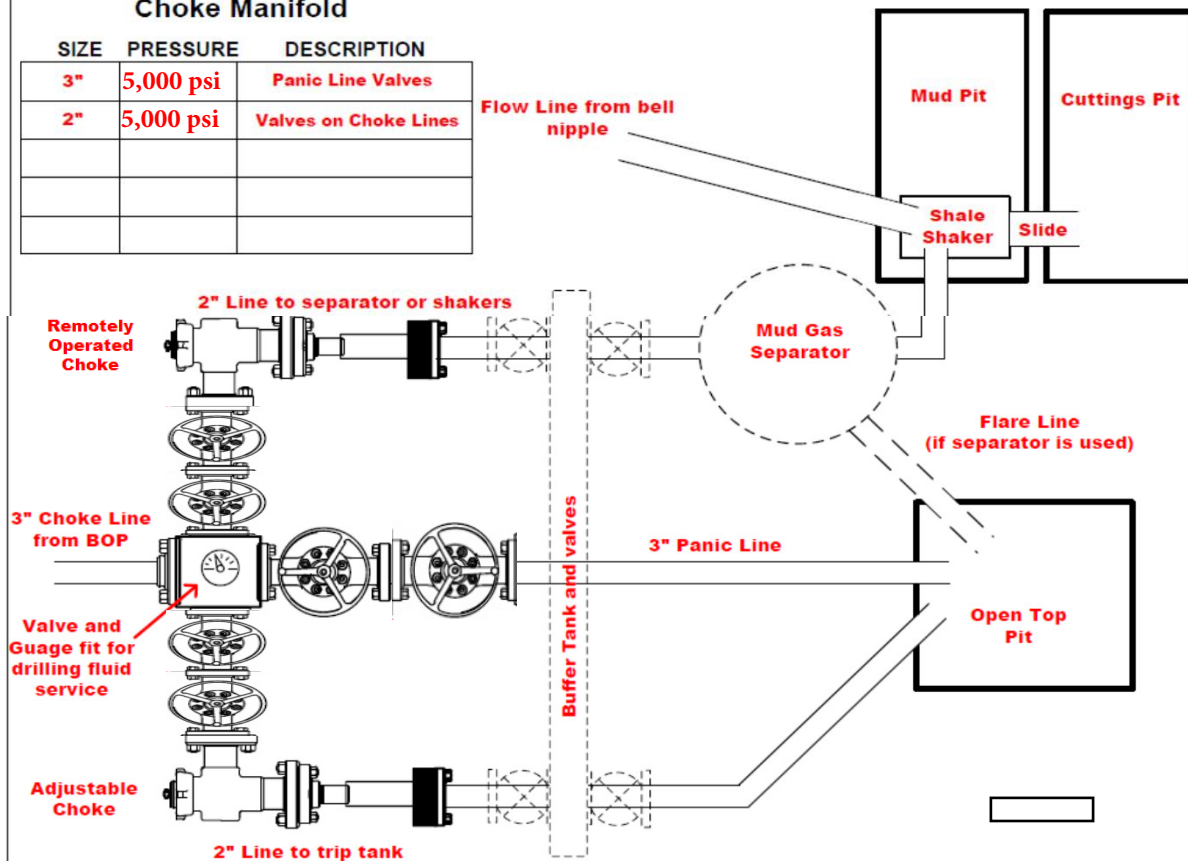

Installation Checklist

The following item must be verified and checked off prior to pressure testing of BOP equipment.

- ☐ The installed BOP equipment meets at least the minimum requirements (rating, type, size, configuration) as shown on this schematic. Components may be substituted for equivalent equipment rated to higher pressures. Additional components may be put into place as long as they meet or exceed the minimum pressure rating of the system.
- ☐ Adjustable Chokes may be Remotely Operated but will have backup hand pump for hydraulic actuation in case of loss of rig air pressure or power.
- ☐ Flare and Panic lines will terminate a minimum of 150' from the wellhead. These lines will terminate at a location as per approved APD.
- ☐ The choke line, kill line, and choke manifold lines will be straight unless turns use tee blocks or are targeted with running tress, and will be anchored to prevent whip and reduce vibration. This excludes the line between mud gas separator and shale shaker.
- ☐ All valves (except chokes) on choke line, kill line, and choke manifold will be full opening and will allow straight through flow. This excludes any valves between mud gas separator and shale shakers.
- ☐ All manual valves will have hand wheels installed.
- ☐ If used, flare system will have effective method for ignition
- ☐ All connections will be flanged, welded, or clamped (no threaded connections like hammer unions)
- ☐ If buffer tank is used, a valve will be used on all lines at any entry or exit point to or from the buffer tank.

After Installation Checklist is complete, fill out the information below and email to Superintendent and Drilling Engineer

Wellname: _____

Representative: _____

Date: _____

Chevron BOPE Testing – 5K and 10K Systems

Minimum Requirements

Closing Unit and Accumulator Checklist

The following item must be performed, verified, and checked off at least once per well prior to low/high pressure testing of BOP equipment. This must be repeated after 6 months on the same well.

- ☐ Precharge pressure for each accumulator bottle must fall within the range below. Bottles may be further charged with nitrogen gas only. **Tested precharge pressures must be recorded for each individual bottle and kept on location through the end of the well. Test will be conducted prior to connecting unit to BOP stack.**

| Check one that applies | Accumulator working pressure rating | Minimum acceptable operating pressure | Desired precharge pressure | Maximum acceptable precharge pressure | Minimum acceptable precharge pressure |
|--------------------------|-------------------------------------|---------------------------------------|----------------------------|---------------------------------------|---------------------------------------|
| <input type="checkbox"/> | 1500 psi | 1500 psi | 750 psi | 800 psi | 700 psi |
| <input type="checkbox"/> | 2000 psi | 2000 psi | 1000 psi | 1100 psi | 900 psi |
| <input type="checkbox"/> | 3000 psi | 3000 psi | 1000 psi | 1100 psi | 900 psi |

- ☐ Accumulator will have sufficient capacity to open the hydraulically-controlled choke line valve (if used), close all rams, close the annular preventer, and retain a minimum of 200 psi above the maximum acceptable precharge pressure (see table above) on the closing manifold without the use of the closing pumps. **This test will be performed with test pressure recorded and kept on location through the end of the well**
- ☐ Accumulator fluid reservoir will be double the usable fluid volume of the accumulator system capacity. Fluid level will be maintained at manufacturer's recommendations. **Usable fluid volume will be recorded. Reservoir capacity will be recorded. Reservoir fluid level will be recorded along with manufacturer's recommendation. All will be kept on location through the end of the well.**
- ☐ Closing unit system will have two independent power sources (not counting accumulator bottles) to close the preventers.
- ☐ Power for the closing unit pumps will be available to the unit at all times so that the pumps will automatically start when the closing valve manifold pressure decreases to the pre-set level. **It is recommended to check that air line to accumulator pump is "ON" during each tour change.**
- ☐ With accumulator bottles isolated, closing unit will be capable of opening the hydraulically-operated choke line valve (if used) plus close the annular preventer on the smallest size drill pipe within 2 minutes and obtain a minimum of 200 psi above maximum acceptable precharge pressure (see table above) on the closing manifold. **Test pressure and closing time will be recorded and kept on location through the end of the well.**
- ☐ Master controls for the BOPE system will be located at the accumulator and will be capable of opening and closing all preventer and the choke line valve (if used)
- ☐ Remote controls for the BOPE system will be readily accessible (clear path) to the driller and located on the rig floor (not in the dog house). Remote controls will be capable of closing all preventers.
- ☐ Record accumulator tests in drilling reports and IADC sheet

BOPE 5K Test Checklist

The following items must be checked off prior to beginning test:

- ☐ BLM will be given at least 4 hour notice prior to beginning BOPE testing.
- ☐ Valve on casing head below test plug will be open.
- ☐ Test will be performed using clear water.

The following items must be performed during the BOPE testing:

- ☐ BOPE will be pressure tested when initially installed, whenever any seal subject to test pressure is broken, following related repairs, and at a minimum of 30 day intervals. **Test pressure and times will be recorded by a 3rd party on a test charge and kept on location through the end of the well.**
- ☐ Test plug will be used.
- ☐ Ram type preventer and all related well control equipment will be tested to 250 psi (low) and 5,000 psi (high).
- ☐ Annular type preventer will be tested to 250 psi (low) and 3,500 psi (high).
- ☐ Valves will be tested from the working pressure side with all downstream valves open. The check valve will be held open to test the kill line valve(s).
- ☐ Each pressure test will be held for 10 minutes with no allowable leak off.
- ☐ Master controls and remote controls to the closing unit (accumulator) must be function tested as part of the BOPE test.
- ☐ Record BOP tests and pressures in drilling reports and IADC sheet.

BOPE 10K (with 5K annular) Test Checklist

The following items must be checked off prior to beginning test:


- ☐ BLM will be given at least 4 hour notice prior to beginning BOPE testing.
- ☐ Valve on casing head below test plug will be open.
- ☐ Test will be performed using clear water.

The following items must be performed during the BOPE testing:

- ☐ BOPE will be pressure tested when initially installed, whenever any seal subject to test pressure is broken, following related repairs, and at a minimum of 30 day intervals. **Test pressure and times will be recorded by a 3rd party on a test charge and kept on location through the end of the well.**
- ☐ Test plug will be used.
- ☐ Ram type preventer and all related well control equipment will be tested to 250 psi (low) and 7,500 psi (high).
- ☐ Annular type preventer will be tested to 250 psi (low) and 5,000 psi (high).
- ☐ Valves will be tested from the working pressure side with all downstream valves open. The check valve will be held open to test the kill line valve(s).
- ☐ Each pressure test will be held for 10 minutes with no allowable leak off.
- ☐ Master controls and remote controls to the closing unit (accumulator) must be function tested as part of the BOPE test.
- ☐ Record BOP tests and pressures in drilling reports and IADC sheet.

CHOKE MANIFOLD SCHEMATIC

| | | | |
|-----------------------------------|------|---------------------------|--------------------------------|
| Operation: | | Intermediate & Production | |
| Minimum System operation pressure | | 5,000 psi | |
| <u>Choke Manifold</u> | | | |
| Part | Size | Pressure Rating | Description |
| A | 3" | 10,000 | HCR (remotely operated) |
| B | 3" | 10,000 | HCR (manually operated) |
| C | 2" | 10,000 | Remotely operated choke |
| D | 2" | 10,000 | Adjustable choke |
| E | 3" | 10,000 | Crown valve with pressure gage |
| F | 3" | 10,000 | Panic line valves |

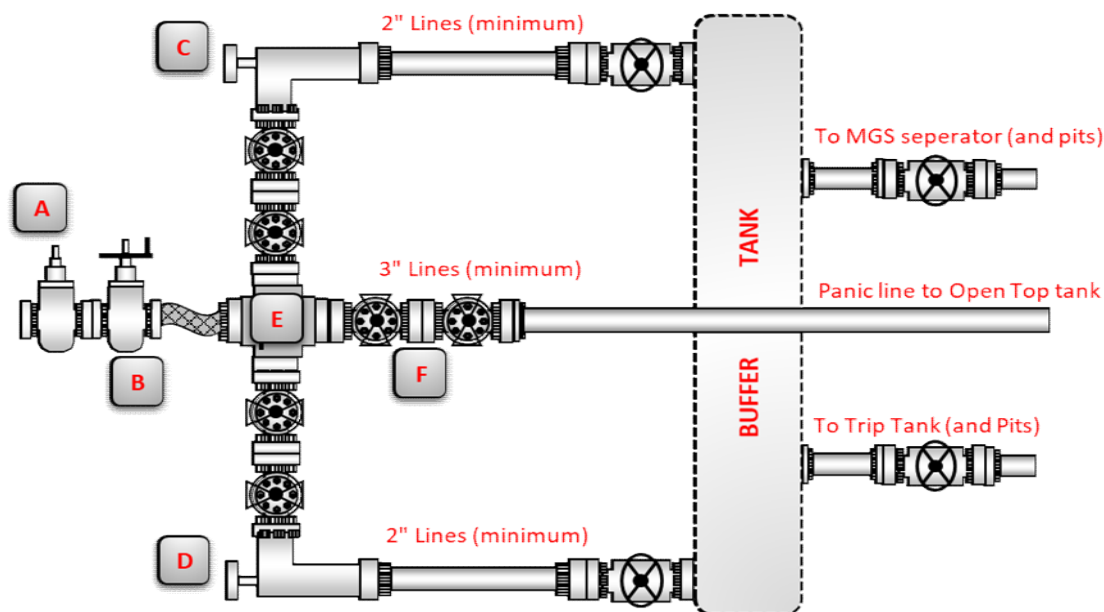

Choke Manifold Installation Checklist: The following items must be verified and checked off prior to pressure testing BOP equipment

The installed BOP equipment meets at least the minimum requirements (rating, type, size, configuration) as shown on this schematic. Components may be substituted for equivalent equipment rated to higher pressures. Additional components may be put into place as long as they meet or exceed the minimum pressure rating of the system.

Adjustable chokes may be remotely operated but will have backup hand pump for hydraulic actuation in case of loss of rig air or power.

Flare and panic lines will terminate a minimum of 150' from the wellhead. These lines will terminate at a location as per approved APD.


All valves (except chokes) on choke line, kill line and choke manifold will be full opening and will allow straight through flow. This excludes any valves between the mud gas separator and shale shakers.

All manual valves will have hand wheels installed.

Flare systems will have an effective method for ignition.

All connections will be flanged, welded or clamped

If buffer tank is used, a valve will be used on all lines at any entry or exit point to or from the buffer tank.

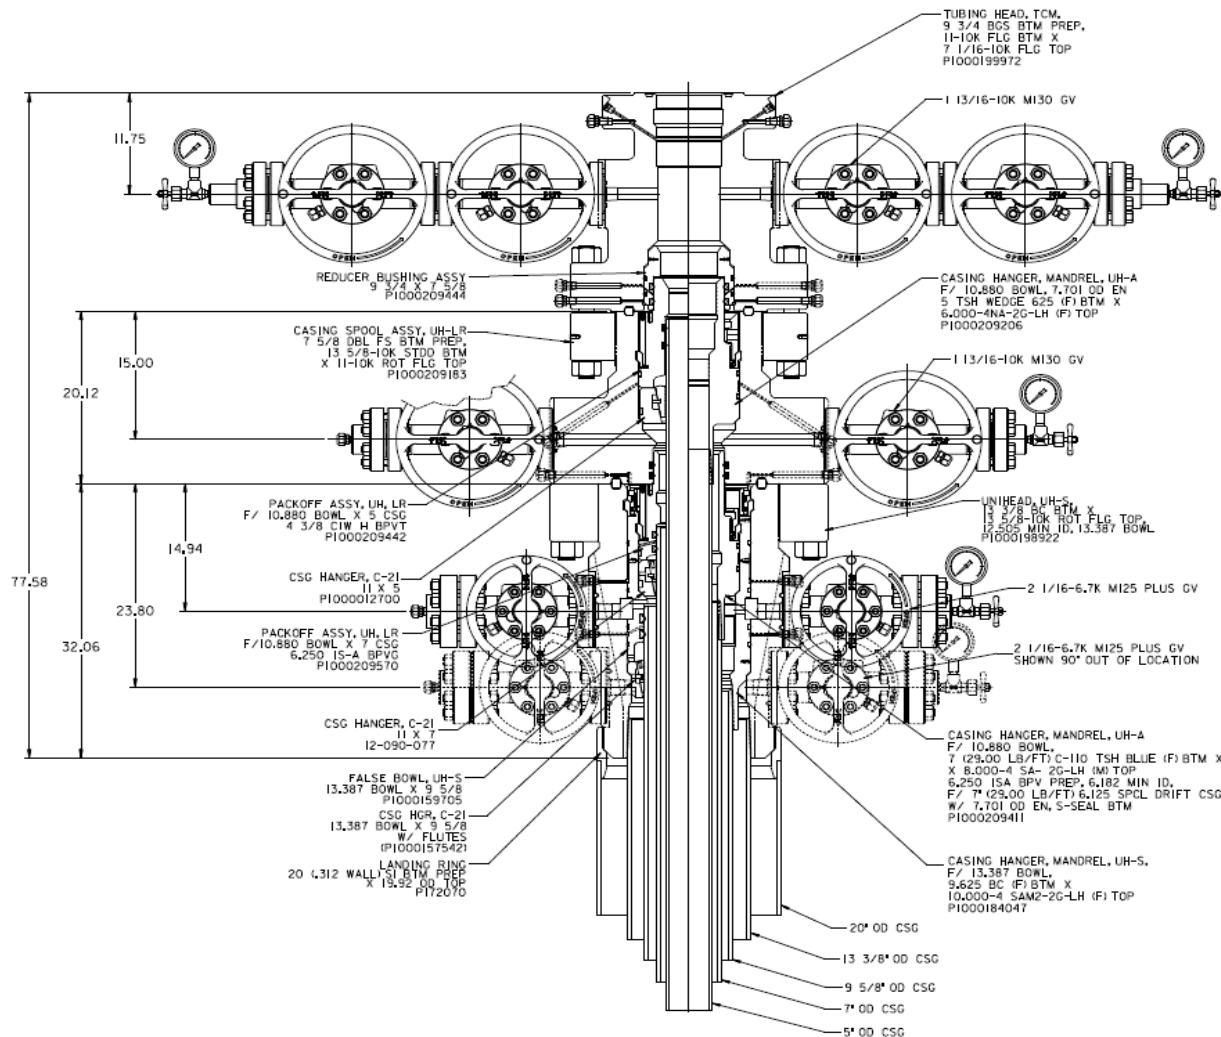

PRODUCTION MODE

6650 PSI UH-S

CHEVRON

20 X 13 3/8 X 9 5/8 X 7 X 5

NEW MEXICO SLIM HOLE


QUOTE# 20395747
CASE# 00225966
F111378
08010163394
REF# 0M100312054
0M100276064

BLOWOUT PREVENTER SCHEMATIC

| | |
|-----------------------------------|---|
| Operation: | Intermediate & Production Drilling Operations |
| Minimum System operation pressure | 5,000 psi |

| BOP Stack | | | |
|-----------|---------|-----------------|--------------------------------------|
| Part | Size | Pressure Rating | Description |
| A | 13-5/8" | N/A | Rotating Head/Bell nipple |
| B | 13-5/8" | 5,000 | Annular |
| C | 13-5/8" | 10,000 | Blind Ram |
| D | 13-5/8" | 10,000 | Pipe Ram |
| E | 13-5/8" | 10,000 | Mud Cross |
| F | 13-5/8" | 10,000 | Pipe Ram |
| Kill Line | | | |
| Part | Size | Pressure Rating | Description |
| G | 2" | 10,000 | Inside Kill Line Valve (gate valve) |
| H | 2" | 10,000 | Outside Kill Line Valve (gate valve) |
| I | 2" | 10,000 | Kill Line Check valve |

| Choke line | | | |
|------------|---------|-----------------|-------------------------|
| Part | Size | Pressure Rating | Description |
| J | 3" | 10,000 | HCR (gate valve) |
| K | 3" | 10,000 | Manual HCR (gate valve) |
| Wellhead | | | |
| Part | Size | Pressure Rating | Description |
| L | 13-5/8" | 5,000 | FMC Multibowl wellhead |

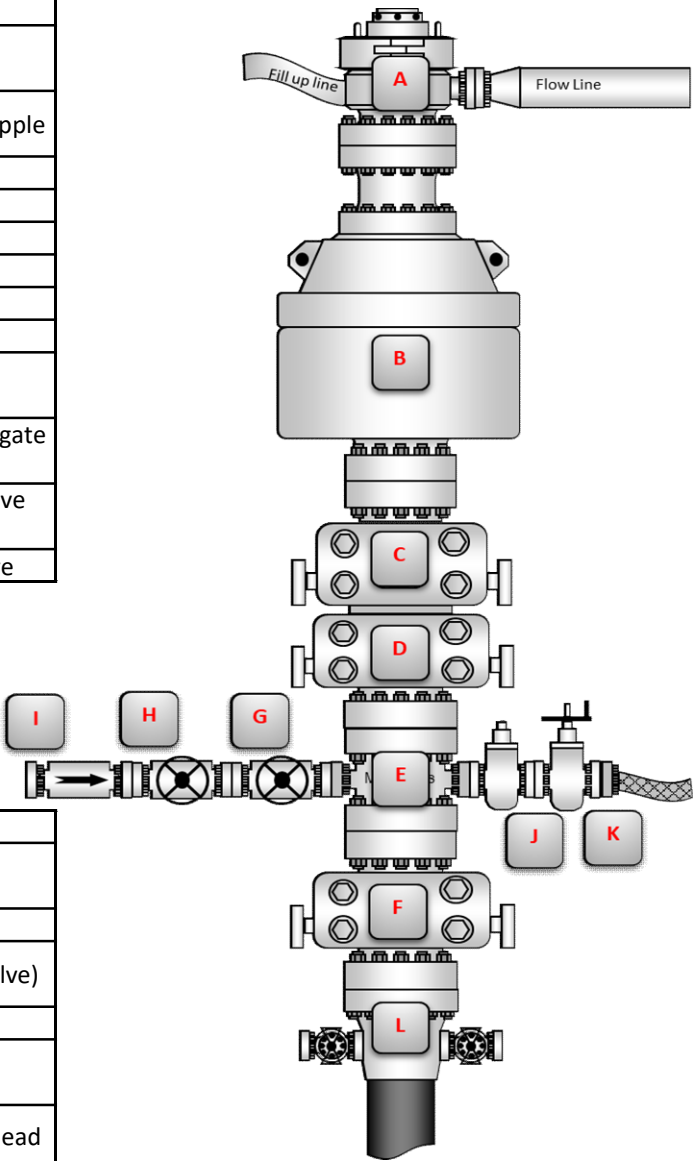

| |
|---|
| BOP Installation Checklist: The following items must be verified and checked off prior to pressure testing BOP equipment |
| The installed BOP equipment meets at least the minimum requirements (rating, type, size, configuration) as shown on this schematic. Components may be substituted for equivalent equipment rated to higher pressures. Additional components may be put into place as long as they meet or exceed the minimum pressure rating of the system. |
| All valves on the kill line and choke line will be full opening and will allow straight flow through. |
| Manual (hand wheels) or automatic locking devices will be installed on all ram preventers. Hand wheels will also be install on all manual valves on the choke and kill line. |
| A valve will be installed in the closing line as close as possible to the annular preventer to act as a locking device. This valve will remain open unless accumulator is inoperative. |
| Upper kelly cock valve with handle will be available on rig floor along with saved valve and subs to fit all drill string connections in use. |

BLOWOUT PREVENTER SCHEMATIC

Operation:

Intermediate & Production

Minimum System operation pressure

5,000 psi

Minimum Requirements

Closing Unit and Accumulator Checklist

The following item must be performed, verified, and checked off at least once per well prior to low/high pressure testing of BOP equipment. This must be repeated after 6 months on the same well.

- ☐ Precharge pressure for each accumulator bottle must fall within the range below. Bottles may be further charged with nitrogen gas only. Tested precharge pressures must be recorded for each individual bottle and kept on location through the end of the well. Test will be conducted prior to connecting unit to BOP stack.

| Check one that applies | Accumulator working pressure rating | Minimum acceptable operating pressure | Desired precharge pressure | Maximum acceptable precharge pressure | Minimum acceptable precharge pressure |
|--------------------------|-------------------------------------|---------------------------------------|----------------------------|---------------------------------------|---------------------------------------|
| <input type="checkbox"/> | 1500 psi | 1500 psi | 750 psi | 800 psi | 700 psi |
| <input type="checkbox"/> | 2000 psi | 2000 psi | 1000 psi | 1100 psi | 900 psi |
| <input type="checkbox"/> | 3000 psi | 3000 psi | 1000 psi | 1100 psi | 900 psi |

- ☐ Accumulator will have sufficient capacity to open the hydraulically-controlled choke line valve (if used), close all rams, close the annular preventer, and retain a minimum of 200 psi above the maximum acceptable precharge pressure (see table above) on the closing manifold without the use of the closing pumps. This test will be performed with test pressure recorded and kept on location through the end of the well
- ☐ Accumulator fluid reservoir will be double the usable fluid volume of the accumulator system capacity. Fluid level will be maintained at manufacturer's recommendations. Usable fluid volume will be recorded. Reservoir capacity will be recorded. Reservoir fluid level will be recorded along with manufacturer's recommendation. All will be kept on location through the end of the well.
- ☐ Closing unit system will have two independent power sources (not counting accumulator bottles) to close the preventers.
- ☐ Power for the closing unit pumps will be available to the unit at all times so that the pumps will automatically start when the closing valve manifold pressure decreases to the pre-set level. It is recommended to check that air line to accumulator pump is "ON" during each tour change.
- ☐ With accumulator bottles isolated, closing unit will be capable of opening the hydraulically-operated choke line valve (if used) plus close the annular preventer on the smallest size drill pipe within 2 minutes and obtain a minimum of 200 psi above maximum acceptable precharge pressure (see table above) on the closing manifold. Test pressure and closing time will be recorded and kept on location through the end of the well.
- ☐ Master controls for the BOPE system will be located at the accumulator and will be capable of opening and closing all preventer and the choke line valve (if used)
- ☐ Remote controls for the BOPE system will be readily accessible (clear path) to the driller and located on the rig floor (not in the dog house). Remote controls will be capable of closing all preventers.
- ☐ Record accumulator tests in drilling reports and IADC sheet

BLOWOUT PREVENTER SCHEMATIC

| | |
|-----------------------------------|---------------------------|
| Operation: | Intermediate & Production |
| Minimum System operation pressure | 5,000 psi |

BOPE 5K Test Checklist

The following items must be checked off prior to beginning test:

- ☐ BLM will be given at least 4 hour notice prior to beginning BOPE testing.
- ☐ Valve on casing head below test plug will be open.
- ☐ Test will be performed using clear water.

The following items must be performed during the BOPE testing:

- ☐ BOPE will be pressure tested when initially installed, whenever any seal subject to test pressure is broken, following related repairs, and at a minimum of 30 day intervals. **Test pressure and times will be recorded by a 3rd party on a test charge and kept on location through the end of the well.**
- ☐ Test plug will be used.
- ☐ Ram type preventer and all related well control equipment will be tested to 250 psi (low) and 5,000 psi (high).
- ☐ Annular type preventer will be tested to 250 psi (low) and 3,500 psi (high).
- ☐ Valves will be tested from the working pressure side with all downstream valves open. The check valve will be held open to test the kill line valve(s).
- ☐ Each pressure test will be held for 10 minutes with no allowable leak off.
- ☐ Master controls and remote controls to the closing unit (accumulator) must be function tested as part of the BOPE test.
- ☐ Record BOP tests and pressures in drilling reports and IADC sheet.

District I

1625 N. French Dr., Hobbs, NM 88240
 Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
 Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
 Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
 Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 289526

CONDITIONS

| | |
|--|---|
| Operator: CHEVRON U S A INC 6301 Deauville Blvd Midland, TX 79706 | OGRID: |
| | 4323 |
| | Action Number: 289526 |
| | Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3) |

CONDITIONS

| Created By | Condition | Condition Date |
|-------------|--|----------------|
| ward.rikala | Notify OCD 24 hours prior to casing & cement | 12/28/2023 |
| ward.rikala | Will require a File As Drilled C-102 and a Directional Survey with the C-104 | 12/28/2023 |
| ward.rikala | Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string | 12/28/2023 |
| ward.rikala | Cement is required to circulate on both surface and intermediate1 strings of casing | 12/28/2023 |
| ward.rikala | If cement does not circulate on any string, a CBL is required for that string of casing | 12/28/2023 |
| ward.rikala | Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system | 12/28/2023 |
