

Form 3160-3
(June 2015)UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

1a. Type of work: ☒ DRILL ☐ REENTER		5. Lease Serial No. NMNM107374
1b. Type of Well: ☐ Oil Well ☒ Gas Well ☐ Other		6. If Indian, Allottee or Tribe Name
1c. Type of Completion: ☐ Hydraulic Fracturing ☐ Single Zone ☒ Multiple Zone		7. If Unit or CA Agreement, Name and No.
2. Name of Operator MEWBOURNE OIL COMPANY		8. Lease Name and Well No. DELAWARE RANCH 11 14 W2BO FED C
3a. Address P O BOX 5270, HOBBS, NM 88241		9. API Well No. 30-015-54587
3b. Phone No. (include area code) (575) 393-5905		10. Field and Pool, or Exploratory PIERCE CROSSING/BONE SPRING
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface NENE / 590 FNL / 920 FEL / LAT 32.0628223 / LONG -104.052242 At proposed prod. zone SWSE / 330 FSL / 2300 FEL / LAT 32.0361853 / LONG -104.0567729		11. Sec., T. R. M. or Blk. and Survey or Area SEC 11/T26S/R28E/NMP
14. Distance in miles and direction from nearest town or post office* 10 miles		12. County or Parish EDDY
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 20 feet		13. State NM
16. No of acres in lease		17. Spacing Unit dedicated to this well 640.0
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. 330 feet		20. BLM/BIA Bond No. in file FED:
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 2973 feet		22. Approximate date work will start* 06/27/2020
		23. Estimated duration 60 days
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|--|---|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification. |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be requested by the BLM. |

25. Signature (Electronic Submission)	Name (Printed/Typed) BRADLEY BISHOP / Ph: (575) 393-5905	Date 11/07/2022
Title Regulatory		
Approved by (Signature) (Electronic Submission)	Name (Printed/Typed) CODY LAYTON / Ph: (575) 234-5959	Date 12/22/2023
Title Assistant Field Manager Lands & Minerals		
Office Carlsbad Field Office		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.



(Continued on page 2)

*(Instructions on page 2)

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-015-54587		² Pool Code 98220		³ Pool Name Purple Sage (Wolfcamp)					
⁴ Property Code 335181		⁵ Property Name DELAWARE RANCH 11/14 W2B0 FED COM						⁶ Well Number 1H	
⁷ OGRID NO. 14744		⁸ Operator Name MEWBOURNE OIL COMPANY						⁹ Elevation 2973'	
¹⁰ Surface Location									
UL or lot no. A	Section 11	Township 26S	Range 28E	Lot Idn	Feet from the 590	North/South line NORTH	Feet From the 920	East/West line EAST	County EDDY
¹¹ Bottom Hole Location If Different From Surface									
UL or lot no. 0	Section 14	Township 26S	Range 28E	Lot Idn	Feet from the 330	North/South line SOUTH	Feet from the 2300	East/West line EAST	County EDDY
¹² Dedicated Acres 640		¹³ Joint or Infill		¹⁴ Consolidation Code		¹⁵ Order No.			

No allowable will be assigned to this completion until all interest have been consolidated or a non-standard unit has been approved by the division.

Project Area Producing Area FTP 330' FNL & 2300' FEL 11 GEODETIC DATA NAD 83 GRID - NM EAST SURFACE LOCATION N: 386705.8 - E: 628413.1 LAT: 32.0628123° N LONG: 104.0522420° W GEODETIC DATA NAD 83 GRID - NM EAST BOTTOM HOLE N: 377012.4 - E: 627034.4 LAT: 32.0361853° N LONG: 104.0567729° W 14 LTP 330' FSL & 2300' FEL 330' 2300' B.H.		¹⁶ CORNER DATA NAD 83 GRID - NM EAST A: FOUND BRASS CAP "1995" N: 376625.5 - E: 623933.6 B: FOUND BRASS CAP "1995" N: 379328.1 - E: 623958.0 C: FOUND BRASS CAP "1995" N: 381983.9 - E: 623982.6 D: FOUND BRASS CAP "1995" N: 384643.3 - E: 624006.1 E: CALCULATED CORNER N: 387283.6 - E: 624038.6 F: FOUND BRASS CAP "1995" N: 387325.3 - E: 626679.4 G: FOUND BRASS CAP "1995" N: 387279.9 - E: 629333.6 H: FOUND BRASS CAP "1995" N: 385960.2 - E: 629332.1 I: FOUND BRASS CAP "1995" N: 384640.5 - E: 629330.8 J: FOUND BRASS CAP "1995" N: 382001.1 - E: 629327.9 K: FOUND 1/2" REBAR N: 380683.3 - E: 629328.6 L: FOUND BRASS CAP "1995" N: 379365.5 - E: 629329.2 M: FOUND BRASS CAP "1995" N: 378050.8 - E: 629335.6 N: FOUND BRASS CAP "1995" N: 376724.4 - E: 629332.8 O: FOUND BRASS CAP "1995" N: 376674.3 - E: 626590.4 P: FOUND BRASS CAP "1995" N: 381988.6 - E: 626650.7	¹⁷ OPERATOR CERTIFICATION I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division. <i>Ryan McDaniel</i> 10/21/22 Signature Date Ryan McDaniel Printed Name RyanMcDaniel@mewbourne.com E-mail Address	¹⁸ SURVEYOR CERTIFICATION I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief. 08/08/2022 Date of Survey Signature and Seal of Professional Surveyor: 19680 Certificate Number ROBERT M. HOWETT NEW MEXICO 19680 PROFESSIONAL SURVEYOR
---	--	---	---	--

Job No: LS22080948

Page 5

State of New Mexico
Energy, Minerals and Natural Resources Department

Submit Electronically
Via E-permitting

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description

Effective May 25, 2021

I. Operator: Mewbourne Oil Co. **OGRID:** 14744 **Date:** 5/2/22

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
Delaware Ranch 11/14 W2BO Fed Com 1H		A 11 26S 28E	590' FNL x 880' FEL	1000	10000	4000

IV. Central Delivery Point Name: Delaware Ranch 11/14 W2BO Fed Com 1H [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Delaware Ranch 11/14 W2BO Fed Com 1H		7/2/22	8/2/22	9/2/22	9/17/22	9/17/22

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Page 6

Section 2 – Enhanced Plan**EFFECTIVE APRIL 1, 2022**

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications**Effective May 25, 2021**

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

Page 8

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature:	<i>Bradley Bishop</i>
Printed Name:	BRADLEY BISHOP
Title:	REGULATORY MANAGER
E-mail Address:	BBISHOP@MEWBOURNE.COM
Date:	5/2/22
Phone:	575-393-5905
OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form)	
Approved By:	
Title:	
Approval Date:	
Conditions of Approval:	

Mewbourne Oil Company

Natural Gas Management Plan – Attachment

- VI. Separation equipment will be sized by construction engineering staff based on stated manufacturer daily throughput capacities and anticipated daily production rates to ensure adequate capacity. Closed vent system piping, compression needs, and VRUs will be sized utilizing ProMax modelling software to ensure adequate capacity for anticipated production volumes and conditions.
- VII. Mewbourne Oil Company (MOC) will take following actions to comply with the regulations listed in 19.15.27.8 :
- A. MOC will maximize the recovery of natural gas by minimizing the waste, as defined by 19.15.2 NMAC, of natural gas through venting and flaring. MOC will ensure that well(s) will be connected to a natural gas gathering system with sufficient capacity to transport natural gas. If there is no adequate takeaway for the gas, well(s) will be shut in until the natural gas gathering system is available.
 - B. All drilling operations will be equipped with a rig flare located at least 100 ft from the nearest surface hole. Rig flare will be utilized to combust any natural gas that is brought to surface during normal drilling operations. In the case of emergency venting or flaring the volumes will be estimated and reported appropriately.
 - C. During completion operations any natural gas brought to surface will be flared. Immediately following the finish of completion operations, all well flow will be directed to permanent separation equipment. Produced natural gas from separation equipment will be sent to sales. It is not anticipated that gas will not meet pipeline standards. However, if natural gas does not meet gathering pipeline quality specifications, MOC will flare the natural gas for 60 days or until the natural gas meets the pipeline quality specifications, whichever is sooner. MOC will ensure that the flare is sized properly and is equipped with automatic igniter or continuous pilot. The gas sample will analyzed twice per week and the gas will be routed into a gathering system as soon as pipeline specifications are met.
 - D. Natural gas will not be flared with the exceptions and provisions listed in the 19.15.27.8 D.(1) through (4). If there is no adequate takeaway for the separator gas, well(s) will be shut in until the natural gas gathering system is available with exception of emergency or malfunction situations. Venting and/or flaring volumes will be estimated and reported appropriately.
 - E. MOC will comply with the performance standards requirements and provisions listed in 19.15.27.8 E.(1) through (8). All equipment will be designed and sized to handle maximum anticipated pressures and throughputs in order to minimize the waste. Production storage tanks constructed after May 25, 2021 will be equipped with automatic gauging system. Flares constructed after May 25, 2021 will be equipped with automatic igniter or continuous pilot. Flares will be located at least 100' from the well and storage tanks unless otherwise approved by the division. MOC will conduct AVO inspections as described in 19.15.27.8 E (5) (a) with frequencies specified in 19.15.27.8 E (5) (b) and (c). All emergencies will be resolved as quickly and safely as feasible to minimize waste.
 - F. The volume of natural gas that is vented or flared as the result of malfunction or emergency during drilling and completions operations will be estimated. The volume of natural gas that is vented, flared or beneficially used during production operations, will be measured or estimated. MOC will install equipment to measure

the volume of natural gas flared from existing process piping or a flowline piped from equipment such as high pressure separators, heater treaters, or vapor recovery units associated with a well or facility associated with a well authorized by an APD issued after May 25, 2021 that has an average daily production greater than 60 Mcf/day. If metering is not practicable due to circumstances such as low flow rate or low pressure venting and flaring, MOC will estimate the volume of vented or flared natural gas. Measuring equipment will conform to industry standards and will not be designed or equipped with a manifold that allows the diversion of natural gas around the metering element except for the sole purpose of inspecting and servicing the measurement equipment.

- VIII. For maintenance activities involving production equipment and compression, venting will be limited to the depressurization of the subject equipment to ensure safe working conditions. For maintenance of production and compression equipment the associated producing wells will be shut in to eliminate venting. For maintenance of VRUs all gas normally routed to the VRU will be routed to flare to eliminate venting.



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Drilling Plan Data Report

12/22/2023

APD ID: 10400088861

Submission Date: 11/07/2022

Highlighted data
reflects the most
recent changes

Operator Name: MEWBOURNE OIL COMPANY

Well Name: DELAWARE RANCH 11 14 W2BO FED COM

Well Number: 1H

Well Type: CONVENTIONAL GAS WELL

Well Work Type: Drill

[Show Final Text](#)

Section 1 - Geologic Formations

Formation ID	Formation Name	Elevation	True Vertical	Measured Depth	Lithologies	Mineral Resources	Producing Formatio
12649139	UNKNOWN	2973	28	28	OTHER : Topsoil	NONE	N
12649159	TOP SALT	2498	475	475	SALT	NONE	N
12649153	BASE OF SALT	531	2442	2442	SALT	NONE	N
12649144	LAMAR	333	2640	2640	LIMESTONE	NATURAL GAS, OIL	N
12649145	BELL CANYON	305	2668	2668	SANDSTONE	NATURAL GAS, OIL	N
12649154	CHERRY CANYON	-543	3516	3516	SANDSTONE	NATURAL GAS, OIL	N
12649147	MANZANITA	-682	3655	3655	LIMESTONE	NATURAL GAS, OIL	N
12649155	BRUSHY CANYON	-3134	6107	6107	SANDSTONE	NATURAL GAS, OIL	N
12649138	BONE SPRING LIME	-3392	6365	6365	LIMESTONE, SHALE	NATURAL GAS, OIL	N
12649156	BONE SPRING 1ST	-4282	7255	7255	SANDSTONE	NATURAL GAS, OIL	N
12649142	BONE SPRING 2ND	-5051	8024	8024	SANDSTONE	NATURAL GAS, OIL	Y
12649157	BONE SPRING 3RD	-6144	9117	9117	SANDSTONE	NATURAL GAS, OIL	N
12649158	WOLFCAMP	-6490	9463	9463	LIMESTONE, SANDSTONE, SHALE	NATURAL GAS, OIL	Y

Section 2 - Blowout Prevention

Operator Name: MEWBOURNE OIL COMPANY**Well Name:** DELAWARE RANCH 11 14 W2BO FED COM **Well Number:** 1H**Pressure Rating (PSI):** 5M**Rating Depth:** 20896**Equipment:** Annular, Pipe Ram, Blind Ram**Requesting Variance?** YES

Variance request: A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. Anchors aren't required by manufacturer. A multi-bowl wellhead is being used. See attached schematic

Testing Procedure: BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all the components installed will be functional and tested. Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold.

Choke Diagram Attachment:

Delaware_Ranch_11_14_W2BO_Fed_Com_1H_5M_BOPE_Choke_Diagram_20221027150612.pdf

Delaware_Ranch_11_14_W2BO_Fed_Com_1H_Flex_Line_Specs_20221027150612.pdf

Delaware_Ranch_11_14_W2BO_Fed_Com_1H_Flex_Line_Specs_API_16C_20221027150612.pdf

BOP Diagram Attachment:

Delaware_Ranch_11_14_W2BO_Fed_Com_1H_5M_BOPE_Schematic_20221027150619.pdf

Delaware_Ranch_11_14_W2BO_Fed_Com_1H_5M_Mutli_Bowl_WH_20221027150619.pdf

Section 3 - Casing

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE	17.5	13.375	NEW	API	N	0	575	0	575	3001	2426	575	H-40	48	ST&C	3.07	6.89	DRY	11.67	DRY	19.6
2	INTERMEDIATE	12.25	9.625	NEW	API	N	0	2570	0	2570	2968	431	2570	J-55	36	LT&C	1.51	2.63	DRY	4.9	DRY	6.1
3	PRODUCTION	8.75	7.0	NEW	API	N	0	10300	0	10142	2968	-7141	10300	P-110	26	LT&C	1.24	1.99	DRY	2.59	DRY	3.1
4	LINER	6.125	4.5	NEW	API	N	10150	20896	9992	10614	-6991	-7613	10746	P-110	13.5	LT&C	1.6	1.86	DRY	2.33	DRY	2.91

Casing Attachments

Operator Name: MEWBOURNE OIL COMPANY**Well Name:** DELAWARE RANCH 11 14 W2BO FED COM **Well Number:** 1H**Casing Attachments**

Casing ID: 1 **String** SURFACE**Inspection Document:****Spec Document:****Tapered String Spec:****Casing Design Assumptions and Worksheet(s):**Delaware_Ranch_11_14_W2BO_Fed_Com_1H_Csg_Assumptions_20221102091655.pdf

Casing ID: 2 **String** INTERMEDIATE**Inspection Document:****Spec Document:****Tapered String Spec:****Casing Design Assumptions and Worksheet(s):**Delaware_Ranch_11_14_W2BO_Fed_Com_1H_Csg_Assumptions_20221102091708.pdf

Casing ID: 3 **String** PRODUCTION**Inspection Document:****Spec Document:****Tapered String Spec:****Casing Design Assumptions and Worksheet(s):**Delaware_Ranch_11_14_W2BO_Fed_Com_1H_Csg_Assumptions_20221102091719.pdf

Operator Name: MEWBOURNE OIL COMPANY

Well Name: DELAWARE RANCH 11 14 W2BO FED COM Well Number: 1H

Casing Attachments

Casing ID: 4 String LINER

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Delaware_Ranch_11_14_W2BO_Fed_Com_1H_Csg_Assumptions_20221102091732.pdf

Section 4 - Cement

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
SURFACE	Lead		0	407	260	2.12	12.5	551	100	Class C	Salt, Gel, Extender, LCM
SURFACE	Tail		407	575	200	1.34	14.8	268	100	Class C	Retarder
INTERMEDIATE	Lead		0	1924	350	2.12	12.5	742	25	Class C	Salt, Gel, Extender, LCM
INTERMEDIATE	Tail		1924	2570	200	1.34	14.8	268	25	Class C	Retarder
PRODUCTION	Lead	3664	2370	2951	50	2.12	12.5	106	25	Class C	Gel, Retarder, Defoamer, Extender
PRODUCTION	Tail		2951	3664	100	1.34	14.8	134	25	Class C	Retarder
PRODUCTION	Lead	3664	3664	7831	390	2.12	12.5	827	25	Class C	Gel, Retarder, Defoamer, Extender
PRODUCTION	Tail		7831	10300	400	1.18	15.6	472	25	Class H	Retarder, Fluid Loss, Defoamer
LINER	Lead		10150	20896	690	1.85	13.5	1277	25	Class C	Salt, Gel, Fluid Loss, Retarder, Dispersant, Defoamer, Anti-Settling Agent

Operator Name: MEWBOURNE OIL COMPANY

Well Name: DELAWARE RANCH 11 14 W2BO FED COM **Well Number:** 1H

Section 5 - Circulating Medium

Mud System Type: Closed

Will an air or gas system be Used? NO

Description of the equipment for the circulating system in accordance with Onshore Order #2:

Diagram of the equipment for the circulating system in accordance with Onshore Order #2:

Describe what will be on location to control well or mitigate other conditions: Lost circulation material Sweeps Mud scavengers in surface hole

Describe the mud monitoring system utilized: PVT/Visual Monitoring

Circulating Medium Table

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
0	575	SPUD MUD	8.6	8.8							
575	2570	SALT SATURATED	10	10							
2570	10300	WATER-BASED MUD	8.6	9.7							
10300	20896	OIL-BASED MUD	8.6	12							

Section 6 - Test, Logging, Coring

List of production tests including testing procedures, equipment and safety measures:

Will use GR/CNL from the offset Delaware Ranch 11/14 W1AP Fed Com #1H

List of open and cased hole logs run in the well:

DIRECTIONAL SURVEY, MEASUREMENT WHILE DRILLING, MUD LOG/GEOLOGIC LITHOLOGY LOG,

Coring operation description for the well:

None

Operator Name: MEWBOURNE OIL COMPANY

Well Name: DELAWARE RANCH 11 14 W2BO FED COM **Well Number:** 1H

Section 7 - Pressure

Anticipated Bottom Hole Pressure: 6947

Anticipated Surface Pressure: 4597

Anticipated Bottom Hole Temperature(F): 140

Anticipated abnormal pressures, temperatures, or potential geologic hazards? NO

Describe:

Contingency Plans geohazards description:

Contingency Plans geohazards

Hydrogen Sulfide drilling operations plan required? YES

Hydrogen sulfide drilling operations

Delaware_Ranch_11_14_W2BO_Fed_Com_1H_H2S_Plan_20221027151019.pdf

Section 8 - Other Information

Proposed horizontal/directional/multi-lateral plan submission:

Delaware_Ranch_11_14_W2BO_Fed_Com_1H_MOC_Dir_Plan_20221027151033.pdf

Delaware_Ranch_11_14_W2BO_Fed_Com_1H_MOC_Dir_Plot_20221027151033.pdf

Other proposed operations facets description:

Other proposed operations facets attachment:

Delaware_Ranch_11_14_W2BO_Fed_Com_1H_Add_Info_20221027151037.pdf

Other Variance attachment:

5M BOPE & Closed Loop Equipment Schematic

Drawing not to scale



GATES E & S NORTH AMERICA, INC.
134 44TH STREET
CORPUS CHRISTI, TEXAS 78405

PHONE: 361-887-9807
FAX: 361-887-0812
EMAIL: Tim.Cantu@gates.com
WEB: www.gates.com

10K CEMENTING ASSEMBLY PRESSURE TEST CERTIFICATE

Customer :	AUSTIN DISTRIBUTING	Test Date:	4/30/2015
Customer Ref. :	4060578	Hose Serial No.:	D-043015-7
Invoice No. :	500506	Created By:	JUSTIN CROPPER
Product Description:	10K3.548.0CK4.1/1610KFLGE/E LE		
End Fitting 1 :	4 1/16 10K FLG	End Fitting 2 :	4 1/16 10K FLG
Gates Part No. :	4773-6290	Assembly Code :	L36554102914D-043015-7
Working Pressure :	10,000 PSI	Test Pressure :	15,000 PSI

Gates E & S North America, Inc. certifies that the following hose assembly has been tested to the Gates Oilfield Roughneck Agreement/Specification requirements and passed the 15 minute hydrostatic test per API Spec 7K/Q1, Fifth Edition, June 2010, Test pressure 9.6.7 and per Table 9 to 15,000 psi in accordance with this product number. Hose burst pressure 9.6.7.2 exceeds the minimum of 2.5 times the working pressure per Table 9.

Quality Manager :
 Date :
 Signature :


QUALITY
4/30/2015
<i>Justin Cropper</i>

Production:
 Date :
 Signature :

PRODUCTION
4/30/2015
<i>Justin Cropper</i>

Form PTC - 01 Rev.02



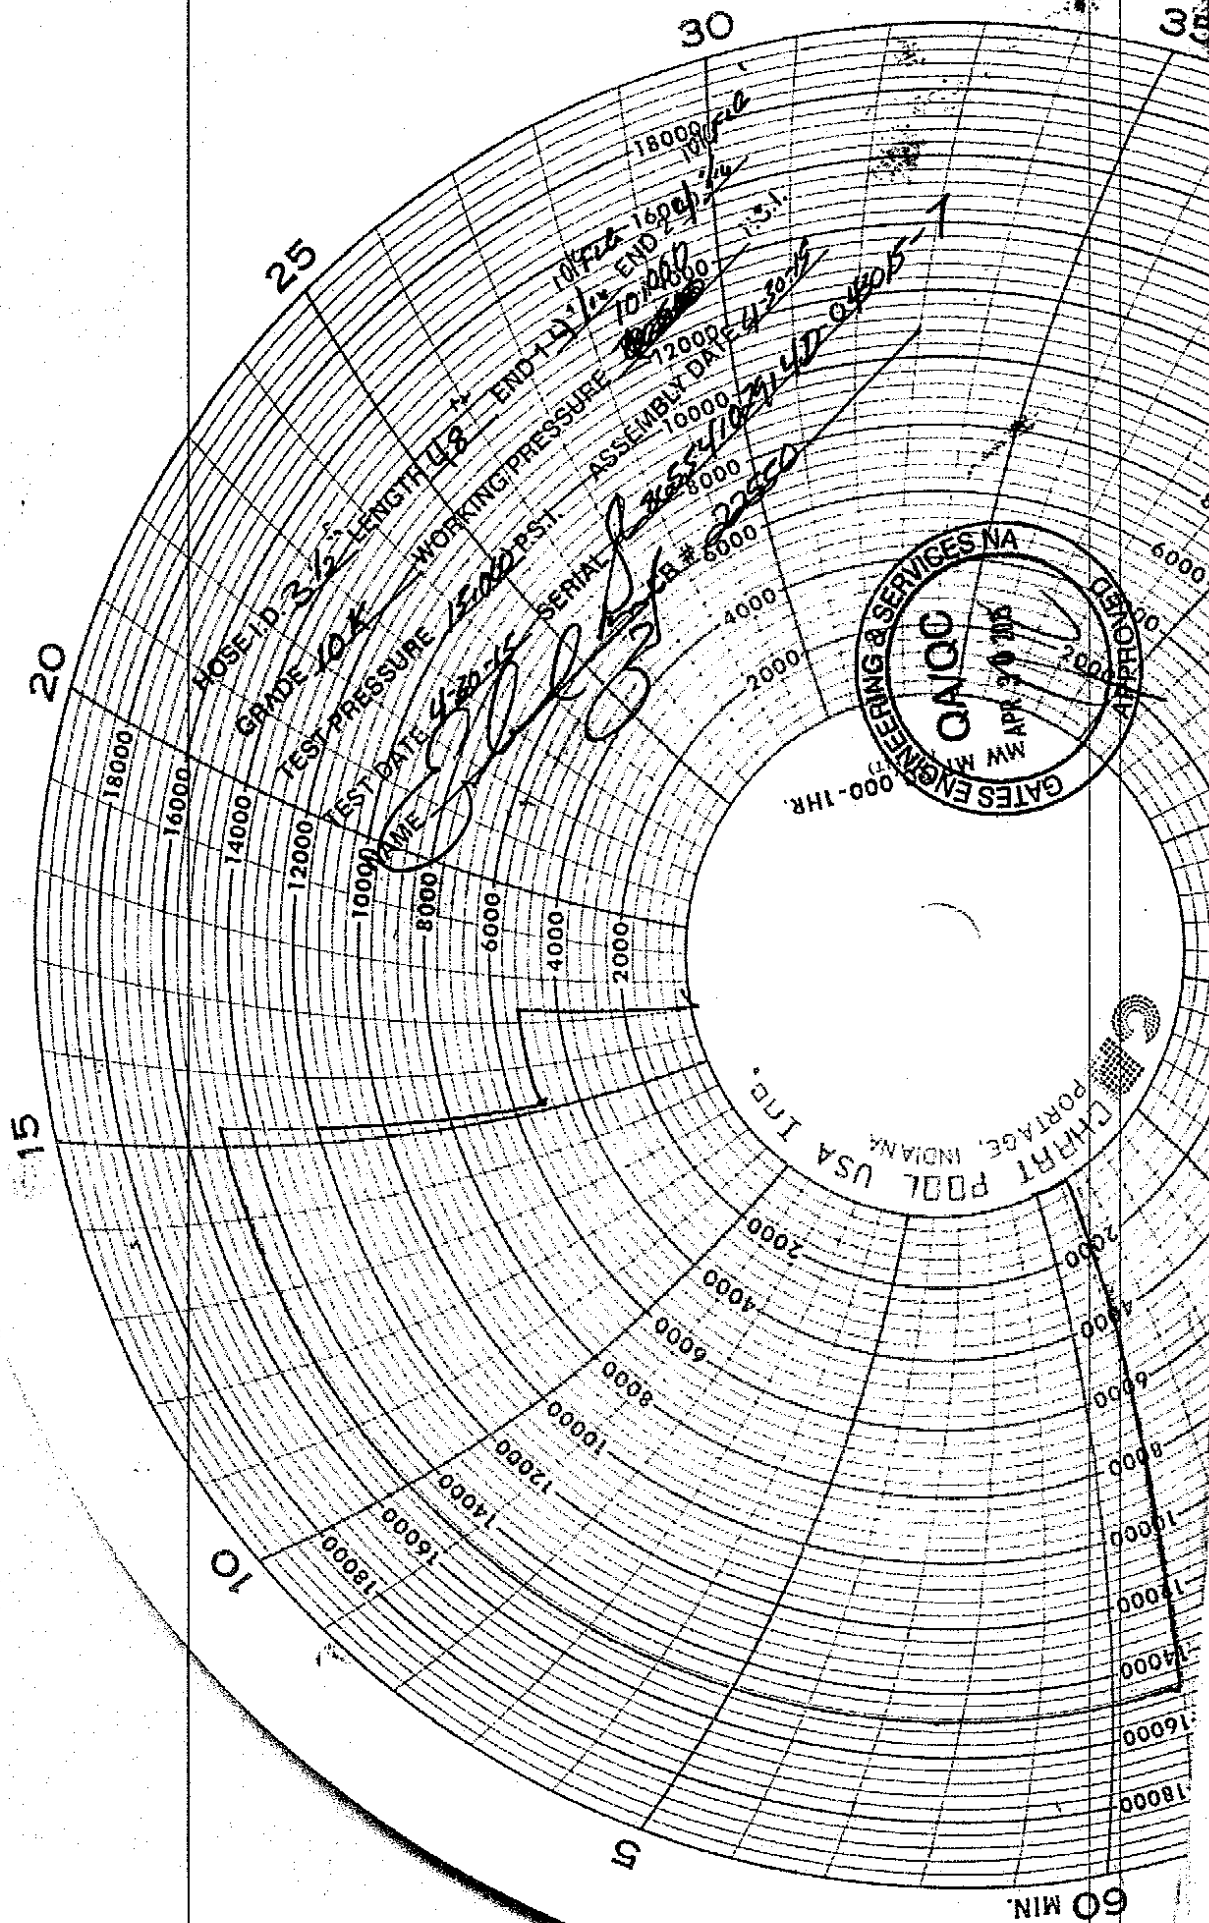



GATES ENGINEERING & SERVICES NORTH AMERICA
7603 Prairie Oak Dr.
Houston, TX 77086

PHONE: (281) 602 - 4119
FAX:
EMAIL: Troy.Schmidt@gates.com
WEB: www.gates.com

10K CHOKE & KILL ASSEMBLY PRESSURE TEST CERTIFICATE

Customer:	A-7 AUSTIN INC DBA AUSTIN HOSE	Test Date:	8/20/2018
Customer Ref.:	4101901	Hose Serial No.:	H-082018-10
Invoice No.:	511956	Created By:	Moosa Naqvi
Product Description:	10KF3.035.0CK41/1610KFLGFXDxFLT L/E		
End Fitting 1:	4 1/16 in. Fixed Flange	End Fitting 2:	4 1/16 in. Float Flange
Gates Part No.:	68503010-9721632	Assembly Code:	L40695052218H-082018-10
Working Pressure:	10,000 psi.	Test Pressure:	15,000 psi.



Gates Engineering & Services North America certifies that the following hose assembly has successfully passed all pressure testing requirements set forth in Gates specifications: GTS-04-052 (for 5K assemblies) or GTS-04-053 (10K assemblies), which include reference to Specification API 16C (2nd Edition); sections 7.5.4, 7.5.9, and 10.8.7. A test graph will accompany this test certificate to illustrate conformity to test requirements.

Quality:	QUALITY	Production:	PRODUCTION
Date :	8/20/2018	Date :	8/20/2018
Signature :		Signature :	

Form PTC - 01 Rev.0 2




Hydril "GK"
13 5/8" 5M

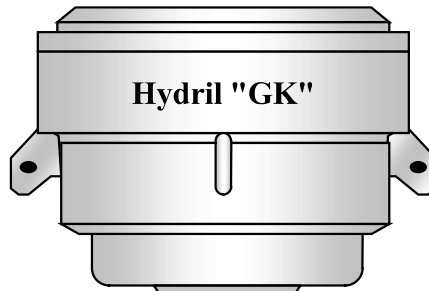


Hydril "GK"


Cameron Type U
13 5/8" 5M



4 1/2" x 5 7/8" VBR




BLIND RAMS



MUD CROSS

H.C.R.




7" RAMS



13 5/8" 5M

13 5/8" 5M

13 5/8" 5M

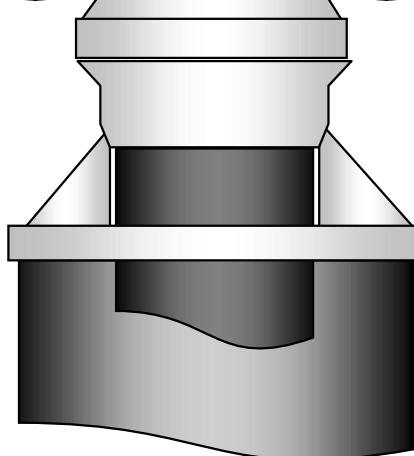



13-5/8" MN-DS Wellhead System



C7585
Rev. 02

NOTE: All dimensions on this drawing are estimated measurements and should be evaluated by engineering.

Cuffing Hanger 57" conductor cut-off

Mewbourne Oil Company, Delaware Ranch 11/14 W2BO Fed Com #1H**Sec 11, T26S, R28E****SHL: 590' FNL & 920' FEL, Sec 11, T26S, R28E****BHL: 330' FSL & 2300' FEL, Sec 14, T26S, R28E****Casing Program**

Hole Size	Casing Interval		Csg. Size	Weight (lbs)	Grade	Conn.	SF Collapse	SF Burst	SF Jt Tension	SF Body Tension
	From	To								
17.5"	0'	575'	13.375"	48	H40	STC	3.07	6.89	11.67	19.60
12.25"	0'	2570'	9.625"	36	J55	LTC	1.51	2.63	4.90	6.10
8.75"	0'	10300'	7"	26	P110	LTC	1.24	1.99	2.59	3.10
6.125"	10150'	20896'	4.5"	13.5	P110	LTC	1.60	1.86	2.33	2.91
BLM Minimum Safety Factor							1.125	1	1.6 Dry 1.8 Wet	1.6 Dry 1.8 Wet

All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h

Must have table for contingency casing

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	Y
Is casing API approved? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	N
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	N
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is well within the designated 4 string boundary.	
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	N
If yes, are the first three strings cemented to surface?	
Is 2 nd string set 100' to 600' below the base of salt?	
Is well located in high Cave/Karst?	Y
If yes, are there two strings cemented to surface?	Y
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	

Mewbourne Oil Company, Delaware Ranch 11/14 W2BO Fed Com #1H**Sec 11, T26S, R28E****SHL: 590' FNL & 920' FEL, Sec 11, T26S, R28E****BHL: 330' FSL & 2300' FEL, Sec 14, T26S, R28E**

Formation	Est. Top	Formation	Est. Top
Rustler		Delaware (Lamar)	2640
Salt Top		Bell Canyon	2668
Salt Base	2442	Cherry Canyon	3516
Yates		Manzanita Marker	3655
Seven Rivers		Basal Brushy Canyon	6107
Queen		Bone Spring	6365
Capitan		1 st Bone Spring	7255
Grayburg		2 nd Bone Spring	8024
San Andres		3 rd Bone Spring	9117
Glorieta		Abo	
Yeso		Wolfcamp	9463

Mewbourne Oil Company, Delaware Ranch 11/14 W2BO Fed Com #1H
Sec 11, T26S, R28E
SHL: 590' FNL & 920' FEL, Sec 11, T26S, R28E
BHL: 330' FSL & 2300' FEL, Sec 14, T26S, R28E

Casing Program

Hole Size	Casing Interval		Csg. Size	Weight (lbs)	Grade	Conn.	SF Collapse	SF Burst	SF Jt Tension	SF Body Tension
	From	To								
17.5"	0'	575'	13.375"	48	H40	STC	3.07	6.89	11.67	19.60
12.25"	0'	2570'	9.625"	36	J55	LTC	1.51	2.63	4.90	6.10
8.75"	0'	10300'	7"	26	P110	LTC	1.24	1.99	2.59	3.10
6.125"	10150'	20896'	4.5"	13.5	P110	LTC	1.60	1.86	2.33	2.91
BLM Minimum Safety Factor							1.125	1	1.6 Dry 1.8 Wet	1.6 Dry 1.8 Wet

All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h
 Must have table for contingency casing

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	Y
Is casing API approved? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	N
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	N
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is well within the designated 4 string boundary.	
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	N
If yes, are the first three strings cemented to surface?	
Is 2 nd string set 100' to 600' below the base of salt?	
Is well located in high Cave/Karst?	Y
If yes, are there two strings cemented to surface?	Y
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	

Mewbourne Oil Company, Delaware Ranch 11/14 W2BO Fed Com #1H**Sec 11, T26S, R28E****SHL: 590' FNL & 920' FEL, Sec 11, T26S, R28E****BHL: 330' FSL & 2300' FEL, Sec 14, T26S, R28E**

Formation	Est. Top	Formation	Est. Top
Rustler		Delaware (Lamar)	2640
Salt Top		Bell Canyon	2668
Salt Base	2442	Cherry Canyon	3516
Yates		Manzanita Marker	3655
Seven Rivers		Basal Brushy Canyon	6107
Queen		Bone Spring	6365
Capitan		1 st Bone Spring	7255
Grayburg		2 nd Bone Spring	8024
San Andres		3 rd Bone Spring	9117
Glorieta		Abo	
Yeso		Wolfcamp	9463

Mewbourne Oil Company, Delaware Ranch 11/14 W2BO Fed Com #1H
Sec 11, T26S, R28E
SHL: 590' FNL & 920' FEL, Sec 11, T26S, R28E
BHL: 330' FSL & 2300' FEL, Sec 14, T26S, R28E

Casing Program

Hole Size	Casing Interval		Csg. Size	Weight (lbs)	Grade	Conn.	SF Collapse	SF Burst	SF Jt Tension	SF Body Tension
	From	To								
17.5"	0'	575'	13.375"	48	H40	STC	3.07	6.89	11.67	19.60
12.25"	0'	2570'	9.625"	36	J55	LTC	1.51	2.63	4.90	6.10
8.75"	0'	10300'	7"	26	P110	LTC	1.24	1.99	2.59	3.10
6.125"	10150'	20896'	4.5"	13.5	P110	LTC	1.60	1.86	2.33	2.91
BLM Minimum Safety Factor							1.125	1	1.6 Dry 1.8 Wet	1.6 Dry 1.8 Wet

All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h
 Must have table for contingency casing

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	Y
Is casing API approved? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	N
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	N
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is well within the designated 4 string boundary.	
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	N
If yes, are the first three strings cemented to surface?	
Is 2 nd string set 100' to 600' below the base of salt?	
Is well located in high Cave/Karst?	Y
If yes, are there two strings cemented to surface?	Y
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	

Mewbourne Oil Company, Delaware Ranch 11/14 W2BO Fed Com #1H**Sec 11, T26S, R28E****SHL: 590' FNL & 920' FEL, Sec 11, T26S, R28E****BHL: 330' FSL & 2300' FEL, Sec 14, T26S, R28E**

Formation	Est. Top	Formation	Est. Top
Rustler		Delaware (Lamar)	2640
Salt Top		Bell Canyon	2668
Salt Base	2442	Cherry Canyon	3516
Yates		Manzanita Marker	3655
Seven Rivers		Basal Brushy Canyon	6107
Queen		Bone Spring	6365
Capitan		1 st Bone Spring	7255
Grayburg		2 nd Bone Spring	8024
San Andres		3 rd Bone Spring	9117
Glorieta		Abo	
Yeso		Wolfcamp	9463

Mewbourne Oil Company, Delaware Ranch 11/14 W2BO Fed Com #1H
Sec 11, T26S, R28E
SHL: 590' FNL & 920' FEL, Sec 11, T26S, R28E
BHL: 330' FSL & 2300' FEL, Sec 14, T26S, R28E

Casing Program

Hole Size	Casing Interval		Csg. Size	Weight (lbs)	Grade	Conn.	SF Collapse	SF Burst	SF Jt Tension	SF Body Tension
	From	To								
17.5"	0'	575'	13.375"	48	H40	STC	3.07	6.89	11.67	19.60
12.25"	0'	2570'	9.625"	36	J55	LTC	1.51	2.63	4.90	6.10
8.75"	0'	10300'	7"	26	P110	LTC	1.24	1.99	2.59	3.10
6.125"	10150'	20896'	4.5"	13.5	P110	LTC	1.60	1.86	2.33	2.91
BLM Minimum Safety Factor							1.125	1	1.6 Dry 1.8 Wet	1.6 Dry 1.8 Wet

All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h
 Must have table for contingency casing

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	Y
Is casing API approved? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	N
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	N
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is well within the designated 4 string boundary.	
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	N
If yes, are the first three strings cemented to surface?	
Is 2 nd string set 100' to 600' below the base of salt?	
Is well located in high Cave/Karst?	Y
If yes, are there two strings cemented to surface?	Y
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	

Mewbourne Oil Company, Delaware Ranch 11/14 W2BO Fed Com #1H**Sec 11, T26S, R28E****SHL: 590' FNL & 920' FEL, Sec 11, T26S, R28E****BHL: 330' FSL & 2300' FEL, Sec 14, T26S, R28E**

Formation	Est. Top	Formation	Est. Top
Rustler		Delaware (Lamar)	2640
Salt Top		Bell Canyon	2668
Salt Base	2442	Cherry Canyon	3516
Yates		Manzanita Marker	3655
Seven Rivers		Basal Brushy Canyon	6107
Queen		Bone Spring	6365
Capitan		1 st Bone Spring	7255
Grayburg		2 nd Bone Spring	8024
San Andres		3 rd Bone Spring	9117
Glorieta		Abo	
Yeso		Wolfcamp	9463

Mewbourne Oil Company

Eddy County, New Mexico NAD 83

Delaware Ranch 11/14 W2BO Fed Com #1H

Sec 11, T26S, R28E

SHL: 590 FNL & 920 FEL (11)

BHL: 330 FSL & 2300 FEL (14)

Plan: Design #1

Standard Planning Report

24 October, 2022

Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Delaware Ranch 11/14 W2BO Fed Com #1H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 3001.0usft (Original Well Elev)
Project:	Eddy County, New Mexico NAD 83	MD Reference:	WELL @ 3001.0usft (Original Well Elev)
Site:	Delaware Ranch 11/14 W2BO Fed Com #1H	North Reference:	Grid
Well:	Sec 11, T26S, R28E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 330 FSL & 2300 FEL (14)		
Design:	Design #1		

Project	Eddy County, New Mexico NAD 83		
Map System:	US State Plane 1983	System Datum:	Ground Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Delaware Ranch 11/14 W2BO Fed Com #1H			
Site Position:		Northing:	386,705.80 usft	Latitude: 32.0628224
From:	Map	Easting:	628,413.10 usft	Longitude: -104.0522421
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "	

Well	Sec 11, T26S, R28E			
Well Position	+N/-S	0.0 usft	Northing:	386,705.80 usft
	+E/-W	0.0 usft	Easting:	628,413.10 usft
Position Uncertainty	0.0 usft		Wellhead Elevation:	3,001.0 usft
Grid Convergence:	0.15 °		Ground Level:	2,973.0 usft

Wellbore	BHL: 330 FSL & 2300 FEL (14)				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2010	12/31/2014	7.36	59.87	48,091.48566054

Design	Design #1			
Audit Notes:				
Version:	Phase:	PROTOTYPE	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0	0.0	0.0	188.09

Plan Survey Tool Program	Date	10/24/2022		
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks
1	0.0	20,895.9	Design #1 (BHL: 330 FSL & 2300	

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
2,600.0	0.00	0.00	2,600.0	0.0	0.0	0.00	0.00	0.00	0.00	
3,215.9	12.32	293.63	3,211.1	26.4	-60.4	2.00	2.00	0.00	293.63	
9,655.8	12.32	293.63	9,502.9	577.0	-1,319.1	0.00	0.00	0.00	0.00	
10,271.7	0.00	0.00	10,114.0	603.4	-1,379.5	2.00	-2.00	0.00	180.00	KOP: 10 FNL & 2300
11,176.1	90.43	180.00	10,687.0	26.1	-1,379.5	10.00	10.00	0.00	180.00	
20,895.9	90.43	180.00	10,614.0	-9,693.4	-1,378.7	0.00	0.00	0.00	0.00	BHL: 330 FSL & 2300

Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Delaware Ranch 11/14 W2BO Fed Com #1H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 3001.0usft (Original Well Elev)
Project:	Eddy County, New Mexico NAD 83	MD Reference:	WELL @ 3001.0usft (Original Well Elev)
Site:	Delaware Ranch 11/14 W2BO Fed Com #1H	North Reference:	Grid
Well:	Sec 11, T26S, R28E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 330 FSL & 2300 FEL (14)		
Design:	Design #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
SHL: 590 FNL & 920 FEL (11)									
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00
1,600.0	0.00	0.00	1,600.0	0.0	0.0	0.0	0.00	0.00	0.00
1,700.0	0.00	0.00	1,700.0	0.0	0.0	0.0	0.00	0.00	0.00
1,800.0	0.00	0.00	1,800.0	0.0	0.0	0.0	0.00	0.00	0.00
1,900.0	0.00	0.00	1,900.0	0.0	0.0	0.0	0.00	0.00	0.00
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.0	0.00	0.00	0.00
2,100.0	0.00	0.00	2,100.0	0.0	0.0	0.0	0.00	0.00	0.00
2,200.0	0.00	0.00	2,200.0	0.0	0.0	0.0	0.00	0.00	0.00
2,300.0	0.00	0.00	2,300.0	0.0	0.0	0.0	0.00	0.00	0.00
2,400.0	0.00	0.00	2,400.0	0.0	0.0	0.0	0.00	0.00	0.00
2,500.0	0.00	0.00	2,500.0	0.0	0.0	0.0	0.00	0.00	0.00
2,600.0	0.00	0.00	2,600.0	0.0	0.0	0.0	0.00	0.00	0.00
2,700.0	2.00	293.63	2,700.0	0.7	-1.6	-0.5	2.00	2.00	0.00
2,800.0	4.00	293.63	2,799.8	2.8	-6.4	-1.9	2.00	2.00	0.00
2,900.0	6.00	293.63	2,899.5	6.3	-14.4	-4.2	2.00	2.00	0.00
3,000.0	8.00	293.63	2,998.7	11.2	-25.5	-7.5	2.00	2.00	0.00
3,100.0	10.00	293.63	3,097.5	17.4	-39.9	-11.7	2.00	2.00	0.00
3,200.0	12.00	293.63	3,195.6	25.1	-57.4	-16.8	2.00	2.00	0.00
3,215.9	12.32	293.63	3,211.1	26.4	-60.4	-17.7	2.00	2.00	0.00
3,300.0	12.32	293.63	3,293.3	33.6	-76.9	-22.5	0.00	0.00	0.00
3,400.0	12.32	293.63	3,391.0	42.2	-96.4	-28.2	0.00	0.00	0.00
3,500.0	12.32	293.63	3,488.7	50.7	-116.0	-33.9	0.00	0.00	0.00
3,600.0	12.32	293.63	3,586.4	59.3	-135.5	-39.6	0.00	0.00	0.00
3,700.0	12.32	293.63	3,684.1	67.8	-155.0	-45.3	0.00	0.00	0.00
3,800.0	12.32	293.63	3,781.8	76.4	-174.6	-51.0	0.00	0.00	0.00
3,900.0	12.32	293.63	3,879.5	84.9	-194.1	-56.7	0.00	0.00	0.00
4,000.0	12.32	293.63	3,977.2	93.5	-213.7	-62.4	0.00	0.00	0.00
4,100.0	12.32	293.63	4,074.9	102.0	-233.2	-68.2	0.00	0.00	0.00
4,200.0	12.32	293.63	4,172.6	110.6	-252.8	-73.9	0.00	0.00	0.00
4,300.0	12.32	293.63	4,270.3	119.1	-272.3	-79.6	0.00	0.00	0.00
4,400.0	12.32	293.63	4,368.0	127.7	-291.9	-85.3	0.00	0.00	0.00
4,500.0	12.32	293.63	4,465.7	136.2	-311.4	-91.0	0.00	0.00	0.00
4,600.0	12.32	293.63	4,563.4	144.8	-330.9	-96.7	0.00	0.00	0.00
4,700.0	12.32	293.63	4,661.1	153.3	-350.5	-102.4	0.00	0.00	0.00
4,800.0	12.32	293.63	4,758.8	161.9	-370.0	-108.1	0.00	0.00	0.00
4,900.0	12.32	293.63	4,856.5	170.4	-389.6	-113.9	0.00	0.00	0.00
5,000.0	12.32	293.63	4,954.2	179.0	-409.1	-119.6	0.00	0.00	0.00

Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Delaware Ranch 11/14 W2BO Fed Com #1H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 3001.0usft (Original Well Elev)
Project:	Eddy County, New Mexico NAD 83	MD Reference:	WELL @ 3001.0usft (Original Well Elev)
Site:	Delaware Ranch 11/14 W2BO Fed Com #1H	North Reference:	Grid
Well:	Sec 11, T26S, R28E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 330 FSL & 2300 FEL (14)		
Design:	Design #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
5,100.0	12.32	293.63	5,051.9	187.5	-428.7	-125.3	0.00	0.00	0.00	
5,200.0	12.32	293.63	5,149.6	196.1	-448.2	-131.0	0.00	0.00	0.00	
5,300.0	12.32	293.63	5,247.3	204.6	-467.8	-136.7	0.00	0.00	0.00	
5,400.0	12.32	293.63	5,345.0	213.2	-487.3	-142.4	0.00	0.00	0.00	
5,500.0	12.32	293.63	5,442.7	221.7	-506.8	-148.1	0.00	0.00	0.00	
5,600.0	12.32	293.63	5,540.4	230.3	-526.4	-153.8	0.00	0.00	0.00	
5,700.0	12.32	293.63	5,638.1	238.8	-545.9	-159.6	0.00	0.00	0.00	
5,800.0	12.32	293.63	5,735.8	247.4	-565.5	-165.3	0.00	0.00	0.00	
5,900.0	12.32	293.63	5,833.5	255.9	-585.0	-171.0	0.00	0.00	0.00	
6,000.0	12.32	293.63	5,931.2	264.5	-604.6	-176.7	0.00	0.00	0.00	
6,100.0	12.32	293.63	6,028.9	273.0	-624.1	-182.4	0.00	0.00	0.00	
6,200.0	12.32	293.63	6,126.6	281.6	-643.7	-188.1	0.00	0.00	0.00	
6,300.0	12.32	293.63	6,224.3	290.1	-663.2	-193.8	0.00	0.00	0.00	
6,400.0	12.32	293.63	6,322.0	298.7	-682.7	-199.5	0.00	0.00	0.00	
6,500.0	12.32	293.63	6,419.7	307.2	-702.3	-205.3	0.00	0.00	0.00	
6,600.0	12.32	293.63	6,517.4	315.8	-721.8	-211.0	0.00	0.00	0.00	
6,700.0	12.32	293.63	6,615.1	324.3	-741.4	-216.7	0.00	0.00	0.00	
6,800.0	12.32	293.63	6,712.8	332.9	-760.9	-222.4	0.00	0.00	0.00	
6,900.0	12.32	293.63	6,810.5	341.4	-780.5	-228.1	0.00	0.00	0.00	
7,000.0	12.32	293.63	6,908.2	350.0	-800.0	-233.8	0.00	0.00	0.00	
7,100.0	12.32	293.63	7,005.9	358.5	-819.6	-239.5	0.00	0.00	0.00	
7,200.0	12.32	293.63	7,103.6	367.1	-839.1	-245.2	0.00	0.00	0.00	
7,300.0	12.32	293.63	7,201.3	375.6	-858.6	-250.9	0.00	0.00	0.00	
7,400.0	12.32	293.63	7,299.0	384.1	-878.2	-256.7	0.00	0.00	0.00	
7,500.0	12.32	293.63	7,396.6	392.7	-897.7	-262.4	0.00	0.00	0.00	
7,600.0	12.32	293.63	7,494.3	401.2	-917.3	-268.1	0.00	0.00	0.00	
7,700.0	12.32	293.63	7,592.0	409.8	-936.8	-273.8	0.00	0.00	0.00	
7,800.0	12.32	293.63	7,689.7	418.3	-956.4	-279.5	0.00	0.00	0.00	
7,900.0	12.32	293.63	7,787.4	426.9	-975.9	-285.2	0.00	0.00	0.00	
8,000.0	12.32	293.63	7,885.1	435.4	-995.5	-290.9	0.00	0.00	0.00	
8,100.0	12.32	293.63	7,982.8	444.0	-1,015.0	-296.6	0.00	0.00	0.00	
8,200.0	12.32	293.63	8,080.5	452.5	-1,034.6	-302.4	0.00	0.00	0.00	
8,300.0	12.32	293.63	8,178.2	461.1	-1,054.1	-308.1	0.00	0.00	0.00	
8,400.0	12.32	293.63	8,275.9	469.6	-1,073.6	-313.8	0.00	0.00	0.00	
8,500.0	12.32	293.63	8,373.6	478.2	-1,093.2	-319.5	0.00	0.00	0.00	
8,600.0	12.32	293.63	8,471.3	486.7	-1,112.7	-325.2	0.00	0.00	0.00	
8,700.0	12.32	293.63	8,569.0	495.3	-1,132.3	-330.9	0.00	0.00	0.00	
8,800.0	12.32	293.63	8,666.7	503.8	-1,151.8	-336.6	0.00	0.00	0.00	
8,900.0	12.32	293.63	8,764.4	512.4	-1,171.4	-342.3	0.00	0.00	0.00	
9,000.0	12.32	293.63	8,862.1	520.9	-1,190.9	-348.1	0.00	0.00	0.00	
9,100.0	12.32	293.63	8,959.8	529.5	-1,210.5	-353.8	0.00	0.00	0.00	
9,200.0	12.32	293.63	9,057.5	538.0	-1,230.0	-359.5	0.00	0.00	0.00	
9,300.0	12.32	293.63	9,155.2	546.6	-1,249.5	-365.2	0.00	0.00	0.00	
9,400.0	12.32	293.63	9,252.9	555.1	-1,269.1	-370.9	0.00	0.00	0.00	
9,500.0	12.32	293.63	9,350.6	563.7	-1,288.6	-376.6	0.00	0.00	0.00	
9,600.0	12.32	293.63	9,448.3	572.2	-1,308.2	-382.3	0.00	0.00	0.00	
9,655.8	12.32	293.63	9,502.9	577.0	-1,319.1	-385.5	0.00	0.00	0.00	
9,700.0	11.43	293.63	9,546.1	580.7	-1,327.4	-387.9	2.00	-2.00	0.00	
9,800.0	9.43	293.63	9,644.4	587.9	-1,344.0	-392.8	2.00	-2.00	0.00	
9,900.0	7.43	293.63	9,743.3	593.8	-1,357.4	-396.7	2.00	-2.00	0.00	
10,000.0	5.43	293.63	9,842.7	598.3	-1,367.7	-399.7	2.00	-2.00	0.00	
10,100.0	3.43	293.63	9,942.4	601.4	-1,374.8	-401.8	2.00	-2.00	0.00	
10,200.0	1.43	293.63	10,042.3	603.1	-1,378.7	-402.9	2.00	-2.00	0.00	

Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Delaware Ranch 11/14 W2BO Fed Com #1H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 3001.0usft (Original Well Elev)
Project:	Eddy County, New Mexico NAD 83	MD Reference:	WELL @ 3001.0usft (Original Well Elev)
Site:	Delaware Ranch 11/14 W2BO Fed Com #1H	North Reference:	Grid
Well:	Sec 11, T26S, R28E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 330 FSL & 2300 FEL (14)		
Design:	Design #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
10,271.7	0.00	0.00	10,114.0	603.4	-1,379.5	-403.2	2.00	-2.00	0.00	
KOP: 10 FNL & 2300 FEL (11)										
10,300.0	2.83	180.00	10,142.3	602.7	-1,379.5	-402.5	10.00	10.00	0.00	
10,350.0	7.83	180.00	10,192.0	598.1	-1,379.5	-397.9	10.00	10.00	0.00	
10,400.0	12.83	180.00	10,241.2	589.1	-1,379.5	-389.0	10.00	10.00	0.00	
10,450.0	17.83	180.00	10,289.4	575.9	-1,379.5	-375.9	10.00	10.00	0.00	
10,500.0	22.83	180.00	10,336.3	558.6	-1,379.5	-358.7	10.00	10.00	0.00	
10,550.0	27.83	180.00	10,381.5	537.2	-1,379.5	-337.6	10.00	10.00	0.00	
10,600.0	32.83	180.00	10,424.6	511.9	-1,379.5	-312.6	10.00	10.00	0.00	
10,650.0	37.83	180.00	10,465.4	483.0	-1,379.5	-284.0	10.00	10.00	0.00	
10,700.0	42.82	180.00	10,503.5	450.7	-1,379.5	-252.0	10.00	10.00	0.00	
10,750.0	47.82	180.00	10,538.7	415.2	-1,379.5	-216.8	10.00	10.00	0.00	
10,800.0	52.82	180.00	10,570.6	376.7	-1,379.5	-178.7	10.00	10.00	0.00	
10,850.0	57.82	180.00	10,599.0	335.6	-1,379.5	-138.0	10.00	10.00	0.00	
10,900.0	62.82	180.00	10,623.8	292.1	-1,379.5	-95.0	10.00	10.00	0.00	
10,909.8	63.80	180.00	10,628.1	283.4	-1,379.5	-86.3	10.00	10.00	0.00	
FTP: 330 FNL & 2300 FEL (11)										
10,950.0	67.82	180.00	10,644.6	246.7	-1,379.5	-50.0	10.00	10.00	0.00	
11,000.0	72.82	180.00	10,661.5	199.7	-1,379.5	-3.4	10.00	10.00	0.00	
11,050.0	77.82	180.00	10,674.1	151.3	-1,379.5	44.4	10.00	10.00	0.00	
11,100.0	82.82	180.00	10,682.5	102.0	-1,379.5	93.2	10.00	10.00	0.00	
11,150.0	87.82	180.00	10,686.6	52.2	-1,379.5	142.5	10.00	10.00	0.00	
11,171.9	90.01	180.00	10,687.0	30.4	-1,379.5	164.2	10.00	10.00	0.00	
LP: 583 FNL & 2300 FEL (11)										
11,176.1	90.43	180.00	10,687.0	26.1	-1,379.5	168.4	10.00	10.00	0.00	
11,200.0	90.43	180.00	10,686.8	2.2	-1,379.5	192.0	0.00	0.00	0.00	
11,300.0	90.43	180.00	10,686.1	-97.8	-1,379.5	291.0	0.00	0.00	0.00	
11,400.0	90.43	180.00	10,685.3	-197.8	-1,379.4	390.0	0.00	0.00	0.00	
11,500.0	90.43	180.00	10,684.6	-297.8	-1,379.4	489.0	0.00	0.00	0.00	
11,600.0	90.43	180.00	10,683.8	-397.8	-1,379.4	588.0	0.00	0.00	0.00	
11,700.0	90.43	180.00	10,683.1	-497.8	-1,379.4	687.0	0.00	0.00	0.00	
11,800.0	90.43	180.00	10,682.3	-597.8	-1,379.4	786.0	0.00	0.00	0.00	
11,900.0	90.43	180.00	10,681.6	-697.8	-1,379.4	885.0	0.00	0.00	0.00	
11,946.4	90.43	180.00	10,681.2	-744.2	-1,379.4	931.0	0.00	0.00	0.00	
PPP2: 1328 FNL & 2300 FEL (11)										
12,000.0	90.43	180.00	10,680.8	-797.8	-1,379.4	984.0	0.00	0.00	0.00	
12,100.0	90.43	180.00	10,680.1	-897.7	-1,379.4	1,083.0	0.00	0.00	0.00	
12,200.0	90.43	180.00	10,679.3	-997.7	-1,379.4	1,182.0	0.00	0.00	0.00	
12,300.0	90.43	180.00	10,678.6	-1,097.7	-1,379.4	1,281.0	0.00	0.00	0.00	
12,400.0	90.43	180.00	10,677.8	-1,197.7	-1,379.4	1,380.0	0.00	0.00	0.00	
12,500.0	90.43	180.00	10,677.1	-1,297.7	-1,379.4	1,479.0	0.00	0.00	0.00	
12,600.0	90.43	180.00	10,676.3	-1,397.7	-1,379.4	1,578.0	0.00	0.00	0.00	
12,700.0	90.43	180.00	10,675.6	-1,497.7	-1,379.3	1,677.0	0.00	0.00	0.00	
12,800.0	90.43	180.00	10,674.8	-1,597.7	-1,379.3	1,776.0	0.00	0.00	0.00	
12,900.0	90.43	180.00	10,674.1	-1,697.7	-1,379.3	1,875.0	0.00	0.00	0.00	
13,000.0	90.43	180.00	10,673.3	-1,797.7	-1,379.3	1,974.0	0.00	0.00	0.00	
13,100.0	90.43	180.00	10,672.6	-1,897.7	-1,379.3	2,073.0	0.00	0.00	0.00	
13,200.0	90.43	180.00	10,671.8	-1,997.7	-1,379.3	2,172.0	0.00	0.00	0.00	
13,300.0	90.43	180.00	10,671.0	-2,097.7	-1,379.3	2,271.0	0.00	0.00	0.00	
13,400.0	90.43	180.00	10,670.3	-2,197.7	-1,379.3	2,370.0	0.00	0.00	0.00	
13,500.0	90.43	180.00	10,669.5	-2,297.7	-1,379.3	2,469.0	0.00	0.00	0.00	
13,600.0	90.43	180.00	10,668.8	-2,397.7	-1,379.3	2,568.0	0.00	0.00	0.00	
13,700.0	90.43	180.00	10,668.0	-2,497.7	-1,379.3	2,667.0	0.00	0.00	0.00	

Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Delaware Ranch 11/14 W2BO Fed Com #1H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 3001.0usft (Original Well Elev)
Project:	Eddy County, New Mexico NAD 83	MD Reference:	WELL @ 3001.0usft (Original Well Elev)
Site:	Delaware Ranch 11/14 W2BO Fed Com #1H	North Reference:	Grid
Well:	Sec 11, T26S, R28E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 330 FSL & 2300 FEL (14)		
Design:	Design #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
13,800.0	90.43	180.00	10,667.3	-2,597.7	-1,379.3	2,766.0	0.00	0.00	0.00	
13,900.0	90.43	180.00	10,666.5	-2,697.7	-1,379.3	2,865.0	0.00	0.00	0.00	
14,000.0	90.43	180.00	10,665.8	-2,797.7	-1,379.2	2,964.0	0.00	0.00	0.00	
14,100.0	90.43	180.00	10,665.0	-2,897.7	-1,379.2	3,063.0	0.00	0.00	0.00	
14,200.0	90.43	180.00	10,664.3	-2,997.7	-1,379.2	3,162.0	0.00	0.00	0.00	
14,300.0	90.43	180.00	10,663.5	-3,097.7	-1,379.2	3,261.0	0.00	0.00	0.00	
14,400.0	90.43	180.00	10,662.8	-3,197.7	-1,379.2	3,360.0	0.00	0.00	0.00	
14,500.0	90.43	180.00	10,662.0	-3,297.7	-1,379.2	3,459.0	0.00	0.00	0.00	
14,600.0	90.43	180.00	10,661.3	-3,397.7	-1,379.2	3,558.0	0.00	0.00	0.00	
14,700.0	90.43	180.00	10,660.5	-3,497.7	-1,379.2	3,657.0	0.00	0.00	0.00	
14,800.0	90.43	180.00	10,659.8	-3,597.7	-1,379.2	3,756.0	0.00	0.00	0.00	
14,900.0	90.43	180.00	10,659.0	-3,697.7	-1,379.2	3,855.0	0.00	0.00	0.00	
15,000.0	90.43	180.00	10,658.3	-3,797.7	-1,379.2	3,954.0	0.00	0.00	0.00	
15,100.0	90.43	180.00	10,657.5	-3,897.7	-1,379.2	4,053.0	0.00	0.00	0.00	
15,200.0	90.43	180.00	10,656.8	-3,997.7	-1,379.1	4,152.0	0.00	0.00	0.00	
15,300.0	90.43	180.00	10,656.0	-4,097.7	-1,379.1	4,251.0	0.00	0.00	0.00	
15,400.0	90.43	180.00	10,655.3	-4,197.7	-1,379.1	4,350.0	0.00	0.00	0.00	
15,500.0	90.43	180.00	10,654.5	-4,297.7	-1,379.1	4,449.0	0.00	0.00	0.00	
15,600.0	90.43	180.00	10,653.8	-4,397.6	-1,379.1	4,548.0	0.00	0.00	0.00	
15,700.0	90.43	180.00	10,653.0	-4,497.6	-1,379.1	4,647.0	0.00	0.00	0.00	
15,800.0	90.43	180.00	10,652.3	-4,597.6	-1,379.1	4,746.0	0.00	0.00	0.00	
15,900.0	90.43	180.00	10,651.5	-4,697.6	-1,379.1	4,845.0	0.00	0.00	0.00	
16,000.0	90.43	180.00	10,650.8	-4,797.6	-1,379.1	4,944.0	0.00	0.00	0.00	
16,100.0	90.43	180.00	10,650.0	-4,897.6	-1,379.1	5,043.0	0.00	0.00	0.00	
16,200.0	90.43	180.00	10,649.3	-4,997.6	-1,379.1	5,142.0	0.00	0.00	0.00	
16,300.0	90.43	180.00	10,648.5	-5,097.6	-1,379.1	5,241.0	0.00	0.00	0.00	
16,400.0	90.43	180.00	10,647.8	-5,197.6	-1,379.1	5,340.0	0.00	0.00	0.00	
16,500.0	90.43	180.00	10,647.0	-5,297.6	-1,379.0	5,439.0	0.00	0.00	0.00	
16,600.0	90.43	180.00	10,646.3	-5,397.6	-1,379.0	5,538.0	0.00	0.00	0.00	
16,700.0	90.43	180.00	10,645.5	-5,497.6	-1,379.0	5,637.0	0.00	0.00	0.00	
16,800.0	90.43	180.00	10,644.8	-5,597.6	-1,379.0	5,736.0	0.00	0.00	0.00	
16,900.0	90.43	180.00	10,644.0	-5,697.6	-1,379.0	5,835.0	0.00	0.00	0.00	
17,000.0	90.43	180.00	10,643.3	-5,797.6	-1,379.0	5,934.0	0.00	0.00	0.00	
17,100.0	90.43	180.00	10,642.5	-5,897.6	-1,379.0	6,033.0	0.00	0.00	0.00	
17,200.0	90.43	180.00	10,641.8	-5,997.6	-1,379.0	6,132.0	0.00	0.00	0.00	
17,300.0	90.43	180.00	10,641.0	-6,097.6	-1,379.0	6,231.0	0.00	0.00	0.00	
17,400.0	90.43	180.00	10,640.3	-6,197.6	-1,379.0	6,330.0	0.00	0.00	0.00	
17,500.0	90.43	180.00	10,639.5	-6,297.6	-1,379.0	6,429.0	0.00	0.00	0.00	
17,600.0	90.43	180.00	10,638.8	-6,397.6	-1,379.0	6,528.0	0.00	0.00	0.00	
17,700.0	90.43	180.00	10,638.0	-6,497.6	-1,379.0	6,627.0	0.00	0.00	0.00	
17,800.0	90.43	180.00	10,637.3	-6,597.6	-1,378.9	6,726.0	0.00	0.00	0.00	
17,900.0	90.43	180.00	10,636.5	-6,697.6	-1,378.9	6,825.0	0.00	0.00	0.00	
18,000.0	90.43	180.00	10,635.7	-6,797.6	-1,378.9	6,924.0	0.00	0.00	0.00	
18,100.0	90.43	180.00	10,635.0	-6,897.6	-1,378.9	7,023.0	0.00	0.00	0.00	
18,200.0	90.43	180.00	10,634.2	-6,997.6	-1,378.9	7,122.0	0.00	0.00	0.00	
18,300.0	90.43	180.00	10,633.5	-7,097.6	-1,378.9	7,221.0	0.00	0.00	0.00	
18,400.0	90.43	180.00	10,632.7	-7,197.6	-1,378.9	7,320.0	0.00	0.00	0.00	
18,500.0	90.43	180.00	10,632.0	-7,297.6	-1,378.9	7,419.0	0.00	0.00	0.00	
18,600.0	90.43	180.00	10,631.2	-7,397.6	-1,378.9	7,518.0	0.00	0.00	0.00	
18,700.0	90.43	180.00	10,630.5	-7,497.6	-1,378.9	7,617.0	0.00	0.00	0.00	
18,800.0	90.43	180.00	10,629.7	-7,597.6	-1,378.9	7,716.0	0.00	0.00	0.00	
18,900.0	90.43	180.00	10,629.0	-7,697.6	-1,378.9	7,815.0	0.00	0.00	0.00	
19,000.0	90.43	180.00	10,628.2	-7,797.6	-1,378.8	7,914.0	0.00	0.00	0.00	



Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Delaware Ranch 11/14 W2BO Fed Com #1H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 3001.0usft (Original Well Elev)
Project:	Eddy County, New Mexico NAD 83	MD Reference:	WELL @ 3001.0usft (Original Well Elev)
Site:	Delaware Ranch 11/14 W2BO Fed Com #1H	North Reference:	Grid
Well:	Sec 11, T26S, R28E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 330 FSL & 2300 FEL (14)		
Design:	Design #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
19,100.0	90.43	180.00	10,627.5	-7,897.6	-1,378.8	8,013.0	0.00	0.00	0.00	
19,200.0	90.43	180.00	10,626.7	-7,997.5	-1,378.8	8,112.0	0.00	0.00	0.00	
19,300.0	90.43	180.00	10,626.0	-8,097.5	-1,378.8	8,211.0	0.00	0.00	0.00	
19,400.0	90.43	180.00	10,625.2	-8,197.5	-1,378.8	8,310.0	0.00	0.00	0.00	
19,500.0	90.43	180.00	10,624.5	-8,297.5	-1,378.8	8,409.0	0.00	0.00	0.00	
19,600.0	90.43	180.00	10,623.7	-8,397.5	-1,378.8	8,508.0	0.00	0.00	0.00	
19,700.0	90.43	180.00	10,623.0	-8,497.5	-1,378.8	8,607.0	0.00	0.00	0.00	
19,800.0	90.43	180.00	10,622.2	-8,597.5	-1,378.8	8,706.0	0.00	0.00	0.00	
19,900.0	90.43	180.00	10,621.5	-8,697.5	-1,378.8	8,805.0	0.00	0.00	0.00	
20,000.0	90.43	180.00	10,620.7	-8,797.5	-1,378.8	8,904.0	0.00	0.00	0.00	
20,100.0	90.43	180.00	10,620.0	-8,897.5	-1,378.8	9,003.0	0.00	0.00	0.00	
20,200.0	90.43	180.00	10,619.2	-8,997.5	-1,378.8	9,102.0	0.00	0.00	0.00	
20,300.0	90.43	180.00	10,618.5	-9,097.5	-1,378.7	9,201.0	0.00	0.00	0.00	
20,400.0	90.43	180.00	10,617.7	-9,197.5	-1,378.7	9,300.0	0.00	0.00	0.00	
20,500.0	90.43	180.00	10,617.0	-9,297.5	-1,378.7	9,399.0	0.00	0.00	0.00	
20,600.0	90.43	180.00	10,616.2	-9,397.5	-1,378.7	9,498.0	0.00	0.00	0.00	
20,700.0	90.43	180.00	10,615.5	-9,497.5	-1,378.7	9,597.0	0.00	0.00	0.00	
20,800.0	90.43	180.00	10,614.7	-9,597.5	-1,378.7	9,696.0	0.00	0.00	0.00	
20,895.9	90.43	180.00	10,614.0	-9,693.4	-1,378.7	9,791.0	0.00	0.00	0.00	
BHL: 330 FSL & 2300 FEL (14)										

Design Targets									
Target Name									
- hit/miss target	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
- Shape									
SHL: 590 FNL & 920 FE - plan hits target center - Point	0.00	0.01	0.0	0.0	0.0	386,705.80	628,413.10	32.0628224	-104.0522421
KOP: 10 FNL & 2300 FE - plan hits target center - Point	0.00	0.00	10,114.0	603.4	-1,379.5	387,309.24	627,033.59	32.0644910	-104.0566903
BHL: 330 FSL & 2300 FI - plan hits target center - Point	0.00	0.00	10,614.0	-9,693.4	-1,378.7	377,012.40	627,034.40	32.0361855	-104.0567729
FTP: 330 FNL & 2300 FI - plan hits target center - Point	0.00	0.00	10,628.2	283.4	-1,379.5	386,989.20	627,033.62	32.0636112	-104.0566929
PPP2: 1328 FNL & 2300 - plan hits target center - Point	0.00	0.00	10,681.2	-744.2	-1,379.4	385,961.61	627,033.70	32.0607864	-104.0567011
LP: 583 FNL & 2300 FEI - plan hits target center - Point	0.00	0.00	10,687.0	30.4	-1,379.5	386,736.17	627,033.64	32.0629157	-104.0566949

Delaware Ranch 11/14 W2BO Fed Com #1H

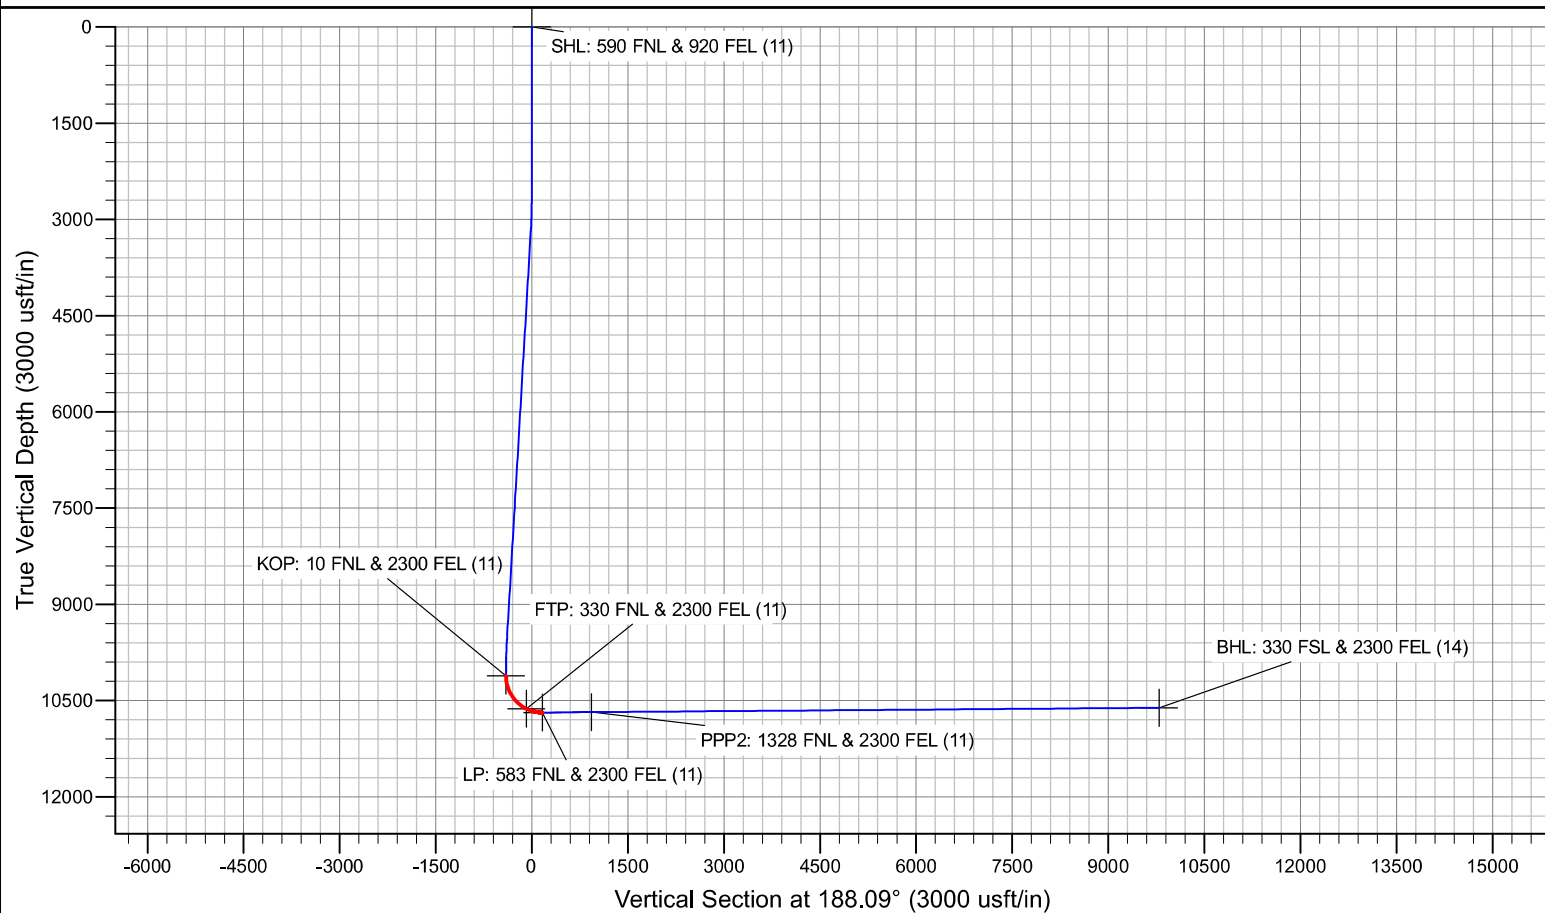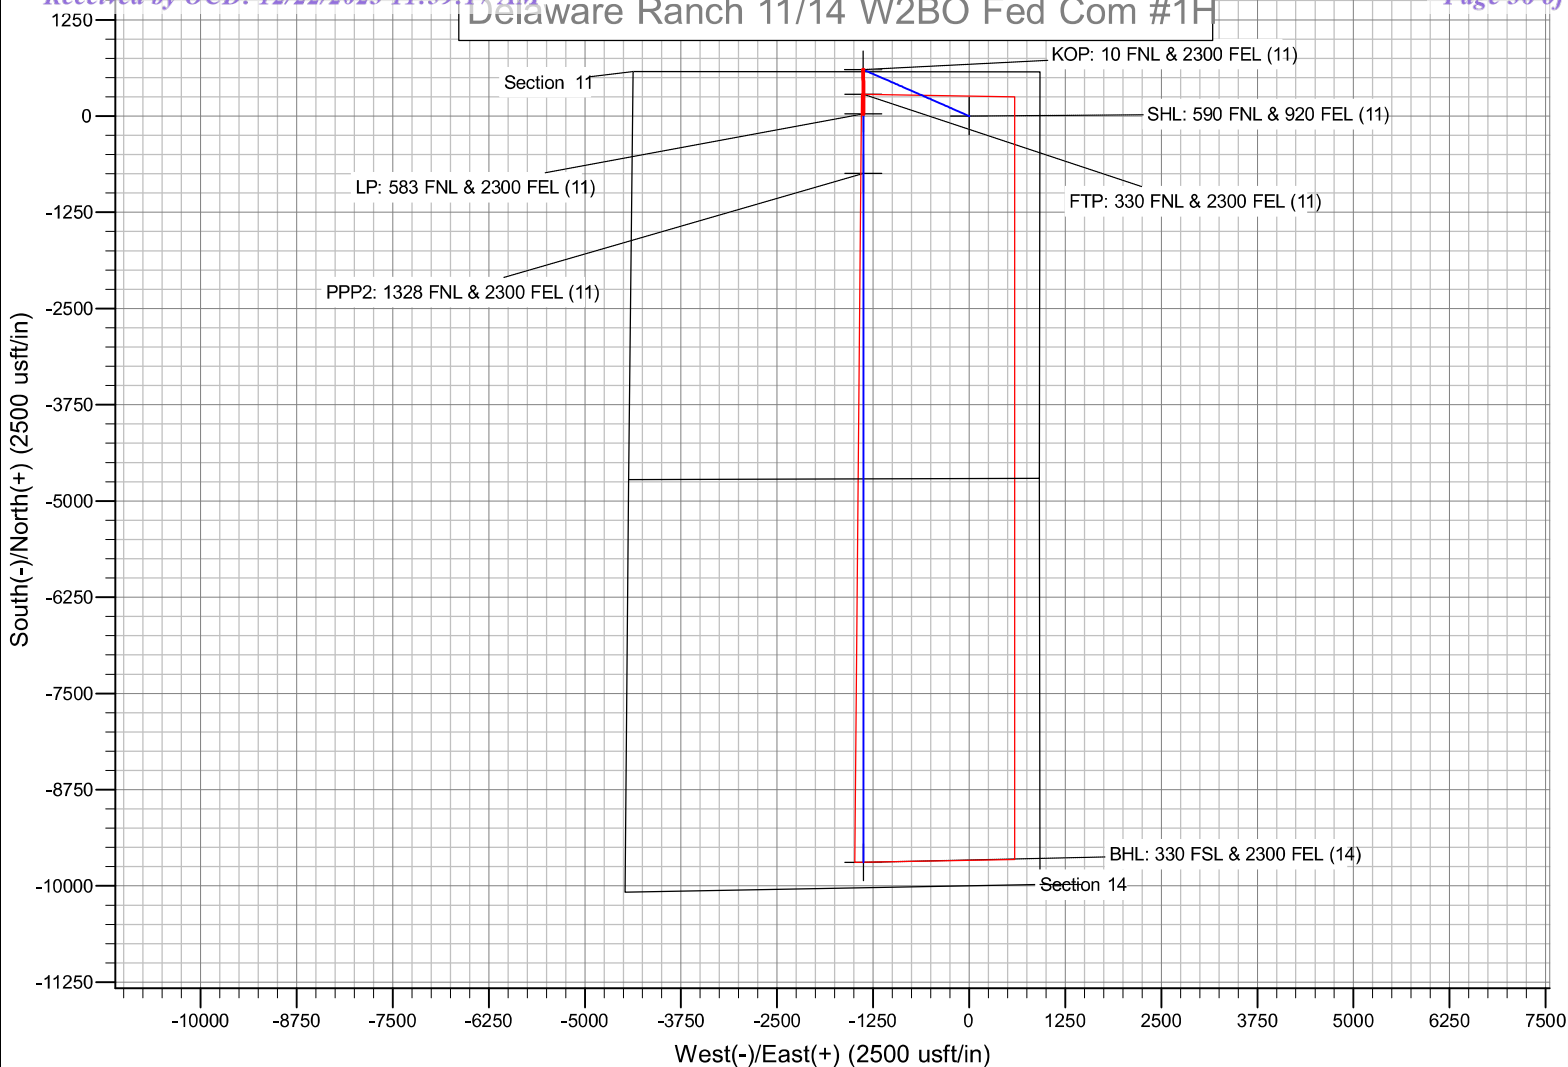

Intent ☒ As Drilled ☐

API #

Operator Name: Mewbourne Oil Co.	Property Name: Delaware Ranch 11/14 W2BO Fed Com	Well Number 1H
-------------------------------------	---	-------------------

Kick Off Point (KOP)

UL B	Section 11	Township 26S	Range 28E	Lot	Feet 10	From N/S N	Feet 2300	From E/W E	County Eddy
Latitude 32.0644910					Longitude -104.0566903				NAD 83

First Take Point (FTP)

UL B	Section 11	Township 26S	Range 28E	Lot	Feet 330	From N/S N	Feet 2300	From E/W E	County Eddy
Latitude 32.0636112					Longitude -104.0566929				NAD 83

Last Take Point (LTP)

UL O	Section 14	Township 26S	Range 28E	Lot	Feet 330	From N/S S	Feet 2300	From E/W E	County Eddy
Latitude 32.0361855					Longitude -104.0567729				NAD 83

Is this well the defining well for the Horizontal Spacing Unit?

☐ N

Is this well an infill well?

☐ Y

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #

Operator Name: Mewbourne Oil Co	Property Name: Delaware Ranch 11/14 W1AP Fed Com	Well Number 1H
------------------------------------	---	-------------------

KZ 06/29/2018

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	Mewbourne Oil Company
LEASE NO.:	NMNM107374
WELL NAME & NO.:	DELAWARE RANCH 11-14 W2BO FED COM 1H
SURFACE HOLE FOOTAGE:	590'/N & 920'/E
BOTTOM HOLE FOOTAGE:	330'/S & 2300'/E
LOCATION:	Section 11, T.26 S., R.28 E., NMP
COUNTY:	Eddy County, New Mexico

COA

H2S	☐ Yes	☒ No	
Potash	☒ None	☐ Secretary	☐ R-111-P
Cave/Karst Potential	☐ Low	☒ Medium	☐ High
Cave/Karst Potential	☐ Critical		
Variance	☐ None	☒ Flex Hose	☐ Other
Wellhead	☐ Conventional	☒ Multibowl	☐ Both
Other	☐ 4 String Area	☐ Capitan Reef	☐ WIPP
Other	☐ Fluid Filled	☐ Cement Squeeze	☐ Pilot Hole
Special Requirements	☐ Water Disposal	☒ COM	☐ Unit

A. HYDROGEN SULFIDE

Hydrogen Sulfide (H2S) monitors shall be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.

B. CASING

Casing Design:

1. The **13-3/8** inch surface casing shall be set at approximately **575** feet (a minimum of **70 feet (Eddy County)** into the Rustler Anhydrite and above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.

- b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The minimum required fill of cement behind the **9-5/8** inch intermediate casing which shall be set at approximately **2,570** feet is:
 - Cement to surface. If cement does not circulate see B.1.a, c-d above.
Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.
Excess cement calculates to 20%, additional cement might be required.
- ❖ In Medium Cave/Karst Areas if cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface.
3. The minimum required fill of cement behind the **7** inch production casing is:

Option 1 (Single Stage):

- Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.
Excess cement calculates to 9%, additional cement might be required.

Option 2:

Operator has proposed a DV tool, the depth may be adjusted as long as the cement is changed proportionally. The DV tool may be cancelled if cement circulates to surface on the first stage.

- a. First stage to DV tool: Cement to circulate. If cement does not circulate off the DV tool, contact the appropriate BLM office before proceeding with second stage cement job.
- b. Second stage above DV tool:
 - Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.
Excess cement calculates to 21%, additional cement might be required.

4. The minimum required fill of cement behind the **4-1/2** inch production liner is:
 - Cement should tie-back **100 feet** into the previous casing. Operator shall provide method of verification.

C. PRESSURE CONTROL

1. **Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'**
2. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
 - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

D. SPECIAL REQUIREMENT (S)

Communitization Agreement

- The operator will submit a Communitization Agreement to the Carlsbad Field Office, 620 E Greene St. Carlsbad, New Mexico 88220, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Eddy County

Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
(575) 361-2822

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)
689-5981

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - Notify the BLM when moving in and removing the Spudder Rig.
 - Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.
 - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not

hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).

- b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the plug. However, **no tests** shall commence until the cement has had a minimum of 24 hours setup time, except the casing pressure test can be initiated immediately after bumping the plug (only applies to single stage cement jobs).
- c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to Onshore Order 2 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
- d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- e. The results of the test shall be reported to the appropriate BLM office.
- f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

OTA03162023

Hydrogen Sulfide Drilling Operations Plan
Mewbourne Oil Company

1. General Requirements

Rule 118 does not apply to this well because MOC has researched this area and no high concentrations of H₂S were found. MOC will have on location and working all H₂S safety equipment before the Delaware formation for purposes of safety and insurance requirements.

2. Hydrogen Sulfide Training

All personnel, whether regularly assigned, contracted, or employed on an unscheduled basis, will have received training from a qualified instructor in the following areas prior to entering the drilling pad area of the well:

1. The hazards and characteristics of hydrogen sulfide gas.
2. The proper use of personal protective equipment and life support systems.
3. The proper use of hydrogen sulfide detectors, alarms, warning systems, briefing areas, evacuation procedures.
4. The proper techniques for first aid and rescue operations.

Additionally, supervisory personnel will be trained in the following areas:

- 1 The effects of hydrogen sulfide on metal components. If high tensile tubular systems are utilized, supervisory personnel will be trained in their special maintenance requirements.
- 2 Corrective action and shut in procedures, blowout prevention, and well control procedures while drilling a well.
- 3 The contents of the Hydrogen Sulfide Drilling Operations Plan.

There will be an initial training session prior to encountering a known hydrogen sulfide source. The initial training session shall include a review of the site specific Hydrogen Sulfide Drilling Operations Plan.

3. Hydrogen Sulfide Safety Equipment and Systems

All hydrogen sulfide safety equipment and systems will be installed, tested, and operational prior to drilling below the 9 5/8" intermediate casing.

1. Well Control Equipment
 - A. Choke manifold with minimum of one adjustable choke/remote choke.
 - B. Blowout preventers equipped with blind rams and pipe rams to accommodate all pipe sizes with properly sized closing unit
 - C. Auxiliary equipment including annular type blowout preventer.
2. Protective Equipment for Essential Personnel

Thirty minute self contained work unit located in the dog house and at briefing areas.

Additionally: If H₂S is encountered in concentrations less than 10 ppm, fans will be placed in work areas to prevent the accumulation of hazardous amounts of poisonous gas. If higher concentrations of H₂S are detected the well will be shut in and a rotating head, mud/gas separator, remote choke and flare line with igniter will be installed.

3. Hydrogen Sulfide Protection and Monitoring Equipment

Two portable hydrogen sulfide monitors positioned on location for optimum coverage and detection. The units shall have audible sirens to notify personnel when hydrogen sulfide levels exceed 20 PPM.

4. Visual Warning Systems

A. Wind direction indicators as indicated on the wellsite diagram.

B. Caution signs shall be posted on roads providing access to location. Signs shall be painted a high visibility color with lettering of sufficient size to be readable at reasonable distances from potentially contaminated areas.

4. **Mud Program**

The mud program has been designed to minimize the amount of hydrogen sulfide entrained in the mud system. Proper mud weight, safe drilling practices, and the use of hydrogen sulfide scavengers will minimize hazards while drilling the well.

5. **Metallurgy**

All tubular systems, wellheads, blowout preventers, drilling spools, kill lines, choke manifolds, and valves shall be suitable for service in a hydrogen sulfide environment when chemically treated.

6. **Communications**

State & County Officials phone numbers are posted on rig floor and supervisors trailer. Communications in company vehicles and toolpushers are either two way radios or cellular phones.

7. **Well Testing**

Drill stem testing is not an anticipated requirement for evaluation of this well. If a drill stem test is required, it will be conducted with a minimum number of personnel in the immediate vicinity. The test will be conducted during daylight hours only.

8. **Emergency Phone Numbers**

Eddy County Sheriff's Office	911 or 575-887-7551
Ambulance Service	911 or 575-885-2111
Carlsbad Fire Dept	911 or 575-885-2111
Loco Hills Volunteer Fire Dept.	911 or 575-677-3266
Closest Medical Facility - Columbia Medical Center of Carlsbad	575-492-5000

Mewbourne Oil Company	Hobbs District Office	575-393-5905
	Fax	575-397-6252
	2nd Fax	575-393-7259

District Manager	Robin Terrell	575-390-4816
Drilling Superintendent	Frosty Lathan	575-390-4103
	Bradley Bishop	575-390-6838
Drilling Foreman	Wesley Noseff	575-441-0729

Operator Name: MEWBOURNE OIL COMPANY

Well Name: DELAWARE RANCH 11 14 W2BO FED COM **Well Number:** 1H

Section 7 - Methods for Handling

Waste type: DRILLING

Waste content description: Drill cuttings

Amount of waste: 940 barrels

Waste disposal frequency : One Time Only

Safe containment description: Drill cuttings will be properly contained in steel tanks (20 yard roll off bins.)

Safe containmant attachment:

Waste disposal type: HAUL TO COMMERCIAL FACILITY **Disposal location ownership:** PRIVATE

Disposal type description:

Disposal location description: NMOCD approved waste disposal locations are CRI or Lea Land, both facilities are located on HWY 62/180, Sec. 27 T20S R32E.

Waste type: SEWAGE

Waste content description: Human waste & grey water

Amount of waste: 1500 gallons

Waste disposal frequency : Weekly

Safe containment description: 2,000 gallon plastic container

Safe containmant attachment:

Waste disposal type: HAUL TO COMMERCIAL FACILITY **Disposal location ownership:** PRIVATE

Disposal type description:

Disposal location description: City of Carlsbad Water Treatment facility

Waste type: GARBAGE

Waste content description: Garbage & trash

Amount of waste: 1500 pounds

Waste disposal frequency : One Time Only

Safe containment description: Enclosed trash trailer

Safe containmant attachment:

Waste disposal type: HAUL TO COMMERCIAL FACILITY **Disposal location ownership:** PRIVATE

Disposal type description:

Disposal location description: Waste Management facility in Carlsbad.

Reserve Pit

Operator Name: MEWBOURNE OIL COMPANY**Well Name:** DELAWARE RANCH 11 14 W2BO FED COM **Well Number:** 1H**Reserve Pit being used?** NO**Temporary disposal of produced water into reserve pit?** NO**Reserve pit length (ft.)****Reserve pit width (ft.)****Reserve pit depth (ft.)****Reserve pit volume (cu. yd.)****Is at least 50% of the reserve pit in cut?****Reserve pit liner****Reserve pit liner specifications and installation description**

Cuttings Area

Cuttings Area being used? NO**Are you storing cuttings on location?** N**Description of cuttings location****Cuttings area length (ft.)****Cuttings area width (ft.)****Cuttings area depth (ft.)****Cuttings area volume (cu. yd.)****Is at least 50% of the cuttings area in cut?****WCuttings area liner****Cuttings area liner specifications and installation description**

Section 8 - Ancillary

Are you requesting any Ancillary Facilities?: N**Ancillary Facilities****Comments:**

Section 9 - Well Site

Well Site Layout Diagram:

Delaware_Ranch_11_14_W2BO_Fed_Com_1H_WellSiteLayout_20221027075427.pdf

Comments: NONE

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 297328

CONDITIONS

Operator: MEWBOURNE OIL CO P.O. Box 5270 Hobbs, NM 88241	OGRID:
	14744
	Action Number: 297328
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

CONDITIONS

Created By	Condition	Condition Date
ward.rikala	Notify OCD 24 hours prior to casing & cement	1/5/2024
ward.rikala	Will require a File As Drilled C-102 and a Directional Survey with the C-104	1/5/2024
ward.rikala	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string	1/5/2024
ward.rikala	Cement is required to circulate on both surface and intermediate1 strings of casing	1/5/2024
ward.rikala	If cement does not circulate on any string, a CBL is required for that string of casing	1/5/2024
ward.rikala	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system	1/5/2024
ward.rikala	This well can not be produced until the well name is changed per proper naming convention.	1/5/2024
