

1625 N. French Dr., Hobbs, NM 88240

State of New Mexico
Energy, Minerals & Natural ResourcesForm C-104
Revised August 1, 2011District I

811 S. First St., Artesia, NM 88210

District III

1000 Rio Brazos Rd., Aztec, NM 87410

District IV

1220 S. St. Francis Dr., Santa Fe, NM 87505

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

Submit one copy to appropriate District Office

☐ AMENDED REPORT**I. REQUEST FOR ALLOWABLE AND AUTHORIZATION TO TRANSPORT**

¹ Operator name and Address OXY USA INC. P.O. BOX 50250 MIDLAND, TX 79710		² OGRID Number: 16696
		³ Reason for Filing Code/ Effective Date: NW - 12/14/2023
⁴ API Number 30 – 015-54030	⁵ Pool Name PIERCE CROSSING; BONE SPRING	⁶ Pool Code 50371
⁷ Property Code: 323066	⁸ Property Name: TIME CC 6-7 FEDERAL COM	⁹ Well Number: 74H

II. ¹⁰ Surface Location

Ul or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South Line	Feet from the	East/West line	County
3	6	24S	29E		450	NORTH	2360	WEST	EDDY

¹¹ Bottom Hole Location

FTP- 996' FNL 486' FEL LTP- 181' FSL 365' FEL

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
P	7	24S	29E		42	SOUTH	359	EAST	EDDY
¹² Lse Code F	¹³ Producing Method Code : P		¹⁴ Gas Connection Date: 12/19/23		¹⁵ C-129 Permit Number		¹⁶ C-129 Effective Date		¹⁷ C-129 Expiration Date

III. Oil and Gas Transporters

¹⁸ Transporter OGRID	¹⁹ Transporter Name and Address	²⁰ O/G/W
214754	LPC CRUDE OIL, INC.	O
151618	ENTERPRISE FIELD SERVICES LLC	G

IV. Well Completion Data

²¹ Spud Date 08/09/23	²² Ready Date 12/14/2023	²³ TD 19545'M 9141'V	²⁴ PBTD 19500'M 9139'V	²⁵ Perforations 9929-19406'	²⁶ DHC, MC
²⁷ Hole Size		²⁸ Casing & Tubing Size		²⁹ Depth Set	³⁰ Sacks Cement
14-3/4"		10-3/4"		472'	430
9-7/8"		7-5/8"		9035'	1957
6-3/4"		5-1/2"		19525'	810
		2-3/8" tbg		9188'	na

V. Well Test Data

³¹ Date New Oil 12/19/23	³² Gas Delivery Date 12/19/23	³³ Test Date 12/21/23	³⁴ Test Length 24 HRS	³⁵ Tbg. Pressure	³⁶ Csg. Pressure 961
³⁷ Choke Size 58	³⁸ Oil 2198	³⁹ Water 2360	⁴⁰ Gas 5059		⁴¹ Test Method F

⁴² I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief.

Signature: 

Printed name: JANA MENDIOLA

Title: SR. REGULATORY ANALYST

E-mail Address:
Janalyn_mendiola@oxy.comDate: 02/20/2024
Phone: 422-695-5936

OIL CONSERVATION DIVISION

Approved by:

PATRICIA MARTINEZ

Title: PETROLEUM SPECIALIST

Approval Date: 5/29/2024

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102 Revised August 1, 2011
Submit one copy to appropriate
District Office

☒ AMENDED REPORT

WELL LOCATION AND ACERAGE DEDICATION AS-DRILLED PLAT

¹ API Number 30-015-54030	² Pool Code 50371	³ Pool Name PIERCE CROSSING; BONE SPRING
⁴ Property Code 323066	⁵ Property Name TIME CC 6_7 FEDERAL COM	⁶ Well Number 74H
⁷ OGRID No. 16696	⁸ Operator Name OXY USA INC.	⁹ Elevation 2960'


¹⁰ Surface Location

UL or lot no. L 3	Section 6	Township 24S	Range 29E	Lot Idn	Feet from the 450	North/South line NORTH	Feet from the 2360	East/West line WEST	County EDDY
----------------------	--------------	-----------------	--------------	---------	----------------------	---------------------------	-----------------------	------------------------	----------------

¹¹ Bottom Hole Location If Different From Surface

UL or lot no. P	Section 7	Township 24S	Range 29E	Lot Idn	Feet from the 42	North/South line SOUTH	Feet from the 359	East/West line EAST	County EDDY
¹² Dedicated Acres 639.88	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.						

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

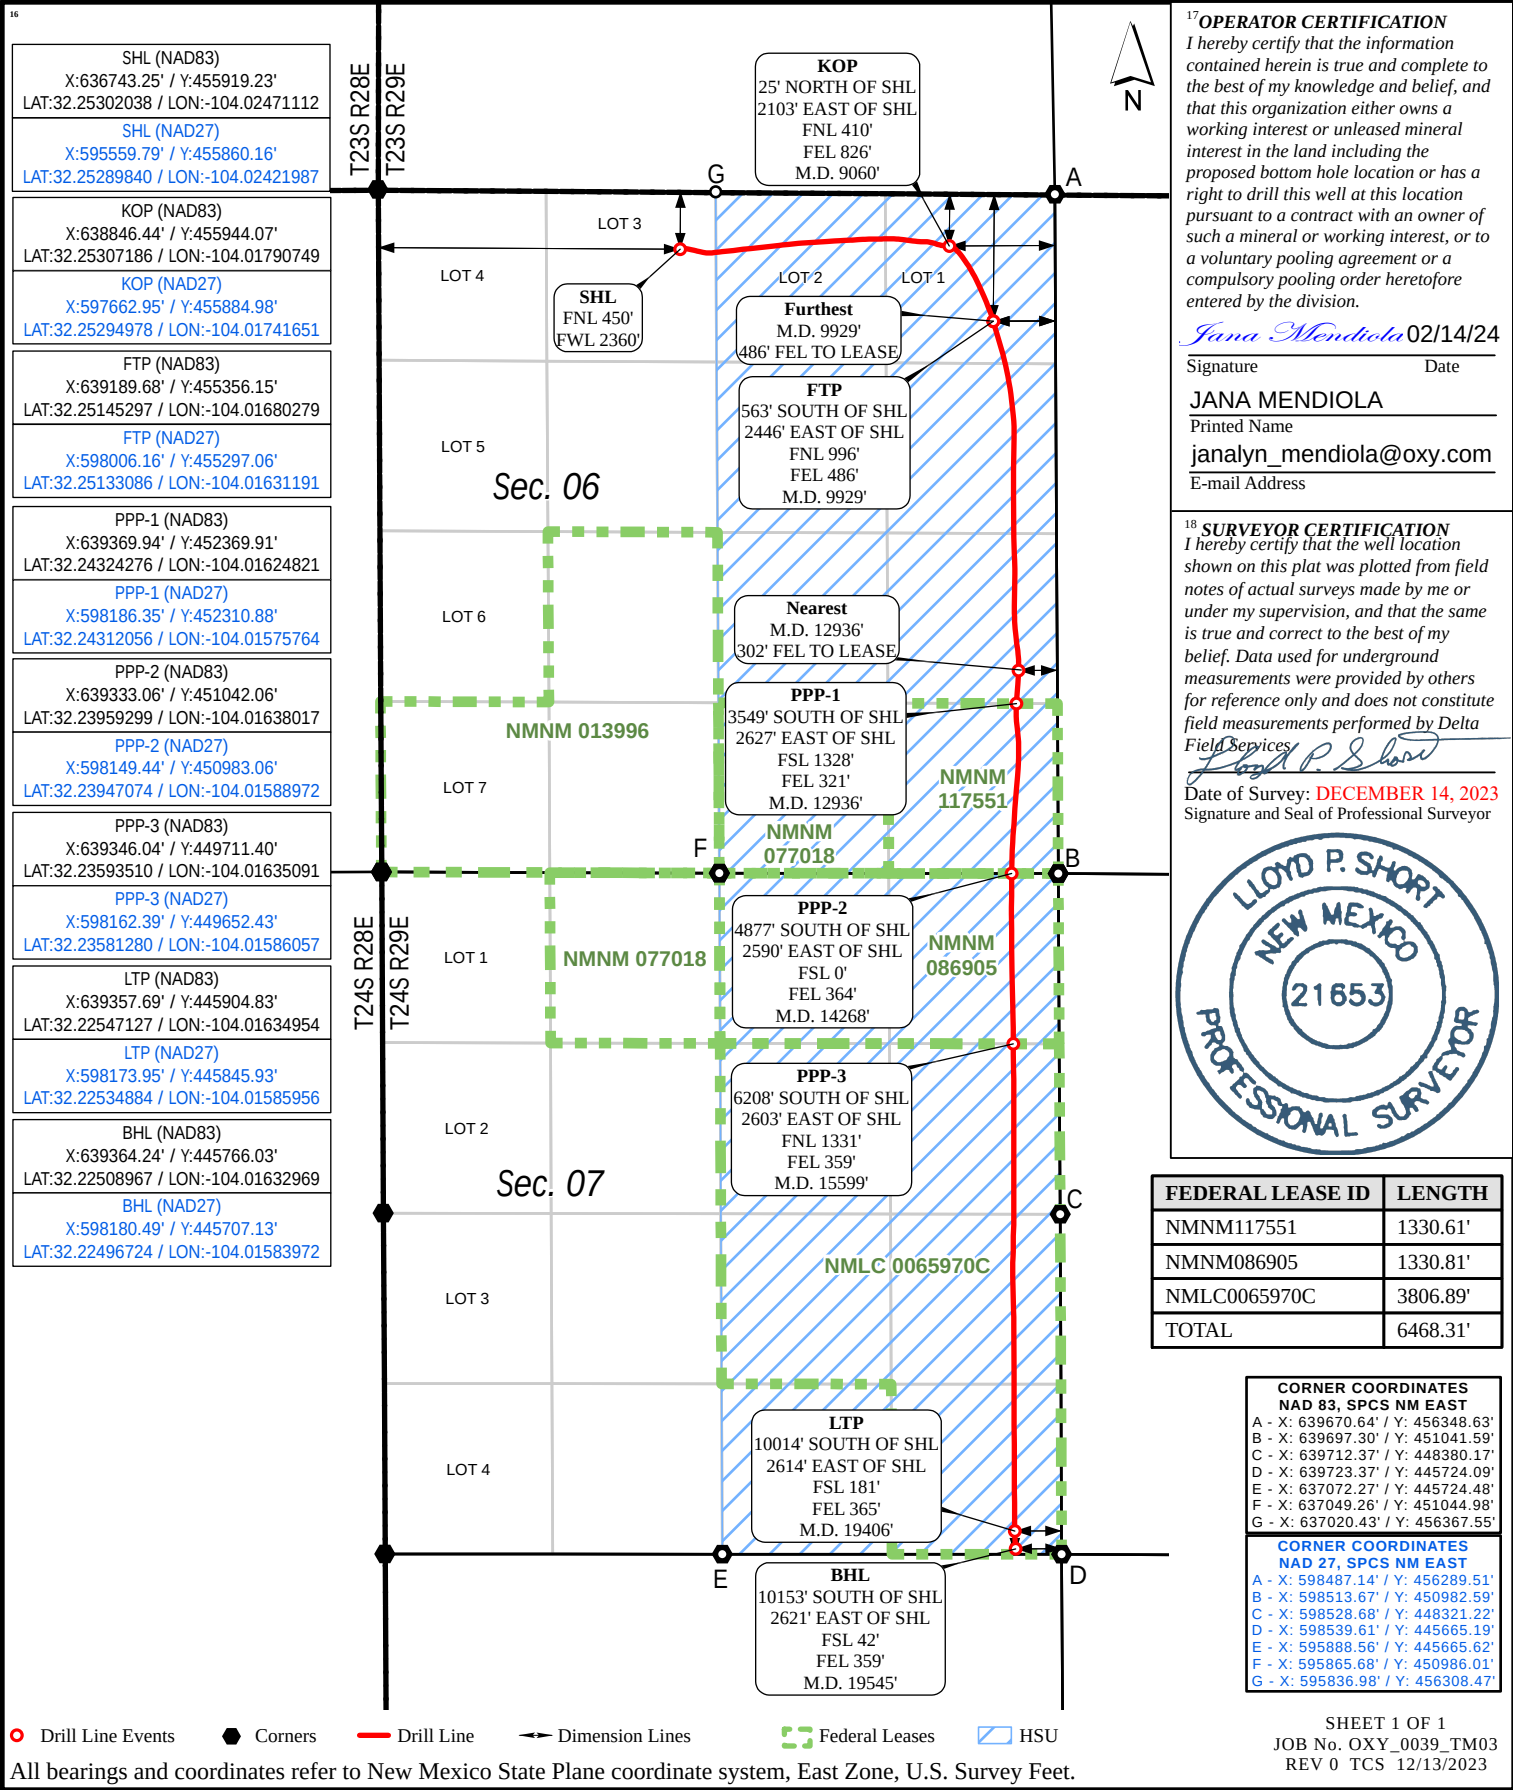




Occidental Petroleum Corporation

FINAL Plan Vs Actual

Project: Eddy County, NM (NAD83)
Site: Time CC 6-7
Well: Time CC 6-7 Federal Com 74H
Wellbore: OH
Design: P1
Rig: Citadel 3

Map System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone Name: New Mexico Eastern Zone

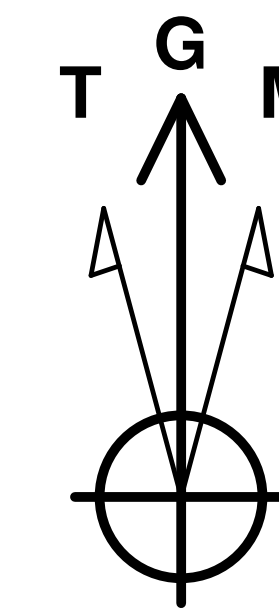

Azimuths to Grid North
True North: -0.16°
Magnetic North: 6.55°
Magnetic Field
Strength: 47422.6nT
Dip Angle: 59.90°
Date: 10/5/2023
Model: IFR

WELL DETAILS



GL 2959.80' + RKB 24' @ 2983.80usft (Citadel 3)
+N/-S +E/-W Northing Easting Latitude Longitude
0.00 0.00 455919.23 636743.25 32° 15' 10.873 N 104° 1' 28.960 W

SECTION DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	Vsect	Departure	Annotation
10.00	0.00	0.00	10.00	0.00	0.00	0.00	0.00	10' KB Offset
9015.00	14.96	88.11	8695.91	25.93	2090.91	501.88	2124.73	Tie-in @ 9015.00' MD
9120.00	20.77	113.92	8795.95	18.81	2121.55	516.49	2156.92	First MWD Svy @ 9120.00' MD
10347.60	90.32	168.41	9115.49	-967.25	2554.56	1579.86	3251.87	Enter 50R/25' @ 10348'MD
12598.50	91.19	178.00	9115.94	-3212.12	2643.53	3774.68	5502.40	Exit 50R/25L' @ 12599'MD
12610.08	90.96	178.59	9115.73	-3223.69	2643.88	3785.97	5513.98	Enter 50R/25L' @ 12610'MD
14273.18	89.55	180.86	9118.53	-4882.36	2589.71	5377.44	7176.01	SLC @ 14273'MD
19486.91	88.43	177.06	9138.56	-10095.25	2617.53	10429.07	12389.45	LTP 100' HLC @ 19487'MD
19525.00	87.68	176.35	9139.86	-10133.26	2619.72	10466.40	12427.53	Last MWD Svy @ 19525.00' MD
19545.00	87.68	176.35	9140.67	-10153.20	2620.99	10486.02	12447.51	Projection to TD @ 19545.00' MD

DESIGN TARGET DETAILS

Name	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
Time CC 6-7 74H FTP	9128.00	331.64	2597.87	456250.87	639341.12	32° 15' 14.080 N	104° 0' 58.696 W
Time CC 6-7 74H LTP	9128.00	-10095.26	2649.64	445823.97	639392.89	32° 13' 30.895 N	104° 0' 58.451 W
Time CC 6-7 74H PBHL	9128.00	-10175.26	2650.04	445743.97	639393.29	32° 13' 30.104 N	104° 0' 58.449 W

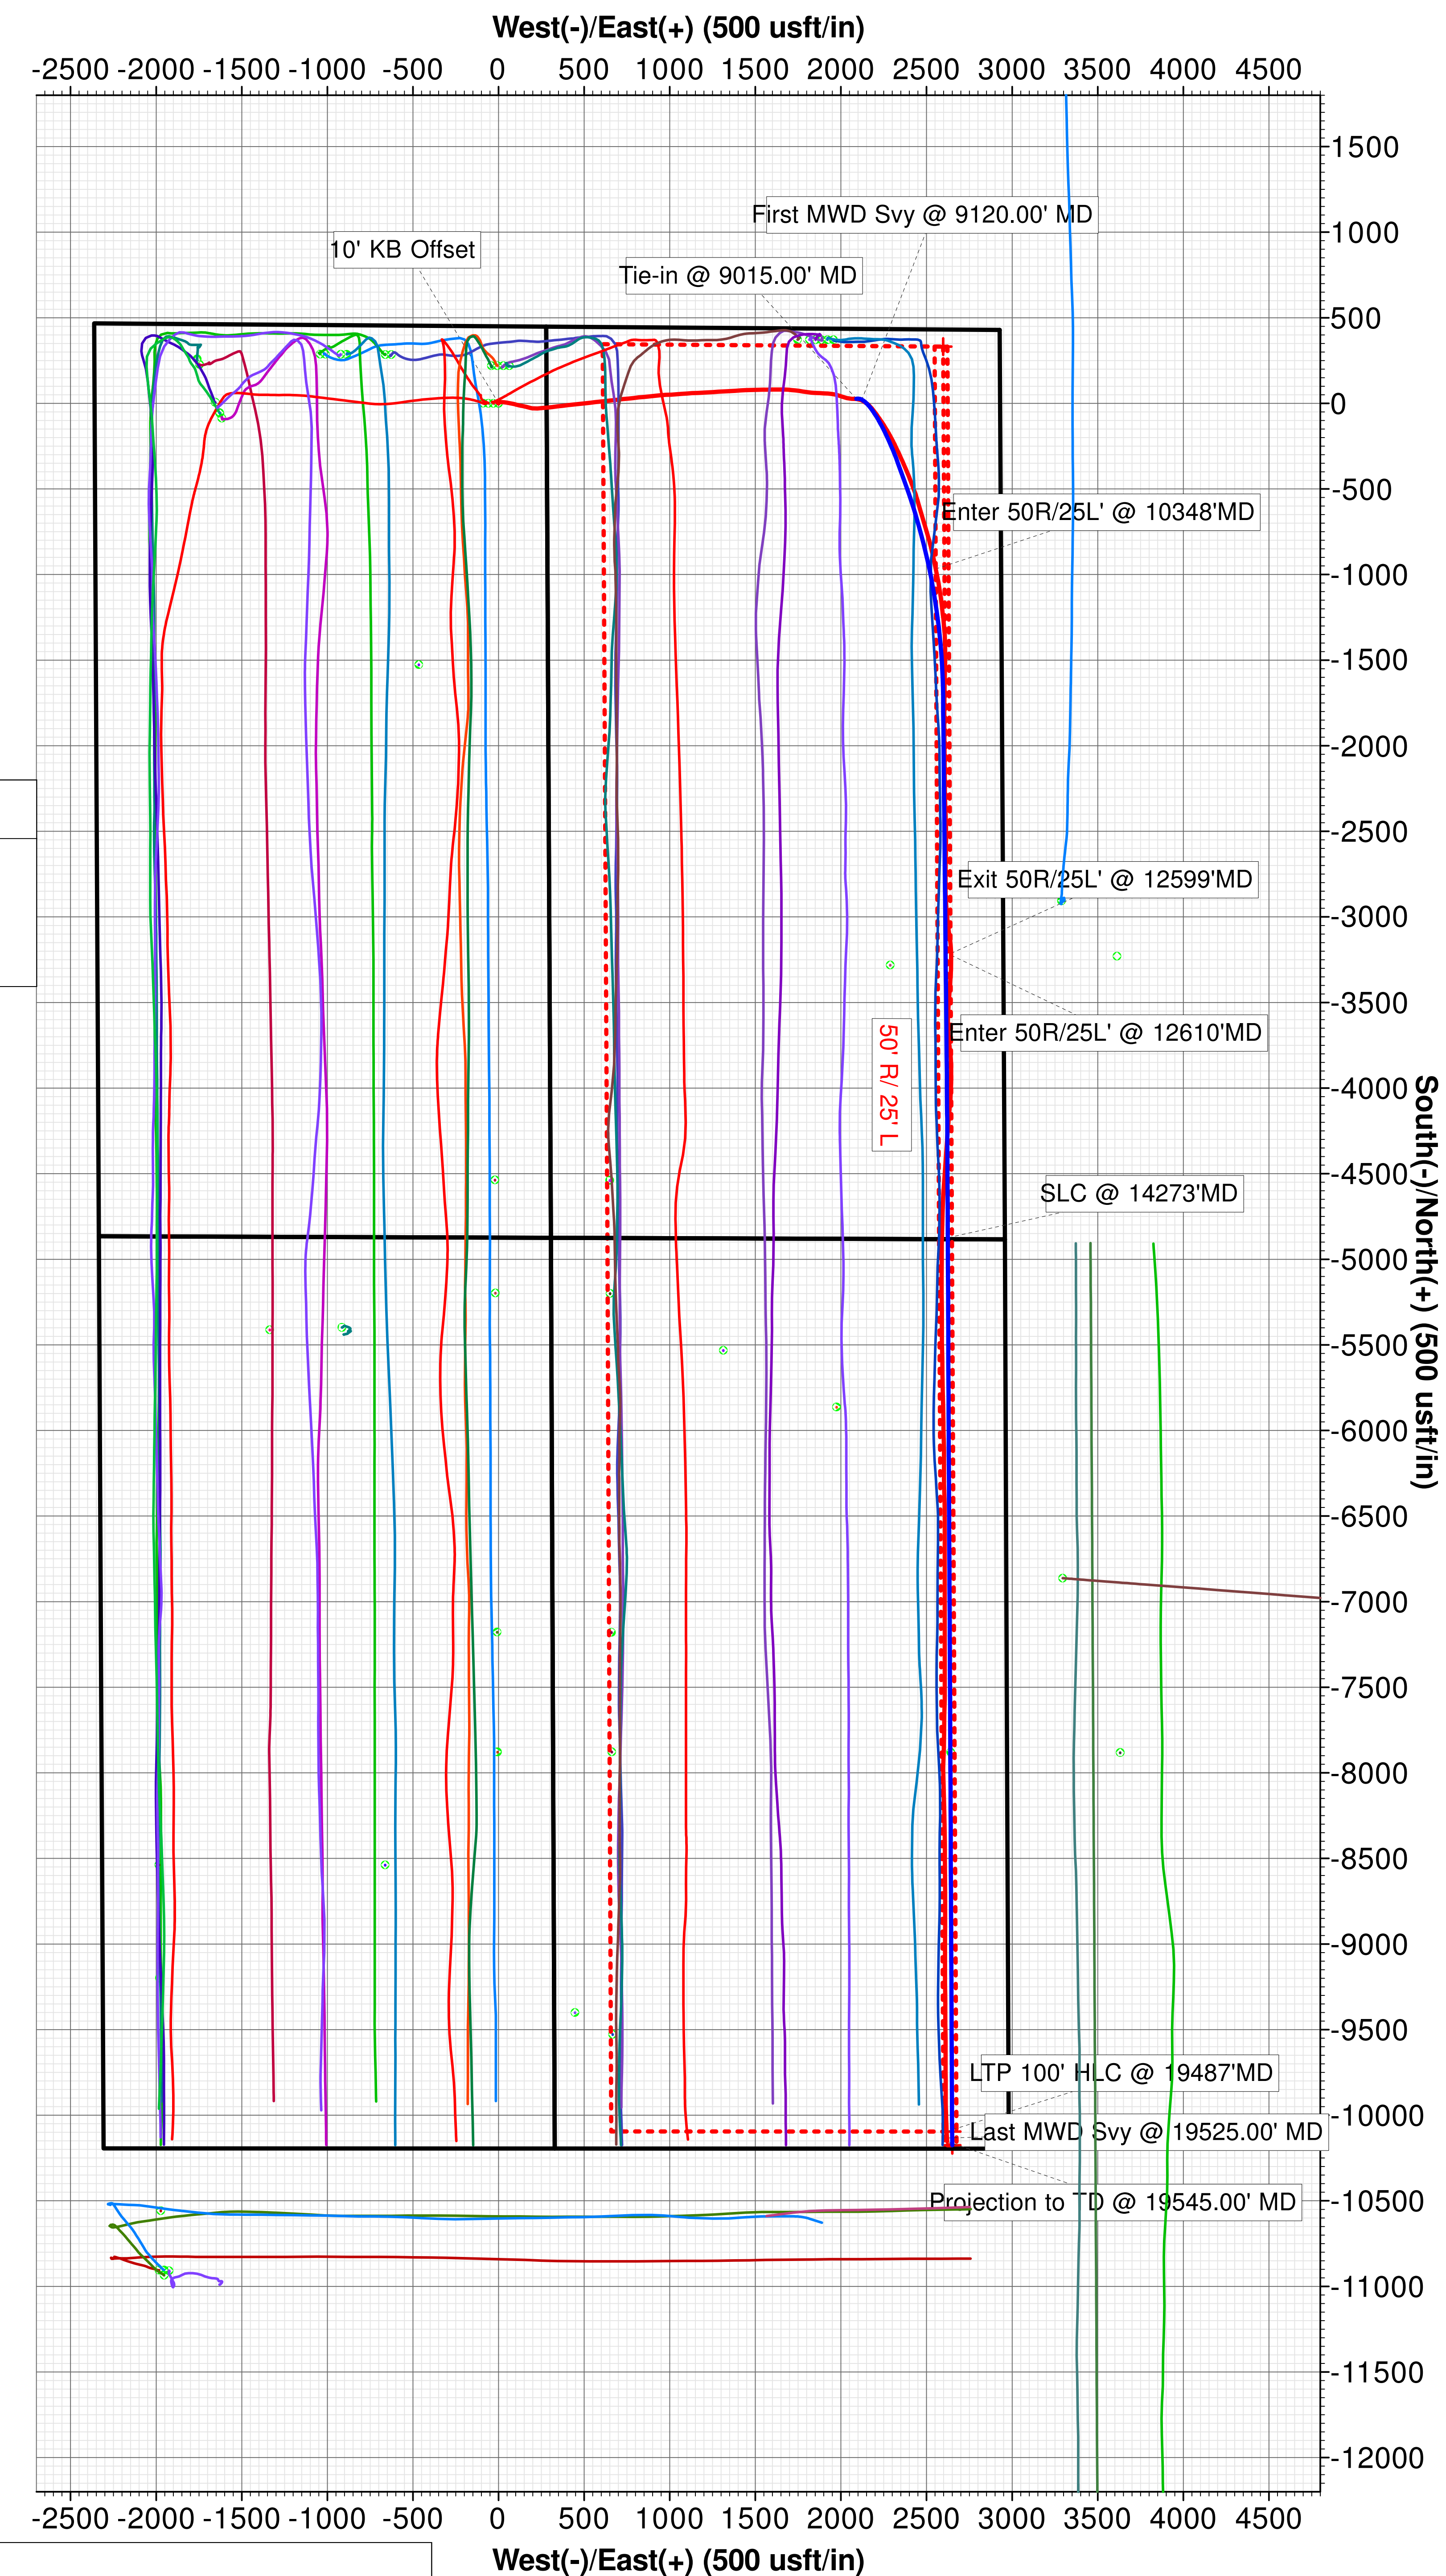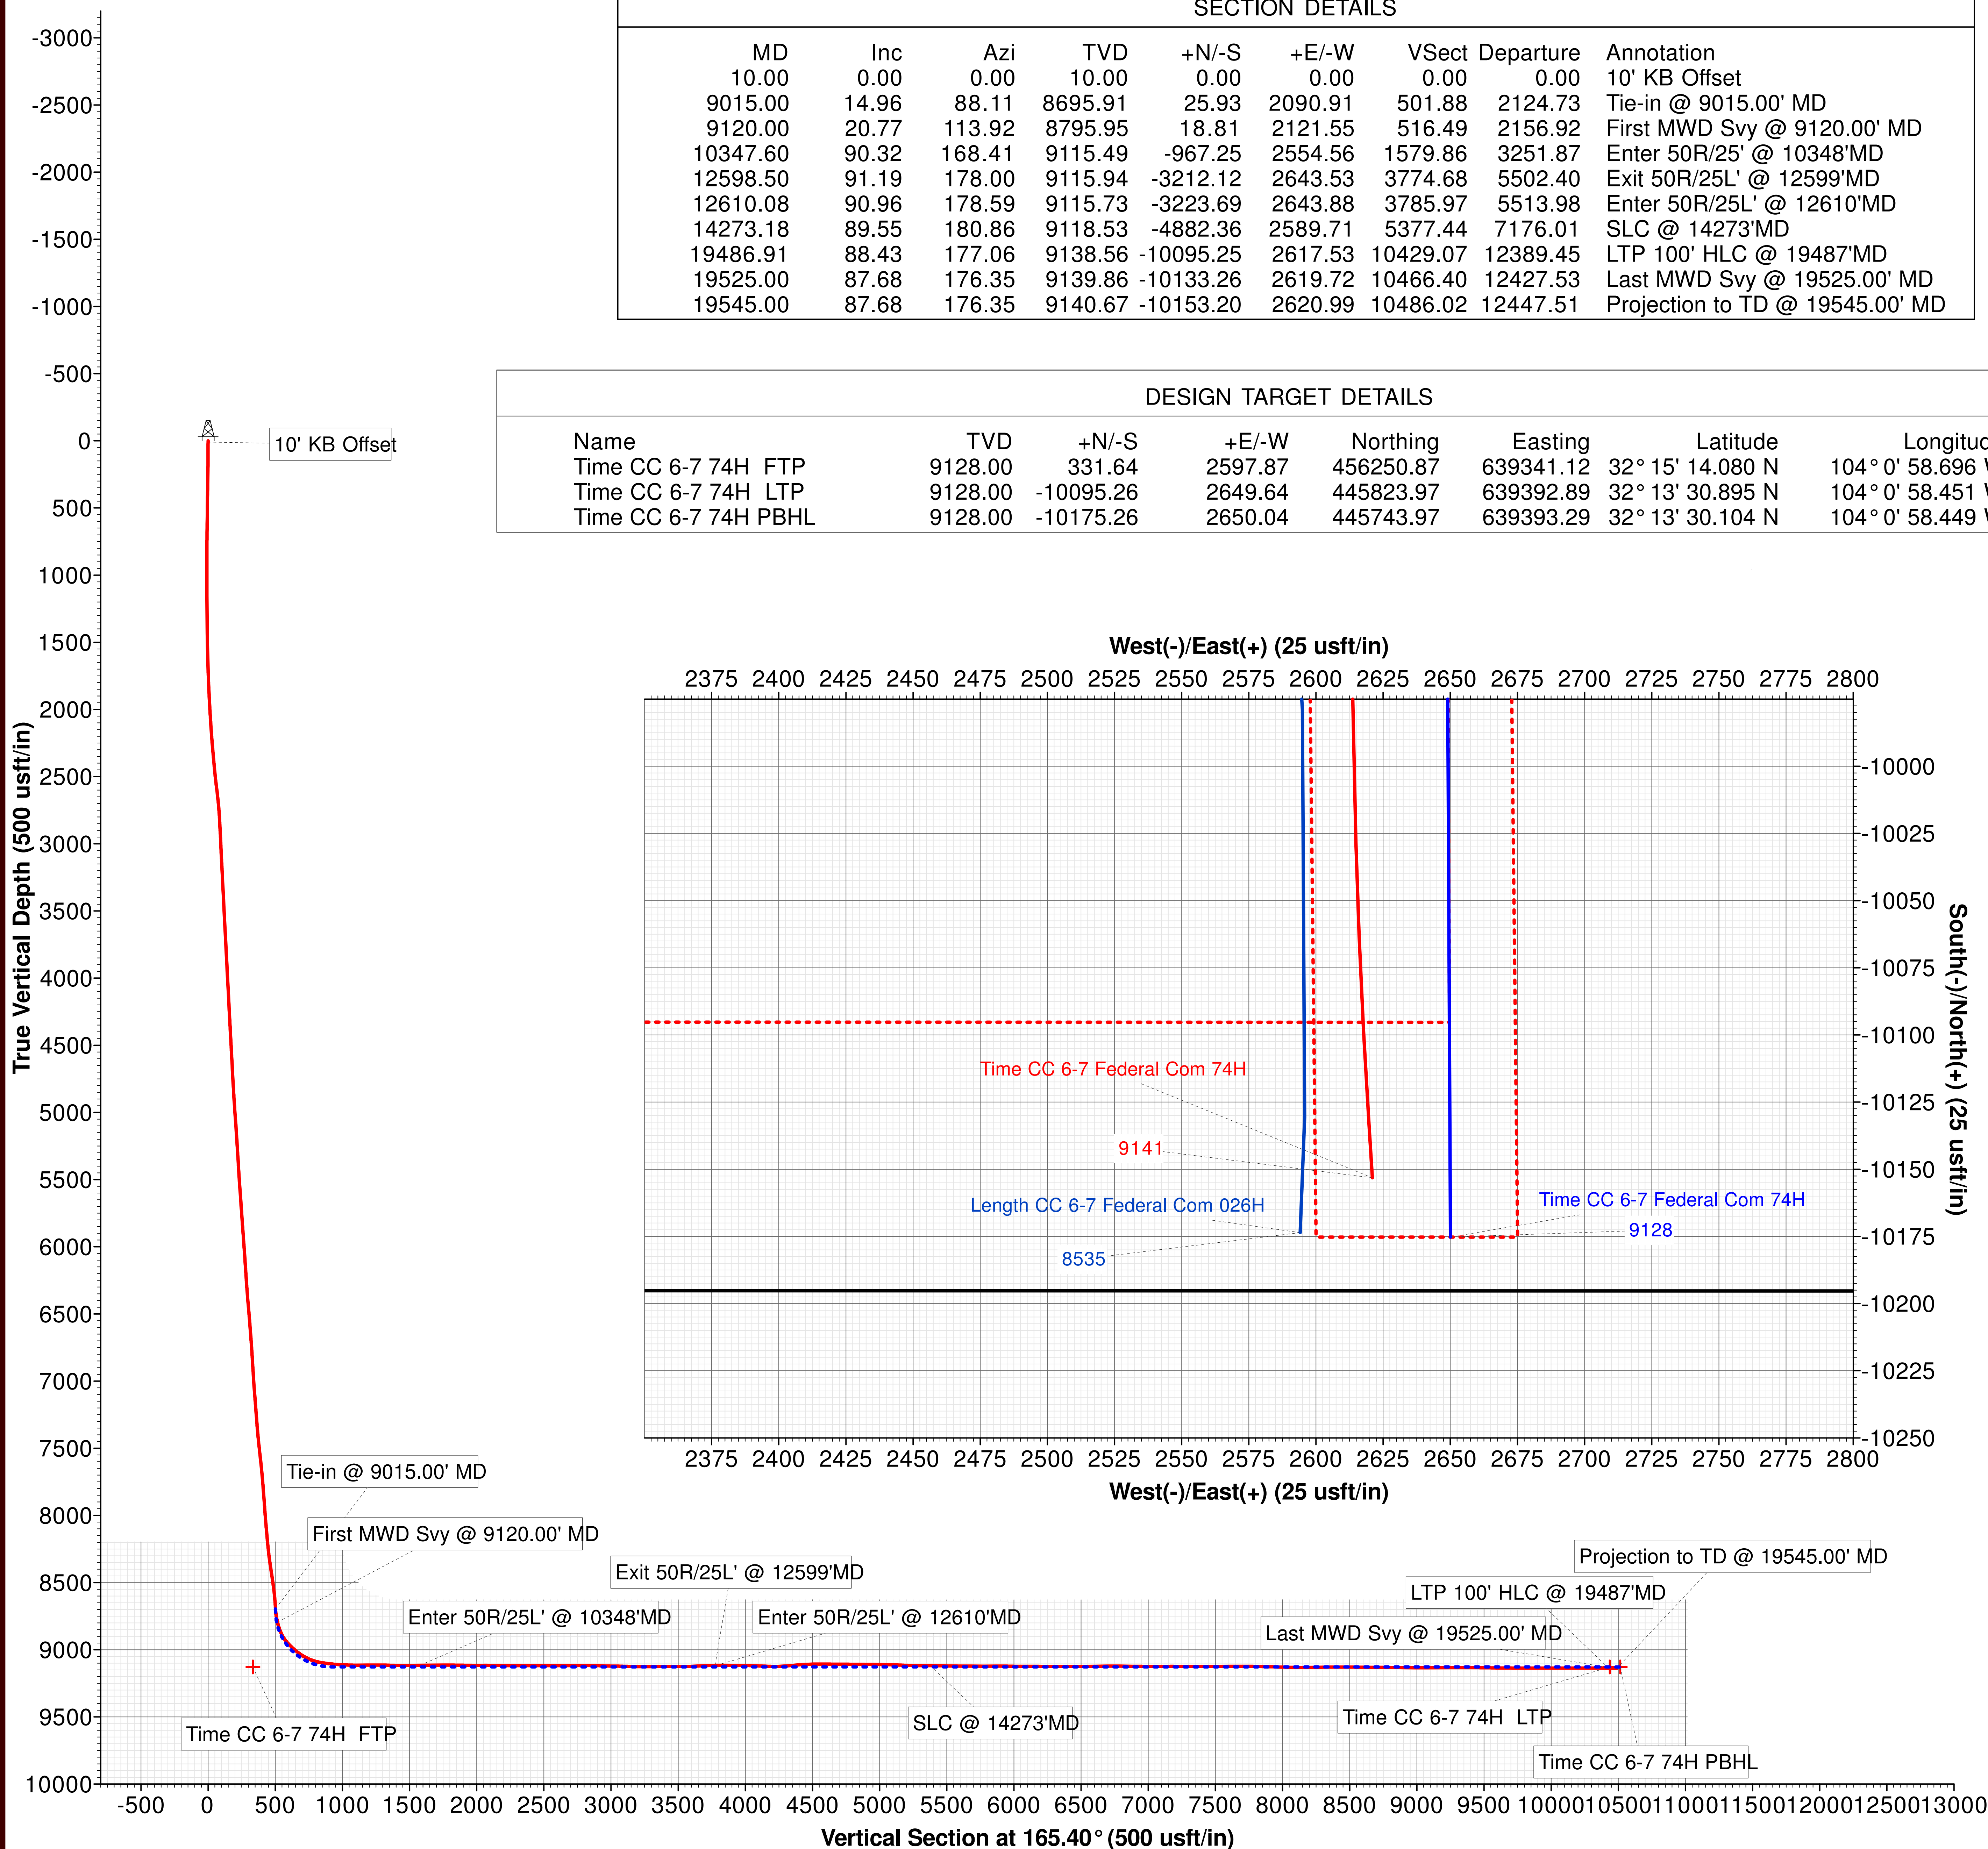

Target Center Line
9128' TVD @ 0' VS; 90.00° INC

Created By: M Hudson
Date: 10:19, October 30 2023

HALLIBURTON | Sperry Drilling

Job# 908908098
Citadel 3

Occidental Petroleum Corporation

Eddy County, NM (NAD83) Time CC 6-7
API# 30-015-54030
Time CC 6-7 Federal Com 74H

OH
Design: Final Surveys

Sperry Drilling Services
Combo Report
30 October, 2023

Well Coordinates:	32° 15' 10.873 N 104° 1' 28.960 W	North American Datum 1983 New Mexico Eastern Zone 455,919.23 N 636,743.25 E
Ground Level:	2,959.80 usft	
Local Coordinate Origin:		Centered on Well Time CC 6-7 Federal Com 74H
Viewing Datum:		GL 2959.80' + RKB 24' @ 2983.80usft (Citadel 3)
TVDs to System:		N
North Reference:		Grid
Unit System:		API-US Survey Feet
Compass Version:	5000.15 Build: 91E	
Report Version:	Midcon Combo v1.15	

HALLIBURTON

HALLIBURTON**Design Report for Time CC 6-7 Federal Com 74H - Final Surveys**

Measured Depth (usft)	Inclination (°)	Grid Azimuth (°)	Vertical Depth (usft)	Local Coordinates		Map Coordinates		Dogleg Rate (°/100ft)	Vertical Section (usft)	Toolface Angle (°)	Comments
				Northing (usft)	Easting (usft)	Northing (usft)	Easting (usft)				
0.00	0.00	0.00	0.00	0.00 N	0.00 E	455,919.23	636,743.25	0.00	0.00	0.00	
10.00	0.00	0.00	10.00	0.00 N	0.00 E	455,919.23	636,743.25	0.00	0.00	0.00	10' KB Offset
72.00	0.34	333.69	72.00	0.17 N	0.08 W	455,919.40	636,743.17	0.55	-0.18	333.69	
122.00	0.33	320.60	122.00	0.41 N	0.24 W	455,919.64	636,743.01	0.15	-0.46	-104.73	
222.00	0.88	318.93	221.99	1.21 N	0.92 W	455,920.44	636,742.33	0.55	-1.40	-2.68	
322.00	0.89	310.28	321.98	2.29 N	2.02 W	455,921.52	636,741.23	0.13	-2.72	-87.53	
422.00	1.26	298.98	421.96	3.32 N	3.57 W	455,922.55	636,739.68	0.42	-4.12	-35.74	
436.00	1.15	301.97	435.96	3.47 N	3.83 W	455,922.70	636,739.42	0.87	-4.32	150.29	
587.00	0.99	310.35	586.93	5.12 N	6.11 W	455,924.35	636,737.14	0.15	-6.50	140.47	
682.00	1.15	303.51	681.92	6.18 N	7.53 W	455,925.41	636,735.72	0.22	-7.88	-42.05	
776.00	0.09	55.79	775.91	6.74 N	8.26 W	455,925.97	636,734.99	1.26	-8.61	175.98	
965.00	0.08	84.63	964.91	6.84 N	8.00 W	455,926.07	636,735.25	0.02	-8.63	117.31	
1,059.00	0.03	117.60	1,058.91	6.83 N	7.92 W	455,926.06	636,735.33	0.06	-8.61	163.42	
1,153.00	1.21	76.79	1,152.90	7.05 N	6.93 W	455,926.28	636,736.32	1.26	-8.57	-41.76	
1,246.00	2.00	91.18	1,245.87	7.24 N	4.35 W	455,926.47	636,738.90	0.95	-8.10	34.35	
1,340.00	2.81	84.49	1,339.78	7.43 N	0.42 W	455,926.66	636,742.83	0.91	-7.29	-22.48	
1,433.00	3.48	89.82	1,432.64	7.65 N	4.68 E	455,926.88	636,747.93	0.79	-6.23	26.26	
1,527.00	4.28	92.95	1,526.43	7.48 N	11.03 E	455,926.71	636,754.28	0.88	-4.46	16.39	
1,621.00	5.01	93.25	1,620.12	7.07 N	18.63 E	455,926.30	636,761.88	0.78	-2.15	2.06	
1,716.00	5.65	93.04	1,714.71	6.59 N	27.44 E	455,925.82	636,770.69	0.67	0.54	-1.85	
1,811.00	6.55	96.61	1,809.17	5.71 N	37.50 E	455,924.94	636,780.75	1.03	3.92	24.64	
1,906.00	7.16	99.04	1,903.49	4.16 N	48.73 E	455,923.39	636,791.98	0.71	8.25	26.64	
2,095.00	8.49	101.75	2,090.73	0.53 S	74.02 E	455,918.70	636,817.27	0.73	19.17	16.85	
2,190.00	8.81	102.09	2,184.64	3.48 S	88.00 E	455,915.75	636,831.25	0.34	25.55	9.25	
2,284.00	9.68	106.28	2,277.42	7.21 S	102.62 E	455,912.02	636,845.87	1.17	32.84	39.81	
2,379.00	10.92	103.24	2,370.89	11.51 S	119.05 E	455,907.72	636,862.30	1.42	41.14	-25.17	
2,473.00	13.21	98.99	2,462.81	15.23 S	138.33 E	455,904.00	636,881.58	2.61	49.60	-23.29	
2,569.00	14.28	105.02	2,556.07	20.01 S	160.60 E	455,899.22	636,903.85	1.86	59.84	56.20	
2,663.00	13.96	103.82	2,647.23	25.72 S	182.81 E	455,893.51	636,926.06	0.46	70.96	-138.13	
2,758.00	13.27	95.05	2,739.57	29.42 S	204.80 E	455,889.81	636,948.05	2.29	80.08	-112.71	
2,853.00	14.04	87.50	2,831.89	29.88 S	227.17 E	455,889.35	636,970.42	2.04	86.17	-70.33	
2,947.00	17.95	84.45	2,922.23	27.98 S	252.99 E	455,891.25	636,996.24	4.25	90.84	-13.60	
3,042.00	19.07	82.64	3,012.32	24.57 S	282.95 E	455,894.66	637,026.20	1.32	95.09	-28.02	
3,137.00	18.63	84.06	3,102.22	21.01 S	313.44 E	455,898.22	637,056.69	0.67	99.33	134.47	
3,231.00	19.79	83.70	3,190.99	17.71 S	344.19 E	455,901.52	637,087.44	1.24	103.89	-6.00	
3,326.00	19.59	83.34	3,280.43	14.10 S	375.99 E	455,905.13	637,119.24	0.25	108.41	-148.93	

HALLIBURTON**Design Report for Time CC 6-7 Federal Com 74H - Final Surveys**

Measured Depth (usft)	Inclination (°)	Grid Azimuth (°)	Vertical Depth (usft)	Local Coordinates		Map Coordinates		Dogleg Rate (°/100ft)	Vertical Section (usft)	Toolface Angle (°)	Comments
				Northing (usft)	Easting (usft)	Northing (usft)	Easting (usft)				
3,421.00	19.70	83.35	3,369.90	10.40 S	407.72 E	455,908.83	637,150.97	0.12	112.82	1.76	
3,515.00	19.81	83.37	3,458.37	6.73 S	439.28 E	455,912.50	637,182.53	0.12	117.22	3.53	
3,705.00	19.73	84.00	3,637.17	0.34 N	503.15 E	455,919.57	637,246.40	0.12	126.48	110.87	
3,799.00	19.66	83.81	3,725.67	3.71 N	534.65 E	455,922.94	637,277.90	0.10	131.16	-137.64	
3,894.00	19.59	83.21	3,815.15	7.31 N	566.35 E	455,926.54	637,309.60	0.22	135.66	-109.44	
3,988.00	19.50	83.83	3,903.74	10.86 N	597.60 E	455,930.09	637,340.85	0.24	140.10	113.75	
4,083.00	19.67	83.69	3,993.24	14.32 N	629.26 E	455,933.55	637,372.51	0.19	144.73	-15.50	
4,177.00	19.64	83.72	4,081.76	17.79 N	660.68 E	455,937.02	637,403.93	0.03	149.30	161.42	
4,272.00	19.49	83.78	4,171.28	21.25 N	692.31 E	455,940.48	637,435.56	0.16	153.92	172.40	
4,367.00	19.77	84.30	4,260.76	24.57 N	724.05 E	455,943.80	637,467.30	0.35	158.71	32.21	
4,461.00	19.42	83.39	4,349.31	27.94 N	755.39 E	455,947.17	637,498.64	0.49	163.34	-139.34	
4,556.00	19.98	83.94	4,438.75	31.48 N	787.22 E	455,950.71	637,530.47	0.62	167.95	18.58	
4,651.00	19.22	84.45	4,528.25	34.70 N	818.92 E	455,953.93	637,562.17	0.82	172.81	167.55	
4,746.00	19.88	83.75	4,617.77	37.97 N	850.54 E	455,957.20	637,593.79	0.74	177.62	-19.87	
4,841.00	19.70	84.45	4,707.16	41.28 N	882.54 E	455,960.51	637,625.79	0.31	182.48	127.55	
4,935.00	19.82	84.03	4,795.63	44.47 N	914.16 E	455,963.70	637,657.41	0.20	187.36	-50.00	
5,030.00	19.45	85.15	4,885.10	47.48 N	945.93 E	455,966.71	637,689.18	0.56	192.46	135.04	
5,125.00	19.82	86.95	4,974.58	49.68 N	977.78 E	455,968.91	637,721.03	0.75	198.36	59.39	
5,219.00	19.77	86.48	5,063.02	51.50 N	1,009.56 E	455,970.73	637,752.81	0.18	204.60	-107.66	
5,314.00	19.23	86.30	5,152.57	53.50 N	1,041.21 E	455,972.73	637,784.46	0.57	210.65	-173.74	
5,409.00	18.83	86.21	5,242.38	55.52 N	1,072.12 E	455,974.75	637,815.37	0.42	216.48	-175.85	
5,503.00	17.97	85.96	5,331.58	57.54 N	1,101.72 E	455,976.77	637,844.97	0.92	221.98	-174.88	
5,598.00	18.58	86.05	5,421.78	59.62 N	1,131.44 E	455,978.85	637,874.69	0.64	227.46	2.69	
5,693.00	18.83	87.09	5,511.77	61.44 N	1,161.85 E	455,980.67	637,905.10	0.44	233.37	53.64	
5,787.00	18.82	87.21	5,600.74	62.95 N	1,192.14 E	455,982.18	637,935.39	0.04	239.54	104.54	
5,882.00	19.13	87.27	5,690.58	64.43 N	1,222.99 E	455,983.66	637,966.24	0.33	245.88	3.63	
5,977.00	19.43	86.52	5,780.25	66.13 N	1,254.32 E	455,985.36	637,997.57	0.41	252.13	-39.89	
6,071.00	20.21	86.71	5,868.68	68.02 N	1,286.13 E	455,987.25	638,029.38	0.83	258.33	4.81	
6,166.00	20.71	86.58	5,957.69	69.96 N	1,319.28 E	455,989.19	638,062.53	0.53	264.80	-5.25	
6,260.00	19.48	86.85	6,045.96	71.81 N	1,351.52 E	455,991.04	638,094.77	1.31	271.13	175.81	
6,355.00	19.76	86.51	6,135.45	73.66 N	1,383.37 E	455,992.89	638,126.62	0.32	277.37	-22.34	
6,450.00	18.44	86.32	6,225.21	75.60 N	1,414.39 E	455,994.83	638,157.64	1.39	283.31	-177.39	
6,545.00	20.14	87.04	6,314.88	77.41 N	1,445.72 E	455,996.64	638,188.97	1.81	289.46	8.30	
6,639.00	20.13	88.72	6,403.13	78.61 N	1,478.06 E	455,997.84	638,221.31	0.62	296.45	91.78	
6,734.00	19.90	89.47	6,492.40	79.12 N	1,510.57 E	455,998.35	638,253.82	0.36	304.14	132.21	
6,829.00	18.00	88.73	6,582.24	79.60 N	1,541.41 E	455,998.83	638,284.66	2.02	311.46	-173.14	
6,924.00	17.75	89.26	6,672.66	80.11 N	1,570.57 E	455,999.34	638,313.82	0.31	318.31	147.20	

HALLIBURTON**Design Report for Time CC 6-7 Federal Com 74H - Final Surveys**

Measured Depth (usft)	Inclination (°)	Grid Azimuth (°)	Vertical Depth (usft)	Local Coordinates		Map Coordinates		Dogleg Rate (°/100ft)	Vertical Section (usft)	Toolface Angle (°)	Comments
				Northing (usft)	Easting (usft)	Northing (usft)	Easting (usft)				
7,018.00	16.10	88.73	6,762.58	80.58 N	1,597.93 E	455,999.81	638,341.18	1.76	324.75	-174.91	
7,112.00	14.86	88.67	6,853.17	81.15 N	1,623.01 E	456,000.38	638,366.26	1.32	330.52	-179.29	
7,207.00	13.79	89.85	6,945.22	81.47 N	1,646.51 E	456,000.70	638,389.76	1.17	336.14	165.31	
7,301.00	13.72	92.79	7,036.52	80.95 N	1,668.85 E	456,000.18	638,412.10	0.75	342.26	97.14	
7,396.00	13.63	93.80	7,128.83	79.66 N	1,691.27 E	455,998.89	638,434.52	0.27	349.16	111.14	
7,491.00	12.60	95.83	7,221.35	77.87 N	1,712.75 E	455,997.10	638,456.00	1.19	356.31	156.89	
7,586.00	12.19	96.41	7,314.14	75.70 N	1,733.02 E	455,994.93	638,476.27	0.45	363.53	163.39	
7,680.00	13.56	97.88	7,405.77	73.08 N	1,753.80 E	455,992.31	638,497.05	1.50	371.30	14.16	
7,775.00	15.27	99.76	7,497.78	69.43 N	1,777.16 E	455,988.66	638,520.41	1.87	380.72	16.22	
7,869.00	16.14	98.00	7,588.27	65.51 N	1,802.30 E	455,984.74	638,545.55	1.06	390.84	-29.55	
7,964.00	15.46	95.14	7,679.68	62.54 N	1,827.99 E	455,981.77	638,571.24	1.09	400.19	-132.50	
8,059.00	14.71	92.79	7,771.40	60.82 N	1,852.65 E	455,980.05	638,595.90	1.02	408.07	-141.93	
8,154.00	14.46	93.26	7,863.34	59.56 N	1,876.54 E	455,978.79	638,619.79	0.29	415.31	154.89	
8,248.00	14.64	89.91	7,954.33	58.91 N	1,900.13 E	455,978.14	638,643.38	0.92	421.89	-79.55	
8,342.00	14.52	95.11	8,045.31	57.88 N	1,923.75 E	455,977.11	638,667.00	1.40	428.84	97.75	
8,437.00	12.96	98.11	8,137.59	55.31 N	1,946.16 E	455,974.54	638,689.41	1.80	436.97	156.90	
8,532.00	11.96	103.24	8,230.35	51.56 N	1,966.29 E	455,970.79	638,709.54	1.57	445.68	134.58	
8,626.00	14.04	108.13	8,321.94	45.78 N	1,986.61 E	455,965.01	638,729.86	2.50	456.39	30.27	
8,721.00	15.49	108.12	8,413.80	38.24 N	2,009.62 E	455,957.47	638,752.87	1.53	469.48	-0.11	
8,815.00	17.37	103.52	8,503.96	31.06 N	2,035.19 E	455,950.29	638,778.44	2.43	482.88	-36.91	
8,910.00	16.45	95.20	8,594.87	26.52 N	2,062.38 E	455,945.75	638,805.63	2.72	494.12	-114.76	
9,005.00	15.30	87.58	8,686.25	25.83 N	2,088.30 E	455,945.06	638,831.55	2.50	501.32	-122.52	
9,015.00	14.96	88.11	8,695.91	25.93 N	2,090.91 E	455,945.16	638,834.16	3.67	501.88	158.12	Tie-in @ 9015.00' MD
9,120.00	20.77	113.92	8,795.95	18.81 N	2,121.55 E	455,938.04	638,864.80	9.23	516.49	66.53	First MWD Svy @ 9120.00' MD
9,215.00	29.70	130.66	8,881.91	3.42 S	2,154.91 E	455,915.81	638,898.16	11.95	546.42	46.46	
9,310.00	46.78	142.59	8,956.35	46.63 S	2,194.13 E	455,872.60	638,937.38	19.52	598.12	28.28	
9,404.00	52.61	145.82	9,017.13	104.79 S	2,235.96 E	455,814.44	638,979.21	6.73	664.94	23.97	
9,499.00	65.56	150.36	9,065.86	173.91 S	2,278.75 E	455,745.32	639,022.00	14.23	742.62	17.96	
9,593.00	79.95	154.40	9,093.66	253.29 S	2,320.14 E	455,665.94	639,063.39	15.85	829.86	15.66	
9,688.00	84.44	155.99	9,106.56	338.70 S	2,359.61 E	455,580.53	639,102.86	5.01	922.47	19.45	
9,782.00	87.57	157.94	9,113.11	424.98 S	2,396.29 E	455,494.25	639,139.54	3.92	1,015.21	31.93	
9,877.00	89.70	160.45	9,115.37	513.75 S	2,430.02 E	455,405.48	639,173.27	3.46	1,109.61	49.71	
9,951.00	91.25	163.73	9,114.76	584.15 S	2,452.77 E	455,335.08	639,196.02	4.90	1,183.47	64.70	
10,046.00	89.38	163.96	9,114.24	675.39 S	2,479.20 E	455,243.84	639,222.45	1.98	1,278.43	172.99	
10,140.00	88.37	163.42	9,116.08	765.59 S	2,505.59 E	455,153.64	639,248.84	1.22	1,372.37	-151.88	
10,235.00	90.94	166.62	9,116.65	857.34 S	2,530.14 E	455,061.89	639,273.39	4.32	1,467.34	51.25	
10,330.00	90.34	168.05	9,115.59	950.02 S	2,550.97 E	454,969.21	639,294.22	1.63	1,562.28	112.75	

HALLIBURTON**Design Report for Time CC 6-7 Federal Com 74H - Final Surveys**

Measured Depth (usft)	Inclination (°)	Grid Azimuth (°)	Vertical Depth (usft)	Local Coordinates		Map Coordinates		Dogleg Rate (°/100ft)	Vertical Section (usft)	Toolface Angle (°)	Comments
				Northing (usft)	Easting (usft)	Northing (usft)	Easting (usft)				
10,347.60	90.32	168.41	9,115.49	967.25 S	2,554.56 E	454,951.98	639,297.81	2.04	1,579.86	93.29	Enter 50R/25L' @ 10348'MD
10,424.00	90.23	169.96	9,115.12	1,042.29 S	2,568.90 E	454,876.94	639,312.15	2.04	1,656.09	93.29	
10,519.00	90.02	172.21	9,114.92	1,136.14 S	2,583.62 E	454,783.09	639,326.87	2.38	1,750.62	95.33	
10,614.00	89.86	173.66	9,115.02	1,230.41 S	2,595.30 E	454,688.82	639,338.55	1.54	1,844.79	96.30	
10,709.00	88.86	175.42	9,116.08	1,324.97 S	2,604.34 E	454,594.26	639,347.59	2.13	1,938.58	119.61	
10,803.00	90.48	178.71	9,116.62	1,418.83 S	2,609.15 E	454,500.40	639,352.40	3.90	2,030.62	63.80	
10,897.00	89.23	181.59	9,116.86	1,512.82 S	2,608.91 E	454,406.41	639,352.16	3.34	2,121.51	113.46	
10,992.00	88.93	181.01	9,118.38	1,607.78 S	2,606.75 E	454,311.45	639,350.00	0.69	2,212.87	-117.36	
11,086.00	90.79	181.32	9,118.61	1,701.76 S	2,604.84 E	454,217.47	639,348.09	2.01	2,303.33	9.46	
11,181.00	89.58	179.92	9,118.31	1,796.75 S	2,603.81 E	454,122.48	639,347.06	1.95	2,394.99	-130.83	
11,275.00	89.83	179.71	9,118.79	1,890.75 S	2,604.12 E	454,028.48	639,347.37	0.35	2,486.03	-40.03	
11,369.00	90.09	179.43	9,118.85	1,984.74 S	2,604.82 E	453,934.49	639,348.07	0.41	2,577.17	-47.12	
11,464.00	90.69	179.55	9,118.21	2,079.74 S	2,605.67 E	453,839.49	639,348.92	0.64	2,669.31	11.31	
11,557.00	90.01	179.67	9,117.64	2,172.73 S	2,606.30 E	453,746.50	639,349.55	0.74	2,759.47	169.99	
11,652.00	89.58	179.10	9,117.98	2,267.73 S	2,607.32 E	453,651.50	639,350.57	0.75	2,851.65	-127.03	
11,747.00	87.88	177.18	9,120.09	2,362.64 S	2,610.40 E	453,556.59	639,353.65	2.70	2,944.28	-131.55	
11,841.00	89.52	179.04	9,122.22	2,456.56 S	2,613.50 E	453,462.67	639,356.75	2.64	3,035.95	48.61	
11,936.00	88.28	180.54	9,124.04	2,551.54 S	2,613.85 E	453,367.69	639,357.10	2.05	3,127.95	129.60	
12,031.00	89.28	180.34	9,126.07	2,646.51 S	2,613.12 E	453,272.72	639,356.37	1.07	3,219.67	-11.31	
12,126.00	91.07	181.32	9,125.77	2,741.50 S	2,611.74 E	453,177.73	639,354.99	2.15	3,311.24	28.70	
12,221.00	90.64	179.29	9,124.36	2,836.48 S	2,611.24 E	453,082.75	639,354.49	2.18	3,403.03	-101.94	
12,316.00	88.76	176.32	9,124.85	2,931.39 S	2,614.88 E	452,987.84	639,358.13	3.70	3,495.80	-122.33	
12,410.00	91.88	173.69	9,124.33	3,025.02 S	2,623.06 E	452,894.21	639,366.31	4.34	3,588.46	-40.13	
12,505.00	93.56	171.68	9,119.82	3,119.13 S	2,635.14 E	452,800.10	639,378.39	2.76	3,682.58	-50.03	
12,598.50	91.19	178.00	9,115.94	3,212.12 S	2,643.53 E	452,707.11	639,386.78	7.21	3,774.68	110.44	Exit 50R/25L' @ 12599'MD
12,600.00	91.15	178.10	9,115.91	3,213.62 S	2,643.58 E	452,705.61	639,386.83	7.21	3,776.14	110.70	
12,610.08	90.96	178.59	9,115.73	3,223.69 S	2,643.88 E	452,695.54	639,387.13	5.18	3,785.97	111.80	Enter 50R/25L' @ 12610'MD
12,695.00	89.32	182.67	9,115.52	3,308.58 S	2,642.95 E	452,610.65	639,386.20	5.18	3,867.89	111.81	
12,789.00	89.33	184.05	9,116.63	3,402.41 S	2,637.44 E	452,516.82	639,380.69	1.47	3,957.30	89.59	
12,884.00	88.31	184.70	9,118.59	3,497.11 S	2,630.19 E	452,422.12	639,373.44	1.27	4,047.12	147.50	
12,979.00	87.59	181.56	9,121.99	3,591.90 S	2,625.01 E	452,327.33	639,368.26	3.39	4,137.53	-102.98	
13,073.00	88.72	175.61	9,125.02	3,685.78 S	2,627.33 E	452,233.45	639,370.58	6.44	4,228.97	-79.35	
13,168.00	97.48	172.65	9,119.88	3,780.04 S	2,637.01 E	452,139.19	639,380.26	9.73	4,322.63	-18.59	
13,263.00	93.75	178.57	9,110.58	3,874.25 S	2,644.23 E	452,044.98	639,387.48	7.34	4,415.61	122.02	
13,358.00	90.94	181.43	9,106.69	3,969.15 S	2,644.22 E	451,950.08	639,387.47	4.22	4,507.45	134.45	
13,453.00	88.86	184.14	9,106.86	4,064.02 S	2,639.61 E	451,855.21	639,382.86	3.60	4,598.10	127.50	

HALLIBURTON**Design Report for Time CC 6-7 Federal Com 74H - Final Surveys**

Measured Depth (usft)	Inclination (°)	Grid Azimuth (°)	Vertical Depth (usft)	Local Coordinates		Map Coordinates		Dogleg Rate (°/100ft)	Vertical Section (usft)	Toolface Angle (°)	Comments
				Northing (usft)	Easting (usft)	Northing (usft)	Easting (usft)				
13,547.00	90.16	185.20	9,107.66	4,157.70 S	2,631.96 E	451,761.53	639,375.21	1.78	4,686.83	39.20	
13,642.00	89.36	184.11	9,108.06	4,252.39 S	2,624.25 E	451,666.84	639,367.50	1.42	4,776.51	-126.28	
13,737.00	89.71	184.45	9,108.83	4,347.12 S	2,617.16 E	451,572.11	639,360.41	0.51	4,866.40	44.17	
13,832.00	89.09	183.29	9,109.83	4,441.90 S	2,610.75 E	451,477.33	639,354.00	1.38	4,956.50	-118.13	
13,927.00	89.00	185.05	9,111.41	4,536.63 S	2,603.84 E	451,382.60	639,347.09	1.85	5,046.43	92.94	
14,022.00	87.93	182.75	9,113.96	4,631.37 S	2,597.38 E	451,287.86	639,340.63	2.67	5,136.48	-114.98	
14,116.00	88.33	181.35	9,117.02	4,725.25 S	2,594.02 E	451,193.98	639,337.27	1.55	5,226.49	-74.07	
14,211.00	90.09	181.99	9,118.33	4,820.20 S	2,591.25 E	451,099.03	639,334.50	1.97	5,317.68	19.99	
14,273.18	89.55	180.86	9,118.53	4,882.36 S	2,589.71 E	451,036.87	639,332.96	2.02	5,377.44	-115.36	SLC @ 14273'MD
14,306.00	89.27	180.26	9,118.86	4,915.17 S	2,589.39 E	451,004.06	639,332.64	2.02	5,409.12	-115.36	
14,401.00	88.93	180.06	9,120.36	5,010.16 S	2,589.12 E	450,909.07	639,332.37	0.42	5,500.97	-149.54	
14,496.00	89.55	180.75	9,121.62	5,105.15 S	2,588.45 E	450,814.08	639,331.70	0.98	5,592.72	48.06	
14,591.00	89.76	179.26	9,122.19	5,200.15 S	2,588.44 E	450,719.08	639,331.69	1.58	5,684.65	-81.98	
14,686.00	89.81	179.26	9,122.54	5,295.14 S	2,589.67 E	450,624.09	639,332.92	0.05	5,776.88	0.00	
14,780.00	90.45	180.49	9,122.33	5,389.14 S	2,589.87 E	450,530.09	639,333.12	1.48	5,867.90	62.51	
14,875.00	89.22	179.00	9,122.60	5,484.13 S	2,590.30 E	450,435.10	639,333.55	2.03	5,959.93	-129.54	
14,970.00	89.70	178.83	9,123.50	5,579.11 S	2,592.09 E	450,340.12	639,335.34	0.54	6,052.30	-19.50	
15,065.00	89.92	179.76	9,123.81	5,674.10 S	2,593.26 E	450,245.13	639,336.51	1.01	6,144.52	76.69	
15,159.00	89.31	178.48	9,124.45	5,768.08 S	2,594.71 E	450,151.15	639,337.96	1.51	6,235.83	-115.48	
15,254.00	89.53	178.53	9,125.41	5,863.05 S	2,597.18 E	450,056.18	639,340.43	0.24	6,328.35	12.80	
15,349.00	90.98	179.77	9,124.99	5,958.03 S	2,598.59 E	449,961.20	639,341.84	2.01	6,420.63	40.53	
15,444.00	89.59	177.70	9,124.51	6,053.00 S	2,600.69 E	449,866.23	639,343.94	2.62	6,513.06	-123.87	
15,539.00	91.22	179.72	9,123.84	6,147.96 S	2,602.83 E	449,771.27	639,346.08	2.73	6,605.50	51.09	
15,633.00	91.21	180.59	9,121.85	6,241.94 S	2,602.58 E	449,677.29	639,345.83	0.93	6,696.38	90.65	
15,728.00	89.11	178.31	9,121.58	6,336.93 S	2,603.49 E	449,582.30	639,346.74	3.26	6,788.52	-132.64	
15,823.00	89.18	179.16	9,123.00	6,431.89 S	2,605.58 E	449,487.34	639,348.83	0.90	6,880.95	85.30	
15,917.00	89.34	180.01	9,124.21	6,525.88 S	2,606.27 E	449,393.35	639,349.52	0.92	6,972.08	79.34	
16,012.00	90.35	180.11	9,124.47	6,620.88 S	2,606.17 E	449,298.35	639,349.42	1.07	7,063.99	5.65	
16,107.00	90.19	179.85	9,124.02	6,715.88 S	2,606.20 E	449,203.35	639,349.45	0.32	7,155.93	-121.61	
16,201.00	89.33	179.99	9,124.42	6,809.87 S	2,606.33 E	449,109.36	639,349.58	0.93	7,246.92	170.75	
16,296.00	89.85	179.81	9,125.10	6,904.87 S	2,606.50 E	449,014.36	639,349.75	0.58	7,338.90	-19.09	
16,390.00	90.33	179.96	9,124.95	6,998.87 S	2,606.68 E	448,920.36	639,349.93	0.53	7,429.91	17.35	
16,485.00	90.59	179.78	9,124.19	7,093.87 S	2,606.90 E	448,825.36	639,350.15	0.33	7,521.89	-34.69	
16,580.00	90.03	180.18	9,123.67	7,188.87 S	2,606.93 E	448,730.36	639,350.18	0.72	7,613.83	144.46	
16,674.00	90.24	179.92	9,123.45	7,282.87 S	2,606.85 E	448,636.36	639,350.10	0.36	7,704.78	-51.07	
16,769.00	88.69	180.37	9,124.34	7,377.86 S	2,606.61 E	448,541.37	639,349.86	1.70	7,796.64	163.81	
16,864.00	88.69	179.97	9,126.51	7,472.83 S	2,606.33 E	448,446.40	639,349.58	0.42	7,888.48	-90.00	

HALLIBURTON**Design Report for Time CC 6-7 Federal Com 74H - Final Surveys**

Measured Depth (usft)	Inclination (°)	Grid Azimuth (°)	Vertical Depth (usft)	Local Coordinates		Map Coordinates		Dogleg Rate (°/100ft)	Vertical Section (usft)	Toolface Angle (°)	Comments
				Northing (usft)	Easting (usft)	Northing (usft)	Easting (usft)				
16,959.00	88.28	180.20	9,129.02	7,567.80 S	2,606.19 E	448,351.43	639,349.44	0.49	7,980.34	150.72	
17,053.00	89.31	182.01	9,131.00	7,661.76 S	2,604.38 E	448,257.47	639,347.63	2.22	8,070.81	60.37	
17,148.00	89.65	179.51	9,131.86	7,756.74 S	2,603.12 E	448,162.49	639,346.37	2.66	8,162.41	-82.27	
17,243.00	91.37	182.73	9,131.02	7,851.70 S	2,601.26 E	448,067.53	639,344.51	3.84	8,253.84	61.88	
17,337.00	90.23	181.00	9,129.70	7,945.63 S	2,598.20 E	447,973.60	639,341.45	2.20	8,343.97	-123.37	
17,432.00	89.78	178.32	9,129.69	8,040.62 S	2,598.76 E	447,878.61	639,342.01	2.86	8,436.03	-99.53	
17,527.00	89.86	178.80	9,129.99	8,135.59 S	2,601.15 E	447,783.64	639,344.40	0.51	8,528.54	80.54	
17,621.00	89.65	178.22	9,130.39	8,229.56 S	2,603.60 E	447,689.67	639,346.85	0.66	8,620.09	-109.90	
17,811.00	89.35	179.69	9,132.05	8,419.51 S	2,607.06 E	447,499.72	639,350.31	0.79	8,804.79	101.54	
17,905.00	89.29	179.75	9,133.17	8,513.51 S	2,607.52 E	447,405.72	639,350.77	0.09	8,895.86	135.00	
18,000.00	89.29	179.53	9,134.35	8,608.50 S	2,608.12 E	447,310.73	639,351.37	0.23	8,987.94	-90.00	
18,095.00	90.46	179.48	9,134.55	8,703.49 S	2,608.94 E	447,215.74	639,352.19	1.23	9,080.07	-2.45	
18,285.00	90.12	180.50	9,133.59	8,893.49 S	2,608.97 E	447,025.74	639,352.22	0.57	9,263.94	108.43	
18,379.00	89.90	180.25	9,133.57	8,987.48 S	2,608.36 E	446,931.75	639,351.61	0.35	9,354.75	-131.35	
18,474.00	89.74	180.09	9,133.87	9,082.48 S	2,608.07 E	446,836.75	639,351.32	0.24	9,446.61	-135.00	
18,569.00	89.14	179.87	9,134.80	9,177.48 S	2,608.11 E	446,741.75	639,351.36	0.67	9,538.55	-159.87	
18,664.00	89.43	178.79	9,135.99	9,272.46 S	2,609.22 E	446,646.77	639,352.47	1.18	9,630.74	-74.98	
18,758.00	89.90	180.09	9,136.54	9,366.46 S	2,610.14 E	446,552.77	639,353.39	1.47	9,721.93	70.13	
18,853.00	90.01	179.62	9,136.61	9,461.45 S	2,610.38 E	446,457.78	639,353.63	0.51	9,813.93	-76.83	
18,948.00	89.41	179.34	9,137.09	9,556.45 S	2,611.24 E	446,362.78	639,354.49	0.70	9,906.07	-154.98	
19,042.00	90.61	180.52	9,137.08	9,650.45 S	2,611.35 E	446,268.78	639,354.60	1.79	9,997.06	44.52	
19,137.00	89.60	179.02	9,136.90	9,745.44 S	2,611.74 E	446,173.79	639,354.99	1.90	10,089.09	-123.95	
19,231.00	90.43	180.26	9,136.88	9,839.44 S	2,612.33 E	446,079.79	639,355.58	1.59	10,180.20	56.20	
19,326.00	89.54	179.19	9,136.90	9,934.43 S	2,612.78 E	445,984.80	639,356.03	1.47	10,272.24	-129.75	
19,420.00	89.74	178.31	9,137.49	10,028.41 S	2,614.83 E	445,890.82	639,358.08	0.96	10,363.70	-77.20	
19,486.91	88.43	177.06	9,138.56	10,095.25 S	2,617.53 E	445,823.98	639,360.78	2.71	10,429.07	-136.45	LTP 100' HLC @ 19487'MD
19,525.00	87.68	176.35	9,139.86	10,133.26 S	2,619.72 E	445,785.97	639,362.97	2.71	10,466.40	-136.43	Last MWD Svy @ 19525.00' MD
19,545.00	87.68	176.35	9,140.67	10,153.20 S	2,620.99 E	445,766.03	639,364.24	0.00	10,486.02	0.00	Projection to TD @ 19545.00' MD

HALLIBURTON**Design Report for Time CC 6-7 Federal Com 74H - Final Surveys****Design Annotations**

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
10.00	10.00	0.00	0.00	10' KB Offset
9,015.00	8,695.91	25.93	2,090.91	Tie-in @ 9015.00' MD
9,120.00	8,795.95	18.81	2,121.55	First MWD Svy @ 9120.00' MD
10,347.60	9,115.49	-967.25	2,554.56	Enter 50R/25L' @ 10348'MD
12,598.50	9,115.94	-3,212.12	2,643.53	Exit 50R/25L' @ 12599'MD
12,610.08	9,115.73	-3,223.69	2,643.88	Enter 50R/25L' @ 12610'MD
14,273.18	9,118.53	-4,882.36	2,589.71	SLC @ 14273'MD
19,486.91	9,138.56	-10,095.25	2,617.53	LTP 100' HLC @ 19487'MD
19,525.00	9,139.86	-10,133.26	2,619.72	Last MWD Svy @ 19525.00' MD
19,545.00	9,140.67	-10,153.20	2,620.99	Projection to TD @ 19545.00' MD

Vertical Section Information

Angle Type	Target	Azimuth (°)	Origin Type	Origin		Start TVD (usft)
				+N/_S (usft)	+E/-W (usft)	
Target	Time CC 6-7 74H PBHL	165.40	Slot	0.00	0.00	0.00

Survey tool program

From (usft)	To (usft)	Survey/Plan	Survey Tool
10.00	436.00	SURFACE (adjusted to 24' RKB)	3_Gyro-GC_Csg
587.00	9,015.00	Intermediate	Superior
9,120.00	12,410.00	Production 1	MWD+IFR1+SAG+FDIR Superior
12,505.00	13,073.00	Production 2	MWD+IFR1+SAG+FDIR
13,168.00	19,525.00	Production 3	3_MWD+IFR1+Sag Superior
19,545.00	19,545.00	PTD	MWD+IFR1+SAG+FDIR 3_Blind



Design Report for Time CC 6-7 Federal Com 74H - Final Surveys

Design Targets

Target Name - hit/miss target	Dip Angle ()	Dip Dir. ()	TVD ()	+N/-S ()	+E/-W ()	Northing ()	Easting ()	Latitude	Longitude
()									

Directional Difficulty Index

Average Dogleg over Survey:	1.77 °/100ft	Maximum Dogleg over Survey:	19.52 °/100ft at 9,310.00 usft
Net Tortousity applicable to Plans:	0.82 °/100ft	Directional Difficulty Index:	6.964

Audit Info


HALLIBURTON

North Reference Sheet for Time CC 6-7 - Time CC 6-7 Federal Com 74H - OH

All data is in US Feet unless otherwise stated. Directions and Coordinates are relative to Grid North Reference.
Vertical Depths are relative to GL 2959.80' + RKB 24' @ 2983.80usft (Citadel 3). Northing and Easting are relative to Time CC 6-7 Federal Com 74H
Coordinate System is US State Plane 1983, New Mexico Eastern Zone using datum North American Datum 1983, ellipsoid GRS 1980
Projection method is Transverse Mercator (Gauss-Kruger)
Central Meridian is 104° 20' 0.000 W°, Longitude Origin:0° 0' 0.000 E°, Latitude Origin:0° 0' 0.000 N°
False Easting: 541,337.50usft, False Northing: 0.00usft, Scale Reduction: 0.99991952

Grid Coordinates of Well: 455,919.23 usft N, 636,743.25 usft E
Geographical Coordinates of Well: 32° 15' 10.873 N, 104° 1' 28.960 W
Grid Convergence at Surface is: 0.16°

Based upon Minimum Curvature type calculations, at a Measured Depth of 19,545.00usft
the Bottom Hole Displacement is 10,486.04usft in the Direction of 165.53° (Grid).
Magnetic Convergence at surface is: -6.55° (5 October 2023, , IFR)

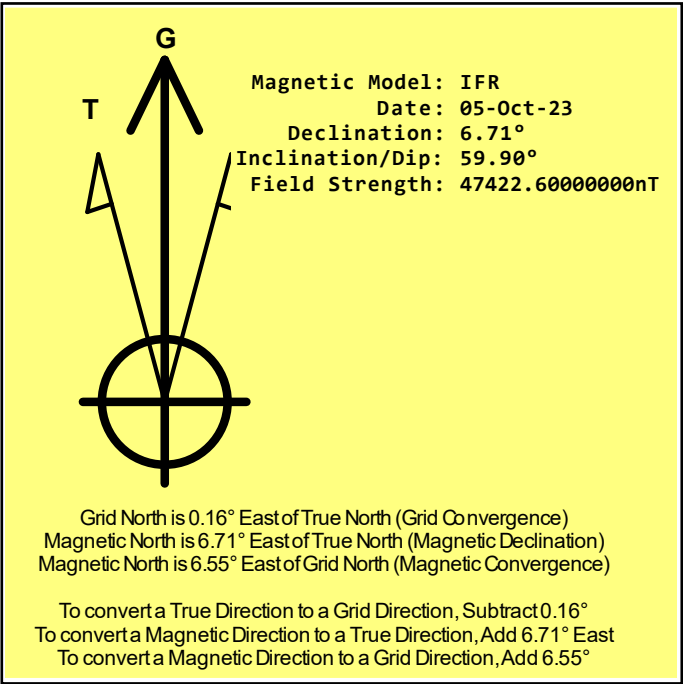

Intent ☐ As Drilled ☐

API #		
Operator Name:	Property Name:	Well Number

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

First Take Point (FTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Is this well the defining well for the Horizontal Spacing Unit? ☐Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018

Well Name: TIME CC 6-7 FEDERAL COM	Well Location: T24S / R29E / SEC 6 / LOT 3 / 32.2530204 / -104.0247111	County or Parish/State: EDDY / NM
Well Number: 74H	Type of Well: OIL WELL	Allottee or Tribe Name:
Lease Number: NMNM117551	Unit or CA Name:	Unit or CA Number:
US Well Number: 3001554030	Well Status: Producing Oil Well	Operator: OXY USA INCORPORATED

Subsequent Report

Sundry ID: 2772594

Type of Submission: Subsequent Report

Date Sundry Submitted: 01/30/2024

Date Operation Actually Began: 11/09/2023

Type of Action: Workover Operations

Time Sundry Submitted: 03:01

Actual Procedure: RUPU 11/09/23, RIH & clean out to PBTD @ 19500', pressure test casing to 6000# for 30 min, good test. RIH & perf @ 9929-19406' Total 1170 holes. Frac in 38 stages w/ 472047BBL Produced Water + 25256020# sand, RD Liberty 12/05/23. Well ready to produce 12/14/23. 01/29/24 RIH with 2-3/8" L80 tbg & gas lift set @ 9188', RD 01/29/24.

Received by OCD: 2/20/2024 2:19:37 PM

Page 16 of 22

Well Name: TIME CC 6-7 FEDERAL COM	Well Location: T24S / R29E / SEC 6 / LOT 3 / 32.2530204 / -104.0247111	County or Parish/State: EDDY / NM
Well Number: 74H	Type of Well: OIL WELL	Allottee or Tribe Name:
Lease Number: NMNM117551	Unit or CA Name:	Unit or CA Number:
US Well Number: 3001554030	Well Status: Producing Oil Well	Operator: OXY USA INCORPORATED

Operator

I certify that the foregoing is true and correct. Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction. Electronic submission of Sundry Notices through this system satisfies regulations requiring a

Operator Electronic Signature: JANA MENDIOLA	Signed on: JAN 30, 2024 03:00 PM
Name: OXY USA INCORPORATED	
Title: Regulatory Coordinator	
Street Address: PO BOX 50250	
City: Midland	State: TX
Phone: (432) 685-5936	
Email address: Janalyn_mendiola@oxy.com	

Field

Representative Name:		
Street Address:		
City:	State:	Zip:
Phone:		
Email address:		

BLM Point of Contact

BLM POC Name: JONATHON W SHEPARD	BLM POC Title: Petroleum Engineer
BLM POC Phone: 5752345972	BLM POC Email Address: jshepard@blm.gov
Disposition: Accepted	Disposition Date: 02/07/2024
Signature: Jonathon Shepard	

Submit To Appropriate District Office Two Copies District I 1625 N. French Dr., Hobbs, NM 88240 District II 811 S. First St., Artesia, NM 88210 District III 1000 Rio Brazos Rd., Aztec, NM 87410 District IV 1220 S. St. Francis Dr., Santa Fe, NM 87505		State of New Mexico Energy, Minerals and Natural Resources Oil Conservation Division 1220 South St. Francis Dr. Santa Fe, NM 87505				Form C-105 Revised April 3, 2017				
1. WELL API NO. 30-015-54030										
2. Type of Lease ☐ STATE ☐ FEE ☒ FED/INDIAN										
3. State Oil & Gas Lease No.										
WELL COMPLETION OR RECOMPLETION REPORT AND LOG										
4. Reason for filing: ☒ COMPLETION REPORT (Fill in boxes #1 through #31 for State and Fee wells only) ☐ C-144 CLOSURE ATTACHMENT (Fill in boxes #1 through #9, #15 Date Rig Released and #32 and/or #33; attach this and the plat to the C-144 closure report in accordance with 19.15.17.13.K NMAC)						5. Lease Name or Unit Agreement Name TIME CC 6-7 FEDERAL COM				
						6. Well Number: 74H				
7. Type of Completion: ☒ NEW WELL ☐ WORKOVER ☐ DEEPENING ☐ PLUGBACK ☐ DIFFERENT RESERVOIR ☐ OTHER										
8. Name of Operator: OXY USA INC.						9. OGRID: 16696				
10. Address of Operator: P.O. BOX 50250 MIDLAND, TX 79710						11. Pool name or Wildcat PIERCE CROSSING; BONE SPRING				
12. Location	Unit Ltr	Section	Township	Range	Lot	Feet from the	N/S Line	Feet from the	E/W Line	County
Surface:	C	6	24S	29E	3	450	NORTH	2360	WEST	EDDY
BH:	P	7	24S	29E		42	SOUTH	359	EAST	EDDY
13. Date Spudded 08/09/23		14. Date T.D. Reached 10/26/2023		15. Date Rig Released 10/29/2023		16. Date Completed (Ready to Produce) 12/14/2023		17. Elevations (DF and RKB, RT, GR, etc.) 2960' GL		
18. Total Measured Depth of Well 19545'M 9141'V				19. Plug Back Measured Depth 19500'M 9139'V		20. Was Directional Survey Made? YES		21. Type Electric and Other Logs Run CBL		
22. Producing Interval(s), of this completion - Top, Bottom, Name 9929-19406' 2 ND BONE SPRING										
23. CASING RECORD (Report all strings set in well)										
CASING SIZE		WEIGHT LB./FT.		DEPTH SET		HOLE SIZE		CEMENTING RECORD		AMOUNT PULLED
10.75" J55		45.5		472'		14.75"		430sx-surf circ		
7.625" HCL-80		26.4		9035'		9.875"		1957sx-surf		
5.5" P110 ICY		20		19525'		6.75"		810sx-TOC@7225'		
24. LINER RECORD										
SIZE	TOP	BOTTOM	SACKS CEMENT	SCREEN	25. TUBING RECORD					
					SIZE	DEPTH SET	PACKER SET			
					2-3/8"	9188'				
26. Perforation record (interval, size, and number) 9929-19406' Total 1170 holes, Hole Size=0.42					27. ACID, SHOT, FRACTURE, CEMENT, SQUEEZE, ETC.					
					DEPTH INTERVAL		AMOUNT AND KIND MATERIAL USED			
					9929-19406'		472047BBL Produced Water + 25256020# sand			
28. PRODUCTION										
Date First Production 12/19/2023		Production Method (Flowing, gas lift, pumping - Size and type pump) GAS LIFT				Well Status (Prod. or Shut-in) Prod.				
Date of Test 12/21/2023	Hours Tested 24 hrs.	Choke Size 58	Prod'n For Test Period	Oil - Bbl 2198	Gas - MCF 5059	Water - Bbl. 2360	Gas - Oil Ratio 2302			
Flow Tubing Press.	Casing Pressure 961	Calculated 24- Hour Rate	Oil - Bbl. 2198	Gas - MCF 5059	Water - Bbl. 2360	Oil Gravity - API - (Corr.)				
29. Disposition of Gas (Sold, used for fuel, vented, etc.) SOLD							30. Test Witnessed By			
31. List Attachments WBD, C-104, As-Drilled C-102, Kickoff Points Form, Final Directional Survey, Completion Sundry C-103										
32. If a temporary pit was used at the well, attach a plat with the location of the temporary pit.							33. Rig Release Date:			
34. If an on-site burial was used at the well, report the exact location of the on-site burial:										
Latitude _____ Longitude _____ NAD83										
I hereby certify that the information shown on both sides of this form is true and complete to the best of my knowledge and belief										
Printed										
Signature: <i>Jana Mendiola</i>		Name: <u>Jana Mendiola</u>			Title: <u>Sr. Regulatory Analyst</u>			Date: <u>02/20/2024</u>		
E-mail Address: <u>janalyn_mendiola@oxy.com</u>										

This form is to be filed with the appropriate District Office of the Division not later than 20 days after the completion of any newly-drilled or deepened well and not later than 60 days after completion of closure. When submitted as a completion report, this shall be accompanied by one copy of all electrical and radio-activity logs run on the well and a summary of all special tests conducted, including drill stem tests. All depths reported shall be measured depths. In the case of directionally drilled wells, true vertical depths shall also be reported. For multiple completions, items 11, 12 and 26-31 shall be reported for each zone.

Southeastern New Mexico		Northwestern New Mexico	
T. Rustler 208'	T. Bell Canyon 2831'	T. Ojo Alamo	T. Penn A"
T. Salado 698'	T. Strawn	T. Kirtland	T. Penn. "B"
T. Castile 1371'	T. Atoka	T. Fruitland	T. Penn. "C"
T. Delaware 2787'	T. Miss	T. Pictured Cliffs	T. Penn. "D"
T. Cherry Canyon 3754'	T. Devonian	T. Cliff House	T. Leadville
T. Brushy Canyon 5151'	T. Silurian	T. Menefee	T. Madison
T. Grayburg	T. Montoya	T. Point Lookout	T. Elbert
T. San Andres	T. Simpson	T. Mancos	T. McCracken
T. Glorieta	T. McKee	T. Gallup	T. Ignacio Otzte
T. Paddock	T. Ellenburger	Base Greenhorn	T. Granite
T. Blinebry	T. Gr. Wash	T. Dakota	
T. Tubb	T. Delaware Sand	T. Morrison	
T. Drinkard	T. Bone Spring 6772'	T. Todilto	
T. Abo	T. 1st Bone Spring 7770'	T. Entrada	
T. Wolfcamp	T. 2nd Bone Spring 8565'	T. Wingate	
T. Penn	T. 3 rd Bone Spring	T. Chinle	
T. Cisco (Bough C)	T.	T. Permian	

No. 1, from.....to.....

No. 2, from.....to.....

No. 3, from.....to.....

No. 4, from.....to.....


Include data on rate of water inflow and elevation to which water rose in hole.

No. 1, from.....to.....feet.....
 No. 2, from.....to.....feet.....
 No. 3, from.....to.....feet.....

From	To	Thickness In Feet	Lithology

From	To	Thickness In Feet	Lithology

OXY USA Inc.
TIME CC 6-7 FEDERAL COM 74H
API No. 30-015-54030

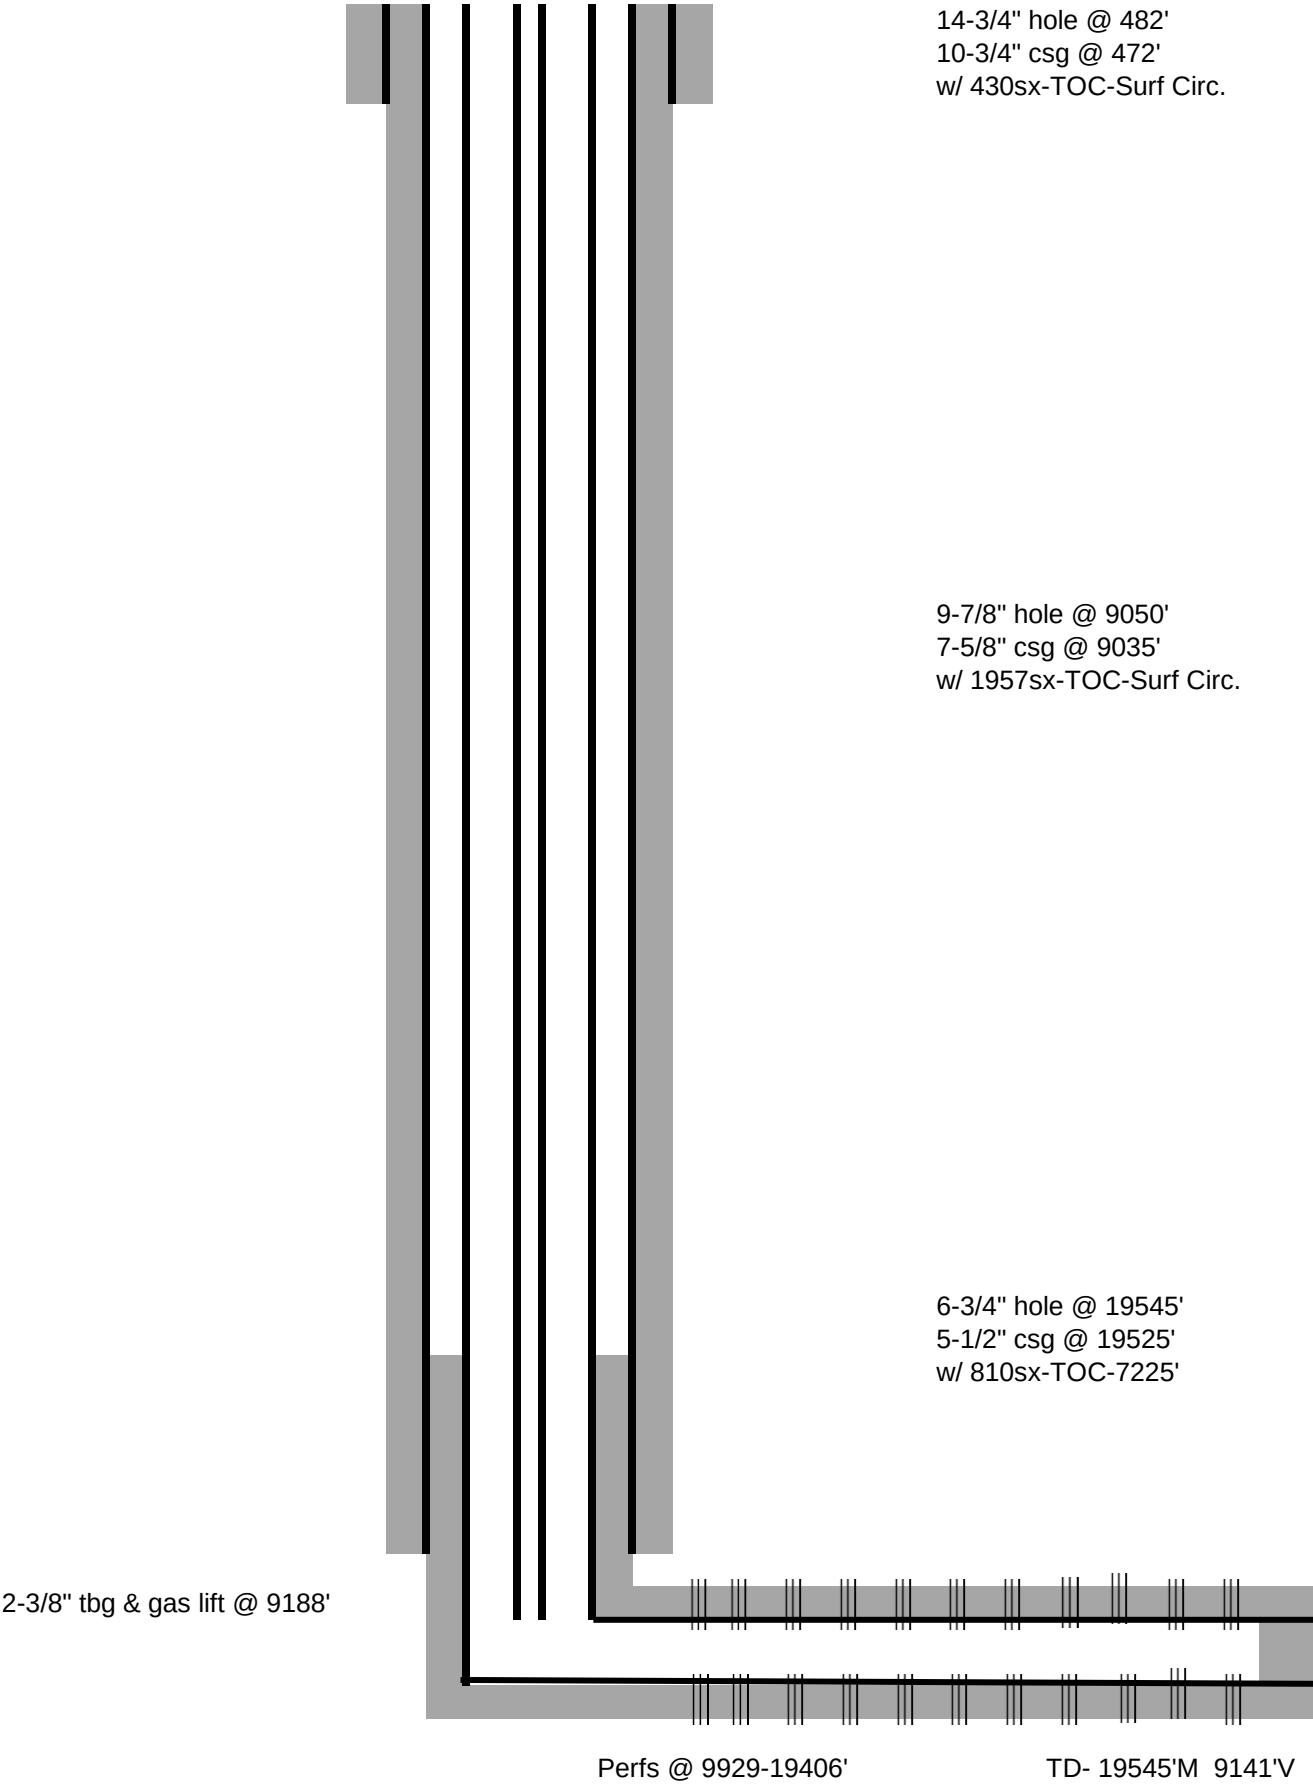

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

ACKNOWLEDGMENTS

Action 316086

ACKNOWLEDGMENTS

Operator: OXY USA INC P.O. Box 4294 Houston, TX 772104294	OGRID: 16696
	Action Number: 316086
	Action Type: [C-104] Completion Packet (C-104C)

ACKNOWLEDGMENTS

☒	I hereby certify that the required Water Use Report has been, or will be, submitted for this wells completion.
☒	I hereby certify that the required FracFocus disclosure has been, or will be, submitted for this wells completion.

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 316086

CONDITIONS

Operator: OXY USA INC P.O. Box 4294 Houston, TX 772104294	OGRID: 16696
	Action Number: 316086
	Action Type: [C-104] Completion Packet (C-104C)

CONDITIONS

Created By	Condition	Condition Date
plmartinez	File 3160-4 Completion Report within 10 days of BLM approval.	5/29/2024
