

Submit a Copy To Appropriate District Office
 District I – (575) 393-6161
 1625 N. French Dr., Hobbs, NM 88240
 District II – (575) 748-1283
 811 S. First St., Artesia, NM 88210
 District III – (505) 334-6178
 1000 Rio Brazos Rd., Aztec, NM 87410
 District IV – (505) 476-3460
 1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
 Energy, Minerals and Natural Resources

Form C-103
 Revised July 18, 2013

OIL CONSERVATION DIVISION
 1220 South St. Francis Dr.
 Santa Fe, NM 87505

WELL API NO. 30-025-52319
5. Indicate Type of Lease STATE ☒ FEE ☐
6. State Oil & Gas Lease No.
7. Lease Name or Unit Agreement Name SATELLITE STATE COM
8. Well Number 703H
9. OGRID Number 331595
10. Pool name [970] AIRSTRIP; WOLFCAMP

SUNDRY NOTICES AND REPORTS ON WELLS (DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)	
1. Type of Well: Oil Well ☒ Gas Well ☐ Other ☐	7. Lease Name or Unit Agreement Name SATELLITE STATE COM
2. Name of Operator FRANKLIN MOUNTAIN ENERGY 3, LLC	8. Well Number 703H
3. Address of Operator 44 COOK STREET, SUITE 1000, DENVER, CO 80206	9. OGRID Number 331595
4. Well Location Unit Letter <u>B</u> : <u>1132</u> feet from the <u>NORTH</u> line and <u>2055</u> feet from the <u>EAST</u> line Section <u>36</u> Township <u>18S</u> Range <u>34E</u> NMPM County <u>Lea</u>	10. Pool name [970] AIRSTRIP; WOLFCAMP
11. Elevation (Show whether DR, RKB, RT, GR, etc.) 3961	

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:

PERFORM REMEDIAL WORK ☐ PLUG AND ABANDON ☐
 TEMPORARILY ABANDON ☐ CHANGE PLANS ☒
 PULL OR ALTER CASING ☐ MULTIPLE COMPL ☐
 DOWNHOLE COMMINGLE ☐
 CLOSED-LOOP SYSTEM ☐
 OTHER: ☐

SUBSEQUENT REPORT OF:

REMEDIAL WORK ☐ ALTERING CASING ☐
 COMMENCE DRILLING OPNS. ☐ P AND A ☐
 CASING/CEMENT JOB ☐
 OTHER: ☐

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

Franklin Mountain Energy 3, LLC (FME3), Operator, respectfully requests approval to make the following changes to the APD and drilling plan for the above referenced well:

Surface Hole Location: FME requests approval to swap wellhead surface locations with the SATELLITE STATE COM #303H (30-025-52739) well.

The SATELLITE STATE COM #703H would move from B-36-18S-34E, 1132 FNL 2055 FEL to **B-36-18S-34E, 1132 FNL 2175 FEL.**

Target formation remains the same.

BHL remains the same: B-24-18S-34E, 130 FNL 1680 FEL

Please see attached revised C-102, directional plan, 14-point plan and geoprogram.

Spud Date:

Rig Release Date:

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE  TITLE Dir. Ops Planning & Regulatory DATE 5/20/2024

Type or print name Rachael Overbey E-mail address: roverbey@fmellc.com PHONE: 303.570.4057

For State Use Only

APPROVED BY: _____ TITLE _____ DATE _____

Conditions of Approval (if any):

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico

Energy, Minerals & Natural Resources Department

OIL CONSERVATION DIVISION

1220 South St. Francis Dr.

Santa Fe, NM 87505

Form C-102

Revised August 1, 2011

Submit one copy to appropriate District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-025-52319	² Pool Code 970	³ Pool Name AIRSTRIP; WOLFCAMP
⁴ Property Code 335014	⁵ Property Name SATELLITE STATE COM	⁶ Well Number 703H
⁷ OGRID No. 331595	⁸ Operator Name FRANKLIN MOUNTAIN ENERGY 3, LLC	⁹ Elevation 3961.8'


¹⁰ Surface Location

UL or lot no. B	Section 36	Township 18S	Range 34E	Lot Idn	Feet from the 1132	North/South line NORTH	Feet from the 2175	East/West line EAST	County LEA
--------------------	---------------	-----------------	--------------	---------	-----------------------	---------------------------	-----------------------	------------------------	---------------

¹¹ Bottom Hole Location If Different From Surface


UL or lot no. B	Section 24	Township 18S	Range 34E	Lot Idn	Feet from the 130	North/South line NORTH	Feet from the 1680	East/West line EAST	County LEA
¹² Dedicated Acres 360	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.						

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

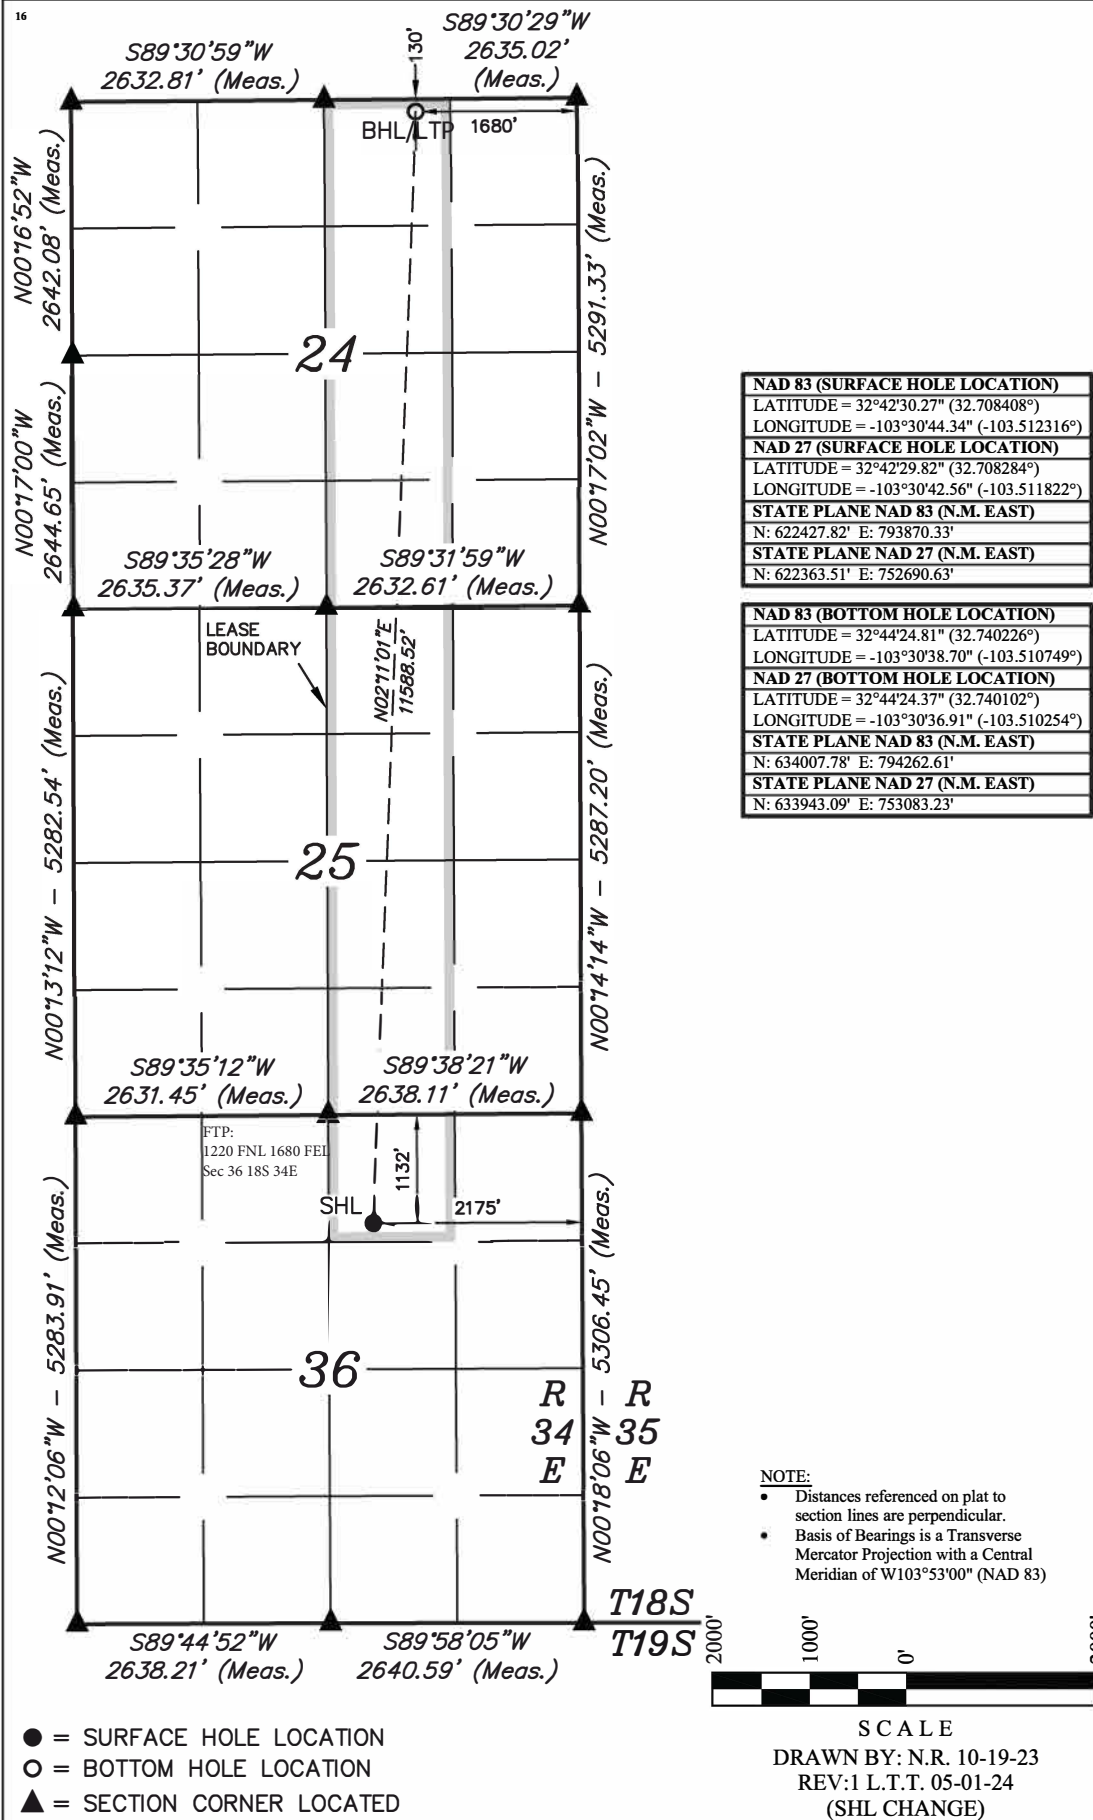

¹⁷ OPERATOR
CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.


Signature
5/20/2024
Date

Rachael Overbey
Printed Name

roverbey@fmlc.com
E-mail Address

¹⁸ SURVEYOR
CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

October 04, 2023

Date of Survey

Signature and Seal of Professional Surveyor:



Certificate Number:



Satellite State Com 703H

1. **Geologic name of surface location:** Permian
2. **Estimated tops of important geological markers:**

Formations	PROG SS	PROG TVD	Picked TVD	delta	Potential/Issues
Cenozoic Alluvium (surface)	3,962'	30'	30'	0	Sand/Gravels/Unconsolidated
Rustler	2,044'	1,947'			Carbonates
Salado	1,768'	2,224'			Salt, Carbonate & Clastics
Base Salt	733'	3,259'			Shaley Carbonate & Shale
Yates	427'	3,564'			Anhydrite/Shale
Seven Rivers	81'	3,911'			Interbedded Shale/Carbonate
Queen	-697'	4,689'			Sandstone & Dolomite & Anhydrite
Delaware Mtn Group	-2,359'	6,351'			Sandstone/Carb/Shale - oil/gas/water
Bone Spring Lime	-3,769'	7,760'			Shale/Carbonates - oil/gas
First Bone Spring Sand	-5,248'	9,240'			Sandstone - oil/gas/water
Second Bone Spring Carbonate	-5,411'	9,402'			Shale/Carbonates - oil/gas
Second Bone Spring Sand	-5,530'	9,522'			Sandstone - oil/gas/water
Third Bone Spring Carbonate	-6,156'	10,147'			Shale/Carbonates - oil/gas
Third Bone Spring Sand	-6,246'	10,238'			Sandstone - oil/gas/water
Wolfcamp	-6,782'	10,774'			Overpressure Shale/Sand- oil/gas
HZ Target	-7,014'	11,006'			Overpressure Shale - oil/gas
Wolfcamp B	-7,244'	11,236'			Overpressure Shale - oil/gas

3. **Estimated depth of anticipated fresh water, oil or gas:**

Upper Permian Sands	0- 400'	Fresh Water
Delaware Sands	6,351'	Oil
1 st Bone Spring Sand	9,240'	Oil
2 nd Bone Spring Carb	9,402'	Oil
2 nd Bone Spring Sand	9,522'	Oil
3 rd Bone Spring Sand	10,238'	Oil
Wolfcamp	10,774'	Oil
Wolfcamp B	N/A	Oil

No other formations are expected to give up oil, gas or fresh water in measurable quantities. Surface freshwater sands will be protected by setting 13-3/8" casing at 1,997' and circulating cement back to surface.

4. **Casing Program:**

All casing strings will be run new.



Casing string	Weight	Grade	Burst	Collapse	Tension	Conn	Length	API design factor			
								Burst	Collapse	Tension	Coupling
Surface 13 3/8"	54.5	J-55	2730	1130	853	BTC 909	1,997	0.99	1.09	4.08	4.35
Intermediate 9 5/8"	40	HCL-80	7430	4230	916	BTC 1042	4,120	2.04	2.19	3.46	3.94
Production 7"	32	HCP-110	12460	10760	1025	CDC-HTQ 1053	10,456	1.80	2.20	2.36	2.42
Production 5 1/2"	20	HCP-110	12640	12200	641	CDC-HTQ 667	12,050 11,006	1.15	2.16	1.88	1.96 2.08

Tapered production string will be ran with a X-over installed at the KOP of 10,456'.

Cementing Program:

Cementing Stage tool can be placed in the 1st Intermediate string as a contingency to ensure required TOC to surface.

To increase efficiency of drilling operations and minimize disturbance of the area the batch-drilling approach will be used.

Off-line cementing may be utilized for Surface, Intermediate, and Production strings to further optimization of drilling process and reduction of disturbance.

String Type	Hole Size	Casing		Sacks	Type of cmt	Lead			Sacks	Type of cmt	Tail			TOC	Excess
		Size	Setting Depth			Yield ft ³ /sk	Water gal/sk	TOC ft			Yield ft ³ /sk	Water gal/sk	TOC		
Surf	17.5	13.375	1,997	1082	85:15 Compass Poz, 12.8 ppg Class C, 5%Gel, 3#/sk Kol Seal, 4.64#/sk Salt	2.05	11.12	0	441	Tail, 14.8 ppg, 100% Class C, 1%CaCl ₂ , 0.1%	1.34	6.35	1,597	100%	
Int1	12.25	9.625	4,120	658	Lead, 11.3 ppg, HSLD 82 10% Gel, 4% STE, 2#/sk, Gyp Seal	2.74	16.31	0	201	Econolite Tail, 14.8 ppg, 100% Class C, 0.08% C-51	1.33	6.33	3,720	100%	
Prod	8.75	7	10,456	517	HSLD 9420, 10.5 ppg, Class C, 1#/sk Salt, 4% STE 1% C-45	3.99	25.51	3,120							100%
Prod	8.75	5.5	22,506						3007	HSLD 80, 13.ppg, 32#/sk Salt, 4% STE, 1#/sk Gyp Seal	1.52	7.59	10,456	50%	

5. Minimum Specifications for Pressure Control:



The minimum blowout preventer equipment (BOPE) shown in Exhibit #1 will consist of a single ram, mud cross and double ram-type (10,000 psi WP) preventer and an annular preventer (5,000-psi WP). Both units will be hydraulically operated, and the ram-type will be equipped with blind rams on bottom and 4 ½" x 7" variable pipe rams on top. All BOPE will be tested in accordance with Onshore Oil & Gas order No. 2.

Before drilling out of the surface casing, the ram-type BOP and accessory equipment will be tested to 5,000/250 psig and the annular preventer to 3,500/250 psig. The surface casing will be tested to 1500 psi for 30 minutes.

Before drilling out of the intermediate casing, the ram-type BOP and accessory equipment will be tested to 10,000/250 psig and the annular preventer to 3,500/250 psig.

Pipe rams will be operationally checked each 24-hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets.

A hydraulically operated choke will be installed prior to drilling out of the intermediate casing shoe.

6. Types and characteristics of the proposed mud system:

During this procedure we plan to use a Closed-Loop System and haul contents to the required disposal. The applicable depths and properties of the drilling fluid systems are as follows.

Depth	Type	Weight (ppg)	Viscosity	Water Loss
0 – 1,997'	Fresh - Gel	8.6-8.8	28-34	N/c
1,997' – 4,120'	Brine	8.8-10.2	28-34	N/c
4,120" – 11,356'	Brine	8.8-10.2	28-34	N/c
11,356' – 22,506' Lateral	Oil Base	9.0-12	58-68	3 - 6

The highest mud weight needed to balance formation is expected to be 9-12 ppg. In order to maintain hole stability, mud weights up to 12 ppg may be utilized.

An electronic pit volume totalizer (PVT) will be utilized on the circulating system, to monitor pit volume, flow rate, pump pressure and stroke rate.

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept at the wellsite at all times.

7. Auxiliary well control and monitoring equipment:

(A) A kelly cock will be kept in the drill string at all times.

(B) A full opening drill pipe-stabbing valve (inside BOP) with proper drill pipe connections will be kept on the rig floor at all times.

(C) H₂S monitoring and detection equipment will be utilized from surface casing point to TD.

(D) A wear bushing will be installed in the wellhead prior to drilling out of the surface casing.

8. Logging, testing and coring program:

GR–CCL–CNL Will be run in cased hole during completions phase of operations.

Open-hole logs are not planned for this well.

9. Abnormal conditions, pressures, temperatures and potential hazards:



The estimated bottom-hole temperature at 11,006' TVD (deepest point of the well) is 190F with an estimated maximum bottom-hole pressure (BHP) at the same point of 6,868' psig (based on 12 ppg MW). Hydrogen Sulfide may be present in the area. All necessary precautions will be taken before drilling operations commence. See Hydrogen Sulfide Plan below:

10. Hydrogen Sulfide Plan:

- A. All personnel shall receive proper awareness H2S training.
- B. Briefing Area: two perpendicular areas will be designated by signs and readily accessible.
- C. Required Emergency Equipment
 - a. Well Control Equipment
 - i. Flare line 150' from wellhead to be ignited by auto ignition sparking system.
 - ii. Choke manifold with a remotely operated hydraulic choke.
 - iii. Mud/gas separator
 - b. Protective equipment for essential personnel
 - i. Breathing Apparatus
 - 1. Rescue packs (SCBA) – 1 unit shall be placed at each briefing area, 2 shall be stored in a safety trailer on site.
 - 2. Work/Escapes packs – 4 packs shall be stored on the rig floor with sufficient air hose not to restrict work activity
 - 3. Emergency Escape Packs – 4 packs shall be stored in the doghouse for emergency evacuation.
 - ii. Auxiliary Rescue Equipment
 - 1. Stretcher
 - 2. Two OSHA full body harnesses
 - 3. 100 feet of 5/8 inches OSHA approved rope
 - 4. 1-20# class ABC fire extinguisher
 - c. H2S Detection and Monitoring Equipment
 - i. A stationary detector with three sensors will be placed in the doghouse if equipped, set to visually alarm at 10 ppm and audible at 14 ppm. The detector will be calibrated a minimum of every 30 days or as needed. The sensors will be placed in the following places:
 - 1. Rig Floor
 - 2. Below Rig Floor / Near BOPs
 - 3. End of flow line or where well bore fluid is being discharged (near shakers)
 - ii. If H2S is encountered, measured values and formations will be provided to the BLM.
 - d. Visual Warning Systems
 - i. One color code condition sign will be placed at the entrance to the site reflecting the possible conditions at the site.
 - ii. A colored condition flag will be on display, reflecting the current condition at the site at the time.
 - iii. Two windsocks will be placed in strategic locations, visible from all angles.
 - e. Mud Program
 - i. The Mud program will be designed to minimize the volume of H2S circulated to surface. The operator will have the necessary mud products to minimize hazards while drilling in H2S bearing zones.



- f. Metallurgy
 - i. All drill strings, casings, tubing, wellhead, blowout preventer, drilling spool, kill lines, choke manifold and lines, and valves shall be suitable for H₂S service at the anticipated operating pressures to prevent sour sulfide stress cracking.
- g. Communication
 - i. Communication will be via cell phones and walkie talkies on location.

Based on concentrations of offset wells, proximity to main roads, and distance to populated areas, the radius of exposure created by a potential release was determined to be minimal and low enough to not necessitate an H₂S contingency plan. This will be reevaluated during wellbore construction if H₂S is observed and after the well is on production.

11. Anticipated starting date and duration of operations:

The drilling operations on the well should be finished in approximately one month. However, in order to minimize disturbance in the area and to improve efficiency Franklin Mountain is planning to drill all the wells on the pad prior to commence completion operations. To even further reduce the time heavy machinery is used the "batch drilling" method may be used. A batch drilling sequence sundry will be submitted for State approval prior to spud. A drilling rig with walking/skidding capabilities will be used.

12. Disposal/environmental concerns:

- (A) Drilled cuttings will be hauled to and disposed of in a state-certified disposal site.
- (B) Non-hazardous waste mud/cement from the drilling process will also be hauled to and disposed of in a state-certified disposal site.
- (C) Garbage will be hauled to the Pecos City Landfill.
- (D) Sewage (grey water) will be hauled to the Carlsbad City Landfill

13. Wellhead:

A multi-bowl wellhead system will be utilized.

After running the 13 3/8" surface casing, a 13-5/8" BOP/BOPE system with a minimum working pressure of 10,000 psi will be installed on the wellhead system and will be pressure tested to 250 psi low followed by a 5,000 psi pressure test. This pressure test will be repeated at least every 30 days.

The minimum working pressure of the BOP and related BOPE required for drilling below the surface casing shoe shall be 5,000 psi.

The wellhead will be installed by a third party welder while being monitored by WH vendor's representative.

All BOP equipment will be tested utilizing a conventional test plug. Not a cup or J-packer type.

A solid steel body pack-off will be utilized after running and cementing the intermediate casing string. After installation of the first intermediate string the pack-off and lower flanges will be pressure tested to 5000 psi.

Both the surface and intermediate casing strings will be tested as per NMOCD Rules to the one-third of manufacture's rated yield pressure, no less than 600 psi, but not greater than 1,500 psi.

14. Additional variance requests

- A. Casing.



1. Variance is requested to wave/reduce the centralizer requirements for the 7" and 5 ½" production casing due to the tight clearance with 8 ¾" hole.



Franklin Mountain Energy LLC

PV_Lea County, NM(N83-NME3001)

Satellite_Cross Pad 3

(B01) Satellite State Com 703H - Slot (B01) SSC 703H

703H

Plan: Plan01

Standard Planning Report

17 May, 2024



Planning Report

Database:	TZ USA 17.2	Local Co-ordinate Reference:	Well (B01) Satellite State Com 703H - Slot (B01) SSC 703H
Company:	Franklin Mountain Energy LLC	TVD Reference:	3962+30 @ 3992.00usft
Project:	PV_Lea County, NM(N83-NME3001)	MD Reference:	3962+30 @ 3992.00usft
Site:	Satellite_Cross Pad 3	North Reference:	Grid
Well:	(B01) Satellite State Com 703H	Survey Calculation Method:	Minimum Curvature
Wellbore:	703H		
Design:	Plan01		

Project	PV_Lea County, NM(N83-NME3001)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Satellite_Cross Pad 3		
Site Position:		Northing:	622,527.95 usft
From:	Map	Easting:	793,884.28 usft
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16 "
		Latitude:	32.70868257
		Longitude:	-103.51226860

Well	(B01) Satellite State Com 703H - Slot (B01) SSC 703H		
Well Position	+N/-S	0.00 usft	Northing: 622,427.82 usft
	+E/-W	0.00 usft	Easting: 793,870.33 usft
Position Uncertainty	0.00 usft	Wellhead Elevation:	usft
Grid Convergence:	0.44 °	Ground Level:	3,962.00 usft

Wellbore	703H				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	5/25/2024	6.21	60.25	47,474.46150131

Design	Plan01			
Audit Notes:				
Version:	Phase:	PLAN	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.00	0.00	0.00	359.49

Plan Survey Tool Program	Date	5/17/2024		
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks
1	0.00	22,506.36 Plan01 (703H)	MWD+IFR1+MS	
			OWSG MWD + IFR1 + Multi-SI	



Planning Report

Database:	TZ USA 17.2	Local Co-ordinate Reference:	Well (B01) Satellite State Com 703H - Slot (B01) SSC 703H
Company:	Franklin Mountain Energy LLC	TVD Reference:	3962+30 @ 3992.00usft
Project:	PV_Lea County, NM(N83-NME3001)	MD Reference:	3962+30 @ 3992.00usft
Site:	Satellite_Cross Pad 3	North Reference:	Grid
Well:	(B01) Satellite State Com 703H	Survey Calculation Method:	Minimum Curvature
Wellbore:	703H		
Design:	Plan01		

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,500.00	0.00	0.00	2,500.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,952.29	6.78	109.55	2,951.23	-8.95	25.20	1.50	1.50	0.00	109.55	
5,844.46	6.78	109.55	5,823.15	-123.26	347.17	0.00	0.00	0.00	0.00	
6,522.89	0.00	0.00	6,500.00	-136.68	384.98	1.00	-1.00	0.00	180.00	
10,455.93	0.00	0.00	10,433.04	-136.68	384.98	0.00	0.00	0.00	0.00	
11,355.93	90.00	7.70	11,006.00	431.11	461.75	10.00	10.00	0.00	7.70	
11,766.31	90.00	359.49	11,006.00	840.34	487.46	2.00	0.00	-2.00	-90.00	
22,506.36	90.00	359.49	11,006.00	11,579.96	392.28	0.00	0.00	0.00	0.00	02-PBHL(SSC-703H)



Planning Report

Database:	TZ USA 17.2	Local Co-ordinate Reference:	Well (B01) Satellite State Com 703H - Slot (B01) SSC 703H
Company:	Franklin Mountain Energy LLC	TVD Reference:	3962+30 @ 3992.00usft
Project:	PV_Lea County, NM(N83-NME3001)	MD Reference:	3962+30 @ 3992.00usft
Site:	Satellite_Cross Pad 3	North Reference:	Grid
Well:	(B01) Satellite State Com 703H	Survey Calculation Method:	Minimum Curvature
Wellbore:	703H		
Design:	Plan01		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
30.00	0.00	0.00	30.00	0.00	0.00	0.00	0.00	0.00	0.00	
Cenozoic Alluvium (surface)										
100.00	0.00	0.00	100.00	0.00	0.00	0.00	0.00	0.00	0.00	
200.00	0.00	0.00	200.00	0.00	0.00	0.00	0.00	0.00	0.00	
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00	
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00	0.00	
500.00	0.00	0.00	500.00	0.00	0.00	0.00	0.00	0.00	0.00	
600.00	0.00	0.00	600.00	0.00	0.00	0.00	0.00	0.00	0.00	
700.00	0.00	0.00	700.00	0.00	0.00	0.00	0.00	0.00	0.00	
800.00	0.00	0.00	800.00	0.00	0.00	0.00	0.00	0.00	0.00	
900.00	0.00	0.00	900.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,000.00	0.00	0.00	1,000.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,100.00	0.00	0.00	1,100.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,200.00	0.00	0.00	1,200.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,300.00	0.00	0.00	1,300.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,400.00	0.00	0.00	1,400.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,500.00	0.00	0.00	1,500.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,600.00	0.00	0.00	1,600.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,700.00	0.00	0.00	1,700.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,800.00	0.00	0.00	1,800.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,900.00	0.00	0.00	1,900.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,947.00	0.00	0.00	1,947.00	0.00	0.00	0.00	0.00	0.00	0.00	
Rustler										
2,000.00	0.00	0.00	2,000.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,100.00	0.00	0.00	2,100.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,200.00	0.00	0.00	2,200.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,224.00	0.00	0.00	2,224.00	0.00	0.00	0.00	0.00	0.00	0.00	
Salado										
2,300.00	0.00	0.00	2,300.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,400.00	0.00	0.00	2,400.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,500.00	0.00	0.00	2,500.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,600.00	1.50	109.55	2,599.99	-0.44	1.23	-0.45	1.50	1.50	0.00	
2,700.00	3.00	109.55	2,699.91	-1.75	4.93	-1.80	1.50	1.50	0.00	
2,800.00	4.50	109.55	2,799.69	-3.94	11.10	-4.04	1.50	1.50	0.00	
2,900.00	6.00	109.55	2,899.27	-7.00	19.72	-7.18	1.50	1.50	0.00	
2,952.29	6.78	109.55	2,951.23	-8.95	25.20	-9.17	1.50	1.50	0.00	
3,000.00	6.78	109.55	2,998.61	-10.83	30.52	-11.11	0.00	0.00	0.00	
3,100.00	6.78	109.55	3,097.91	-14.79	41.65	-15.16	0.00	0.00	0.00	
3,200.00	6.78	109.55	3,197.21	-18.74	52.78	-19.21	0.00	0.00	0.00	
3,262.23	6.78	109.55	3,259.00	-21.20	59.71	-21.73	0.00	0.00	0.00	
Base Salt										
3,300.00	6.78	109.55	3,296.51	-22.69	63.91	-23.26	0.00	0.00	0.00	
3,400.00	6.78	109.55	3,395.81	-26.64	75.05	-27.31	0.00	0.00	0.00	
3,500.00	6.78	109.55	3,495.11	-30.60	86.18	-31.36	0.00	0.00	0.00	
3,569.38	6.78	109.55	3,564.00	-33.34	93.90	-34.17	0.00	0.00	0.00	
Yates										
3,600.00	6.78	109.55	3,594.41	-34.55	97.31	-35.41	0.00	0.00	0.00	
3,700.00	6.78	109.55	3,693.71	-38.50	108.44	-39.46	0.00	0.00	0.00	
3,800.00	6.78	109.55	3,793.01	-42.45	119.58	-43.52	0.00	0.00	0.00	
3,900.00	6.78	109.55	3,892.31	-46.41	130.71	-47.57	0.00	0.00	0.00	
3,918.82	6.78	109.55	3,911.00	-47.15	132.80	-48.33	0.00	0.00	0.00	



Planning Report

Database:	TZ USA 17.2	Local Co-ordinate Reference:	Well (B01) Satellite State Com 703H - Slot (B01) SSC 703H
Company:	Franklin Mountain Energy LLC	TVD Reference:	3962+30 @ 3992.00usft
Project:	PV_Lea County, NM(N83-NME3001)	MD Reference:	3962+30 @ 3992.00usft
Site:	Satellite_Cross Pad 3	North Reference:	Grid
Well:	(B01) Satellite State Com 703H	Survey Calculation Method:	Minimum Curvature
Wellbore:	703H		
Design:	Plan01		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
Seven Rivers									
4,000.00	6.78	109.55	3,991.61	-50.36	141.84	-51.62	0.00	0.00	0.00
4,100.00	6.78	109.55	4,090.91	-54.31	152.97	-55.67	0.00	0.00	0.00
4,200.00	6.78	109.55	4,190.21	-58.26	164.11	-59.72	0.00	0.00	0.00
4,300.00	6.78	109.55	4,289.51	-62.21	175.24	-63.77	0.00	0.00	0.00
4,400.00	6.78	109.55	4,388.81	-66.17	186.37	-67.82	0.00	0.00	0.00
4,500.00	6.78	109.55	4,488.11	-70.12	197.50	-71.88	0.00	0.00	0.00
4,535.31	6.78	109.55	4,523.17	-71.52	201.43	-73.31	0.00	0.00	0.00
00-EON(SSC-703H)									
4,600.00	6.78	109.55	4,587.41	-74.07	208.63	-75.93	0.00	0.00	0.00
4,700.00	6.78	109.55	4,686.71	-78.02	219.77	-79.98	0.00	0.00	0.00
4,702.31	6.78	109.55	4,689.00	-78.12	220.02	-80.07	0.00	0.00	0.00
Queen									
4,800.00	6.78	109.55	4,786.01	-81.98	230.90	-84.03	0.00	0.00	0.00
4,900.00	6.78	109.55	4,885.31	-85.93	242.03	-88.08	0.00	0.00	0.00
5,000.00	6.78	109.55	4,984.61	-89.88	253.16	-92.13	0.00	0.00	0.00
5,100.00	6.78	109.55	5,083.91	-93.83	264.30	-96.18	0.00	0.00	0.00
5,200.00	6.78	109.55	5,183.21	-97.79	275.43	-100.23	0.00	0.00	0.00
5,300.00	6.78	109.55	5,282.51	-101.74	286.56	-104.29	0.00	0.00	0.00
5,400.00	6.78	109.55	5,381.80	-105.69	297.69	-108.34	0.00	0.00	0.00
5,500.00	6.78	109.55	5,481.10	-109.64	308.83	-112.39	0.00	0.00	0.00
5,600.00	6.78	109.55	5,580.40	-113.60	319.96	-116.44	0.00	0.00	0.00
5,700.00	6.78	109.55	5,679.70	-117.55	331.09	-120.49	0.00	0.00	0.00
5,800.00	6.78	109.55	5,779.00	-121.50	342.22	-124.54	0.00	0.00	0.00
5,844.46	6.78	109.55	5,823.15	-123.26	347.17	-126.34	0.00	0.00	0.00
5,900.00	6.23	109.55	5,878.33	-125.36	353.10	-128.50	1.00	-1.00	0.00
6,000.00	5.23	109.55	5,977.83	-128.70	362.51	-131.93	1.00	-1.00	0.00
6,100.00	4.23	109.55	6,077.49	-131.46	370.28	-134.75	1.00	-1.00	0.00
6,200.00	3.23	109.55	6,177.28	-133.64	376.41	-136.98	1.00	-1.00	0.00
6,300.00	2.23	109.55	6,277.16	-135.23	380.89	-138.62	1.00	-1.00	0.00
6,373.87	1.49	109.55	6,351.00	-136.03	383.15	-139.44	1.00	-1.00	0.00
Delaware Mtn Group									
6,400.00	1.23	109.55	6,377.12	-136.24	383.74	-139.65	1.00	-1.00	0.00
6,500.00	0.23	109.55	6,477.11	-136.66	384.94	-140.09	1.00	-1.00	0.00
6,522.89	0.00	0.00	6,500.00	-136.68	384.98	-140.10	1.00	-1.00	0.00
6,600.00	0.00	0.00	6,577.11	-136.68	384.98	-140.10	0.00	0.00	0.00
6,700.00	0.00	0.00	6,677.11	-136.68	384.98	-140.10	0.00	0.00	0.00
6,800.00	0.00	0.00	6,777.11	-136.68	384.98	-140.10	0.00	0.00	0.00
6,900.00	0.00	0.00	6,877.11	-136.68	384.98	-140.10	0.00	0.00	0.00
7,000.00	0.00	0.00	6,977.11	-136.68	384.98	-140.10	0.00	0.00	0.00
7,100.00	0.00	0.00	7,077.11	-136.68	384.98	-140.10	0.00	0.00	0.00
7,200.00	0.00	0.00	7,177.11	-136.68	384.98	-140.10	0.00	0.00	0.00
7,300.00	0.00	0.00	7,277.11	-136.68	384.98	-140.10	0.00	0.00	0.00
7,400.00	0.00	0.00	7,377.11	-136.68	384.98	-140.10	0.00	0.00	0.00
7,500.00	0.00	0.00	7,477.11	-136.68	384.98	-140.10	0.00	0.00	0.00
7,600.00	0.00	0.00	7,577.11	-136.68	384.98	-140.10	0.00	0.00	0.00
7,700.00	0.00	0.00	7,677.11	-136.68	384.98	-140.10	0.00	0.00	0.00
7,782.89	0.00	0.00	7,760.00	-136.68	384.98	-140.10	0.00	0.00	0.00
Bone Spring Lime									
7,800.00	0.00	0.00	7,777.11	-136.68	384.98	-140.10	0.00	0.00	0.00
7,900.00	0.00	0.00	7,877.11	-136.68	384.98	-140.10	0.00	0.00	0.00
8,000.00	0.00	0.00	7,977.11	-136.68	384.98	-140.10	0.00	0.00	0.00

Planning Report



Database:	TZ USA 17.2	Local Co-ordinate Reference:	Well (B01) Satellite State Com 703H - Slot (B01) SSC 703H
Company:	Franklin Mountain Energy LLC	TVD Reference:	3962+30 @ 3992.00usft
Project:	PV_Lea County, NM(N83-NME3001)	MD Reference:	3962+30 @ 3992.00usft
Site:	Satellite_Cross Pad 3	North Reference:	Grid
Well:	(B01) Satellite State Com 703H	Survey Calculation Method:	Minimum Curvature
Wellbore:	703H		
Design:	Plan01		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
8,100.00	0.00	0.00	8,077.11	-136.68	384.98	-140.10	0.00	0.00	0.00
8,200.00	0.00	0.00	8,177.11	-136.68	384.98	-140.10	0.00	0.00	0.00
8,300.00	0.00	0.00	8,277.11	-136.68	384.98	-140.10	0.00	0.00	0.00
8,400.00	0.00	0.00	8,377.11	-136.68	384.98	-140.10	0.00	0.00	0.00
8,500.00	0.00	0.00	8,477.11	-136.68	384.98	-140.10	0.00	0.00	0.00
8,600.00	0.00	0.00	8,577.11	-136.68	384.98	-140.10	0.00	0.00	0.00
8,700.00	0.00	0.00	8,677.11	-136.68	384.98	-140.10	0.00	0.00	0.00
8,800.00	0.00	0.00	8,777.11	-136.68	384.98	-140.10	0.00	0.00	0.00
8,900.00	0.00	0.00	8,877.11	-136.68	384.98	-140.10	0.00	0.00	0.00
9,000.00	0.00	0.00	8,977.11	-136.68	384.98	-140.10	0.00	0.00	0.00
9,100.00	0.00	0.00	9,077.11	-136.68	384.98	-140.10	0.00	0.00	0.00
9,200.00	0.00	0.00	9,177.11	-136.68	384.98	-140.10	0.00	0.00	0.00
9,262.89	0.00	0.00	9,240.00	-136.68	384.98	-140.10	0.00	0.00	0.00
First Bone Spring Sand									
9,300.00	0.00	0.00	9,277.11	-136.68	384.98	-140.10	0.00	0.00	0.00
9,400.00	0.00	0.00	9,377.11	-136.68	384.98	-140.10	0.00	0.00	0.00
9,424.89	0.00	0.00	9,402.00	-136.68	384.98	-140.10	0.00	0.00	0.00
Second Bone Spring Carbonate									
9,500.00	0.00	0.00	9,477.11	-136.68	384.98	-140.10	0.00	0.00	0.00
9,544.89	0.00	0.00	9,522.00	-136.68	384.98	-140.10	0.00	0.00	0.00
Second Bone Spring Sand									
9,600.00	0.00	0.00	9,577.11	-136.68	384.98	-140.10	0.00	0.00	0.00
9,700.00	0.00	0.00	9,677.11	-136.68	384.98	-140.10	0.00	0.00	0.00
9,800.00	0.00	0.00	9,777.11	-136.68	384.98	-140.10	0.00	0.00	0.00
9,900.00	0.00	0.00	9,877.11	-136.68	384.98	-140.10	0.00	0.00	0.00
10,000.00	0.00	0.00	9,977.11	-136.68	384.98	-140.10	0.00	0.00	0.00
10,100.00	0.00	0.00	10,077.11	-136.68	384.98	-140.10	0.00	0.00	0.00
10,169.89	0.00	0.00	10,147.00	-136.68	384.98	-140.10	0.00	0.00	0.00
Third Bone Spring Carbonate									
10,200.00	0.00	0.00	10,177.11	-136.68	384.98	-140.10	0.00	0.00	0.00
10,260.89	0.00	0.00	10,238.00	-136.68	384.98	-140.10	0.00	0.00	0.00
Third Bone Spring Sand									
10,300.00	0.00	0.00	10,277.11	-136.68	384.98	-140.10	0.00	0.00	0.00
10,400.00	0.00	0.00	10,377.11	-136.68	384.98	-140.10	0.00	0.00	0.00
10,455.93	0.00	0.00	10,433.04	-136.68	384.98	-140.10	0.00	0.00	0.00
KOP: 10455.93' MD/-140.10' VS/10433.04' TVD									
10,500.00	4.41	7.70	10,477.07	-135.00	385.21	-138.43	10.00	10.00	0.00
10,550.00	9.41	7.70	10,526.69	-129.04	386.01	-132.48	10.00	10.00	0.00
10,600.00	14.41	7.70	10,575.60	-118.82	387.39	-122.27	10.00	10.00	0.00
10,650.00	19.41	7.70	10,623.42	-104.42	389.34	-107.88	10.00	10.00	0.00
10,696.21	24.03	7.70	10,666.34	-87.48	391.63	-90.96	10.00	10.00	0.00
100FLL: 10696.21' MD/-90.96VS									
10,700.00	24.41	7.70	10,669.79	-85.94	391.84	-89.42	10.00	10.00	0.00
10,750.00	29.41	7.70	10,714.37	-63.52	394.87	-67.04	10.00	10.00	0.00
10,800.00	34.41	7.70	10,756.80	-37.34	398.41	-40.89	10.00	10.00	0.00
10,821.12	36.52	7.70	10,774.00	-25.20	400.05	-28.76	10.00	10.00	0.00
Wolfcamp									
10,850.00	39.41	7.70	10,796.77	-7.60	402.43	-11.18	10.00	10.00	0.00
10,900.00	44.41	7.70	10,833.97	25.49	406.91	21.86	10.00	10.00	0.00
10,945.14	48.92	7.70	10,864.94	58.02	411.30	54.35	10.00	10.00	0.00
01-T98(SSC-703H)									
10,950.00	49.41	7.70	10,868.12	61.66	411.80	57.99	10.00	10.00	0.00



Planning Report

Database:	TZ USA 17.2	Local Co-ordinate Reference:	Well (B01) Satellite State Com 703H - Slot (B01) SSC 703H
Company:	Franklin Mountain Energy LLC	TVD Reference:	3962+30 @ 3992.00usft
Project:	PV_Lea County, NM(N83-NME3001)	MD Reference:	3962+30 @ 3992.00usft
Site:	Satellite_Cross Pad 3	North Reference:	Grid
Well:	(B01) Satellite State Com 703H	Survey Calculation Method:	Minimum Curvature
Wellbore:	703H		
Design:	Plan01		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
11,000.00	54.41	7.70	10,898.95	100.64	417.07	96.92	10.00	10.00	0.00	
11,050.00	59.41	7.70	10,926.24	142.14	422.68	138.37	10.00	10.00	0.00	
11,100.00	64.41	7.70	10,949.78	185.84	428.59	182.01	10.00	10.00	0.00	
11,150.00	69.41	7.70	10,969.39	231.40	434.75	227.52	10.00	10.00	0.00	
11,200.00	74.41	7.70	10,984.91	278.49	441.11	274.55	10.00	10.00	0.00	
11,250.00	79.41	7.70	10,996.23	326.73	447.63	322.73	10.00	10.00	0.00	
11,300.00	84.41	7.70	11,003.27	375.77	454.26	371.71	10.00	10.00	0.00	
11,350.00	89.41	7.70	11,005.97	425.23	460.95	421.11	10.00	10.00	0.00	
11,355.93	90.00	7.70	11,006.00	431.11	461.75	426.98	10.00	10.00	0.00	
EOC: 11355.93' MD/426.98' VS/11006.00' TVD - HZ Target										
11,400.00	90.00	6.82	11,006.00	474.83	467.32	470.65	2.00	0.00	-2.00	
11,500.00	90.00	4.82	11,006.00	574.31	477.45	570.03	2.00	0.00	-2.00	
11,600.00	90.00	2.82	11,006.00	674.08	484.11	669.74	2.00	0.00	-2.00	
11,700.00	90.00	0.82	11,006.00	774.02	487.28	769.65	2.00	0.00	-2.00	
11,766.31	90.00	359.49	11,006.00	840.34	487.46	835.96	2.00	0.00	-2.00	
11,800.00	90.00	359.49	11,006.00	874.02	487.17	869.65	0.00	0.00	0.00	
11,900.00	90.00	359.49	11,006.00	974.02	486.28	969.65	0.00	0.00	0.00	
12,000.00	90.00	359.49	11,006.00	1,074.01	485.39	1,069.65	0.00	0.00	0.00	
12,100.00	90.00	359.49	11,006.00	1,174.01	484.51	1,169.65	0.00	0.00	0.00	
12,200.00	90.00	359.49	11,006.00	1,274.00	483.62	1,269.65	0.00	0.00	0.00	
12,300.00	90.00	359.49	11,006.00	1,374.00	482.73	1,369.65	0.00	0.00	0.00	
12,400.00	90.00	359.49	11,006.00	1,474.00	481.85	1,469.65	0.00	0.00	0.00	
12,500.00	90.00	359.49	11,006.00	1,573.99	480.96	1,569.65	0.00	0.00	0.00	
12,600.00	90.00	359.49	11,006.00	1,673.99	480.08	1,669.65	0.00	0.00	0.00	
12,700.00	90.00	359.49	11,006.00	1,773.99	479.19	1,769.65	0.00	0.00	0.00	
12,800.00	90.00	359.49	11,006.00	1,873.98	478.30	1,869.65	0.00	0.00	0.00	
12,900.00	90.00	359.49	11,006.00	1,973.98	477.42	1,969.65	0.00	0.00	0.00	
13,000.00	90.00	359.49	11,006.00	2,073.97	476.53	2,069.65	0.00	0.00	0.00	
13,100.00	90.00	359.49	11,006.00	2,173.97	475.64	2,169.65	0.00	0.00	0.00	
13,200.00	90.00	359.49	11,006.00	2,273.97	474.76	2,269.65	0.00	0.00	0.00	
13,300.00	90.00	359.49	11,006.00	2,373.96	473.87	2,369.65	0.00	0.00	0.00	
13,400.00	90.00	359.49	11,006.00	2,473.96	472.99	2,469.65	0.00	0.00	0.00	
13,500.00	90.00	359.49	11,006.00	2,573.95	472.10	2,569.65	0.00	0.00	0.00	
13,600.00	90.00	359.49	11,006.00	2,673.95	471.21	2,669.65	0.00	0.00	0.00	
13,700.00	90.00	359.49	11,006.00	2,773.95	470.33	2,769.65	0.00	0.00	0.00	
13,800.00	90.00	359.49	11,006.00	2,873.94	469.44	2,869.65	0.00	0.00	0.00	
13,900.00	90.00	359.49	11,006.00	2,973.94	468.55	2,969.65	0.00	0.00	0.00	
14,000.00	90.00	359.49	11,006.00	3,073.93	467.67	3,069.65	0.00	0.00	0.00	
14,100.00	90.00	359.49	11,006.00	3,173.93	466.78	3,169.65	0.00	0.00	0.00	
14,200.00	90.00	359.49	11,006.00	3,273.93	465.90	3,269.65	0.00	0.00	0.00	
14,300.00	90.00	359.49	11,006.00	3,373.92	465.01	3,369.65	0.00	0.00	0.00	
14,400.00	90.00	359.49	11,006.00	3,473.92	464.12	3,469.65	0.00	0.00	0.00	
14,500.00	90.00	359.49	11,006.00	3,573.91	463.24	3,569.65	0.00	0.00	0.00	
14,600.00	90.00	359.49	11,006.00	3,673.91	462.35	3,669.65	0.00	0.00	0.00	
14,700.00	90.00	359.49	11,006.00	3,773.91	461.46	3,769.65	0.00	0.00	0.00	
14,800.00	90.00	359.49	11,006.00	3,873.90	460.58	3,869.65	0.00	0.00	0.00	
14,900.00	90.00	359.49	11,006.00	3,973.90	459.69	3,969.65	0.00	0.00	0.00	
15,000.00	90.00	359.49	11,006.00	4,073.90	458.81	4,069.65	0.00	0.00	0.00	
15,100.00	90.00	359.49	11,006.00	4,173.89	457.92	4,169.65	0.00	0.00	0.00	
15,200.00	90.00	359.49	11,006.00	4,273.89	457.03	4,269.65	0.00	0.00	0.00	
15,300.00	90.00	359.49	11,006.00	4,373.88	456.15	4,369.65	0.00	0.00	0.00	
15,400.00	90.00	359.49	11,006.00	4,473.88	455.26	4,469.65	0.00	0.00	0.00	
15,500.00	90.00	359.49	11,006.00	4,573.88	454.37	4,569.65	0.00	0.00	0.00	



Planning Report

Database:	TZ USA 17.2	Local Co-ordinate Reference:	Well (B01) Satellite State Com 703H - Slot (B01) SSC 703H
Company:	Franklin Mountain Energy LLC	TVD Reference:	3962+30 @ 3992.00usft
Project:	PV_Lea County, NM(N83-NME3001)	MD Reference:	3962+30 @ 3992.00usft
Site:	Satellite_Cross Pad 3	North Reference:	Grid
Well:	(B01) Satellite State Com 703H	Survey Calculation Method:	Minimum Curvature
Wellbore:	703H		
Design:	Plan01		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
15,600.00	90.00	359.49	11,006.00	4,673.87	453.49	4,669.65	0.00	0.00	0.00
15,700.00	90.00	359.49	11,006.00	4,773.87	452.60	4,769.65	0.00	0.00	0.00
15,800.00	90.00	359.49	11,006.00	4,873.86	451.72	4,869.65	0.00	0.00	0.00
15,900.00	90.00	359.49	11,006.00	4,973.86	450.83	4,969.65	0.00	0.00	0.00
16,000.00	90.00	359.49	11,006.00	5,073.86	449.94	5,069.65	0.00	0.00	0.00
16,100.00	90.00	359.49	11,006.00	5,173.85	449.06	5,169.65	0.00	0.00	0.00
16,200.00	90.00	359.49	11,006.00	5,273.85	448.17	5,269.65	0.00	0.00	0.00
16,300.00	90.00	359.49	11,006.00	5,373.84	447.28	5,369.65	0.00	0.00	0.00
16,400.00	90.00	359.49	11,006.00	5,473.84	446.40	5,469.65	0.00	0.00	0.00
16,500.00	90.00	359.49	11,006.00	5,573.84	445.51	5,569.65	0.00	0.00	0.00
16,600.00	90.00	359.49	11,006.00	5,673.83	444.63	5,669.65	0.00	0.00	0.00
16,700.00	90.00	359.49	11,006.00	5,773.83	443.74	5,769.65	0.00	0.00	0.00
16,800.00	90.00	359.49	11,006.00	5,873.82	442.85	5,869.65	0.00	0.00	0.00
16,900.00	90.00	359.49	11,006.00	5,973.82	441.97	5,969.65	0.00	0.00	0.00
17,000.00	90.00	359.49	11,006.00	6,073.82	441.08	6,069.65	0.00	0.00	0.00
17,100.00	90.00	359.49	11,006.00	6,173.81	440.19	6,169.65	0.00	0.00	0.00
17,200.00	90.00	359.49	11,006.00	6,273.81	439.31	6,269.65	0.00	0.00	0.00
17,300.00	90.00	359.49	11,006.00	6,373.80	438.42	6,369.65	0.00	0.00	0.00
17,400.00	90.00	359.49	11,006.00	6,473.80	437.54	6,469.65	0.00	0.00	0.00
17,500.00	90.00	359.49	11,006.00	6,573.80	436.65	6,569.65	0.00	0.00	0.00
17,600.00	90.00	359.49	11,006.00	6,673.79	435.76	6,669.65	0.00	0.00	0.00
17,700.00	90.00	359.49	11,006.00	6,773.79	434.88	6,769.65	0.00	0.00	0.00
17,800.00	90.00	359.49	11,006.00	6,873.79	433.99	6,869.65	0.00	0.00	0.00
17,900.00	90.00	359.49	11,006.00	6,973.78	433.10	6,969.65	0.00	0.00	0.00
18,000.00	90.00	359.49	11,006.00	7,073.78	432.22	7,069.65	0.00	0.00	0.00
18,100.00	90.00	359.49	11,006.00	7,173.77	431.33	7,169.65	0.00	0.00	0.00
18,200.00	90.00	359.49	11,006.00	7,273.77	430.45	7,269.65	0.00	0.00	0.00
18,300.00	90.00	359.49	11,006.00	7,373.77	429.56	7,369.65	0.00	0.00	0.00
18,400.00	90.00	359.49	11,006.00	7,473.76	428.67	7,469.65	0.00	0.00	0.00
18,500.00	90.00	359.49	11,006.00	7,573.76	427.79	7,569.65	0.00	0.00	0.00
18,600.00	90.00	359.49	11,006.00	7,673.75	426.90	7,669.65	0.00	0.00	0.00
18,700.00	90.00	359.49	11,006.00	7,773.75	426.01	7,769.65	0.00	0.00	0.00
18,800.00	90.00	359.49	11,006.00	7,873.75	425.13	7,869.65	0.00	0.00	0.00
18,900.00	90.00	359.49	11,006.00	7,973.74	424.24	7,969.65	0.00	0.00	0.00
19,000.00	90.00	359.49	11,006.00	8,073.74	423.36	8,069.65	0.00	0.00	0.00
19,100.00	90.00	359.49	11,006.00	8,173.73	422.47	8,169.65	0.00	0.00	0.00
19,200.00	90.00	359.49	11,006.00	8,273.73	421.58	8,269.65	0.00	0.00	0.00
19,300.00	90.00	359.49	11,006.00	8,373.73	420.70	8,369.65	0.00	0.00	0.00
19,400.00	90.00	359.49	11,006.00	8,473.72	419.81	8,469.65	0.00	0.00	0.00
19,500.00	90.00	359.49	11,006.00	8,573.72	418.92	8,569.65	0.00	0.00	0.00
19,600.00	90.00	359.49	11,006.00	8,673.71	418.04	8,669.65	0.00	0.00	0.00
19,700.00	90.00	359.49	11,006.00	8,773.71	417.15	8,769.65	0.00	0.00	0.00
19,800.00	90.00	359.49	11,006.00	8,873.71	416.27	8,869.65	0.00	0.00	0.00
19,900.00	90.00	359.49	11,006.00	8,973.70	415.38	8,969.65	0.00	0.00	0.00
20,000.00	90.00	359.49	11,006.00	9,073.70	414.49	9,069.65	0.00	0.00	0.00
20,100.00	90.00	359.49	11,006.00	9,173.69	413.61	9,169.65	0.00	0.00	0.00
20,200.00	90.00	359.49	11,006.00	9,273.69	412.72	9,269.65	0.00	0.00	0.00
20,300.00	90.00	359.49	11,006.00	9,373.69	411.83	9,369.65	0.00	0.00	0.00
20,400.00	90.00	359.49	11,006.00	9,473.68	410.95	9,469.65	0.00	0.00	0.00
20,500.00	90.00	359.49	11,006.00	9,573.68	410.06	9,569.65	0.00	0.00	0.00
20,600.00	90.00	359.49	11,006.00	9,673.68	409.18	9,669.65	0.00	0.00	0.00
20,700.00	90.00	359.49	11,006.00	9,773.67	408.29	9,769.65	0.00	0.00	0.00
20,800.00	90.00	359.49	11,006.00	9,873.67	407.40	9,869.65	0.00	0.00	0.00



Planning Report

Database:	TZ USA 17.2	Local Co-ordinate Reference:	Well (B01) Satellite State Com 703H - Slot (B01) SSC 703H
Company:	Franklin Mountain Energy LLC	TVD Reference:	3962+30 @ 3992.00usft
Project:	PV_Lea County, NM(N83-NME3001)	MD Reference:	3962+30 @ 3992.00usft
Site:	Satellite_Cross Pad 3	North Reference:	Grid
Well:	(B01) Satellite State Com 703H	Survey Calculation Method:	Minimum Curvature
Wellbore:	703H		
Design:	Plan01		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
20,900.00	90.00	359.49	11,006.00	9,973.66	406.52	9,969.65	0.00	0.00	0.00	
21,000.00	90.00	359.49	11,006.00	10,073.66	405.63	10,069.65	0.00	0.00	0.00	
21,100.00	90.00	359.49	11,006.00	10,173.66	404.74	10,169.65	0.00	0.00	0.00	
21,200.00	90.00	359.49	11,006.00	10,273.65	403.86	10,269.65	0.00	0.00	0.00	
21,300.00	90.00	359.49	11,006.00	10,373.65	402.97	10,369.65	0.00	0.00	0.00	
21,400.00	90.00	359.49	11,006.00	10,473.64	402.09	10,469.65	0.00	0.00	0.00	
21,500.00	90.00	359.49	11,006.00	10,573.64	401.20	10,569.65	0.00	0.00	0.00	
21,600.00	90.00	359.49	11,006.00	10,673.64	400.31	10,669.65	0.00	0.00	0.00	
21,700.00	90.00	359.49	11,006.00	10,773.63	399.43	10,769.65	0.00	0.00	0.00	
21,800.00	90.00	359.49	11,006.00	10,873.63	398.54	10,869.65	0.00	0.00	0.00	
21,900.00	90.00	359.49	11,006.00	10,973.62	397.65	10,969.65	0.00	0.00	0.00	
22,000.00	90.00	359.49	11,006.00	11,073.62	396.77	11,069.65	0.00	0.00	0.00	
22,100.00	90.00	359.49	11,006.00	11,173.62	395.88	11,169.65	0.00	0.00	0.00	
22,200.00	90.00	359.49	11,006.00	11,273.61	395.00	11,269.65	0.00	0.00	0.00	
22,300.00	90.00	359.49	11,006.00	11,373.61	394.11	11,369.65	0.00	0.00	0.00	
22,400.00	90.00	359.49	11,006.00	11,473.60	393.22	11,469.65	0.00	0.00	0.00	
22,506.36	90.00	359.49	11,006.00	11,579.96	392.28	11,576.01	0.00	0.00	0.00	
TD: 22506.36' MD/11576.01' VS/11006.00' TVD - 02-PBHL(SSC-703H)										

Design Targets									
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
00-EON(SSC-703H)	0.00	0.00	4,500.00	-136.68	384.98	622,291.14	794,255.31	32.70802382	-103.51106841
- hit/miss target									
- plan misses target center by 196.14usft at 4535.31usft MD (4523.17 TVD, -71.52 N, 201.43 E)									
- Point									
02-PBHL(SSC-703H)	0.00	0.00	11,006.00	11,579.96	392.28	634,007.78	794,262.61	32.74022572	-103.51074904
- plan hits target center									
- Point									
01-T98(SSC-703H)	0.00	0.00	11,006.00	-86.53	495.43	622,341.29	794,365.76	32.70815929	-103.51070809
- plan misses target center by 218.79usft at 10945.14usft MD (10864.94 TVD, 58.02 N, 411.30 E)									
- Point									



Planning Report

Database:	TZ USA 17.2	Local Co-ordinate Reference:	Well (B01) Satellite State Com 703H - Slot (B01) SSC 703H
Company:	Franklin Mountain Energy LLC	TVD Reference:	3962+30 @ 3992.00usft
Project:	PV_Lea County, NM(N83-NME3001)	MD Reference:	3962+30 @ 3992.00usft
Site:	Satellite_Cross Pad 3	North Reference:	Grid
Well:	(B01) Satellite State Com 703H	Survey Calculation Method:	Minimum Curvature
Wellbore:	703H		
Design:	Plan01		

Formations						
Measured Depth (usft)	Vertical Depth (usft)	Name	Lithology	Dip (°)	Dip Direction (°)	
30.00	30.00	Cenozoic Alluvium (surface)				
1,947.00	1,947.00	Rustler				
2,224.00	2,224.00	Salado				
3,262.23	3,259.00	Base Salt				
3,569.38	3,564.00	Yates				
3,918.82	3,911.00	Seven Rivers				
4,702.31	4,689.00	Queen				
6,373.87	6,351.00	Delaware Mtn Group				
7,782.89	7,760.00	Bone Spring Lime				
9,262.89	9,240.00	First Bone Spring Sand				
9,424.89	9,402.00	Second Bone Spring Carbonate				
9,544.89	9,522.00	Second Bone Spring Sand				
10,169.89	10,147.00	Third Bone Spring Carbonate				
10,260.89	10,238.00	Third Bone Spring Sand				
10,821.12	10,774.00	Wolfcamp				
11,355.93	11,006.00	HZ Target				

Plan Annotations					
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates			
		+N/-S (usft)	+E/-W (usft)	Comment	
10,455.93	10,433.04	-136.68	384.98	KOP: 10455.93' MD/-140.10' VS/10433.04' TVD	
10,696.21	10,666.34	-87.48	391.63	100FLL: 10696.21' MD/-90.96VS	
11,355.93	11,006.00	431.11	461.75	EOC: 11355.93' MD/426.98' VS/11006.00' TVD	
22,506.36	11,006.00	11,579.96	392.28	TD: 22506.36' MD/11576.01' VS/11006.00' TVD	

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 352109

CONDITIONS

Operator: Franklin Mountain Energy 3, LLC 44 Cook Street Denver, CO 80206	OGRID: 331595
	Action Number: 352109
	Action Type: [C-103] NOI Change of Plans (C-103A)

CONDITIONS

Created By	Condition	Condition Date
pkautz	ALL PREVIOUS COA'S APPLY	6/7/2024
