
Submit 1 Copy To Appropriate District Office	State of N				Form C-103
<u>District I</u> – (575) 393-6161 1625 N. French Dr., Hobbs, NM 88240	Energy, Minerals a	ına Matt	irai Resources	WELL API NO.	
	OIL CONSERV.	ATION	DIVISION	30-025-01157	
District III - (505) 334-6178	1220 South	St. Fran	ncis Dr.		e of Lease
	Santa Fe,	, NM 8	7505	STATE	X FEE
1220 S. St. Francis Dr., Santa Fe, NM 87505				6. State Oil & O	Gas Lease No.
				7. Lease Name	or Unit Agreement Name
DIFFERENT RESERVOIR. USE "APPLI				State R	
	as Well Other			8. Well Number	r 003
V 1	as well office			9. OGRID Num	iber
				12627	8
3. Address of Operator					
P.O. Box 1171, Midland, TX 79	702			Saunders; Permo	Upper Penn
4. Well Location					
Unit LetterB:	660feet from the	North	line and	!980feet from	m theEastline
Section 27	Township	14S	Range 33E	NMPM	County Lea
	11. Elevation (Show whe	ether DR	, RKB, RT, GR, etc.)	
12. Check	Appropriate Box to Ind	licate N	lature of Notice,	Report or Othe	r Data
NOTICE OF IN	NTENTION TO:		SUB	SEQUENT RE	EPORT OF:
PERFORM REMEDIAL WORK 🗌	PLUG AND ABANDON		REMEDIAL WOR	K 🗌	ALTERING CASING
TEMPORARILY ABANDON	CHANGE PLANS				P AND A XX
PULL OR ALTER CASING	MULTIPLE COMPL		CASING/CEMEN	T JOB	PNR
DOWNHOLE COMMINGLE					
OTHER:			OTHER:		
		4 NMAC	C. For Multiple Co	mpletions: Attach	wellbore diagram of
proposed completion or rec	completion.				
District - (375) 393-616 Energy, Minerals and Natural Resources Revised August 1, 291					
	SEE.	ATTA	ACHED		
			= 10.0 to 0		
	PA cor	mplete	5/26/23		
I hereby certify that the information	ahove is true and complete	to the be	est of my knowledg	e and helief	
. Hereby certify that the information	above is true and complete	to the o	ost of my knowledg	o and ochor	
SIGNATURE LACK	the Cart TITLE	4	ert.	D	ATE 5/81/23
Type or print name M. H. M	erchant E-mai	l address	nymerche po	nnoile	HONE: 492-1236
For State Use Only			<u> </u>		
APPROVED BY:	Forther TITLE	_ Co	mpliance Offic	er A D	ATE 8/21/24
Conditions of Approval (if any):					

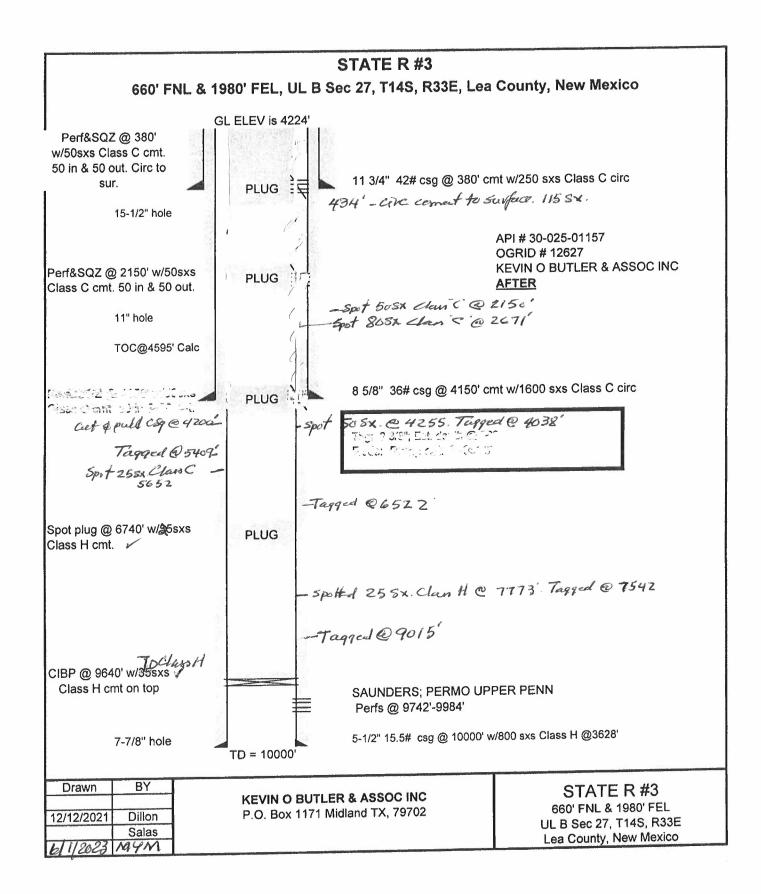

Plugging Report Kevin O. Butler & Assoc. Inc. State R #3 API 30-025-01157

5/11/2023 Removed dirt from anthill from the south side of the wellhead and set the matting board. Rigged up and SION.

5/12/2023 Rods were parted. Laid down 151 7/8" rods and 4 %" rods. Last %" rod was parted at the bottom pin. Dug out intermediate head and plumbed to the pit. Installed BOP. Worked anchor free. Pipe dragging badly. Stood back 39 stands and SION. Pipe still dragging.

5/15/2023 Stood back 124 stands and laid down 65 joints of bad tubing. Last joint had collar looking down. 313 joints of pipe recovered (9850'). Remaining rods left in the casing. Picked up overshot for ¾" rods on a 4' sub and RIH with tubing. Felt tool fall over the rods at 4012'. RIH with 1 more stand (65 total). Picked up and gained 20 points. Felt like the pump unseated and weight fell down to 15 points over string weight. POOH with 62 stands and SION for broken hydraulic line. Shut in.

5/16/2023 Finish pulling tool and laid down remaining rods and the pump. Made gauge ring run and set 5 ½" CIBP at 9640'. RIH with tubing from the derrick (7638') and SION.

Tagged CIBP at 9640' with tubing. Circulated MLF and casing tested to 500#. Spot 70 sx Class H on top of CIBP. Combined with plug at 9123'. WOC and tagged at 9015'. POOH to 7773' and spot 25 sx Class H cement. POOH and SION.

5/18/2023 Tagged cement at 7542'. POOH to 6740' and spot 25 sx Class H cement. WOC and tagged at 6522'. POOH to 5652' and spot 25 sx Class C cement. WOC and tagged at 5409'. Perforated at 4200'. Set packer and got good communication at the intermediate head. Start prepping to pull casing. SION

5/23/2023 Removed top spool and welded on 5 ½" pull stub. Cut casing at 4200'. Laid down 5 ½" casing. Reinstalled wellhead. SION

5/24/2023 RIH with tubing to 4255'. Spot 50 sx cement with CaCl. WOC and tagged at 4038'. POOH to 2671'. Shut down for bad air valve on pump truck.

5/25/2023 Spot 80 sx cement at 2671'. Combined the top of Yates and top of salt plugs. POOH to 2150' and spot 50 sx cement. POOH to 434' and circulated cement to surface. Took 115 sx to get good cement to the pit. Rigged down.

5/26/2023 Dug out wellhead and removed. Filled up 8 5/8" x 13 3/8" annulus with 15 sx cement. Installed standard marker. Removed the anchors and cleaned the pit.

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720

District II 811 S. First St., Artesia, NM 88210 Phone:(575) 748-1283 Fax:(575) 748-9720

District III 1000 Rio Brazos Rd., Aztec, NM 87410 Phone:(505) 334-6178 Fax:(505) 334-6170

1220 S. St Francis Dr., Santa Fe, NM 87505 Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico Energy, Minerals and Natural Resources Oil Conservation Division 1220 S. St Francis Dr. **Santa Fe, NM 87505**

CONDITIONS

Action 349977

CONDITIONS

Operator:	OGRID:
KEVIN O BUTLER & ASSOC INC	12627
P.O. Box 1171	Action Number:
Midland, TX 79702	349977
	Action Type:
	[C-103] Sub. Plugging (C-103P)

CONDITIONS

Created By	Condition	Condition Date
kfortner	Need C103C and marker photo to release	8/21/2024
