

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: ☐ DRILL ☐ REENTER		5. Lease Serial No.
1b. Type of Well: ☐ Oil Well ☐ Gas Well ☐ Other		6. If Indian, Allottee or Tribe Name
1c. Type of Completion: ☐ Hydraulic Fracturing ☐ Single Zone ☐ Multiple Zone		7. If Unit or CA Agreement, Name and No.
2. Name of Operator		8. Lease Name and Well No.
3a. Address		9. API Well No. 30-025-53624
3b. Phone No. (include area code)		10. Field and Pool, or Exploratory
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		11. Sec., T. R. M. or Blk. and Survey or Area
14. Distance in miles and direction from nearest town or post office*		12. County or Parish
		13. State
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No of acres in lease	17. Spacing Unit dedicated to this well
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth	20. BLM/BIA Bond No. in file
21. Elevations (Show whether DF, KDB, RT, GL, etc.)	22. Approximate date work will start*	23. Estimated duration
24. Attachments		
The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)		
1. Well plat certified by a registered surveyor. 2. A Drilling Plan. 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).		4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). 5. Operator certification. 6. Such other site specific information and/or plans as may be requested by the BLM.
25. Signature	Name (Printed/Typed)	Date
Title		
Approved by (Signature)	Name (Printed/Typed)	Date
Title		Office
Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon. Conditions of approval, if any, are attached.		
Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.		

(Continued on page 2)

*(Instructions on page 2)



Approval Date: 09/06/2024

DISTRICT I
1625 N. French Dr., Hobbs, N.M. 88240
Phone: (575) 393-6161 Fax: (575) 393-0720

DISTRICT II
811 S. First St., Artesia, N.M. 88210
Phone: (575) 748-1283 Fax: (575) 748-9720

DISTRICT III
1000 Rio Brazos Rd., Aztec, N.M. 87410
Phone: (505) 334-6178 Fax: (505) 334-6170

DISTRICT IV
1220 S. St. Francis Dr., Santa Fe, N.M. 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department

OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, N.M. 87505

Form C-102
Revised August 1, 2011

Submit one copy to appropriate
District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-025-53624	² Pool Code 37570	³ Pool Name LEA;BONE SPRING
⁴ Property Code 336288	⁵ Property Name LEA UNIT 14 II	⁶ Well Number 203H
⁷ OGRD No. 330396	⁸ Operator Name AVANT OPERATING, LLC	⁹ Elevation 3652.5

¹⁰ Surface Location


UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
I	14	20 S	34 E		2483	SOUTH	1300	EAST	LEA

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
A	II	20 S	34 E		100	NORTH	990	EAST	LEA

¹² Dedicated Acres Section 14: E/4, E/4 80 Ac. Section 11: E/2, E/2 160 Ac. Total: 240 Ac.	¹³ Joint or Infill Infill	¹⁴ Consolidation Code	¹⁵ Order No.
--	---	----------------------------------	-------------------------

NO ALLOWABLE WILL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN CONSOLIDATED OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION

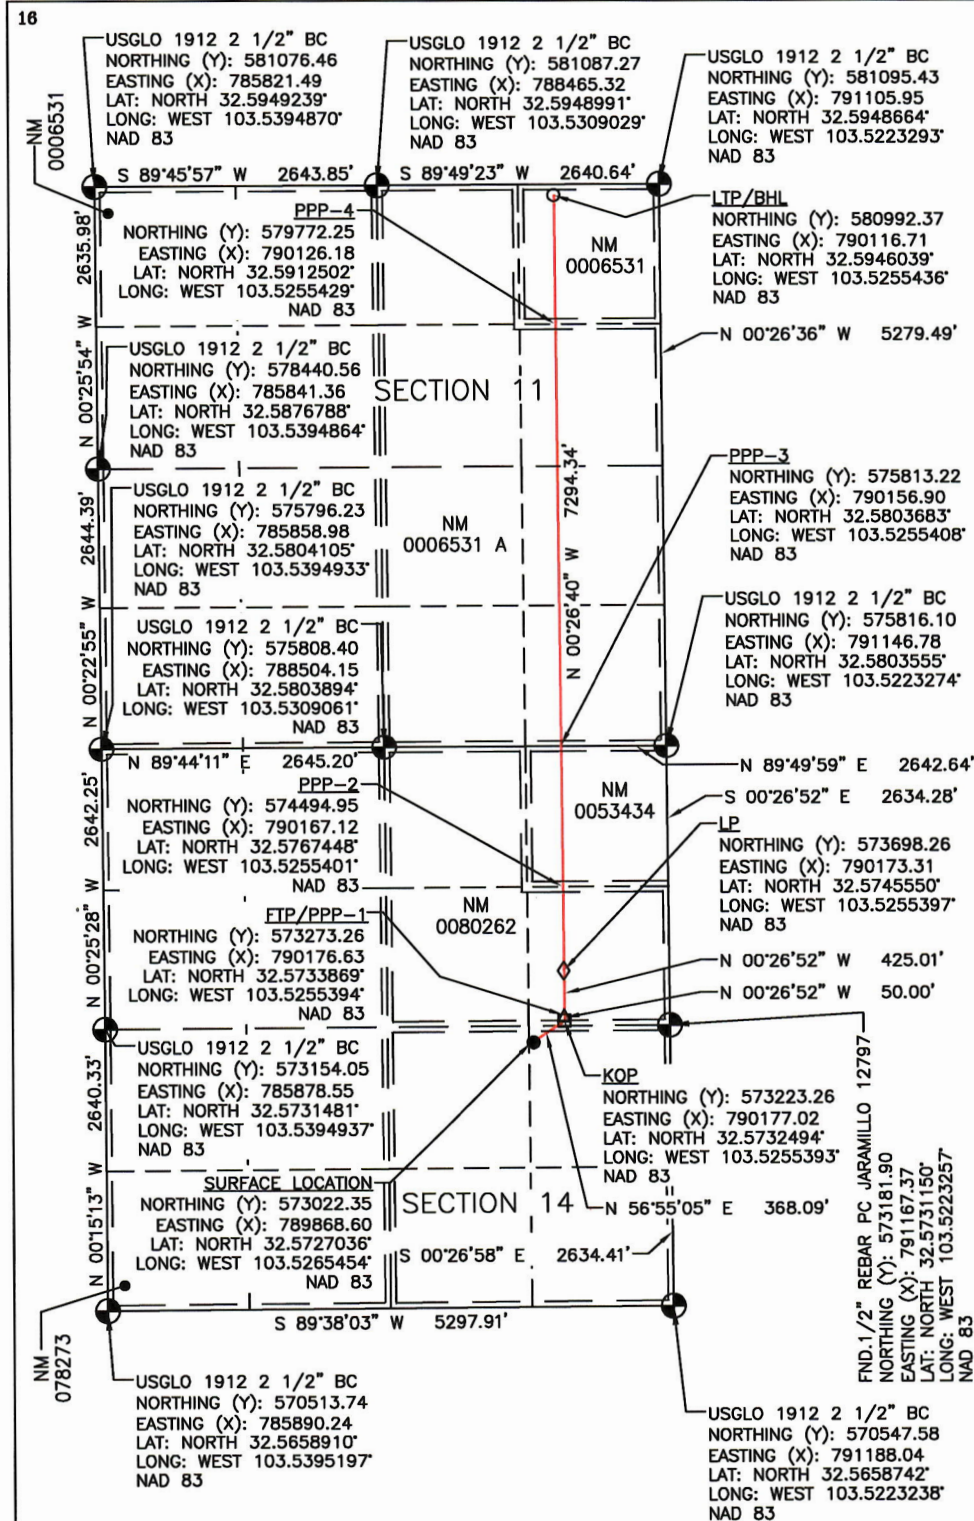

17 OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Signature: Meghan Twele Date: 2/16/24

Printed Name: Meghan Twele

E-mail Address: mtwele@outlook.com

18 SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

Date of Survey: 11/9/23

Signature and Seal of Professional Surveyor: [Signature]

Certificate Number: 14931

- LEGEND:
- = SURFACE LOCATION (SHL)
 - = KICK OFF POINT (KOP)
 - △ = FTP/PPP-1
 - ◇ = LANDING POINT (LP)
 - = LTP/BHL
 - ⊕ = FOUND MONUMENT

FOOTAGES		
SHL	2483' FSL	1300' FEL
KOP	2590' FNL	990' FEL
FTP/PPP-1	2540' FNL	990' FEL
LP	2115' FNL	990' FEL
PPP-2	1318' FNL	990' FEL
PPP-3	0' FNL	990' FEL
PPP-4	1320' FNL	990' FEL
LTP/BHL	100' FNL	990' FEL

State of New Mexico
Energy, Minerals and Natural Resources Department
Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

Submit Electronically
Via E-permitting

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description

Effective May 25, 2021

I. Operator: Avant Operating, LLC **OGRID:** 330396 **Date:** 07/11/2024

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
Lea Unit 14-11 201H		J-14-T20S-R34E	2483FSL/1340FEL	1200 BBL/D	3600 MCF/D	6000 BBL/D
Lea Unit 14-11 202H		I-14-T20S-R34E	2483FSL/1320FEL	1200 BBL/D	3600 MCF/D	6000 BBL/D
Lea Unit 14-11 203H		I-14-T20S-R34E	2483FSL/1300FEL	1200 BBL/D	3600 MCF/D	6000 BBL/D
Lea Unit 14-11 204H		I-14-T20S-R34E	2483FSL/1280FEL	1200 BBL/D	3600 MCF/D	6000 BBL/D
Lea Unit 14-11 751H		I-14-T20S-R34E	2633FSL/1320FEL	1200 BBL/D	3600 MCF/D	6000 BBL/D
Lea Unit 14-11 752H		I-14-T20S-R34E	2633FSL/1300FEL	1200 BBL/D	3600 MCF/D	6000 BBL/D

IV. Central Delivery Point Name: Lea Unit 14-11 CTB [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Lea Unit 14-11 201H		01/04/2025	02/08/2025	02/13/2025	03/07/2025	03/07/2025
Lea Unit 14-11 202H		01/04/2025	02/08/2025	02/13/2025	03/07/2025	03/07/2025
Lea Unit 14-11 203H		01/04/2025	02/08/2025	02/13/2025	03/07/2025	03/07/2025
Lea Unit 14-11 204H		01/04/2025	02/08/2025	02/13/2025	03/07/2025	03/07/2025
Lea Unit 14-11 751H		01/04/2025	02/08/2025	02/13/2025	03/07/2025	03/07/2025
Lea Unit 14-11 752H		01/04/2025	02/08/2025	02/13/2025	03/07/2025	03/07/2025

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices


1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature:	
Printed Name:	John Harper
Title:	SVP Assets and Exploration
E-mail Address:	John@avantnr.com
Date:	07/15/24
Phone:	678-988-6644

OIL CONSERVATION DIVISION
(Only applicable when submitted as a standalone form)

Approved By:
Title:
Approval Date:
Conditions of Approval:

Avant Operating, LLC Natural Gas Management Plan

- VI. Separation equipment will be sized by construction engineering staff based on stated manufacturer daily throughput capacities and anticipated daily production rates to ensure adequate capacity. Closed vent system piping, compression needs, and VRUs will be sized utilizing ProMax modelling software to ensure adequate capacity for anticipated production volumes and conditions.
- VII. Avant Operating, LLC (Avant) will take the following actions to comply with the regulations listed in 19.15.27.8:
- A. Avant will maximize the recovery of natural gas by minimizing the waste, as defined by 19.15.2 NMAC, of natural gas through venting and flaring. Avant will ensure that well(s) will be connected to a natural gas gathering system with sufficient capacity to transport natural gas.
 - B. All drilling operations will be equipped with a rig flare located at least 100' from the nearest surface hole. Rig flare will be utilized to combust any natural gas that is brought to surface during normal drilling operations. In the case of emergency venting or flaring the volumes will be estimated and reported appropriately.
 - C. During completion operations any natural gas brought to surface will be flared. Immediately following the finish of completion operations, all well flowback will be directed to permanent separation equipment. Produced natural gas from separation equipment will be sent to sales. It is not anticipated that gas will not meet pipeline standards. However, if natural gas does not meet gathering pipeline quality specifications, Avant will flare the natural gas for 60 days or until the natural gas meets the pipeline quality specifications. Avant will ensure that the flare is sized properly and is equipped with automatic igniter or continuous pilot. The gas sample will be analyzed twice per week and the gas will be routed into a gathering system as soon as pipeline specifications are met.
 - D. Avant will comply with the performance standards requirements and provisions listed in 19.15.27.8 (1) through (8). All equipment will be designed and sized to handle maximum anticipated pressures and throughputs to minimize the waste. Production storage tanks constructed after May 25, 2021, will be equipped with automatic gauging system. Flares constructed after May 25, 2021, will be equipped with automatic igniter or continuous pilot. Flares will be located at least 100' from the well and storage tanks unless otherwise approved by the division. Avant will conduct AVO inspections as described in 19.15.27.8 E (5) (a) with frequencies specified in 19.15.27.8 E (5) (b) and (c). All emergencies will be resolved as quickly and safely as feasible to minimize waste.
 - E. The volume of natural gas that is vented or flared as the result of malfunction or emergency during drilling and completions operations will be estimated. The volume of natural gas that is vented, flared, or beneficially used during production operations, will be measured, or estimated. Avant will install equipment to measure

Operator Name: AVANT OPERATING LLC

Well Name: LEA UNIT 14 11

Well Number: 203H

Testing Procedure: Before drilling out of the surface casing, the ram-type BOP and accessory equipment will be tested to 5000 (high) / 250 (low) psig and the annular preventer to 3500 (high) / 250 (low) psig by an independent service company. Test charts will always be kept on site. Surface casing will be tested to 1500 psi for 30 minutes. Before drilling out of the intermediate casing, the ram-type BOP and accessory equipment will be tested to 5000 (high) / 250 (low) psig and the annular preventer to 3500 (high) / 250 (low) psig by an independent service company. Test charts will always be kept on site. Intermediate casing will be tested to 1500 psi for 30 minutes. A solid steel body pack-off will be used after running and cementing the intermediate casing. After installation, pack-off and lower flange will be pressure tested to 5000 psi. Pipe rams will be operationally checked each 24-hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. A hydraulically operated choke will be installed prior to drilling out of the intermediate casing shoe. This pressure test will be repeated at least once every 30 days, as per Onshore Order 2. Kelly cock will always be kept in the drill string. Full opening drill pipe stabbing valve (inside BOP) with proper drill pipe connections will always be kept on the rig floor. The multi-bowl wellhead will be installed by a third-party welder while being monitored by the vendors representative. All BOP equipment will be tested using a conventional test plug - not a cup or J-packer type. Both the surface and intermediate casing strings will be tested as per Onshore Order 2 to at least 0.22 psi/ft or 1500 psi, whichever is greater.

Choke Diagram Attachment:
Lea_Unit_5M_Choke_20240116131747.pdf

BOP Diagram Attachment:
Lea_Unit_5M_BOP_Diagram_20240116131751.pdf

Section 3 - Casing

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE	17.5	13.375	NEW	API	N	0	1526	0	1526	3653	2127	1526	J-55	54.5	LT&C	1.125	1.125	DRY	1.6	DRY	1.6
2	INTERMEDIATE	12.25	9.625	NEW	API	N	0	5746	0	5741	3640	-2088	5746	J-55	40	LT&C	1.125	1.125	DRY	1.6	DRY	1.6
3	PRODUCTION	8.75	5.5	NEW	NON API	N	0	16589	0	9000	3679	-5347	16589	HCP-110	20	OTHER - GBCD	1.125	1.125	DRY	1.6	DRY	1.6

Casing Attachments

Operator Name: AVANT OPERATING LLC

Well Name: LEA UNIT 14 11

Well Number: 203H

Casing Attachments

Casing ID: 1

String

SURFACE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Lea_Unit_Casing_Assumptions_Design_20240222135502.pdf

Casing ID: 2

String

INTERMEDIATE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Lea_Unit_Casing_Design_Assumptions_20240116133330.pdf

Casing ID: 3

String

PRODUCTION

Inspection Document:

Spec Document:

Lea_Unit_5.5_Casing_Specs_20240116133643.pdf

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Lea_Unit_Casing_Assumptions_Design_20240222135443.pdf

Section 4 - Cement

Operator Name: AVANT OPERATING LLC

Well Name: LEA UNIT 14 11

Well Number: 203H

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
SURFACE	Lead		0	1526	670	1.9	12.8	1273	50	35% B_POZ & 65% Class C	6% Gel+5% SALT+0.25PPS Pol-E-Flake+0.005GPS
SURFACE	Tail		1220	1526	220	1.33	14.8	293	20	Class C	1% CaCl2+0.005GPS NoFoam V1A
INTERMEDIATE	Lead		0	5746	1050	1.9	12.8	1995	50	35% Class B Poz + 65% Class C	6% Gel+5% SALT+0.25PPS Pol-E-Flake+0.005GPS
INTERMEDIATE	Tail		4596	5746	330	1.36	14.8	449	20	Class C	5% SALT+0.005GPS NoFoam V1A
PRODUCTION	Lead		0	1658 9	760	3.38	10.7	2569	50	100% ProLite	5PPS Plexcrete STE+2% SMS+0.65% R-1300+0.2% FL-24+3PPS Gilsonite+0.005GPS NoFoam V1A
PRODUCTION	Tail		8546	1658 9	2025	1.21	14.5	2450	20	50% B_POZ & 50% Class H	5% SALT+0.05% RCKCAS-100+0.75% R-1201+0.5% FL-24+0.005GPS NoFoam V1A

Section 5 - Circulating Medium

Mud System Type: Closed

Will an air or gas system be Used? NO

Description of the equipment for the circulating system in accordance with Onshore Order #2:

Diagram of the equipment for the circulating system in accordance with Onshore Order #2:

Describe what will be on location to control well or mitigate other conditions: Sufficient mud materials (e. g., barite, bentonite, LCM) to maintain mud properties and meet minimum lost circulation and weight increase requirements will always be kept on site.

Describe the mud monitoring system utilized: An electronic pit volume totalizer (PVT) mud system will monitor pit volumes for gains or losses, flow rate, pump pressures, and stroke rate.

Circulating Medium Table

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
-----------	--------------	----------	----------------------	----------------------	---------------------	-----------------------------	----	----------------	----------------	-----------------	----------------------------

Operator Name: AVANT OPERATING LLC**Well Name:** LEA UNIT 14 11**Well Number:** 203H

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
0	1526	OTHER : Fresh Water	8.4	10.1							
1526	5746	OTHER : Brine	10	10.5							
5746	8546	OTHER : Cut Brine	9.2	9.5							
8546	9296	OTHER : Cut Brine	9.5	9.5							
9296	16589	OIL-BASED MUD	9.5	9.8							

Section 6 - Test, Logging, Coring

List of production tests including testing procedures, equipment and safety measures:

GR log will be acquired by MWD tools throughout the well.

List of open and cased hole logs run in the well:

GAMMA RAY LOG,

Coring operation description for the well:

No core or open hole or cased hole log is planned

Section 7 - Pressure

Anticipated Bottom Hole Pressure: 4320

Anticipated Surface Pressure: 2339

Anticipated Bottom Hole Temperature(F): 164

Anticipated abnormal pressures, temperatures, or potential geologic hazards? NO

Describe:

Contingency Plans geohazards description:

Contingency Plans geohazards

Hydrogen Sulfide drilling operations plan required? YES

Hydrogen sulfide drilling operations

Lea_Unit_14_11_H2S_Plan_20240222113403.pdf

Operator Name: AVANT OPERATING LLC**Well Name:** LEA UNIT 14 11**Well Number:** 203H**Section 8 - Other Information****Proposed horizontal/directional/multi-lateral plan submission:**

Lea_Unit_14_11_203H_Plan_0.1_Report_20240222140054.pdf

Lea_Unit_14_11_203H_Plan_0.1_Anti_Collision_20240516105911.pdf

Other proposed operations facets description:

All casing strings below the conductor will be pressure tested to 0.22 psi/ft x casing string length, or 1500 psi, whichever is greater, but not to exceed 70% of the minimum internal yield. If pressure declines more than 10% in 30 minutes, then corrective action will be taken.

Other proposed operations facets attachment:

Lea_Unit_Speedhead_Specs_20240116140510.pdf

Flex_Line_Certification_20240516105855.pdf

Lea_Unit_14_11_203H_WBS_Updated_Prelim_20240528114719.pdf

Lea_Unit_14_11_203H_Updated_Casing___Cement_20240528114722.pdf

Avant_Natural_Resources___3_String_Bone_Spring_Well___AES_VERT_MP_20240528114730.pdf

Other Variance attachment:

Lea_Unit_14_11_Cement_Variance_Request_20240216134851.pdf

WELL DETAILS: Lea Unit 14 11 203H


Ground Elev: 3652.0 KB: 3678.5

+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
0.0	0.0	573022.33	789868.60	32.5727036°N	103.5265454°W



PROJECT DETAILS: Lea Co., NM (NAD 83)

Geodetic System: US State Plane 1983
 Datum: North American Datum 1983
 Ellipsoid: GRS 1980
 Zone: New Mexico Eastern Zone

System Datum: Mean Sea Level

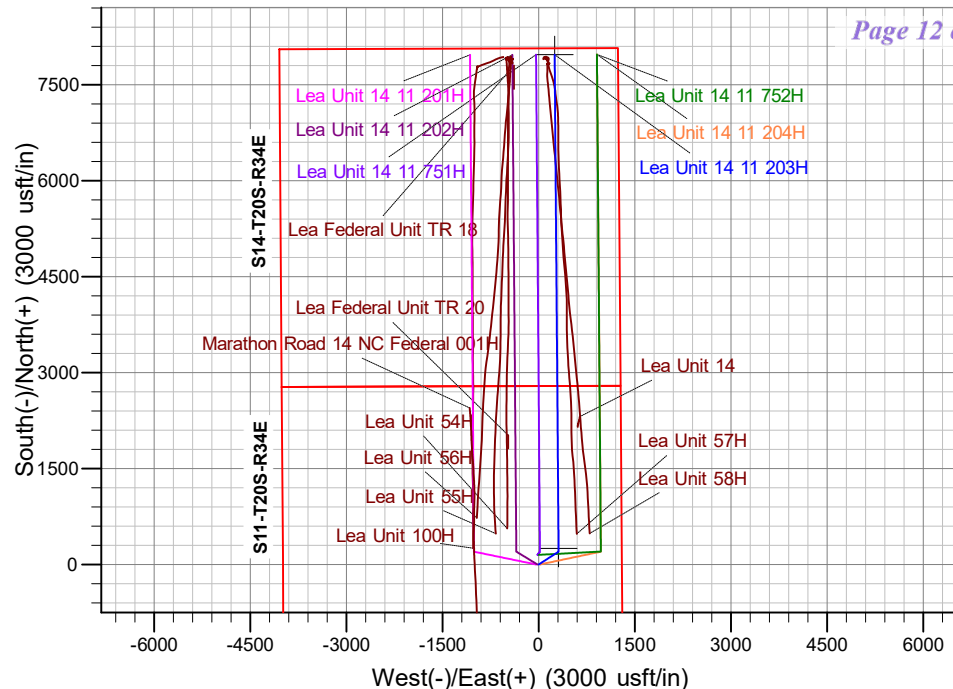**SECTION DETAILS**

Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSect	Annotation
1	0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.0	
2	5300.0	0.00	0.00	5300.0	0.0	0.0	0.00	0.00	0.0	KOP - Start Build 2.00
3	5687.3	7.75	57.17	5686.1	14.2	22.0	2.00	57.17	14.8	Start 2349.2 hold at 5687.3 MD
4	8036.5	7.75	57.17	8013.9	185.8	288.0	0.00	0.00	194.7	Start Drop -2.00
5	8423.8	0.00	0.00	8400.0	200.0	310.0	2.00	180.00	209.5	Start 122.5 hold at 8423.8 MD
6	8546.3	0.00	0.00	8522.5	200.0	310.0	0.00	0.00	209.5	KOP #2 - Start Build 12.00
7	9296.3	90.00	359.54	9000.0	677.4	306.2	12.00	359.54	686.6	LP - Start 7292.8 hold at 9296.3 MD
8	16589.2	90.00	359.54	9000.0	7970.0	248.1	0.00	0.00	7973.9	TD at 16589.2

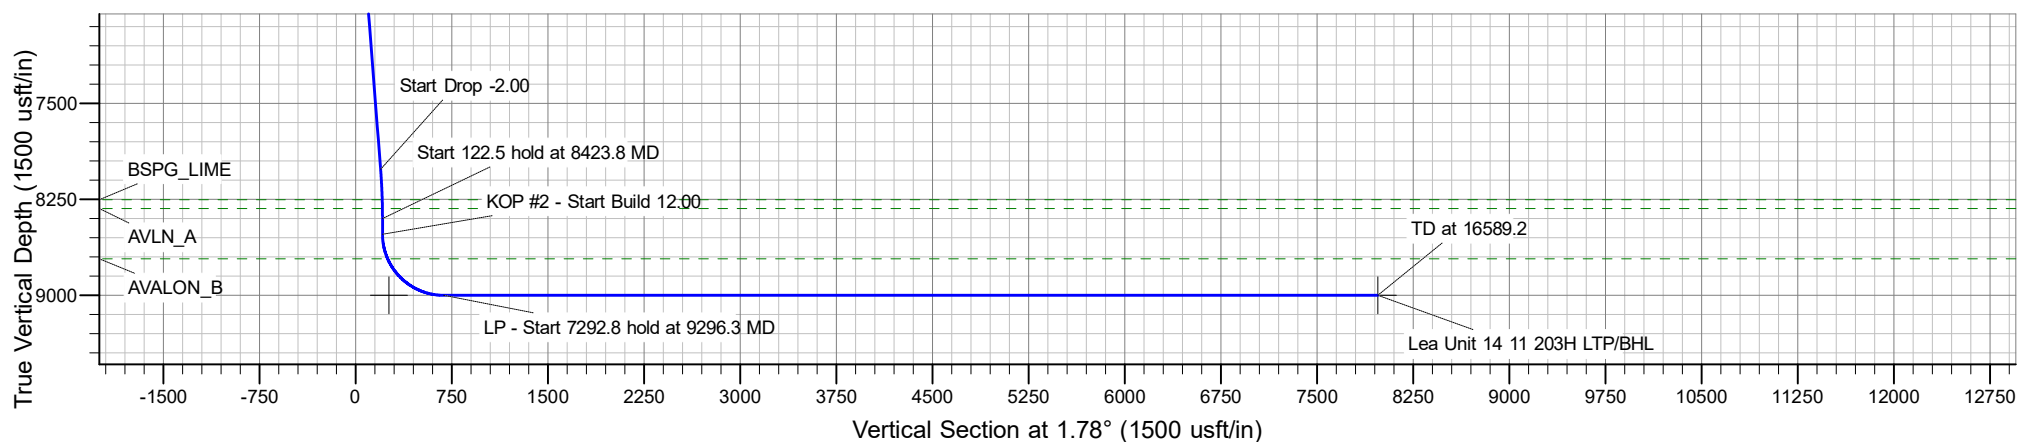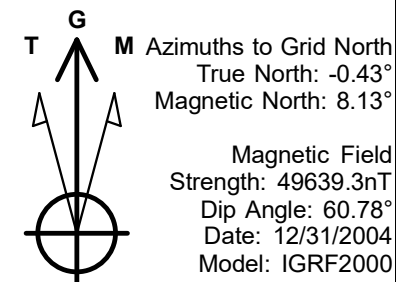



Avant Operating, LLC

Lea Co., NM (NAD 83)

Lea Unit 14 11

Lea Unit 14 11 203H

OH

Plan: Plan 0.1

Standard Planning Report

15 February, 2024





Planning Report



Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Lea Unit 14 11 203H
Company:	Avant Operating, LLC	TVD Reference:	WELL @ 3678.5usft (3678.5)
Project:	Lea Co., NM (NAD 83)	MD Reference:	WELL @ 3678.5usft (3678.5)
Site:	Lea Unit 14 11	North Reference:	Grid
Well:	Lea Unit 14 11 203H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 0.1		

Project	Lea Co., NM (NAD 83)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Lea Unit 14 11		
Site Position:		Northing:	573,022.18 usft
From:	Lat/Long	Easting:	789,828.61 usft
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "
		Latitude:	32.5727040°N
		Longitude:	103.5266752°W

Well	Lea Unit 14 11 203H		
Well Position	+N/-S	0.0 usft	Northing:
	+E/-W	0.0 usft	Easting:
Position Uncertainty	0.0 usft	Wellhead Elevation:	
Grid Convergence:	0.43 °		
		Latitude:	32.5727036°N
		Longitude:	103.5265454°W
		Ground Level:	3,652.0 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2000	12/31/2004	8.57	60.78	49,639.31566762

Design	Plan 0.1			
Audit Notes:				
Version:	Phase:	PROTOTYPE	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0	0.0	0.0	1.78

Plan Survey Tool Program	Date	2/15/2024		
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks
1	0.0	16,589.2 Plan 0.1 (OH)	B001Mb_MWD+HRGM	
			OWSG MWD + HRGM	

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
5,300.0	0.00	0.00	5,300.0	0.0	0.0	0.00	0.00	0.00	0.00	
5,687.3	7.75	57.17	5,686.1	14.2	22.0	2.00	2.00	0.00	57.17	
8,036.5	7.75	57.17	8,013.9	185.8	288.0	0.00	0.00	0.00	0.00	
8,423.8	0.00	0.00	8,400.0	200.0	310.0	2.00	-2.00	0.00	180.00	
8,546.3	0.00	0.00	8,522.5	200.0	310.0	0.00	0.00	0.00	0.00	
9,296.3	90.00	359.54	9,000.0	677.4	306.2	12.00	12.00	0.00	359.54	
16,589.2	90.00	359.54	9,000.0	7,970.0	248.1	0.00	0.00	0.00	0.00	Lea Unit 14 11 203H I



Planning Report



Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Lea Unit 14 11 203H
Company:	Avant Operating, LLC	TVD Reference:	WELL @ 3678.5usft (3678.5)
Project:	Lea Co., NM (NAD 83)	MD Reference:	WELL @ 3678.5usft (3678.5)
Site:	Lea Unit 14 11	North Reference:	Grid
Well:	Lea Unit 14 11 203H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 0.1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00
1,501.0	0.00	0.00	1,501.0	0.0	0.0	0.0	0.00	0.00	0.00
RUSTLER									
1,600.0	0.00	0.00	1,600.0	0.0	0.0	0.0	0.00	0.00	0.00
1,700.0	0.00	0.00	1,700.0	0.0	0.0	0.0	0.00	0.00	0.00
1,800.0	0.00	0.00	1,800.0	0.0	0.0	0.0	0.00	0.00	0.00
1,900.0	0.00	0.00	1,900.0	0.0	0.0	0.0	0.00	0.00	0.00
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.0	0.00	0.00	0.00
2,100.0	0.00	0.00	2,100.0	0.0	0.0	0.0	0.00	0.00	0.00
2,200.0	0.00	0.00	2,200.0	0.0	0.0	0.0	0.00	0.00	0.00
2,300.0	0.00	0.00	2,300.0	0.0	0.0	0.0	0.00	0.00	0.00
2,400.0	0.00	0.00	2,400.0	0.0	0.0	0.0	0.00	0.00	0.00
2,500.0	0.00	0.00	2,500.0	0.0	0.0	0.0	0.00	0.00	0.00
2,600.0	0.00	0.00	2,600.0	0.0	0.0	0.0	0.00	0.00	0.00
2,700.0	0.00	0.00	2,700.0	0.0	0.0	0.0	0.00	0.00	0.00
2,800.0	0.00	0.00	2,800.0	0.0	0.0	0.0	0.00	0.00	0.00
2,900.0	0.00	0.00	2,900.0	0.0	0.0	0.0	0.00	0.00	0.00
3,000.0	0.00	0.00	3,000.0	0.0	0.0	0.0	0.00	0.00	0.00
3,100.0	0.00	0.00	3,100.0	0.0	0.0	0.0	0.00	0.00	0.00
3,200.0	0.00	0.00	3,200.0	0.0	0.0	0.0	0.00	0.00	0.00
3,300.0	0.00	0.00	3,300.0	0.0	0.0	0.0	0.00	0.00	0.00
3,400.0	0.00	0.00	3,400.0	0.0	0.0	0.0	0.00	0.00	0.00
3,500.0	0.00	0.00	3,500.0	0.0	0.0	0.0	0.00	0.00	0.00
3,534.0	0.00	0.00	3,534.0	0.0	0.0	0.0	0.00	0.00	0.00
YATES									
3,600.0	0.00	0.00	3,600.0	0.0	0.0	0.0	0.00	0.00	0.00
3,700.0	0.00	0.00	3,700.0	0.0	0.0	0.0	0.00	0.00	0.00
3,800.0	0.00	0.00	3,800.0	0.0	0.0	0.0	0.00	0.00	0.00
3,900.0	0.00	0.00	3,900.0	0.0	0.0	0.0	0.00	0.00	0.00
4,000.0	0.00	0.00	4,000.0	0.0	0.0	0.0	0.00	0.00	0.00
4,100.0	0.00	0.00	4,100.0	0.0	0.0	0.0	0.00	0.00	0.00
4,200.0	0.00	0.00	4,200.0	0.0	0.0	0.0	0.00	0.00	0.00
4,300.0	0.00	0.00	4,300.0	0.0	0.0	0.0	0.00	0.00	0.00
4,400.0	0.00	0.00	4,400.0	0.0	0.0	0.0	0.00	0.00	0.00
4,500.0	0.00	0.00	4,500.0	0.0	0.0	0.0	0.00	0.00	0.00
4,600.0	0.00	0.00	4,600.0	0.0	0.0	0.0	0.00	0.00	0.00
4,700.0	0.00	0.00	4,700.0	0.0	0.0	0.0	0.00	0.00	0.00
4,800.0	0.00	0.00	4,800.0	0.0	0.0	0.0	0.00	0.00	0.00



Planning Report



Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Lea Unit 14 11 203H
Company:	Avant Operating, LLC	TVD Reference:	WELL @ 3678.5usft (3678.5)
Project:	Lea Co., NM (NAD 83)	MD Reference:	WELL @ 3678.5usft (3678.5)
Site:	Lea Unit 14 11	North Reference:	Grid
Well:	Lea Unit 14 11 203H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 0.1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
4,900.0	0.00	0.00	4,900.0	0.0	0.0	0.0	0.00	0.00	0.00
5,000.0	0.00	0.00	5,000.0	0.0	0.0	0.0	0.00	0.00	0.00
5,100.0	0.00	0.00	5,100.0	0.0	0.0	0.0	0.00	0.00	0.00
5,200.0	0.00	0.00	5,200.0	0.0	0.0	0.0	0.00	0.00	0.00
5,300.0	0.00	0.00	5,300.0	0.0	0.0	0.0	0.00	0.00	0.00
KOP - Start Build 2.00									
5,400.0	2.00	57.17	5,400.0	0.9	1.5	1.0	2.00	2.00	0.00
5,500.0	4.00	57.17	5,499.8	3.8	5.9	4.0	2.00	2.00	0.00
5,600.0	6.00	57.17	5,599.5	8.5	13.2	8.9	2.00	2.00	0.00
5,687.3	7.75	57.17	5,686.1	14.2	22.0	14.8	2.00	2.00	0.00
Start 2349.2 hold at 5687.3 MD									
5,700.0	7.75	57.17	5,698.7	15.1	23.4	15.8	0.00	0.00	0.00
5,776.0	7.75	57.17	5,774.0	20.7	32.0	21.6	0.00	0.00	0.00
CHERRY_CNYN									
5,800.0	7.75	57.17	5,797.8	22.4	34.7	23.5	0.00	0.00	0.00
5,900.0	7.75	57.17	5,896.9	29.7	46.1	31.1	0.00	0.00	0.00
6,000.0	7.75	57.17	5,996.0	37.0	57.4	38.8	0.00	0.00	0.00
6,100.0	7.75	57.17	6,095.1	44.3	68.7	46.4	0.00	0.00	0.00
6,200.0	7.75	57.17	6,194.1	51.6	80.0	54.1	0.00	0.00	0.00
6,300.0	7.75	57.17	6,293.2	58.9	91.4	61.8	0.00	0.00	0.00
6,400.0	7.75	57.17	6,392.3	66.2	102.7	69.4	0.00	0.00	0.00
6,500.0	7.75	57.17	6,491.4	73.6	114.0	77.1	0.00	0.00	0.00
6,600.0	7.75	57.17	6,590.5	80.9	125.3	84.7	0.00	0.00	0.00
6,668.1	7.75	57.17	6,658.0	85.8	133.1	89.9	0.00	0.00	0.00
BRUSHY_CANYON									
6,700.0	7.75	57.17	6,689.6	88.2	136.7	92.4	0.00	0.00	0.00
6,800.0	7.75	57.17	6,788.7	95.5	148.0	100.0	0.00	0.00	0.00
6,900.0	7.75	57.17	6,887.8	102.8	159.3	107.7	0.00	0.00	0.00
7,000.0	7.75	57.17	6,986.8	110.1	170.6	115.3	0.00	0.00	0.00
7,100.0	7.75	57.17	7,085.9	117.4	182.0	123.0	0.00	0.00	0.00
7,200.0	7.75	57.17	7,185.0	124.7	193.3	130.7	0.00	0.00	0.00
7,300.0	7.75	57.17	7,284.1	132.0	204.6	138.3	0.00	0.00	0.00
7,400.0	7.75	57.17	7,383.2	139.3	215.9	146.0	0.00	0.00	0.00
7,500.0	7.75	57.17	7,482.3	146.6	227.3	153.6	0.00	0.00	0.00
7,600.0	7.75	57.17	7,581.4	153.9	238.6	161.3	0.00	0.00	0.00
7,700.0	7.75	57.17	7,680.5	161.2	249.9	168.9	0.00	0.00	0.00
7,800.0	7.75	57.17	7,779.5	168.5	261.2	176.6	0.00	0.00	0.00
7,900.0	7.75	57.17	7,878.6	175.9	272.6	184.3	0.00	0.00	0.00
8,000.0	7.75	57.17	7,977.7	183.2	283.9	191.9	0.00	0.00	0.00
8,036.5	7.75	57.17	8,013.9	185.8	288.0	194.7	0.00	0.00	0.00
Start Drop -2.00									
8,100.0	6.48	57.17	8,076.9	190.1	294.6	199.2	2.00	-2.00	0.00
8,200.0	4.48	57.17	8,176.4	195.3	302.7	204.6	2.00	-2.00	0.00
8,276.7	2.94	57.17	8,253.0	198.0	306.8	207.4	2.00	-2.00	0.00
BSPG_LIME									
8,300.0	2.48	57.17	8,276.2	198.6	307.8	208.0	2.00	-2.00	0.00
8,345.8	1.56	57.17	8,322.0	199.4	309.1	208.9	2.00	-2.00	0.00
AVLN_A									
8,400.0	0.48	57.17	8,376.2	199.9	309.9	209.5	2.00	-2.00	0.00
8,423.8	0.00	0.00	8,400.0	200.0	310.0	209.5	2.00	-2.00	-240.27
Start 122.5 hold at 8423.8 MD									
8,500.0	0.00	0.00	8,476.2	200.0	310.0	209.5	0.00	0.00	0.00
8,546.3	0.00	0.00	8,522.5	200.0	310.0	209.5	0.00	0.00	0.00



Planning Report



Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Lea Unit 14 11 203H
Company:	Avant Operating, LLC	TVD Reference:	WELL @ 3678.5usft (3678.5)
Project:	Lea Co., NM (NAD 83)	MD Reference:	WELL @ 3678.5usft (3678.5)
Site:	Lea Unit 14 11	North Reference:	Grid
Well:	Lea Unit 14 11 203H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 0.1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
KOP #2 - Start Build 12.00									
8,600.0	6.44	359.54	8,576.1	203.0	310.0	212.6	12.00	12.00	0.00
8,700.0	18.44	359.54	8,673.6	224.5	309.8	234.0	12.00	12.00	0.00
8,743.3	23.64	359.54	8,714.0	240.1	309.7	249.6	12.00	12.00	0.00
AVALON_B									
8,800.0	30.44	359.54	8,764.4	265.8	309.5	275.3	12.00	12.00	0.00
8,900.0	42.44	359.54	8,844.7	325.1	309.0	334.6	12.00	12.00	0.00
8,947.6	48.15	359.54	8,878.2	358.9	308.7	368.4	12.00	12.00	0.00
Lea Unit 14 11 203H FTP									
9,000.0	54.44	359.54	8,911.0	399.8	308.4	409.2	12.00	12.00	0.00
9,100.0	66.44	359.54	8,960.2	486.6	307.7	496.0	12.00	12.00	0.00
9,200.0	78.44	359.54	8,990.3	581.8	307.0	591.0	12.00	12.00	0.00
9,296.3	90.00	359.54	9,000.0	677.4	306.2	686.6	12.00	12.00	0.00
LP - Start 7292.8 hold at 9296.3 MD									
9,300.0	90.00	359.54	9,000.0	681.1	306.2	690.3	0.00	0.00	0.00
9,400.0	90.00	359.54	9,000.0	781.1	305.4	790.2	0.00	0.00	0.00
9,500.0	90.00	359.54	9,000.0	881.1	304.6	890.2	0.00	0.00	0.00
9,600.0	90.00	359.54	9,000.0	981.1	303.8	990.1	0.00	0.00	0.00
9,700.0	90.00	359.54	9,000.0	1,081.1	303.0	1,090.0	0.00	0.00	0.00
9,800.0	90.00	359.54	9,000.0	1,181.1	302.2	1,189.9	0.00	0.00	0.00
9,900.0	90.00	359.54	9,000.0	1,281.1	301.4	1,289.9	0.00	0.00	0.00
10,000.0	90.00	359.54	9,000.0	1,381.1	300.6	1,389.8	0.00	0.00	0.00
10,100.0	90.00	359.54	9,000.0	1,481.1	299.8	1,489.7	0.00	0.00	0.00
10,200.0	90.00	359.54	9,000.0	1,581.1	299.0	1,589.6	0.00	0.00	0.00
10,300.0	90.00	359.54	9,000.0	1,681.1	298.2	1,689.6	0.00	0.00	0.00
10,400.0	90.00	359.54	9,000.0	1,781.1	297.4	1,789.5	0.00	0.00	0.00
10,500.0	90.00	359.54	9,000.0	1,881.1	296.6	1,889.4	0.00	0.00	0.00
10,600.0	90.00	359.54	9,000.0	1,981.1	295.8	1,989.3	0.00	0.00	0.00
10,700.0	90.00	359.54	9,000.0	2,081.1	295.0	2,089.2	0.00	0.00	0.00
10,800.0	90.00	359.54	9,000.0	2,181.1	294.2	2,189.2	0.00	0.00	0.00
10,900.0	90.00	359.54	9,000.0	2,281.1	293.4	2,289.1	0.00	0.00	0.00
11,000.0	90.00	359.54	9,000.0	2,381.1	292.6	2,389.0	0.00	0.00	0.00
11,100.0	90.00	359.54	9,000.0	2,481.1	291.8	2,488.9	0.00	0.00	0.00
11,200.0	90.00	359.54	9,000.0	2,581.1	291.0	2,588.9	0.00	0.00	0.00
11,300.0	90.00	359.54	9,000.0	2,681.1	290.2	2,688.8	0.00	0.00	0.00
11,400.0	90.00	359.54	9,000.0	2,781.1	289.4	2,788.7	0.00	0.00	0.00
11,500.0	90.00	359.54	9,000.0	2,881.1	288.6	2,888.6	0.00	0.00	0.00
11,600.0	90.00	359.54	9,000.0	2,981.0	287.8	2,988.6	0.00	0.00	0.00
11,700.0	90.00	359.54	9,000.0	3,081.0	287.1	3,088.5	0.00	0.00	0.00
11,800.0	90.00	359.54	9,000.0	3,181.0	286.3	3,188.4	0.00	0.00	0.00
11,900.0	90.00	359.54	9,000.0	3,281.0	285.5	3,288.3	0.00	0.00	0.00
12,000.0	90.00	359.54	9,000.0	3,381.0	284.7	3,388.3	0.00	0.00	0.00
12,100.0	90.00	359.54	9,000.0	3,481.0	283.9	3,488.2	0.00	0.00	0.00
12,200.0	90.00	359.54	9,000.0	3,581.0	283.1	3,588.1	0.00	0.00	0.00
12,300.0	90.00	359.54	9,000.0	3,681.0	282.3	3,688.0	0.00	0.00	0.00
12,400.0	90.00	359.54	9,000.0	3,781.0	281.5	3,787.9	0.00	0.00	0.00
12,500.0	90.00	359.54	9,000.0	3,881.0	280.7	3,887.9	0.00	0.00	0.00
12,600.0	90.00	359.54	9,000.0	3,981.0	279.9	3,987.8	0.00	0.00	0.00
12,700.0	90.00	359.54	9,000.0	4,081.0	279.1	4,087.7	0.00	0.00	0.00
12,800.0	90.00	359.54	9,000.0	4,181.0	278.3	4,187.6	0.00	0.00	0.00
12,900.0	90.00	359.54	9,000.0	4,281.0	277.5	4,287.6	0.00	0.00	0.00
13,000.0	90.00	359.54	9,000.0	4,381.0	276.7	4,387.5	0.00	0.00	0.00
13,100.0	90.00	359.54	9,000.0	4,481.0	275.9	4,487.4	0.00	0.00	0.00



Planning Report



Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Lea Unit 14 11 203H
Company:	Avant Operating, LLC	TVD Reference:	WELL @ 3678.5usft (3678.5)
Project:	Lea Co., NM (NAD 83)	MD Reference:	WELL @ 3678.5usft (3678.5)
Site:	Lea Unit 14 11	North Reference:	Grid
Well:	Lea Unit 14 11 203H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 0.1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
13,200.0	90.00	359.54	9,000.0	4,581.0	275.1	4,587.3	0.00	0.00	0.00	
13,300.0	90.00	359.54	9,000.0	4,681.0	274.3	4,687.3	0.00	0.00	0.00	
13,400.0	90.00	359.54	9,000.0	4,781.0	273.5	4,787.2	0.00	0.00	0.00	
13,500.0	90.00	359.54	9,000.0	4,881.0	272.7	4,887.1	0.00	0.00	0.00	
13,600.0	90.00	359.54	9,000.0	4,981.0	271.9	4,987.0	0.00	0.00	0.00	
13,700.0	90.00	359.54	9,000.0	5,081.0	271.1	5,087.0	0.00	0.00	0.00	
13,800.0	90.00	359.54	9,000.0	5,181.0	270.3	5,186.9	0.00	0.00	0.00	
13,900.0	90.00	359.54	9,000.0	5,281.0	269.5	5,286.8	0.00	0.00	0.00	
14,000.0	90.00	359.54	9,000.0	5,381.0	268.7	5,386.7	0.00	0.00	0.00	
14,100.0	90.00	359.54	9,000.0	5,481.0	267.9	5,486.7	0.00	0.00	0.00	
14,200.0	90.00	359.54	9,000.0	5,581.0	267.1	5,586.6	0.00	0.00	0.00	
14,300.0	90.00	359.54	9,000.0	5,681.0	266.3	5,686.5	0.00	0.00	0.00	
14,400.0	90.00	359.54	9,000.0	5,781.0	265.5	5,786.4	0.00	0.00	0.00	
14,500.0	90.00	359.54	9,000.0	5,881.0	264.8	5,886.3	0.00	0.00	0.00	
14,600.0	90.00	359.54	9,000.0	5,981.0	264.0	5,986.3	0.00	0.00	0.00	
14,700.0	90.00	359.54	9,000.0	6,080.9	263.2	6,086.2	0.00	0.00	0.00	
14,800.0	90.00	359.54	9,000.0	6,180.9	262.4	6,186.1	0.00	0.00	0.00	
14,900.0	90.00	359.54	9,000.0	6,280.9	261.6	6,286.0	0.00	0.00	0.00	
15,000.0	90.00	359.54	9,000.0	6,380.9	260.8	6,386.0	0.00	0.00	0.00	
15,100.0	90.00	359.54	9,000.0	6,480.9	260.0	6,485.9	0.00	0.00	0.00	
15,200.0	90.00	359.54	9,000.0	6,580.9	259.2	6,585.8	0.00	0.00	0.00	
15,300.0	90.00	359.54	9,000.0	6,680.9	258.4	6,685.7	0.00	0.00	0.00	
15,400.0	90.00	359.54	9,000.0	6,780.9	257.6	6,785.7	0.00	0.00	0.00	
15,500.0	90.00	359.54	9,000.0	6,880.9	256.8	6,885.6	0.00	0.00	0.00	
15,600.0	90.00	359.54	9,000.0	6,980.9	256.0	6,985.5	0.00	0.00	0.00	
15,700.0	90.00	359.54	9,000.0	7,080.9	255.2	7,085.4	0.00	0.00	0.00	
15,800.0	90.00	359.54	9,000.0	7,180.9	254.4	7,185.4	0.00	0.00	0.00	
15,900.0	90.00	359.54	9,000.0	7,280.9	253.6	7,285.3	0.00	0.00	0.00	
16,000.0	90.00	359.54	9,000.0	7,380.9	252.8	7,385.2	0.00	0.00	0.00	
16,100.0	90.00	359.54	9,000.0	7,480.9	252.0	7,485.1	0.00	0.00	0.00	
16,200.0	90.00	359.54	9,000.0	7,580.9	251.2	7,585.0	0.00	0.00	0.00	
16,300.0	90.00	359.54	9,000.0	7,680.9	250.4	7,685.0	0.00	0.00	0.00	
16,400.0	90.00	359.54	9,000.0	7,780.9	249.6	7,784.9	0.00	0.00	0.00	
16,500.0	90.00	359.54	9,000.0	7,880.9	248.8	7,884.8	0.00	0.00	0.00	
16,589.2	90.00	359.54	9,000.0	7,970.0	248.1	7,973.9	0.00	0.00	0.00	
TD at 16589.2 - Lea Unit 14 11 203H LTP/BHL										

Design Targets										
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude		Longitude
- hit/miss target										
- Shape										
Lea Unit 14 11 203H FTI	0.00	0.01	9,000.0	250.9	308.0	573,273.28	790,176.61	32.5733869°N		103.5255394°W
- plan misses target center by 162.8usft at 8947.6usft MD (8878.2 TVD, 358.9 N, 308.7 E)										
- Point										
Lea Unit 14 11 203H LTF	0.00	0.00	9,000.0	7,970.0	248.1	580,992.38	790,116.71	32.5946039°N		103.5255436°W
- plan hits target center										
- Point										



Planning Report



Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Lea Unit 14 11 203H
Company:	Avant Operating, LLC	TVD Reference:	WELL @ 3678.5usft (3678.5)
Project:	Lea Co., NM (NAD 83)	MD Reference:	WELL @ 3678.5usft (3678.5)
Site:	Lea Unit 14 11	North Reference:	Grid
Well:	Lea Unit 14 11 203H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 0.1		

Casing Points				
Measured Depth (usft)	Vertical Depth (usft)	Name	Casing Diameter (")	Hole Diameter (")
9,296.3	9,000.0	LP	5-1/2	6

Measured Depth (usft)	Vertical Depth (usft)	Name	Lithology	Dip (°)	Dip Direction (°)
1,501.0	1,501.0	RUSTLER			
3,534.0	3,534.0	YATES			
5,776.0	5,774.0	CHERRY_CNYN			
6,668.1	6,658.0	BRUSHY_CANYON			
8,276.7	8,253.0	BSPG_LIME			
8,345.8	8,322.0	AVLN_A			
8,743.3	8,714.0	AVALON_B			

Plan Annotations				
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
5,300.0	5,300.0	0.0	0.0	KOP - Start Build 2.00
5,687.3	5,686.1	14.2	22.0	Start 2349.2 hold at 5687.3 MD
8,036.5	8,013.9	185.8	288.0	Start Drop -2.00
8,423.8	8,400.0	200.0	310.0	Start 122.5 hold at 8423.8 MD
8,546.3	8,522.5	200.0	310.0	KOP #2 - Start Build 12.00
9,296.3	9,000.0	677.4	306.2	LP - Start 7292.8 hold at 9296.3 MD
16,589.2	9,000.0	7,970.0	248.1	TD at 16589.2



Avant Operating, LLC

Lea Co., NM (NAD 83)

Lea Unit 14 11

Lea Unit 14 11 203H

OH

Plan 0.1

Anticollision Summary Report

15 February, 2024





Anticollision Summary Report



Company:	Avant Operating, LLC	Local Co-ordinate Reference:	Well Lea Unit 14 11 203H
Project:	Lea Co., NM (NAD 83)	TVD Reference:	WELL @ 3678.5usft (3678.5)
Reference Site:	Lea Unit 14 11	MD Reference:	WELL @ 3678.5usft (3678.5)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Lea Unit 14 11 203H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.16 Single User Db
Reference Design:	Plan 0.1	Offset TVD Reference:	Offset Datum

Reference	Plan 0.1
Filter type:	NO GLOBAL FILTER: Using user defined selection & filtering criteria
Interpolation Method:	Stations
Depth Range:	Unlimited
Results Limited by:	Maximum centre distance of 1,000.0usft
Warning Levels Evaluated at:	2.00 Sigma
Error Model:	ISCWSA
Scan Method:	Closest Approach 3D
Error Surface:	Pedal Curve
Casing Method:	Not applied

Survey Tool Program	Date	2/15/2024
From (usft)	To (usft)	Survey (Wellbore)
0.0	16,589.2	Plan 0.1 (OH)
		Tool Name
		B001Mb_MWD+HRGM
		Description
		OWSG MWD + HRGM

Summary						
Site Name	Reference Measured Depth (usft)	Offset Measured Depth (usft)	Distance Between Centres (usft)	Distance Between Ellipses (usft)	Separation Factor	Warning
Offset Well - Wellbore - Design						
Lea Unit 14 11						
Lea Federal Unit TR 18 - OH - OH	16,228.3	8,988.7	637.7	317.0	1.989	CC, ES, SF
Lea Federal Unit TR 20 - OH - OH	10,585.1	8,972.0	774.1	541.0	3.321	CC, ES
Lea Federal Unit TR 20 - OH - OH	10,600.0	8,972.2	774.3	541.1	3.320	SF
Lea Unit 100H - OH - OH						Out of range
Lea Unit 14 - OH - P&A	10,907.0	8,971.0	344.4	98.6	1.401	Level 3, CC, ES, SF
Lea Unit 14 11 201H - OH - Plan 0.1	2,000.0	2,000.0	40.0	26.1	2.880	CC, ES
Lea Unit 14 11 201H - OH - Plan 0.1	2,100.0	2,098.6	41.7	27.1	2.858	SF
Lea Unit 14 11 202H - OH - Plan 0.1	5,300.0	5,300.0	20.0	-17.6	0.533	Level 1, CC, ES, SF
Lea Unit 14 11 204H - OH - Plan 0.1	2,000.0	2,000.0	20.0	6.1	1.442	Level 3, CC, ES, SF
Lea Unit 14 11 751H - OH - Plan 0.1	5,987.6	5,984.2	139.9	97.5	3.300	CC
Lea Unit 14 11 751H - OH - Plan 0.1	6,100.0	6,095.7	140.6	97.4	3.255	ES
Lea Unit 14 11 751H - OH - Plan 0.1	6,200.0	6,194.9	142.4	98.5	3.243	SF
Lea Unit 14 11 752H - OH - Plan 0.1	6,642.7	6,637.5	102.3	55.6	2.189	CC
Lea Unit 14 11 752H - OH - Plan 0.1	6,700.0	6,694.5	102.4	55.3	2.175	ES
Lea Unit 14 11 752H - OH - Plan 0.1	6,800.0	6,794.1	103.4	55.6	2.166	SF
Lea Unit 54H - OH - OH	16,542.5	9,004.7	755.7	625.6	5.811	CC, ES, SF
Lea Unit 55H - OH - OH	16,531.5	9,011.1	712.9	531.7	3.934	CC, ES, SF
Lea Unit 56H - OH - OH	16,553.3	9,017.0	681.1	545.4	5.020	CC, ES, SF
Lea Unit 57H - OH - OH	16,543.5	9,009.1	103.5	-27.6	0.789	Level 1, CC, ES, SF
Lea Unit 58H - OH - OH	16,446.4	9,007.4	114.7	-20.8	0.846	Level 1, CC, ES, SF
Marathon Road 14 Federal 001 - OH - OH						Out of range
Marathon Road 14 NC Federal 001H - OH - OH						Out of range

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Anticollision Summary Report



Company:	Avant Operating, LLC	Local Co-ordinate Reference:	Well Lea Unit 14 11 203H
Project:	Lea Co., NM (NAD 83)	TVD Reference:	WELL @ 3678.5usft (3678.5)
Reference Site:	Lea Unit 14 11	MD Reference:	WELL @ 3678.5usft (3678.5)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Lea Unit 14 11 203H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.16 Single User Db
Reference Design:	Plan 0.1	Offset TVD Reference:	Offset Datum

Reference Depths are relative to WELL @ 3678.5usft (3678.5)


Offset Depths are relative to Offset Datum

Central Meridian is 104.333333°W

Coordinates are relative to: Lea Unit 14 11 203H

Coordinate System is US State Plane 1983, New Mexico Eastern Zone

Grid Convergence at Surface is: 0.43°

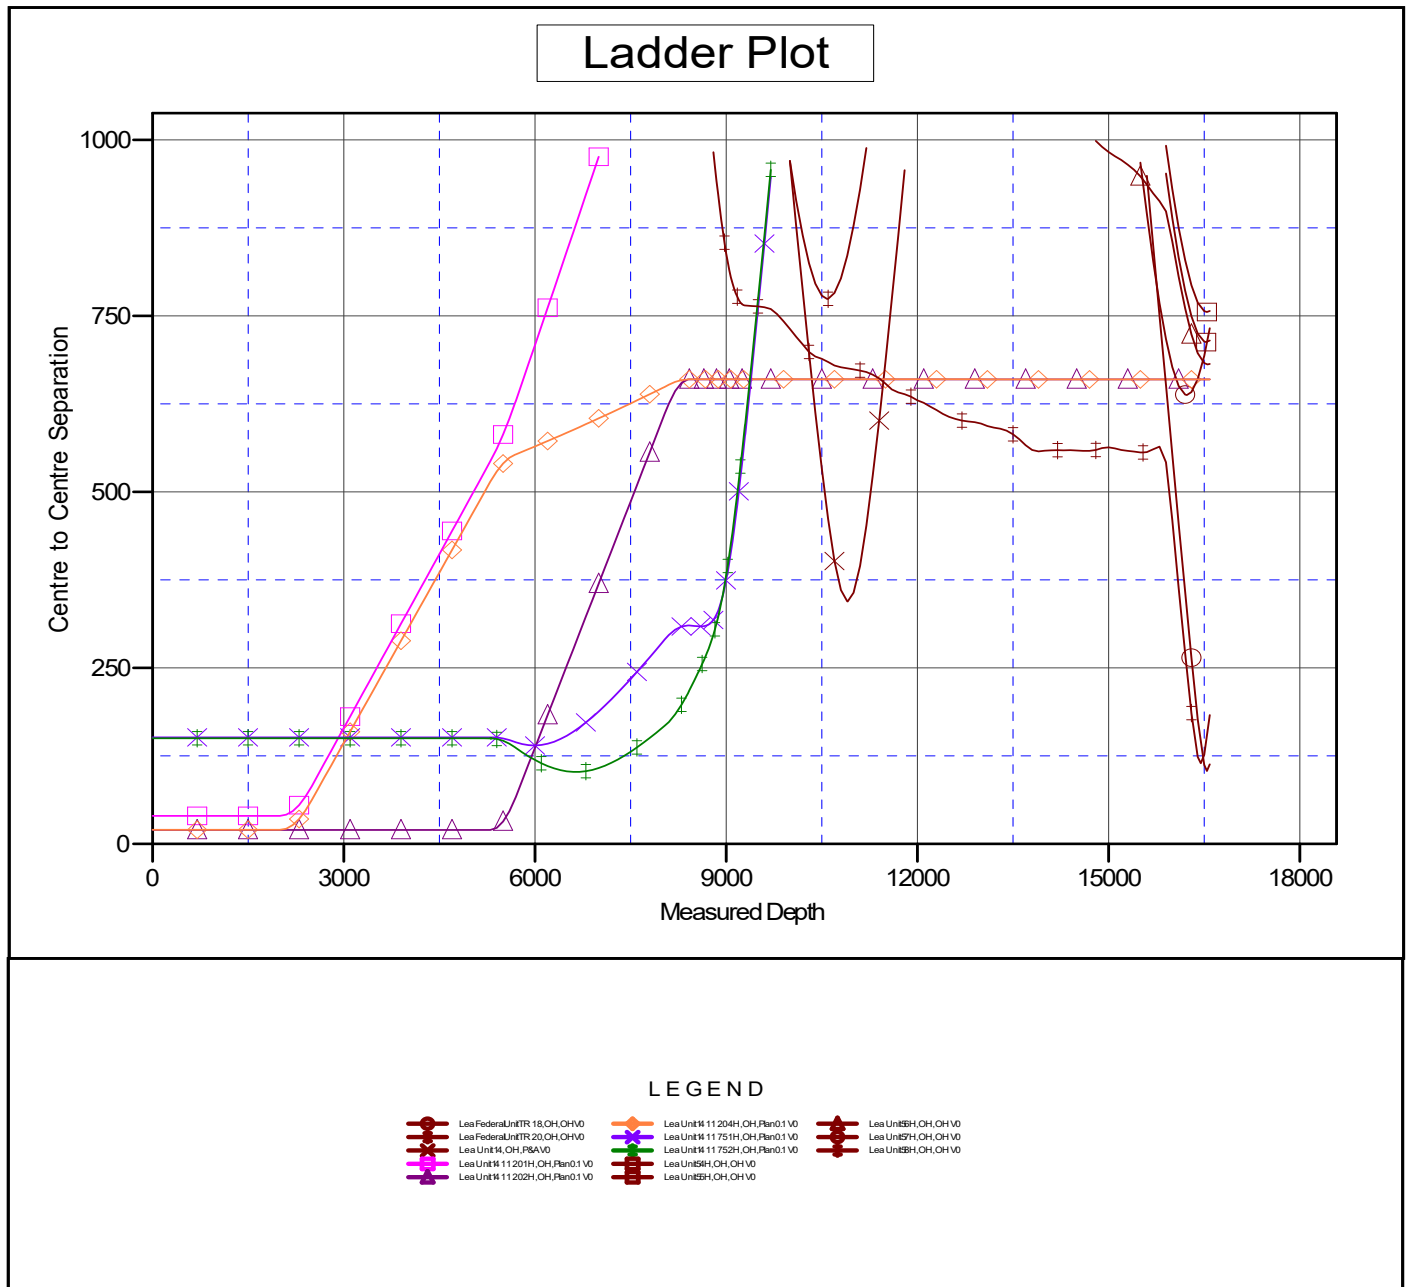

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Anticollision Summary Report



Company:	Avant Operating, LLC	Local Co-ordinate Reference:	Well Lea Unit 14 11 203H
Project:	Lea Co., NM (NAD 83)	TVD Reference:	WELL @ 3678.5usft (3678.5)
Reference Site:	Lea Unit 14 11	MD Reference:	WELL @ 3678.5usft (3678.5)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Lea Unit 14 11 203H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.16 Single User Db
Reference Design:	Plan 0.1	Offset TVD Reference:	Offset Datum

Reference Depths are relative to WELL @ 3678.5usft (3678.5)

Offset Depths are relative to Offset Datum


Central Meridian is 104.333333°W

Coordinates are relative to: Lea Unit 14 11 203H

Coordinate System is US State Plane 1983, New Mexico Eastern Zone

Grid Convergence at Surface is: 0.43°

Separation Factor Plot

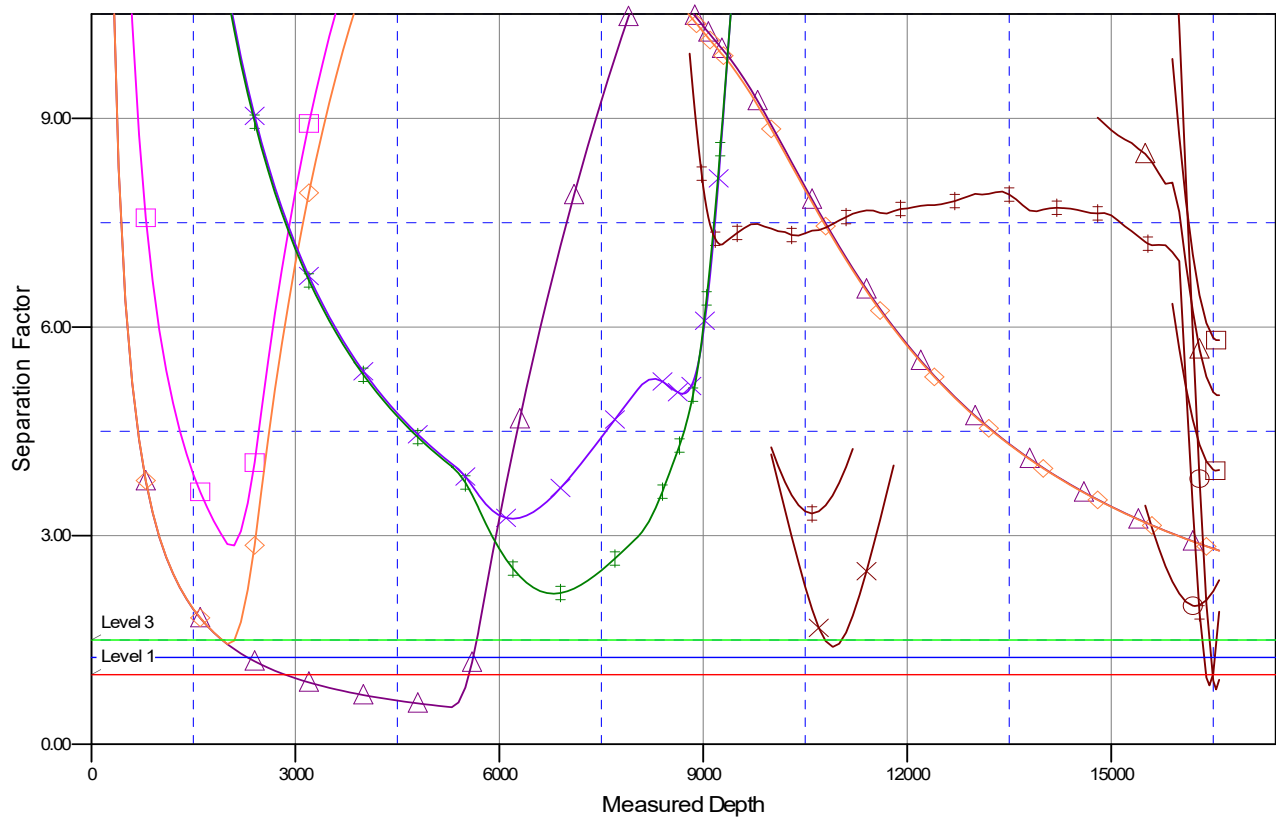

LEGEND

Lea FederalUnitR 18,OH,OHV0	Lea UnitW 11 204H,OH,Plan0.1V0	Lea UnitBH,OH,OHV0
Lea FederalUnitR 20,OH,OHV0	Lea UnitW 11 751H,OH,Plan0.1V0	Lea UnitBH,OH,OHV0
Lea UnitW,OH,PSAV0	Lea UnitW 11 752H,OH,Plan0.1V0	Lea UnitBH,OH,OHV0
Lea UnitW 11 201H,OH,Plan0.1V0	Lea UnitBH,OH,OHV0	
Lea UnitW 11 202H,OH,Plan0.1V0	Lea UnitBH,OH,OHV0	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

**PECOS DISTRICT
DRILLING CONDITIONS OF APPROVAL**

OPERATOR'S NAME:	Avant Operating LLC
LEASE NO.:	NMNM080262
LOCATION:	Section 14, T.20 S., R.34 E., NMPM
COUNTY:	Lea County, New Mexico ▼

WELL NAME & NO.:	Lea Unit 14 11 201H
BOTTOM HOLE FOOTAGE	100'/N & 2310'/E
ATS/API ID:	ATS-24-996
APD ID:	10400097165
Sundry ID:	N/a
Date APD Submitted:	N/a

WELL NAME & NO.:	Lea Unit 14 11 202H
BOTTOM HOLE FOOTAGE	100'/N & 1650'/E
ATS/API ID:	ATS-24-1010
APD ID:	10400097272
Sundry ID:	N/a
Date APD Submitted:	N/a

WELL NAME & NO.:	Lea Unit 14 11 203H
BOTTOM HOLE FOOTAGE	100'/N & 990'/E
ATS/API ID:	ATS-24-1009
APD ID:	10400097275
Sundry ID:	N/a
Date APD Submitted:	N/a

COA

H2S	Yes		
Potash	None		
Cave/Karst Potential	Low		
Cave/Karst Potential	☐ Critical		
Variance	☒ None	☒ Flex Hose	☒ Other
Wellhead	Conventional and Multibowl		
Other	☐ 4 String	Capitan Reef Int 1	☐ WIPP
Other	Pilot Hole None	☐ Open Annulus	
Cementing	Contingency Squeeze None	Echo-Meter None	Primary Cement Squeeze None
Special Requirements	☐ Water Disposal/Injection	☐ COM	☒ Unit
Special Requirements	☐ Batch Sundry	Waste Prevention None	
Special Requirements Variance	☐ Break Testing	☐ Offline Cementing	☐ Casing Clearance

A. HYDROGEN SULFIDE

A Hydrogen Sulfide (H₂S) Drilling Plan shall be activated 500 feet prior to drilling into the **Morrow** formation. As a result, the Hydrogen Sulfide area must meet **43 CFR part 3170 Subpart 3176** requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, please provide measured values and formations to the BLM.

B. CASING

1. The **13-3/8** inch surface casing shall be set at approximately **1680 feet** (a minimum of **25 feet (Lea County)** into the Rustler Anhydrite and above the salt when present, and below usable fresh water) and cemented to the surface. The surface hole shall be **17 1/2** inch in diameter.

- a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
- b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
- c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
- d. If cement falls back, remedial cementing will be done prior to drilling out that string.

2. The minimum required fill of cement behind the **9-5/8** inch intermediate casing is:

- Cement to surface. If cement does not circulate see B.1.a, c-d above.
Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst, potash or capitan reef.

❖ **Special Capitan Reef requirements.** If lost circulation (50% or greater) occurs below the Base of the Salt, the operator shall do the following:

- Switch to fresh water mud to protect the Capitan Reef and use fresh water mud until setting the intermediate casing. The appropriate BLM office is to be notified for a PET to witness the switch to fresh water.
- Daily drilling reports from the Base of the Salt to the setting of the intermediate casing are to be submitted to the BLM CFO engineering staff via e-mail by 0800 hours each morning. Any lost circulation encountered is to be recorded on

these drilling reports. The daily drilling report should show mud volume per shift/tour. Failure to submit these reports will result in an Incidence of Non-Compliance being issued for failure to comply with the Conditions of Approval. If not already planned, the operator shall run a caliper survey for the intermediate well bore and submit to the appropriate BLM office.

- ❖ In Capitan Reef Areas if cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface.

3. The minimum required fill of cement behind the 5-1/2 inch production casing is:

- Cement should tie-back at least **50 feet** on top of Capitan Reef top **or 200** into the previous casing, whichever is greater. Operator shall provide method of verification.

Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst, potash or capitan reef.

C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'

2.

Option 1:

- a. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **3000 (3M)** psi.
- b. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the 9-5/8 inch intermediate casing shoe shall be **5000 (5M)** psi.

Option 2:

Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the 13-3/8 inch surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.

- a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
- b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.

- c. Manufacturer representative shall install the test plug for the initial BOP test.
- d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
- e. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172.6(b)(9) must be followed.

D. SPECIAL REQUIREMENT (S)

Unit Wells

The well sign for a unit well shall include the unit number in addition to the surface and bottom hole lease numbers. This also applies to participating area numbers. If a participating area has not been established, the operator can use the general unit designation, but will replace the unit number with the participating area number when the sign is replaced.

Commercial Well Determination

A commercial well determination shall be submitted after production has been established for at least six months.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ **Lea County**

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240,
(575) 689-5981

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - Notify the BLM when moving in and removing the Spudder Rig.
 - Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - BOP/BOPE test to be conducted per **43 CFR part 3170 Subpart 3172** as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.

2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends of both lead and tail cement, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in **43 CFR part 3170 Subpart 3172 and API STD 53 Sec. 5.3**.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke

manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.

3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172.6(b)(9) must be followed.
 - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead cement), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the cement plug. The BOPE test can be

initiated after bumping the cement plug with the casing valve open. (only applies to single stage cement jobs, prior to the cement setting up.)

- c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer and can be initiated immediately with the casing valve open. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to **43 CFR part 3170 Subpart 3172** with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for 8 hours or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
- d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- e. The results of the test shall be reported to the appropriate BLM office.
- f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per **43 CFR part 3170 Subpart 3172**.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and

disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

Long Vo (LVO) 6/5/2024

Hydrogen Sulfide Plan Summary

- A. All personnel shall receive proper H₂S training in accordance with Onshore Order III.C.3.a.
- B. Briefing Area: two perpendicular areas will be designated by signs and readily accessible.
- C. Required Emergency Equipment:

- Well control equipment
 - a. Flare line 150' from wellhead to be ignited by flare gun.
 - b. Choke manifold with a remotely operated choke.
 - c. Mud/gas separator

- Protective equipment for essential personnel.

Breathing apparatus:

- a. Rescue Packs (SCBA) — 1 unit shall be placed at each breathing area, 2 shall be stored in the safety trailer.
- b. Work/Escapes packs — 4 packs shall be stored on the rig floor with sufficient air hose not to restrict work activity.
- c. Emergency Escape Packs — 4 packs shall be stored in the doghouse for emergency evacuation.

Auxiliary Rescue Equipment:

- a. Stretcher
- b. Two OSHA full body harness
- c. 100 ft 5/8 inch OSHA approved rope
- d. 1-20# class ABC fire extinguisher

- H₂S detection and monitoring equipment:

The stationary detector with three sensors will be placed in the upper dog house if equipped, set to visually alarm @ 10 ppm and audible @ 14 ppm. Calibrate a minimum of every 30 days or as needed. The sensors will be placed in the following places: Rig floor / Bell nipple / End of flow line or where well bore fluid is being discharged.

(Gas sample tubes will be stored in the safety trailer)

- Visual warning systems.
 - a. One color code condition sign will be placed at the entrance to the site reflecting the possible conditions at the site.
 - b. A colored condition flag will be on display, reflecting the current condition at the site at the time.
 - c. Two wind socks will be placed in strategic locations, visible from all angles.



- Mud program:
The mud program has been designed to minimize the volume of H2S circulated to surface. The operator will have the necessary mud products to minimize hazards while drilling in H2S bearing zones.
- Metallurgy:
All drill strings, casings, tubing, wellhead, blowout preventer, drilling spool, kill lines, choke manifold and lines, and valves shall be suitable for H2S service.
- Communication:
Communication will be via cell phones and land lines where available.

Company Personnel to be Notified

John Harper, Vice President of Geoscience	Office: (720) 746-5045
	Mobile: (678) 988-6644
Braden Harris, Engineer	Mobile: (406) 600-3310

Local & County Agencies

Maljamar Volunter Fire Department	911 or (575) 676-4100
Lea County Sheriff (Lovington)	911 or (575) 396-3611
Lea County Emergency Management (Lovington)	(575) 396-8602
Lea Regional Medical Center Hopital (Hobbs)	(575) 492-5000

State Agencies

NM State Police (Hobbs)	(575) 392-5588
NM Oil Conservation (Hobbs)	(575) 370-3186
NM Oil Conservation (Santa Fe)	(505) 476-3440
NM Dept. of Transportation (Roswell)	(575) 637-7201



Federal Agencies

BLM (Carlsbad)	(575) 234-5972
BLM (Hobbs)	(575) 393-3612
National Response Center	(800) 424-8802
US EPA Region 6 (Dallas)	(800) 887-6063
	(214) 665-6444

Veterinarians

Lovington Veterinary Clinic	(575) 396-7387
Hobbs Animal Clinic	(575) 392-5563
Dal Paso Animal Hospital (Hobbs)	(575) 397-2286

Residents within 2 miles

None

Air Evacuation

AeroCare (Lubbock)	(800) 627-2376
Med Flight Air Ambulance (Albuquerque)	(800) 842-4431
Lifeguard (Albuquerque)	(888) 866-7256



LEA UNIT 14 11 PAD
SECTION 14, T-20-S, R-34-E, N.M.P.M.,
LEA COUNTY, N.M.

**Before digging
call for utility
line location!**

Proposed
Pad Elevation
3652'

CENTER OF WELL PAD FOOTAGES	NAD 83
2601' FSL, 1325' FEL	LAT.=32.5730277° N LONG.=103.5286268° W

WELL FLAG	FSL	FEL
201H	2483'	1340'
202H	2483'	1320'
203H	PREVAILING WIND DIRECTION	
204H	BLOW FROM SOUTHWEST	
75		
752H	2633'	1300'

PREVAILING WINDS
BLOW FROM SOUTH

NOTES:

- NOTES:**
1. BASIS OF BEARING: S MEASURED ALONG THE EAST LINE OF THE SOUTHEAST QUARTER OF SECTION 11, T-20-S, R-34-E, N.M.P.M., LEA COUNTY, NEW MEXICO.
BEARS: S 00°26'56" E = 26344.11
 2. ALL BEARINGS, DISTANCES & COORDINATES SHOWN ARE BASED UPON THE NEW MEXICO STATE PLANE COORDINATE SYSTEM, EAST ZONE, NAD 83, IN U.S. SURVEY FEET.
 3. CONTRACTOR SHALL CONTACT "ONE-CALL" FOR LOCATION OF ANY MARKED OR UNMARKED BURIED PIPELINE OR CABLES ON WELL PAD AND/OR ACCESS ROAD AT LEAST TWO (2) WORKING DAYS PRIOR TO CONSTRUCTION.
 4. UNITED FIELD SERVICES, INC. IS NOT LIABLE FOR UNDERGROUND UTILITIES OR PIPELINES.
 5. CUT AND FILL CALCULATIONS ARE ROUNDED TO THE NEAREST FOOT.

I, JOHN A. VUKONICH, NEW MEXICO PROFESSIONAL SURVEYOR NO. 14831, DO HEREBY CERTIFY THAT THIS SURVEY PLAT AND ~~THE~~ SURVEY SURVEY ON THE GROUND UPON WHICH IT IS BASED WERE PERFORMED BY ME OR UNDER MY DIRECT SUPERVISION; THAT I AM RESPONSIBLE FOR THIS SURVEY, THAT THIS SURVEY MEETS THE MINIMUM STANDARDS FOR SURVEYING IN NEW MEXICO, AND THAT IT IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF. I FURTHER CERTIFY THAT THIS SURVEY IS NOT A LAND DIVISION OR SUBDIVISION AS DEFINED IN THE NEW MEXICO SUBDIVISION ACT.

JOHN A. VUKONICH P.E./P.S. N.M.P.S. #14831

DATE 7/

OWNER	SQ. FT.	ACRES
BUREAU OF LAND MANAGEMENT	118,573	2.722
KENNETH SMITH INC.	154,235	3.541
TOTAL	272,808	6.263



United
Field Services Inc.


P.O. Box 3651
Farmington, NM 87499
Office: (505) 334-0408

DWG. No. : 11855-PAD		Revision/By: 2/C.B.
Drawn by: A.A.D.	Date Drawn: 11/13/23	Rev. Date: 1/24/25
Surveyed: 11/9/23	App by: J.A.V.	Sheet: 1


Avant Operating, LLC

Lea Unit 14 11 Pad
H2S Contingency Plan:
Radius Map

Section 14, Township 20S, Range 34E
Lea County, New Mexico





Pad Center



NAD 1983 New Mexico State Plane East
FIPS 3001 Feet



Prepared by Permits West, Inc., January 22, 2024
for Avant Operating, LLC

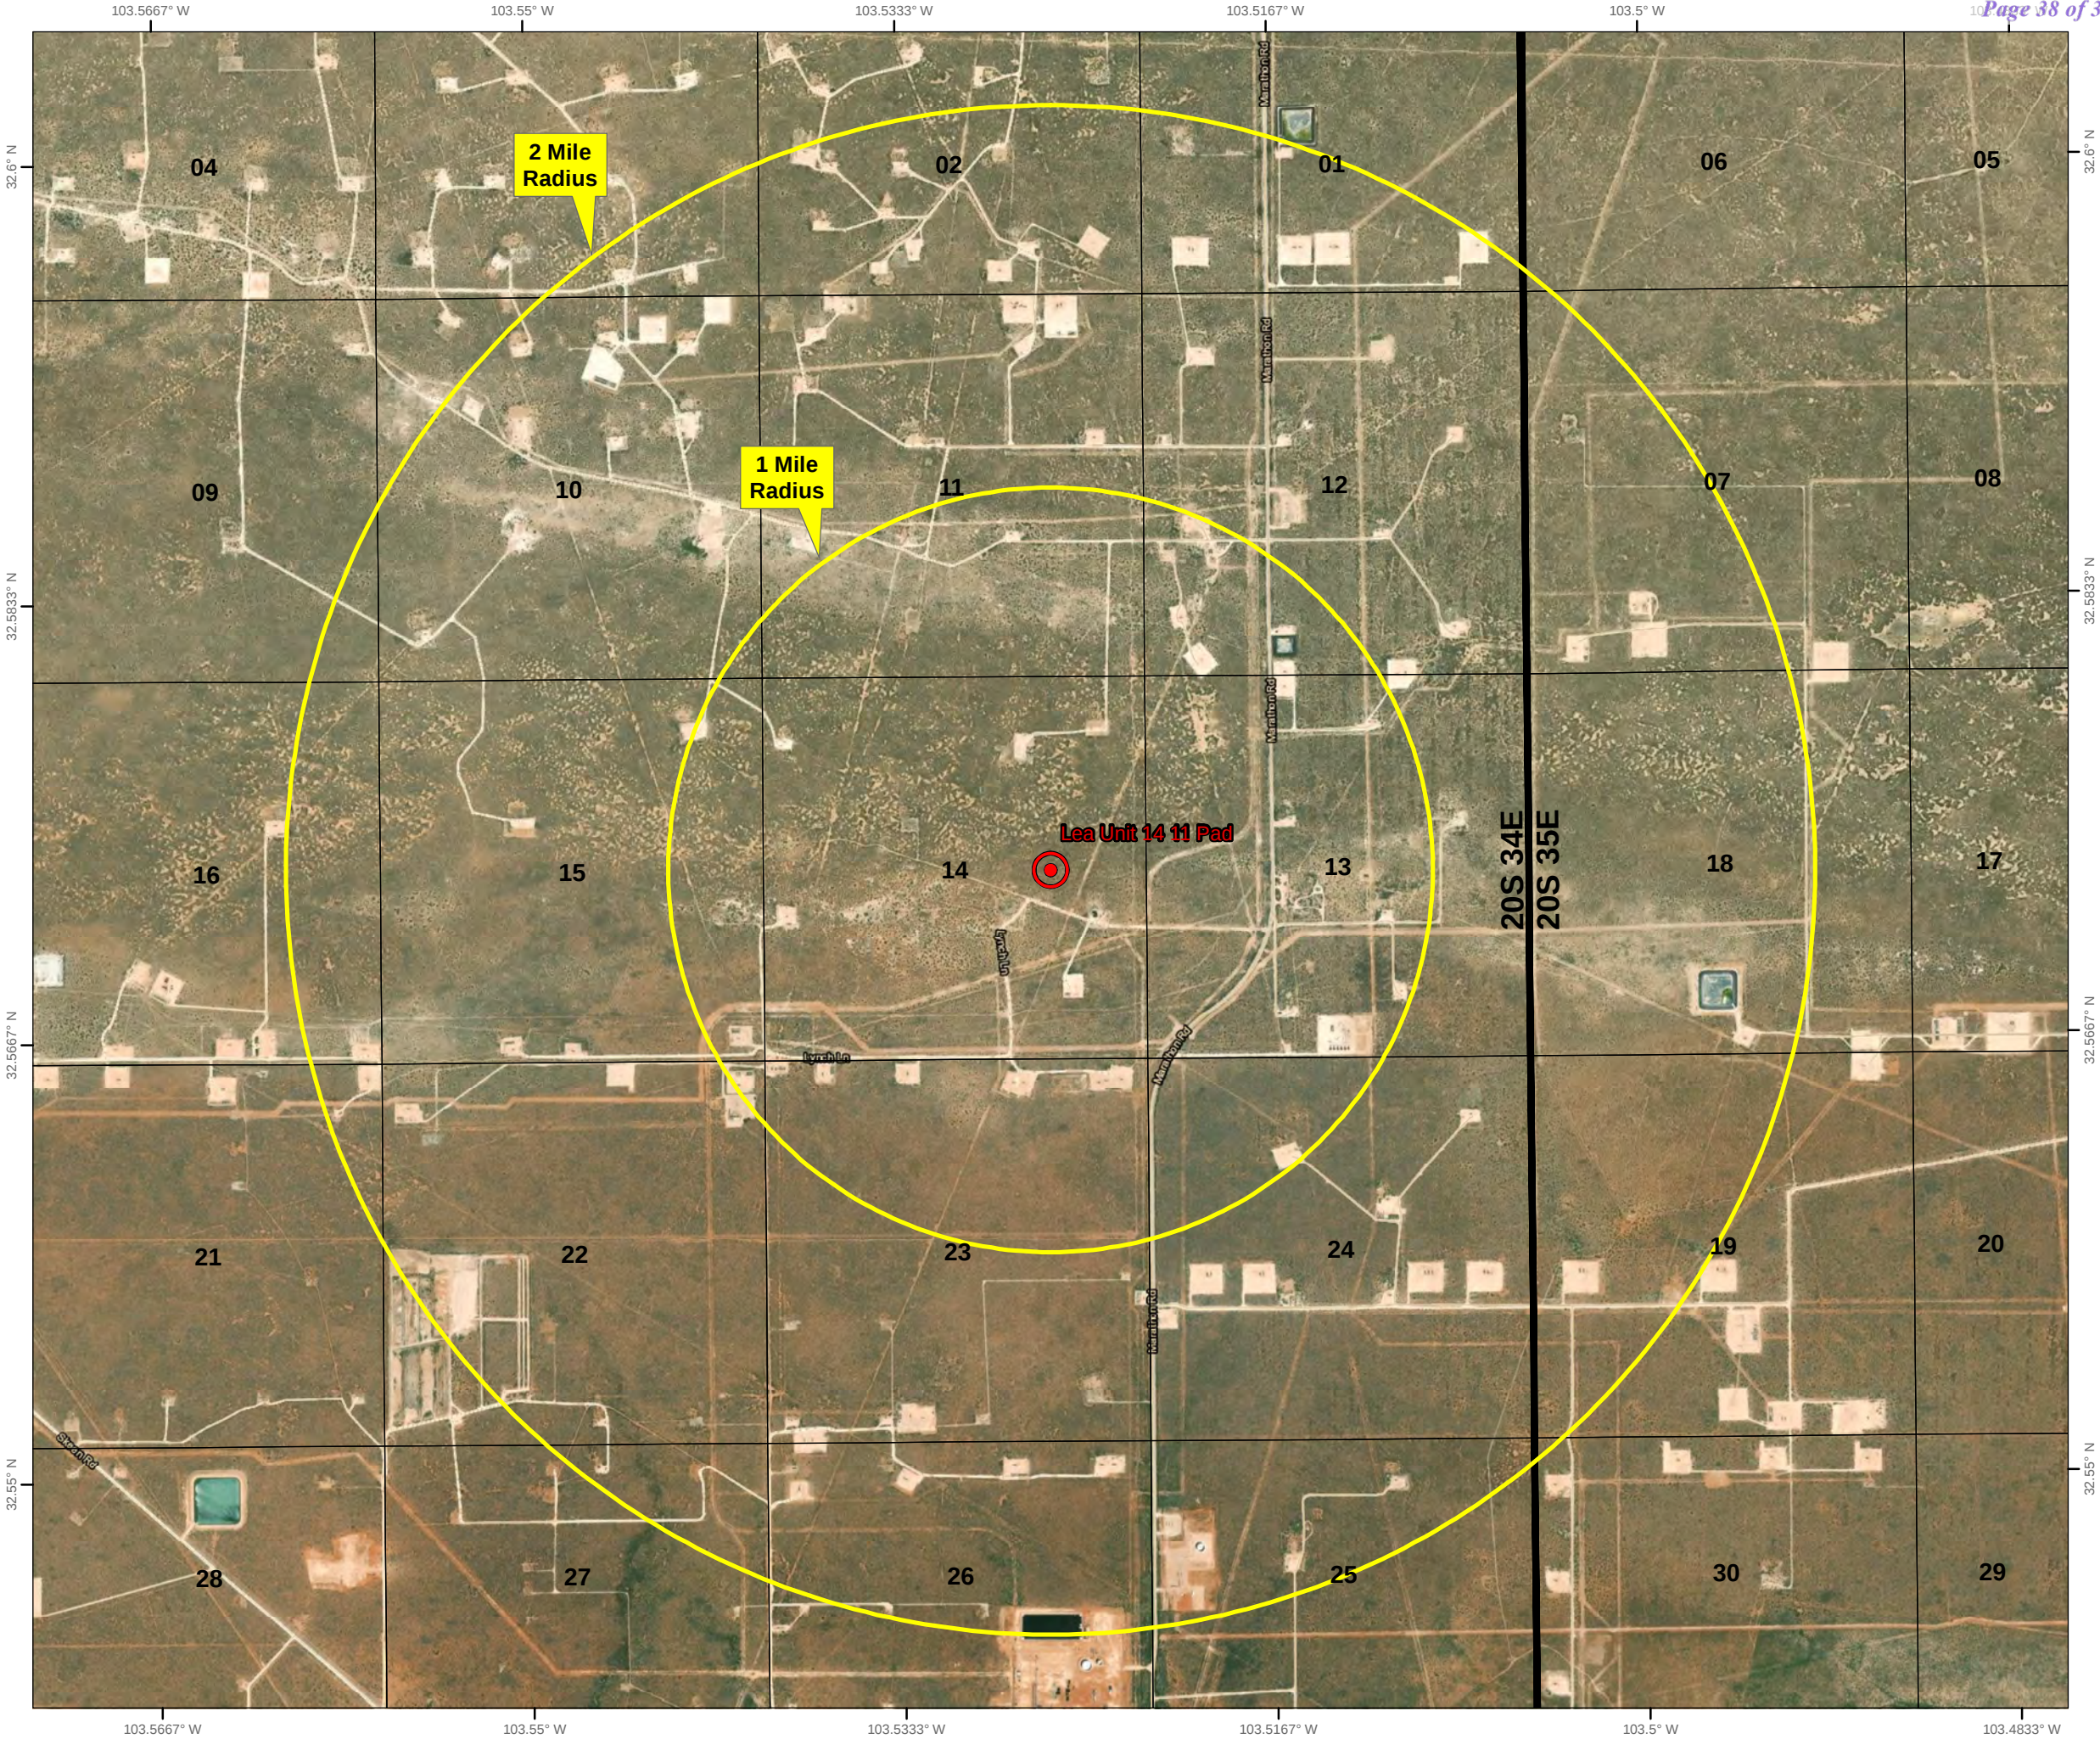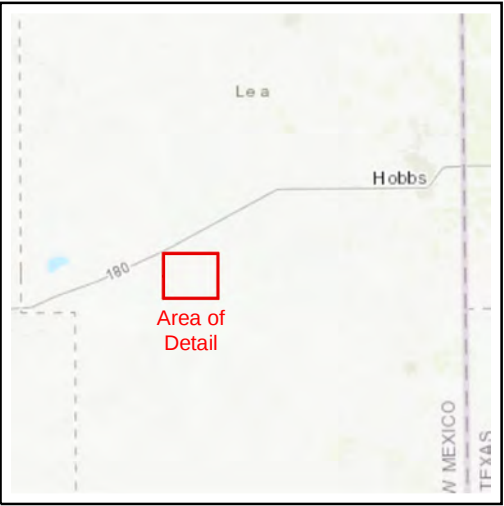

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 381485

CONDITIONS

Operator: Avant Operating, LLC 1515 Wynkoop Street Denver, CO 80202	OGRID: 330396
	Action Number: 381485
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

CONDITIONS

Created By	Condition	Condition Date
pkautz	REQUIRES NAME CHANGE	9/30/2024
pkautz	MUST SUBMIT C-102 ON NEW FORM	9/30/2024
