

C-104 Submit Electronically Via OCD Permitting	State of New Mexico Energy, Minerals & Natural Resources Department OIL CONSERVATION DIVISION	Revised July 9, 2024
--	---	----------------------

REQUEST FOR ALLOWABLE AND AUTHORIZATION TO TRANSPORT

Section 1 - Operator and Well Information

Submittal Type: ☐ Test Allowable (C-104RT) ☒ New Well (C-104NW) ☐ Recomplete (C-104RC) ☐ Pay Add (C-104RC) ☐ Amended	
Operator Name: OXY USA INC	OGRID: 16696
Property Name and Well Number: OLIVE WON UNIT 136H	Property Code: 336102
Mineral Owner: ☐ State ☐ Fee ☐ Tribal ☒ Federal	API Number: 30-0 15-54756
Pool Name: Livingston Ridge; Bone Spring	Pool Code: 39350

Section 2 – Surface Location

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude	Longitude	County
P	25	22S	31E		652' FSL	1087'FEL	32.35698130	-103.72645066	EDDY

Section 3 – Completion Information

Producing Method	Ready Date	Perforations MD	Perforations TVD
Gas lift	06/24/24	11779-21733'MD	11563-11567'TVD

Section 4 – Action IDs for Submissions and Order Numbers

List Action IDs for Drilling Sundries	Was an Order required / needed (Y/N), if yes list Order number:
C-104 RT Action ID (if C-104NW):	Communitization Agreement ☐ Yes ☒ No, Order No.
Surface Casing Action ID: 374744	Unit: ☒ Yes ☐ No, Order No. NMNM106319137
Intermediate 1 Casing Action ID: 374744	Compulsory Pooling: ☐ Yes ☒ No, Order No.
Intermediate 2 Casing Action ID:	Down Hole Commingling: ☐ Yes ☒ No, Order No.
Production Casing Action ID: 374744	Surface Commingling: ☒ Yes ☐ No, Order No. PLC-844-D
All casing was pressure tested in accordance with NMAC ☒ Yes ☐ No	Non-standard Location: ☐ Yes ☒ No ☐ Common ownership Order No.
Liner 1 Action ID: NA	Non-standard Proration: ☐ Yes ☒ No, Order No.
Casing was installed prior to OCD's Action ID system (Y/N): N	Simultaneous Dedication: ☐ Yes ☒ No, Order No.

Section 5 - Operator Signature and Certification

☒ I hereby certify that the required Water Use Report has been, or will be, submitted for this well's completion.	
☒ I hereby certify that the required Fracfocus disclosure has been, or will be, submitted for this well's completion.	
☒ I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief.	
Name Jana Mendiola	<i>Jana Mendiola</i>
Title Regulatory Advisor	Date 09/12/24

C-102 Submit Electronically Via OCD Permitting	State of New Mexico Energy, Minerals, & Natural Resources Department OIL CONSERVATION DIVISION	Revised July 9, 2024
	Submittal Type: ☐ Initial Submittal ☐ Amended Report ☒ As Drilled	

WELL LOCATION INFORMATION

API Number 30-015-54756	Pool Code 39350	Pool Name Livingston Ridge; Bone Spring
Property Code 336102	Property Name OLIVE WON UNIT	Well Number 136H
OGRID No. 16696	Operator Name OXY USA INC.	Ground Level Elevation 3547'
Surface Owner: ☐ State ☐ Fee ☐ Tribal ☒ Federal		Mineral Owner: ☐ State ☐ Fee ☐ Tribal ☒ Federal

Surface Location

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude (NAD83)	Longitude (NAD83)	County
P	25	22S	31E		652' FSL	1087' FEL	32.35698130	-103.72645066	EDDY

Bottom Hole Location

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude (NAD83)	Longitude (NAD83)	County
A	24	22S	31E		102' FNL	332' FEL	32.38396211	-103.72402291	EDDY

Dedicated Acres 320.00	Infill or Defining Well	Defining Well API	Overlapping Spacing Unit (Y/N)	Consolidation Code
Order Numbers:			Well setbacks are under Common Ownership: ☐ Yes ☐ No	

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude (NAD83)	Longitude (NAD83)	County
P	25	22S	31E		74' FSL	390' FEL	32.35538434	-103.72419300	EDDY

First Take Point (FTP)

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude (NAD83)	Longitude (NAD83)	County
P	25	22S	31E		412' FSL	429' FEL	32.35631439	-103.72431922	EDDY

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude (NAD83)	Longitude (NAD83)	County
A	24	22S	31E		226' FNL	334' FEL	32.38362131	-103.72402872	EDDY

Unitized Area or Area of Uniform Interest	Spacing Unit Type: ☒ Horizontal ☐ Vertical	Ground Floor Elevation 3547'
---	---	---------------------------------

OPERATOR CERTIFICATIONS

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and, if the well is a vertical or directional well, that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of a working interest or unleased mineral interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

If this well is a horizontal well, I further certify that this organization has received the consent of at least one lessee or owner of a working interest or unleased mineral interest in each tract (in the target pool or formation) in which any part of the well's completed interval will be located or obtained a compulsory pooling order from the division.

Jana Mendiola 09/11/24
Signature Date

Jana Mendiola
Printed Name

janalyn_mendiola@oxy.com
Email Address

SURVEYOR CERTIFICATIONS

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief. Data used for underground measurements were provided by others for reference only and does not constitute field measurements performed by Delta Field Services



Signature and Seal of Professional Surveyor

Certificate Number

21653

Date of Survey

AUGUST 09, 2024

ACREAGE DEDICATION PLATS

NOW I WON 25_24 FED COM 36H

BHL (NAD83)
X:729426.63' / Y:503952.59'
LAT:32.38396211 / LON:-103.72402291

BHL (NAD27)
X:688244.25' / Y:503892.17'
LAT:32.38383942 / LON:-103.72353437

LTP (NAD83)
X:729425.54' / Y:503828.60'
LAT:32.38362131 / LON:-103.72402872

LTP (NAD27)
X:688243.16' / Y:503768.19'
LAT:32.38349863 / LON:-103.72354020

PPP-1 (NAD83)
X:729436.39' / Y:498774.49'
LAT:32.36972900 / LON:-103.72408680

PPP-1 (NAD27)
X:688253.86' / Y:498714.22'
LAT:32.36960625 / LON:-103.72359882

FTP (NAD83)
X:729392.40' / Y:493893.88'
LAT:32.35631439 / LON:-103.72431922

FTP (NAD27)
X:688209.73' / Y:493833.73'
LAT:32.35619158 / LON:-103.72383176


KOP (NAD83)
X:729433.30' / Y:493555.75'
LAT:32.35538434 / LON:-103.72419300

KOP (NAD27)
X:688250.62' / Y:493495.61'
LAT:32.35526151 / LON:-103.72370558

SHL (NAD83)
X:728732.86' / Y:494132.76'
LAT:32.35698130 / LON:-103.72645066

SHL (NAD27)
X:687550.20' / Y:494072.61'
LAT:32.35685850 / LON:-103.72596311

CORNER COORDINATES NAD 83, SPCS NM EAST	CORNER COORDINATES NAD 27, SPCS NM EAST
A - X: 729757.89' / Y: 504056.71'	A - X: 688575.51' / Y: 503996.29'
B - X: 729772.30' / Y: 501414.79'	B - X: 688589.85' / Y: 501354.44'
C - X: 729786.86' / Y: 498775.98'	C - X: 688604.33' / Y: 498715.70'
D - X: 729824.17' / Y: 493482.52'	D - X: 688641.49' / Y: 493422.39'
E - X: 728503.11' / Y: 493480.62'	E - X: 687320.44' / Y: 493420.48'
F - X: 728466.38' / Y: 498770.37'	F - X: 687283.86' / Y: 498710.09'
G - X: 728436.32' / Y: 504049.62'	G - X: 687253.96' / Y: 503989.20'

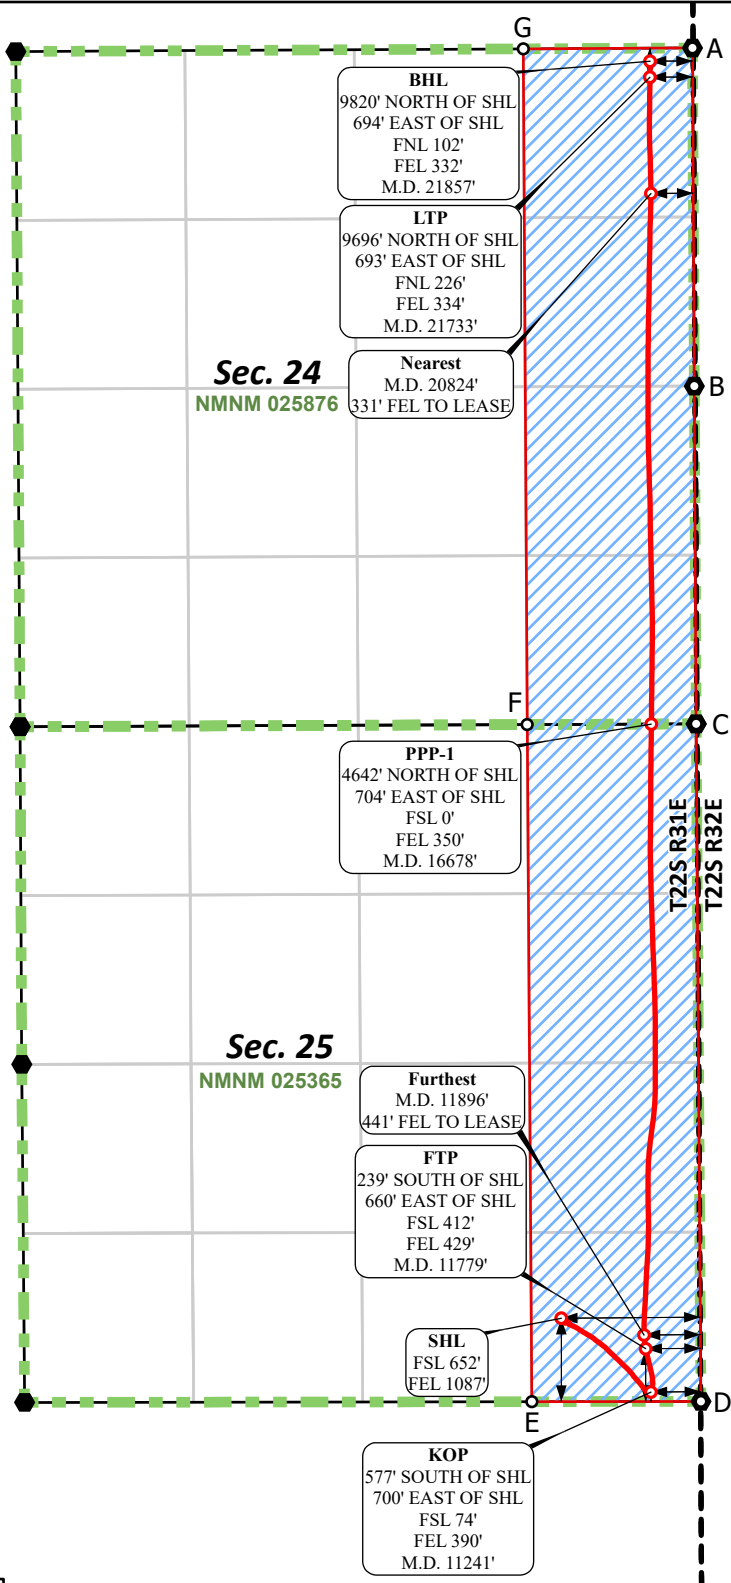

*FTP TO LTP LEASE DISTANCES

FEDERAL LEASE ID	LENGTH
NMNM025365	4885.87'
NMNM025876	5054.96'
TOTAL	9940.83'



○ Drill Line Events ● Section Corners — Drill Line — Dimension Lines — Federal Leases — HSU ○ HSU Corners

All bearings and coordinates refer to New Mexico State Plane Coordinate System, East Zone, U.S. Survey Feet.

JOB No. OXY_0008_NW01
REV 1 NDS 8/6/2024


Distances/areas relative to NAD 83 grid measurements. Combined Scale Factor: 0.99978405 and a Convergence Angle: 0.31759444°




Project: Eddy County, NM (NAD83-NME)
Site: Now I Won 25_24
Well: Now I Won 25_24 Fed Com 36H
Wellbore: OH / 74283
Design: Plan 4 04-04-24
Rig: Citadel 3



PHOENIX
TECHNOLOGY SERVICES

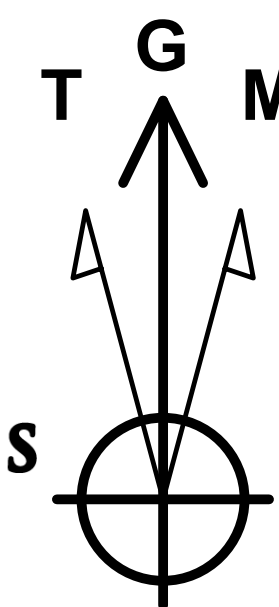

Azimuths to Grid North
True North: -0.32°
Magnetic North: 6.24°
Magnetic Field
Strength: 47597.5nT
Dip Angle: 60.00°
Date: 3/30/2024
Model: IFR





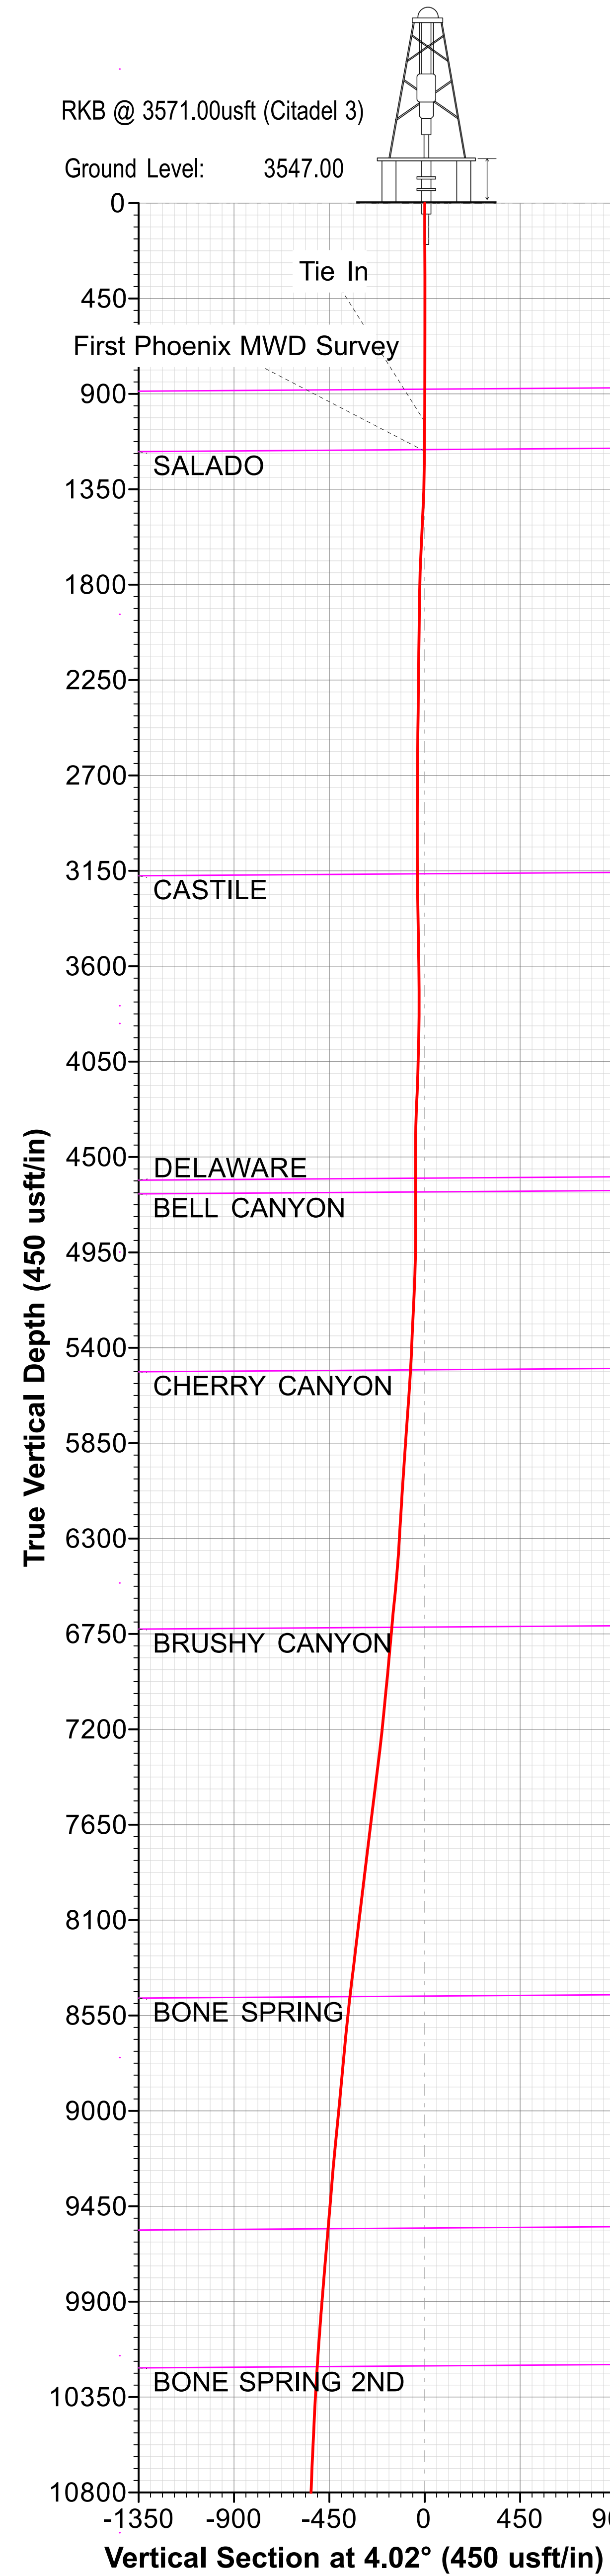


WELL DETAILS									
		Ground Level:		3547.00					
+N/-S	+E/-W	Northing	Easting	Latitude		Longitude			
0.00	0.00	494132.76	728732.86	32° 21' 25.132664 N		103° 43' 35.222323 W			

SECTION DETAILS									
MD	Inc	Azi	TVD	+N/-S	+E/-W	VSect	Departure	Annotation	
1031.00	0.51	220.28	1030.99	-0.21	0.57	-0.17	5.27	Tie In	
1170.00	0.67	227.23	1169.98	-1.24	-0.43	-1.26	6.70	First Phoenix MWD Survey	
11330.06	23.51	19.88	11259.75	-550.78	708.79	-499.79	1003.21	FTP: 11330.06' MD, 23.51° Inc	
16677.81	91.12	0.55	11590.64	4641.73	703.53	4679.61	6208.75	SL: 16677.81' MD, 91.12° Inc	
21740.00	89.51	0.49	11567.48	9702.84	692.77	9727.53	11270.76	Final Phoenix MWD Survey	
21857.00	89.51	0.49	11568.48	9819.83	693.77	9844.30	11387.75	Projection to TD	

FORMATION TOP DETAILS		
TVDPath	MDPath	Formation
878.00	878.01	RUSTLER
1163.01	1163.03	SALADO
3164.01	3164.03	CASTILE
4600.01	4600.03	DELAWARE
4665.01	4665.03	BELL CANYON
5504.28	5507.88	CHERRY CANYON
6719.26	6748.37	BRUSHY CANYON
8461.71	8529.76	BONE SPRING
9556.46	9641.40	BONE SPRING 1ST
10206.71	10294.77	BONE SPRING 2ND
11271.57	11364.24	BONE SPRING 3RD

Map System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone Name: New Mexico Eastern Zone
Local Origin: Well Now I Won 25_24 Fed Com 36H, Grid North
Latitude: 32° 21' 25.132664 N
Longitude: 103° 43' 35.222323 W
Grid East: 728732.86
Grid North: 494132.76
Scale Factor: 1.000
Geomagnetic Model: IFR
Sample Date: 30-Mar-24
Magnetic Declination: 6.567°
Dip Angle from Horizontal: 60.002°
Magnetic Field Strength: 47597.50000000nT
To convert a Magnetic Direction to a Grid Direction, Add 6.242°
To convert a Magnetic Direction to a True Direction, Add 6.567° East
To convert a True Direction to a Grid Direction, Subtract 0.325°

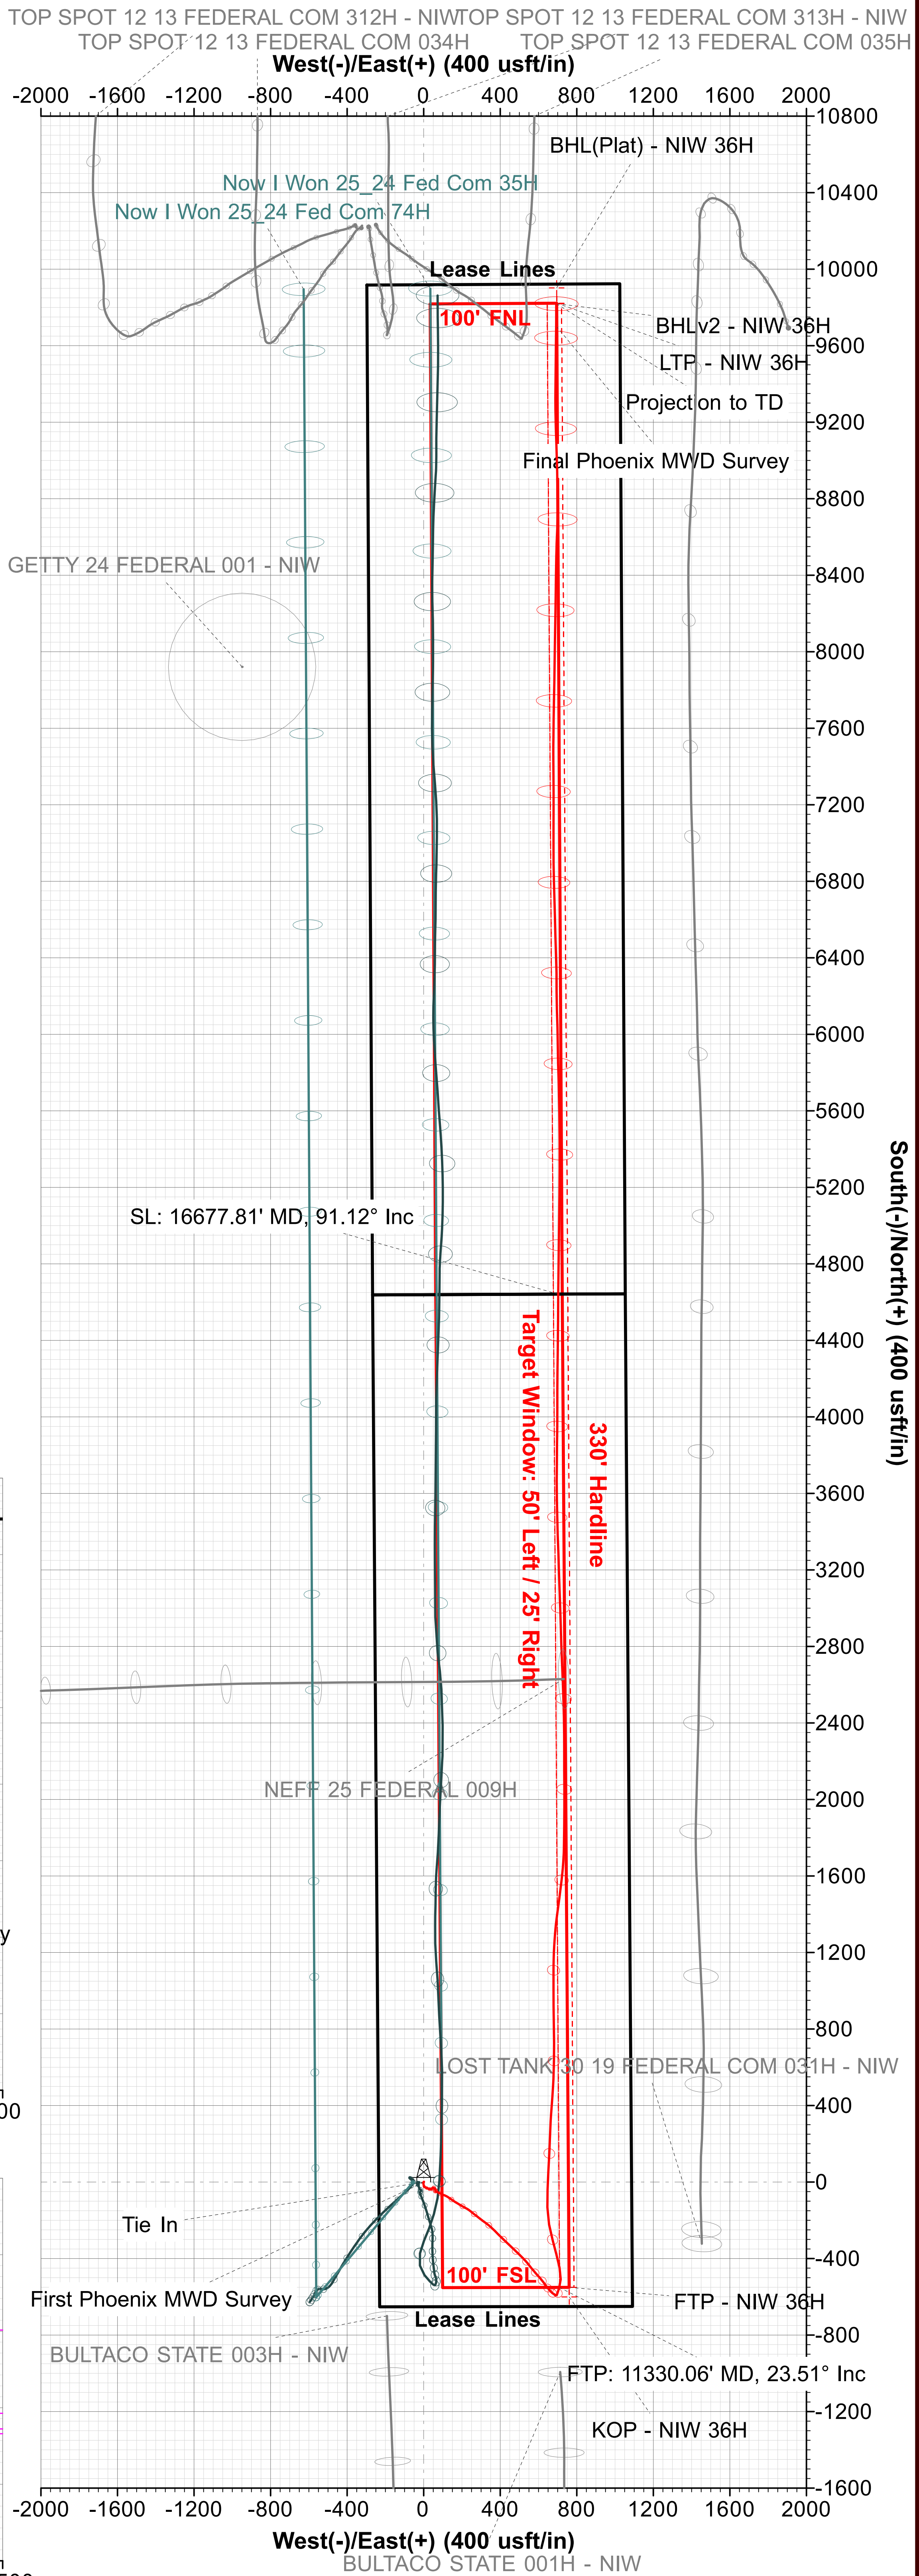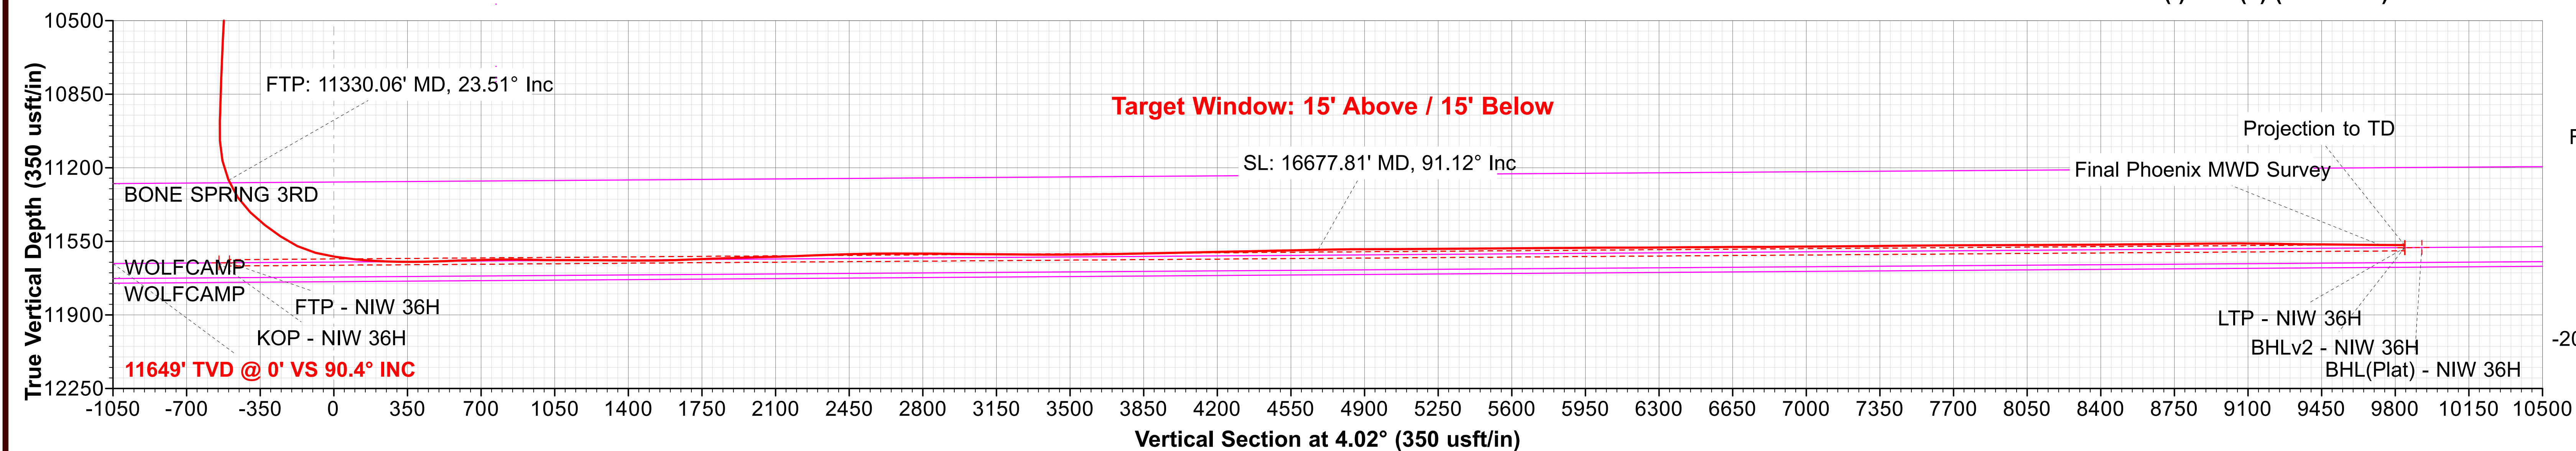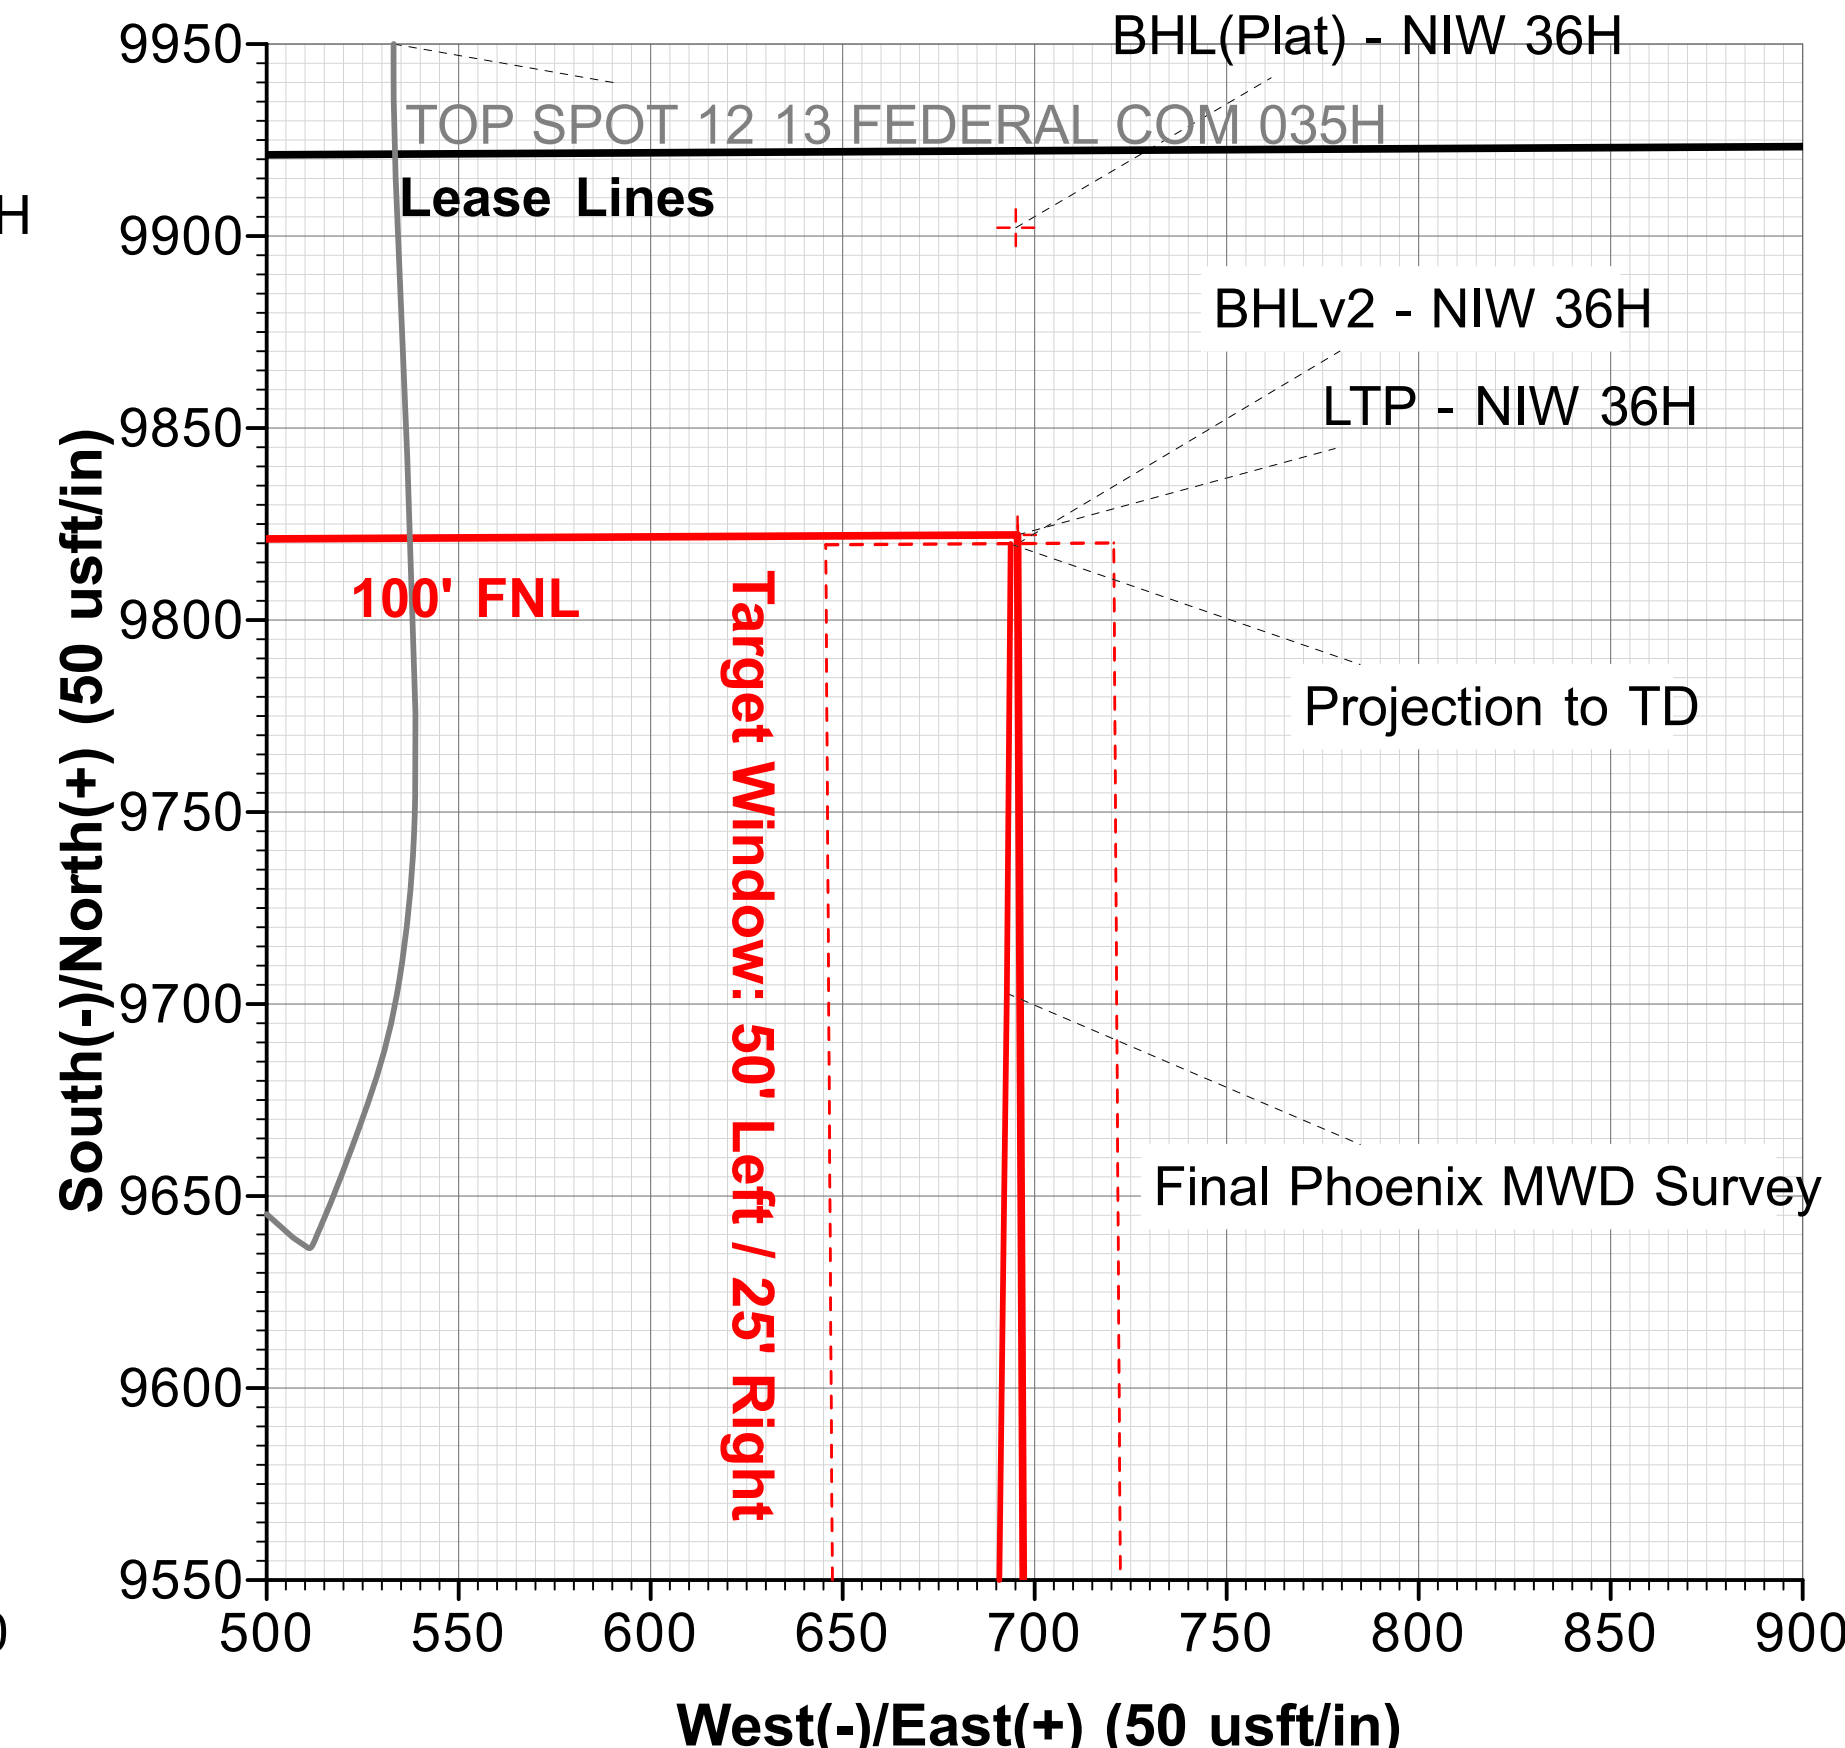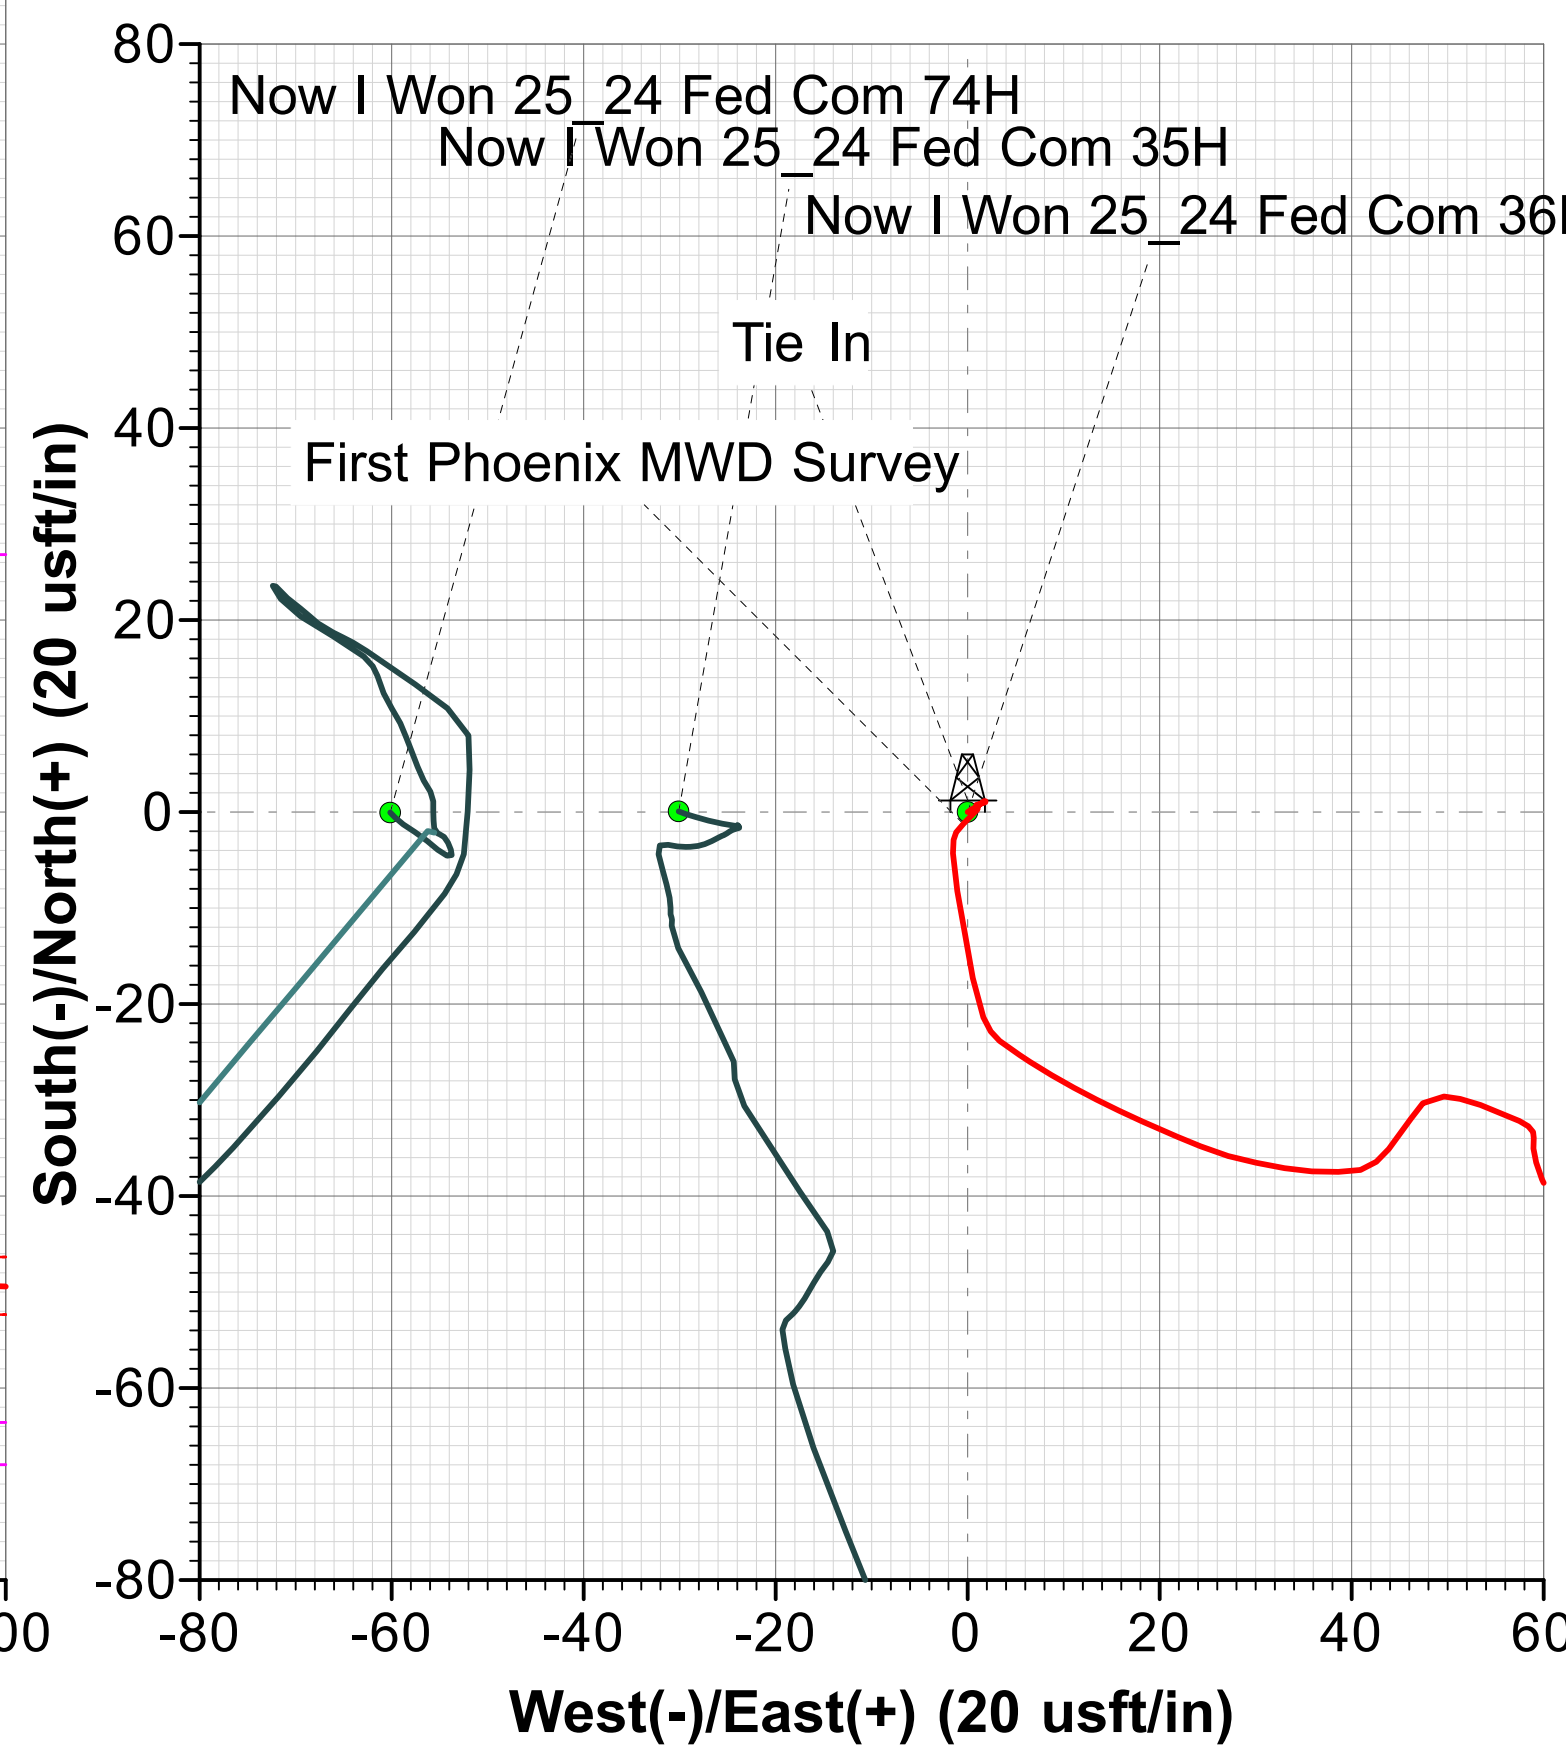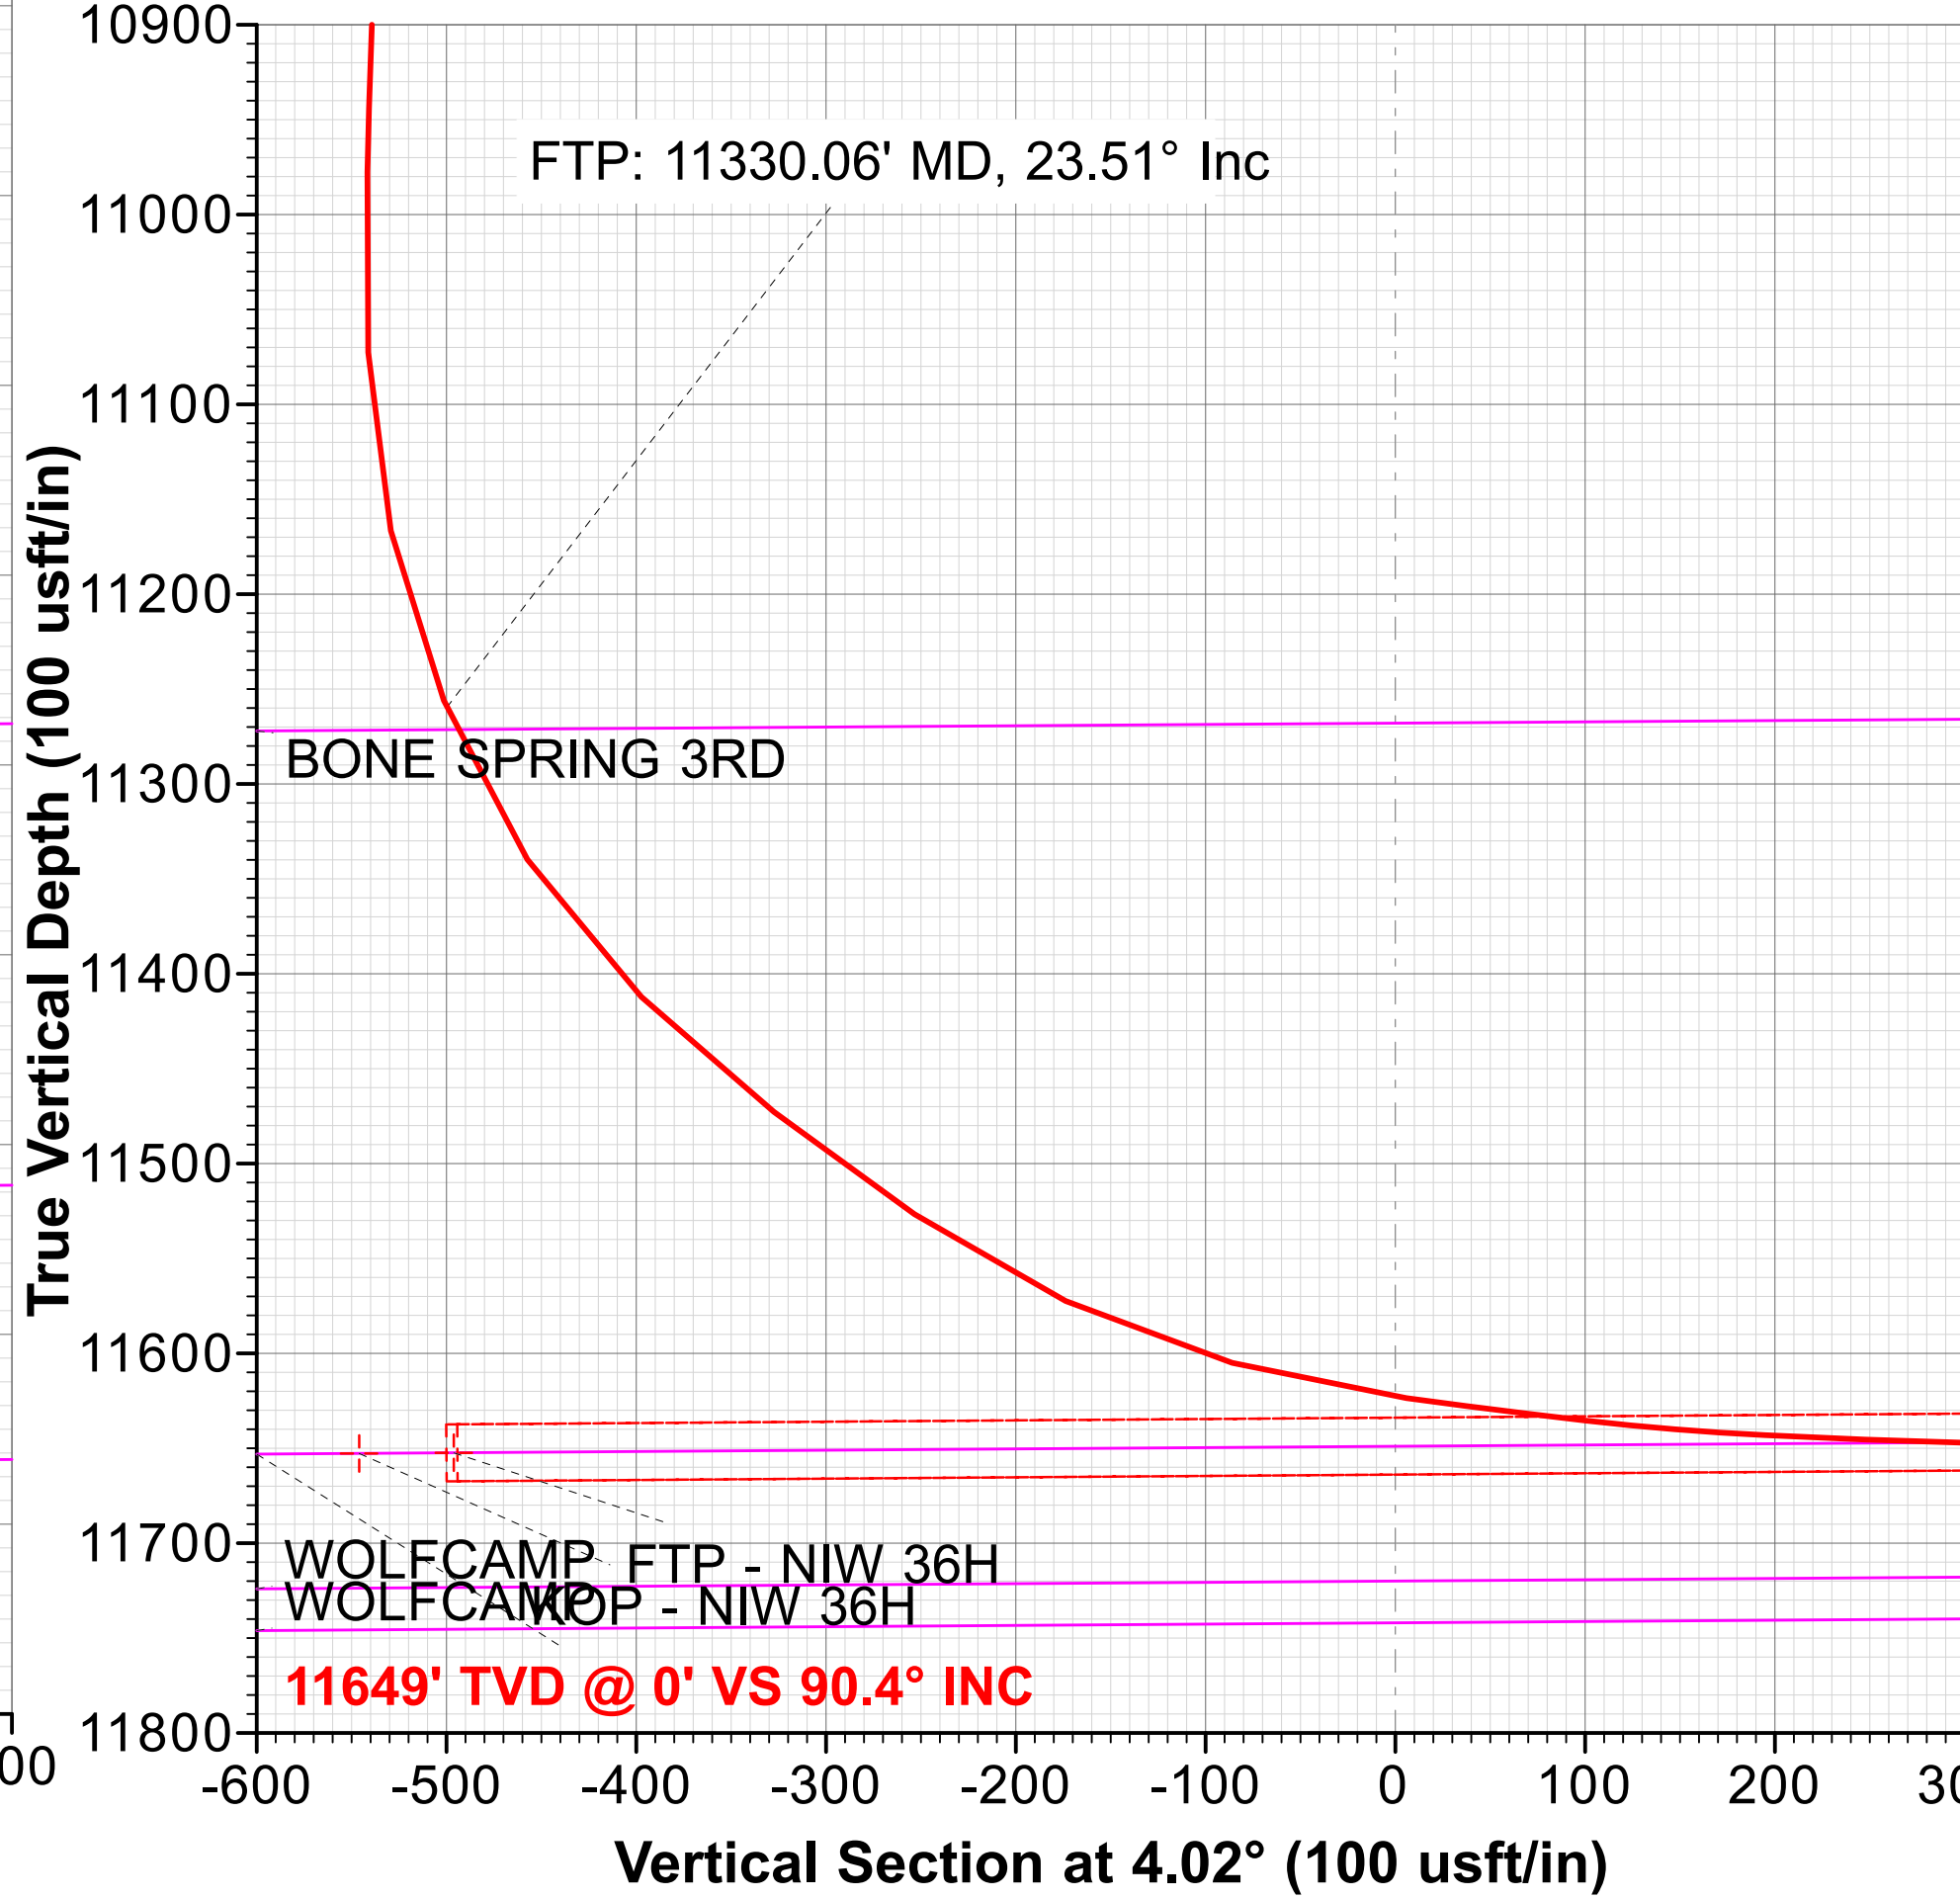



OXY USA INC.

Eddy County, NM (NAD83-NME)

Now I Won 25_24

Now I Won 25_24 Fed Com 36H

OH / 74283

Design: Surveys (Citadel 3)

Standard Survey Report

20 May, 2024





Company:	OXY USA INC.	Local Co-ordinate Reference:	Well Now I Won 25_24 Fed Com 36H
Project:	Eddy County, NM (NAD83-NME)	TVD Reference:	RKB @ 3571.00usft (Citadel 3)
Site:	Now I Won 25_24	MD Reference:	RKB @ 3571.00usft (Citadel 3)
Well:	Now I Won 25_24 Fed Com 36H	North Reference:	Grid
Wellbore:	OH / 74283	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Citadel 3)	Database:	USAEDMDB

Project	Eddy County, NM (NAD83-NME)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Now I Won 25_24		
Site Position:		Northing:	494,132.79 usft
From:	Map	Easting:	726,591.88 usft
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16 "
		Latitude:	32° 21' 25.252377 N
		Longitude:	103° 44' 0.182082 W

Well	Now I Won 25_24 Fed Com 36H		
Well Position	+N/-S	0.00 usft	Northing: 494,132.76 usft
	+E/-W	0.00 usft	Easting: 728,732.86 usft
Position Uncertainty	2.00 usft	Wellhead Elevation:	usft
Grid Convergence:	0.325 °	Ground Level:	3,547.00 usft

Wellbore	OH / 74283				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IFR	3/30/2024	6.567	60.002	47,597.50000000

Design	Surveys (Citadel 3)				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)	
	0.00	0.00	0.00	4.02	

Survey Program	Date	5/20/2024			
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
24.00	1,031.00	SDT MWD Surveys - Adj Surface (OH / 74	B004Mc_MWD+HRGM+S	MWD+HRGM+Sag	
1,170.00	21,857.00	Phoenix MWD Surves - SQC Final Survey	SQC_C705Mb_MWD+IFF	MWD+IFR1+Sag+FDIR	

Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
24.00	0.00	0.00	24.00	0.00	0.00	0.00	0.00	0.00	0.00	
174.00	0.40	55.78	174.00	0.29	0.43	0.32	0.27	0.27	0.00	
261.00	0.51	63.52	261.00	0.64	1.03	0.71	0.14	0.13	8.90	
348.00	0.31	39.16	347.99	0.99	1.53	1.10	0.30	-0.23	-28.00	
434.00	0.12	108.83	433.99	1.14	1.76	1.26	0.34	-0.22	81.01	
521.00	0.06	80.73	520.99	1.12	1.89	1.25	0.08	-0.07	-32.30	
607.00	0.18	219.97	606.99	1.03	1.85	1.15	0.27	0.14	161.91	
695.00	0.49	263.09	694.99	0.87	1.38	0.97	0.43	0.35	49.00	



Phoenix Survey Report



Company:	OXY USA INC.	Local Co-ordinate Reference:	Well Now I Won 25_24 Fed Com 36H
Project:	Eddy County, NM (NAD83-NME)	TVD Reference:	RKB @ 3571.00usft (Citadel 3)
Site:	Now I Won 25_24	MD Reference:	RKB @ 3571.00usft (Citadel 3)
Well:	Now I Won 25_24 Fed Com 36H	North Reference:	Grid
Wellbore:	OH / 74283	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Citadel 3)	Database:	USAEDMDB

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
781.00	0.18	229.63	780.99	0.74	0.92	0.81	0.41	-0.36	-38.91
868.00	0.36	100.70	867.99	0.60	1.08	0.68	0.57	0.21	-148.20
954.00	0.53	227.86	953.99	0.29	1.05	0.36	0.93	0.20	147.86
1,031.00	0.51	220.28	1,030.99	-0.21	0.57	-0.17	0.09	-0.03	-9.84
Tie In									
1,170.00	0.67	227.23	1,169.98	-1.24	-0.43	-1.26	0.13	0.12	5.00
First Phoenix MWD Survey									
1,265.00	0.73	216.15	1,264.97	-2.10	-1.20	-2.18	0.16	0.06	-11.66
1,359.00	2.07	178.87	1,358.94	-4.28	-1.52	-4.38	1.65	1.43	-39.66
1,454.00	2.72	169.60	1,453.86	-8.22	-1.07	-8.27	0.79	0.68	-9.76
1,549.00	2.75	169.70	1,548.75	-12.68	-0.26	-12.66	0.03	0.03	0.11
1,644.00	2.89	170.46	1,643.64	-17.28	0.54	-17.20	0.15	0.15	0.80
1,739.00	2.26	157.93	1,738.54	-21.38	1.65	-21.21	0.89	-0.66	-13.19
1,833.00	1.50	127.06	1,832.49	-23.84	3.32	-23.55	1.32	-0.81	-32.84
1,928.00	1.61	123.23	1,927.46	-25.32	5.43	-24.88	0.16	0.12	-4.03
2,023.00	1.74	121.90	2,022.42	-26.81	7.77	-26.20	0.14	0.14	-1.40
2,118.00	1.85	118.77	2,117.37	-28.31	10.34	-27.52	0.16	0.12	-3.29
2,213.00	1.81	116.87	2,212.32	-29.73	13.02	-28.74	0.08	-0.04	-2.00
2,307.00	1.87	115.87	2,306.27	-31.07	15.73	-29.89	0.07	0.06	-1.06
2,402.00	1.83	114.24	2,401.22	-32.37	18.51	-30.99	0.07	-0.04	-1.72
2,497.00	1.91	112.60	2,496.17	-33.60	21.35	-32.02	0.10	0.08	-1.73
2,592.00	1.90	112.83	2,591.12	-34.82	24.26	-33.03	0.01	-0.01	0.24
2,687.00	1.79	105.65	2,686.07	-35.83	27.14	-33.84	0.27	-0.12	-7.56
2,782.00	1.85	100.96	2,781.02	-36.52	30.08	-34.32	0.17	0.06	-4.94
2,877.00	1.77	101.18	2,875.97	-37.10	33.02	-34.69	0.08	-0.08	0.23
2,972.00	1.69	91.71	2,970.93	-37.42	35.86	-34.82	0.31	-0.08	-9.97
3,067.00	1.62	90.22	3,065.89	-37.47	38.61	-34.67	0.09	-0.07	-1.57
3,161.00	1.25	78.70	3,159.86	-37.27	40.94	-34.32	0.50	-0.39	-12.26
3,256.00	1.08	44.75	3,254.84	-36.43	42.59	-33.36	0.74	-0.18	-35.74
3,351.00	1.17	43.38	3,349.83	-35.09	43.88	-31.94	0.10	0.09	-1.44
3,540.00	1.22	29.53	3,538.78	-31.94	46.20	-28.63	0.15	0.03	-7.33
3,635.00	1.24	45.07	3,633.76	-30.34	47.43	-26.94	0.35	0.02	16.36
3,730.00	1.78	91.09	3,728.73	-29.64	49.63	-26.09	1.35	0.57	48.44
3,825.00	2.99	109.74	3,823.65	-30.50	53.44	-26.69	1.50	1.27	19.63
3,920.00	2.30	115.84	3,918.55	-32.17	57.48	-28.07	0.78	-0.73	6.42
4,015.00	1.17	192.16	4,013.51	-33.95	59.00	-29.73	2.44	-1.19	80.34
4,109.00	2.03	164.57	4,107.48	-36.49	59.24	-32.25	1.20	0.91	-29.35
4,204.00	3.02	153.24	4,202.38	-40.35	60.81	-35.99	1.16	1.04	-11.93
4,299.00	2.81	153.14	4,297.26	-44.66	62.99	-40.14	0.22	-0.22	-0.11
4,394.00	0.42	212.89	4,392.22	-47.03	63.85	-42.44	2.76	-2.52	62.89
4,488.00	0.43	259.77	4,486.22	-47.38	63.32	-42.83	0.36	0.01	49.87
4,583.00	0.32	293.54	4,581.22	-47.34	62.72	-42.83	0.25	-0.12	35.55
4,678.00	0.51	295.66	4,676.21	-47.05	62.10	-42.59	0.20	0.20	2.23



Phoenix Survey Report



Company:	OXY USA INC.	Local Co-ordinate Reference:	Well Now I Won 25_24 Fed Com 36H
Project:	Eddy County, NM (NAD83-NME)	TVD Reference:	RKB @ 3571.00usft (Citadel 3)
Site:	Now I Won 25_24	MD Reference:	RKB @ 3571.00usft (Citadel 3)
Well:	Now I Won 25_24 Fed Com 36H	North Reference:	Grid
Wellbore:	OH / 74283	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Citadel 3)	Database:	USAEDMDB

Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
4,773.00	0.45	312.97	4,771.21	-46.61	61.45	-42.20	0.16	-0.06	18.22	
4,868.00	0.74	151.78	4,866.21	-46.90	61.46	-42.48	1.24	0.31	-169.67	
4,962.00	2.39	120.25	4,960.17	-48.42	63.44	-43.86	1.92	1.76	-33.54	
5,057.00	5.08	114.92	5,054.96	-51.19	68.97	-46.24	2.85	2.83	-5.61	
5,152.00	6.95	115.14	5,149.43	-55.41	77.99	-49.81	1.97	1.97	0.23	
5,247.00	7.97	115.42	5,243.63	-60.68	89.14	-54.29	1.07	1.07	0.29	
5,341.00	7.94	113.12	5,336.72	-66.02	101.00	-58.79	0.34	-0.03	-2.45	
5,436.00	7.95	111.90	5,430.81	-71.05	113.13	-62.95	0.18	0.01	-1.28	
5,531.00	7.71	121.22	5,524.93	-76.80	124.67	-67.88	1.36	-0.25	9.81	
5,626.00	7.68	126.12	5,619.08	-83.85	135.25	-74.17	0.69	-0.03	5.16	
5,721.00	7.68	124.79	5,713.22	-91.21	145.59	-80.79	0.19	0.00	-1.40	
5,816.00	8.13	123.50	5,807.32	-98.54	156.41	-87.35	0.51	0.47	-1.36	
5,910.00	8.41	122.20	5,900.34	-105.87	167.77	-93.87	0.36	0.30	-1.38	
6,005.00	8.45	121.27	5,994.32	-113.20	179.61	-100.34	0.15	0.04	-0.98	
6,100.00	8.30	119.67	6,088.30	-120.22	191.53	-106.51	0.29	-0.16	-1.68	
6,195.00	8.16	119.18	6,182.33	-126.90	203.38	-112.34	0.16	-0.15	-0.52	
6,290.00	8.09	118.07	6,276.37	-133.33	215.16	-117.94	0.18	-0.07	-1.17	
6,384.00	8.35	117.90	6,369.41	-139.64	227.03	-123.39	0.28	0.28	-0.18	
6,479.00	9.32	128.77	6,463.28	-147.68	239.13	-130.57	2.03	1.02	11.44	
6,574.00	9.65	128.56	6,556.99	-157.46	251.35	-139.47	0.35	0.35	-0.22	
6,669.00	9.70	128.81	6,650.63	-167.44	263.81	-148.56	0.07	0.05	0.26	
6,764.00	9.16	127.60	6,744.35	-177.07	276.04	-157.31	0.61	-0.57	-1.27	
6,859.00	9.05	127.54	6,838.15	-186.24	287.96	-165.61	0.12	-0.12	-0.06	
7,048.00	10.35	127.46	7,024.45	-205.62	313.22	-183.18	0.69	0.69	-0.04	
7,143.00	10.19	126.69	7,117.92	-215.83	326.73	-192.42	0.22	-0.17	-0.81	
7,238.00	10.54	126.33	7,211.37	-226.00	340.47	-201.60	0.37	0.37	-0.38	
7,333.00	10.95	135.53	7,304.72	-237.59	353.79	-212.23	1.85	0.43	9.68	
7,523.00	10.68	134.35	7,491.34	-262.77	379.02	-235.59	0.18	-0.14	-0.62	
7,618.00	10.58	134.05	7,584.71	-274.99	391.59	-246.89	0.12	-0.11	-0.32	
7,713.00	10.96	134.37	7,678.04	-287.37	404.31	-258.35	0.40	0.40	0.34	
7,808.00	10.76	133.77	7,771.34	-299.82	417.17	-269.87	0.24	-0.21	-0.63	
7,902.00	10.78	133.95	7,863.68	-311.99	429.84	-281.12	0.04	0.02	0.19	
7,997.00	10.46	133.28	7,957.05	-324.07	442.51	-292.28	0.36	-0.34	-0.71	
8,092.00	10.84	134.11	8,050.42	-336.20	455.20	-303.50	0.43	0.40	0.87	
8,187.00	10.92	133.38	8,143.71	-348.60	468.16	-314.96	0.17	0.08	-0.77	
8,282.00	10.51	133.24	8,237.05	-360.71	481.01	-326.14	0.43	-0.43	-0.15	
8,377.00	10.24	133.75	8,330.50	-372.49	493.42	-337.02	0.30	-0.28	0.54	
8,471.00	10.37	134.47	8,422.98	-384.19	505.49	-347.85	0.19	0.14	0.77	
8,566.00	9.64	135.82	8,516.54	-395.89	517.14	-358.70	0.81	-0.77	1.42	
8,661.00	8.63	137.25	8,610.33	-406.82	527.52	-368.88	1.09	-1.06	1.51	
8,756.00	7.07	138.36	8,704.44	-416.43	536.24	-377.85	1.65	-1.64	1.17	
8,851.00	7.78	142.12	8,798.64	-425.87	544.08	-386.73	0.91	0.75	3.96	
9,041.00	6.63	142.04	8,987.14	-444.67	558.72	-404.45	0.61	-0.61	-0.04	
9,135.00	8.21	138.44	9,080.35	-453.97	566.51	-413.19	1.75	1.68	-3.83	



Phoenix Survey Report



Company:	OXY USA INC.	Local Co-ordinate Reference:	Well Now I Won 25_24 Fed Com 36H
Project:	Eddy County, NM (NAD83-NME)	TVD Reference:	RKB @ 3571.00usft (Citadel 3)
Site:	Now I Won 25_24	MD Reference:	RKB @ 3571.00usft (Citadel 3)
Well:	Now I Won 25_24 Fed Com 36H	North Reference:	Grid
Wellbore:	OH / 74283	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Citadel 3)	Database:	USAEDMDB

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
9,230.00	7.96	140.24	9,174.40	-464.11	575.22	-422.68	0.37	-0.26	1.89
9,325.00	6.75	142.20	9,268.62	-473.57	582.85	-431.60	1.30	-1.27	2.06
9,420.00	6.63	136.98	9,362.97	-481.99	590.01	-439.49	0.65	-0.13	-5.49
9,515.00	7.17	135.72	9,457.29	-490.25	597.89	-447.18	0.59	0.57	-1.33
9,609.00	6.92	138.76	9,550.58	-498.71	605.72	-455.07	0.48	-0.27	3.23
9,704.00	6.74	141.05	9,644.90	-507.35	613.00	-463.17	0.34	-0.19	2.41
9,799.00	6.52	143.05	9,739.27	-515.99	619.74	-471.33	0.34	-0.23	2.11
9,894.00	6.16	142.63	9,833.69	-524.35	626.08	-479.22	0.38	-0.38	-0.44
9,989.00	6.12	144.10	9,928.14	-532.51	632.14	-486.93	0.17	-0.04	1.55
10,083.00	5.65	144.57	10,021.65	-540.34	637.76	-494.35	0.50	-0.50	0.50
10,178.00	5.32	140.23	10,116.21	-547.53	643.29	-501.14	0.56	-0.35	-4.57
10,273.00	4.84	140.44	10,210.84	-554.01	648.66	-507.22	0.51	-0.51	0.22
10,368.00	4.41	139.06	10,305.53	-559.85	653.61	-512.71	0.47	-0.45	-1.45
10,463.00	4.17	137.94	10,400.26	-565.18	658.32	-517.69	0.27	-0.25	-1.18
10,558.00	4.27	138.75	10,495.00	-570.40	662.96	-522.58	0.12	0.11	0.85
10,653.00	4.03	136.87	10,589.76	-575.50	667.58	-527.33	0.29	-0.25	-1.98
10,748.00	4.22	129.41	10,684.51	-580.15	672.56	-531.63	0.60	0.20	-7.85
10,842.00	4.32	124.26	10,778.25	-584.34	678.16	-535.42	0.42	0.11	-5.48
11,008.00	4.00	116.01	10,943.81	-590.40	688.53	-540.73	0.41	-0.19	-4.97
11,042.00	3.53	117.67	10,977.74	-591.41	690.52	-541.60	1.42	-1.38	4.88
11,137.00	3.25	56.32	11,072.60	-591.27	695.35	-541.12	3.65	-0.29	-64.58
11,232.00	12.54	11.25	11,166.66	-579.63	699.62	-529.21	11.05	9.78	-47.44
11,326.00	23.14	20.93	11,256.03	-552.29	708.23	-501.33	11.67	11.28	10.30
11,330.06	23.51	19.88	11,259.76	-550.78	708.79	-499.79	13.76	9.14	-25.96
FTP: 11330.06' MD, 23.51° Inc									
11,421.00	33.15	2.79	11,339.84	-508.72	716.20	-457.32	13.76	10.60	-18.79
11,516.00	47.50	348.00	11,412.24	-448.06	710.14	-397.23	18.07	15.11	-15.57
11,611.00	53.14	345.71	11,472.88	-376.92	693.46	-327.43	6.22	5.94	-2.41
11,706.00	57.75	344.99	11,526.75	-301.25	673.66	-253.33	4.89	4.85	-0.76
11,801.00	64.77	349.33	11,572.42	-220.09	655.28	-173.66	8.40	7.39	4.57
11,896.00	75.07	359.29	11,605.06	-131.53	646.71	-85.92	14.63	10.84	10.48
11,990.00	82.16	1.85	11,623.61	-39.45	647.65	6.00	8.00	7.54	2.72
12,085.00	83.51	3.39	11,635.46	54.70	651.96	100.22	2.15	1.42	1.62
12,180.00	87.19	2.43	11,643.16	149.25	656.76	194.87	4.00	3.87	-1.01
12,285.00	88.45	2.15	11,647.15	254.09	660.96	299.75	1.23	1.20	-0.27
12,380.00	90.62	3.64	11,647.92	348.95	665.75	394.72	2.77	2.28	1.57
12,475.00	92.63	4.48	11,645.23	443.67	672.48	489.67	2.29	2.12	0.88
12,570.00	91.42	2.35	11,641.87	538.44	678.13	584.60	2.58	-1.27	-2.24
12,665.00	91.67	1.13	11,639.31	633.36	681.02	679.49	1.31	0.26	-1.28
12,760.00	91.26	359.61	11,636.88	728.32	681.63	774.26	1.66	-0.43	-1.60
12,854.00	89.13	358.84	11,636.56	822.30	680.36	867.93	2.41	-2.27	-0.82
12,949.00	88.64	359.49	11,638.41	917.28	678.97	962.57	0.86	-0.52	0.68
13,044.00	89.99	0.09	11,639.54	1,012.27	678.62	1,057.30	1.56	1.42	0.63



Phoenix Survey Report



Company:	OXY USA INC.	Local Co-ordinate Reference:	Well Now I Won 25_24 Fed Com 36H
Project:	Eddy County, NM (NAD83-NME)	TVD Reference:	RKB @ 3571.00usft (Citadel 3)
Site:	Now I Won 25_24	MD Reference:	RKB @ 3571.00usft (Citadel 3)
Well:	Now I Won 25_24 Fed Com 36H	North Reference:	Grid
Wellbore:	OH / 74283	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Citadel 3)	Database:	USAEDMDB

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
13,139.00	89.79	0.07	11,639.73	1,107.26	678.76	1,152.08	0.21	-0.21	-0.02
13,234.00	89.78	2.38	11,640.08	1,202.24	680.79	1,246.96	2.43	-0.01	2.43
13,329.00	89.42	4.56	11,640.75	1,297.05	686.54	1,341.95	2.33	-0.38	2.29
13,424.00	89.61	7.79	11,641.55	1,391.49	696.75	1,436.86	3.41	0.20	3.40
13,518.00	90.52	7.51	11,641.44	1,484.65	709.27	1,530.67	1.01	0.97	-0.30
13,613.00	92.01	6.66	11,639.35	1,578.90	720.98	1,625.51	1.81	1.57	-0.89
13,708.00	92.43	3.76	11,635.67	1,673.42	729.60	1,720.41	3.08	0.44	-3.05
13,803.00	91.95	0.73	11,632.04	1,768.27	733.32	1,815.28	3.23	-0.51	-3.19
13,898.00	91.70	0.61	11,629.01	1,863.21	734.43	1,910.07	0.29	-0.26	-0.13
13,993.00	91.59	0.47	11,626.28	1,958.17	735.32	2,004.86	0.19	-0.12	-0.15
14,088.00	91.60	359.51	11,623.64	2,053.13	735.31	2,099.59	1.01	0.01	-1.01
14,183.00	92.17	359.71	11,620.51	2,148.08	734.66	2,194.25	0.64	0.60	0.21
14,277.00	92.36	0.25	11,616.80	2,242.01	734.63	2,287.95	0.61	0.20	0.57
14,372.00	91.76	359.45	11,613.38	2,336.94	734.38	2,382.63	1.05	-0.63	-0.84
14,467.00	91.56	359.12	11,610.63	2,431.90	733.20	2,477.27	0.41	-0.21	-0.35
14,562.00	90.89	357.41	11,608.60	2,526.83	730.32	2,571.77	1.93	-0.71	-1.80
14,657.00	89.59	358.54	11,608.20	2,621.76	726.96	2,666.23	1.81	-1.37	1.19
14,752.00	89.96	356.91	11,608.58	2,716.68	723.19	2,760.66	1.76	0.39	-1.72
14,847.00	89.47	358.36	11,609.05	2,811.60	719.27	2,855.07	1.61	-0.52	1.53
14,942.00	89.18	358.43	11,610.17	2,906.55	716.61	2,949.60	0.31	-0.31	0.07
15,037.00	89.66	358.06	11,611.13	3,001.50	713.70	3,044.12	0.64	0.51	-0.39
15,132.00	89.66	357.85	11,611.69	3,096.44	710.31	3,138.58	0.22	0.00	-0.22
15,227.00	89.51	358.24	11,612.38	3,191.38	707.07	3,233.06	0.44	-0.16	0.41
15,321.00	89.46	358.15	11,613.23	3,285.33	704.11	3,326.58	0.11	-0.05	-0.10
15,416.00	89.58	357.79	11,614.02	3,380.27	700.75	3,421.04	0.40	0.13	-0.38
15,511.00	91.08	358.96	11,613.47	3,475.23	698.05	3,515.58	2.00	1.58	1.23
15,606.00	91.03	358.75	11,611.73	3,570.19	696.15	3,610.18	0.23	-0.05	-0.22
15,701.00	90.45	0.17	11,610.50	3,665.18	695.26	3,704.87	1.61	-0.61	1.49
15,796.00	91.17	0.80	11,609.16	3,760.16	696.06	3,799.68	1.01	0.76	0.66
15,891.00	91.02	0.55	11,607.34	3,855.14	697.18	3,894.50	0.31	-0.16	-0.26
15,986.00	91.29	0.58	11,605.43	3,950.11	698.12	3,989.30	0.29	0.28	0.03
16,080.00	91.62	359.97	11,603.04	4,044.08	698.57	4,083.07	0.74	0.35	-0.65
16,175.00	91.25	0.22	11,600.66	4,139.05	698.73	4,177.82	0.47	-0.39	0.26
16,270.00	91.00	0.38	11,598.79	4,234.03	699.22	4,272.60	0.31	-0.26	0.17
16,365.00	91.20	1.14	11,596.97	4,329.01	700.48	4,367.43	0.83	0.21	0.80
16,460.00	91.04	0.44	11,595.11	4,423.98	701.79	4,462.26	0.76	-0.17	-0.74
16,555.00	91.30	0.47	11,593.17	4,518.96	702.55	4,557.06	0.28	0.27	0.03
16,649.00	91.11	0.43	11,591.20	4,612.93	703.29	4,650.86	0.21	-0.20	-0.04
16,677.81	91.12	0.55	11,590.64	4,641.73	703.53	4,679.61	0.42	0.04	0.42
SL: 16677.81' MD, 91.12° Inc									
16,744.00	91.15	0.83	11,589.32	4,707.91	704.33	4,745.67	0.42	0.04	0.42
16,839.00	90.34	0.57	11,588.09	4,802.89	705.49	4,840.50	0.90	-0.85	-0.27
16,934.00	90.21	0.65	11,587.63	4,897.88	706.50	4,935.34	0.16	-0.14	0.08
17,029.00	90.30	0.52	11,587.21	4,992.88	707.47	5,030.16	0.17	0.09	-0.14



Phoenix Survey Report



Company:	OXY USA INC.	Local Co-ordinate Reference:	Well Now I Won 25_24 Fed Com 36H
Project:	Eddy County, NM (NAD83-NME)	TVD Reference:	RKB @ 3571.00usft (Citadel 3)
Site:	Now I Won 25_24	MD Reference:	RKB @ 3571.00usft (Citadel 3)
Well:	Now I Won 25_24 Fed Com 36H	North Reference:	Grid
Wellbore:	OH / 74283	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Citadel 3)	Database:	USAEDMDB

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
17,124.00	90.35	0.78	11,586.67	5,087.87	708.55	5,125.00	0.28	0.05	0.27
17,219.00	90.33	0.84	11,586.11	5,182.86	709.89	5,219.85	0.07	-0.02	0.06
17,313.00	90.19	0.19	11,585.68	5,276.85	710.74	5,313.67	0.71	-0.15	-0.69
17,408.00	90.40	359.79	11,585.19	5,371.85	710.72	5,408.44	0.48	0.22	-0.42
17,503.00	90.69	359.87	11,584.29	5,466.85	710.44	5,503.18	0.32	0.31	0.08
17,598.00	90.41	358.98	11,583.38	5,561.84	709.49	5,597.87	0.98	-0.29	-0.94
17,693.00	90.50	359.17	11,582.62	5,656.82	707.95	5,692.51	0.22	0.09	0.20
17,788.00	90.14	358.29	11,582.09	5,751.80	705.85	5,787.11	1.00	-0.38	-0.93
17,882.00	90.45	357.90	11,581.61	5,845.74	702.72	5,880.60	0.53	0.33	-0.41
17,977.00	90.70	359.80	11,580.65	5,940.71	700.82	5,975.21	2.02	0.26	2.00
18,072.00	89.78	358.36	11,580.26	6,035.70	699.29	6,069.85	1.80	-0.97	-1.52
18,167.00	90.30	358.07	11,580.19	6,130.65	696.33	6,164.36	0.63	0.55	-0.31
18,262.00	90.14	0.00	11,579.82	6,225.63	694.73	6,259.00	2.04	-0.17	2.03
18,357.00	90.71	359.19	11,579.12	6,320.63	694.06	6,353.71	1.04	0.60	-0.85
18,452.00	90.40	357.92	11,578.20	6,415.59	691.66	6,448.28	1.38	-0.33	-1.34
18,547.00	90.09	358.50	11,577.79	6,510.54	688.70	6,542.79	0.69	-0.33	0.61
18,642.00	90.60	358.43	11,577.22	6,605.51	686.15	6,637.34	0.54	0.54	-0.07
18,737.00	89.88	358.67	11,576.82	6,700.47	683.75	6,731.91	0.80	-0.76	0.25
18,831.00	90.39	358.13	11,576.60	6,794.44	681.12	6,825.45	0.79	0.54	-0.57
18,926.00	90.49	359.49	11,575.87	6,889.41	679.15	6,920.06	1.44	0.11	1.43
19,021.00	90.49	359.69	11,575.06	6,984.41	678.47	7,014.77	0.21	0.00	0.21
19,116.00	90.29	0.53	11,574.41	7,079.40	678.65	7,109.55	0.91	-0.21	0.88
19,211.00	90.61	359.84	11,573.67	7,174.40	678.96	7,204.33	0.80	0.34	-0.73
19,306.00	90.41	359.98	11,572.82	7,269.39	678.81	7,299.08	0.26	-0.21	0.15
19,401.00	90.63	359.47	11,571.96	7,364.39	678.35	7,393.81	0.58	0.23	-0.54
19,496.00	90.79	359.77	11,570.78	7,459.38	677.72	7,488.53	0.36	0.17	0.32
19,590.00	90.14	0.70	11,570.02	7,553.37	678.11	7,582.32	1.21	-0.69	0.99
19,685.00	90.52	0.88	11,569.47	7,648.36	679.42	7,677.16	0.44	0.40	0.19
19,780.00	90.29	1.19	11,568.80	7,743.34	681.14	7,772.03	0.41	-0.24	0.33
19,875.00	90.03	1.14	11,568.53	7,838.32	683.07	7,866.92	0.28	-0.27	-0.05
19,970.00	90.40	0.41	11,568.18	7,933.31	684.35	7,961.76	0.86	0.39	-0.77
20,065.00	90.04	1.16	11,567.81	8,028.30	685.65	8,056.61	0.88	-0.38	0.79
20,160.00	90.27	0.89	11,567.56	8,123.29	687.35	8,151.48	0.37	0.24	-0.28
20,254.00	90.43	0.93	11,566.98	8,217.27	688.85	8,245.34	0.18	0.17	0.04
20,349.00	90.42	0.88	11,566.28	8,312.26	690.35	8,340.20	0.05	-0.01	-0.05
20,444.00	90.20	1.10	11,565.76	8,407.24	691.99	8,435.06	0.33	-0.23	0.23
20,539.00	90.77	0.69	11,564.96	8,502.23	693.47	8,529.92	0.74	0.60	-0.43
20,634.00	90.39	2.75	11,564.00	8,597.18	696.32	8,624.83	2.20	-0.40	2.17
20,729.00	90.46	1.44	11,563.29	8,692.11	699.80	8,719.77	1.38	0.07	-1.38
20,824.00	91.04	359.62	11,562.05	8,787.09	700.67	8,814.59	2.01	0.61	-1.92
20,919.00	90.35	358.07	11,560.90	8,882.06	698.76	8,909.19	1.79	-0.73	-1.63
21,013.00	90.50	359.18	11,560.20	8,976.03	696.50	9,002.77	1.19	0.16	1.18
21,108.00	89.23	358.09	11,560.42	9,071.00	694.24	9,097.35	1.76	-1.34	-1.15



Company:	OXY USA INC.	Local Co-ordinate Reference:	Well Now I Won 25_24 Fed Com 36H
Project:	Eddy County, NM (NAD83-NME)	TVD Reference:	RKB @ 3571.00usft (Citadel 3)
Site:	Now I Won 25_24	MD Reference:	RKB @ 3571.00usft (Citadel 3)
Well:	Now I Won 25_24 Fed Com 36H	North Reference:	Grid
Wellbore:	OH / 74283	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Citadel 3)	Database:	USAEDMDB

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
21,203.00	89.44	357.91	11,561.53	9,165.94	690.93	9,191.82	0.29	0.22	-0.19
21,298.00	88.70	359.22	11,563.07	9,260.89	688.55	9,286.37	1.58	-0.78	1.38
21,393.00	89.50	0.84	11,564.56	9,355.87	688.60	9,381.13	1.90	0.84	1.71
21,488.00	89.58	0.66	11,565.32	9,450.86	689.84	9,475.97	0.21	0.08	-0.19
21,583.00	89.64	0.49	11,565.97	9,545.86	690.79	9,570.80	0.19	0.06	-0.18
21,677.00	89.31	0.95	11,566.83	9,639.84	691.98	9,664.64	0.60	-0.35	0.49
21,740.00	89.51	0.49	11,567.48	9,702.84	692.77	9,727.53	0.80	0.32	-0.73
Final Phoenix MWD Survey									
21,857.00	89.51	0.49	11,568.48	9,819.83	693.77	9,844.30	0.00	0.00	0.00
Projection to TD									

Design Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
1,031.00	1,030.99	-0.21	0.57	Tie In
1,170.00	1,169.98	-1.24	-0.43	First Phoenix MWD Survey
11,330.06	11,259.76	-550.78	708.79	FTP: 11330.06' MD, 23.51° Inc
16,677.81	11,590.64	4,641.73	703.53	SL: 16677.81' MD, 91.12° Inc
21,740.00	11,567.48	9,702.84	692.77	Final Phoenix MWD Survey
21,857.00	11,568.48	9,819.83	693.77	Projection to TD

C-105 Submit Electronically Via OCD Permitting	State of New Mexico Energy, Minerals & Natural Resources Department OIL CONSERVATION DIVISION	Revised July 9, 2024
--	---	----------------------

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

Section 1 - Operator and Well Information

Submittal Type: ☒ New Well ☐ Workover ☐ Deepening ☐ Plugback ☐ Different Reservoir ☐ C-144 Closure Attachment ☐ Other	
Operator Name: OXY USA INC	OGRID: 16696
Property Name and Well Number: OLIVE WON UNIT 136H	Property Code: 336102
Mineral Owner: ☐ State ☐ Fee ☐ Tribal ☒ Federal	API Number: 30-0 15-54756
Pool Name: Livingston Ridge; Bone Spring	Pool Code: 39350

Section 2 – Well Location

	UI or lot no.	Section	Township	Range	Lot Id	Feet from	N/S Line	Feet from	E/W Line	County
SHL:	P	25	22S	31E		652'	S	1087'	E	EDDY
BHL	A	24	22S	31E		102'	N	332'	E	EDDY

Section 3 – Completion Information

Date T.D. Reached 05/08/24	Total Measured Depth of Well 21857'MD	Acid Volume (bbls)	☒ Directional Survey Submitted ☐ Deviation Survey Submitted
Date Rig Released 05/12/24	Plug-Back Measured Depth 21812'MD	Completion Fluid Used (bbls) 347817	Were Logs Ran (Y/N) Y
Completion Date 06/24/24	Perforations (MD and TVD) 11779-21733'MD/11563-11567'TVD	Completion Proppant Used (lbs) 24921260#	List Type of Logs Ran if applicable: CBL

Section 4 – Action IDs for Submissions and Order Numbers

Surface Casing Action ID: 374744	UIC Permit/Order (UIC wells only) ☐ Yes ☒ No, Order No.
Intermediate 1 Casing Action ID: 374744	NOI Recomplete Action ID (if applicable):
Intermediate 2 Casing Action ID: NA	NOI Plugback Action ID (if applicable):
Production Casing Action ID: 374744	Cement Squeeze Action ID (if applicable):
Tubing Action ID: 382894	All casing was pressure tested in accordance with NMAC ☒ Yes ☐ No
Liner 1 Action ID: NA	Casing was installed prior to Action ID system (Y/N): N

Section 5 – Test Data

Date First Production 06/27/24	Production Method Gas lift	Well Status Producing	Gas – Oil Ratio 1720
Date of Test 07/13/24	Choke Size 53	Flowing Tubing Pressure	Casing Pressure 922
24 hr Oil (bbls) 1773	24 hr Gas (MCF) 3049	24 hr Water (bbls) 6352	Oil Gravity - API
Disposition of Gas: sold			

Section 6 – Pits


☐ A temporary pit was used at the well. If so, attach a plat with the location of the temporary pit.
☒ A Closed Loop System was used.
☐ If an on-site burial was used at the well, report the exact location of the on-site burial: LAT: _____ LONG: _____

Section 7 - Operator Signature and Certification

☒ I hereby certify that the required Water Use Report has been, or will be, submitted for this well’s completion.	
☒ I hereby certify that the required Fracfocus disclosure has been, or will be, submitted for this well’s completion.	
☒ I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief.	
Name Jana Mendiola	<i>Jana Mendiola</i>
Title Regulatory Advisor	Date 09/12/24

South Formations				North Formations			
Formation/Zone	MD	TVD	W/O/G	Formation/Zone	MD	TVD	W/O/G
T. Anhy	851'	851'	W	T. San Jose			
T. Salt	1128'	1128'		T. Nacimiento			
B. Salt	3193'	3192'		T. Ojo Alamo			
T. Yates				T. Kirtland			
T. 7 Rivers				T. Fruitland			
T. Queen				T. Pictured Cliffs			
T. Grayburg				T. Lewis Shale			
T. San Andres				T. Chacra			
T. Glorieta				T. Cliff House			
T. Yeso				T. Menefee			
T. Paddock				T. Point Lookout			
T. Blinebry				T. Mancos			
T.Tubb				T. Gallup			
T. Drinkard				T. Greenhorn			
T. Abo				T. Graneros			
T. Wolfcamp				T. Dakota			
T. Penn				T. Morrison			
T. Cisco				T. Bluff			
T. Canyon				T.Todilto			
T. Strawn				T. Entrada			
T. Atoka				T. Wingate			
T. Morrow				T. Chinle			
T. Barnett Shale				T. Permian			
T. Miss				T. Penn A"			
T. Woodford Shale				T. Penn. "B"			
T. Devonian				T. Penn. "C"			
T. Silurian				T. Penn. "D"			
T. Fusselman				T. Leadville			
T. Montoya				T. Madison			
T. Simpson				T. Elbert			
T. McKee				T. McCracken			
T. Waddell				T. Ignacio Otzte			
T. Connel				T. Granite			
T. Ellenburger				T. Hermosa			
T. Gr. Wash				T. De Chelly			
T. Delaware Sand				T. Pinkerton			
T. Lamar Lime	4558'	4556'	o/g				
T. Bell Canyon	4600'	4598'	o/g				
T. Cherry Canyon	5467'	5461'	o/g				
T. Brushy Canyon	6655'	6637'	o/g				
T. Bone Springs	8462'	8414'	o/g				
T. 1st BS Sand	9549'	9491'	o/g				
T. 2nd BS Carbonate							
T. 2nd BS Sand	10263'	10201'	o/g				
T. 3rd BS Carbonate							
T. 3rd BS Sand	11332'	11262'	o/g				

OXY USA Inc.
OLIVE WON UNIT 136H
API No. 30-015-54756

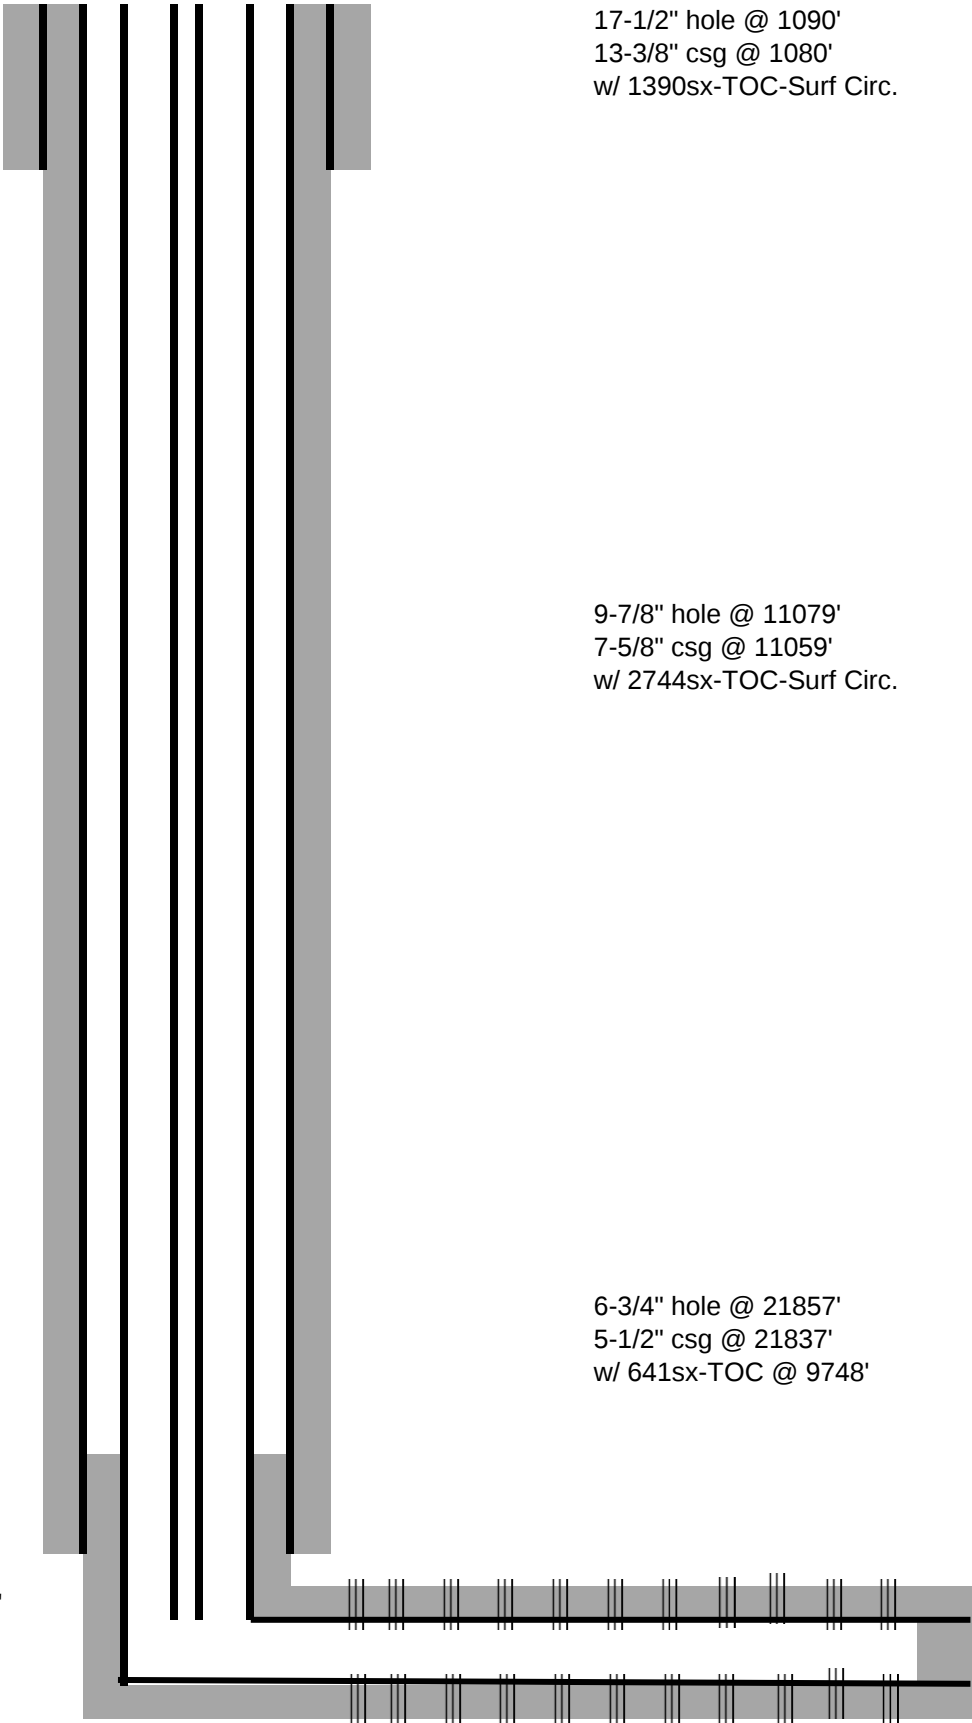

17-1/2" hole @ 1090'
13-3/8" csg @ 1080'
w/ 1390sx-TOC-Surf Circ.

9-7/8" hole @ 11079'
7-5/8" csg @ 11059'
w/ 2744sx-TOC-Surf Circ.

6-3/4" hole @ 21857'
5-1/2" csg @ 21837'
w/ 641sx-TOC @ 9748'

2-3/8" tbg & gas lift @ 11417'

Perfs @ 11779-21733' TD- 21857'M 11568'V

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/ocd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

ACKNOWLEDGMENTS

Action 383263

ACKNOWLEDGMENTS

Operator: OXY USA INC P.O. Box 4294 Houston, TX 772104294	OGRID: 16696
	Action Number: 383263
	Action Type: [C-104] Completion Packet - New Well (C-104NW)

ACKNOWLEDGMENTS

☒	I hereby certify that the required Water Use Report has been, or will be, submitted for this wells completion.
☒	I hereby certify that the required FracFocus disclosure has been, or will be, submitted for this wells completion.
☒	I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief.

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/oed/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 383263

CONDITIONS

Operator: OXY USA INC P.O. Box 4294 Houston, TX 772104294	OGRID: 16696
	Action Number: 383263
	Action Type: [C-104] Completion Packet - New Well (C-104NW)

CONDITIONS

Created By	Condition	Condition Date
plmartinez	File 3160-4 within 10 days of BLM Approval.	12/3/2024
