

Form 3160-3  
(June 2015)FORM APPROVED  
OMB No. 1004-0137  
Expires: January 31, 2018UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT  
**APPLICATION FOR PERMIT TO DRILL OR REENTER**

1a. Type of work: <input type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No.
1b. Type of Well: <input type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other		6. If Indian, Allottee or Tribe Name
1c. Type of Completion: <input type="checkbox"/> Hydraulic Fracturing <input type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		7. If Unit or CA Agreement, Name and No.
2. Name of Operator		8. Lease Name and Well No.
3a. Address	3b. Phone No. (include area code)	9. API Well No.
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		10. Field and Pool, or Exploratory
14. Distance in miles and direction from nearest town or post office*		11. Sec., T. R. M. or Blk. and Survey or Area
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)		12. County or Parish
16. No of acres in lease		13. State
17. Spacing Unit dedicated to this well		
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.		
19. Proposed Depth		
20. BLM/BIA Bond No. in file		
21. Elevations (Show whether DF, KDB, RT, GL, etc.)		
22. Approximate date work will start*		
23. Estimated duration		
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- |  |   |
|--|---|
| 1. Well plat certified by a registered surveyor.   | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan.  | 5. Operator certification.  |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be requested by the BLM.            |

25. Signature	Name (Printed/Typed)	Date
Title		
Approved by (Signature)	Name (Printed/Typed)	Date
Title		
Office		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.  
Conditions of approval, if any, are attached.



Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)


\*(Instructions on page 2)



Approval Date: 12/10/2024

C-102 Submit Electronically Via OCD Permitting	State of New Mexico Energy, Minerals & Natural Resources Department OIL CONSERVATION DIVISION					Revised July 9, 2024			
						Submittal Type:	<input checked="" type="checkbox"/> Initial Submittal		
							<input type="checkbox"/> Amended Report		
<input type="checkbox"/> As Drilled									
<b>WELL LOCATION INFORMATION</b>									
API Number <b>30-025-54116</b>		Pool Code <b>41442</b>		Pool Name <b>LUSK;BONE SPRING, EAST</b>					
Property Code <b>336580</b>		Property Name <b>GRAYLING 14 FED COM</b>					Well Number <b>#505H</b>		
OGRID No. <b>330396</b>		Operator Name <b>AVANT OPERATING, LLC</b>					Ground Level Elevation <b>3624'</b>		
Surface Owner: <input type="checkbox"/> State <input type="checkbox"/> Fee <input type="checkbox"/> Tribal <input checked="" type="checkbox"/> Federal					Mineral Owner: <input type="checkbox"/> State <input type="checkbox"/> Fee <input type="checkbox"/> Tribal <input checked="" type="checkbox"/> Federal				
<b>Surface Location</b>									
UL O	Section 14	Township 19 S	Range 32 E	Lot	Ft. from N/S 914' FSL	Ft. from E/W 1463' FEL	Latitude 32.655611°	Longitude -103.733056°	County LEA
<b>Bottom Hole Location</b>									
UL A	Section 11	Township 19 S	Range 32 E	Lot	Ft. from N/S 100' FNL	Ft. from E/W 1254' FEL	Latitude 32.681859°	Longitude -103.732434°	County LEA
Dedicated Acres 1280.00		Infill or Defining Well Infill		Defining Well API		Overlapping Spacing Unit (Y/N) No		Consolidation Code	
Order Numbers. <b>R-24254 Pending Approval</b>					Well setbacks are under Common Ownership: <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No				
<b>Kick Off Point (KOP)</b>									
UL O	Section 14	Township 19 S	Range 32 E	Lot	Ft. from N/S 914' FSL	Ft. from E/W 1463' FEL	Latitude 32.655611°	Longitude -103.733056°	County LEA
<b>First Take Point (FTP)</b>									
UL P	Section 14	Township 19 S	Range 32 E	Lot	Ft. from N/S 100' FSL	Ft. from E/W 1254' FEL	Latitude 32.653372°	Longitude -103.732372°	County LEA
<b>Last Take Point (LTP)</b>									
UL A	Section 11	Township 19 S	Range 32 E	Lot	Ft. from N/S 100' FNL	Ft. from E/W 1254' FEL	Latitude 32.681859°	Longitude -103.732434°	County LEA
Unitized Area or Area of Uniform Interest				Spacing Unit Type <input checked="" type="checkbox"/> Horizontal <input type="checkbox"/> Vertical			Ground Floor Elevation: 3624'		
<b>OPERATOR CERTIFICATIONS</b> <i>I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and, if the well is a vertical or directional well, that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of a working interest or unleased mineral interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.</i>  <i>If this well is a horizontal well, I further certify that this organization has received the consent of at least one lessee or owner of a working interest or unleased mineral interest in each tract (in the target pool or formation) in which any part of the well's completed interval will be located or obtained a compulsory pooling order from the division.</i>					<b>SURVEYOR CERTIFICATIONS</b> <i>I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.</i>				
 Signature					 Signature and Seal of Professional Surveyor				
Date 12/11/2024					23203      OCTOBER 11, 2024				
Printed Name Meghan Twele					Certificate Number				
Email Address mtwele@outlook.com					Date of Survey				

Note: No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

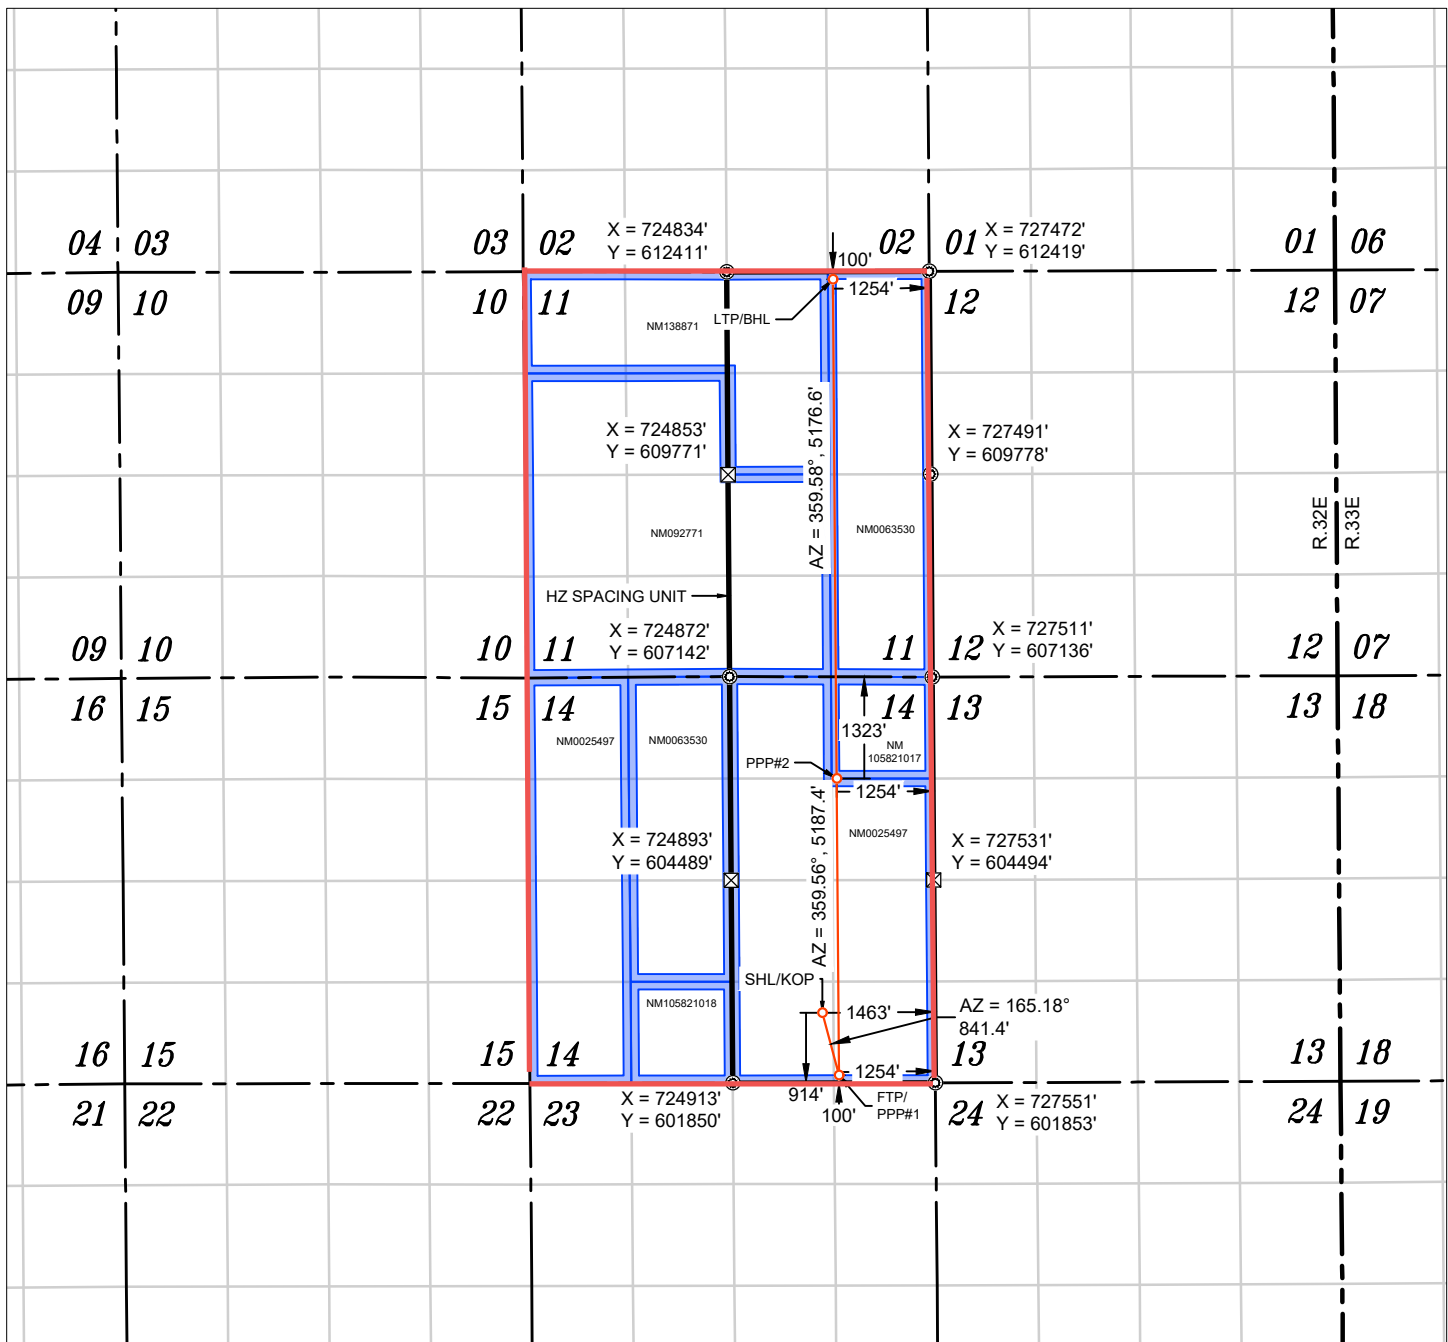

WELL NAME: GRAYLING 14 FED COM #505H  
ELEVATION: 3624'


NAD 83 (SHL/KOP) 914' FSL & 1463' FEL
LATITUDE = 32.655611°
LONGITUDE = -103.733056°
NAD 27 (SHL/KOP)
LATITUDE = 32.655490°
LONGITUDE = -103.732557°
STATE PLANE NAD 83 (N.M. EAST)
N: 602764.60' E: 726081.41'
STATE PLANE NAD 27 (N.M. EAST)
N: 602701.62' E: 684901.85'

NAD 83 (FTP/PPP#1) 100' FSL & 1254' FEL
LATITUDE = 32.653372°
LONGITUDE = -103.732372°
NAD 27 (FTP/PPP#1)
LATITUDE = 32.653251°
LONGITUDE = -103.731873°
STATE PLANE NAD 83 (N.M. EAST)
N: 601951.19' E: 726296.62'
STATE PLANE NAD 27 (N.M. EAST)
N: 601888.23' E: 685117.03'

APPROXIMATE WELL BORE DISTANCE FROM FTP TO LTP	
NM0025497	3864.05'
NM105821017	1323.35'
NM0063530	5176.64'
TOTAL	10364.04'


NAD 83 (PPP#2) 1323' FNL & 1254' FEL
LATITUDE = 32.663993°
LONGITUDE = -103.732397°
NAD 27 (PPP#2)
LATITUDE = 32.663872°
LONGITUDE = -103.731897°
STATE PLANE NAD 83 (N.M. EAST)
N: 605815.13' E: 726267.08'
STATE PLANE NAD 27 (N.M. EAST)
N: 605752.07' E: 685087.60'

NAD 83 (LTP/BHL) 100' FNL & 1254' FEL
LATITUDE = 32.681859°
LONGITUDE = -103.732434°
NAD 27 (LTP/BHL)
LATITUDE = 32.681738°
LONGITUDE = -103.731934°
STATE PLANE NAD 83 (N.M. EAST)
N: 612314.94' E: 726218.79'
STATE PLANE NAD 27 (N.M. EAST)
N: 612251.72' E: 685039.49'



## NOTES

1. ALL COORDINATES, BEARINGS, AND DISTANCES CONTAINED HEREIN ARE GRID, BASED UPON THE NEW MEXICO STATE PLANE COORDINATES SYSTEM, NORTH AMERICAN DATUM 83, NEW MEXICO EAST (3001).
2. THIS DOCUMENT IS BASED UPON AN ON THE GROUND SURVEY PERFORMED DURING OCTOBER, 2024. CERTIFICATION OF THIS DOCUMENT IS ONLY TO THE LOCATION OF THIS EASEMENT IN RELATION TO RECORDED MONUMENT OF DEEDS PROVIDED BY THE CLIENT.
3. ELEVATIONS MSL, DERIVED FROM G.N.S.S. OBSERVATION AND DERIVED FROM SAID ON-THE-GROUND SURVEY.



State of New Mexico  
Energy, Minerals and Natural Resources Department

Submit Electronically  
Via E-permitting

Oil Conservation Division  
1220 South St. Francis Dr.  
Santa Fe, NM 87505

## NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

### Section 1 – Plan Description

Effective May 25, 2021

**I. Operator:** Avant Operating, LLC    **OGRID:** 330396    **Date:** 07/15/2024

**II. Type:** ☒ Original   ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: \_\_\_\_\_

**III. Well(s):** Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
Grayling 14 Fed Com 204H		P-14-T19S-R32E	1120FSL/1243FEL	1250 BBL/D	2300 MCF/D	7000 BBL/D
Grayling 14 Fed Com 205H		P-14-T19S-R32E	1105FSL/1231FEL	1250 BBL/D	2300 MCF/D	7000 BBL/D
Grayling 14 Fed Com 206H		P-14-T19S-R32E	1089FSL/1218FEL	1250 BBL/D	2300 MCF/D	7000 BBL/D
Grayling 14 Fed Com 304H		O-14-T19S-R32E	1025FSL/1359FEL	950 BBL/D	1900 MCF/D	5000 BBL/D
Grayling 14 Fed Com 305H		O-14-T19S-R32E	1009FSL/1347FEL	950 BBL/D	1900 MCF/D	5000 BBL/D
Grayling 14 Fed Com 306H		O-14-T19S-R32E	994FSL/1334FEL	950 BBL/D	1900 MCF/D	5000 BBL/D
Grayling 14 Fed Com 504H		O-14-T19S-R32E	929FSL/1476FEL	1400 BBL/D	2800 MCF/D	7000 BBL/D
Grayling 14 Fed Com 505H		O-14-T19S-R32E	914FSL/1463FEL	1400 BBL/D	2800 MCF/D	7000 BBL/D
Grayling 14 Fed Com 506H		O-14-T19S-R32E	898FSL/1450FEL	1400 BBL/D	2800 MCF/D	7000 BBL/D
Grayling 14 Fed Com 604H		O-14-T19S-R32E	833FSL/1592FEL	1300 BBL/D	2600 MCF/D	7000 BBL/D
Grayling 14 Fed Com 605H		O-14-T19S-R32E	818FSL/1579FEL	1300 BBL/D	2600 MCF/D	7000 BBL/D
Grayling 14 Fed Com 606H		O-14-T19S-R32E	803FSL/1567FEL	1300 BBL/D	2600 MCF/D	7000 BBL/D

**IV. Central Delivery Point Name:** Grayling CTB [See 19.15.27.9(D)(1) NMAC]

**V. Anticipated Schedule:** Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Grayling 14 Fed Com 204H		12/15/2024	01/26/2025	02/01/2025	03/26/2025	03/26/2025
Grayling 14 Fed Com 205H		12/15/2024	01/26/2025	02/01/2025	03/26/2025	03/26/2025
Grayling 14 Fed Com 206H		12/15/2024	01/26/2025	02/01/2025	03/26/2025	03/26/2025
Grayling 14 Fed Com 304H		12/15/2024	01/26/2025	02/01/2025	03/26/2025	03/26/2025
Grayling 14 Fed Com 305H		12/15/2024	01/26/2025	02/01/2025	03/26/2025	03/26/2025
Grayling 14 Fed Com 306H		12/15/2024	01/26/2025	02/01/2025	03/26/2025	03/26/2025
Grayling 14 Fed Com 504H		12/15/2024	01/26/2025	02/01/2025	03/26/2025	03/26/2025
Grayling 14 Fed Com 505H		12/15/2024	01/26/2025	02/01/2025	03/26/2025	03/26/2025
Grayling 14 Fed Com 506H		12/15/2024	01/26/2025	02/01/2025	03/26/2025	03/26/2025
Grayling 14 Fed Com 604H		12/15/2024	01/26/2025	02/01/2025	03/26/2025	03/26/2025
Grayling 14 Fed Com 605H		12/15/2024	01/26/2025	02/01/2025	03/26/2025	03/26/2025
Grayling 14 Fed Com 606H		12/15/2024	01/26/2025	02/01/2025	03/26/2025	03/26/2025

**VI. Separation Equipment:** ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

**VII. Operational Practices:** ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

**VIII. Best Management Practices:** ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

### **Section 3 - Certifications**

**Effective May 25, 2021**

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

***If Operator checks this box, Operator will select one of the following:***

**Well Shut-In.** ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

**Venting and Flaring Plan.** ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

### **Section 4 - Notices**


1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature: 
Printed Name: John Harper
Title: SVP Assets and Exploration
E-mail Address: John@avantnr.com
Date: 07/15/24
Phone: 678-988-6644
<b>OIL CONSERVATION DIVISION</b> <b>(Only applicable when submitted as a standalone form)</b>
Approved By:
Title:
Approval Date:
Conditions of Approval:

**Avant Operating, LLC Natural Gas Management Plan**

- VI. Separation equipment will be sized by construction engineering staff based on stated manufacturer daily throughput capacities and anticipated daily production rates to ensure adequate capacity. Closed vent system piping, compression needs, and VRUs will be sized utilizing ProMax modelling software to ensure adequate capacity for anticipated production volumes and conditions.
- VII. Avant Operating, LLC (Avant) will take the following actions to comply with the regulations listed in 19.15.27.8:
- A. Avant will maximize the recovery of natural gas by minimizing the waste, as defined by 19.15.2 NMAC, of natural gas through venting and flaring. Avant will ensure that well(s) will be connected to a natural gas gathering system with sufficient capacity to transport natural gas.
  - B. All drilling operations will be equipped with a rig flare located at least 100' from the nearest surface hole. Rig flare will be utilized to combust any natural gas that is brought to surface during normal drilling operations. In the case of emergency venting or flaring the volumes will be estimated and reported appropriately.
  - C. During completion operations any natural gas brought to surface will be flared. Immediately following the finish of completion operations, all well flowback will be directed to permanent separation equipment. Produced natural gas from separation equipment will be sent to sales. It is not anticipated that gas will not meet pipeline standards. However, if natural gas does not meet gathering pipeline quality specifications, Avant will flare the natural gas for 60 days or until the natural gas meets the pipeline quality specifications. Avant will ensure that the flare is sized properly and is equipped with automatic igniter or continuous pilot. The gas sample will be analyzed twice per week and the gas will be routed into a gathering system as soon as pipeline specifications are met.
  - D. Avant will comply with the performance standards requirements and provisions listed in 19.15.27.8 (1) through (8). All equipment will be designed and sized to handle maximum anticipated pressures and throughputs to minimize the waste. Production storage tanks constructed after May 25, 2021, will be equipped with automatic gauging system. Flares constructed after May 25, 2021, will be equipped with automatic igniter or continuous pilot. Flares will be located at least 100' from the well and storage tanks unless otherwise approved by the division. Avant will conduct AVO inspections as described in 19.15.27.8 E (5) (a) with frequencies specified in 19.15.27.8 E (5) (b) and (c). All emergencies will be resolved as quickly and safely as feasible to minimize waste.
  - E. The volume of natural gas that is vented or flared as the result of malfunction or emergency during drilling and completions operations will be estimated. The volume of natural gas that is vented, flared, or beneficially used during production operations, will be measured, or estimated. Avant will install equipment to measure



U.S. Department of the Interior  
BUREAU OF LAND MANAGEMENT

# Drilling Plan Data Report

12/11/2024

APD ID: 10400096963

Submission Date: 02/05/2024

Highlighted data  
reflects the most  
recent changes

Operator Name: AVANT OPERATING LLC

Well Name: GRAYLING 14 FED COM

Well Number: 505H

Well Type: OIL WELL

Well Work Type: Drill

[Show Final Text](#)

## Section 1 - Geologic Formations

Formation ID	Formation Name	Elevation	True Vertical	Measured Depth	Lithologies	Mineral Resources	Producing Formatio
14653652	QUATERNARY	3624	0	0	OTHER : Caliche	USEABLE WATER	N
14653653	RUSTLER ANHYDRITE	2497	1127	1127	ANHYDRITE	NONE	N
14653655	SALADO	2194	1430	1430	SALT	NONE	N
14653654	YATES	824	2800	2805	SANDSTONE	NATURAL GAS, OIL	N
14653663	CAPITAN REEF	74	3550	3561	LIMESTONE	USEABLE WATER	N
14653656	CHERRY CANYON	-2251	5875	5907	SANDSTONE	NATURAL GAS, OIL	N
14653661	BRUSHY CANYON	-2833	6457	6494	SANDSTONE	NATURAL GAS, OIL	N
14653658	BONE SPRING	-3876	7500	7546	SANDSTONE	NATURAL GAS, OIL	N
14653664	FIRST BONE SPRING SAND	-5059	8683	8739	SANDSTONE	NATURAL GAS, OIL	N
14653651	BONE SPRING 2ND	-5803	9427	9510	SANDSTONE	NATURAL GAS, OIL	Y

## Section 2 - Blowout Prevention

Pressure Rating (PSI): 5M

Rating Depth: 15000

**Equipment:** A minimum 5M system will be used. The minimum blowout preventer equipment (BOPE) shown in BOP Diagram will consist of a single ram, mud cross and double ram-type (10,000 psi WP) preventer, and an annular preventer (5000-psi WP). Both units will be hydraulically operated, and the ram-type will be equipped with blind rams on bottom and drill pipe rams on top. All BOPE will be tested in accordance with Onshore Oil & Gas Order 2.

Requesting Variance? YES

**Variance request:** Variance is requested to use a co-flex line between the BOP and choke manifold (instead of using a 4" OD steel line). Co-flex line will be tested in accordance with highest BOP test pressures (5000 psi) before drilling out of surface casing and (5000 psi) before drilling out of intermediate casing. Pressure tests will be charted for records. The manufacturers hydrostatic test report will be kept on location for inspection.

Operator Name: AVANT OPERATING LLC

Well Name: GRAYLING 14 FED COM

Well Number: 505H

**Testing Procedure:** Before drilling out of the surface casing, the ram-type BOP and accessory equipment will be tested to 5000 (high) / 250 (low) psig and the annular preventer to 3500 (high) / 250 (low) psig by an independent service company. Test charts will always be kept on site. Surface casing will be tested to 1500 psi for 30 minutes. Before drilling out of the intermediate casing, the ram-type BOP and accessory equipment will be tested to 5000 (high) / 250 (low) psig and the annular preventer to 3500 (high) / 250 (low) psig by an independent service company. Test charts will always be kept on site. Intermediate casing will be tested to 1500 psi for 30 minutes. A solid steel body pack-off will be used after running and cementing the intermediate casing. After installation, pack-off and lower flange will be pressure tested to 5000 psi. Pipe rams will be operationally checked each 24-hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. A hydraulically operated choke will be installed prior to drilling out of the intermediate casing shoe. This pressure test will be repeated at least once every 30 days, as per Onshore Order 2. Kelly cock will always be kept in the drill string. Full opening drill pipe stabbing valve (inside BOP) with proper drill pipe connections will always be kept on the rig floor. The multi-bowl wellhead will be installed by a third-party welder while being monitored by the vendors representative. All BOP equipment will be tested using a conventional test plug - not a cup or J-packer type. Both the surface and intermediate casing strings will be tested as per Onshore Order 2 to at least 0.22 psi/ft or 1500 psi, whichever is greater.

**Choke Diagram Attachment:**

5M\_Choke\_Diagram\_20240130141108.pdf

**BOP Diagram Attachment:**

5M\_BOP\_Diagram\_20240130141112.pdf

Section 3 - Casing

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE	17.5	13.375	NEW	API	N	0	1152	0	1152	3624	2472	1152	J-55	54.5	LT&C	1.125	1.125	DRY	1.6	DRY	1.6
2	INTERMEDIATE	12.25	9.625	NEW	API	N	0	5503	0	5475	3640	-1851	5503	J-55	40	LT&C	1.125	1.125	DRY	1.6	DRY	1.6
3	PRODUCTION	8.75	5.5	NEW	NON API	N	0	19863	0	9600	3679	-5976	19863	HCP-110	20	OTHER - GBCD	1.125	1.125	DRY	1.6	DRY	1.6

Casing Attachments

Operator Name: AVANT OPERATING LLC

Well Name: GRAYLING 14 FED COM

Well Number: 505H

Casing Attachments

Casing ID: 1	String	SURFACE
Inspection Document:		
Spec Document:		
Tapered String Spec:		
Casing Design Assumptions and Worksheet(s):		
Grayling_Pad_3_Casing_Design_Assumptions_20240202092130.pdf		
Casing ID: 2	String	INTERMEDIATE
Inspection Document:		
Spec Document:		
Tapered String Spec:		
Casing Design Assumptions and Worksheet(s):		
Grayling_Pad_3_Casing_Design_Assumptions_20240130152438.pdf		
Casing ID: 3	String	PRODUCTION
Inspection Document:		
Spec Document:		
5.5_Casing_Specs_20240130152531.pdf		
Tapered String Spec:		
Casing Design Assumptions and Worksheet(s):		
Grayling_Pad_3_Casing_Design_Assumptions_20240202092117.pdf		

Section 4 - Cement

Operator Name: AVANT OPERATING LLC

Well Name: GRAYLING 14 FED COM

Well Number: 505H

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
SURFACE	Lead		0	1152	470	1.9	12.8	893	50	35% B_POZ & 65% Class C	6% Gel+5% SALT+0.25PPS Pol-E-Flake+0.005GPS
SURFACE	Tail		852	1152	215	1.33	14.8	286	20	Class C	1% CaCl2+0.005GPS NoFoam V1A
INTERMEDIATE	Lead		0	5503	1045	1.9	12.8	1985	50	35% Class B Poz + 65% Class C	6% Gel+5% SALT+0.3% R-1300+0.005GPS
INTERMEDIATE	Tail		4476	5503	300	1.36	14.8	408	20	Class C	5% SALT+0.005GPS NoFoam V1A
PRODUCTION	Lead		0	1986 3	840	3.38	10.7	2839	50	100% ProLite	5PPS Plexcrete STE+2% SMS+0.65% R-1300+0.2% FL-24+3PPS Gilsonite+0.005GPS NoFoam V1A
PRODUCTION	Tail		9179	1986 3	2685	1.21	14.5	3249	20	50% B_POZ & 50% Class H	5% SALT+0.05% RCKCAS-100+0.75% R-1201+0.5% FL-24+0.005GPS NoFoam V1A

### Section 5 - Circulating Medium

Mud System Type: Closed

Will an air or gas system be Used? NO

Description of the equipment for the circulating system in accordance with Onshore Order #2:

Diagram of the equipment for the circulating system in accordance with Onshore Order #2:

**Describe what will be on location to control well or mitigate other conditions:** Sufficient mud materials (e. g., barite, bentonite, LCM) to maintain mud properties and meet minimum lost circulation and weight increase requirements will always be kept on site.

**Describe the mud monitoring system utilized:** An electronic pit volume totalizer (PVT) mud system will monitor pit volumes for gains or losses, flow rate, pump pressures, and stroke rate.

### Circulating Medium Table

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
-----------	--------------	----------	----------------------	----------------------	---------------------	-----------------------------	----	----------------	----------------	-----------------	----------------------------

**Operator Name:** AVANT OPERATING LLC**Well Name:** GRAYLING 14 FED COM**Well Number:** 505H

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
0	1152	OTHER : Fresh Water	8.4	10.1							
1152	5503	OTHER : Brine	10	10.5							
5503	9179	OTHER : Cut Brine	9.2	9.5							
9179	9929	OTHER : Cut Brine	9.5	9.5							
9929	1986 3	OIL-BASED MUD	9.5	9.8							

## Section 6 - Test, Logging, Coring

**List of production tests including testing procedures, equipment and safety measures:**

GR log will be acquired by MWD tools throughout the well.

**List of open and cased hole logs run in the well:**

GAMMA RAY LOG,

**Coring operation description for the well:**

No core or open hole or cased hole log is planned

## Section 7 - Pressure

**Anticipated Bottom Hole Pressure:** 4608

**Anticipated Surface Pressure:** 2496

**Anticipated Bottom Hole Temperature(F):** 171

**Anticipated abnormal pressures, temperatures, or potential geologic hazards?** NO

**Describe:**

**Contingency Plans geohazards description:**

**Contingency Plans geohazards**

**Hydrogen Sulfide drilling operations plan required?** YES

**Hydrogen sulfide drilling operations**

Grayling\_Pad\_3\_H2S\_Packet\_20240130141524.pdf

**Operator Name:** AVANT OPERATING LLC**Well Name:** GRAYLING 14 FED COM**Well Number:** 505H**Section 8 - Other Information****Proposed horizontal/directional/multi-lateral plan submission:**

Grayling\_14\_Fed\_Com\_505H\_Plan\_0.1\_Report\_20240202100847.pdf

**Other proposed operations facets description:**

All casing strings below the conductor will be pressure tested to 0.22 psi/ft x casing string length, or 1500 psi, whichever is greater, but not to exceed 70% of the minimum internal yield. If pressure declines more than 10% in 30 minutes, then corrective action will be taken.

**Other proposed operations facets attachment:**

Grayling\_Speedhead\_Specs\_20240130154745.pdf

Avant\_Natural\_Resources\_Grayling\_14\_Fed\_Com\_505H\_240126163912\_A\_Entire\_Well\_No\_Pricing\_20240202100859.pdf

Grayling\_14\_Fed\_Com\_505H\_WBS\_Prelim\_20240202100909.pdf

Grayling\_14\_Fed\_Com\_505H\_Plan\_0.1\_Anti\_Collision\_20240202100917.pdf

Flex\_Line\_Certification\_20240614095435.pdf

Avant\_Natural\_Resources\_3\_String\_Bone\_Spring\_Well\_AES\_VERT\_MP\_20240614095440.pdf


**Other Variance attachment:**

Grayling\_505H\_Casing\_Cementing\_Variance\_20240202100922.pdf

## Choke Manifold Diagram


Avant Natural Resources  
5M BOPE Choke Manifold

1. Cameron 2 1/16" 10,000 PSI WP Gate Valve
2. 4 1/16" 10,000 PSI WP Manual Choke
3. Cameron 4 1/16" 10,000 PSI WP Manual Valve
4. 8" OD x 4" ID 10,000 PSI WP Flex Choke Line
5. Cameron 4 1/16" 10,000 PSI WP Manual Valve & Pressure Gauge on Pressure Block
6. 10,000 PSI WP Hydraulic Choke Valve
7. 8" Expansion Chamber
8. LP Butterfly Valve
9. LP Valve
10. 4" Panic Line
11. 5" Butterfly Valve
12. 10-3/4" Butterfly Valve
13. 6" Butterfly Valve

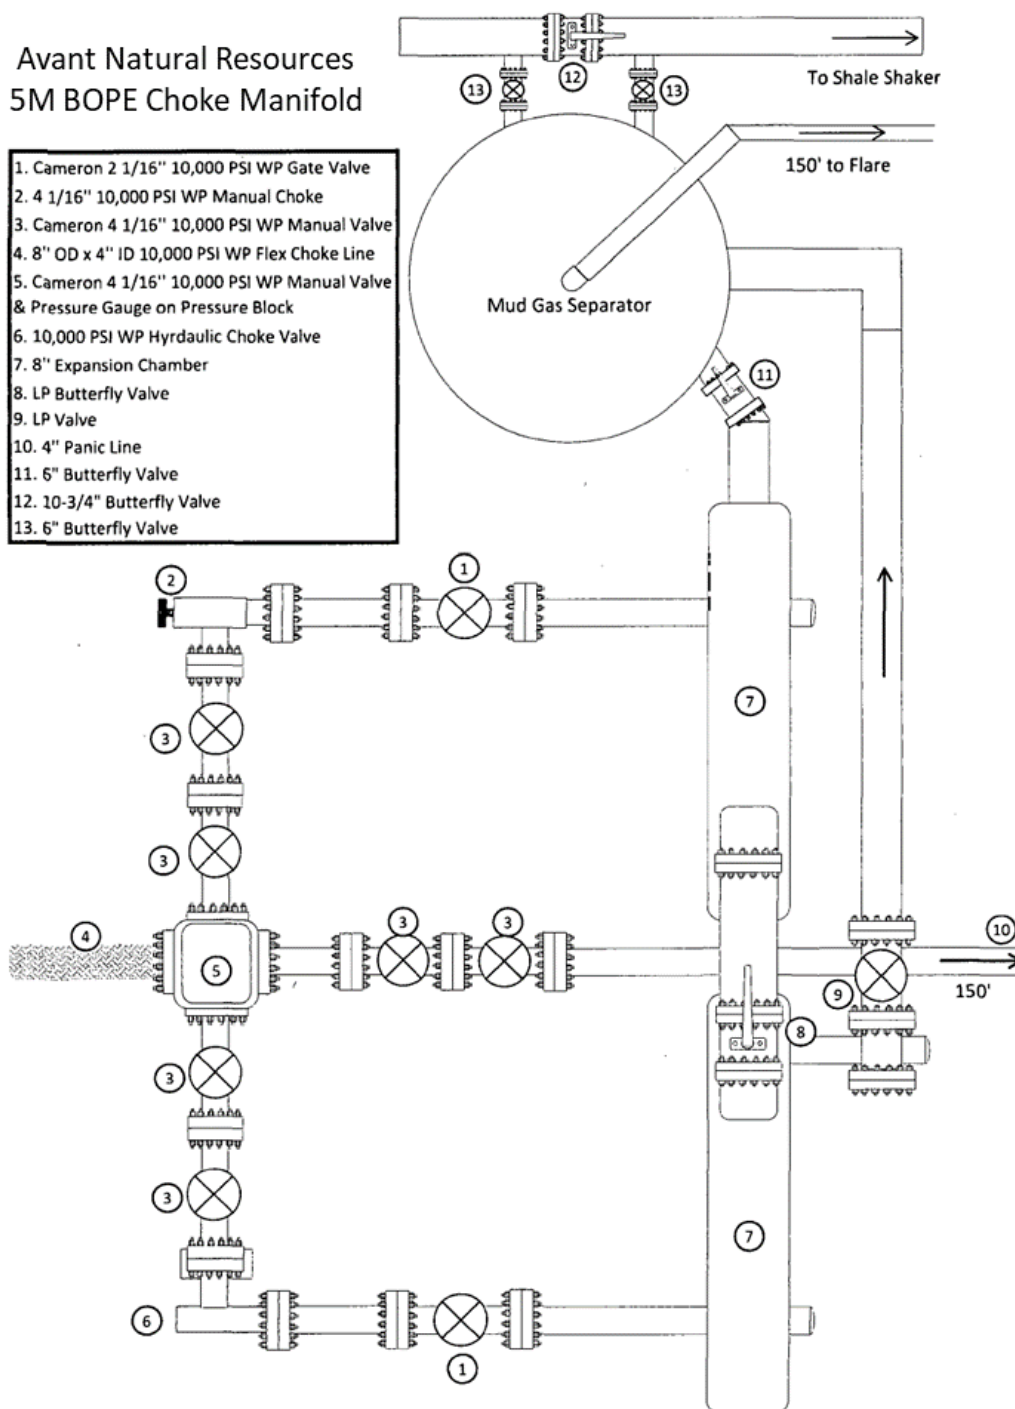

## Avant Natural Resources 5M BOP Diagram

1. 13 5/8" Rotating Head
2. NOV 13 5/8" 5,000 PSI WP GK Annular Preventor
3. 13 5/8" Cameron Type "U" 10,000 PSI WP Ram Preventors
4. 2 1/16" - 10,000 PSI WP Check Valve
5. 10,000 PSI WP - 1502 Union to kill line
6. 2 1/16" - 10,000 PSI WP Manual Valves
7. 13 5/8" 3,000 PSI WP x 13 5/8" 5,000 PSI WP Spacer Spool
8. 4 1/16" 10,000 PSI WP HCR Valve
9. 4 1/16" 10,000 PSI WP Manual Valve
10. 6" OD x 3" ID 10,000 PSI WP Steel Armoured Flex Choke Line
11. DSA - 13 5/8" 10,000 PSI WP x 13 5/8" 5,000 PSI WP
12. Mud Cross - 13 5/8" 10,000 PSI WP
13. Blind Rams
14. Pipe Rams
15. 13 5/8" Cameron Type "U" 10,000 PSI WP Pipe Rams
16. Flow Line
17. 2" Fill Line

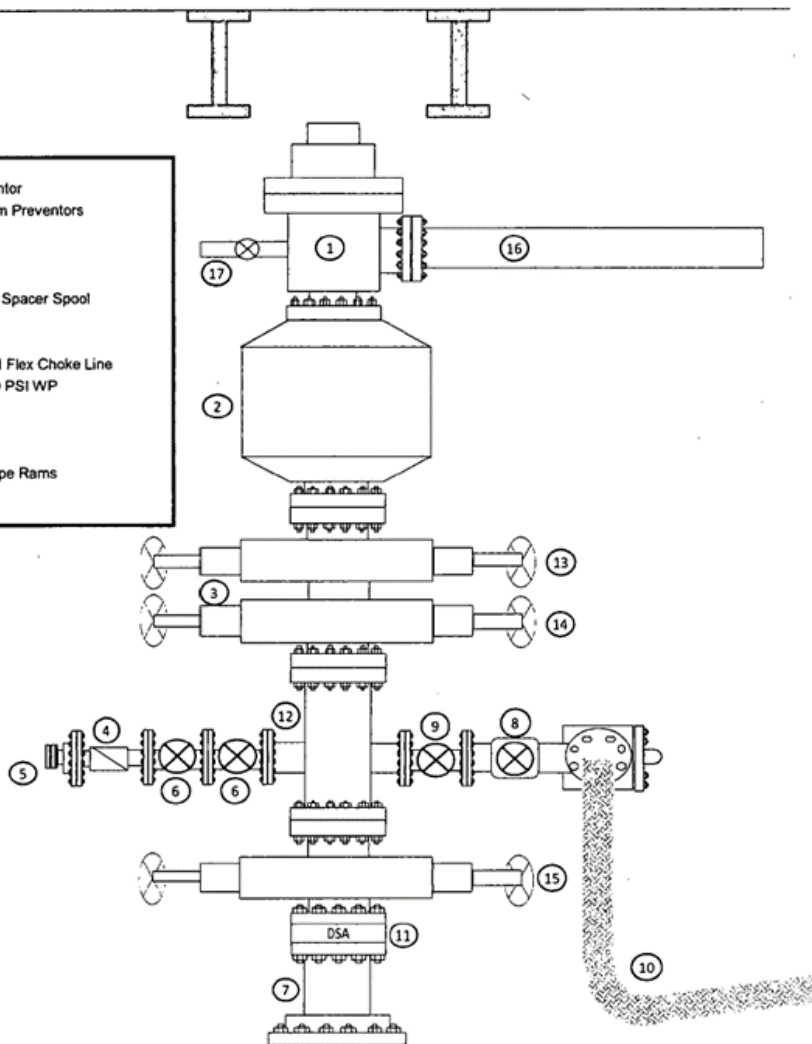



PERFORMANCE  
DATA SHEET

Revised May 2020

5.500" 20.0# IP HCP-110 with GB CD Butt

DIMENSIONAL DATA

Casing OD	5.500 in	Pipe Grade	IP HCP-110
Coupling OD	6.300 in	Coupling Grade	P-110
Pipe Gauge	0.361 in	T&C WPF	20.00 lbs/ft
Drift Diameter	4.653 in	PE WPF	19.83 lbs/ft

MECHANICAL DATA

Pipe IP Yield Minimum	125,000 psi	Collapse Pressure	12,200 psi
Pipe Tensile Minimum	125,000 psi	Pipe Body Internal Yield Pressure	14,360 psi
Coupling Yield Minimum	110,000 psi	Leak at E7 Plane	21,500 psi
Coupling Tensile Minimum	125,000 psi	Pipe Hydrostatic Test @ 80% SMYS	13,100 psi

CONNECTION & PIPE DATA

Thread Name	GB CD Butt	Coupling Thread Fracture Strength	1,013,000 lbs
Joint Strength	685,000 lbs	Pipe Body Plain End Yield	729,000 lbs
Minimum Makeup Torque	10,000 ft-lbs	Pipe Thread Fracture Strength	685,000 lbs
Maximum Make-up Torque	20,000 ft-lbs	Coupling Internal Yield Pressure	16,240 psi
Maximum Operating Torque	33,660 ft-lbs		
Connection Yield Torque	35,440 ft-lbs		

Note:

This document is for general information only. It should not, therefore, be relied upon for any specific application without independent competent professional examination and verification of its accuracy, suitability, and applicability. Anyone making use of this material does so at his own risk and assumes any and all liability resulting from such use. Centric Pipe, LLC disclaims any and all expressed or implied warranties of merchantability and/or fitness for any general or particular purpose.

## CASING DESIGN CRITERIA & LOAD CASE ASSUMPTIONS

### SURFACE CASING:

SIZE (in)	SURFACE CASING	ID (in)	DRIFT (in)	BURST (psi)	COLLAPSE (psi)	TENSION (k-lbs)	JOINT STRENGTH (k-lbs)	DEPTHS
13.375"	54.5# J-55 LTC	12.615	12.459	2740	1130	853	909	0' – SCP

Collapse:  $DF_c = 1.25$

- Full internal evacuation: Collapse force equal to the mud gradient in which the casing will be ran.
- Cementing: Collapse force equal to the gradient of the planned cement slurries to planned depths and an internal force equal to the fluid gradient of displacement fluid.

Burst:  $DF_B = 1.25$

- Pressure Test: Casing test per Onshore Oil and Gas Order No. 2 with an external force equal to the gradient in which the casing will be ran.

Tension:  $DF_T = 1.6$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string, without considering buoyancy.

### INTERMEIDATE CASING:

SIZE (in)	INTERMEDIATE CASING	ID (in)	DRIFT (in)	BURST (psi)	COLLAPSE (psi)	TENSION (k-lbs)	JOINT STRENGTH (k-lbs)	DEPTHS
9-5/8"	40# J-55 LTC	8.835	8.679	3950	2570	630	520	0' – ICP'

Collapse:  $DF_c = 1.25$

- Full Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be ran.
- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and an internal force equal to fluid gradient of displacement fluid.

Burst:  $DF_B = 1.25$

- Pressure Test: Casing test per Onshore Oil and Gas Order No. 2 with an external force equal to the mud gradient in which the casing will be ran.
- Gas Kick Profile: Internal burst force at the shoe will be fracture pressure at that depth. Surface burst pressure will be fracture gradient at setting depth less a gas gradient to equivalent height of 50bbl kick with Drill Pipe inside casing and mud gradient with which the next hole section will be ran above that. External force will be equal to the mud gradient in which the casing will be ran.

- Fracture at Shoe with 1/3 BHP at Surface: Internal burst force at the shoe will be fracture pressure at setting depth. Internal burst force at surface will be 1/3 of pore pressure at setting depth. External force will be equal to the mud gradient in which the casing will be ran.

Tension:  $DF_T = 1.6$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string, without considering buoyancy.

#### PRODUCTION CASING:

SIZE (in)	PRODUCTION CASING	ID (in)	DRIFT (in)	BURST (psi)	COLLAPSE (psi)	TENSION (k-lbs)	JOINT TENSION (k-lbs)	DEPTHS
5-1/2"	20# HCP-110 GBCD	4.778	4.653	12,640	12,200	641	641	0' – 24,000'

Collapse:  $DF_C = 1.25$

- Partial Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be ran. Internal force equal to gas gradient over one-third of setting depth and mud gradient with which the next hole section will be ran below that.
- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and mud gradient in which the casing will be ran above that and an internal force equal to the fluid gradient of displacement fluid.

Burst:  $DF_B = 1.25$

- Pressure Test: 80% of burst casing test with an external force equal to the mud gradient in which the casing will be ran.
- Injection Down Casing: 9800 psi surface injection pressure plus an internal pressure gradient of with an external force equal to the mud gradient in which the casing will be ran.

Tension:  $DF_T = 1.6$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string, without considering buoyancy.

**WELL DETAILS: Grayling 14 Fed Com 505H**


Ground Elev: 3624.0 KB: 3649.5

+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
0.0	0.0	602764.47	726081.50	32.6556110°N	103.7330560°W



**PROJECT DETAILS: Lea Co., NM (NAD 83)**

Geodetic System: US State Plane 1983  
Datum: North American Datum 1983  
Ellipsoid: GRS 1980  
Zone: New Mexico Eastern Zone

System Datum: Mean Sea Level

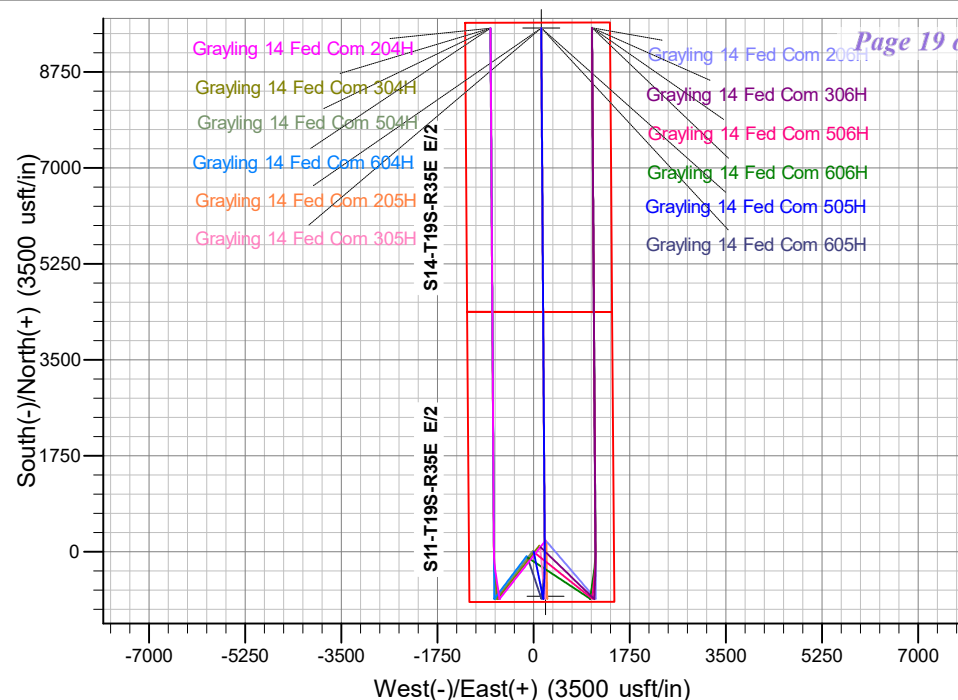**SECTION DETAILS**

Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	Vsect	Annotation
1	0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.0	
2	2000.0	0.00	0.00	2000.0	0.0	0.0	0.00	0.00	0.0	KOP - Start Build 2.00
3	2377.5	7.55	168.50	2376.4	-24.3	5.0	2.00	168.50	-24.3	Start 6301.9 hold at 2377.5 MD
4	8679.3	7.55	168.50	8623.6	-835.7	170.0	0.00	0.00	-833.1	Start Drop -2.00
5	9056.8	0.00	0.00	9000.0	-860.0	175.0	2.00	180.00	-857.4	Start 122.5 hold at 9056.8 MD
6	9179.3	0.00	0.00	9122.5	-860.0	175.0	0.00	0.00	-857.4	KOP #2 - Start Build 12.00
7	9929.3	90.00	2.87	9600.0	-383.1	198.9	12.00	2.87	-380.2	LP - Start 1.1 hold at 9929.3 MD
8	9930.5	90.00	2.87	9600.0	-382.0	199.0	0.00	0.00	-379.1	Start DLS 2.00 TFO -90.00
9	10093.3	90.00	359.62	9600.0	-219.2	202.5	2.00	-90.00	-216.3	Start 9770.0 hold at 10093.3 MD
10	19863.3	90.00	359.62	9600.0	9550.5	137.4	0.00	0.00	9551.5	TD at 19863.3

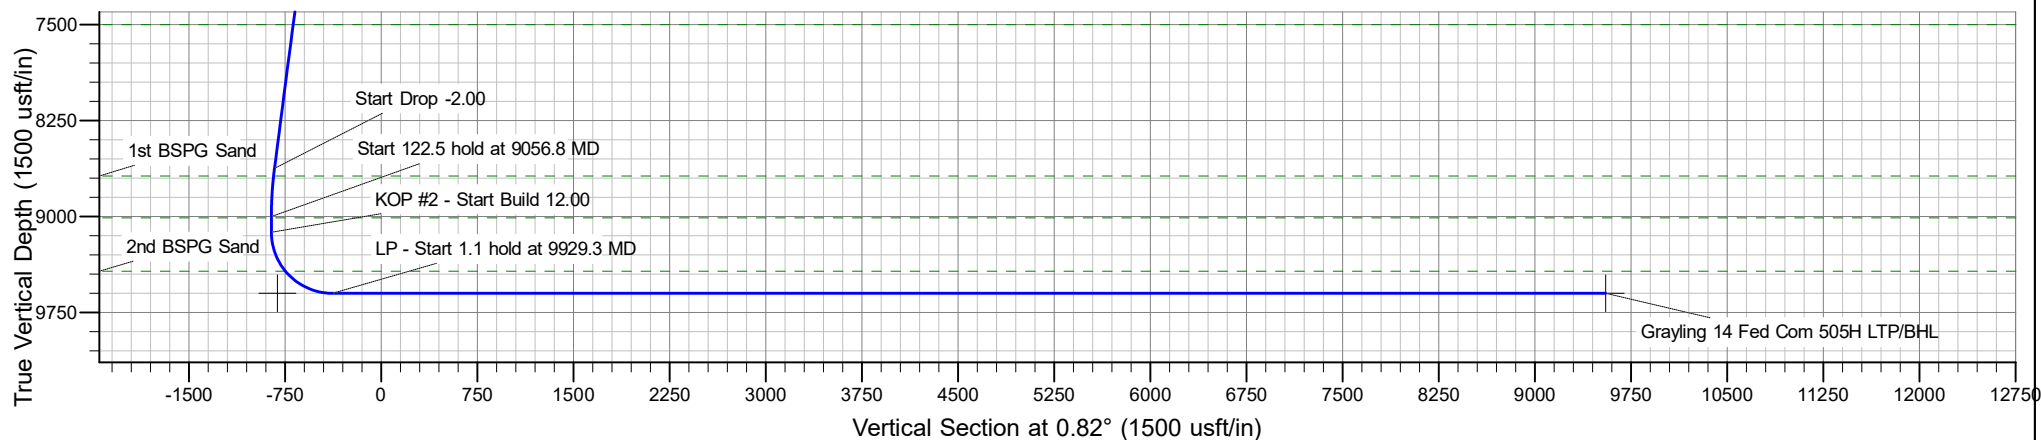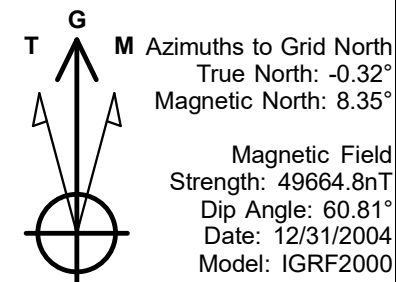



## **Avant Operating, LLC**

**Lea Co., NM (NAD 83)**

**Grayling 14 Fed Com Pad 3**

**Grayling 14 Fed Com 505H**

**OH**

**Plan: Plan 0.1**

## **Standard Planning Report**

**30 January, 2024**





Planning Report



Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Grayling 14 Fed Com 505H
Company:	Avant Operating, LLC	TVD Reference:	WELL @ 3649.5usft (3649.5)
Project:	Lea Co., NM (NAD 83)	MD Reference:	WELL @ 3649.5usft (3649.5)
Site:	Grayling 14 Fed Com Pad 3	North Reference:	Grid
Well:	Grayling 14 Fed Com 505H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 0.1		

Project	Lea Co., NM (NAD 83)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Grayling 14 Fed Com Pad 3		
Site Position:		Northing:	602,875.65 usft
From:	Lat/Long	Easting:	726,183.98 usft
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "
		Latitude:	32.6559150°N
		Longitude:	103.7327210°W

Well	Grayling 14 Fed Com 505H		
Well Position	+N/-S	0.0 usft	Northing:
	+E/-W	0.0 usft	Easting:
Position Uncertainty	0.0 usft	Wellhead Elevation:	
Grid Convergence:	0.32 °		
		Latitude:	32.6556110°N
		Longitude:	103.7330560°W
		Ground Level:	3,624.0 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2000	12/31/2004	8.67	60.81	49,664.81576353

Design	Plan 0.1			
Audit Notes:				
Version:	Phase:	PROTOTYPE	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0	0.0	0.0	0.82

Plan Survey Tool Program	Date	1/30/2024		
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks
1	0.0	19,863.1 Plan 0.1 (OH)	B001Mb_MWD+HRGM	
			OWSG MWD + HRGM	



Planning Report



Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Grayling 14 Fed Com 505H
Company:	Avant Operating, LLC	TVD Reference:	WELL @ 3649.5usft (3649.5)
Project:	Lea Co., NM (NAD 83)	MD Reference:	WELL @ 3649.5usft (3649.5)
Site:	Grayling 14 Fed Com Pad 3	North Reference:	Grid
Well:	Grayling 14 Fed Com 505H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 0.1		

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.00	0.00	0.00	0.00	
2,377.5	7.55	168.50	2,376.4	-24.3	5.0	2.00	2.00	0.00	168.50	
8,679.3	7.55	168.50	8,623.6	-835.7	170.0	0.00	0.00	0.00	0.00	
9,056.8	0.00	0.00	9,000.0	-860.0	175.0	2.00	-2.00	0.00	180.00	
9,179.3	0.00	0.00	9,122.5	-860.0	175.0	0.00	0.00	0.00	0.00	
9,929.3	90.00	2.87	9,600.0	-383.1	198.9	12.00	12.00	0.00	2.87	
9,930.5	90.00	2.87	9,600.0	-382.0	199.0	0.00	0.00	0.00	0.00	
10,093.3	90.00	359.62	9,600.0	-219.2	202.5	2.00	0.00	-2.00	-90.00	
19,863.3	90.00	359.62	9,600.0	9,550.5	137.4	0.00	0.00	0.00	0.00	Grayling 14 Fed Com



## Planning Report



<b>Database:</b>	EDM 5000.16 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Grayling 14 Fed Com 505H
<b>Company:</b>	Avant Operating, LLC	<b>TVD Reference:</b>	WELL @ 3649.5usft (3649.5)
<b>Project:</b>	Lea Co., NM (NAD 83)	<b>MD Reference:</b>	WELL @ 3649.5usft (3649.5)
<b>Site:</b>	Grayling 14 Fed Com Pad 3	<b>North Reference:</b>	Grid
<b>Well:</b>	Grayling 14 Fed Com 505H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	OH		
<b>Design:</b>	Plan 0.1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00
1,127.0	0.00	0.00	1,127.0	0.0	0.0	0.0	0.00	0.00	0.00
<b>Rustler</b>									
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00
1,430.0	0.00	0.00	1,430.0	0.0	0.0	0.0	0.00	0.00	0.00
<b>Solado</b>									
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00
1,600.0	0.00	0.00	1,600.0	0.0	0.0	0.0	0.00	0.00	0.00
1,700.0	0.00	0.00	1,700.0	0.0	0.0	0.0	0.00	0.00	0.00
1,800.0	0.00	0.00	1,800.0	0.0	0.0	0.0	0.00	0.00	0.00
1,900.0	0.00	0.00	1,900.0	0.0	0.0	0.0	0.00	0.00	0.00
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.0	0.00	0.00	0.00
<b>KOP - Start Build 2.00</b>									
2,100.0	2.00	168.50	2,100.0	-1.7	0.3	-1.7	2.00	2.00	0.00
2,200.0	4.00	168.50	2,199.8	-6.8	1.4	-6.8	2.00	2.00	0.00
2,300.0	6.00	168.50	2,299.5	-15.4	3.1	-15.3	2.00	2.00	0.00
2,377.5	7.55	168.50	2,376.4	-24.3	5.0	-24.3	2.00	2.00	0.00
<b>Start 6301.9 hold at 2377.5 MD</b>									
2,400.0	7.55	168.50	2,398.7	-27.2	5.5	-27.2	0.00	0.00	0.00
2,500.0	7.55	168.50	2,497.8	-40.1	8.2	-40.0	0.00	0.00	0.00
2,600.0	7.55	168.50	2,597.0	-53.0	10.8	-52.8	0.00	0.00	0.00
2,700.0	7.55	168.50	2,696.1	-65.9	13.4	-65.7	0.00	0.00	0.00
2,800.0	7.55	168.50	2,795.2	-78.7	16.0	-78.5	0.00	0.00	0.00
2,804.8	7.55	168.50	2,800.0	-79.3	16.1	-79.1	0.00	0.00	0.00
<b>Yates</b>									
2,900.0	7.55	168.50	2,894.4	-91.6	18.6	-91.3	0.00	0.00	0.00
3,000.0	7.55	168.50	2,993.5	-104.5	21.3	-104.2	0.00	0.00	0.00
3,100.0	7.55	168.50	3,092.6	-117.4	23.9	-117.0	0.00	0.00	0.00
3,200.0	7.55	168.50	3,191.8	-130.2	26.5	-129.8	0.00	0.00	0.00
3,300.0	7.55	168.50	3,290.9	-143.1	29.1	-142.7	0.00	0.00	0.00
3,400.0	7.55	168.50	3,390.0	-156.0	31.7	-155.5	0.00	0.00	0.00
3,500.0	7.55	168.50	3,489.2	-168.9	34.4	-168.3	0.00	0.00	0.00
3,561.4	7.55	168.50	3,550.0	-176.8	36.0	-176.2	0.00	0.00	0.00
<b>Capitan Reef</b>									
3,600.0	7.55	168.50	3,588.3	-181.7	37.0	-181.2	0.00	0.00	0.00
3,700.0	7.55	168.50	3,687.4	-194.6	39.6	-194.0	0.00	0.00	0.00
3,800.0	7.55	168.50	3,786.6	-207.5	42.2	-206.8	0.00	0.00	0.00
3,900.0	7.55	168.50	3,885.7	-220.4	44.8	-219.7	0.00	0.00	0.00
4,000.0	7.55	168.50	3,984.8	-233.2	47.5	-232.5	0.00	0.00	0.00
4,100.0	7.55	168.50	4,084.0	-246.1	50.1	-245.4	0.00	0.00	0.00



## Planning Report



<b>Database:</b>	EDM 5000.16 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Grayling 14 Fed Com 505H
<b>Company:</b>	Avant Operating, LLC	<b>TVD Reference:</b>	WELL @ 3649.5usft (3649.5)
<b>Project:</b>	Lea Co., NM (NAD 83)	<b>MD Reference:</b>	WELL @ 3649.5usft (3649.5)
<b>Site:</b>	Grayling 14 Fed Com Pad 3	<b>North Reference:</b>	Grid
<b>Well:</b>	Grayling 14 Fed Com 505H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	OH		
<b>Design:</b>	Plan 0.1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
4,200.0	7.55	168.50	4,183.1	-259.0	52.7	-258.2	0.00	0.00	0.00
4,300.0	7.55	168.50	4,282.2	-271.8	55.3	-271.0	0.00	0.00	0.00
4,400.0	7.55	168.50	4,381.4	-284.7	57.9	-283.9	0.00	0.00	0.00
4,500.0	7.55	168.50	4,480.5	-297.6	60.6	-296.7	0.00	0.00	0.00
4,600.0	7.55	168.50	4,579.6	-310.5	63.2	-309.5	0.00	0.00	0.00
4,700.0	7.55	168.50	4,678.8	-323.3	65.8	-322.4	0.00	0.00	0.00
4,800.0	7.55	168.50	4,777.9	-336.2	68.4	-335.2	0.00	0.00	0.00
4,900.0	7.55	168.50	4,877.0	-349.1	71.0	-348.0	0.00	0.00	0.00
5,000.0	7.55	168.50	4,976.2	-362.0	73.7	-360.9	0.00	0.00	0.00
5,100.0	7.55	168.50	5,075.3	-374.8	76.3	-373.7	0.00	0.00	0.00
5,200.0	7.55	168.50	5,174.4	-387.7	78.9	-386.5	0.00	0.00	0.00
5,300.0	7.55	168.50	5,273.6	-400.6	81.5	-399.4	0.00	0.00	0.00
5,400.0	7.55	168.50	5,372.7	-413.5	84.1	-412.2	0.00	0.00	0.00
5,500.0	7.55	168.50	5,471.8	-426.3	86.8	-425.1	0.00	0.00	0.00
5,600.0	7.55	168.50	5,571.0	-439.2	89.4	-437.9	0.00	0.00	0.00
5,700.0	7.55	168.50	5,670.1	-452.1	92.0	-450.7	0.00	0.00	0.00
5,800.0	7.55	168.50	5,769.2	-465.0	94.6	-463.6	0.00	0.00	0.00
5,900.0	7.55	168.50	5,868.4	-477.8	97.2	-476.4	0.00	0.00	0.00
5,906.7	7.55	168.50	5,875.0	-478.7	97.4	-477.3	0.00	0.00	0.00
Cherry Canyon									
6,000.0	7.55	168.50	5,967.5	-490.7	99.9	-489.2	0.00	0.00	0.00
6,100.0	7.55	168.50	6,066.6	-503.6	102.5	-502.1	0.00	0.00	0.00
6,200.0	7.55	168.50	6,165.8	-516.5	105.1	-514.9	0.00	0.00	0.00
6,300.0	7.55	168.50	6,264.9	-529.3	107.7	-527.7	0.00	0.00	0.00
6,400.0	7.55	168.50	6,364.0	-542.2	110.3	-540.6	0.00	0.00	0.00
6,493.8	7.55	168.50	6,457.0	-554.3	112.8	-552.6	0.00	0.00	0.00
Brushy Canyon									
6,500.0	7.55	168.50	6,463.2	-555.1	113.0	-553.4	0.00	0.00	0.00
6,600.0	7.55	168.50	6,562.3	-568.0	115.6	-566.2	0.00	0.00	0.00
6,700.0	7.55	168.50	6,661.4	-580.8	118.2	-579.1	0.00	0.00	0.00
6,800.0	7.55	168.50	6,760.6	-593.7	120.8	-591.9	0.00	0.00	0.00
6,900.0	7.55	168.50	6,859.7	-606.6	123.4	-604.7	0.00	0.00	0.00
7,000.0	7.55	168.50	6,958.8	-619.5	126.1	-617.6	0.00	0.00	0.00
7,100.0	7.55	168.50	7,058.0	-632.3	128.7	-630.4	0.00	0.00	0.00
7,200.0	7.55	168.50	7,157.1	-645.2	131.3	-643.3	0.00	0.00	0.00
7,300.0	7.55	168.50	7,256.2	-658.1	133.9	-656.1	0.00	0.00	0.00
7,400.0	7.55	168.50	7,355.4	-671.0	136.5	-668.9	0.00	0.00	0.00
7,500.0	7.55	168.50	7,454.5	-683.8	139.2	-681.8	0.00	0.00	0.00
7,545.9	7.55	168.50	7,500.0	-689.7	140.4	-687.7	0.00	0.00	0.00
Bone Spring									
7,600.0	7.55	168.50	7,553.6	-696.7	141.8	-694.6	0.00	0.00	0.00
7,700.0	7.55	168.50	7,652.8	-709.6	144.4	-707.4	0.00	0.00	0.00
7,800.0	7.55	168.50	7,751.9	-722.5	147.0	-720.3	0.00	0.00	0.00
7,900.0	7.55	168.50	7,851.0	-735.3	149.6	-733.1	0.00	0.00	0.00
8,000.0	7.55	168.50	7,950.2	-748.2	152.3	-745.9	0.00	0.00	0.00
8,100.0	7.55	168.50	8,049.3	-761.1	154.9	-758.8	0.00	0.00	0.00
8,200.0	7.55	168.50	8,148.4	-774.0	157.5	-771.6	0.00	0.00	0.00
8,300.0	7.55	168.50	8,247.6	-786.8	160.1	-784.4	0.00	0.00	0.00
8,400.0	7.55	168.50	8,346.7	-799.7	162.7	-797.3	0.00	0.00	0.00
8,500.0	7.55	168.50	8,445.8	-812.6	165.4	-810.1	0.00	0.00	0.00
8,600.0	7.55	168.50	8,545.0	-825.5	168.0	-823.0	0.00	0.00	0.00
8,679.3	7.55	168.50	8,623.6	-835.7	170.0	-833.1	0.00	0.00	0.00
Start Drop -2.00									



## Planning Report



<b>Database:</b>	EDM 5000.16 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Grayling 14 Fed Com 505H
<b>Company:</b>	Avant Operating, LLC	<b>TVD Reference:</b>	WELL @ 3649.5usft (3649.5)
<b>Project:</b>	Lea Co., NM (NAD 83)	<b>MD Reference:</b>	WELL @ 3649.5usft (3649.5)
<b>Site:</b>	Grayling 14 Fed Com Pad 3	<b>North Reference:</b>	Grid
<b>Well:</b>	Grayling 14 Fed Com 505H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	OH		
<b>Design:</b>	Plan 0.1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
8,700.0	7.14	168.50	8,644.1	-838.3	170.6	-835.7	2.00	-2.00	0.00
8,739.2	6.35	168.50	8,683.0	-842.8	171.5	-840.2	2.00	-2.00	0.00
<b>1st BSPG Sand</b>									
8,800.0	5.14	168.50	8,743.5	-848.7	172.7	-846.2	2.00	-2.00	0.00
8,900.0	3.14	168.50	8,843.3	-855.8	174.1	-853.2	2.00	-2.00	0.00
9,000.0	1.14	168.50	8,943.2	-859.4	174.9	-856.8	2.00	-2.00	0.00
9,056.8	0.00	0.00	9,000.0	-860.0	175.0	-857.4	2.00	-2.00	0.00
<b>Start 122.5 hold at 9056.8 MD</b>									
9,066.8	0.00	0.00	9,010.0	-860.0	175.0	-857.4	0.00	0.00	0.00
<b>2nd BSPG Carb</b>									
9,100.0	0.00	0.00	9,043.2	-860.0	175.0	-857.4	0.00	0.00	0.00
9,179.3	0.00	0.00	9,122.5	-860.0	175.0	-857.4	0.00	0.00	0.00
<b>KOP #2 - Start Build 12.00</b>									
9,200.0	2.48	2.87	9,143.2	-859.6	175.0	-856.9	12.00	12.00	0.00
9,300.0	14.48	2.87	9,241.9	-844.9	175.8	-842.2	12.00	12.00	0.00
9,400.0	26.48	2.87	9,335.4	-810.0	177.5	-807.3	12.00	12.00	0.00
9,500.0	38.48	2.87	9,419.6	-756.4	180.2	-753.8	12.00	12.00	0.00
9,509.5	39.62	2.87	9,427.0	-750.5	180.5	-747.8	12.00	12.00	0.00
<b>2nd BSPG Sand</b>									
9,588.6	49.11	2.87	9,483.5	-695.3	183.3	-692.6	12.00	12.00	0.00
<b>Grayling 14 Fed Com 505H FTP</b>									
9,600.0	50.48	2.87	9,490.8	-686.6	183.7	-683.9	12.00	12.00	0.00
9,700.0	62.48	2.87	9,546.0	-603.5	187.9	-600.7	12.00	12.00	0.00
9,800.0	74.48	2.87	9,582.6	-510.7	192.5	-507.9	12.00	12.00	0.00
9,900.0	86.48	2.87	9,599.1	-412.4	197.5	-409.5	12.00	12.00	0.00
9,929.3	90.00	2.87	9,600.0	-383.1	198.9	-380.2	12.00	12.00	0.00
<b>LP - Start 1.1 hold at 9929.3 MD</b>									
9,930.5	90.00	2.87	9,600.0	-382.0	199.0	-379.1	0.00	0.00	0.00
<b>Start DLS 2.00 TFO -90.00</b>									
10,000.0	90.00	1.48	9,600.0	-312.5	201.6	-309.6	2.00	0.00	-2.00
10,093.3	90.00	359.62	9,600.0	-219.2	202.5	-216.3	2.00	0.00	-2.00
<b>Start 9770.0 hold at 10093.3 MD</b>									
10,100.0	90.00	359.62	9,600.0	-212.5	202.5	-209.6	0.00	0.00	0.00
10,200.0	90.00	359.62	9,600.0	-112.5	201.8	-109.6	0.00	0.00	0.00
10,300.0	90.00	359.62	9,600.0	-12.5	201.2	-9.7	0.00	0.00	0.00
10,400.0	90.00	359.62	9,600.0	87.5	200.5	90.3	0.00	0.00	0.00
10,500.0	90.00	359.62	9,600.0	187.4	199.8	190.3	0.00	0.00	0.00
10,600.0	90.00	359.62	9,600.0	287.4	199.2	290.3	0.00	0.00	0.00
10,700.0	90.00	359.62	9,600.0	387.4	198.5	390.3	0.00	0.00	0.00
10,800.0	90.00	359.62	9,600.0	487.4	197.8	490.2	0.00	0.00	0.00
10,900.0	90.00	359.62	9,600.0	587.4	197.2	590.2	0.00	0.00	0.00
11,000.0	90.00	359.62	9,600.0	687.4	196.5	690.2	0.00	0.00	0.00
11,100.0	90.00	359.62	9,600.0	787.4	195.8	790.2	0.00	0.00	0.00
11,200.0	90.00	359.62	9,600.0	887.4	195.2	890.1	0.00	0.00	0.00
11,300.0	90.00	359.62	9,600.0	987.4	194.5	990.1	0.00	0.00	0.00
11,400.0	90.00	359.62	9,600.0	1,087.4	193.8	1,090.1	0.00	0.00	0.00
11,500.0	90.00	359.62	9,600.0	1,187.4	193.2	1,190.1	0.00	0.00	0.00
11,600.0	90.00	359.62	9,600.0	1,287.4	192.5	1,290.1	0.00	0.00	0.00
11,700.0	90.00	359.62	9,600.0	1,387.4	191.8	1,390.0	0.00	0.00	0.00
11,800.0	90.00	359.62	9,600.0	1,487.4	191.2	1,490.0	0.00	0.00	0.00
11,900.0	90.00	359.62	9,600.0	1,587.4	190.5	1,590.0	0.00	0.00	0.00
12,000.0	90.00	359.62	9,600.0	1,687.4	189.8	1,690.0	0.00	0.00	0.00
12,100.0	90.00	359.62	9,600.0	1,787.4	189.2	1,789.9	0.00	0.00	0.00



## Planning Report



<b>Database:</b>	EDM 5000.16 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Grayling 14 Fed Com 505H
<b>Company:</b>	Avant Operating, LLC	<b>TVD Reference:</b>	WELL @ 3649.5usft (3649.5)
<b>Project:</b>	Lea Co., NM (NAD 83)	<b>MD Reference:</b>	WELL @ 3649.5usft (3649.5)
<b>Site:</b>	Grayling 14 Fed Com Pad 3	<b>North Reference:</b>	Grid
<b>Well:</b>	Grayling 14 Fed Com 505H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	OH		
<b>Design:</b>	Plan 0.1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
12,200.0	90.00	359.62	9,600.0	1,887.4	188.5	1,889.9	0.00	0.00	0.00
12,300.0	90.00	359.62	9,600.0	1,987.4	187.8	1,989.9	0.00	0.00	0.00
12,400.0	90.00	359.62	9,600.0	2,087.4	187.2	2,089.9	0.00	0.00	0.00
12,500.0	90.00	359.62	9,600.0	2,187.4	186.5	2,189.9	0.00	0.00	0.00
12,600.0	90.00	359.62	9,600.0	2,287.4	185.8	2,289.8	0.00	0.00	0.00
12,700.0	90.00	359.62	9,600.0	2,387.4	185.2	2,389.8	0.00	0.00	0.00
12,800.0	90.00	359.62	9,600.0	2,487.4	184.5	2,489.8	0.00	0.00	0.00
12,900.0	90.00	359.62	9,600.0	2,587.4	183.8	2,589.8	0.00	0.00	0.00
13,000.0	90.00	359.62	9,600.0	2,687.4	183.2	2,689.7	0.00	0.00	0.00
13,100.0	90.00	359.62	9,600.0	2,787.4	182.5	2,789.7	0.00	0.00	0.00
13,200.0	90.00	359.62	9,600.0	2,887.4	181.8	2,889.7	0.00	0.00	0.00
13,300.0	90.00	359.62	9,600.0	2,987.4	181.2	2,989.7	0.00	0.00	0.00
13,400.0	90.00	359.62	9,600.0	3,087.4	180.5	3,089.7	0.00	0.00	0.00
13,500.0	90.00	359.62	9,600.0	3,187.4	179.8	3,189.6	0.00	0.00	0.00
13,600.0	90.00	359.62	9,600.0	3,287.4	179.1	3,289.6	0.00	0.00	0.00
13,700.0	90.00	359.62	9,600.0	3,387.4	178.5	3,389.6	0.00	0.00	0.00
13,800.0	90.00	359.62	9,600.0	3,487.4	177.8	3,489.6	0.00	0.00	0.00
13,900.0	90.00	359.62	9,600.0	3,587.4	177.1	3,589.5	0.00	0.00	0.00
14,000.0	90.00	359.62	9,600.0	3,687.4	176.5	3,689.5	0.00	0.00	0.00
14,100.0	90.00	359.62	9,600.0	3,787.4	175.8	3,789.5	0.00	0.00	0.00
14,200.0	90.00	359.62	9,600.0	3,887.4	175.1	3,889.5	0.00	0.00	0.00
14,300.0	90.00	359.62	9,600.0	3,987.4	174.5	3,989.5	0.00	0.00	0.00
14,400.0	90.00	359.62	9,600.0	4,087.4	173.8	4,089.4	0.00	0.00	0.00
14,500.0	90.00	359.62	9,600.0	4,187.4	173.1	4,189.4	0.00	0.00	0.00
14,600.0	90.00	359.62	9,600.0	4,287.4	172.5	4,289.4	0.00	0.00	0.00
14,700.0	90.00	359.62	9,600.0	4,387.4	171.8	4,389.4	0.00	0.00	0.00
14,800.0	90.00	359.62	9,600.0	4,487.4	171.1	4,489.4	0.00	0.00	0.00
14,900.0	90.00	359.62	9,600.0	4,587.4	170.5	4,589.3	0.00	0.00	0.00
15,000.0	90.00	359.62	9,600.0	4,687.3	169.8	4,689.3	0.00	0.00	0.00
15,100.0	90.00	359.62	9,600.0	4,787.3	169.1	4,789.3	0.00	0.00	0.00
15,200.0	90.00	359.62	9,600.0	4,887.3	168.5	4,889.3	0.00	0.00	0.00
15,300.0	90.00	359.62	9,600.0	4,987.3	167.8	4,989.2	0.00	0.00	0.00
15,400.0	90.00	359.62	9,600.0	5,087.3	167.1	5,089.2	0.00	0.00	0.00
15,500.0	90.00	359.62	9,600.0	5,187.3	166.5	5,189.2	0.00	0.00	0.00
15,600.0	90.00	359.62	9,600.0	5,287.3	165.8	5,289.2	0.00	0.00	0.00
15,700.0	90.00	359.62	9,600.0	5,387.3	165.1	5,389.2	0.00	0.00	0.00
15,800.0	90.00	359.62	9,600.0	5,487.3	164.5	5,489.1	0.00	0.00	0.00
15,900.0	90.00	359.62	9,600.0	5,587.3	163.8	5,589.1	0.00	0.00	0.00
16,000.0	90.00	359.62	9,600.0	5,687.3	163.1	5,689.1	0.00	0.00	0.00
16,100.0	90.00	359.62	9,600.0	5,787.3	162.5	5,789.1	0.00	0.00	0.00
16,200.0	90.00	359.62	9,600.0	5,887.3	161.8	5,889.0	0.00	0.00	0.00
16,300.0	90.00	359.62	9,600.0	5,987.3	161.1	5,989.0	0.00	0.00	0.00
16,400.0	90.00	359.62	9,600.0	6,087.3	160.5	6,089.0	0.00	0.00	0.00
16,500.0	90.00	359.62	9,600.0	6,187.3	159.8	6,189.0	0.00	0.00	0.00
16,600.0	90.00	359.62	9,600.0	6,287.3	159.1	6,289.0	0.00	0.00	0.00
16,700.0	90.00	359.62	9,600.0	6,387.3	158.5	6,388.9	0.00	0.00	0.00
16,800.0	90.00	359.62	9,600.0	6,487.3	157.8	6,488.9	0.00	0.00	0.00
16,900.0	90.00	359.62	9,600.0	6,587.3	157.1	6,588.9	0.00	0.00	0.00
17,000.0	90.00	359.62	9,600.0	6,687.3	156.5	6,688.9	0.00	0.00	0.00
17,100.0	90.00	359.62	9,600.0	6,787.3	155.8	6,788.8	0.00	0.00	0.00
17,200.0	90.00	359.62	9,600.0	6,887.3	155.1	6,888.8	0.00	0.00	0.00
17,300.0	90.00	359.62	9,600.0	6,987.3	154.5	6,988.8	0.00	0.00	0.00
17,400.0	90.00	359.62	9,600.0	7,087.3	153.8	7,088.8	0.00	0.00	0.00
17,500.0	90.00	359.62	9,600.0	7,187.3	153.1	7,188.8	0.00	0.00	0.00



Planning Report



Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Grayling 14 Fed Com 505H
Company:	Avant Operating, LLC	TVD Reference:	WELL @ 3649.5usft (3649.5)
Project:	Lea Co., NM (NAD 83)	MD Reference:	WELL @ 3649.5usft (3649.5)
Site:	Grayling 14 Fed Com Pad 3	North Reference:	Grid
Well:	Grayling 14 Fed Com 505H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 0.1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
17,600.0	90.00	359.62	9,600.0	7,287.3	152.5	7,288.7	0.00	0.00	0.00	
17,700.0	90.00	359.62	9,600.0	7,387.3	151.8	7,388.7	0.00	0.00	0.00	
17,800.0	90.00	359.62	9,600.0	7,487.3	151.1	7,488.7	0.00	0.00	0.00	
17,900.0	90.00	359.62	9,600.0	7,587.3	150.5	7,588.7	0.00	0.00	0.00	
18,000.0	90.00	359.62	9,600.0	7,687.3	149.8	7,688.6	0.00	0.00	0.00	
18,100.0	90.00	359.62	9,600.0	7,787.3	149.1	7,788.6	0.00	0.00	0.00	
18,200.0	90.00	359.62	9,600.0	7,887.3	148.5	7,888.6	0.00	0.00	0.00	
18,300.0	90.00	359.62	9,600.0	7,987.3	147.8	7,988.6	0.00	0.00	0.00	
18,400.0	90.00	359.62	9,600.0	8,087.3	147.1	8,088.6	0.00	0.00	0.00	
18,500.0	90.00	359.62	9,600.0	8,187.3	146.5	8,188.5	0.00	0.00	0.00	
18,600.0	90.00	359.62	9,600.0	8,287.3	145.8	8,288.5	0.00	0.00	0.00	
18,700.0	90.00	359.62	9,600.0	8,387.3	145.1	8,388.5	0.00	0.00	0.00	
18,800.0	90.00	359.62	9,600.0	8,487.3	144.5	8,488.5	0.00	0.00	0.00	
18,900.0	90.00	359.62	9,600.0	8,587.3	143.8	8,588.4	0.00	0.00	0.00	
19,000.0	90.00	359.62	9,600.0	8,687.3	143.1	8,688.4	0.00	0.00	0.00	
19,100.0	90.00	359.62	9,600.0	8,787.3	142.5	8,788.4	0.00	0.00	0.00	
19,200.0	90.00	359.62	9,600.0	8,887.3	141.8	8,888.4	0.00	0.00	0.00	
19,300.0	90.00	359.62	9,600.0	8,987.3	141.1	8,988.4	0.00	0.00	0.00	
19,400.0	90.00	359.62	9,600.0	9,087.3	140.5	9,088.3	0.00	0.00	0.00	
19,500.0	90.00	359.62	9,600.0	9,187.2	139.8	9,188.3	0.00	0.00	0.00	
19,600.0	90.00	359.62	9,600.0	9,287.2	139.1	9,288.3	0.00	0.00	0.00	
19,700.0	90.00	359.62	9,600.0	9,387.2	138.5	9,388.3	0.00	0.00	0.00	
19,800.0	90.00	359.62	9,600.0	9,487.2	137.8	9,488.2	0.00	0.00	0.00	
19,863.3	90.00	359.62	9,600.0	9,550.5	137.4	9,551.5	0.00	0.00	0.00	
TD at 19863.3 - Grayling 14 Fed Com 505H LTP/BHL										

Design Targets										
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude	
- hit/miss target										
- Shape										
Grayling 14 Fed Com 5C	0.00	0.00	9,600.0	9,550.5	137.4	612,314.97	726,218.87	32.6818590°N	103.7324340°W	
- plan hits target center										
- Point										
Grayling 14 Fed Com 5C	0.00	0.00	9,600.0	-813.4	215.1	601,951.08	726,296.62	32.6533720°N	103.7323720°W	
- plan misses target center by 168.9usft at 9588.6usft MD (9483.5 TVD, -695.3 N, 183.3 E)										
- Point										



## Planning Report



<b>Database:</b>	EDM 5000.16 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Grayling 14 Fed Com 505H
<b>Company:</b>	Avant Operating, LLC	<b>TVD Reference:</b>	WELL @ 3649.5usft (3649.5)
<b>Project:</b>	Lea Co., NM (NAD 83)	<b>MD Reference:</b>	WELL @ 3649.5usft (3649.5)
<b>Site:</b>	Grayling 14 Fed Com Pad 3	<b>North Reference:</b>	Grid
<b>Well:</b>	Grayling 14 Fed Com 505H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	OH		
<b>Design:</b>	Plan 0.1		

Formations						
Measured Depth (usft)	Vertical Depth (usft)	Name	Lithology	Dip (°)	Dip Direction (°)	
1,127.0	1,127.0	Rustler				
1,430.0	1,430.0	Solado				
2,804.8	2,800.0	Yates				
3,561.4	3,550.0	Capitan Reef				
5,906.7	5,875.0	Cherry Canyon				
6,493.8	6,457.0	Brushy Canyon				
7,545.9	7,500.0	Bone Spring				
8,739.2	8,683.0	1st BSPG Sand				
9,066.8	9,010.0	2nd BSPG Carb				
9,509.5	9,427.0	2nd BSPG Sand				

Plan Annotations					
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates			
		+N/-S (usft)	+E/-W (usft)	Comment	
2,000.0	2,000.0	0.0	0.0	KOP - Start Build 2.00	
2,377.5	2,376.4	-24.3	5.0	Start 6301.9 hold at 2377.5 MD	
8,679.3	8,623.6	-835.7	170.0	Start Drop -2.00	
9,056.8	9,000.0	-860.0	175.0	Start 122.5 hold at 9056.8 MD	
9,179.3	9,122.5	-860.0	175.0	KOP #2 - Start Build 12.00	
9,929.3	9,600.0	-383.1	198.9	LP - Start 1.1 hold at 9929.3 MD	
9,930.5	9,600.0	-382.0	199.0	Start DLS 2.00 TFO -90.00	
10,093.3	9,600.0	-219.2	202.5	Start 9770.0 hold at 10093.3 MD	
19,863.3	9,600.0	9,550.5	137.4	TD at 19863.3	

**PECOS DISTRICT  
DRILLING CONDITIONS OF APPROVAL**

<b>OPERATOR'S NAME:</b>	Avant Operating LLC
<b>LEASE NO.:</b>	NMNM025497
<b>LOCATION:</b>	Section 14, T.19 S., R.32 E., NMPM
<b>COUNTY:</b>	Lea County, New Mexico ▼

<b>WELL NAME &amp; NO.:</b>	Grayling 14 Fed Com 201H
<b>BOTTOM HOLE FOOTAGE</b>	100'/N & 330'/W
<b>ATS/API ID:</b>	ATS-24-995
<b>APD ID:</b>	10400097547
<b>Sundry ID:</b>	N/a
<b>Date APD Submitted:</b>	N/a

<b>WELL NAME &amp; NO.:</b>	Grayling 14 Fed Com 202H
<b>BOTTOM HOLE FOOTAGE</b>	100'/N & 1254'/W
<b>ATS/API ID:</b>	ATS-24-1300
<b>APD ID:</b>	10400097802
<b>Sundry ID:</b>	N/a
<b>Date APD Submitted:</b>	N/a

<b>WELL NAME &amp; NO.:</b>	Grayling 14 Fed Com 204H
<b>BOTTOM HOLE FOOTAGE</b>	100'/N & 2178'/E
<b>ATS/API ID:</b>	ATS-24-835
<b>APD ID:</b>	10400096908
<b>Sundry ID:</b>	N/a
<b>Date APD Submitted:</b>	N/a

<b>WELL NAME &amp; NO.:</b>	Grayling 14 Fed Com 205H
<b>BOTTOM HOLE FOOTAGE</b>	100'/N & 1254'/E
<b>ATS/API ID:</b>	ATS-24-836
<b>APD ID:</b>	10400096950
<b>Sundry ID:</b>	N/a
<b>Date APD Submitted:</b>	N/a

<b>WELL NAME &amp; NO.:</b>	Grayling 14 Fed Com 206H
<b>BOTTOM HOLE FOOTAGE</b>	100'/N & 330'/E
<b>ATS/API ID:</b>	ATS-24-837
<b>APD ID:</b>	10400096951
<b>Sundry ID:</b>	N/a
<b>Date APD Submitted:</b>	N/a

<b>WELL NAME &amp; NO.:</b>	<b>Grayling 14 Fed Com 304H</b>
<b>BOTTOM HOLE FOOTAGE</b>	100'/N & 2178'/E
<b>ATS/API ID:</b>	<b>ATS-24-838</b>
<b>APD ID:</b>	<b>10400096954</b>
<b>Sundry ID:</b>	N/a
<b>Date APD Submitted:</b>	N/a

<b>WELL NAME &amp; NO.:</b>	<b>Grayling 14 Fed Com 305H</b>
<b>BOTTOM HOLE FOOTAGE</b>	100'/N & 1254'/E
<b>ATS/API ID:</b>	<b>ATS-24-839</b>
<b>APD ID:</b>	<b>10400096955</b>
<b>Sundry ID:</b>	N/a
<b>Date APD Submitted:</b>	N/a

<b>WELL NAME &amp; NO.:</b>	<b>Grayling 14 Fed Com 306H</b>
<b>BOTTOM HOLE FOOTAGE</b>	100'/N & 330'/E
<b>ATS/API ID:</b>	<b>ATS-24-840</b>
<b>APD ID:</b>	<b>10400096956</b>
<b>Sundry ID:</b>	N/a
<b>Date APD Submitted:</b>	N/a

<b>WELL NAME &amp; NO.:</b>	<b>Grayling 14 Fed Com 504H</b>
<b>BOTTOM HOLE FOOTAGE</b>	100'/N & 2178'/E
<b>ATS/API ID:</b>	<b>ATS-24-841</b>
<b>APD ID:</b>	<b>10400096962</b>
<b>Sundry ID:</b>	N/a
<b>Date APD Submitted:</b>	N/a

<b>WELL NAME &amp; NO.:</b>	<b>Grayling 14 Fed Com 505H</b>
<b>BOTTOM HOLE FOOTAGE</b>	100'/N & 1254'/E
<b>ATS/API ID:</b>	<b>ATS-24-842</b>
<b>APD ID:</b>	<b>10400096963</b>
<b>Sundry ID:</b>	N/a
<b>Date APD Submitted:</b>	N/a

## COA

H2S	Yes		
Potash	None		
Cave/Karst Potential	Low		
Cave/Karst Potential	<input type="checkbox"/> Critical		
Variance	<input checked="" type="checkbox"/> None	<input checked="" type="checkbox"/> Flex Hose	<input checked="" type="checkbox"/> Other
Wellhead	Conventional and Multibowl		
Other	<input type="checkbox"/> 4 String	Capitan Reef Int 1	<input type="checkbox"/> WIPP
Other	Pilot Hole None	<input type="checkbox"/> Open Annulus	
Cementing	Contingency Squeeze None	Echo-Meter None	Primary Cement Squeeze None
Special Requirements	<input type="checkbox"/> Water Disposal/Injection	<input checked="" type="checkbox"/> COM	<input type="checkbox"/> Unit
Special Requirements	<input type="checkbox"/> Batch Sundry	Waste Prevention None	
Special Requirements Variance	<input type="checkbox"/> Break Testing	<input type="checkbox"/> Offline Cementing	<input type="checkbox"/> Casing Clearance

## A. HYDROGEN SULFIDE

A Hydrogen Sulfide (H<sub>2</sub>S) Drilling Plan shall be activated 500 feet prior to drilling into the **Bone Springs** formation. As a result, the Hydrogen Sulfide area must meet **43 CFR part 3170 Subpart 3176** requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, please provide measured values and formations to the BLM.

## B. CASING

1. The **13-3/8** inch surface casing shall be set at approximately **1220 feet** (a minimum of **25 feet (Lea County)** into the Rustler Anhydrite and above the salt when present, and below usable fresh water) and cemented to the surface. The surface hole shall be **17 1/2** inch in diameter.
  - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
  - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
  - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
  - d. If cement falls back, remedial cementing will be done prior to drilling out that string.

**Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.**

2. The minimum required fill of cement behind the **9-5/8** inch intermediate casing is:
  - Cement to surface. If cement does not circulate see B.1.a, c-d above. **Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst, potash or capitan reef.**
  - ❖ **Special Capitan Reef requirements.** If lost circulation (50% or greater) occurs below the Base of the Salt, the operator shall do the following:
    - Switch to fresh water mud to protect the Capitan Reef and use fresh water mud until setting the intermediate casing. The appropriate BLM office is to be notified for a PET to witness the switch to fresh water.

- Daily drilling reports from the Base of the Salt to the setting of the intermediate casing are to be submitted to the BLM CFO engineering staff via e-mail by 0800 hours each morning. Any lost circulation encountered is to be recorded on these drilling reports. The daily drilling report should show mud volume per shift/tour. Failure to submit these reports will result in an Incidence of Non-Compliance being issued for failure to comply with the Conditions of Approval. If not already planned, the operator shall run a caliper survey for the intermediate well bore and submit to the appropriate BLM office.
  - ❖ In Capitan Reef Areas if cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface.
3. The minimum required fill of cement behind the 5-1/2 inch production casing is:
- Cement should tie-back at least **50 feet** on top of Capitan Reef top **or 200** into the previous casing, whichever is greater. Operator shall provide method of verification.  
**Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst, potash or capitan reef. Cement excess is less than 25%, more cement is required if washout occurs. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.**

### C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'
- 2.

#### Option 1:

- a. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **3000 (3M)** psi.
- b. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the 9-5/8 inch intermediate casing shoe shall be **5000 (5M)** psi.

#### Option 2:

Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the 13-3/8 inch surface casing. Minimum working

pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.

- a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
- b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
- c. Manufacturer representative shall install the test plug for the initial BOP test.
- d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
- e. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172.6(b)(9) must be followed.

#### **D. SPECIAL REQUIREMENT (S)**

##### **Communitization Agreement**

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- The operator will submit an as-drilled survey well plat of the well completion, but are not limited to, those specified in **43 CFR part 3170 Subpart 3171**
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

## GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240,  
(575) 689-5981

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
  - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
  - b. When the operator proposes to set surface casing with Spudder Rig
    - Notify the BLM when moving in and removing the Spudder Rig.
    - Notify the BLM when moving in the 2<sup>nd</sup> Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
    - BOP/BOPE test to be conducted per **43 CFR part 3170 Subpart 3172** as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.

### A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.

2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends of both lead and tail cement, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in **43 CFR part 3170 Subpart 3172 and API STD 53 Sec. 5.3**.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke

manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.

3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
  - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
  - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
  - c. Manufacturer representative shall install the test plug for the initial BOP test.
  - d. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172.6(b)(9) must be followed.
  - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
  - a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead cement), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
  - b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the cement plug. The BOPE test can be

initiated after bumping the cement plug with the casing valve open. (only applies to single stage cement jobs, prior to the cement setting up.)

- c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer and can be initiated immediately with the casing valve open. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to **43 CFR part 3170 Subpart 3172** with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for 8 hours or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
- d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- e. The results of the test shall be reported to the appropriate BLM office.
- f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per **43 CFR part 3170 Subpart 3172**.

#### C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

#### D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and

disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

Long Vo (LVO) 6/25/2024

## Hydrogen Sulfide Plan Summary

- A. All personnel shall receive proper H<sub>2</sub>S training in accordance with Onshore Order III.C.3.a.
- B. Briefing Area: two perpendicular areas will be designated by signs and readily accessible.
- C. Required Emergency Equipment:

- Well control equipment
  - a. Flare line 150' from wellhead to be ignited by flare gun.
  - b. Choke manifold with a remotely operated choke.
  - c. Mud/gas separator

- Protective equipment for essential personnel.

### Breathing apparatus:

- a. Rescue Packs (SCBA) — 1 unit shall be placed at each breathing area, 2 shall be stored in the safety trailer.
- b. Work/Escape packs — 4 packs shall be stored on the rig floor th sufficient air hose not to restrict work activity.
- c. Emergency Escape Packs — 4 packs shall be stored in the doghouse for emergency evacuation.

### Auxiliary Rescue Equipment:

- a. Stretcher
- b. Two OSHA full body harness
- c. 100 ft 5/8 inch OSHA approved rope
- d. 1-20# class ABC fire extinguisher

- H<sub>2</sub>S detection and monitoring equipment:

The stationary detector with three sensors will be placed in the upper dog house if equipped, set to visually alarm @ 10 ppm and audible @ 14 ppm. Calibrate a minimum of every 30 days or as needed. The sensors will be placed in the following places: Rig floor / Bell nipple / End of flow line or where well bore fluid is being discharged.

(Gas sample tubes will be stored in the safety trailer)

- Visual warning systems.
  - a. One color code condition sign will be placed at the entrance to the site reflecting the possible conditions at the site.
  - b. A colored condition flag will be on display, reflecting the current condition at the site at the time.
  - c. Two wind socks will be placed in strategic locations, visible from all angles.



- **Mud program:**  
The mud program has been designed to minimize the volume of H2S circulated to surface. The operator will have the necessary mud products to minimize hazards while drilling in H2S bearing zones.
- **Metallurgy:**  
All drill strings, casings, tubing, wellhead, blowout preventer, drilling spool, kill lines, choke manifold and lines, and valves shall be suitable for H2S service.
- **Communication:**  
Communication will be via cell phones and land lines where available.

#### Company Personnel to be Notified

John Harper, Vice President of Geoscience	Office: (720) 746-5045
	Mobile: (678) 988-6644
Braden Harris, Engineer	Mobile: (406) 600-3310

#### Local & County Agencies

Maljamar Volunter Fire Department	911 or (575) 676-4100
Lea County Sheriff (Lovington)	911 or (575) 396-3611
Lea County Emergency Management (Lovington)	(575) 396-8602
Lea Regional Medical Center Hopital (Hobbs)	(575) 492-5000

#### State Agencies

NM State Police (Hobbs)	(575) 392-5588
NM Oil Conservation (Hobbs)	(575) 370-3186
NM Oil Conservation (Santa Fe)	(505) 476-3440
NM Dept. of Transportation (Roswell)	(575) 637-7201



Federal Agencies

BLM (Carlsbad)	(575) 234-5972
BLM (Hobbs)	(575) 393-3612
National Response Center	(800) 424-8802
US EPA Region 6 (Dallas)	(800) 887-6063
	(214) 665-6444

Veterinarians

Lovington Veterinary Clinic	(575) 396-7387
Hobbs Animal Clinic	(575) 392-5563
Dal Paso Animal Hospital (Hobbs)	(575) 397-2286


Residents within 2 miles

None

Air Evacuation

AeroCare (Lubbock)	(800) 627-2376
Med Flight Air Ambulance (Albuquerque)	(800) 842-4431
Lifeguard (Albuquerque)	(888) 866-7256



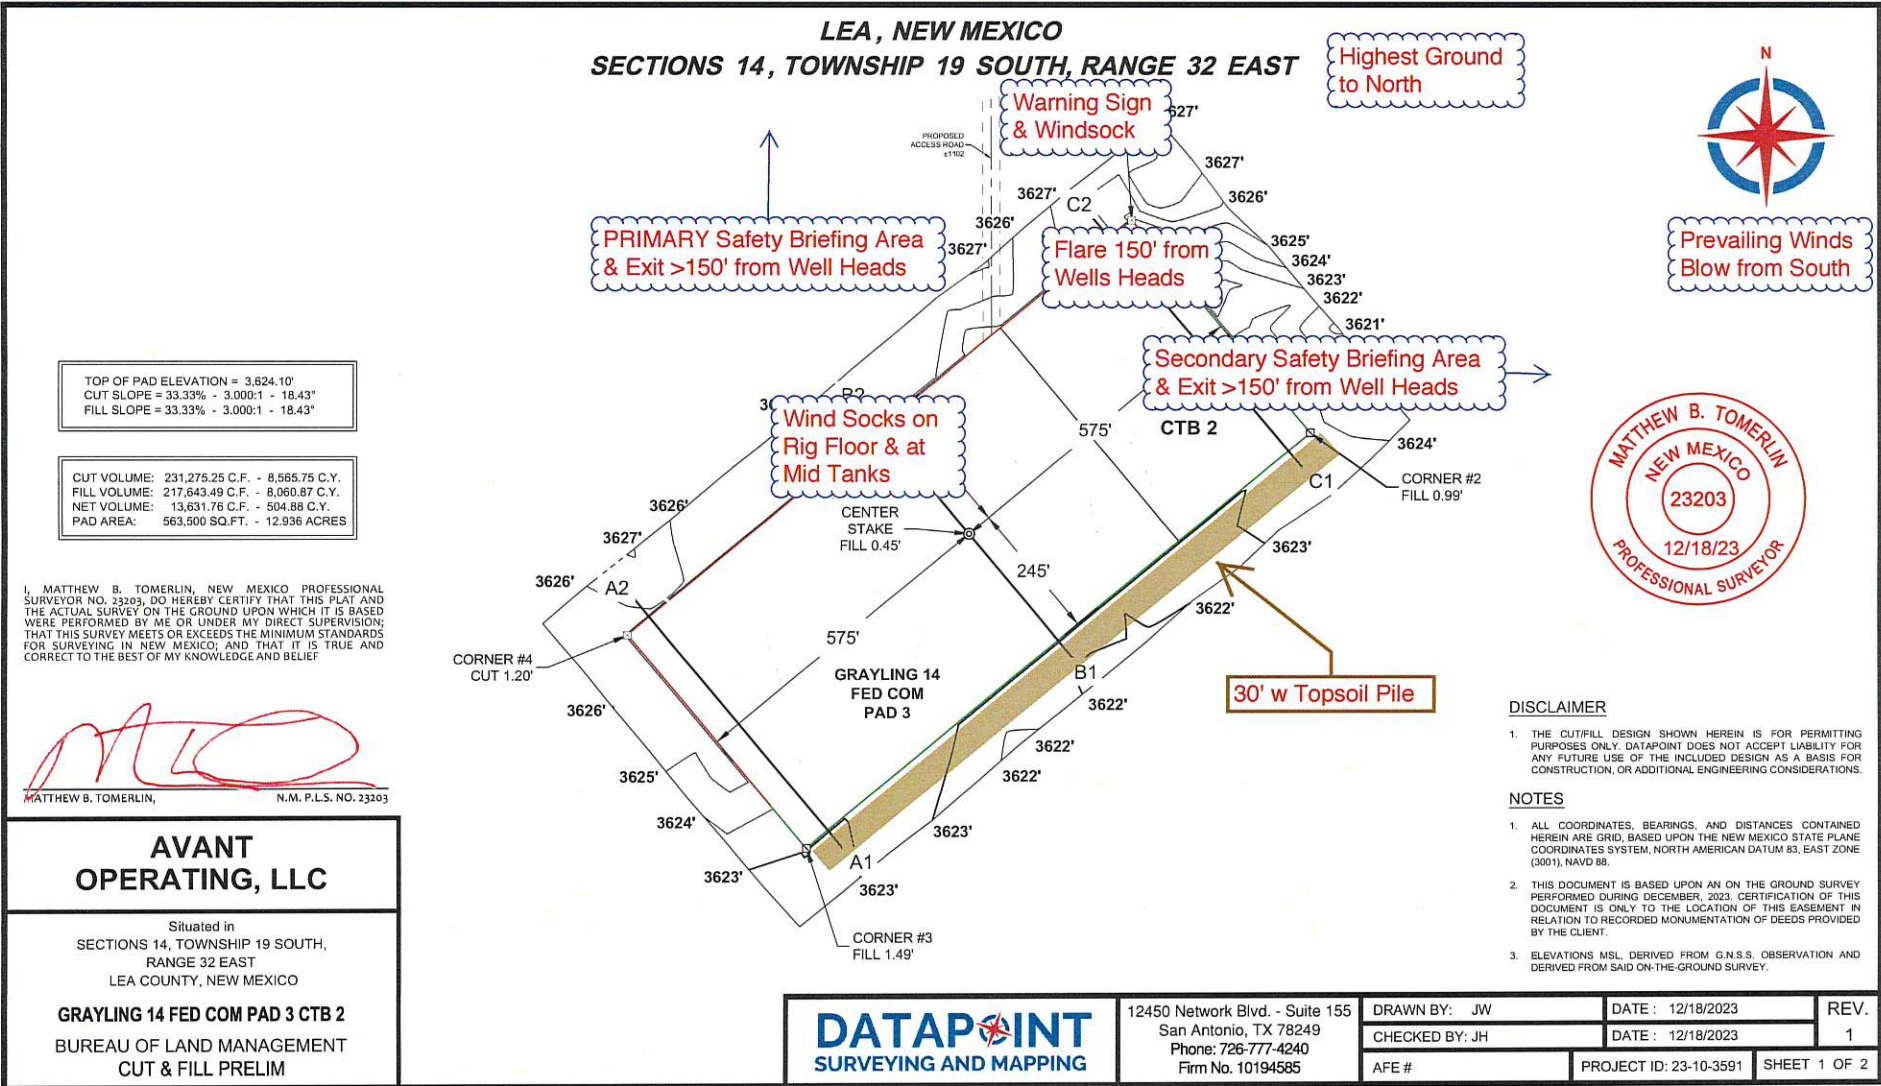


Z:\2023\AVANT OPERATING, LLC\23-10-3591 - GRAYLING 14 FED COM\PLATS\CUT-FILL\PAD 3 CTB 2\20231208\GRAYLING 14 FED COM PAD 3 CTB 2\_CUT-FILL\_R1.dwg  
12/15/2023 1:47 PM JOSH WILSON


# Avant Operating, LLC

Grayling 14 Fed Com  
Pad 3  
H2S Contingency Plan:  
Radius Map

Section 14, Township 19S, Range 32E  
Lea County, New Mexico





Pad Center



NAD 1983 New Mexico State Plane East  
FIPS 3001 Feet



Prepared by Permits West, Inc., December 20, 2023  
for Avant Operating, LLC

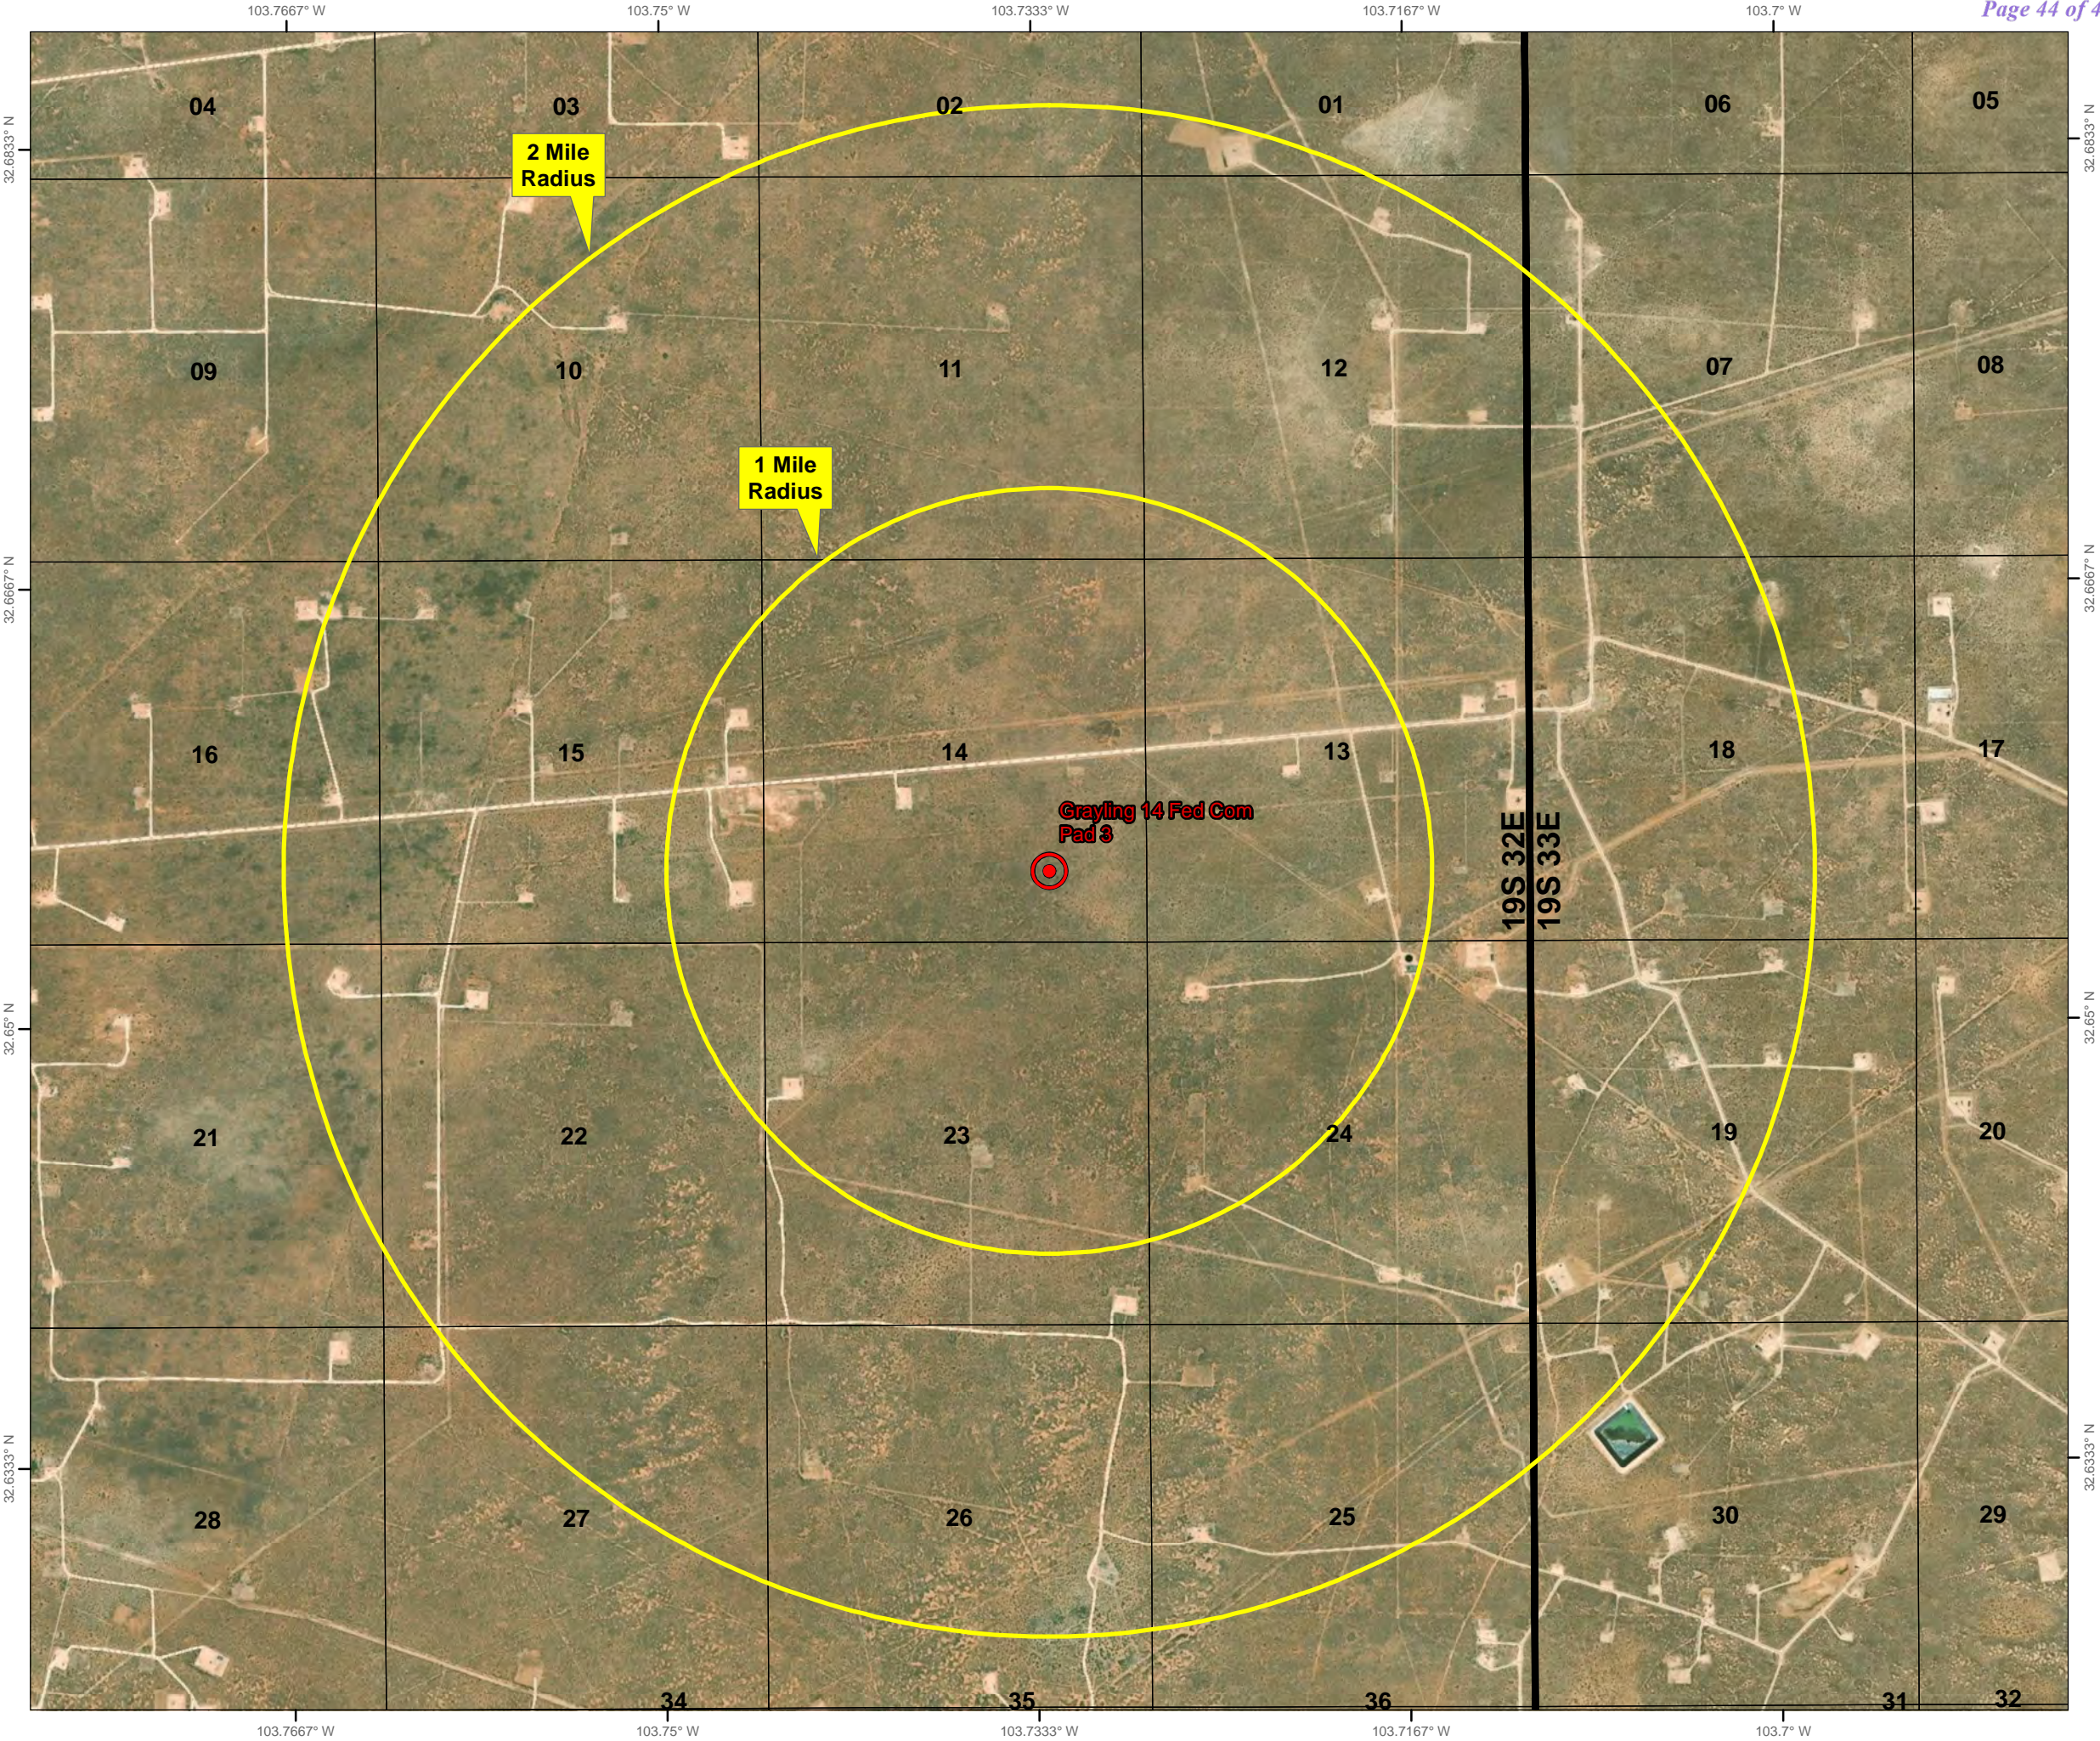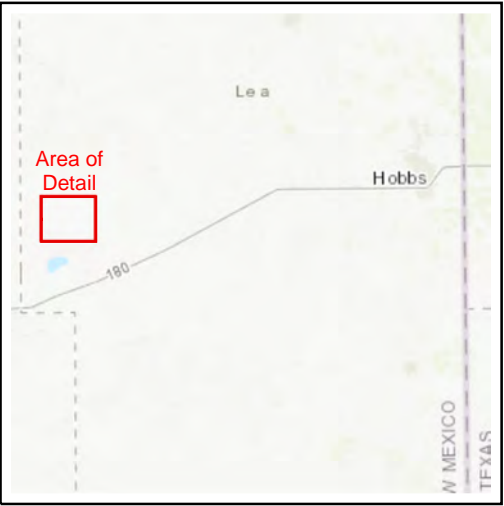

Sante Fe Main Office  
Phone: (505) 476-3441

General Information  
Phone: (505) 629-6116

Online Phone Directory  
<https://www.emnrd.nm.gov/ocd/contact-us>

State of New Mexico

Energy, Minerals and Natural Resources

Oil Conservation Division

1220 S. St Francis Dr.

Santa Fe, NM 87505

CONDITIONS

Action 410781

CONDITIONS

Operator:  Avant Operating, LLC 1515 Wynkoop Street Denver, CO 80202	OGRID:  330396
	Action Number:  410781
	Action Type:  [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

CONDITIONS

Created By	Condition	Condition Date
twelem	Cement is required to circulate on both surface and intermediate1 strings of casing.	12/11/2024
twelem	If cement does not circulate on any string, a Cement Bond Log (CBL) is required for that string of casing.	12/11/2024
pkautz	Administrative order required for non-standard spacing unit prior to production.	12/19/2024
pkautz	File As Drilled C-102 and a directional Survey with C-104 completion packet.	12/19/2024
pkautz	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string.	12/19/2024
pkautz	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system.	12/19/2024
