

Form 3160-3  
(June 2015)FORM APPROVED  
OMB No. 1004-0137  
Expires: January 31, 2018

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT  
**APPLICATION FOR PERMIT TO DRILL OR REENTER**

1a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER 1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other 1c. Type of Completion: <input type="checkbox"/> Hydraulic Fracturing <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		5. Lease Serial No. <b>NMNM118722</b> 6. If Indian, Allottee or Tribe Name  7. If Unit or CA Agreement, Name and No.  8. Lease Name and Well No.  <b>SD 14 23 FED P305</b>  <b>307H</b>
2. Name of Operator <b>CHEVRON USA INCORPORATED</b>		9. API Well No.  10. Field and Pool, or Exploratory <b>Jennings/UPPER BONE SPRING SHALE</b>
3a. Address <b>PO BOX 1392, BAKERSFIELD, CA 93302</b>	3b. Phone No. (include area code) <b>(661) 633-4000</b>	11. Sec., T. R. M. or Blk. and Survey or Area <b>SEC 14/T26S/R32E/NMP</b>
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface <b>NWNE / 312 FNL / 2346 FEL / LAT 32.049447 / LONG -103.644573</b> At proposed prod. zone <b>SWSE / 25 FSL / 1635 FEL / LAT 32.020964 / LONG -103.642323</b>		
14. Distance in miles and direction from nearest town or post office* <b>39 miles</b>		12. County or Parish <b>LEA</b>
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) <b>312 feet</b>	16. No of acres in lease  	17. Spacing Unit dedicated to this well  <b>640.0</b>
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. <b>250 feet</b>	19. Proposed Depth <b>9900 feet / 20410 feet</b>	20. BLM/BIA Bond No. in file <b>FED:</b>
21. Elevations (Show whether DF, KDB, RT, GL, etc.) <b>3207 feet</b>	22. Approximate date work will start* <b>01/05/2024</b>	23. Estimated duration <b>130 days</b>
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- |   |   |
|---|---|
| 1. Well plat certified by a registered surveyor.<br>2. A Drilling Plan.<br>3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).<br>5. Operator certification.<br>6. Such other site specific information and/or plans as may be requested by the BLM. |
|---|---|

25. Signature (Electronic Submission)	Name (Printed/Typed) <b>CAROL ADLER / Ph: (432) 687-7866</b>	Date <b>09/30/2022</b>
Title <b>Sr Regulatory Affairs Coordinator</b>		
Approved by (Signature) (Electronic Submission)	Name (Printed/Typed) <b>CODY LAYTON / Ph: (575) 234-5959</b>	Date <b>09/23/2024</b>
Title <b>Assistant Field Manager Lands &amp; Minerals</b>		
Office <b>Carlsbad Field Office</b>		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

\*(Instructions on page 2)



Approval Date: 09/23/2024

Santa Fe Main Office Phone: (505) 476-3441 Fax: (55) 476-3462 General Information Phone: (505) 629-6116  Online Phone Directory Visit: <a href="https://www.emnrd.nm.gov/ocd/contact-us/">https://www.emnrd.nm.gov/ocd/contact-us/</a>	State of New Mexico Energy, Minerals & Natural Resources Department OIL CONSERVATION DIVISION	C-102 Revised July 9, 2024 Submit Electronically via OCD Permitting	
		Submittal Type:	<input checked="" type="checkbox"/> Initial Submittal
			<input type="checkbox"/> Amended Report
		<input type="checkbox"/> As Drilled	

## WELL LOCATION INFORMATION

API Number N/A	Pool Code 97903	Pool Name WC-025 G-08 S253235G; LOWER BONE SPRING
Property Code N/A	Property Name SD 14 23 FED P305	Well Number 307H
OGRID No. 4323	Operator Name CHEVRON U.S.A. INC.	Ground Level Elevation 3,207'
Surface Owner: <input type="checkbox"/> State <input type="checkbox"/> Fee <input type="checkbox"/> Tribal <input checked="" type="checkbox"/> Federal		Mineral Owner: <input type="checkbox"/> State <input type="checkbox"/> Fee <input type="checkbox"/> Tribal <input checked="" type="checkbox"/> Federal

## Surface Location

UL B	Section 14	Township 26 SOUTH	Range 32 EAST, N.M.P.M.	Lot N/A	Ft. from N/S 312' NORTH	Ft. from E/W 2,346' EAST	Latitude 32.049447° N	Longitude 103.644573° W	County LEA
---------	---------------	----------------------	-------------------------------	------------	----------------------------	-----------------------------	--------------------------	----------------------------	---------------

## Bottom Hole Location

UL O	Section 23	Township 26 SOUTH	Range 32 EAST, N.M.P.M.	Lot N/A	Ft. from N/S 25' SOUTH	Ft. from E/W 1,635' EAST	Latitude 32.020964° N	Longitude 103.642323° W	County LEA
---------	---------------	----------------------	-------------------------------	------------	---------------------------	-----------------------------	--------------------------	----------------------------	---------------

Dedicated Acres 640	Infill or Defining Well INFILL	Defining Well API 30-025-49786	Overlapping Spacing Unit (Y/N) N	Consolidation Code N/A
Order Numbers. N/A			Well setbacks are under Common Ownership: <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	

## Kick Off Point (KOP)

UL B	Section 14	Township 26 SOUTH	Range 32 EAST, N.M.P.M.	Lot N/A	Ft. from N/S 100' NORTH	Ft. from E/W 1,635' EAST	Latitude 32.050030° N	Longitude 103.642276° W	County LEA
---------	---------------	----------------------	-------------------------------	------------	----------------------------	-----------------------------	--------------------------	----------------------------	---------------

## First Take Point (FTP)

UL B	Section 14	Township 26 SOUTH	Range 32 EAST, N.M.P.M.	Lot N/A	Ft. from N/S 100' NORTH	Ft. from E/W 1,635' EAST	Latitude 32.050030° N	Longitude 103.642276° W	County LEA
---------	---------------	----------------------	-------------------------------	------------	----------------------------	-----------------------------	--------------------------	----------------------------	---------------

## Last Take Point (LTP)

UL O	Section 23	Township 26 SOUTH	Range 32 EAST, N.M.P.M.	Lot N/A	Ft. from N/S 100' SOUTH	Ft. from E/W 1,635' EAST	Latitude 32.021171° N	Longitude 103.642322° W	County LEA
---------	---------------	----------------------	-------------------------------	------------	----------------------------	-----------------------------	--------------------------	----------------------------	---------------

Unitized Area or Area of Uniform Interest N/A	Spacing Unit Type <input checked="" type="checkbox"/> Horizontal <input type="checkbox"/> Vertical	Ground Floor Elevation: 3,207'
--	--	-----------------------------------

## OPERATOR CERTIFICATIONS

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and, if the well is a vertical or directional well, that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of a working interest or unleased mineral interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

If this well is a horizontal well, I further certify that this organization has received the consent of at least one lessee or owner of a working interest or unleased mineral interest in each tract (in the target pool or formation) in which any part of the well's completed interval will be located or obtained a compulsory pooling order from the division.

Nicole Taylor 1/16/2025  
Signature Date


Nicole Taylor  
Printed Name

nicole.taylor@chevron.com  
Email Address

## SURVEYOR CERTIFICATIONS

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

See Sheet 2 of 2 for plat.

  
Signature and Seal of Professional Surveyor


02/04/2022  
Certificate Number Date of Survey

## ACREAGE DEDICATION PLATS

This grid represents a standard section. You may superimpose a non-standard section, or larger area, over this grid. Operators must outline the dedicated acreage in a red box, clearly show the well surface location and bottom hole location, if it is directionally drilled, with the dimensions from the section lines in the cardinal directions. If this is a horizontal wellbore show on this plat the location of the First Take Point and Last Take Point, and the point within the Completed interval (other than the First Take Point or Last Take Point) that is closest to any outer boundary of the tract.

Surveyors shall use the latest United States government survey or dependent resurvey. Well locations will be in reference to the New Mexico Principal Meridian. If the land is not surveyed, contact the OCD Engineering Bureau. Independent subdivision surveys will not be acceptable.

See Sheet 1 of 2 for notes & certification.

**SD 14 23 FEDERAL 307H**

X = 713,546' (NAD27 NM E)  
Y = 382,350'  
LAT. 32.049322° N (NAD27)  
LONG. 103.644103° W  
X = 754,733' (NAD83/2011 NM E)  
Y = 382,408'  
LAT. 32.049447° N (NAD83/2011)  
LONG. 103.644573° W

**PROPOSED  
KICK OFF POINT/  
FIRST TAKE POINT**

X = 714,256' (NAD27 NM E)  
Y = 382,567'  
LAT. 32.049905° N (NAD27)  
LONG. 103.641806° W  
X = 755,443' (NAD83/2011 NM E)  
Y = 382,624'  
LAT. 32.050030° N (NAD83/2011)  
LONG. 103.642276° W

**PROPOSED MID-POINT**

X = 714,287' (NAD27 NM E)  
Y = 377,326'  
LAT. 32.035497° N (NAD27)  
LONG. 103.641814° W  
X = 755,474' (NAD83/2011 NM E)  
Y = 377,383'  
LAT. 32.035622° N (NAD83/2011)  
LONG. 103.642283° W

**PROPOSED LAST TAKE POINT**


X = 714,308' (NAD27 NM E)  
Y = 372,068'  
LAT. 32.021045° N (NAD27)  
LONG. 103.641854° W  
X = 755,496' (NAD83/2011 NM E)  
Y = 372,126'  
LAT. 32.021171° N (NAD83/2011)  
LONG. 103.642322° W

**PROPOSED  
BOTTOM HOLE LOCATION**

X = 714,309' (NAD27 NM E)  
Y = 371,993'  
LAT. 32.020839° N (NAD27)  
LONG. 103.641854° W  
X = 755,496' (NAD83/2011 NM E)  
Y = 372,050'  
LAT. 32.020964° N (NAD83/2011)  
LONG. 103.642323° W

## CORNER COORDINATES TABLE (NAD 27)

A - X=710579.74, Y=382643.92  
B - X=713234.95, Y=382660.57  
C - X=714562.55, Y=382668.90  
D - X=715890.15, Y=382677.22  
E - X=710603.40, Y=375958.74  
F - X=713265.42, Y=375978.66  
G - X=714596.43, Y=375988.62  
H - X=715927.44, Y=375998.58  
I - X=710630.44, Y=371945.53  
J - X=713287.04, Y=371962.12  
K - X=714615.34, Y=371970.41  
L - X=715943.63, Y=371978.70

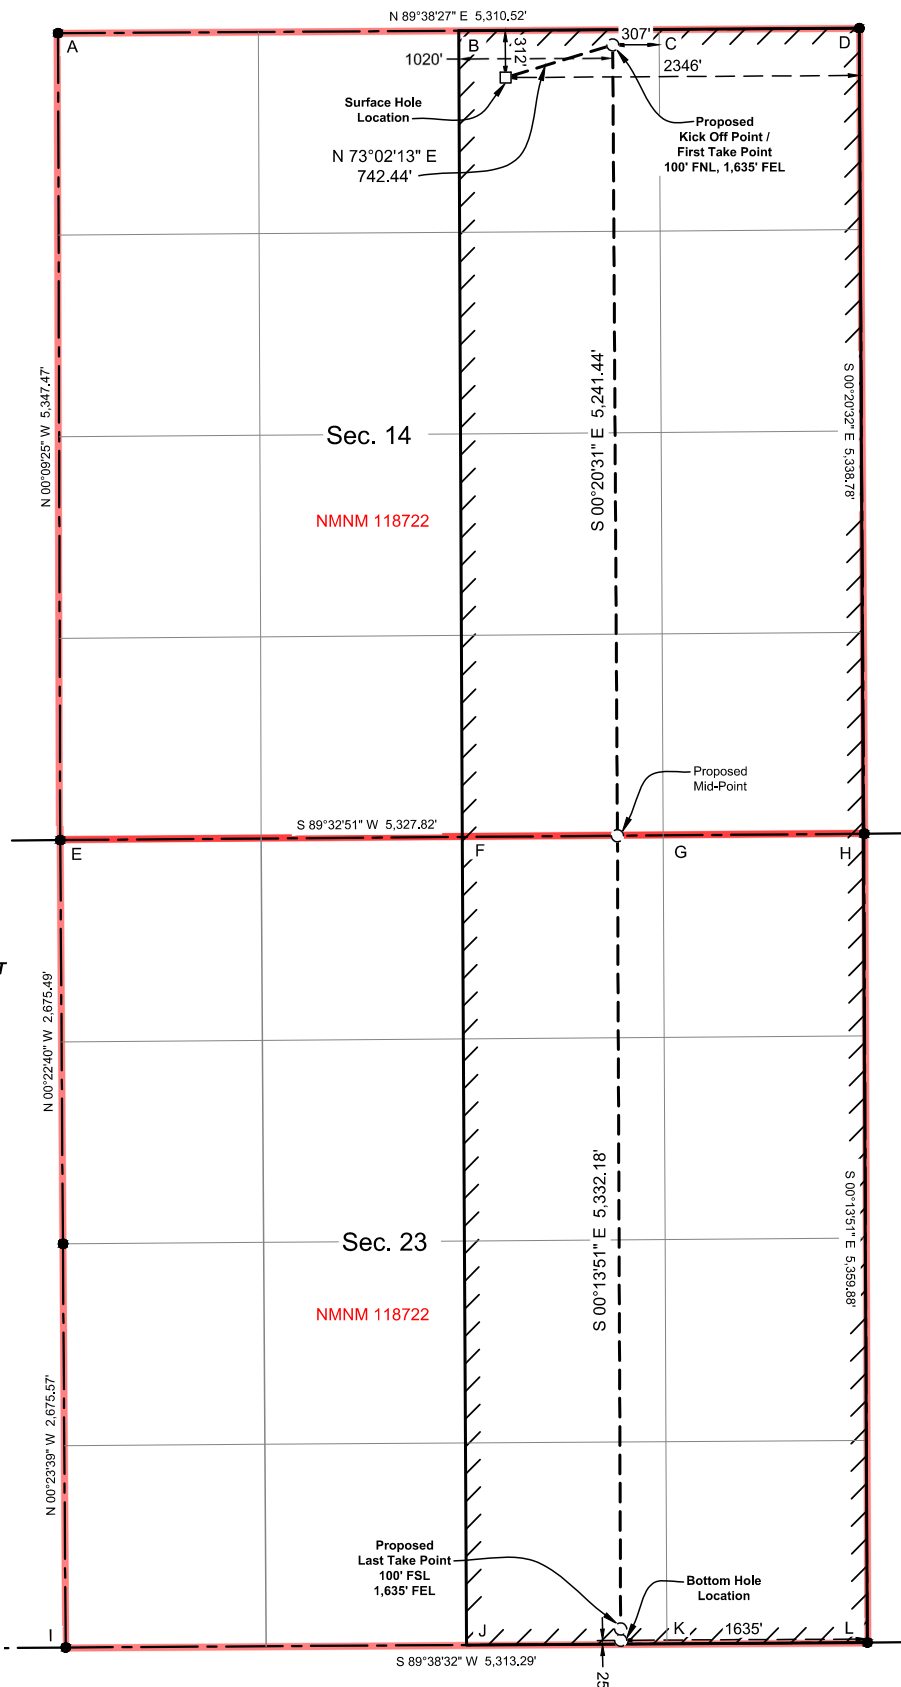

State of New Mexico  
Energy, Minerals and Natural Resources Department

Submit Electronically  
Via E-permitting

Oil Conservation Division  
1220 South St. Francis Dr.  
Santa Fe, NM 87505

## NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

### Section 1 – Plan Description

Effective May 25, 2021

**I. Operator:** Chevron USA Inc **OGRID:** 4323 **Date:** 09/27/2022

**II. Type:** ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: \_\_\_\_\_

**III. Well(s):** Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
SD 14 23 Fed Pad 305 #204H	Pending	UL: B Sect 14 T26S R32E	312" FNL 2406' FEL	1440 BBL/D	3815 MCF/D	2890 BBL/D
SD 14 23 Fed Pad 305 #205H	Pending	UL: B Sect 14 T26S R32E	312" FNL 2366' FEL	1440 BBL/D	3815 MCF/D	2890 BBL/D
SD 14 23 Fed Pad 305 #206H	Pending	UL: B Sect 14 T26S R32E	312" FNL 2326' FEL	1440 BBL/D	3815 MCF/D	2890 BBL/D
SD 14 23 Fed Pad 305 #305H	Pending	UL: B Sect 14 T26S R32E	312" FNL 2426' FEL	1440 BBL/D	3815 MCF/D	2890 BBL/D
SD 14 23 Fed Pad 305 #306H	Pending	UL: B Sect 14 T26S R32E	312" FNL 2386' FEL	1440 BBL/D	3815 MCF/D	2890 BBL/D
SD 14 23 Fed Pad 305 #307H	Pending	UL: B Sect 14 T26S R32E	312" FNL 2346' FEL	1440 BBL/D	3815 MCF/D	2890 BBL/D
SD 14 23 Fed Pad 305 #308H	Pending	UL: B Sect 14 T26S R32E	312" FNL 2306' FEL	1440 BBL/D	3815 MCF/D	2890 BBL/D

**IV. Central Delivery Point Name:** Salado Draw Satellite 14 [See 19.15.27.9(D)(1) NMAC]

**V. Anticipated Schedule:** Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
SD 14 23 Fed Pad 305 #204H	TBD	4/1/2026	N/A	N/A	N/A	N/A
SD 14 23 Fed Pad 305 #205H	TBD	4/21/2026	N/A	N/A	N/A	N/A
SD 14 23 Fed Pad 305 #206H	TBD	5/11/2026	N/A	N/A	N/A	N/A

SD 14 23 Fed Pad 305 #305H	TBD	5/31/2026	N/A	N/A	N/A	N/A
SD 14 23 Fed Pad 305 #306H	TBD	6/20/2026	N/A	N/A	N/A	N/A
SD 14 23 Fed Pad 305 #307H	TBD	7/10/2026	N/A	N/A	N/A	N/A
SD 14 23 Fed Pad 305 #308H	TBD	7/30/2026	N/A	N/A	N/A	N/A

**VI. Separation Equipment:** ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

**VII. Operational Practices:** ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

**VIII. Best Management Practices:** ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

## **Section 2 – Enhanced Plan** **EFFECTIVE APRIL 1, 2022**

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

### **IX. Anticipated Natural Gas Production:**

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

### **X. Natural Gas Gathering System (NGGS):**

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

**XI. Map.** ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

**XII. Line Capacity.** The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

**XIII. Line Pressure.** Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

**XIV. Confidentiality:** ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.



### **Section 3 - Certifications**

**Effective May 25, 2021**

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

***If Operator checks this box, Operator will select one of the following:***

**Well Shut-In.** ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

**Venting and Flaring Plan.** ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

### **Section 4 - Notices**

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature:	<i>Cindy Herrera-Murillo</i>
Printed Name:	Cindy Herrera-Murillo
Title:	Sr HSE Regulatory affairs Coordinator
E-mail Address	eeof@chevron.com
Date:	09/27/2022
Phone:	575-263-0431
<b>OIL CONSERVATION DIVISION</b> <b>(Only applicable when submitted as a standalone form)</b>	
Approved By:	
Title:	
Approval Date:	
Conditions of Approval:	



**VI. Separation Equipment:**

Separation equipment installed at each Chevron facility is designed for maximum anticipated throughput and pressure to minimize waste. Separation equipment is designed and built according to ASME Sec VIII Div I to ensure gas is separated from liquid streams according to projected production.

**VII./VIII. Operational & Best Management Practices:****1. General Requirements for Venting and Flaring of Natural Gas:**

- In all circumstances, Chevron will flare rather than vent unless flaring is technically infeasible and venting of natural gas will avoid a risk of an immediate and substantial adverse impact on safety, public health, or the environment.
- Chevron installs and operates vapor recovery units (VRUs) in new facilities to minimize venting and flaring. If a VRU experiences operating issues, it is quickly assessed so that action can be taken to return the VRU to operation or, if necessary, facilities are shut-in to reduce the venting or flaring of natural gas.

**2. During Drilling Operations:**

- Flare stacks will be located a minimum of 110 feet from the nearest surface hole location.
- If an emergency or malfunction occurs, gas will be flared or vented to avoid a risk of an immediate and substantial adverse impact on public health, safety or the environment and be properly reported to the NMOCD pursuant to 19.15.27.8.G.
- Natural gas is captured or combusted if technically feasible using best industry practices and control technologies, such as the use of separators (e.g., Sand Commanders) during normal drilling and completions operations.

**3. During Completions:**

- Chevron typically does not complete traditional flowback, instead Chevron will flow produced oil, water, and gas to a centralized tank battery and continuously recover salable quality gas. If Chevron completes traditional flowback, Chevron conducts reduced emission completions as required by 40 CFR 60.5375a by routing gas to a gas flow line as soon as practicable once there is enough gas to operate a separator. Venting does not occur once there is enough gas to operate a separator
- Normally, during completions a flare is not on-site. A Snubbing Unit will have a flare on-site, and the flare volume will be estimated.
- If natural gas does not meet pipeline quality specification, the gas is sampled twice per week until the gas meets the specifications.

**4. During Production:**

- An audio, visual and olfactory (AVO) inspection will be performed daily (at minimum) for active wells and facilities to confirm that all production equipment is operating properly and there are no leaks or releases except as allowed in Subsection D of 19.15.27.8 NMAC. Inactive, temporarily abandoned, or shut-in wells and facilities will be inspected weekly. Inspection records will be kept for a minimum of five years and will be available upon request by the division.
- Monitor manual liquid unloading for wells on-site, takes all reasonable actions to achieve a stabilized rate and pressure at the earliest practical time and takes reasonable actions to minimize venting to the maximum extent practicable.
- In all circumstances, Chevron will flare rather than vent unless flaring is technically infeasible and venting of natural gas will avoid a risk of an immediate and substantial adverse impact on safety, public health, or the environment.
- Chevron's design for new facilities utilizes air-activated pneumatic controllers and pumps.
- If natural gas does not meet pipeline quality specification, the gas is sampled twice per week until the gas meets the specifications.
- Chevron does not produce oil or gas until all flowlines, tank batteries, and oil/gas takeaway are installed, tested, and determined operational.

5. Performance Standards

- Equipment installed at each facility is designed for maximum anticipated throughput and pressure to minimize waste. Tank pressure relief systems utilize a soft seated or metal seated PSVs, as appropriate, which are both designed to not leak.
- Flare stack has been designed for proper size and combustion efficiency. New flares will have a continuous pilot and will be located at least 100 feet from the well and storage tanks and will be securely anchored.
- New tanks will be equipped with an automatic gauging system.
- An audio, visual and olfactory (AVO) inspection will be performed daily (at minimum) for active wells and facilities to confirm that all production equipment is operating properly and there are no leaks or releases except as allowed in Subsection D of 19.15.27.8 NMAC. Inactive, temporarily abandoned, or shut-in wells and facilities will be inspected weekly. Inspection records will be kept for a minimum of five years and will be available upon request by the division.

6. Measurement or Estimation of Vented and Flared Natural Gas

- Chevron estimates or measures the volume of natural gas that is vented, flared, or beneficially used during drilling, operations, regardless of the reason or authorization for such venting or flaring.
- Where technically practicable, Chevron will install meters on flares installed after May 25, 2021. Meters will conform to industry standards. Bypassing the meter will only occur for inspecting and servicing of the meter.

**Operator Name:** CHEVRON USA INCORPORATED**Well Name:** SD 14 23 FED P305**Well Number:** 307H

utilized.

**Testing Procedure:** The stack will be tested as specified in the attached testing requirements. Batch drilling of the surface, production, and production liner will take place. A full BOP test will be performed per hole section, unless approval from BLM is received otherwise (see variance request ). Flex choke hose will be used for all wells on the pad (see attached specs and variance). BOP test pressures and other documented tests may be recorded and documented via utilization of the IPT 'Suretec' Digital BOP Test Method in lieu of the standard test chart. In the event the IPT system is unavailable, the standard test chart will be used.

**Choke Diagram Attachment:**

BLM\_5M\_Choke\_Manifold\_Diagram\_20220928073227.pdf

**BOP Diagram Attachment:**

BLM\_5M\_Annular\_10M\_Rams\_Stackup\_and\_Test\_Plan\_20220928073255.pdf

NM\_Slim\_Hole\_Wellhead\_6650\_psi\_UH\_S\_20220928073336.pdf

BLM\_Choke\_Hose\_Test\_Specs\_and\_Pressure\_Test\_Continental\_20220928073403.pdf

Sundry\_Break\_Testing\_and\_WOC\_500\_psi\_SD\_P305\_20220928073443.pdf

**Section 3 - Casing**

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE	17.5	13.375	NEW	API	N	0	995	0	995	3207	2212	995	J-55	54.5	OTHER - BTC	3.72	1.98	BUOY	15.73	BUOY	15.73
2	INTERMEDIATE	12.25	9.625	NEW	API	N	0	4633	0	4593	3159	-1386	4633	L-80	40	BUTT	2.24	2.46	BUOY	4.99	BUOY	4.99
3	INTERMEDIATE	8.75	7.0	NEW	API	N	0	9457	0	9407	3159	-6200	9457	OTHER	29	OTHER - BLUE	2.94	4.18	BUOY	3.41	BUOY	3.41
4	PRODUCTION	6.125	5.0	NEW	API	N	9157	9907	8907	9807	-5700	-6600	750	P-110	18	OTHER - W-513	2.35	3.94	BUOY	2.08	BUOY	2.08
5	PRODUCTION	6.125	4.5	NEW	API	N	9907	20410	9807	9900	-6600	-6693	10503	P-110	11.6	OTHER - W-521	2.35	3.94	BUOY	2.08	BUOY	2.08

**Casing Attachments**

Operator Name: CHEVRON USA INCORPORATED

Well Name: SD 14 23 FED P305

Well Number: 307H

Casing Attachments

Casing ID: 1StringSURFACE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

13.375\_54.5ppf\_J55\_BTC\_20190802115131.pdf

Casing ID: 2StringINTERMEDIATE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

9.625\_L80IC\_20190802115220.pdf

Casing ID: 3StringINTERMEDIATE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

7\_29ppf\_TN110SS\_TSH\_Blue\_20220928074833.pdf

Operator Name: CHEVRON USA INCORPORATED

Well Name: SD 14 23 FED P305

Well Number: 307H

Casing Attachments

Casing ID: 4

String

PRODUCTION

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

5\_18ppf\_P110\_Flush\_W513\_20220928075129.pdf

Casing ID: 5

String

PRODUCTION

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

4.5\_11.6ppf\_P110\_TSH\_W521\_20220928075110.pdf

Section 4 - Cement

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
SURFACE	Lead		0	0	0	0	0	0	0	N/A	N/A
SURFACE	Tail		0	995	650	1.33	14.8	864	25	CLASS C	Extender, Antifoam, Retarder, Viscosifier
PRODUCTION	Lead		0	0	0	0	0	0	0	N/A	NA

INTERMEDIATE	Lead		0	3633	571	2.49	11.9	1422	25	Class C	Extender, Antifoam, Retarder, Viscosifier
--------------	------	--	---	------	-----	------	------	------	----	---------	---

**Operator Name:** CHEVRON USA INCORPORATED**Well Name:** SD 14 23 FED P305**Well Number:** 307H

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
INTERMEDIATE	Tail		3633	4633	323	1.33	14.8	429	25	Class C	Extender, Antifoam, Retarder, Viscosifier
INTERMEDIATE	Lead		0	8457	583	2.49	11.9	1453	25	Class C	Extender, Antifoam, Retarder, Viscosifier
INTERMEDIATE	Tail		8457	9457	141	1.33	14.8	188	25	Class C	Extender, Antifoam, Retarder, Viscosifier
PRODUCTION	Lead		9157	20410	996	1.33	14.8	1325	25	Class C	Extender, Antifoam, Retarder, Viscosifier

### Section 5 - Circulating Medium

**Mud System Type:** Closed**Will an air or gas system be Used?** NO**Description of the equipment for the circulating system in accordance with Onshore Order #2:****Diagram of the equipment for the circulating system in accordance with Onshore Order #2:**

**Describe what will be on location to control well or mitigate other conditions:** If an open reserve pit is not approved by OCD, a closed system will be used consisting of above ground steel tanks and all wastes accumulated during drilling operations will be contained in a portable trash cage and removed from location and deposited in an approved sanitary landfill. If an open reserve pit is in place, pit construction, operation, and closure will follow all applicable rules and regulation. Sanitary wastes will be contained in a chemical porta-toilet and then hauled to an approved sanitary landfill.

**Describe the mud monitoring system utilized:** All fluids and cuttings will be disposed of in accordance with New Mexico Oil Conservation Division rules and regulations. And transporting of E&P waste will follow EPA regulations and accompanying manifests. A mud test shall be performed every 24 hours after mudding up to determine, as applicable: density, viscosity, gel strength, filtration, and pH. Visual mud monitoring equipment shall be in place to detect volume changes indicating loss or gain of circulating fluid volume. When abnormal pressures are anticipated -- a pit volume totalizer (PVT), stroke counter, and flow sensor will be used to detect volume changes indicating loss or gain of circulating fluid volume.

### Circulating Medium Table

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
4633	9457	WATER-BASED MUD	8.7	9							F. Vis 70 - 75, Filtrate 25 - 30

**Operator Name:** CHEVRON USA INCORPORATED**Well Name:** SD 14 23 FED P305**Well Number:** 307H

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
9457	20410	OIL-BASED MUD	9.2	9.5							F. Vis 70 - 75, Filtrate 25 - 30 -Due to wellbore instability in the lateral, may exceed the MW weight window needed to maintain overburden stresses
0	995	SPUD MUD	8.3	8.9							F. Vis 32-34, Filtrate NC - NC
995	4633	OTHER : BRINE	8.9	10							F. Vis 28 - 30, Filtrate 25 - 30 -Saturated brine would be used through salt sections.

## Section 6 - Test, Logging, Coring

### List of production tests including testing procedures, equipment and safety measures:

Production tests are not planned.

Logs run include: Gamma Ray Log, Directional Survey

Coring Operations are not planned.

### List of open and cased hole logs run in the well:

GAMMA RAY LOG,DIRECTIONAL SURVEY,

### Coring operation description for the well:

Conventional whole core samples are not planned. A Directional Survey will be run.

## Section 7 - Pressure

**Anticipated Bottom Hole Pressure:** 4891

**Anticipated Surface Pressure:** 2712

**Anticipated Bottom Hole Temperature(F):** 165

**Anticipated abnormal pressures, temperatures, or potential geologic hazards?** NO

**Describe:**

**Contingency Plans geohazards description:**

**Contingency Plans geohazards**

**Operator Name:** CHEVRON USA INCORPORATED**Well Name:** SD 14 23 FED P305**Well Number:** 307H**Hydrogen Sulfide drilling operations plan required?** YES**Hydrogen sulfide drilling operations**

Chevron\_Standard\_H2S\_Contingency\_Plan\_2022\_20220928080336.pdf

## Section 8 - Other Information

**Proposed horizontal/directional/multi-lateral plan submission:**

DefPlan100ft\_SD1423FEDP305No.307H\_R0\_20220929144111.pdf

SD\_P305\_307H\_9P\_20220930133159.pdf

**Other proposed operations facets description:**

Chevron requests authorization to use the spudder rig to spud the well and set surface casing. The drilling rig will move in less than 90 days to continue drilling operations. Rig layouts attached.

**Other proposed operations facets attachment:**

7\_well\_rig\_layout\_patterson\_20220928080517.pdf

CUSA\_Spudder\_Rig\_Data\_20220928080541.pdf

Gas\_Management\_Plan\_\_SD\_Pad\_305\_20220928083019.pdf

Operational\_Best\_Management\_Practices\_V2\_20220928083027.pdf

**Other Variance attachment:**





## SD 14 23 FED P305 No. 307H R0 mdv 24May22 Proposal Geodetic Report

(Def Plan)

<b>Report Date:</b>	May 26, 2022 - 12:06 PM	<b>Survey / DLS Computation:</b>	Minimum Curvature / Lubinski
<b>Client:</b>	Chevron	<b>Vertical Section Azimuth:</b>	179.730 ° (Grid North)
<b>Field:</b>	NM Lea County (NAD 27)	<b>Vertical Section Origin:</b>	0.000 ft, 0.000 ft
<b>Structure / Slot:</b>	Chevron Salado Draw Pad 305 / 307H	<b>TVD Reference Datum:</b>	RKB = 28ft
<b>Well:</b>	SD 14 23 FED P305 No. 307H	<b>TVD Reference Elevation:</b>	3235.000 ft above MSL
<b>Borehole:</b>	SD 14 23 FED P305 No. 307H	<b>Seabed / Ground Elevation:</b>	3207.000 ft above MSL
<b>UWI / API#:</b>	Unknown / Unknown	<b>Magnetic Declination:</b>	6.387 °
<b>Survey Name:</b>	SD 14 23 FED P305 No. 307H R0 mdv 24May22	<b>Total Gravity Field Strength:</b>	998.4329mgn (9.80665 Based)
<b>Survey Date:</b>	May 26, 2022	<b>Gravity Model:</b>	GARM
<b>Tort / AHD / DDI / ERD Ratio:</b>	107.014 ° / 11382.929 ft / 6.396 / 1.138	<b>Total Magnetic Field Strength:</b>	47436.403 nT
<b>Coordinate Reference System:</b>	NAD27 New Mexico State Plane, Eastern Zone, US Feet	<b>Magnetic Dip Angle:</b>	59.589 °
<b>Location Lat / Long:</b>	N 32° 2' 57.55702", W 103° 38' 38.76566"	<b>Declination Date:</b>	May 26, 2022
<b>Location Grid N/E Y/X:</b>	N 382350.000 ftUS, E 713546.000 ftUS	<b>Magnetic Declination Model:</b>	HDGM 2022
<b>CRS Grid Convergence Angle:</b>	0.3658 °	<b>North Reference:</b>	Grid North
<b>Grid Scale Factor:</b>	0.99996132	<b>Grid Convergence Used:</b>	0.3658 °
<b>Version / Patch:</b>	2.10.829.1	<b>Total Corr Mag North-&gt;Grid North:</b>	6.0208 °
		<b>Local Coord Referenced To:</b>	Well Head

Comments	MD (ft)	Incl (°)	Azim Grid (°)	TVD (ft)	VSEC (ft)	NS (ft)	EW (ft)	DLS (°/100ft)	Northing (ftUS)	Easting (ftUS)	Latitude (N/S ° ' ")	Longitude (E/W ° ' ")	
Surface	0.00	0.00	0.00	0.00	0.00	0.00	0.00	N/A	382350.00	713546.00	N 32 2 57.56	W 103 38 38.77	
Dockum (DCKM)	50.00	0.00	69.38	50.00	0.00	0.00	0.00	0.00	382350.00	713546.00	N 32 2 57.56	W 103 38 38.77	
	100.00	0.00	69.38	100.00	0.00	0.00	0.00	0.00	382350.00	713546.00	N 32 2 57.56	W 103 38 38.77	
	200.00	0.00	69.38	200.00	0.00	0.00	0.00	0.00	382350.00	713546.00	N 32 2 57.56	W 103 38 38.77	
	300.00	0.00	69.38	300.00	0.00	0.00	0.00	0.00	382350.00	713546.00	N 32 2 57.56	W 103 38 38.77	
Dewey Lake (DWLK)	400.00	0.00	69.38	400.00	0.00	0.00	0.00	0.00	382350.00	713546.00	N 32 2 57.56	W 103 38 38.77	
	500.00	0.00	69.38	500.00	0.00	0.00	0.00	0.00	382350.00	713546.00	N 32 2 57.56	W 103 38 38.77	
	600.00	0.00	69.38	600.00	0.00	0.00	0.00	0.00	382350.00	713546.00	N 32 2 57.56	W 103 38 38.77	
Rustler (RSLR)	685.08	0.00	69.38	685.08	0.00	0.00	0.00	0.00	382350.00	713546.00	N 32 2 57.56	W 103 38 38.77	
Build 1.5"/100ft	700.00	0.00	69.38	700.00	0.00	0.00	0.00	0.00	382350.00	713546.00	N 32 2 57.56	W 103 38 38.77	
	800.00	0.00	69.38	800.00	0.00	0.00	0.00	0.00	382350.00	713546.00	N 32 2 57.56	W 103 38 38.77	
	900.00	1.50	69.38	899.99	-0.46	0.46	1.23	1.50	382350.46	713547.23	N 32 2 57.56	W 103 38 38.75	
Los Medanos	970.06	2.55	69.38	970.00	-1.32	1.33	3.54	1.50	382351.33	713549.54	N 32 2 57.57	W 103 38 38.72	
Salado (SLDO)	1000.00	3.00	69.38	999.91	-1.82	1.84	4.90	1.50	382351.84	713550.90	N 32 2 57.57	W 103 38 38.71	
	1080.58	4.21	69.38	1080.33	-3.58	3.63	9.64	1.50	382353.63	713555.64	N 32 2 57.59	W 103 38 38.65	
	1100.00	4.50	69.38	1099.69	-4.09	4.15	11.02	1.50	382354.15	713557.02	N 32 2 57.60	W 103 38 38.64	
	1200.00	6.00	69.38	1199.27	-7.28	7.37	19.58	1.50	382357.37	713565.58	N 32 2 57.63	W 103 38 38.54	
Hold	1300.00	7.50	69.38	1298.57	-11.36	11.51	30.59	1.50	382361.51	713576.58	N 32 2 57.67	W 103 38 38.41	
	1333.32	8.00	69.38	1331.59	-12.92	13.09	34.79	1.50	382363.09	713580.79	N 32 2 57.68	W 103 38 38.36	
	1400.00	8.00	69.38	1397.62	-16.15	16.35	43.48	0.00	382366.35	713589.47	N 32 2 57.72	W 103 38 38.26	
	1500.00	8.00	69.38	1496.65	-20.99	21.25	56.50	0.00	382371.25	713602.50	N 32 2 57.76	W 103 38 38.11	
	1600.00	8.00	69.38	1595.67	-25.83	26.15	69.53	0.00	382376.15	713615.53	N 32 2 57.81	W 103 38 37.96	
	1700.00	8.00	69.38	1694.70	-30.67	31.05	82.55	0.00	382381.05	713628.55	N 32 2 57.86	W 103 38 37.80	
	1800.00	8.00	69.38	1793.73	-35.50	35.95	95.58	0.00	382385.95	713641.58	N 32 2 57.91	W 103 38 37.65	
	1900.00	8.00	69.38	1892.75	-40.34	40.85	108.61	0.00	382390.85	713654.60	N 32 2 57.95	W 103 38 37.50	
	2000.00	8.00	69.38	1991.78	-45.18	45.75	121.63	0.00	382395.75	713667.63	N 32 2 58.00	W 103 38 37.35	
	2100.00	8.00	69.38	2090.81	-50.02	50.65	134.66	0.00	382400.65	713680.65	N 32 2 58.05	W 103 38 37.20	
	2200.00	8.00	69.38	2189.83	-54.86	55.55	147.68	0.00	382405.55	713693.68	N 32 2 58.10	W 103 38 37.05	
	2300.00	8.00	69.38	2288.86	-59.70	60.45	160.71	0.00	382410.45	713706.70	N 32 2 58.15	W 103 38 36.89	
	2400.00	8.00	69.38	2387.89	-64.54	65.35	173.73	0.00	382415.35	713719.73	N 32 2 58.19	W 103 38 36.74	
	2500.00	8.00	69.38	2486.92	-69.37	70.25	186.76	0.00	382420.25	713732.75	N 32 2 58.24	W 103 38 36.59	
	2600.00	8.00	69.38	2585.94	-74.21	75.15	199.79	0.00	382425.15	713745.78	N 32 2 58.29	W 103 38 36.44	
	2700.00	8.00	69.38	2684.97	-79.05	80.05	212.81	0.00	382430.05	713758.80	N 32 2 58.34	W 103 38 36.29	
Castile (CSTL)	2800.00	8.00	69.38	2784.00	-83.89	84.95	225.84	0.00	382434.95	713771.83	N 32 2 58.38	W 103 38 36.14	
	2814.93	8.00	69.38	2798.78	-84.61	85.69	227.78	0.00	382435.68	713773.77	N 32 2 58.39	W 103 38 36.11	
	2900.00	8.00	69.38	2883.02	-88.73	89.85	238.86	0.00	382439.85	713784.85	N 32 2 58.43	W 103 38 35.98	
	3000.00	8.00	69.38	2982.05	-93.57	94.75	251.89	0.00	382444.75	713797.88	N 32 2 58.48	W 103 38 35.83	
	3100.00	8.00	69.38	3081.08	-98.41	99.65	264.91	0.00	382449.65	713810.90	N 32 2 58.53	W 103 38 35.68	
	3200.00	8.00	69.38	3180.10	-103.24	104.55	277.94	0.00	382454.55	713823.93	N 32 2 58.57	W 103 38 35.53	
	3300.00	8.00	69.38	3279.13	-108.08	109.45	290.97	0.00	382459.45	713836.95	N 32 2 58.62	W 103 38 35.38	
	3400.00	8.00	69.38	3378.16	-112.92	114.35	303.99	0.00	382464.35	713849.98	N 32 2 58.67	W 103 38 35.23	
	3500.00	8.00	69.38	3477.18	-117.76	119.25	317.02	0.00	382469.25	713863.00	N 32 2 58.72	W 103 38 35.07	
	3600.00	8.00	69.38	3576.21	-122.60	124.15	330.04	0.00	382474.15	713876.03	N 32 2 58.76	W 103 38 34.92	
	3700.00	8.00	69.38	3675.24	-127.44	129.05	343.07	0.00	382479.05	713889.06	N 32 2 58.81	W 103 38 34.77	
	3800.00	8.00	69.38	3774.26	-132.28	133.95	356.10	0.00	382483.95	713902.08	N 32 2 58.86	W 103 38 34.62	
	3900.00	8.00	69.38	3873.29	-137.11	138.85	369.12	0.00	382488.85	713915.11	N 32 2 58.91	W 103 38 34.47	
	4000.00	8.00	69.38	3972.32	-141.95	143.75	382.15	0.00	382493.75	713928.13	N 32 2 58.96	W 103 38 34.32	
	4100.00	8.00	69.38	4071.35	-146.79	148.65	395.17	0.00	382498.65	713941.16	N 32 2 59.00	W 103 38 34.16	
	4200.00	8.00	69.38	4170.37	-151.63	153.55	408.20	0.00	382503.55	713954.18	N 32 2 59.05	W 103 38 34.01	
4300.00	8.00	69.38	4269.40	-156.47	158.45	421.22	0.00	382508.45	713967.21	N 32 2 59.10	W 103 38 33.86		
4400.00	8.00	69.38	4368.43	-161.31	163.35	434.25	0.00	382513.35	713980.23	N 32 2 59.15	W 103 38 33.71		
4500.00	8.00	69.38	4467.45	-166.14	168.25	447.28	0.00	382518.25	713993.26	N 32 2 59.19	W 103 38 33.56		
4600.00	8.00	69.38	4566.48	-170.98	173.15	460.30	0.00	382523.15	714006.28	N 32 2 59.24	W 103 38 33.41		
Lamar (LMAR)	4652.19	8.00	69.38	4618.16	-173.51	175.71	467.10	0.00	382525.70	714013.08	N 32 2 59.27	W 103 38 33.33	
Bell Canyon (BLCN)	4657.04	8.00	69.38	4622.96	-173.74	175.95	467.73	0.00	382525.94	714013.71	N 32 2 59.27	W 103 38 33.32	
	4700.00	8.00	69.38	4665.51	-175.82	178.05	473.33	0.00	382528.05	714019.31	N 32 2 59.29	W 103 38 33.25	
	4800.00	8.00	69.38	4764.53	-180.66	182.95	486.35	0.00	382532.95	714032.33	N 32 2 59.34	W 103 38 33.10	
	4900.00	8.00	69.38	4863.56	-185.50	187.85	499.38	0.00	382537.85	714045.36	N 32 2 59.38	W 103 38 32.95	
	5000.00	8.00	69.38	4962.59	-190.34	192.75	512.40	0.00	382542.75	714058.38	N 32 2 59.43	W 103 38 32.80	
	5100.00	8.00	69.38	5061.61	-195.18	197.65	525.43	0.00	382547.65	714071.41	N 32 2 59.48	W 103 38 32.65	
	5200.00	8.00	69.38	5160.64	-200.01	202.55	538.46	0.00	382552.55	714084.43	N 32 2 59.53	W 103 38 32.49	
	5300.00	8.00	69.38	5259.67	-204.85	207.45	551.48	0.00	382557.45	714097.46	N 32 2 59.58	W 103 38 32.34	
	5400.00	8.00	69.38	5358.69	-209.69	212.35	564.51	0.00	382562.35	714110.48	N 32 2 59.62	W 103 38 32.19	
	5500.00	8.00	69.38	5457.72	-214.53	217.25	577.53	0.00	382567.25	714123.51	N 32 2 59.67	W 103 38 32.04	
	5600.00	8.00	69.38	5556.75	-219.37	222.15	590.56	0.00	382572.15	714136.53	N 32 2 59.72	W 103 38 31.89	
	5700.00	8.00	69.38	5655.78	-224.21	227.05	603.58	0.00	382577.05	714149.56	N 32 2 59.77	W 103 38 31.74	
	Cherry Canyon (CRCN)	5703.31	8.00	69.38	5659.05	-224.37	227.22	604.02	0.00	382577.21	714149.99	N 32 2 59.77	W 103 38 31.73
	Drop .75"/100ft	5800.00	8.00	69.38	5754.80	-229.05	231.95	616.61	0.00	382581.94	714162.59	N 32 2 59.81	W 103 38 31.58
		5900.00	8.00	69.38	5853.83	-233.88	236.85	629.64	0.00	382586.84	714175.61	N 32 2 59.86	W 103 38 31.43
		5981.24	8.00	69.38	5934.28	-237.82	240.83	640.22	0.00	382590.83	714186.19	N 32 2 59.90	W 103 38 31.31
6000.00		7.86	69.38	5952.86	-238.72	241.75	642.64	0.75	382591.74	714188.61	N 32 2 59.91	W 103 38 31.28	
6100.00		7.11	69.38	6052.01	-243.24	246.33	654.83	0.75	382596.32	714200.80	N 32 2 59.95	W 103 38 31.14	
6200.00		6.36	69.38	6151.32	-247.32	250.46	665.81	0.75	382600.45	714211.78	N 32 2 59.99	W 103 38 31.01	
6300.00		5.61	69.38	6250.77	-250.95	254.13	675.56	0.75	382604.12	714221.54	N 32 3 0.03	W 103 38 30.90	
6400.00		4.86	69.38	6350.35	-254.12	257.34	684.10	0.75	382607.33	714230.07	N 32 3 0.06	W 103 38 30.80	
6500.00		4.11	69.38	6450.05	-256.83	260.10	691.42	0.75	382610.09	714237.39	N 32 3 0.09	W 103 38 30.71	

Comments	MD (ft)	Incl (°)	Azim Grid (°)	TVD (ft)	VSEC (ft)	NS (ft)	EW (ft)	DLS (°/100ft)	Northing (RUS)	Easting (RUS)	Latitude (N/S ° ' ")	Longitude (E/W ° ' ")
Hold	6600.00	3.36	69.38	6549.83	-259.10	262.39	697.52	0.75	382612.38	714243.49	N 32 3 0.11	W 103 38 30.64
	6700.00	2.61	69.38	6649.70	-260.91	264.22	702.39	0.75	382614.21	714248.36	N 32 3 0.13	W 103 38 30.59
	6800.00	1.86	69.38	6749.62	-262.26	265.59	706.04	0.75	382615.58	714252.01	N 32 3 0.14	W 103 38 30.54
	6900.00	1.11	69.38	6849.59	-263.16	266.51	708.46	0.75	382616.50	714254.43	N 32 3 0.15	W 103 38 30.51
	7000.00	0.36	69.38	6949.58	-263.61	266.96	709.66	0.75	382616.95	714255.63	N 32 3 0.15	W 103 38 30.50
	7047.87	0.00	69.38	6997.45	-263.66	267.01	709.80	0.75	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	7100.00	0.00	69.38	7049.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	7200.00	0.00	69.38	7149.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	7271.20	0.00	69.38	7220.78	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	7300.00	0.00	69.38	7249.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
Brushy Canyon (BCN)	7400.00	0.00	69.38	7349.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	7500.00	0.00	69.38	7449.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	7600.00	0.00	69.38	7549.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	7700.00	0.00	69.38	7649.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	7800.00	0.00	69.38	7749.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	7900.00	0.00	69.38	7849.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	8000.00	0.00	69.38	7949.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	8100.00	0.00	69.38	8049.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	8200.00	0.00	69.38	8149.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	8300.00	0.00	69.38	8249.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	8400.00	0.00	69.38	8349.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	8500.00	0.00	69.38	8449.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	8600.00	0.00	69.38	8549.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	8700.00	0.00	69.38	8649.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	8800.00	0.00	69.38	8749.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	8900.00	0.00	69.38	8849.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	8960.65	0.00	69.38	8910.23	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	8975.14	0.00	69.38	8924.72	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	9000.00	0.00	69.38	8949.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	9100.00	0.00	69.38	9049.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	9200.00	0.00	69.38	9149.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	9300.00	0.00	69.38	9249.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	9370.93	0.00	69.38	9320.51	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	9400.00	0.00	69.38	9349.58	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	9457.87	0.00	69.38	9407.45	-263.66	267.01	709.80	0.00	382617.00	714255.77	N 32 3 0.15	W 103 38 30.50
	9500.00	4.21	179.66	9449.54	-262.11	265.46	709.81	10.00	382615.45	714255.78	N 32 3 0.14	W 103 38 30.50
	9600.00	14.21	179.66	9548.12	-246.12	249.47	709.90	10.00	382599.46	714255.87	N 32 2 59.98	W 103 38 30.50
	9698.80	24.09	179.66	9641.34	-213.75	217.10	710.09	10.00	382567.09	714256.07	N 32 2 59.66	W 103 38 30.50
	9700.00	24.21	179.66	9642.43	-213.26	216.61	710.10	10.00	382566.60	714256.07	N 32 2 59.66	W 103 38 30.50
	9799.27	34.14	179.66	9729.00	-164.93	168.28	710.38	10.00	382518.27	714256.35	N 32 2 59.18	W 103 38 30.50
	9800.00	34.21	179.66	9729.60	-164.52	167.87	710.39	10.00	382517.86	714256.36	N 32 2 59.17	W 103 38 30.50
	9878.10	42.02	179.66	9791.00	-116.35	119.70	710.67	10.00	382469.69	714256.64	N 32 2 58.70	W 103 38 30.50
	9900.00	44.21	179.66	9806.99	-101.38	104.73	710.76	10.00	382454.72	714256.73	N 32 2 58.55	W 103 38 30.50
	10000.00	54.21	179.66	9872.23	-25.76	29.11	711.21	10.00	382379.11	714257.18	N 32 2 57.80	W 103 38 30.50
	10100.00	64.21	179.66	9923.35	60.04	-56.69	711.71	10.00	382293.32	714257.68	N 32 2 56.95	W 103 38 30.50
	10200.00	74.21	179.66	9958.79	153.41	-150.06	712.26	10.00	382199.95	714258.23	N 32 2 56.03	W 103 38 30.50
	10300.00	84.21	179.66	9977.49	251.52	-248.16	712.84	10.00	382101.85	714258.81	N 32 2 55.06	W 103 38 30.50
	10350.62	89.27	179.66	9980.36	302.04	-298.68	713.14	10.00	382051.33	714259.11	N 32 2 54.56	W 103 38 30.50
	10400.00	89.27	179.66	9980.99	351.42	-348.06	713.43	0.00	382001.95	714259.40	N 32 2 54.07	W 103 38 30.50
	10500.00	89.27	179.66	9982.25	451.41	-448.05	714.02	0.00	381901.97	714260.00	N 32 2 53.08	W 103 38 30.50
	10600.00	89.27	179.66	9983.52	551.40	-548.04	714.61	0.00	381801.98	714260.59	N 32 2 52.09	W 103 38 30.50
	10700.00	89.27	179.66	9984.79	651.39	-648.03	715.21	0.00	381702.00	714261.18	N 32 2 51.10	W 103 38 30.50
	10800.00	89.27	179.66	9986.05	751.39	-748.02	715.80	0.00	381602.01	714261.77	N 32 2 50.11	W 103 38 30.51
	10900.00	89.27	179.66	9987.32	851.38	-848.01	716.39	0.00	381502.02	714262.36	N 32 2 49.12	W 103 38 30.51
	11000.00	89.27	179.66	9988.58	951.37	-948.00	716.98	0.00	381402.04	714262.95	N 32 2 48.13	W 103 38 30.51
	11100.00	89.27	179.66	9989.85	1051.36	-1047.99	717.57	0.00	381302.05	714263.54	N 32 2 47.14	W 103 38 30.51
	11200.00	89.27	179.66	9991.12	1151.35	-1147.98	718.16	0.00	381202.07	714264.13	N 32 2 46.15	W 103 38 30.51
	11300.00	89.27	179.66	9992.38	1251.34	-1247.97	718.75	0.00	381102.08	714264.72	N 32 2 45.16	W 103 38 30.51
	11400.00	89.27	179.66	9993.65	1351.34	-1347.96	719.34	0.00	381002.09	714265.31	N 32 2 44.17	W 103 38 30.51
	11500.00	89.27	179.66	9994.91	1451.33	-1447.95	719.93	0.00	380902.11	714265.90	N 32 2 43.18	W 103 38 30.51
	11600.00	89.27	179.66	9996.18	1551.32	-1547.94	720.52	0.00	380802.12	714266.49	N 32 2 42.19	W 103 38 30.51
	11700.00	89.27	179.66	9997.45	1651.31	-1647.93	721.11	0.00	380702.13	714267.08	N 32 2 41.20	W 103 38 30.51
	11800.00	89.27	179.66	9998.71	1751.30	-1747.92	721.70	0.00	380602.15	714267.67	N 32 2 40.21	W 103 38 30.51
	11900.00	89.27	179.66	9999.98	1851.30	-1847.91	722.29	0.00	380502.16	714268.26	N 32 2 39.23	W 103 38 30.51
	11934.97	89.27	179.66	10000.42	1886.26	-1882.88	722.50	0.00	380467.20	714268.47	N 32 2 38.88	W 103 38 30.51
	11977.49	90.13	179.66	10000.64	1928.78	-1						

Comments	MD (ft)	Incl (°)	Azim Grid (°)	TVD (ft)	VSEC (ft)	NS (ft)	EW (ft)	DLS (°/100ft)	Northing (ftUS)	Easting (ftUS)	Latitude (N/S ° ' ")	Longitude (E/W ° ' ")
	15500.00	91.01	179.76	9986.76	5451.22	-5447.78	742.81	0.00	376902.44	714288.78	N 32 2 3.60	W 103 38 30.54
	15600.00	91.01	179.76	9985.00	5551.21	-5547.77	743.23	0.00	376802.46	714289.20	N 32 2 2.61	W 103 38 30.54
	15700.00	91.01	179.76	9983.24	5651.19	-5647.75	743.64	0.00	376702.48	714289.61	N 32 2 1.62	W 103 38 30.55
	15800.00	91.01	179.76	9981.48	5751.17	-5747.73	744.05	0.00	376602.50	714290.02	N 32 2 0.63	W 103 38 30.55
	15900.00	91.01	179.76	9979.72	5851.16	-5847.72	744.46	0.00	376502.52	714290.43	N 32 1 59.64	W 103 38 30.55
	16000.00	91.01	179.76	9977.96	5951.14	-5947.70	744.87	0.00	376402.54	714290.84	N 32 1 58.65	W 103 38 30.55
	16100.00	91.01	179.76	9976.20	6051.13	-6047.68	745.28	0.00	376302.56	714291.25	N 32 1 57.66	W 103 38 30.56
	16200.00	91.01	179.76	9974.44	6151.11	-6147.67	745.70	0.00	376202.58	714291.67	N 32 1 56.68	W 103 38 30.56
	16300.00	91.01	179.76	9972.67	6251.10	-6247.65	746.11	0.00	376102.60	714292.08	N 32 1 55.69	W 103 38 30.56
	16400.00	91.01	179.76	9970.91	6351.08	-6347.63	746.52	0.00	376002.62	714292.49	N 32 1 54.70	W 103 38 30.56
	16500.00	91.01	179.76	9969.15	6451.07	-6447.62	746.93	0.00	375902.64	714292.90	N 32 1 53.71	W 103 38 30.57
	16600.00	91.01	179.76	9967.39	6551.05	-6547.60	747.34	0.00	375802.66	714293.31	N 32 1 52.72	W 103 38 30.57
	16700.00	91.01	179.76	9965.63	6651.03	-6647.59	747.75	0.00	375702.69	714293.72	N 32 1 51.73	W 103 38 30.57
	16800.00	91.01	179.76	9963.87	6751.02	-6747.57	748.17	0.00	375602.71	714294.14	N 32 1 50.74	W 103 38 30.58
	16900.00	91.01	179.76	9962.11	6851.00	-6847.55	748.58	0.00	375502.73	714294.55	N 32 1 49.75	W 103 38 30.58
	17000.00	91.01	179.76	9960.35	6950.99	-6947.54	748.99	0.00	375402.75	714294.96	N 32 1 48.76	W 103 38 30.58
	17100.00	91.01	179.76	9958.59	7050.97	-7047.52	749.40	0.00	375302.77	714295.37	N 32 1 47.77	W 103 38 30.58
	17200.00	91.01	179.76	9956.83	7150.96	-7147.50	749.81	0.00	375202.79	714295.78	N 32 1 46.78	W 103 38 30.59
	17300.00	91.01	179.76	9955.06	7250.94	-7247.49	750.22	0.00	375102.81	714296.19	N 32 1 45.79	W 103 38 30.59
	17400.00	91.01	179.76	9953.30	7350.93	-7347.47	750.64	0.00	375002.83	714296.61	N 32 1 44.80	W 103 38 30.59
	17500.00	91.01	179.76	9951.54	7450.91	-7447.45	751.05	0.00	374902.85	714297.02	N 32 1 43.81	W 103 38 30.59
	17600.00	91.01	179.76	9949.78	7550.90	-7547.44	751.46	0.00	374802.87	714297.43	N 32 1 42.82	W 103 38 30.60
	17700.00	91.01	179.76	9948.02	7650.88	-7647.42	751.87	0.00	374702.89	714297.84	N 32 1 41.83	W 103 38 30.60
	17800.00	91.01	179.76	9946.26	7750.86	-7747.41	752.28	0.00	374602.91	714298.25	N 32 1 40.84	W 103 38 30.60
	17900.00	91.01	179.76	9944.50	7850.85	-7847.39	752.70	0.00	374502.93	714298.66	N 32 1 39.86	W 103 38 30.60
	18000.00	91.01	179.76	9942.74	7950.83	-7947.37	753.11	0.00	374402.95	714299.08	N 32 1 38.87	W 103 38 30.61
	18100.00	91.01	179.76	9940.98	8050.82	-8047.36	753.52	0.00	374302.97	714299.49	N 32 1 37.88	W 103 38 30.61
	18200.00	91.01	179.76	9939.22	8150.80	-8147.34	753.93	0.00	374202.99	714299.90	N 32 1 36.89	W 103 38 30.61
	18300.00	91.01	179.76	9937.45	8250.79	-8247.32	754.34	0.00	374103.01	714300.31	N 32 1 35.90	W 103 38 30.62
	18400.00	91.01	179.76	9935.69	8350.77	-8347.31	754.75	0.00	374003.03	714300.72	N 32 1 34.91	W 103 38 30.62
	18500.00	91.01	179.76	9933.93	8450.76	-8447.29	755.17	0.00	373903.05	714301.13	N 32 1 33.92	W 103 38 30.62
	18600.00	91.01	179.76	9932.17	8550.74	-8547.27	755.58	0.00	373803.07	714301.55	N 32 1 32.93	W 103 38 30.62
	18700.00	91.01	179.76	9930.41	8650.72	-8647.26	755.99	0.00	373703.09	714301.96	N 32 1 31.94	W 103 38 30.63
	18800.00	91.01	179.76	9928.65	8750.71	-8747.24	756.40	0.00	373603.11	714302.37	N 32 1 30.95	W 103 38 30.63
	18900.00	91.01	179.76	9926.89	8850.69	-8847.23	756.81	0.00	373503.13	714302.78	N 32 1 29.96	W 103 38 30.63
	19000.00	91.01	179.76	9925.13	8950.68	-8947.21	757.22	0.00	373403.16	714303.19	N 32 1 28.97	W 103 38 30.63
	19100.00	91.01	179.76	9923.37	9050.66	-9047.19	757.64	0.00	373303.18	714303.60	N 32 1 27.98	W 103 38 30.64
	19200.00	91.01	179.76	9921.61	9150.65	-9147.18	758.05	0.00	373203.20	714304.02	N 32 1 26.99	W 103 38 30.64
	19300.00	91.01	179.76	9919.84	9250.63	-9247.16	758.46	0.00	373103.22	714304.43	N 32 1 26.00	W 103 38 30.64
	19400.00	91.01	179.76	9918.08	9350.62	-9347.14	758.87	0.00	373003.24	714304.84	N 32 1 25.01	W 103 38 30.64
	19500.00	91.01	179.76	9916.32	9450.60	-9447.13	759.28	0.00	372903.26	714305.25	N 32 1 24.02	W 103 38 30.65
	19600.00	91.01	179.76	9914.56	9550.58	-9547.11	759.69	0.00	372803.28	714305.66	N 32 1 23.03	W 103 38 30.65
	19700.00	91.01	179.76	9912.80	9650.57	-9647.09	760.11	0.00	372703.30	714306.08	N 32 1 22.05	W 103 38 30.65
	19800.00	91.01	179.76	9911.04	9750.55	-9747.08	760.52	0.00	372603.32	714306.49	N 32 1 21.06	W 103 38 30.65
	19900.00	91.01	179.76	9909.28	9850.54	-9847.06	760.93	0.00	372503.34	714306.90	N 32 1 20.07	W 103 38 30.66
	20000.00	91.01	179.76	9907.52	9950.52	-9947.05	761.34	0.00	372403.36	714307.31	N 32 1 19.08	W 103 38 30.66
	20100.00	91.01	179.76	9905.76	10050.51	-10047.03	761.75	0.00	372303.38	714307.72	N 32 1 18.09	W 103 38 30.66
	20200.00	91.01	179.76	9904.00	10150.49	-10147.01	762.16	0.00	372203.40	714308.13	N 32 1 17.10	W 103 38 30.67
	20300.00	91.01	179.76	9902.23	10250.48	-10247.00	762.58	0.00	372103.42	714308.55	N 32 1 16.11	W 103 38 30.67
LTP Cross	20335.31	91.01	179.76	9901.61	10285.78	-10282.30	762.72	0.00	372068.12	714308.69	N 32 1 15.76	W 103 38 30.67
	20400.00	91.01	179.76	9900.47	10350.46	-10346.98	762.99	0.00	372003.44	714308.96	N 32 1 15.12	W 103 38 30.67
SD 14 23 FED P305 No. 307H BHL	20410.44	91.01	179.76	9900.29	10360.90	-10357.42	763.03	0.00	371993.00	714309.00	N 32 1 15.02	W 103 38 30.67

Survey Type: Def Plan

Survey Error Model: ISCWSA Rev 3 \*\*\* 3-D 97.071% Confidence 3.0000 sigma  
Survey Program:

Description	Part	MD From (ft)	MD To (ft)	EOU Freq (ft)	Hole Size (in)	Casing Diameter (in)	Expected Max Inclination (deg)	Survey Tool Type	Borehole / Survey
	1	0.000	28.000	1/100.000	30.000	30.000		B001Mb_MWD+HRGM-Depth Only	SD 14 23 FED P305 No. 307H / SD 14 23 FED P305 No. 307H R0 mdv 24May22
	1	28.000	20410.443	1/100.000	30.000	30.000		B001Mb_MWD+HRGM	SD 14 23 FED P305 No. 307H / SD 14 23 FED P305 No. 307H R0

## PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	EOG Resources Inc
WELL NAME & NO.:	LAKEWOOD 28 FED COM 742H
LOCATION:	Section 28, T.25S., R.34E.
COUNTY:	Lea County, New Mexico

COA

H2S	<input checked="" type="radio"/> Yes	<input type="radio"/> No	
Potash	<input checked="" type="radio"/> None	<input type="radio"/> Secretary	<input type="radio"/> R-111-P
Cave/Karst Potential	<input checked="" type="radio"/> Low	<input type="radio"/> Medium	<input type="radio"/> High
Cave/Karst Potential	<input type="radio"/> Critical		
Variance	<input type="radio"/> None	<input checked="" type="radio"/> Flex Hose	<input type="radio"/> Other
Wellhead	<input type="radio"/> Conventional	<input checked="" type="radio"/> Multibowl	<input type="radio"/> Both
Wellhead Variance	<input type="radio"/> Diverter		
Other	<input type="checkbox"/> 4 String	<input type="checkbox"/> Capitan Reef	<input type="checkbox"/> WIPP
Other	<input checked="" type="checkbox"/> Fluid Filled	<input type="checkbox"/> Pilot Hole	<input type="checkbox"/> Open Annulus
Cementing	<input type="checkbox"/> Contingency Cement Squeeze	<input checked="" type="checkbox"/> EchoMeter	<input checked="" type="checkbox"/> Primary Cement Squeeze
Special Requirements	<input type="checkbox"/> Water Disposal	<input checked="" type="checkbox"/> COM	<input type="checkbox"/> Unit
Special Requirements	<input type="checkbox"/> Batch Sundry		
Special Requirements Variance	<input checked="" type="checkbox"/> Break Testing	<input checked="" type="checkbox"/> Offline Cementing	<input checked="" type="checkbox"/> Casing Clearance

### A. HYDROGEN SULFIDE

A Hydrogen Sulfide (H2S) Drilling Plan shall be activated AT SPUD. As a result, the Hydrogen Sulfide area must meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, please provide measured values and formations to the BLM.

### B. CASING

#### Primary Casing Design:

1. The **9-5/8** inch surface casing shall be set at approximately **930** feet (a minimum of 25 feet (Lea County) into the Rustler Anhydrite, above the salt, and below usable fresh water) and cemented to the surface.
  - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run

- to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
- b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
  - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
  - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The **7-5/8** inch intermediate casing shall be set at approximately **12,130 feet TVD**. The minimum required fill of cement behind the **7-5/8** inch intermediate casing is:

**Option 1 (Single Stage):**

- Cement to surface. If cement does not circulate see B.1.a, c-d above.

**Option 2:**

Operator has proposed to cement in two stages by conventionally cementing the first stage and performing a bradenhead squeeze on the second stage, contingent upon no returns to surface.

- a. First stage: Operator will cement with intent to reach the top of the **Brushy Canyon**
- b. Second stage:
  - Operator will perform bradenhead squeeze and top-out. Cement to surface. If cement does not reach surface, the appropriate BLM office shall be notified.

**Operator has proposed to pump down 7-5/8" X 9-5/8" annulus. Operator must top out cement after the bradenhead squeeze and verify cement to surface. Operator can also check TOC with Echo-meter. CBL must be run from TD of the 7-5/8" casing to surface if confidence is lacking on the quality of the bradenhead squeeze cement job. Submit results to BLM.**

**If cement does not tie-back into the previous casing shoe, a third stage remediation BH may be performed. The appropriate BLM office shall be notified.**

**Bradenhead squeeze in the production interval is only as an edge case remediation measure and is NOT approved in this COA. If production cement job experiences losses and a bradenhead squeeze is needed for tie-back, BLM Engineering should be**

**notified prior to job with volumes and planned wellbore schematic. CBL will be needed when this occurs.**

**If cement does not reach surface, the next casing string must come to surface.**

**Operator must use a limited flush fluid volume of 1 bbl following backside cementing procedures.**

3. The **5-1/2** inch production casing shall be set at approximately **23,410** feet. The minimum required fill of cement behind the **5-1/2** inch production casing is:

**Option 1 (Single Stage):**

- Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

**Alternate Casing Design:**

1. The **10-3/4** inch surface casing shall be set at approximately **930** feet (a minimum of 25 feet (Lea County) into the Rustler Anhydrite, above the salt, and below usable fresh water) and cemented to the surface.
  - e. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
  - f. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
  - g. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
  - h. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The **8-3/4** inch intermediate casing shall be set at approximately **12,130 feet TVD**. The minimum required fill of cement behind the **8-3/4** inch intermediate casing is:

**Option 1 (Single Stage):**

- Cement to surface. If cement does not circulate see B.1.a, c-d above.

**Option 2:**

Operator has proposed to cement in two stages by conventionally cementing the first stage and performing a bradenhead squeeze on the second stage, contingent upon no returns to surface.

- c. First stage: Operator will cement with intent to reach the top of the **Brushy Canyon**
- d. Second stage:
  - Operator will perform bradenhead squeeze and top-out. Cement to surface. If cement does not reach surface, the appropriate BLM office shall be notified.

**Operator has proposed to pump down 10-3/4 X 8-3/4" annulus. Operator must top out cement after the bradenhead squeeze and verify cement to surface. Operator can also check TOC with Echo-meter. CBL must be run from TD of the 8-3/4" casing to surface if confidence is lacking on the quality of the bradenhead squeeze cement job. Submit results to BLM.**

**If cement does not tie-back into the previous casing shoe, a third stage remediation BH may be performed. The appropriate BLM office shall be notified.**

**Bradenhead squeeze in the production interval is only as an edge case remediation measure and is NOT approved in this COA. If production cement job experiences losses and a bradenhead squeeze is needed for tie-back, BLM Engineering should be notified prior to job with volumes and planned wellbore schematic. CBL will be needed when this occurs.**

**If cement does not reach surface, the next casing string must come to surface.**

**Operator must use a limited flush fluid volume of 1 bbl following backside cementing procedures.**

**Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.**

3. The **6** inch production casing shall be set at approximately **23,410** feet. The minimum required fill of cement behind the **6** inch production casing is:

**Option 1 (Single Stage):**

- Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

**Production casing must be kept fluid filled to meet BLM minimum collapse requirement.**



### C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'
2. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **10,000 (10M) psi. Variance is approved to use a 5000 (5M) Annular which shall be tested to 3500 (70% Working Pressure) psi.**
  - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
  - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
  - c. Manufacturer representative shall install the test plug for the initial BOP test.
  - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
  - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

### D. SPECIAL REQUIREMENT (S)

#### Communitization Agreement

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- The operator will submit an as-drilled survey well plat of the well completion, but are not limited to, those specified in Onshore Order 1 and 2.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

**(Note: For a minimum 5M BOPE or less (Utilizing a 10M BOPE system) BOPE Break Testing Variance**



- BOPE Break Testing is ONLY permitted for 5M BOPE or less. (**Annular preventer must be tested to a minimum of 70% of BOPE working pressure and shall be higher than the MASP**)
- BOPE Break Testing is NOT permitted to drilling the production hole section.
- Variance only pertains to the intermediate hole-sections and no deeper than the Bone Springs formation.
- While in transfer between wells, the BOPE shall be secured by the hydraulic carrier or cradle.
- Any well control event while drilling require notification to the BLM Petroleum Engineer (**575-706-2779**) prior to the commencement of any BOPE Break Testing operations.
- A full BOPE test is required prior to drilling the first deep intermediate hole section. If any subsequent hole interval is deeper than the first, a full BOPE test will be required. (200' TVD tolerance between intermediate shoes is allowable).
- The BLM is to be contacted (575-689-5981 Lea County) 4 hours prior to BOPE tests.
- As a minimum, a full BOPE test shall be performed at 21-day intervals.
- In the event any repairs or replacement of the BOPE is required, the BOPE shall test as per 43 CFR part 3170 Subpart 3172.
- If in the event break testing is not utilized, then a full BOPE test would be conducted.

#### **Offline Cementing**

Offline cementing approved for surface and intermediate intervals. Contact the BLM PETs prior to the commencement of any offline cementing procedure.

## **GENERAL REQUIREMENTS**

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

#### **Contact Eddy County Petroleum Engineering Inspection Staff:**

Email or call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220; [BLM NM CFO DrillingNotifications@BLM.GOV](mailto:BLM_NM_CFO_DrillingNotifications@BLM.GOV); (575) 361-2822

#### **Contact Lea County Petroleum Engineering Inspection Staff:**

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575) 689-5981

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
  - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
  - b. When the operator proposes to set surface casing with Spudder Rig

- i. Notify the BLM when moving in and removing the Spudder Rig.
  - ii. Notify the BLM when moving in the 2<sup>nd</sup> Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
  - iii. BOP/BOPE test to be conducted per **43 CFR 3172** as soon as 2<sup>nd</sup> Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. For intervals in which cement to surface is required, cement to surface should be verified with a visual check and density or pH check to differentiate cement from spacer and drilling mud. The results should be documented in the driller's log and daily reports.

#### A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends of both lead and tail cement, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.

7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-Q potash area, the NMOCD requirements shall be followed.

#### **B. PRESSURE CONTROL**

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in **43 CFR 3172**.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
  - i. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
  - ii. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
  - iii. Manufacturer representative shall install the test plug for the initial BOP test.
  - iv. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172.6(b)(9) must be followed.
  - v. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
  - i. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead cement), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
  - ii. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the cement plug. The BOPE test can be initiated after bumping the cement plug with the casing

- valve open. (only applies to single stage cement jobs, prior to the cement setting up.)
- iii. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer and can be initiated immediately with the casing valve open. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to **43 CFR 3172** with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for 8 hours or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
  - iv. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
  - v. The results of the test shall be reported to the appropriate BLM office.
  - vi. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
  - vii. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
  - viii. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per **43 CFR 3172**.

#### C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

#### D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area. Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

KPI 9/18/2024



# H<sub>2</sub>S Preparedness and Contingency Plan Summary

## Training

MCBU Drilling and Completions H<sub>2</sub>S training requirements are intended to define the minimum level of training required for employees, contractors and visitors to enter or perform work at MCBU Drilling and Completions locations that have known concentrations of H<sub>2</sub>S.

## Awareness Level

Employees and visitors to MCBU Drilling and Completions locations that have known concentrations of H<sub>2</sub>S, who are not required to perform work in H<sub>2</sub>S areas, will be provided with an awareness level of H<sub>2</sub>S training prior to entering any H<sub>2</sub>S areas. At a minimum, awareness level training will include:

1. Physical and chemical properties of H<sub>2</sub>S
2. Health hazards of H<sub>2</sub>S
3. Personal protective equipment
4. Information regarding potential sources of H<sub>2</sub>S
5. Alarms and emergency evacuation procedures

Awareness level training will be developed and conducted by personnel who are qualified either by specific training, educational experience and/or work-related background.

## Advanced Level H<sub>2</sub>S Training

Employees and contractors required to work in areas that may contain H<sub>2</sub>S will be provided with Advanced Level H<sub>2</sub>S training prior to initial assignment. In addition to the Awareness Level requirements, Advanced Level H<sub>2</sub>S training will include:

1. H<sub>2</sub>S safe work practice procedures;
2. Emergency contingency plan procedures;
3. Methods to detect the presence or release of H<sub>2</sub>S (e.g., alarms, monitoring equipment), including hands-on training with direct reading and personal monitoring H<sub>2</sub>S equipment.
4. Basic overview of respiratory protective equipment suitable for use in H<sub>2</sub>S environments. Note: Employees who work at sites that participate in the Chevron Respirator User program will require separate respirator training as required by the MCBU Respiratory Protection Program;
5. Basic overview of emergency rescue techniques, first aid, CPR and medical evaluation procedures. Employees who may be required to perform "standby" duties are required to receive additional first aid and CPR training, which is not covered in the Advanced Level H<sub>2</sub>S training;
6. Proficiency examination covering all course material.

Advanced H<sub>2</sub>S training courses will be instructed by personnel who have successfully completed an appropriate H<sub>2</sub>S train-the-trainer development course (ANSI/ASSE Z390.1-2006) or who possess significant past experience through educational or work-related background.

# H<sub>2</sub>S Preparedness and Contingency Plan Summary

## H<sub>2</sub>S Training Certification

All employees and visitors will be issued an H<sub>2</sub>S training certification card (or certificate) upon successful completion of the appropriate H<sub>2</sub>S training course. Personnel working in an H<sub>2</sub>S environment will carry a current H<sub>2</sub>S training certification card as proof of having received the proper training on their person at all times.

## Briefing Area

A minimum of two briefing areas will be established in locations that at least one area will be upwind from the well at all times. Upon recognition of an emergency situation, all personnel should assemble at the designated upwind briefing areas for instructions.

## H<sub>2</sub>S Equipment

### Respiratory Protection

- a) Six 30 minute SCBAs – 2 at each briefing area and 2 in the Safety Trailer.
- b) Eight 5 minute EBAs – 5 in the dog house at the rig floor, 1 at the accumulator, 1 at the shale shakers and 1 at the mud pits.

## Visual Warning System

- a) One color code sign, displaying all possible conditions, will be placed at the entrance to the location with a flag displaying the current condition.
- b) Two windsocks will be on location, one on the dog house and one on the Drill Site Manager's Trailer.

## H<sub>2</sub>S Detection and Monitoring System

- a) H<sub>2</sub>S monitoring system (sensor head, warning light and siren) placed throughout rig.
  - Drilling Rig Locations: at a minimum, in the area of the Shale shaker, rig floor, and bell nipple.
  - Workover Rig Locations: at a minimum, in the area of the Cellar, rig floor and circulating tanks or shale shaker.



## H<sub>2</sub>S Preparedness and Contingency Plan Summary

### Well Control Equipment

- a) Flare Line 150' from wellhead with igniter.
- b) Choke manifold with a remotely operated choke.
- c) Mud / gas separator

### Mud Program

In the event of drilling, completions, workover and well servicing operations involving a hydrogen sulfide concentration of 100 ppm or greater the following shall be considered:

- 1. Use of a degasser
- 2. Use of a zinc based mud treatment
- 3. Increasing mud weight

### Public Safety - Emergency Assistance

<u>Agency</u>	<u>Telephone Number</u>
Lea County Sheriff's Department	575-396-3611
Fire Department:	
Carlsbad	575-885-3125
Artesia	575-746-5050
Lea County Regional Medical Center	575-492-5000
Jal Community Hospital	505-395-2511
Lea County Emergency Management	575-396-8602
Poison Control Center	800-222-1222



## H<sub>2</sub>S Preparedness and Contingency Plan Summary

### Chevron MCBU D&C Emergency Notifications


Below are lists of contacts to be used in emergency situations.


	Name	Title	Office Number	Cell Phone
1.	<b>TBD</b>	Drilling Engineer		
2.	Sergio Hernandez	Superintendent	713 372 1402	
5.	Dennis Mchugh	Drilling Manager	(713) 372-4496	
6.	Kyle Eastman	Operations Manager	713-372-5863	
7.	TBD	D&C HES		
8.	TBD	Completion Engineer		





## H<sub>2</sub>S Preparedness and Contingency Plan Summary

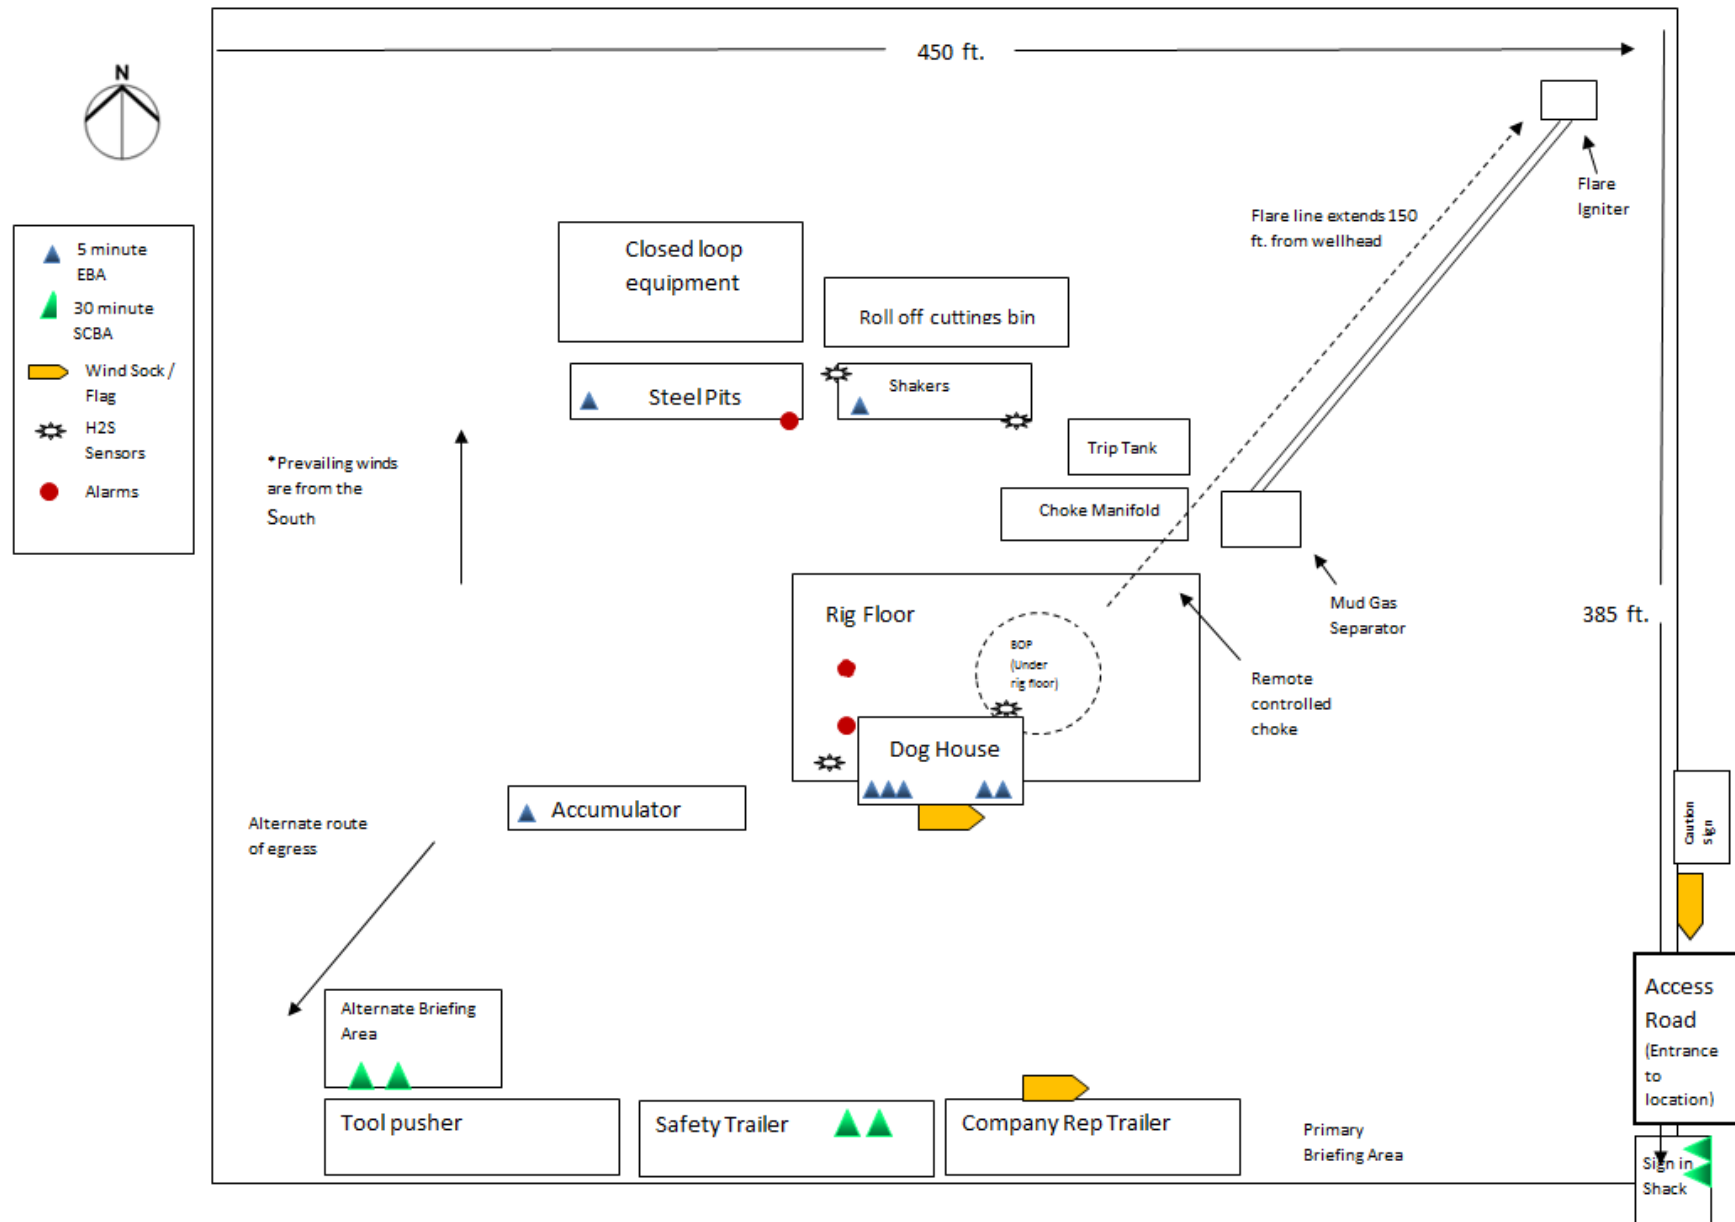

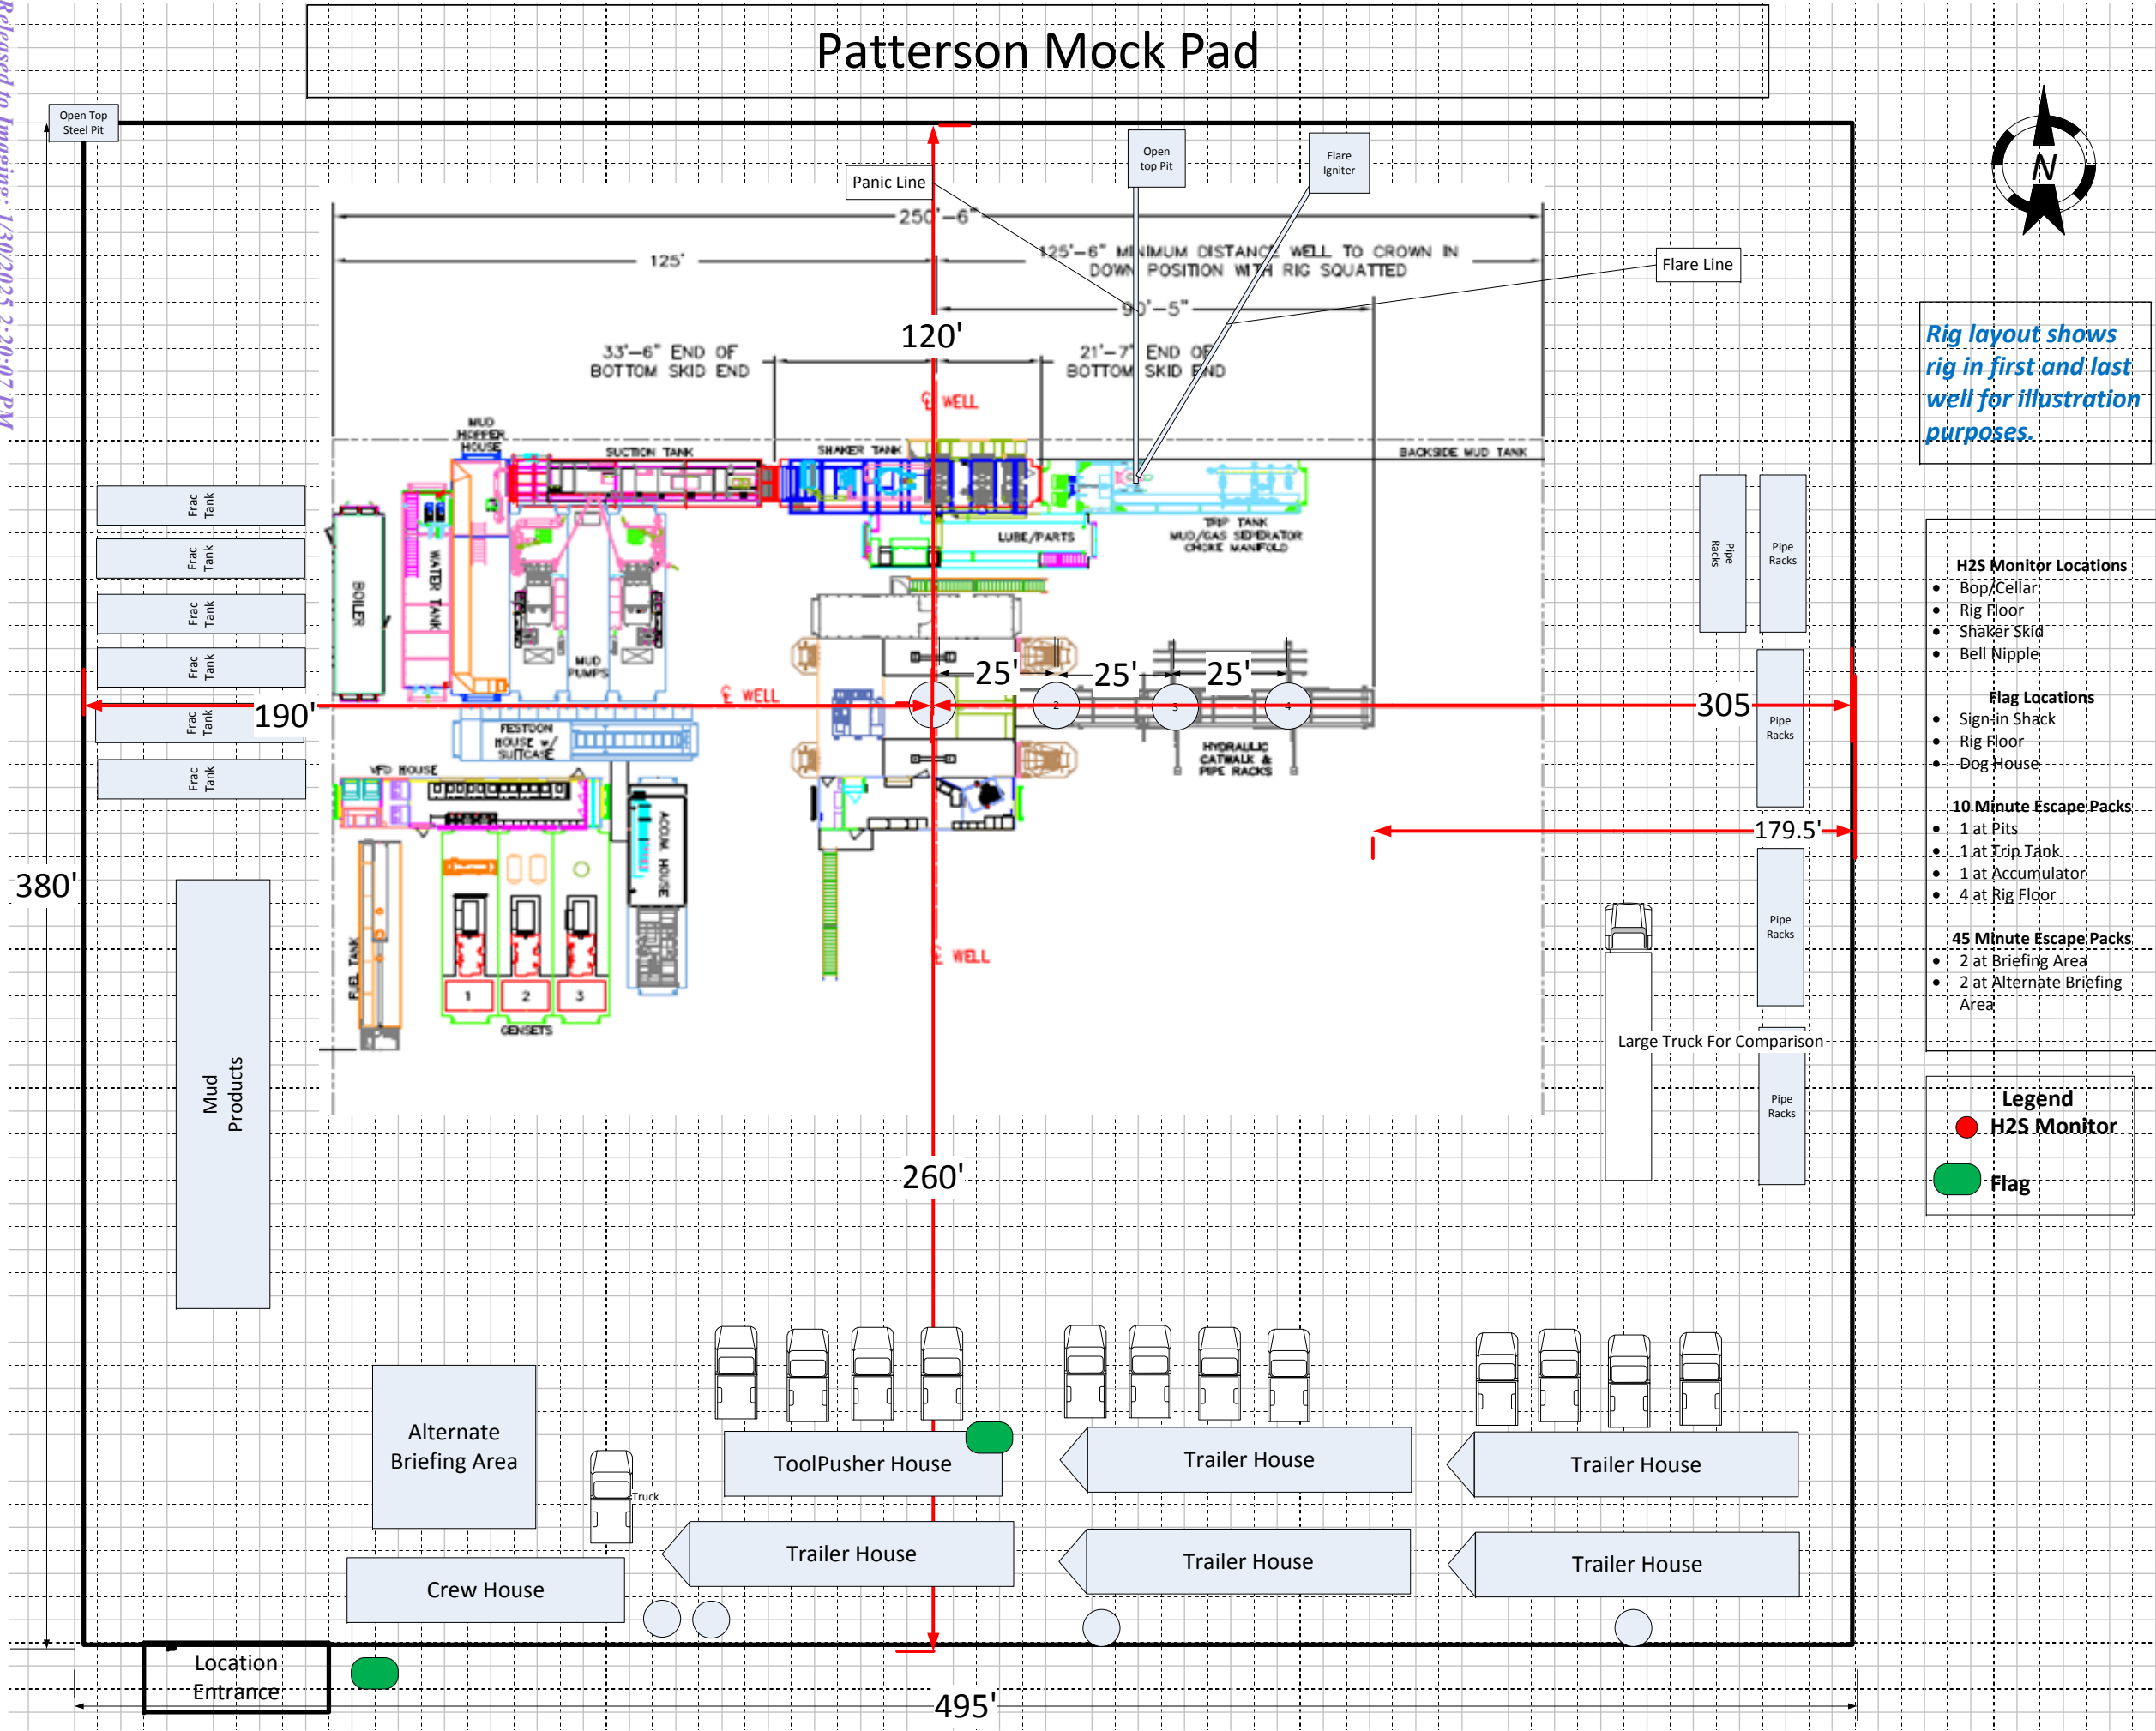



U.S. Department of the Interior  
BUREAU OF LAND MANAGEMENT

# Drilling Plan Data Report

09/24/2024

APD ID: 10400088467

Submission Date: 09/30/2022

Highlighted data  
reflects the most  
recent changes

Operator Name: CHEVRON USA INCORPORATED

Well Name: SD 14 23 FED P305

Well Number: 307H

Well Type: OIL WELL

Well Work Type: Drill

[Show Final Text](#)

## Section 1 - Geologic Formations

Formation ID	Formation Name	Elevation	True Vertical	Measured Depth	Lithologies	Mineral Resources	Producing Formatio
14190239	RUSTLER	3207	685	685	DOLOMITE	NATURAL GAS, OIL	N
14190240	SALADO	2127	1080	1080	HALITE, SALT	NATURAL GAS, OIL	N
14190241	CASTILE	408	2799	2799	ANHYDRITE	NONE	N
14190242	LAMAR	-1411	4618	4658	LIMESTONE	NATURAL GAS, OIL	N
14190243	BELL CANYON	-1416	4623	4663	SANDSTONE	NATURAL GAS, OIL	N
14190244	CHERRY CANYON	-2452	5659	5699	SANDSTONE	NATURAL GAS, OIL	N
14190245	BRUSHY CANYON	-4014	7221	7271	SANDSTONE	NATURAL GAS, OIL	N
14190250	BONE SPRING LIME	-5703	8910	8960	LIMESTONE	NATURAL GAS, OIL	N
14190251	AVALON SAND	-5718	8925	8975	LIMESTONE, SHALE	NATURAL GAS, OIL	N
14190252	BONE SPRING 1ST	-6584	9791	9841	SANDSTONE	NATURAL GAS, OIL	Y

## Section 2 - Blowout Prevention

Pressure Rating (PSI): 10M

Rating Depth: 9901

**Equipment:** Chevron will have a minimum of a 5,000 psi rig stack (see proposed schematic) for drill out below surface casing.

**Requesting Variance?** YES

**Variance request:** "Chevron respectfully request to vary from the Onshore Order 2 where it states: "(A full BOP Test) shall be performed: when initially installed and whenever any seal subject to test pressure is broken." We propose to break test if able to finish the next hole section within 21 days of the previous full BOP test. No BOP components nor any break will ever surpass 21 days between testing. A break test will consist of a 250 psi low / 5,000 psi high for 10 min each test against the connection that was broken when skidding the rig. Upon the first nipple up of the pad a full BOP test will be performed. A full BOP test will be completed prior to drilling the production lateral sections unless the BOP connection was not broken prior to drilling that hole section (example: drilling straight from production into production liner hole section). A break test will only be performed on operations where BLM documentation states a 5M or less BOP can be

BLOWOUT PREVENTER SCHEMATIC

Operation: Intermediate & Production Drilling Operations

Minimum System operation pressure 5,000 psi

BOP Stack

Part	Size	Pressure Rating	Description
A	13-5/8"	N/A	Rotating Head/Bell nipple
B	13-5/8"	5,000	Annular
C	13-5/8"	10,000	Blind Ram
D	13-5/8"	10,000	Pipe Ram
E	13-5/8"	10,000	Mud Cross
F	13-5/8"	10,000	Pipe Ram

Kill Line


Part	Size	Pressure Rating	Description
G	2"	10,000	Inside Kill Line Valve (gate valve)
H	2"	10,000	Outside Kill Line Valve (gate valve)
I	2"	10,000	Kill Line Check valve

Choke line

Part	Size	Pressure Rating	Description
J	3"	10,000	HCR (gate valve)
K	3"	10,000	Manual HCR (gate valve)

Wellhead

Part	Size	Pressure Rating	Description
L	13-5/8"	5,000	FMC Multibowl wellhead

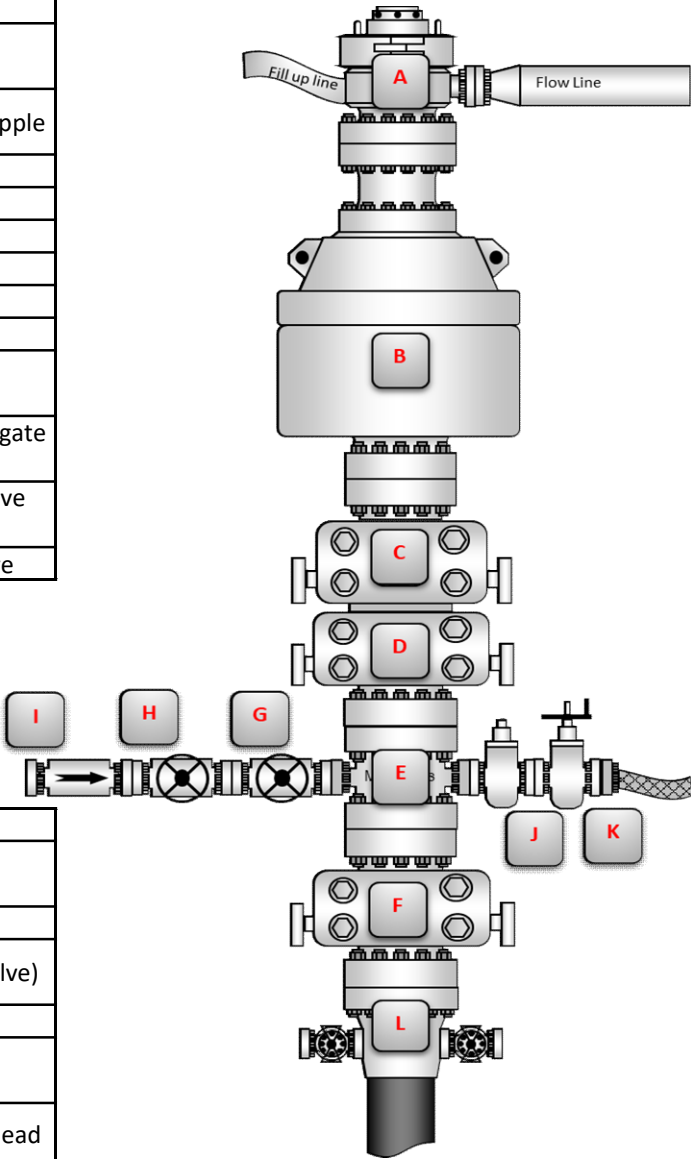

BOP Installation Checklist: The following items must be verified and checked off prior to pressure testing BOP equipment

- The installed BOP equipment meets at least the minimum requirements (rating, type, size, configuration) as shown on this schematic. Components may be substituted for equivalent equipment rated to higher pressures. Additional components may be put into place as long as they meet or exceed the minimum pressure rating of the system.
- All valves on the kill line and choke line will be full opening and will allow straight flow through.
- Manual (hand wheels) or automatic locking devices will be installed on all ram preventers. Hand wheels will also be install on all manual valves on the choke and kill line.
- A valve will be installed in the closing line as close as possible to the annular preventer to act as a locking device. This valve will remain open unless accumulator is inoperative.
- Upper kelly cock valve with handle will be available on rig floor along with saved valve and subs to fit all drill string connections in use.

Sante Fe Main Office  
Phone: (505) 476-3441

General Information  
Phone: (505) 629-6116

Online Phone Directory  
<https://www.emnrd.nm.gov/oed/contact-us>

**State of New Mexico**  
**Energy, Minerals and Natural Resources**  
**Oil Conservation Division**  
**1220 S. St Francis Dr.**  
**Santa Fe, NM 87505**

CONDITIONS

Action 421829

**CONDITIONS**

Operator: CHEVRON U S A INC 6301 Deauville Blvd Midland, TX 79706	OGRID: 4323
	Action Number: 421829
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

**CONDITIONS**

Created By	Condition	Condition Date
ntaylor	Cement is required to circulate on both surface and intermediate1 strings of casing.	1/16/2025
ntaylor	If cement does not circulate on any string, a Cement Bond Log (CBL) is required for that string of casing.	1/16/2025
pkautz	Prior to production of this well a change to the well name/number is required to comply with the OCD well naming convention.	1/30/2025
pkautz	File As Drilled C-102 and a directional Survey with C-104 completion packet.	1/30/2025
pkautz	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string.	1/30/2025
pkautz	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system.	1/30/2025
