

District I
1625 N. French Dr., Hobbs, NM 88240
District II
811 S. First St., Artesia, NM 88210
District III
1000 Rio Brazos Rd., Aztec, NM 87410
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals & Natural Resources

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-104
Revised August 1, 2011

Submit one copy to appropriate District Office

☐ AMENDED REPORT

I. REQUEST FOR ALLOWABLE AND AUTHORIZATION TO TRANSPORT

¹ Operator name and Address Devon Energy Production Company, L.P. 333 West Sheridan, Oklahoma City, OK 73102		² OGRID Number 6137
		³ Reason for Filing Code/ Effective Date NW / 9/28/22
⁴ API Number 30-015-49048	⁵ Pool Name LAGUNA SALADO; BONE SPRING	⁶ Pool Code 96721
⁷ Property Code 328289	⁸ Property Name Hot Potato 26-23 Fed	⁹ Well Number 236H

II. ¹⁰ Surface Location

Ul or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
O	26	23S	29E		450	South	1410	East	Eddy

¹¹ Bottom Hole Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
A	23	23S	29E		91	North	394	East	Eddy
¹² Lse Code F	¹³ Producing Method Code F	¹⁴ Gas Connection Date 9/28/22	¹⁵ C-129 Permit Number	¹⁶ C-129 Effective Date	¹⁷ C-129 Expiration Date				

III. Oil and Gas Transporters

¹⁸ Transporter OGRID	¹⁹ Transporter Name and Address	²⁰ O/G/W
036785	DCP Midstream P.O. Box 50020 Midland, TX 79710-0020	Gas
320009	EnLink Midstream Operating, LP 2501 Cedar Springs Road, Suite 100, Dallas, TX 75201	Oil

IV. Well Completion Data

²¹ Spud Date 5/27/22	²² Ready Date 9/28/22	²³ TD 19222	²⁴ PBDT 19204 MD/9033 TVD	²⁵ Perforations 9389 - 19193	²⁶ DHC, MC
²⁷ Hole Size	²⁸ Casing & Tubing Size	²⁹ Depth Set	³⁰ Sacks Cement		
17-1/2"	13-3/8"	446	520 sx CIC; Circ 90 sx		
12-1/4"	9-5/8"	3301	810 sx CIC ; Circ 234 sx		
8-1/2"	5-1/2"	19207	2380 sx CIH; Circ 0 sx		
	Tubing: 2-7/8"	8552			

V. Well Test Data

³¹ Date New Oil 10/4/22	³² Gas Delivery Date 10/4/22	³³ Test Date 10/4/22	³⁴ Test Length 24 hrs	³⁵ Tbg. Pressure 197 psi	³⁶ Csg. Pressure 919 psi
³⁷ Choke Size N/A	³⁸ Oil 141 bbl	³⁹ Water 2797 bbl	⁴⁰ Gas 275 mcf		⁴¹ Test Method flowing
⁴² I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief. Signature: 			OIL CONSERVATION DIVISION		
Printed name: Shayda Omoumi			Approved by: PATRICIA MARTINEZ		
Title: Regulatory Compliance Professional			Title: PETROLEUM SPECIALIST		
E-mail Address: shayda.omoumi@dvni.com			Approval Date: 2/14/2025		
Date: 11/1/2022		Phone: 405-552-3513			

District I1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720**District II**811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720**District III**1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170**District IV**1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102

Revised August 1, 2011

Submit one copy to
appropriate District Office☒ AMENDED REPORT**WELL LOCATION AND ACREAGE DEDICATION PLAT**

¹ API Number 3001549048	² Pool Code 96721	³ Pool Name LAGUNA SALADO; BONE SPRING
⁴ Property Code 328289	⁵ Property Name HOT POTATO 26-23 FED	
⁷ OGRID No. 6137	⁸ Operator Name DEVON ENERGY PRODUCTION COMPANY, L.P.	⁶ Well Number 236H
		⁹ Elevation 3071.3'

¹⁰Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
O	26	23-S	29-E		450	SOUTH	1410	EAST	EDDY

¹¹Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
A	23	23-S	29-E		91	NORTH	394	EAST	EDDY

¹² Dedicated Acres 640	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.
---	-------------------------------	----------------------------------	-------------------------

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

16

USGLO BRASS CAP**HOT POTATO 26-23****FED 236H**

ELEV: 3071.3'
LAT: 32.2698366°
LON: -103.9512270°
N: 462109.83
E: 659438.07

KICK OFF POINT

LAT: 32.2691644°
LON: -103.9480000°
N: 461868.84
E: 660436.37

FIRST TAKE POINT

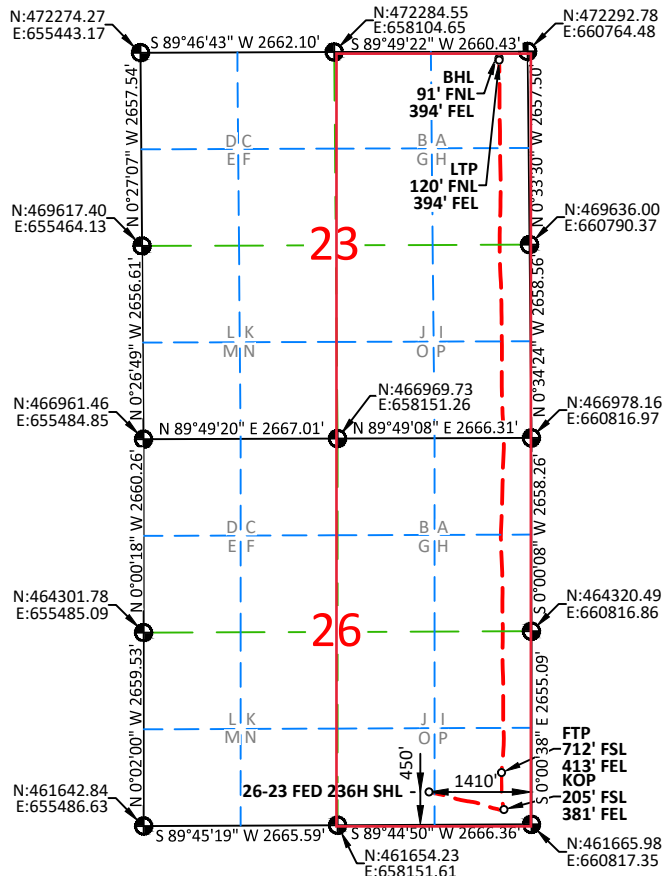
LAT: 32.2705609°
LON: -103.9480975°
N: 462376.76
E: 660404.39

LAST TAKE POINT

LAT: 32.2974845°
LON: -103.9480889°
N: 472171.25
E: 660371.89

BOTTOM HOLE LOCATION

LAT: 32.2975641°
LON: -103.9480911°
N: 472200.21
E: 660371.09

**¹⁷OPERATOR CERTIFICATION**

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order, heretofore entered by the division.

Signature: *Shayda Omoumi* Date: 9/28/2022

Printed Name: Shayda Omoumi

shayda.omoumi@dvn.com

E-mail Address


¹⁸SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

07/08/2022

Date of Survey

Signature and Seal of Professional Surveyor:



Certificate No. 23261

Albert Dehoyos

Drawn by: JEB

Checked by: ARD

Date: 09/15/2022

NOTES:

1. BEARINGS SHOWN ARE GRID BASED ON THE NEW MEXICO STATE PLANE EAST ZONE COORDINATE SYSTEM (3001), NAD 83 (2011), BASED FROM GPS OBSERVATIONS, OCCUPYING A WHS CONTROL POINT (5/8" REBAR), LOCATED AT NORTH: 456034.443, EAST: 653560.641, ELEVATION: 3101.4, DETERMINED BY AN OPUS SOLUTION ON NOVEMBER 9TH, 2019.
2. DISTANCES DEPICTED HEREON ARE REPORTED AS GROUND DISTANCES IN US SURVEY FEET USING A COMBINED SCALE FACTOR OF 1.000220989 AND ALL ELEVATIONS SHOWN ARE EXISTING GROUND ELEVATIONS.
3. DRILL PATH INFORMATION HAS BEEN PROVIDED TO WHS BY THE CLIENT.

Intent ☐ As Drilled ☒

API # 3001549048		
Operator Name: DEVON ENERGY PRODUCTION COMPANY, L.P.	Property Name: HOT POTATO 26-23 FED	Well Number 236H

Kick Off Point (KOP)

UL P	Section 26	Township 23-S	Range 29-E	Lot	Feet 205	From N/S SOUTH	Feet 381	From E/W EAST	County EDDY
Latitude 32.2691644°					Longitude -103.9480000°			NAD 83	

First Take Point (FTP)

UL P	Section 26	Township 23-S	Range 29-E	Lot	Feet 712	From N/S SOUTH	Feet 413	From E/W EAST	County EDDY
Latitude 32.2705609°					Longitude -103.9480975°			NAD 83	

Last Take Point (LTP)

UL A	Section 23	Township 23-S	Range 29-E	Lot	Feet 120	From N/S NORTH	Feet 394	From E/W EAST	County EDDY
Latitude 32.2974845°					Longitude -103.9480889°			NAD 83	

Is this well the defining well for the Horizontal Spacing Unit? ☐ NIs this well an infill well? ☐ Y

If infill is yes provide API if available, Operator name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018



Survey Report



Company:	Devon	Local Co-ordinate Reference:	Well Hot Potato 26-23 Fed 236H
Project:	Eddy County, NM (NAD83)	TVD Reference:	RKB @ 3093.80usft (Nabors M7503)
Site:	Hot Potato 26-23 Fed	MD Reference:	RKB @ 3093.80usft (Nabors M7503)
Well:	Hot Potato 26-23 Fed 236H	North Reference:	Grid
Wellbore:	OH / 69871	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Nabors M7503)	Database:	USA Compass

Project	Eddy County, NM (NAD83)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Hot Potato 26-23 Fed		
Site Position:		Northing:	462,109.70 usft
From:	Map	Easting:	659,408.07 usft
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16 "
		Latitude:	32° 16' 11.411613 N
		Longitude:	103° 57' 4.766687 W
		Grid Convergence:	0.204 °

Well	Hot Potato 26-23 Fed 236H		
Well Position	+N/-S	0.00 usft	Northing: 462,109.83 usft
	+E/-W	0.00 usft	Easting: 659,438.08 usft
Position Uncertainty	1.00 usft	Wellhead Elevation:	usft
		Latitude:	32° 16' 11.411842 N
		Longitude:	103° 57' 4.417206 W
		Ground Level:	3,071.30 usft

Wellbore	OH / 69871		
Magnetics	Model Name	Sample Date	Declination (°)
	MVHD	7/23/2022	6.661
			Dip Angle (°) 59.909
			Field Strength (nT) 47,616.92201753

Design	Surveys (Nabors M7503)		
Audit Notes:			
Version:	1.0	Phase:	ACTUAL
		Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)
	0.00	0.00	0.00
			Direction (°) 5.37

Survey Program	Date 7/7/2022		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name
111.00	19,222.00	Phoenix MWD Surveys (OH / 69871)	MWD+HRGM
			Description OWSG MWD + HRGM

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
111.00	0.36	257.13	111.00	-0.08	-0.34	-0.11	0.32	0.32	0.00
First Phoenix MWD Survey									
206.00	0.49	256.47	206.00	-0.24	-1.03	-0.33	0.14	0.14	-0.69
301.00	0.56	241.05	300.99	-0.56	-1.83	-0.73	0.17	0.07	-16.23
380.00	0.56	226.82	379.99	-1.01	-2.45	-1.23	0.18	0.00	-18.01
525.00	0.56	214.13	524.98	-2.08	-3.36	-2.39	0.09	0.00	-8.75
620.00	0.41	215.98	619.98	-2.74	-3.82	-3.09	0.16	-0.16	1.95
715.00	0.44	196.51	714.98	-3.37	-4.12	-3.74	0.15	0.03	-20.49
810.00	0.47	189.16	809.97	-4.10	-4.29	-4.48	0.07	0.03	-7.74
905.00	0.50	207.92	904.97	-4.85	-4.55	-5.26	0.17	0.03	19.75



Survey Report



Company:	Devon	Local Co-ordinate Reference:	Well Hot Potato 26-23 Fed 236H
Project:	Eddy County, NM (NAD83)	TVD Reference:	RKB @ 3093.80usft (Nabors M7503)
Site:	Hot Potato 26-23 Fed	MD Reference:	RKB @ 3093.80usft (Nabors M7503)
Well:	Hot Potato 26-23 Fed 236H	North Reference:	Grid
Wellbore:	OH / 69871	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Nabors M7503)	Database:	USA Compass

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
1,001.00	0.41	204.94	1,000.97	-5.53	-4.89	-5.97	0.10	-0.09	-3.10
1,095.00	0.34	185.32	1,094.96	-6.12	-5.05	-6.56	0.15	-0.07	-20.87
1,190.00	0.36	202.45	1,189.96	-6.67	-5.19	-7.13	0.11	0.02	18.03
1,285.00	0.43	198.95	1,284.96	-7.28	-5.42	-7.76	0.08	0.07	-3.68
1,380.00	0.52	207.72	1,379.96	-8.00	-5.74	-8.51	0.12	0.09	9.23
1,475.00	0.31	196.58	1,474.95	-8.63	-6.01	-9.16	0.24	-0.22	-11.73
1,570.00	2.35	106.84	1,569.93	-9.44	-4.22	-9.80	2.49	2.15	-94.46
1,665.00	5.50	98.03	1,664.69	-10.64	2.15	-10.39	3.37	3.32	-9.27
1,760.00	7.58	96.08	1,759.07	-11.94	12.89	-10.68	2.20	2.19	-2.05
1,855.00	9.40	97.75	1,853.03	-13.65	26.81	-11.08	1.93	1.92	1.76
1,950.00	9.10	97.75	1,946.79	-15.71	41.94	-11.72	0.32	-0.32	0.00
2,045.00	9.65	99.59	2,040.52	-18.05	57.24	-12.62	0.66	0.58	1.94
2,141.00	11.18	103.55	2,134.94	-21.57	74.22	-14.53	1.76	1.59	4.13
2,236.00	10.50	103.07	2,228.24	-25.69	91.60	-17.00	0.72	-0.72	-0.51
2,331.00	10.29	101.22	2,321.68	-29.30	108.36	-19.03	0.42	-0.22	-1.95
2,426.00	12.10	101.36	2,414.87	-32.91	126.44	-20.93	1.91	1.91	0.15
2,521.00	11.96	101.83	2,507.79	-36.89	145.84	-23.08	0.18	-0.15	0.49
2,616.00	11.79	102.96	2,600.75	-41.08	164.93	-25.47	0.30	-0.18	1.19
2,711.00	11.23	102.71	2,693.84	-45.29	183.42	-27.93	0.59	-0.59	-0.26
2,806.00	11.06	105.87	2,787.05	-49.82	201.20	-30.77	0.67	-0.18	3.33
2,901.00	10.88	108.30	2,880.32	-55.13	218.48	-34.44	0.52	-0.19	2.56
2,996.00	10.78	111.29	2,973.62	-61.17	235.27	-38.88	0.60	-0.11	3.15
3,091.00	10.58	110.55	3,066.98	-67.46	251.72	-43.60	0.26	-0.21	-0.78
3,187.00	11.29	102.78	3,161.24	-72.63	269.13	-47.12	1.70	0.74	-8.09
3,246.00	10.92	102.82	3,219.14	-75.15	280.22	-48.59	0.63	-0.63	0.07
3,362.00	10.10	102.81	3,333.19	-79.84	300.85	-51.33	0.71	-0.71	-0.01
3,457.00	11.59	107.06	3,426.49	-84.49	318.09	-54.35	1.78	1.57	4.47
3,553.00	12.25	111.47	3,520.42	-91.04	336.79	-59.13	1.17	0.69	4.59
3,648.00	14.08	104.95	3,612.93	-97.72	357.34	-63.84	2.48	1.93	-6.86
3,743.00	15.24	101.22	3,704.83	-103.13	380.75	-67.04	1.57	1.22	-3.93
3,838.00	14.86	102.17	3,796.58	-108.12	404.91	-69.76	0.48	-0.40	1.00
3,933.00	15.11	101.61	3,888.34	-113.18	428.94	-72.54	0.30	0.26	-0.59
4,028.00	15.25	100.43	3,980.03	-117.94	453.36	-74.99	0.36	0.15	-1.24
4,123.00	14.68	100.15	4,071.81	-122.32	477.50	-77.10	0.60	-0.60	-0.29
4,219.00	13.84	99.13	4,164.85	-126.29	500.81	-78.86	0.91	-0.88	-1.06
4,314.00	13.92	98.87	4,257.08	-129.85	523.32	-80.31	0.11	0.08	-0.27
4,409.00	14.03	98.25	4,349.26	-133.27	546.00	-81.58	0.20	0.12	-0.65
4,504.00	14.70	96.80	4,441.29	-136.35	569.37	-82.46	0.80	0.71	-1.53
4,599.00	14.30	99.37	4,533.27	-139.68	592.91	-83.58	0.80	-0.42	2.71
4,694.00	12.42	106.33	4,625.70	-144.47	614.30	-86.34	2.60	-1.98	7.33
4,789.00	12.12	106.55	4,718.53	-150.18	633.66	-90.22	0.32	-0.32	0.23
4,884.00	11.80	106.61	4,811.47	-155.80	652.53	-94.04	0.34	-0.34	0.06
4,979.00	11.83	108.05	4,904.45	-161.59	671.10	-98.08	0.31	0.03	1.52



Survey Report



Company:	Devon	Local Co-ordinate Reference:	Well Hot Potato 26-23 Fed 236H
Project:	Eddy County, NM (NAD83)	TVD Reference:	RKB @ 3093.80usft (Nabors M7503)
Site:	Hot Potato 26-23 Fed	MD Reference:	RKB @ 3093.80usft (Nabors M7503)
Well:	Hot Potato 26-23 Fed 236H	North Reference:	Grid
Wellbore:	OH / 69871	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Nabors M7503)	Database:	USA Compass

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
5,074.00	11.93	108.44	4,997.42	-167.71	689.67	-102.43	0.13	0.11	0.41
5,169.00	12.20	108.39	5,090.32	-173.99	708.51	-106.92	0.28	0.28	-0.05
5,265.00	12.11	107.80	5,184.17	-180.26	727.72	-111.37	0.16	-0.09	-0.61
5,360.00	12.57	109.46	5,276.97	-186.76	746.96	-116.03	0.61	0.48	1.75
5,455.00	11.50	108.23	5,369.88	-193.16	765.70	-120.65	1.16	-1.13	-1.29
5,550.00	10.69	107.90	5,463.11	-198.83	783.08	-124.67	0.86	-0.85	-0.35
5,645.00	10.30	108.66	5,556.52	-204.26	799.51	-128.54	0.44	-0.41	0.80
5,740.00	9.84	109.74	5,650.05	-209.72	815.20	-132.50	0.52	-0.48	1.14
5,836.00	8.51	110.81	5,744.82	-215.01	829.56	-136.43	1.40	-1.39	1.11
5,931.00	8.29	111.64	5,838.81	-220.03	842.50	-140.22	0.26	-0.23	0.87
6,026.00	10.46	98.77	5,932.54	-223.88	857.39	-142.65	3.16	2.28	-13.55
6,121.00	9.83	99.91	6,026.06	-226.59	873.90	-143.81	0.70	-0.66	1.20
6,216.00	9.59	101.62	6,119.69	-229.58	889.64	-145.31	0.39	-0.25	1.80
6,312.00	8.71	103.63	6,214.47	-232.90	904.54	-147.22	0.98	-0.92	2.09
6,407.00	9.00	105.14	6,308.34	-236.54	918.70	-149.52	0.39	0.31	1.59
6,502.00	9.02	108.32	6,402.17	-240.82	932.94	-152.45	0.52	0.02	3.35
6,597.00	8.73	109.97	6,496.03	-245.62	946.79	-155.93	0.41	-0.31	1.74
6,692.00	8.86	111.73	6,589.91	-250.79	960.36	-159.81	0.31	0.14	1.85
6,787.00	8.67	114.98	6,683.81	-256.52	973.65	-164.28	0.56	-0.20	3.42
6,882.00	7.55	109.69	6,777.85	-261.65	986.01	-168.22	1.42	-1.18	-5.57
6,978.00	5.37	95.30	6,873.25	-264.19	996.43	-169.78	2.81	-2.27	-14.99
7,073.00	2.87	74.40	6,968.00	-263.96	1,003.15	-168.92	3.03	-2.63	-22.00
7,168.00	1.66	16.77	7,062.93	-262.00	1,005.83	-166.72	2.55	-1.27	-60.66
7,263.00	1.30	10.11	7,157.90	-259.63	1,006.42	-164.30	0.42	-0.38	-7.01
7,358.00	1.11	329.62	7,252.88	-257.77	1,006.14	-162.48	0.90	-0.20	-42.62
7,453.00	1.01	300.16	7,347.87	-256.56	1,004.95	-161.38	0.58	-0.11	-31.01
7,548.00	0.82	311.30	7,442.85	-255.69	1,003.72	-160.63	0.27	-0.20	11.73
7,643.00	0.31	326.30	7,537.85	-255.02	1,003.07	-160.03	0.55	-0.54	15.79
7,738.00	1.28	111.14	7,632.84	-255.19	1,003.91	-160.12	1.63	1.02	152.46
7,833.00	2.31	104.33	7,727.79	-256.05	1,006.76	-160.71	1.11	1.08	-7.17
7,928.00	2.33	62.48	7,822.72	-255.63	1,010.33	-159.96	1.74	0.02	-44.05
8,024.00	1.28	351.35	7,918.68	-253.67	1,011.90	-157.86	2.36	-1.09	-74.09
8,119.00	2.22	304.39	8,013.64	-251.58	1,010.22	-155.93	1.73	0.99	-49.43
8,214.00	1.85	303.69	8,108.58	-249.69	1,007.42	-154.31	0.39	-0.39	-0.74
8,309.00	1.84	306.82	8,203.53	-247.93	1,004.93	-152.79	0.11	-0.01	3.29
8,404.00	2.32	312.93	8,298.47	-245.70	1,002.30	-150.82	0.56	0.51	6.43
8,487.00	1.62	312.06	8,381.42	-243.77	1,000.20	-149.10	0.84	-0.84	-1.05
8,531.00	1.49	286.01	8,425.41	-243.20	999.19	-148.62	1.62	-0.30	-59.20
8,626.00	7.23	347.35	8,520.12	-237.02	996.69	-142.70	6.99	6.04	64.57
8,721.00	24.46	350.75	8,611.17	-211.58	992.18	-117.80	18.16	18.14	3.58
8,816.00	32.26	350.68	8,694.70	-167.08	984.90	-74.17	8.21	8.21	-0.07
8,911.00	32.51	351.09	8,774.92	-116.84	976.84	-24.91	0.35	0.26	0.43
9,006.00	38.16	353.58	8,852.40	-62.41	969.60	28.61	6.14	5.95	2.62



Survey Report



Company:	Devon	Local Co-ordinate Reference:	Well Hot Potato 26-23 Fed 236H
Project:	Eddy County, NM (NAD83)	TVD Reference:	RKB @ 3093.80usft (Nabors M7503)
Site:	Hot Potato 26-23 Fed	MD Reference:	RKB @ 3093.80usft (Nabors M7503)
Well:	Hot Potato 26-23 Fed 236H	North Reference:	Grid
Wellbore:	OH / 69871	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Nabors M7503)	Database:	USA Compass

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
9,101.00	52.05	0.13	8,919.32	4.58	966.39	95.00	15.40	14.62	6.89
9,196.00	63.32	359.45	8,970.02	84.73	966.06	174.77	11.88	11.86	-0.72
9,291.00	71.77	358.57	9,006.28	172.43	964.53	261.94	8.94	8.89	-0.93
9,386.00	77.61	3.27	9,031.36	263.98	966.05	353.23	7.78	6.15	4.95
9,481.00	84.16	7.09	9,046.41	357.33	974.54	446.96	7.95	6.89	4.02
9,576.00	92.41	4.17	9,049.25	451.74	983.84	541.83	9.21	8.68	-3.07
9,671.00	90.48	3.65	9,046.86	546.48	990.32	636.76	2.10	-2.03	-0.55
9,767.00	90.11	3.34	9,046.36	642.30	996.17	732.71	0.50	-0.39	-0.32
9,862.00	89.86	359.44	9,046.39	737.25	998.47	827.46	4.11	-0.26	-4.11
9,957.00	90.00	358.03	9,046.50	832.23	996.38	921.82	1.49	0.15	-1.48
10,052.00	90.70	358.15	9,045.92	927.17	993.21	1,016.05	0.75	0.74	0.13
10,147.00	91.54	358.35	9,044.06	1,022.11	990.31	1,110.30	0.91	0.88	0.21
10,242.00	92.24	0.53	9,040.93	1,117.05	989.38	1,204.74	2.41	0.74	2.29
10,337.00	89.94	0.87	9,039.12	1,212.02	990.54	1,299.40	2.45	-2.42	0.36
10,432.00	90.22	359.94	9,038.99	1,307.01	991.21	1,394.04	1.02	0.29	-0.98
10,527.00	92.30	0.12	9,036.90	1,401.98	991.26	1,488.60	2.20	2.19	0.19
10,622.00	91.71	358.83	9,033.58	1,496.92	990.39	1,583.04	1.49	-0.62	-1.36
10,717.00	90.90	357.35	9,031.42	1,591.84	987.23	1,677.24	1.78	-0.85	-1.56
10,813.00	89.52	358.11	9,031.06	1,687.76	983.43	1,772.39	1.64	-1.44	0.79
10,908.00	88.04	359.58	9,033.09	1,782.71	981.51	1,866.75	2.20	-1.56	1.55
11,003.00	89.36	359.92	9,035.24	1,877.69	981.10	1,961.26	1.43	1.39	0.36
11,098.00	88.96	0.56	9,036.63	1,972.67	981.49	2,055.87	0.79	-0.42	0.67
11,193.00	89.75	0.95	9,037.70	2,067.66	982.75	2,150.56	0.93	0.83	0.41
11,288.00	91.43	1.06	9,036.73	2,162.64	984.41	2,245.27	1.77	1.77	0.12
11,383.00	90.73	359.69	9,034.93	2,257.61	985.03	2,339.89	1.62	-0.74	-1.44
11,478.00	89.69	358.19	9,034.59	2,352.59	983.28	2,434.29	1.92	-1.09	-1.58
11,573.00	90.84	357.67	9,034.15	2,447.53	979.84	2,528.49	1.33	1.21	-0.55
11,668.00	88.77	0.58	9,034.47	2,542.50	978.39	2,622.91	3.76	-2.18	3.06
11,763.00	87.12	1.26	9,037.88	2,637.42	979.92	2,717.56	1.88	-1.74	0.72
11,858.00	87.84	0.73	9,042.05	2,732.32	981.57	2,812.19	0.94	0.76	-0.56
11,954.00	89.41	359.39	9,044.36	2,828.28	981.67	2,907.74	2.15	1.64	-1.40
12,049.00	90.67	358.13	9,044.29	2,923.26	979.61	3,002.11	1.88	1.33	-1.33
12,143.00	91.85	358.21	9,042.22	3,017.18	976.61	3,095.34	1.26	1.26	0.09
12,238.00	91.65	357.75	9,039.32	3,112.08	973.26	3,189.51	0.53	-0.21	-0.48
12,333.00	90.73	356.77	9,037.35	3,206.95	968.72	3,283.53	1.41	-0.97	-1.03
12,428.00	88.15	357.19	9,038.28	3,301.81	963.72	3,377.51	2.75	-2.72	0.44
12,524.00	84.87	358.64	9,044.12	3,397.55	960.23	3,472.50	3.73	-3.42	1.51
12,619.00	85.63	359.06	9,051.99	3,492.20	958.33	3,566.56	0.91	0.80	0.44
12,714.00	88.12	2.07	9,057.17	3,587.04	959.27	3,661.07	4.11	2.62	3.17
12,809.00	89.05	2.83	9,059.51	3,681.92	963.33	3,755.92	1.26	0.98	0.80
12,904.00	91.79	2.64	9,058.82	3,776.80	967.86	3,850.80	2.89	2.88	-0.20
12,999.00	93.89	1.97	9,054.11	3,871.60	971.68	3,945.55	2.32	2.21	-0.71
13,094.00	95.13	1.59	9,046.64	3,966.26	974.62	4,040.06	1.36	1.31	-0.40
13,189.00	94.09	1.98	9,039.01	4,060.90	977.57	4,134.57	1.17	-1.09	0.41



Survey Report



Company:	Devon	Local Co-ordinate Reference:	Well Hot Potato 26-23 Fed 236H
Project:	Eddy County, NM (NAD83)	TVD Reference:	RKB @ 3093.80usft (Nabors M7503)
Site:	Hot Potato 26-23 Fed	MD Reference:	RKB @ 3093.80usft (Nabors M7503)
Well:	Hot Potato 26-23 Fed 236H	North Reference:	Grid
Wellbore:	OH / 69871	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Nabors M7503)	Database:	USA Compass

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
13,284.00	92.32	1.29	9,033.69	4,155.71	980.27	4,229.21	2.00	-1.86	-0.73
13,380.00	90.87	0.82	9,031.02	4,251.66	982.04	4,324.90	1.59	-1.51	-0.49
13,475.00	92.18	1.32	9,028.49	4,346.60	983.81	4,419.60	1.48	1.38	0.53
13,570.00	92.47	1.43	9,024.64	4,441.50	986.09	4,514.29	0.33	0.31	0.12
13,665.00	90.62	3.30	9,022.08	4,536.37	990.01	4,609.12	2.77	-1.95	1.97
13,760.00	87.93	3.33	9,023.28	4,631.20	995.50	4,704.04	2.83	-2.83	0.03
13,855.00	86.47	1.44	9,027.92	4,726.00	999.45	4,798.79	2.51	-1.54	-1.99
13,950.00	86.27	359.63	9,033.94	4,820.80	1,000.34	4,893.26	1.91	-0.21	-1.91
14,039.00	86.97	357.88	9,039.18	4,909.62	998.41	4,981.51	2.11	0.79	-1.97
14,134.00	89.02	356.40	9,042.51	5,004.43	993.67	5,075.46	2.66	2.16	-1.56
14,229.00	91.12	356.91	9,042.39	5,099.27	988.13	5,169.36	2.27	2.21	0.54
14,324.00	91.90	356.37	9,039.89	5,194.07	982.56	5,263.23	1.00	0.82	-0.57
14,419.00	90.56	358.19	9,037.85	5,288.93	978.05	5,357.25	2.38	-1.41	1.92
14,514.00	90.81	358.11	9,036.71	5,383.88	974.99	5,451.49	0.28	0.26	-0.08
14,609.00	90.17	358.89	9,035.90	5,478.84	972.50	5,545.81	1.06	-0.67	0.82
14,704.00	89.94	359.36	9,035.81	5,573.83	971.05	5,640.24	0.55	-0.24	0.49
14,799.00	88.91	0.11	9,036.76	5,668.82	970.61	5,734.78	1.34	-1.08	0.79
14,894.00	88.66	0.60	9,038.78	5,763.80	971.20	5,829.39	0.58	-0.26	0.52
14,990.00	89.61	0.14	9,040.23	5,859.78	971.82	5,925.01	1.10	0.99	-0.48
15,085.00	90.42	0.10	9,040.20	5,954.78	972.02	6,019.62	0.85	0.85	-0.04
15,180.00	91.85	0.51	9,038.32	6,049.76	972.52	6,114.22	1.57	1.51	0.43
15,275.00	91.48	359.54	9,035.56	6,144.72	972.57	6,208.77	1.09	-0.39	-1.02
15,370.00	91.71	358.85	9,032.92	6,239.67	971.23	6,303.18	0.77	0.24	-0.73
15,465.00	91.40	359.05	9,030.34	6,334.62	969.49	6,397.55	0.39	-0.33	0.21
15,560.00	91.06	359.63	9,028.30	6,429.59	968.40	6,492.00	0.71	-0.36	0.61
15,655.00	90.73	359.77	9,026.81	6,524.58	967.90	6,586.53	0.38	-0.35	0.15
15,750.00	91.15	359.16	9,025.26	6,619.56	967.01	6,681.01	0.78	0.44	-0.64
15,845.00	90.11	359.07	9,024.21	6,714.54	965.55	6,775.44	1.10	-1.09	-0.09
15,940.00	88.85	358.80	9,025.07	6,809.52	963.78	6,869.83	1.36	-1.33	-0.28
16,035.00	90.53	358.86	9,025.59	6,904.50	961.84	6,964.21	1.77	1.77	0.06
16,130.00	89.61	357.20	9,025.47	6,999.44	958.57	7,058.43	2.00	-0.97	-1.75
16,224.00	89.80	356.59	9,025.96	7,093.30	953.48	7,151.40	0.68	0.20	-0.65
16,319.00	90.00	357.79	9,026.12	7,188.18	948.83	7,245.43	1.28	0.21	1.26
16,414.00	89.94	357.41	9,026.17	7,283.10	944.85	7,339.56	0.40	-0.06	-0.40
16,509.00	89.86	359.65	9,026.34	7,378.06	942.41	7,433.87	2.36	-0.08	2.36
16,604.00	89.75	359.47	9,026.66	7,473.05	941.68	7,528.39	0.22	-0.12	-0.19
16,699.00	90.42	0.46	9,026.52	7,568.05	941.62	7,622.96	1.26	0.71	1.04
16,794.00	89.66	0.79	9,026.45	7,663.05	942.66	7,717.63	0.87	-0.80	0.35
16,889.00	89.05	1.15	9,027.52	7,758.03	944.27	7,812.35	0.75	-0.64	0.38
16,985.00	88.09	2.00	9,029.92	7,853.96	946.91	7,908.11	1.34	-1.00	0.89
17,079.00	89.19	1.41	9,032.15	7,947.89	949.70	8,001.89	1.33	1.17	-0.63
17,174.00	90.59	1.21	9,032.33	8,042.86	951.87	8,096.64	1.49	1.47	-0.21
17,269.00	89.33	1.32	9,032.40	8,137.84	953.97	8,191.40	1.33	-1.33	0.12



Survey Report



Company:	Devon	Local Co-ordinate Reference:	Well Hot Potato 26-23 Fed 236H
Project:	Eddy County, NM (NAD83)	TVD Reference:	RKB @ 3093.80usft (Nabors M7503)
Site:	Hot Potato 26-23 Fed	MD Reference:	RKB @ 3093.80usft (Nabors M7503)
Well:	Hot Potato 26-23 Fed 236H	North Reference:	Grid
Wellbore:	OH / 69871	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Nabors M7503)	Database:	USA Compass

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
17,364.00	89.33	0.29	9,033.51	8,232.82	955.30	8,286.09	1.08	0.00	-1.08
17,459.00	90.11	0.70	9,033.97	8,327.81	956.13	8,380.74	0.93	0.82	0.43
17,554.00	89.52	358.88	9,034.28	8,422.81	955.78	8,475.29	2.01	-0.62	-1.92
17,649.00	90.28	358.38	9,034.45	8,517.78	953.51	8,569.63	0.96	0.80	-0.53
17,744.00	89.05	358.94	9,035.00	8,612.75	951.28	8,663.98	1.42	-1.29	0.59
17,839.00	88.71	358.99	9,036.86	8,707.72	949.57	8,758.37	0.36	-0.36	0.05
17,934.00	90.22	359.20	9,037.75	8,802.70	948.07	8,852.79	1.60	1.59	0.22
18,029.00	91.76	359.40	9,036.10	8,897.67	946.91	8,947.24	1.63	1.62	0.21
18,124.00	90.08	359.59	9,034.58	8,992.65	946.07	9,041.73	1.78	-1.77	0.20
18,219.00	89.30	359.37	9,035.09	9,087.65	945.21	9,136.22	0.85	-0.82	-0.23
18,314.00	90.28	358.58	9,035.44	9,182.63	943.51	9,230.63	1.33	1.03	-0.83
18,409.00	89.41	359.52	9,035.70	9,277.61	941.93	9,325.05	1.35	-0.92	0.99
18,504.00	89.33	359.50	9,036.74	9,372.60	941.12	9,419.55	0.09	-0.08	-0.02
18,599.00	90.08	359.11	9,037.23	9,467.60	939.97	9,514.01	0.89	0.79	-0.41
18,694.00	89.44	359.79	9,037.63	9,562.59	939.06	9,608.50	0.98	-0.67	0.72
18,789.00	89.13	0.14	9,038.82	9,657.58	939.00	9,703.07	0.49	-0.33	0.37
18,884.00	89.83	359.98	9,039.68	9,752.58	939.10	9,797.66	0.76	0.74	-0.17
18,979.00	90.56	359.27	9,039.35	9,847.57	938.48	9,892.18	1.07	0.77	-0.75
19,074.00	91.65	358.75	9,037.52	9,942.54	936.84	9,986.58	1.27	1.15	-0.55
19,157.00	92.35	358.43	9,034.63	10,025.46	934.80	10,068.95	0.93	0.84	-0.39
Final Phoenix MWD Survey									
19,220.00	92.35	358.43	9,032.04	10,088.39	933.07	10,131.43	0.00	0.00	0.00
Projection to TD									
19,222.00	92.35	358.43	9,031.96	10,090.38	933.02	10,133.42	0.00	0.00	0.00

Design Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
111.00	111.00	-0.08	-0.34	First Phoenix MWD Survey
19,157.00	9,034.63	10,025.46	934.80	Final Phoenix MWD Survey
19,220.00	9,032.04	10,088.39	933.07	Projection to TD

Submit 1 Copy To Appropriate District
Office
District I – (575) 393-6161
1625 N. French Dr., Hobbs, NM 88240
District II – (575) 748-1283
811 S. First St., Artesia, NM 88210
District III – (505) 334-6178
1000 Rio Brazos Rd., Aztec, NM 87410
District IV – (505) 476-3460
1220 S. St. Francis Dr., Santa Fe, NM
87505

State of New Mexico
Energy, Minerals and Natural Resources

OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-103

Revised August 1, 2011

SUNDRY NOTICES AND REPORTS ON WELLS (DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)		WELL API NO. 30-015-49048
1. Type of Well: Oil Well ☒ Gas Well ☐ Other ☐		5. Indicate Type of Lease STATE ☐ FEE ☐
2. Name of Operator Devon Energy Production Company, L.P.		6. State Oil & Gas Lease No.
3. Address of Operator 333 West Sheridan, Oklahoma City, OK 73102		7. Lease Name or Unit Agreement Name Hot Potato 26-23 Fed
4. Well Location Unit Letter <u>O</u> : <u>450</u> feet from the <u>South</u> line and <u>1410</u> feet from the <u>East</u> line Section <u>26</u> Township <u>23S</u> Range <u>29E</u> NMPM County <u>Eddy</u>		8. Well Number 236H
11. Elevation (Show whether DR, RKB, RT, GR, etc.) GL: 3071.3'		9. OGRID Number 6137
		10. Pool name or Wildcat LAGUNA SALADO; BONE SPRING

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:

PERFORM REMEDIAL WORK ☐ PLUG AND ABANDON ☐
 TEMPORARILY ABANDON ☐ CHANGE PLANS ☐
 PULL OR ALTER CASING ☐ MULTIPLE COMPL ☐
 DOWNHOLE COMMINGLE ☐

SUBSEQUENT REPORT OF:

REMEDIAL WORK ☐ ALTERING CASING ☐
 COMMENCE DRILLING OPNS. ☐ P AND A ☐
 CASING/CEMENT JOB ☐

OTHER: ☐

OTHER: Completion ☒

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

8/17/22-9/28/22: MIRU WL & PT. TIH & ran CBL, found TOC @ 1480'. PT csg for 30 min, OK. TIH w/pump through frac plug and guns. Perf Bone Spring, 9389'-19193', total 1174 holes. Frac totals 19,461,150# proppant, 780 bbl acid. ND frac, MIRU PU, NU BOP, DO plugs & CO to PBTD w/ float collar 19,204' MD/9,033' TVD. CHC, FWB, ND BOP. RIH w/257 jts 2-7/8" L-80 tbg, set @ 8552'. TOP.

I hereby certify that the information above is true and complete to the best of my knowledge and belief.


SIGNATURE Shayda Omoumi TITLE Regulatory Compliance Professional DATE 11/1/2022

Type or print name Shayda Omoumi E-mail address: shayda.omoumi@dmn.com PHONE: 405-552-3513

For State Use Only

APPROVED BY: _____ TITLE _____ DATE _____

Conditions of Approval (if any):

Submit To Appropriate District Office Two Copies District I 1625 N. French Dr., Hobbs, NM 88240 District II 811 S. First St., Artesia, NM 88210 District III 1000 Rio Brazos Rd., Aztec, NM 87410 District IV 1220 S. St. Francis Dr., Santa Fe, NM 87505		State of New Mexico Energy, Minerals and Natural Resources Oil Conservation Division 1220 South St. Francis Dr. Santa Fe, NM 87505				Form C-105 Revised August 1, 2011				
		1. WELL API NO.		30-015-49048						
		2. Type of Lease		☐ STATE ☐ FEE ☒ FED/INDIAN						
		3. State Oil & Gas Lease No.								
WELL COMPLETION OR RECOMPLETION REPORT AND LOG										
4. Reason for filing:						5. Lease Name or Unit Agreement Name				
☒ COMPLETION REPORT (Fill in boxes #1 through #31 for State and Fee wells only) ☐ C-144 CLOSURE ATTACHMENT (Fill in boxes #1 through #9, #15 Date Rig Released and #32 and/or #33; attach this and the plat to the C-144 closure report in accordance with 19.15.17.13.K NMAC)						Hot Potato 26-23 Fed 6. Well Number:				
						236H				
7. Type of Completion:										
☒ NEW WELL ☐ WORKOVER ☐ DEEPENING ☐ PLUGBACK ☐ DIFFERENT RESERVOIR ☐ OTHER										
8. Name of Operator						9. OGRID				
Devon Energy Production Company, L.P.						6137				
10. Address of Operator						11. Pool name or Wildcat				
333 West Sheridan Avenue, Oklahoma City, OK 73102						LAGUNA SALADO; BONE SPRING				
12. Location	Unit Ltr	Section	Township	Range	Lot	Feet from the	N/S Line	Feet from the	E/W Line	County
Surface:	O	26	23S	29E		450	South	1410	East	Eddy
BH:	A	23	23S	29E		91	North	394	East	Eddy
13. Date Spudded	14. Date T.D. Reached		15. Date Rig Released		16. Date Completed (Ready to Produce)		17. Elevations (DF and RKB, RT, GR, etc.)			
5/27/22	6/26/22		6/30/22		9/28/22		3071.3' GL			
18. Total Measured Depth of Well			19. Plug Back Measured Depth			20. Was Directional Survey Made?		21. Type Electric and Other Logs Run		
19222 MD, 9032 TVD			19204 MD/9033 TVD			Yes		CBL		
22. Producing Interval(s), of this completion - Top, Bottom, Name										
9389-19193, BONE SPRING										
23. CASING RECORD (Report all strings set in well)										
CASING SIZE		WEIGHT LB./FT.		DEPTH SET		HOLE SIZE		CEMENTING RECORD		AMOUNT PULLED
13-3/8"		54.5		446		17-1/2"		520 sx CIC; circ 90 sx		
9-5/8"		40		3301		12-1/4"		810 sx CIC; circ 234 sx		
5-1/2"		20		19207		8-1/2"		2380 sx CIH; circ 0 sx		TOC @ 1470
24. LINER RECORD										
SIZE	TOP	BOTTOM	SACKS CEMENT	SCREEN	25. TUBING RECORD					
					SIZE	DEPTH SET	PACKER SET			
					2-7/8" L-80	8552				
26. Perforation record (interval, size, and number)					27. ACID, SHOT, FRACTURE, CEMENT, SQUEEZE, ETC.					
9389 - 19193, total 1174 holes					DEPTH INTERVAL		AMOUNT AND KIND MATERIAL USED			
					9389-19193		Acidize and frac in 39 stages. See detailed summary attached.			
28. PRODUCTION										
Date First Production		Production Method (Flowing, gas lift, pumping - Size and type pump)				Well Status (Prod. or Shut-in)				
9/28/22		Flowing				Producing				
Date of Test	Hours Tested	Choke Size	Prod'n For Test Period	Oil - Bbl	Gas - MCF	Water - Bbl.	Gas - Oil Ratio			
10/4/22	24	N/A		141	275	2797	1950.35461			
Flow Tubing Press.	Casing Pressure	Calculated 24-Hour Rate	Oil - Bbl.	Gas - MCF	Water - Bbl.	Oil Gravity - API - (Corr.)				
197 psi	919 psi									
29. Disposition of Gas (Sold, used for fuel, vented, etc.)							30. Test Witnessed By			
Sold										
31. List Attachments										
Directional Survey, Logs										
32. If a temporary pit was used at the well, attach a plat with the location of the temporary pit.										
33. If an on-site burial was used at the well, report the exact location of the on-site burial:										
Latitude			Longitude			NAD 1927 1983				
I hereby certify that the information shown on both sides of this form is true and complete to the best of my knowledge and belief										
Signature		Printed Name		Title		Regulatory Compliance Professional		Date		
		Shayda Omoumi						11/1/2022		
E-mail Address shayda.omoumi@dvn.com										

This form is to be filed with the appropriate District Office of the Division not later than 20 days after the completion of any newly-drilled or deepened well and not later than 60 days after completion of closure. When submitted as a completion report, this shall be accompanied by one copy of all electrical and radio-activity logs run on the well and a summary of all special tests conducted, including drill stem tests. All depths reported shall be measured depths. In the case of directionally drilled wells, true vertical depths shall also be reported. For multiple completions, items 11, 12 and 26-31 shall be reported for each zone.

Southeastern New Mexico		Northwestern New Mexico	
Rustler - 234			
Salt - 523			
Base of Salt - 2954			
Lamar - 3192			
Delaware - 3220			
Cherry Canyon - 4045			
Brushy Canyon - 5663			
1st Bone Spring Lime - 6916			
1st Bone Spring Sand - 7947			
2nd Bone Spring Sand - 8762			
3rd Bone Spring Lime - 9098			
3rd Bone Spring Sand - 9895			
Wolfcamp - 10221			
Strawn - 11915			

No. 1, from..... N/Ato..... N/A
 No. 2, from..... N/Ato..... N/A
 No. 3, from..... N/Ato..... N/A
 No. 4, from..... N/Ato..... N/A

Include data on rate of water inflow and elevation to which water rose in hole.

No. 1, from.....to.....feet.....

No. 2, from.....to.....feet.....

No. 3, from.....to.....feet.....

From	To	Thickness In Feet	Lithology

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/ocd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

ACKNOWLEDGMENTS

Action 155191

ACKNOWLEDGMENTS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 155191
	Action Type: [C-104] Completion Packet (C-104C)

ACKNOWLEDGMENTS

☒	I hereby certify that the required Water Use Report has been, or will be, submitted for this wells completion.
☒	I hereby certify that the required FracFocus disclosure has been, or will be, submitted for this wells completion.

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/oed/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 155191

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 155191
	Action Type: [C-104] Completion Packet (C-104C)

CONDITIONS

Created By	Condition	Condition Date
plmartinez	File 3160-4 Completion Report and 3160-5 Completion Sundry within 10 days of BLM approval.	2/14/2025
