

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER 1b. Type of Well: <input type="checkbox"/> Oil Well <input checked="" type="checkbox"/> Gas Well <input type="checkbox"/> Other 1c. Type of Completion: <input type="checkbox"/> Hydraulic Fracturing <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone			5. Lease Serial No. NMNM62171
2. Name of Operator TAP ROCK OPERATING LLC			6. If Indian, Allottee or Tribe Name 7. If Unit or CA Agreement, Name and No. 8. Lease Name and Well No. UPSLOPE FED COM 211H
3a. Address 602 PARK POINT DRIVE SUITE 200, GOLDEN, CO 80401		3b. Phone No. (include area code) (720) 460-3316	9. API Well No. 30-015-56197
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface SENE / 2357 FNL / 551 FEL / LAT 32.1451318 / LONG -104.3769973 At proposed prod. zone NWNW / 990 FNL / 5 FWL / LAT 32.1489739 / LONG -104.409811			10. Field and Pool, or Exploratory PURPLE SAGE/(WOLFCAMP) GAS 11. Sec., T. R. M. or Blk. and Survey or Area SEC 10/T25S/R25E/NMP
14. Distance in miles and direction from nearest town or post office* 3 miles		12. County or Parish EDDY	13. State NM
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 551 feet		16. No of acres in lease 17. Spacing Unit dedicated to this well 1280.0	
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. 30 feet		19. Proposed Depth 7934 feet / 18787 feet 20. BLM/BIA Bond No. in file FED: NMB105800930	
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 3509 feet		22. Approximate date work will start* 01/15/2025	23. Estimated duration 60 days
24. Attachments			

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|---|---|
| 1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification.
6. Such other site specific information and/or plans as may be requested by the BLM. |
|---|---|

25. Signature (Electronic Submission)		Name (Printed/Typed) BILL RAMSEY / Ph: (720) 460-3316	Date 07/08/2024
Title Regulatory Analyst			
Approved by (Signature) (Electronic Submission)		Name (Printed/Typed) CHRISTOPHER WALLS / Ph: (575) 234-2234	Date 01/07/2025
Title Petroleum Engineer		Office Carlsbad Field Office	

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
 Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)



C-102 Submit Electronically Via OCD Permitting	State of New Mexico Energy, Minerals & Natural Resources Department OIL CONSERVATION DIVISION	Revised July 9, 2024	
		Submittal Type:	<input type="checkbox"/> Initial Submittal
			<input type="checkbox"/> Amended Report
		<input type="checkbox"/> As Drilled	

WELL LOCATION AND ACREAGE DEDICATION PLAT

API Number 30-015-56197	Pool Code 98220	Pool Name Purple Sage; Wolfcamp (Gas)
Property Code 337038	Property Name UPSLOPE FED COM	Well Number 211H
OGRID No. 372043	Operator Name TAP ROCK OPERATING, LLC.	Ground Level Elevation 3509'
Surface Owner: <input type="checkbox"/> State <input type="checkbox"/> Fee <input type="checkbox"/> Tribal <input type="checkbox"/> Federal		Mineral Owner: <input type="checkbox"/> State <input type="checkbox"/> Fee <input type="checkbox"/> Tribal <input type="checkbox"/> Federal

Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the N/S	Feet from the E/W	Latitude	Longitude	County
H	10	25-S	25-E	-	2357' N	551' E	N 32.1451318	W 104.3769973	EDDY

Bottom Hole Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the N/S	Feet from the E/W	Latitude	Longitude	County
D	9	25-S	25-E	-	990' N	5' W	N 32.1489739	W 104.4098110	EDDY

Dedicated Acres 1280	Infill or Defining Well -	Defining Well API -	Overlapping Spacing Unit (Y/N) -	Consolidated Code -
Order Numbers			Well Setbacks are under Common Ownership: <input type="checkbox"/> Yes <input type="checkbox"/> No	

Kick Off Point (KOP)

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the N/S	Feet from the E/W	Latitude	Longitude	County
A	10	25-S	25-E	-	990' N	50' E	N 32.1488840	W 104.3754248	EDDY


First Take Point (FTP)

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the N/S	Feet from the E/W	Latitude	Longitude	County
A	10	25-S	25-E	-	990' N	330' E	N 32.1488864	W 104.3763296	EDDY


Last Take Point (LTP)

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the N/S	Feet from the E/W	Latitude	Longitude	County
D	9	25-S	25-E	-	990' N	330' W	N 32.1489713	W 104.4087608	EDDY



Unitized Area or Area of Uniform Intrest -	Spacing Unity Type <input type="checkbox"/> Horizontal <input type="checkbox"/> Vertical	Ground Floor Elevation
---	---	------------------------

OPERATOR CERTIFICATION <i>I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief; and, if the well is a vertical or directional well, that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of a working interest or unleased mineral interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.</i> <i>If this well is a horizontal well, I further certify that this organization has received The consent of at least one lessee or owner of a working interest or unleased mineral interest in each tract (in the target pool or formation) in which any part of the well's completed interval will be located or obtained a compulsory pooling order from the division.</i>		SURVEYORS CERTIFICATION <i>I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.</i>  8/30/2024 12:31:40 PM	
Signature _____ Date _____		Signature and Seal of Professional Surveyor _____ Date _____	
Print Name _____		Certificate Number _____	Date of Survey 05/08/2024
E-mail Address _____			


C-102 Submit Electronically Via OCD Permitting	State of New Mexico Energy, Minerals & Natural Resources Department OIL CONSERVATION DIVISION	Revised July 9, 2024	
		Submittal Type:	<input type="checkbox"/> Initial Submittal
			<input type="checkbox"/> Amended Report
		<input type="checkbox"/> As Drilled	
Property Name and Well Number UPSLOPE FED COM 211H			

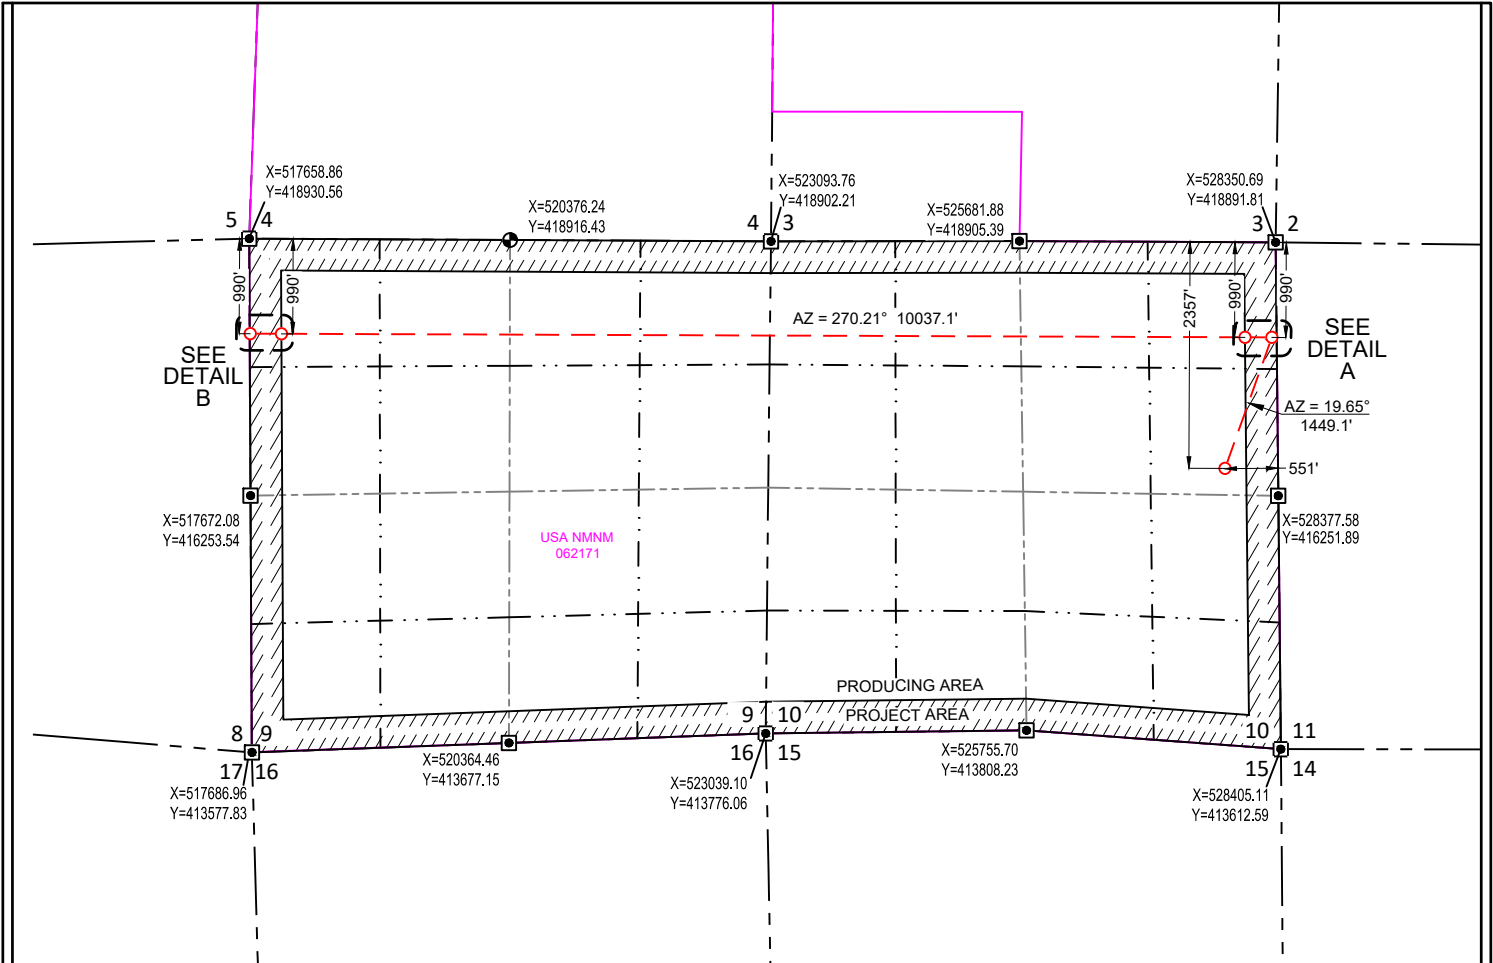

SURFACE LOCATION (SHL)	KICK OFF POINT (KOP)	FIRST TAKE POINT (FTP)
NEW MEXICO EAST NAD 1983 X=527824 Y=416537 LAT.: N 32.1451318 LONG.: W 104.3769973 2357' FNL 551' FEL	NEW MEXICO EAST NAD 1983 X=528311 Y=417902 LAT.: N 32.1488840 LONG.: W 104.3754248 990' FNL 50' FEL	NEW MEXICO EAST NAD 1983 X=528031 Y=417903 LAT.: N 32.1488864 LONG.: W 104.3763296 990' FNL 330' FEL
LAST TAKE POINT (LTP)	BOTTOM HOLE LOCATION (BHL)	
NEW MEXICO EAST NAD 1983 X=517994 Y=417939 LAT.: N 32.1489713 LONG.: W 104.4087608 990' FNL 330' FWL	NEW MEXICO EAST NAD 1983 X=517669 Y=417941 LAT.: N 32.1489739 LONG.: W 104.4098110 990' FNL 5' FWL	



SURVEYORS CERTIFICATION I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief. 05/08/2024 Date of Survey
 8/30/2024 12:31:40 PM

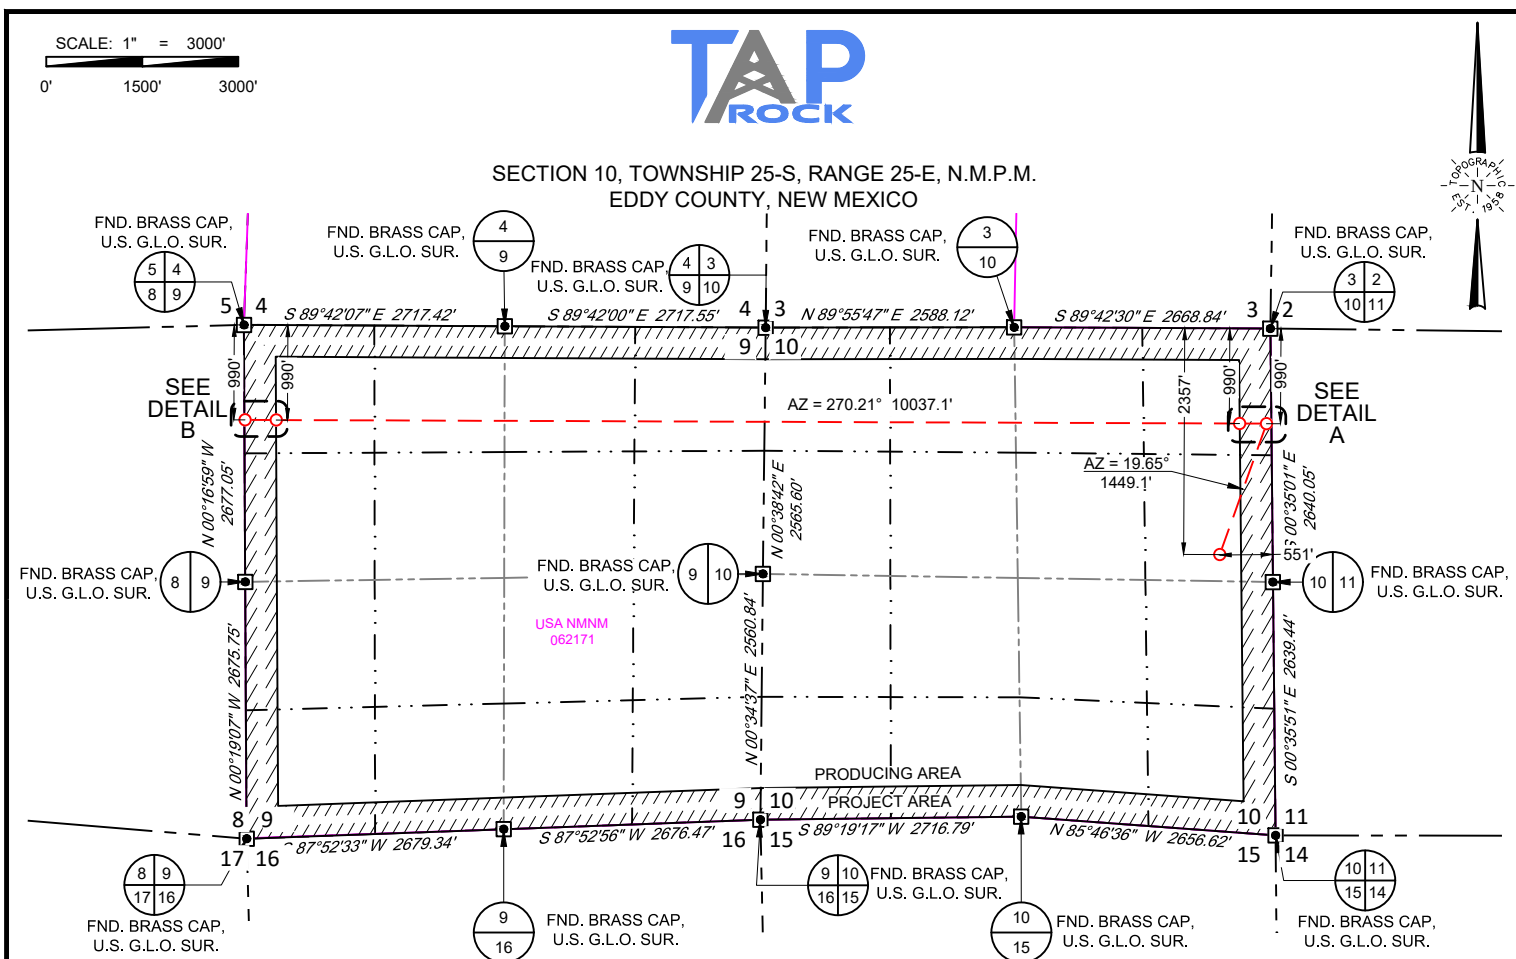

NEW MEXICO EAST
NAD 1983

SURFACE LOCATION (SHL) KICK OFF POINT (KOP) FIRST TAKE POINT (FTP)

NEW MEXICO EAST NAD 1983	NEW MEXICO EAST NAD 1983	NEW MEXICO EAST NAD 1983
X=527824 Y=416537	X=528311 Y=417902	X=528031 Y=417903
LAT.: N 32.1451318	LAT.: N 32.1488840	LAT.: N 32.1488864
LONG.: W 104.3769973	LONG.: W 104.3754248	LONG.: W 104.3763296
2357' FNL 551' FEL	990' FNL 50' FEL	990' FNL 330' FEL

LAST TAKE POINT (LTP) BOTTOM HOLE LOCATION (BHL)

NEW MEXICO EAST NAD 1983	NEW MEXICO EAST NAD 1983
X=517994 Y=417939	X=517669 Y=417941
LAT.: N 32.1489713	LAT.: N 32.1489739
LONG.: W 104.4087608	LONG.: W 104.4098110
990' FNL 330' FWL	990' FNL 5' FWL

LEASE NAME & WELL NO.: UPSLOPE FED COM 211H

SECTION 10 TWP 25-S RGE 25-E SURVEY N.M.P.M.

COUNTY EDDY STATE NM

DESCRIPTION 2357' FNL & 551' FEL



DISTANCE & DIRECTION

FROM INT. OF FM 180. & CR. 724. GO EAST ON CR. 724 ±1.3 MILES. THENCE RIGHT ON LEASE RD ±0.25 MILES TO A POINT ±221 FEET NORTHEAST OF THE LOCATION.

ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREON ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET

THIS EASEMENT/SERVITUDE LOCATION SHOWN HEREON HAS BEEN SURVEYED ON THE GROUND UNDER MY SUPERVISION AND PREPARED ACCORDING TO THE EVIDENCE FOUND AT THE TIME OF SURVEY, AND DATA PROVIDED BY TAP ROCK OPERATING, LLC. THIS CERTIFICATION IS MADE AND LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE. THIS SURVEY IS CERTIFIED FOR THIS TRANSACTION ONLY.

AS OF THE DATE OF SURVEY, ALL ABOVE GROUND APPURTENANCES WITHIN 300' OF THE STAKED LOCATION ARE SHOWN HEREON.



8/30/2024 12:31:40 PM

Ramon A. Dominguez, P.S. No. 24508




481 WINSCOTT ROAD, Ste. 200 • BENBROOK, TEXAS 76126
TELEPHONE: (817) 744-7512 • FAX (817) 744-7554
2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705
TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743
WWW.TOPOGRAPHIC.COM



LEGEND


----- SECTION LINE
 --- PROPOSED ROAD

SECTION 10, TOWNSHIP 25-S, RANGE 25-E, N.M.P.M.
 EDDY COUNTY, NEW MEXICO

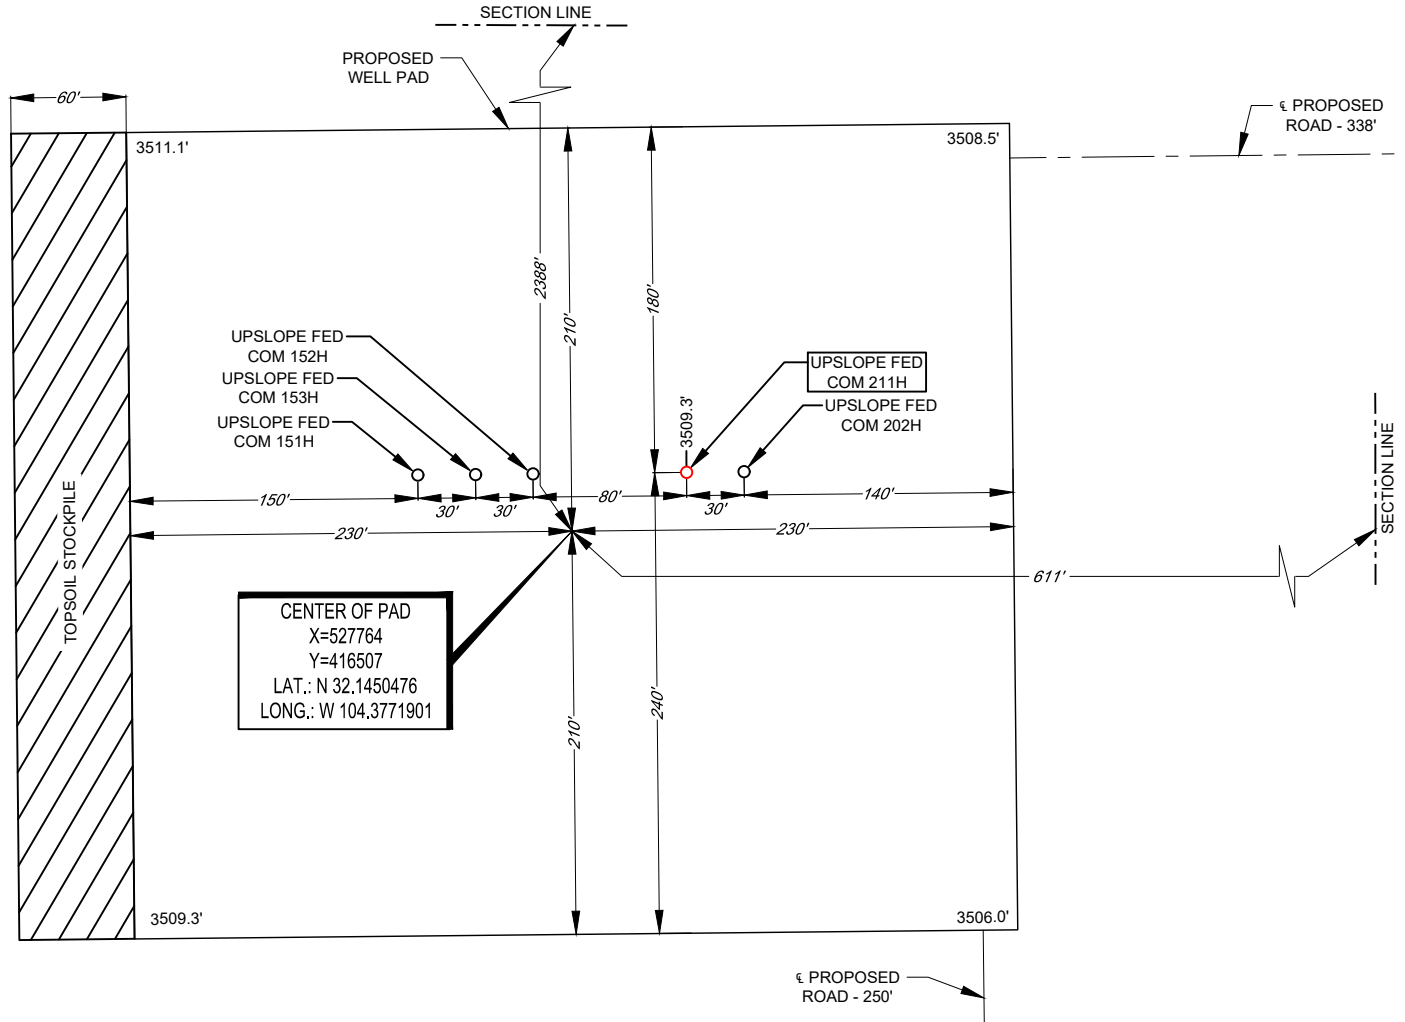

LEASE NAME & WELL NO.: UPSLOPE FED COM 211H
 211H LATITUDE N 32.1451318 211H LONGITUDE W 104.3769973

CENTER OF PAD IS 2388' FNL & 611' FEL




8/30/2024 12:31:41 PM

Ramon A. Dominguez, P.S. No. 24508

ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREON ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET. ELEVATIONS USED ARE NAVD88, OBTAINED THROUGH AN OPUS SOLUTION.

THIS PROPOSED PAD SITE LOCATION SHOWN HEREON HAS BEEN SURVEYED ON THE GROUND UNDER MY SUPERVISION AND PREPARED ACCORDING TO THE EVIDENCE FOUND AT THE TIME OF SURVEY, AND DATA PROVIDED BY TAP ROCK OPERATING, LLC. ONLY THE DATA SHOWN ABOVE IS BEING CERTIFIED TO. ALL OTHER INFORMATION WAS INTENTIONALLY OMITTED. THIS PLAT IS ONLY INTENDED TO BE USED FOR A PERMIT AND IS NOT A BOUNDARY SURVEY. THIS CERTIFICATION IS MADE AND LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE. THIS SURVEY IS CERTIFIED FOR THIS TRANSACTION ONLY.

ORIGINAL DOCUMENT SIZE: 8.5" X 11"



SCALE: 1" = 100'
 0' 50' 100'



481 WINSOTT ROAD, Ste. 200 • BENBROOK, TEXAS 76126
 TELEPHONE: (817) 744-7512 • FAX (817) 744-7554
 2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705
 TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743
 WWW.TOPOGRAPHIC.COM

State of New Mexico
Energy, Minerals and Natural Resources Department

Submit Electronically
Via E-permitting

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description **Effective May 25, 2021**

I. Operator: _____ Tap Rock Operating LLC _____ **OGRID:** _____ 372043 _____ **Date:** _10/_01/_2024

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
Upslope Fed Com 202H		H, 10, 25S 25E	2357 FNL, 521 FEL	1053	3000	5500
Upslope Fed Com 204H		I, 10, 25S 25E	1591 FNL, 561 FEL	1053	3000	5500
Upslope Fed Com 211H		H, 10, 25S 25E	2357 FNL, 551 FEL	1053	3000	5500
Upslope Fed Com 213H		I, 10, 25S 25E	1589 FSL, 531 FEL	1053	3000	5500

IV. Central Delivery Point Name: _____ Highlife/Upslope Fed Com CDP _____ [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Upslope Fed Com 202H		8/1/2025	9/20/2025	11/1/2025	12/1/2025	12/1/2025
Upslope Fed Com 204H		8/1/2025	9/20/2025	11/1/2025	12/1/2025	12/1/2025
Upslope Fed Com 211H		8/1/2025	9/20/2025	11/1/2025	12/1/2025	12/1/2025
Upslope Fed Com 213H		8/1/2025	9/20/2025	11/1/2025	12/1/2025	12/1/2025

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 2 – Enhanced Plan

EFFECTIVE APRIL 1, 2022

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature: 
Printed Name: Bill Ramsey
Title: Sr. Environmental and Regulatory Specialist
E-mail Address: brmasey@taprk.com
Date: 10/1/2024
Phone: 720-238-2787
OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form)
Approved By:
Title:
Approval Date:
Conditions of Approval:



Tap Rock Operating Natural Gas Management Plan

VI. Separation Equipment:

Each surface facility design includes the following process equipment: 3-phase separators (1 separator per well), a sales gas scrubber, one or two 3-phase heater treaters, a vapor recovery tower (VRT), a VRU compressor, multiple water and oil tanks, as well as flare knockouts (HP & LP), and flares (HP & LP). All process vessels will be sized to separate oil, water, gas based upon typical/historical & predicted well performance. Each process vessel will be fitted with an appropriately sized PSV as per ASME code requirements to mitigate vessel rupture and loss of containment. Additionally, the process vessels will be fitted with pressure transmitters tied to the facility control system which will allow operations to monitor pressures and when necessary, shut-in the facility to avoid vessel over-pressure and the potential vent of natural gas. Natural gas will preferentially be sold to pipeline, and only during upset/emergency conditions will gas be directed to the HP flare system. Flash gas from both the 3-phase heater treater and the VRT will be recompressed using a VRU compressor and this gas will also preferentially be directed to the gas sales pipeline. Oil tanks & water tanks will be fitted with 16 oz thief hatches as well as PVRVs to protect the tanks from rupture/collapse. Additionally, the tank vapor outlets and tank vapor capture system will be sized to keep tank pressures below 12 oz. The tank vapor capture system will include a tank vapor blower & knockout as well as a low-pressure flare and knockout. Tank vapors will preferentially be directed to the VRU and the sales gas pipeline. Only during process upsets/emergency conditions will tank vapors be directed to the LP flare system.

VII. Operational Practices:

- During drilling operations- Gas meters will be installed at the shakers and Volume Totalizers will be installed on the pits. In the event that elevated gas levels, or a pit gain are observed, returns will be diverted to a gas buster. Gas coming off the gas buster will be combusted at the flare stack. A 10' or taller flare will be located at least 100' from the SHL.
- During completions operations, including stimulation and frac plug drill out operations, hydrocarbon production to surface is minimized. When gas production does occur, gas will be combusted at a flare stack. A 10' or taller flare will be located at least 100' from the SHL.
- During production operations, all process vessels (separators, heater treaters, VRTs, Tanks) will recompress (where necessary) and route gas outlets into the natural gas gathering pipeline. Gas will preferentially be routed to natural gas gathering pipeline and the flare system will be used only during emergency, malfunction, or if the gas does not meet pipeline specifications. In the event of flaring off-specification gas, operations will pull gas samples twice a week and will also route gas back to pipeline as soon as the gas meets specification. Exceptions to this will include only those qualified emergencies as mentioned in the BLM Waste Prevention Rule.



- To comply with state performance standards, separation and storage equipment will be designed to handle the maximum anticipated throughput and pressure to minimize waste and reduce the likelihood of venting gas to atmosphere. Additionally, each storage atmospheric tank (Oil & Water) will be fitted with a level transmitter to facilitate gauging of the tank without opening of the thief hatch. Any gas collected through the tank vent system is expected to be recompressed and routed to sales. However, in the event of an emergency, the tank vapor capture system will be designed to combust the gas using a flare stack fitted with a continuous or automatic ignitor. The flare stack will be properly anchored and will be located a minimum of 100 feet from the well and storage tanks. Operators will conduct weekly AVO inspections. These AVO inspection records will be stored for the required 5-year period and will be made available upon Division request.

VIII. Best Management Practices:

- When performing routine or preventive maintenance on a vessel or tank, initially all inlet valves are closed, and the vessel or tank is allowed to depressurize through the normal outlet connections to gas sales and/or liquid tanks. Once the vessel or tank is depressurized to lowest acceptable sales outlet pressure, usually around 20 psig, a temporary low-pressure flowline is connected from the vessel or tank to the Vapor Recovery Unit (VRU) for further pressure reduction. Once depressurized to less than 1-2 psig, the remaining natural gas in the vessel or tank is vented to atmosphere through a controlled pressure relief valve. Once the vessel or tank is depressurized to atmospheric pressure, the vessel or tank can be safely opened, and maintenance performed.



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Drilling Plan Data Report

01/08/2025

APD ID: 10400099557

Submission Date: 07/08/2024

Highlighted data
reflects the most
recent changes

Operator Name: TAP ROCK OPERATING LLC

Well Name: UPSLOPE FED COM

Well Number: 211H

Well Type: CONVENTIONAL GAS WELL

Well Work Type: Drill

[Show Final Text](#)

Section 1 - Geologic Formations

Formation ID	Formation Name	Elevation	True Vertical	Measured Depth	Lithologies	Mineral Resources	Producing Formatio
14798247	QUATERNARY	3509	0	0	OTHER : None	NONE	N
14798248	RUSTLER ANHYDRITE	3479	30	30	ANHYDRITE	NONE	N
14798249	TOP SALT	3175	334	334	SALT	OTHER : Salt	N
14798232	BASE OF SALT	2276	1233	1235	SALT	NONE	N
14798233	DELAWARE	2080	1429	1433	SANDSTONE	NONE	N
14798234	LAMAR	2071	1438	1442	SANDSTONE	NATURAL GAS, OIL	N
14798235	BELL CANYON	2027	1482	1487	SANDSTONE	NATURAL GAS, OIL	N
14798236	RAMSEY SAND	1970	1539	1545	SANDSTONE	NATURAL GAS, OIL	N
14798237	CHERRY CANYON	1087	2422	2460	LIMESTONE	NATURAL GAS, OIL	N
14798238	BRUSHY CANYON	210	3299	3421	SANDSTONE	NATURAL GAS, OIL	N
14798239	BONE SPRING LIME	-1497	5006	5244	LIMESTONE, OTHER : Carbonate	NATURAL GAS, OIL	N
14798240	AVALON SAND	-1612	5121	5361	OTHER : Upper - Carbonate	NATURAL GAS, OIL	N
14798241	AVALON SAND	-1872	5381	5624	OTHER : Middle - Carbonate	NATURAL GAS, OIL	N
14798242	BONE SPRING 1ST	-2334	5843	6088	SANDSTONE	NATURAL GAS, OIL	N
14798243	BONE SPRING 2ND	-2503	6012	6257	OTHER : Carbonate	NATURAL GAS, OIL	N
14798244	BONE SPRING 2ND	-2892	6401	6646	SANDSTONE	NATURAL GAS, OIL	N
14798245	BONE SPRING 3RD	-4147	7656	7901	SANDSTONE	NATURAL GAS, OIL	N

Operator Name: TAP ROCK OPERATING LLC

Well Name: UPSLOPE FED COM

Well Number: 211H

Formation ID	Formation Name	Elevation	True Vertical	Measured Depth	Lithologies	Mineral Resources	Producing Formatio
14798246	WOLFCAMP	-4513	8022	8337	OTHER, SHALE : A	NATURAL GAS, OIL	Y

Section 2 - Blowout Prevention

Pressure Rating (PSI): 5M

Rating Depth: 18000

Equipment: At 18,757', a 5M pressure control system is required. The BOP stack consisting of 3 rams with 2 pipe rams, 1 blind ram, and 1 annular preventer will be used below surface casing to TD. See attachments for BOP and choke manifold diagrams. Also present will be an accumulator that meets the requirements of 43 CFR 3172 for the pressure rating of the BOP stack. A rotating head will also be installed as needed. BOP will be inspected and operated as recommended in 43 CFR 3172. A top drive check valve and sub equipped with a full opening valve sized to fit the drill pipe and collars will be available on the rig floor in the open position. The wellhead will be a multi-bowl speed head.

Requesting Variance? YES

Variance request: Tap Rock requests a variance to run a multi-bowl speed head for setting the Intermediate and Production Strings. Tap Rock requests a variance to drill this well using a co-flex line between the BOP and choke manifold. Certification for proposed co-flex hose is attached. The hose is not required by the manufacturer to be anchored. In the event the specific hose is not available, one of equal or higher rating will be used. Tap Rock requests a variance to have the option of batch drilling this well with other wells on the same pad. If this well is batch drilled, after cementing a casing string, a 5M dry hole cap with bleed off valve will be installed. The rig will then walk to another well on the pad. Tap Rock Operating requests to only test BOP connection breaks after rig walks per the procedures and stipulations set forth in the "BOP Shell Test Procedure" document emailed to the BLM on 8/11/22.

Testing Procedure: After surface casing is set and the BOP is nipped up, the BOP pressure tests will be made with a third party tester to 250 psi low, 5000 psi high, and the annular preventer will be tested to 250 psi low, 2500 psi high.

Choke Diagram Attachment:

5M_Choke_Diagram_20241029140002.pdf

BOP Diagram Attachment:

5M_BOP_Diagram_20241029140012.pdf

Section 3 - Casing

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE	14.75	11.75	NEW	API	N	0	320	0	320	3509	3189	320	J-55	42	BUTT	1.13	1.15	DRY	1.6	DRY	1.6
2	INTERMEDIATE	11	8.625	NEW	API	N	0	1492	0	1488	3509	2021	1492	J-55	32	BUTT	1.13	1.15	DRY	1.6	DRY	1.6

Operator Name: TAP ROCK OPERATING LLC

Well Name: UPSLOPE FED COM

Well Number: 211H

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
3	PRODUCTION	7.875	5.5	NEW	NON API	N	0	18787	0	7934	3509	-4425	18787	P-110	20	OTHER - TXP	1.13	1.15	DRY	1.6	DRY	1.6

Casing Attachments

Casing ID: 1StringSURFACE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Casing_Design_Assumptions_20240705120132.pdf

Casing ID: 2StringINTERMEDIATE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Casing_Design_Assumptions_20240705120206.pdf

Operator Name: TAP ROCK OPERATING LLC

Well Name: UPSLOPE FED COM

Well Number: 211H

Casing Attachments

Casing ID: 3StringPRODUCTION

Inspection Document:

Spec Document:
5.5in_TXP_Casing_Spec_20240706104828.PDF

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):
Casing_Design_Assumptions_20240705120253.pdf

Section 4 - Cement

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
SURFACE	Lead		0	0	0	0	0	0	0	None	None
SURFACE	Tail		0	320	334	1.33	14.8	445	100	Class C	5% NCI + LCM
INTERMEDIATE	Lead		0	992	142	2.7	11	384	75	Class C	Bentonite + 1% CaCL2 + 8% NaCl + LCM
INTERMEDIATE	Tail		992	1492	124	1.33	14.8	165	30	Class C	5% NaCl + LCM
PRODUCTION	Lead		1292	7845	405	3.35	10.5	1358	20	Class C	Fluid Loss + Dispersant + Retarder + LCM
PRODUCTION	Tail		7845	18787	2209	1.63	13.2	3603	20	Class H	Fluid Loss + Dispersant + Retarder + LCM

Operator Name: TAP ROCK OPERATING LLC

Well Name: UPSLOPE FED COM

Well Number: 211H

Section 5 - Circulating Medium

Mud System Type: Closed

Will an air or gas system be Used? NO

Description of the equipment for the circulating system in accordance with Onshore Order #2:

Diagram of the equipment for the circulating system in accordance with Onshore Order #2:

Describe what will be on location to control well or mitigate other conditions: All necessary mud products (i.e., barite, pac) for weight addition and fluid loss control will always be on site. Mud program is subject to change due to hole conditions.

Describe the mud monitoring system utilized: Electronic Pason mud monitor system complying with 43 CFR 3172 will be used.

Circulating Medium Table

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
0	320	OTHER : Fresh Water Spud Mud	8.4	8.4							
320	1492	OTHER : Salt Saturated Brine Water	10	10							
1492	1878 7	OTHER : Fresh Water/Cut Brine	9	9							

Section 6 - Test, Logging, Coring

List of production tests including testing procedures, equipment and safety measures:

Electric Logging Program: No open-hole logs are planned at this time. GR will be collected while drilling through the MWD tools from KOP to TD. A 2-person mud logging program will be used from KOP to TD. CBL w/ CCL from as far as gravity will let it fall to TOC.

List of open and cased hole logs run in the well:

GAMMA RAY LOG, MUD LOG/GEOLOGICAL LITHOLOGY LOG, CEMENT BOND LOG,

Coring operation description for the well:

No DSTs or cores are planned at this time.

Operator Name: TAP ROCK OPERATING LLC

Well Name: UPSLOPE FED COM

Well Number: 211H

Section 7 - Pressure

Anticipated Bottom Hole Pressure: 3713

Anticipated Surface Pressure: 1939

Anticipated Bottom Hole Temperature(F): 160

Anticipated abnormal pressures, temperatures, or potential geologic hazards? NO

Describe:

Contingency Plans geohazards description:

Contingency Plans geohazards

Hydrogen Sulfide drilling operations plan required? YES

Hydrogen sulfide drilling operations

Upslope_Slot1_H2S_Plan_20240705120446.pdf

Section 8 - Other Information

Proposed horizontal/directional/multi-lateral plan submission:

Upslope_211H_Directional_Plan_20240705120457.pdf

Other proposed operations facets description:

Other proposed operations facets attachment:

Upslope_211H_Anticollision_Report_20240705120513.pdf

Wellhead_Diagram_3T_20240705120526.pdf

CoFlex_Certs_20240708110115.pdf

Upslope_211H_Drill_Plan_v2_20241029140059.pdf

BOP_Shell_Test_Procedure_20241029140109.pdf

Upslope_WMP_Slot_1_2_20241029140127.pdf

Other Variance attachment:

Tap Rock

Eddy County, NM (NAD83 - NM E)

Upslope


Upslope Fed Com 211H

OH

Plan: Plan #1

Standard Planning Report

24 May, 2024

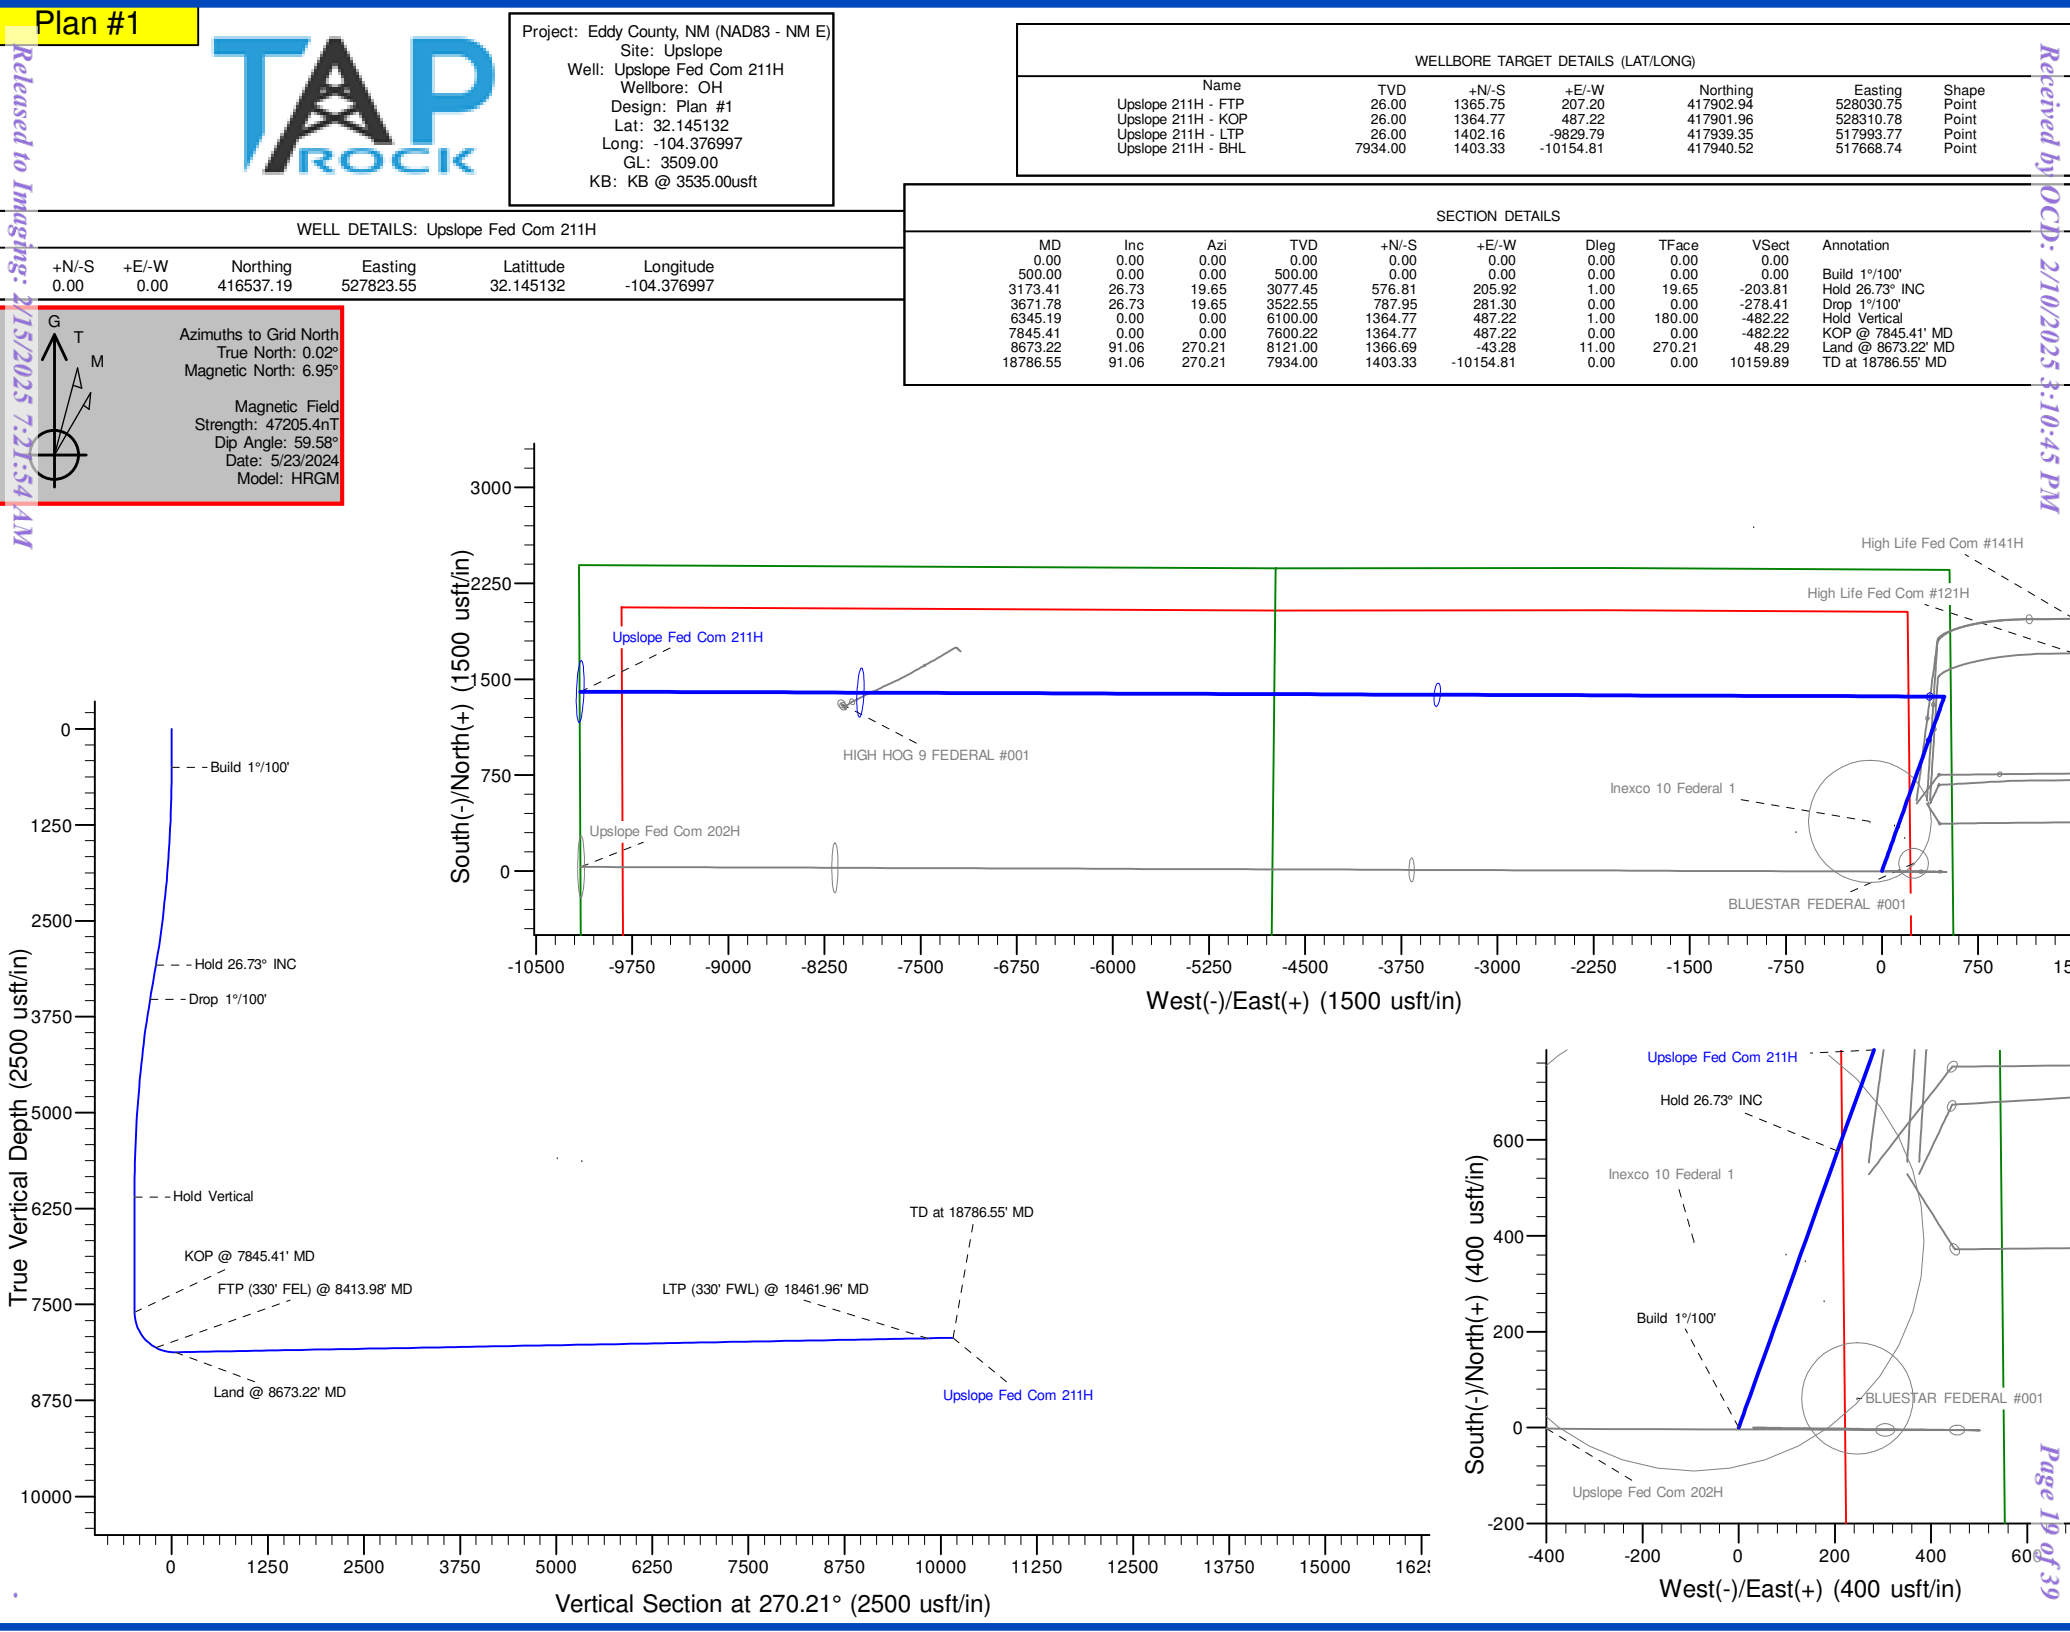

Planning Report

Database:	Fhartmann	Local Co-ordinate Reference:	Well Upslope Fed Com 211H
Company:	Tap Rock	TVD Reference:	KB @ 3535.00usft
Project:	Eddy County, NM (NAD83 - NM E)	MD Reference:	KB @ 3535.00usft
Site:	Upslope	North Reference:	Grid
Well:	Upslope Fed Com 211H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #1		

Project	Eddy County, NM (NAD83 - NM E)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Upslope				
Site Position:		Northing:	415,250.97 usft	Latitude:	32.141596
From:	Lat/Long	Easting:	527,857.02 usft	Longitude:	-104.376888
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16 "		

Well	Upslope Fed Com 211H					
Well Position	+N/-S	0.00 usft	Northing:	416,537.19 usft	Latitude:	32.145132
	+E/-W	0.00 usft	Easting:	527,823.56 usft	Longitude:	-104.376998
Position Uncertainty		0.00 usft	Wellhead Elevation:	usft	Ground Level:	3,509.00 usft
Grid Convergence:	-0.02 °					

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	HRGM	5/23/2024	6.92	59.58	47,205.38458235

Design	Plan #1			
Audit Notes:				
Version:	Phase:	PLAN	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.00	0.00	0.00	270.21

Plan Survey Tool Program			Date	5/24/2024	
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks	
1	0.00	18,786.48	Plan #1 (OH)	MWD+HRGM	
				OWSG MWD + HRGM	

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
500.00	0.00	0.00	500.00	0.00	0.00	0.00	0.00	0.00	0.00	
3,173.41	26.73	19.65	3,077.45	576.81	205.92	1.00	1.00	0.00	19.65	
3,671.78	26.73	19.65	3,522.55	787.95	281.30	0.00	0.00	0.00	0.00	
6,345.19	0.00	0.00	6,100.00	1,364.77	487.22	1.00	-1.00	0.00	180.00	
7,845.41	0.00	0.00	7,600.22	1,364.77	487.22	0.00	0.00	0.00	0.00	
8,673.22	91.06	270.21	8,121.00	1,366.69	-43.28	11.00	11.00	-10.85	270.21	
18,786.55	91.06	270.21	7,934.00	1,403.33	-10,154.81	0.00	0.00	0.00	0.00	Upslope 211H - BHL

Planning Report

Database:	Fhartmann	Local Co-ordinate Reference:	Well Upslope Fed Com 211H
Company:	Tap Rock	TVD Reference:	KB @ 3535.00usft
Project:	Eddy County, NM (NAD83 - NM E)	MD Reference:	KB @ 3535.00usft
Site:	Upslope	North Reference:	Grid
Well:	Upslope Fed Com 211H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Rustler Anhydrite									
100.00	0.00	0.00	100.00	0.00	0.00	0.00	0.00	0.00	0.00
200.00	0.00	0.00	200.00	0.00	0.00	0.00	0.00	0.00	0.00
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00
334.00	0.00	0.00	334.00	0.00	0.00	0.00	0.00	0.00	0.00
Top Salt									
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00	0.00
500.00	0.00	0.00	500.00	0.00	0.00	0.00	0.00	0.00	0.00
Build 1°/100'									
600.00	1.00	19.65	599.99	0.82	0.29	-0.29	1.00	1.00	0.00
700.00	2.00	19.65	699.96	3.29	1.17	-1.16	1.00	1.00	0.00
800.00	3.00	19.65	799.86	7.40	2.64	-2.61	1.00	1.00	0.00
900.00	4.00	19.65	899.68	13.14	4.69	-4.64	1.00	1.00	0.00
1,000.00	5.00	19.65	999.37	20.53	7.33	-7.26	1.00	1.00	0.00
1,100.00	6.00	19.65	1,098.90	29.56	10.55	-10.44	1.00	1.00	0.00
1,200.00	7.00	19.65	1,198.26	40.22	14.36	-14.21	1.00	1.00	0.00
1,235.01	7.35	19.65	1,233.00	44.34	15.83	-15.67	1.00	1.00	0.00
Base Salt									
1,300.00	8.00	19.65	1,297.40	52.51	18.75	-18.55	1.00	1.00	0.00
1,400.00	9.00	19.65	1,396.30	66.43	23.72	-23.47	1.00	1.00	0.00
1,433.12	9.33	19.65	1,429.00	71.40	25.49	-25.23	1.00	1.00	0.00
Delaware Mountain Gp									
1,442.24	9.42	19.65	1,438.00	72.80	25.99	-25.72	1.00	1.00	0.00
Lamar									
1,486.87	9.87	19.65	1,482.00	79.84	28.50	-28.21	1.00	1.00	0.00
Bell Canyon									
1,500.00	10.00	19.65	1,494.93	81.98	29.27	-28.97	1.00	1.00	0.00
1,544.78	10.45	19.65	1,539.00	89.46	31.94	-31.61	1.00	1.00	0.00
Ramsey Sand									
1,600.00	11.00	19.65	1,593.26	99.14	35.39	-35.03	1.00	1.00	0.00
1,700.00	12.00	19.65	1,691.25	117.92	42.10	-41.66	1.00	1.00	0.00
1,800.00	13.00	19.65	1,788.87	138.30	49.37	-48.87	1.00	1.00	0.00
1,900.00	14.00	19.65	1,886.11	160.29	57.22	-56.63	1.00	1.00	0.00
2,000.00	15.00	19.65	1,982.92	183.87	65.64	-64.97	1.00	1.00	0.00
2,100.00	16.00	19.65	2,079.29	209.03	74.62	-73.86	1.00	1.00	0.00
2,200.00	17.00	19.65	2,175.17	235.78	84.17	-83.31	1.00	1.00	0.00
2,300.00	18.00	19.65	2,270.54	264.10	94.28	-93.31	1.00	1.00	0.00
2,400.00	19.00	19.65	2,365.37	293.98	104.95	-103.87	1.00	1.00	0.00
2,460.00	19.60	19.65	2,422.00	312.66	111.62	-110.47	1.00	1.00	0.00
Cherry Canyon									
2,500.00	20.00	19.65	2,459.63	325.42	116.17	-114.98	1.00	1.00	0.00
2,600.00	21.00	19.65	2,553.30	358.40	127.95	-126.63	1.00	1.00	0.00
2,700.00	22.00	19.65	2,646.34	392.92	140.27	-138.83	1.00	1.00	0.00
2,800.00	23.00	19.65	2,738.72	428.96	153.14	-151.56	1.00	1.00	0.00
2,900.00	24.00	19.65	2,830.43	466.51	166.54	-164.83	1.00	1.00	0.00
3,000.00	25.00	19.65	2,921.42	505.57	180.49	-178.63	1.00	1.00	0.00
3,100.00	26.00	19.65	3,011.68	546.11	194.96	-192.96	1.00	1.00	0.00
3,173.41	26.73	19.65	3,077.45	576.81	205.92	-203.81	1.00	1.00	0.00
Hold 26.73° INC									
3,200.00	26.73	19.65	3,101.20	588.08	209.94	-207.79	0.00	0.00	0.00
3,300.00	26.73	19.65	3,190.51	630.45	225.07	-222.76	0.00	0.00	0.00
3,400.00	26.73	19.65	3,279.82	672.81	240.19	-237.73	0.00	0.00	0.00

Planning Report

Database:	Fhartmann	Local Co-ordinate Reference:	Well Upslope Fed Com 211H
Company:	Tap Rock	TVD Reference:	KB @ 3535.00usft
Project:	Eddy County, NM (NAD83 - NM E)	MD Reference:	KB @ 3535.00usft
Site:	Upslope	North Reference:	Grid
Well:	Upslope Fed Com 211H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
3,421.47	26.73	19.65	3,299.00	681.91	243.44	-240.94	0.00	0.00	0.00	
Brushy Canyon										
3,500.00	26.73	19.65	3,369.13	715.18	255.32	-252.69	0.00	0.00	0.00	
3,600.00	26.73	19.65	3,458.44	757.55	270.44	-267.66	0.00	0.00	0.00	
3,671.78	26.73	19.65	3,522.55	787.96	281.30	-278.41	0.00	0.00	0.00	
Drop 1°/100'										
3,700.00	26.45	19.65	3,547.78	799.85	285.55	-282.61	1.00	-1.00	0.00	
3,800.00	25.45	19.65	3,637.70	841.07	300.26	-297.17	1.00	-1.00	0.00	
3,900.00	24.45	19.65	3,728.37	880.80	314.44	-311.21	1.00	-1.00	0.00	
4,000.00	23.45	19.65	3,819.75	919.03	328.09	-324.72	1.00	-1.00	0.00	
4,100.00	22.45	19.65	3,911.83	955.75	341.20	-337.70	1.00	-1.00	0.00	
4,200.00	21.45	19.65	4,004.58	990.96	353.77	-350.14	1.00	-1.00	0.00	
4,300.00	20.45	19.65	4,097.97	1,024.64	365.79	-362.04	1.00	-1.00	0.00	
4,400.00	19.45	19.65	4,191.97	1,056.77	377.27	-373.39	1.00	-1.00	0.00	
4,500.00	18.45	19.65	4,286.55	1,087.36	388.19	-384.20	1.00	-1.00	0.00	
4,600.00	17.45	19.65	4,381.68	1,116.39	398.55	-394.45	1.00	-1.00	0.00	
4,700.00	16.45	19.65	4,477.33	1,143.84	408.35	-404.16	1.00	-1.00	0.00	
4,800.00	15.45	19.65	4,573.48	1,169.73	417.59	-413.30	1.00	-1.00	0.00	
4,900.00	14.45	19.65	4,670.09	1,194.03	426.27	-421.89	1.00	-1.00	0.00	
5,000.00	13.45	19.65	4,767.14	1,216.73	434.37	-429.91	1.00	-1.00	0.00	
5,100.00	12.45	19.65	4,864.59	1,237.84	441.91	-437.37	1.00	-1.00	0.00	
5,200.00	11.45	19.65	4,962.42	1,257.34	448.87	-444.26	1.00	-1.00	0.00	
5,244.43	11.01	19.65	5,006.00	1,265.49	451.78	-447.14	1.00	-1.00	0.00	
Bone Spring Lime										
5,300.00	10.45	19.65	5,060.60	1,275.24	455.26	-450.58	1.00	-1.00	0.00	
5,361.36	9.84	19.65	5,121.00	1,285.41	458.89	-454.18	1.00	-1.00	0.00	
Bone Spring Lime Base										
5,400.00	9.45	19.65	5,159.10	1,291.51	461.07	-456.33	1.00	-1.00	0.00	
5,500.00	8.45	19.65	5,257.88	1,306.17	466.30	-461.51	1.00	-1.00	0.00	
5,600.00	7.45	19.65	5,356.91	1,319.19	470.95	-466.11	1.00	-1.00	0.00	
5,624.28	7.21	19.65	5,381.00	1,322.11	471.99	-467.14	1.00	-1.00	0.00	
Avalon Middle										
5,700.00	6.45	19.65	5,456.18	1,330.59	475.02	-470.14	1.00	-1.00	0.00	
5,800.00	5.45	19.65	5,555.64	1,340.36	478.51	-473.59	1.00	-1.00	0.00	
5,900.00	4.45	19.65	5,655.26	1,348.49	481.41	-476.46	1.00	-1.00	0.00	
6,000.00	3.45	19.65	5,755.02	1,354.98	483.73	-478.76	1.00	-1.00	0.00	
6,088.10	2.57	19.65	5,843.00	1,359.34	485.28	-480.30	1.00	-1.00	0.00	
1st Bone Spring Sand										
6,100.00	2.45	19.65	5,854.89	1,359.83	485.46	-480.47	1.00	-1.00	0.00	
6,200.00	1.45	19.65	5,954.83	1,363.04	486.60	-481.60	1.00	-1.00	0.00	
6,257.18	0.88	19.65	6,012.00	1,364.13	486.99	-481.99	1.00	-1.00	0.00	
2nd Bone Spring Carb FS										
6,300.00	0.45	19.65	6,054.82	1,364.60	487.16	-482.16	1.00	-1.00	0.00	
6,345.19	0.00	0.00	6,100.01	1,364.77	487.22	-482.22	1.00	-1.00	0.00	
Hold Vertical										
6,400.00	0.00	0.00	6,154.82	1,364.77	487.22	-482.22	0.00	0.00	0.00	
6,500.00	0.00	0.00	6,254.82	1,364.77	487.22	-482.22	0.00	0.00	0.00	
6,600.00	0.00	0.00	6,354.82	1,364.77	487.22	-482.22	0.00	0.00	0.00	
6,646.19	0.00	0.00	6,401.00	1,364.77	487.22	-482.22	0.00	0.00	0.00	
2nd Bone Spring Sand										
6,700.00	0.00	0.00	6,454.82	1,364.77	487.22	-482.22	0.00	0.00	0.00	
6,800.00	0.00	0.00	6,554.82	1,364.77	487.22	-482.22	0.00	0.00	0.00	
6,900.00	0.00	0.00	6,654.82	1,364.77	487.22	-482.22	0.00	0.00	0.00	

Planning Report

Database:	Fhartmann	Local Co-ordinate Reference:	Well Upslope Fed Com 211H
Company:	Tap Rock	TVD Reference:	KB @ 3535.00usft
Project:	Eddy County, NM (NAD83 - NM E)	MD Reference:	KB @ 3535.00usft
Site:	Upslope	North Reference:	Grid
Well:	Upslope Fed Com 211H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
6,997.19	0.00	0.00	6,752.00	1,364.77	487.22	-482.22	0.00	0.00	0.00	
3rd Bone Spring Carbonate										
7,000.00	0.00	0.00	6,754.82	1,364.77	487.22	-482.22	0.00	0.00	0.00	
7,100.00	0.00	0.00	6,854.82	1,364.77	487.22	-482.22	0.00	0.00	0.00	
7,200.00	0.00	0.00	6,954.82	1,364.77	487.22	-482.22	0.00	0.00	0.00	
7,300.00	0.00	0.00	7,054.82	1,364.77	487.22	-482.22	0.00	0.00	0.00	
7,400.00	0.00	0.00	7,154.82	1,364.77	487.22	-482.22	0.00	0.00	0.00	
7,500.00	0.00	0.00	7,254.82	1,364.77	487.22	-482.22	0.00	0.00	0.00	
7,600.00	0.00	0.00	7,354.82	1,364.77	487.22	-482.22	0.00	0.00	0.00	
7,700.00	0.00	0.00	7,454.82	1,364.77	487.22	-482.22	0.00	0.00	0.00	
7,800.00	0.00	0.00	7,554.82	1,364.77	487.22	-482.22	0.00	0.00	0.00	
7,845.41	0.00	0.00	7,600.23	1,364.77	487.22	-482.22	0.00	0.00	0.00	
KOP @ 7845.41' MD										
7,850.00	0.51	270.21	7,604.82	1,364.77	487.20	-482.19	11.01	11.01	0.00	
7,900.00	6.01	270.21	7,654.72	1,364.78	484.36	-479.36	11.00	11.00	0.00	
7,901.29	6.15	270.21	7,656.00	1,364.78	484.23	-479.22	11.00	11.00	0.00	
3rd Bone Spring Sand										
7,950.00	11.51	270.21	7,704.11	1,364.81	476.75	-471.75	11.00	11.00	0.00	
8,000.00	17.01	270.21	7,752.56	1,364.85	464.45	-459.44	11.00	11.00	0.00	
8,050.00	22.51	270.21	7,799.59	1,364.91	447.55	-442.55	11.00	11.00	0.00	
8,100.00	28.01	270.21	7,844.80	1,364.99	426.23	-421.22	11.00	11.00	0.00	
8,150.00	33.51	270.21	7,887.75	1,365.08	400.67	-395.66	11.00	11.00	0.00	
8,150.30	33.54	270.21	7,888.00	1,365.08	400.50	-395.50	11.00	11.00	0.00	
3rd BS W Sand										
8,200.00	39.01	270.21	7,928.05	1,365.19	371.11	-366.11	11.00	11.00	0.00	
8,250.00	44.51	270.21	7,965.34	1,365.31	337.83	-332.82	11.00	11.00	0.00	
8,300.00	50.01	270.21	7,999.26	1,365.44	301.12	-296.12	11.00	11.00	0.00	
8,336.97	54.07	270.21	8,022.00	1,365.55	271.98	-266.97	11.00	11.00	0.00	
Wolfcamp A X Sand										
8,350.00	55.51	270.21	8,029.51	1,365.59	261.33	-256.33	11.00	11.00	0.00	
8,400.00	61.01	270.21	8,055.81	1,365.74	218.83	-213.82	11.00	11.00	0.00	
8,413.98	62.54	270.21	8,062.42	1,365.79	206.51	-201.51	11.00	11.00	0.00	
FTP (330' FEL) @ 8413.98' MD										
8,450.00	66.51	270.21	8,077.91	1,365.90	174.00	-169.00	11.00	11.00	0.00	
8,463.15	67.95	270.21	8,083.00	1,365.95	161.88	-156.87	11.00	11.00	0.00	
Wolfcamp A Y Sand										
8,500.00	72.01	270.21	8,095.61	1,366.07	127.26	-122.26	11.00	11.00	0.00	
8,550.00	77.51	270.21	8,108.75	1,366.25	79.04	-74.03	11.00	11.00	0.00	
8,600.00	83.01	270.21	8,117.21	1,366.43	29.78	-24.77	11.00	11.00	0.00	
8,650.00	88.51	270.21	8,120.91	1,366.61	-20.06	25.07	11.00	11.00	0.00	
8,673.22	91.06	270.21	8,121.00	1,366.69	-43.28	48.29	11.00	11.00	0.00	
Land @ 8673.22' MD										
8,700.00	91.06	270.21	8,120.51	1,366.79	-70.05	75.06	0.00	0.00	0.00	
8,800.00	91.06	270.21	8,118.66	1,367.15	-170.04	175.05	0.00	0.00	0.00	
8,900.00	91.06	270.21	8,116.81	1,367.51	-270.02	275.03	0.00	0.00	0.00	
9,000.00	91.06	270.21	8,114.96	1,367.87	-370.00	375.01	0.00	0.00	0.00	
9,100.00	91.06	270.21	8,113.11	1,368.24	-469.98	475.00	0.00	0.00	0.00	
9,200.00	91.06	270.21	8,111.26	1,368.60	-569.97	574.98	0.00	0.00	0.00	
9,300.00	91.06	270.21	8,109.41	1,368.96	-669.95	674.96	0.00	0.00	0.00	
9,400.00	91.06	270.21	8,107.56	1,369.32	-769.93	774.94	0.00	0.00	0.00	
9,500.00	91.06	270.21	8,105.71	1,369.69	-869.91	874.93	0.00	0.00	0.00	
9,600.00	91.06	270.21	8,103.87	1,370.05	-969.89	974.91	0.00	0.00	0.00	
9,700.00	91.06	270.21	8,102.02	1,370.41	-1,069.88	1,074.89	0.00	0.00	0.00	

Planning Report

Database:	Fhartmann	Local Co-ordinate Reference:	Well Upslope Fed Com 211H
Company:	Tap Rock	TVD Reference:	KB @ 3535.00usft
Project:	Eddy County, NM (NAD83 - NM E)	MD Reference:	KB @ 3535.00usft
Site:	Upslope	North Reference:	Grid
Well:	Upslope Fed Com 211H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
9,800.00	91.06	270.21	8,100.17	1,370.77	-1,169.86	1,174.88	0.00	0.00	0.00	
9,900.00	91.06	270.21	8,098.32	1,371.14	-1,269.84	1,274.86	0.00	0.00	0.00	
10,000.00	91.06	270.21	8,096.47	1,371.50	-1,369.82	1,374.84	0.00	0.00	0.00	
10,100.00	91.06	270.21	8,094.62	1,371.86	-1,469.81	1,474.82	0.00	0.00	0.00	
10,200.00	91.06	270.21	8,092.77	1,372.22	-1,569.79	1,574.81	0.00	0.00	0.00	
10,300.00	91.06	270.21	8,090.92	1,372.58	-1,669.77	1,674.79	0.00	0.00	0.00	
10,400.00	91.06	270.21	8,089.07	1,372.95	-1,769.75	1,774.77	0.00	0.00	0.00	
10,500.00	91.06	270.21	8,087.22	1,373.31	-1,869.74	1,874.76	0.00	0.00	0.00	
10,600.00	91.06	270.21	8,085.37	1,373.67	-1,969.72	1,974.74	0.00	0.00	0.00	
10,700.00	91.06	270.21	8,083.53	1,374.03	-2,069.70	2,074.72	0.00	0.00	0.00	
10,800.00	91.06	270.21	8,081.68	1,374.40	-2,169.68	2,174.70	0.00	0.00	0.00	
10,900.00	91.06	270.21	8,079.83	1,374.76	-2,269.66	2,274.69	0.00	0.00	0.00	
11,000.00	91.06	270.21	8,077.98	1,375.12	-2,369.65	2,374.67	0.00	0.00	0.00	
11,100.00	91.06	270.21	8,076.13	1,375.48	-2,469.63	2,474.65	0.00	0.00	0.00	
11,200.00	91.06	270.21	8,074.28	1,375.85	-2,569.61	2,574.64	0.00	0.00	0.00	
11,300.00	91.06	270.21	8,072.43	1,376.21	-2,669.59	2,674.62	0.00	0.00	0.00	
11,400.00	91.06	270.21	8,070.58	1,376.57	-2,769.58	2,774.60	0.00	0.00	0.00	
11,500.00	91.06	270.21	8,068.73	1,376.93	-2,869.56	2,874.59	0.00	0.00	0.00	
11,600.00	91.06	270.21	8,066.88	1,377.29	-2,969.54	2,974.57	0.00	0.00	0.00	
11,700.00	91.06	270.21	8,065.03	1,377.66	-3,069.52	3,074.55	0.00	0.00	0.00	
11,800.00	91.06	270.21	8,063.19	1,378.02	-3,169.50	3,174.53	0.00	0.00	0.00	
11,900.00	91.06	270.21	8,061.34	1,378.38	-3,269.49	3,274.52	0.00	0.00	0.00	
12,000.00	91.06	270.21	8,059.49	1,378.74	-3,369.47	3,374.50	0.00	0.00	0.00	
12,100.00	91.06	270.21	8,057.64	1,379.11	-3,469.45	3,474.48	0.00	0.00	0.00	
12,200.00	91.06	270.21	8,055.79	1,379.47	-3,569.43	3,574.47	0.00	0.00	0.00	
12,300.00	91.06	270.21	8,053.94	1,379.83	-3,669.42	3,674.45	0.00	0.00	0.00	
12,400.00	91.06	270.21	8,052.09	1,380.19	-3,769.40	3,774.43	0.00	0.00	0.00	
12,500.00	91.06	270.21	8,050.24	1,380.56	-3,869.38	3,874.41	0.00	0.00	0.00	
12,600.00	91.06	270.21	8,048.39	1,380.92	-3,969.36	3,974.40	0.00	0.00	0.00	
12,700.00	91.06	270.21	8,046.54	1,381.28	-4,069.34	4,074.38	0.00	0.00	0.00	
12,800.00	91.06	270.21	8,044.70	1,381.64	-4,169.33	4,174.36	0.00	0.00	0.00	
12,900.00	91.06	270.21	8,042.85	1,382.00	-4,269.31	4,274.35	0.00	0.00	0.00	
13,000.00	91.06	270.21	8,041.00	1,382.37	-4,369.29	4,374.33	0.00	0.00	0.00	
13,100.00	91.06	270.21	8,039.15	1,382.73	-4,469.27	4,474.31	0.00	0.00	0.00	
13,200.00	91.06	270.21	8,037.30	1,383.09	-4,569.26	4,574.29	0.00	0.00	0.00	
13,300.00	91.06	270.21	8,035.45	1,383.45	-4,669.24	4,674.28	0.00	0.00	0.00	
13,400.00	91.06	270.21	8,033.60	1,383.82	-4,769.22	4,774.26	0.00	0.00	0.00	
13,500.00	91.06	270.21	8,031.75	1,384.18	-4,869.20	4,874.24	0.00	0.00	0.00	
13,600.00	91.06	270.21	8,029.90	1,384.54	-4,969.18	4,974.23	0.00	0.00	0.00	
13,700.00	91.06	270.21	8,028.05	1,384.90	-5,069.17	5,074.21	0.00	0.00	0.00	
13,800.00	91.06	270.21	8,026.20	1,385.27	-5,169.15	5,174.19	0.00	0.00	0.00	
13,900.00	91.06	270.21	8,024.36	1,385.63	-5,269.13	5,274.17	0.00	0.00	0.00	
14,000.00	91.06	270.21	8,022.51	1,385.99	-5,369.11	5,374.16	0.00	0.00	0.00	
14,100.00	91.06	270.21	8,020.66	1,386.35	-5,469.10	5,474.14	0.00	0.00	0.00	
14,200.00	91.06	270.21	8,018.81	1,386.71	-5,569.08	5,574.12	0.00	0.00	0.00	
14,300.00	91.06	270.21	8,016.96	1,387.08	-5,669.06	5,674.11	0.00	0.00	0.00	
14,400.00	91.06	270.21	8,015.11	1,387.44	-5,769.04	5,774.09	0.00	0.00	0.00	
14,500.00	91.06	270.21	8,013.26	1,387.80	-5,869.03	5,874.07	0.00	0.00	0.00	
14,600.00	91.06	270.21	8,011.41	1,388.16	-5,969.01	5,974.06	0.00	0.00	0.00	
14,700.00	91.06	270.21	8,009.56	1,388.53	-6,068.99	6,074.04	0.00	0.00	0.00	
14,800.00	91.06	270.21	8,007.71	1,388.89	-6,168.97	6,174.02	0.00	0.00	0.00	
14,900.00	91.06	270.21	8,005.86	1,389.25	-6,268.95	6,274.00	0.00	0.00	0.00	
15,000.00	91.06	270.21	8,004.02	1,389.61	-6,368.94	6,373.99	0.00	0.00	0.00	
15,100.00	91.06	270.21	8,002.17	1,389.98	-6,468.92	6,473.97	0.00	0.00	0.00	

Planning Report

Database:	Fhartmann	Local Co-ordinate Reference:	Well Upslope Fed Com 211H
Company:	Tap Rock	TVD Reference:	KB @ 3535.00usft
Project:	Eddy County, NM (NAD83 - NM E)	MD Reference:	KB @ 3535.00usft
Site:	Upslope	North Reference:	Grid
Well:	Upslope Fed Com 211H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
15,200.00	91.06	270.21	8,000.32	1,390.34	-6,568.90	6,573.95	0.00	0.00	0.00	
15,300.00	91.06	270.21	7,998.47	1,390.70	-6,668.88	6,673.94	0.00	0.00	0.00	
15,400.00	91.06	270.21	7,996.62	1,391.06	-6,768.87	6,773.92	0.00	0.00	0.00	
15,500.00	91.06	270.21	7,994.77	1,391.42	-6,868.85	6,873.90	0.00	0.00	0.00	
15,600.00	91.06	270.21	7,992.92	1,391.79	-6,968.83	6,973.88	0.00	0.00	0.00	
15,700.00	91.06	270.21	7,991.07	1,392.15	-7,068.81	7,073.87	0.00	0.00	0.00	
15,800.00	91.06	270.21	7,989.22	1,392.51	-7,168.79	7,173.85	0.00	0.00	0.00	
15,900.00	91.06	270.21	7,987.37	1,392.87	-7,268.78	7,273.83	0.00	0.00	0.00	
16,000.00	91.06	270.21	7,985.53	1,393.24	-7,368.76	7,373.82	0.00	0.00	0.00	
16,100.00	91.06	270.21	7,983.68	1,393.60	-7,468.74	7,473.80	0.00	0.00	0.00	
16,200.00	91.06	270.21	7,981.83	1,393.96	-7,568.72	7,573.78	0.00	0.00	0.00	
16,300.00	91.06	270.21	7,979.98	1,394.32	-7,668.71	7,673.76	0.00	0.00	0.00	
16,400.00	91.06	270.21	7,978.13	1,394.69	-7,768.69	7,773.75	0.00	0.00	0.00	
16,500.00	91.06	270.21	7,976.28	1,395.05	-7,868.67	7,873.73	0.00	0.00	0.00	
16,600.00	91.06	270.21	7,974.43	1,395.41	-7,968.65	7,973.71	0.00	0.00	0.00	
16,700.00	91.06	270.21	7,972.58	1,395.77	-8,068.63	8,073.70	0.00	0.00	0.00	
16,800.00	91.06	270.21	7,970.73	1,396.13	-8,168.62	8,173.68	0.00	0.00	0.00	
16,900.00	91.06	270.21	7,968.88	1,396.50	-8,268.60	8,273.66	0.00	0.00	0.00	
17,000.00	91.06	270.21	7,967.03	1,396.86	-8,368.58	8,373.64	0.00	0.00	0.00	
17,100.00	91.06	270.21	7,965.19	1,397.22	-8,468.56	8,473.63	0.00	0.00	0.00	
17,200.00	91.06	270.21	7,963.34	1,397.58	-8,568.55	8,573.61	0.00	0.00	0.00	
17,300.00	91.06	270.21	7,961.49	1,397.95	-8,668.53	8,673.59	0.00	0.00	0.00	
17,400.00	91.06	270.21	7,959.64	1,398.31	-8,768.51	8,773.58	0.00	0.00	0.00	
17,500.00	91.06	270.21	7,957.79	1,398.67	-8,868.49	8,873.56	0.00	0.00	0.00	
17,600.00	91.06	270.21	7,955.94	1,399.03	-8,968.47	8,973.54	0.00	0.00	0.00	
17,700.00	91.06	270.21	7,954.09	1,399.40	-9,068.46	9,073.53	0.00	0.00	0.00	
17,800.00	91.06	270.21	7,952.24	1,399.76	-9,168.44	9,173.51	0.00	0.00	0.00	
17,900.00	91.06	270.21	7,950.39	1,400.12	-9,268.42	9,273.49	0.00	0.00	0.00	
18,000.00	91.06	270.21	7,948.54	1,400.48	-9,368.40	9,373.47	0.00	0.00	0.00	
18,100.00	91.06	270.21	7,946.69	1,400.84	-9,468.39	9,473.46	0.00	0.00	0.00	
18,200.00	91.06	270.21	7,944.85	1,401.21	-9,568.37	9,573.44	0.00	0.00	0.00	
18,300.00	91.06	270.21	7,943.00	1,401.57	-9,668.35	9,673.42	0.00	0.00	0.00	
18,400.00	91.06	270.21	7,941.15	1,401.93	-9,768.33	9,773.41	0.00	0.00	0.00	
18,461.96	91.06	270.21	7,940.00	1,402.16	-9,830.28	9,835.35	0.00	0.00	0.00	
LTP (330' FWL) @ 18461.96' MD										
18,500.00	91.06	270.21	7,939.30	1,402.29	-9,868.32	9,873.39	0.00	0.00	0.00	
18,600.00	91.06	270.21	7,937.45	1,402.66	-9,968.30	9,973.37	0.00	0.00	0.00	
18,700.00	91.06	270.21	7,935.60	1,403.02	-10,068.28	10,073.35	0.00	0.00	0.00	
18,786.55	91.06	270.21	7,934.00	1,403.33	-10,154.81	10,159.89	0.00	0.00	0.00	
TD at 18786.55' MD										

Planning Report

Database:	Fhartmann	Local Co-ordinate Reference:	Well Upslope Fed Com 211H
Company:	Tap Rock	TVD Reference:	KB @ 3535.00usft
Project:	Eddy County, NM (NAD83 - NM E)	MD Reference:	KB @ 3535.00usft
Site:	Upslope	North Reference:	Grid
Well:	Upslope Fed Com 211H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #1		

Design Targets									
Target Name									
- hit/miss target	Dip Angle	Dip Dir.	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
- Shape	(°)	(°)	(usft)	(usft)	(usft)	(usft)	(usft)		
Upslope 211H - LTP	0.00	360.00	26.00	1,402.16	-9,829.79	417,939.35	517,993.77	32.148971	-104.408761
- plan misses target center by 7912.66usft at 18607.80usft MD (7937.31 TVD, 1402.68 N, -9976.10 E)									
- Point									
Upslope 211H - FTP	0.00	0.00	26.00	1,365.75	207.20	417,902.94	528,030.75	32.148886	-104.376330
- plan misses target center by 1381.38usft at 26.00usft MD (26.00 TVD, 0.00 N, 0.00 E)									
- Point									
Upslope 211H - KOP	0.00	0.00	26.00	1,364.77	487.22	417,901.96	528,310.78	32.148884	-104.375425
- plan misses target center by 1449.13usft at 26.00usft MD (26.00 TVD, 0.00 N, 0.00 E)									
- Point									
Upslope 211H - BHL	0.00	0.00	7,934.00	1,403.33	-10,154.81	417,940.52	517,668.75	32.148974	-104.409811
- plan hits target center									
- Point									

Formations						
Measured Depth	Vertical Depth	Name	Lithology	Dip	Dip Direction	
(usft)	(usft)			(°)	(°)	
0.00	0.00	Rustler Anhydrite				
334.00	334.00	Top Salt				
1,235.01	1,233.00	Base Salt				
1,433.12	1,429.00	Delaware Mountain Gp				
1,442.24	1,438.00	Lamar				
1,486.87	1,482.00	Bell Canyon				
1,544.78	1,539.00	Ramsey Sand				
2,460.00	2,422.00	Cherry Canyon				
3,421.47	3,299.00	Brushy Canyon				
5,244.43	5,006.00	Bone Spring Lime				
5,361.36	5,121.00	Bone Spring Lime Base				
5,624.28	5,381.00	Avalon Middle				
6,088.10	5,843.00	1st Bone Spring Sand				
6,257.18	6,012.00	2nd Bone Spring Carb FS				
6,646.19	6,401.00	2nd Bone Spring Sand				
6,997.19	6,752.00	3rd Bone Spring Carbonate				
7,901.29	7,656.00	3rd Bone Spring Sand				
8,150.30	7,888.00	3rd BS W Sand				
8,336.97	8,022.00	Wolfcamp A X Sand				
8,463.15	8,083.00	Wolfcamp A Y Sand				

Planning Report

Database:	Fhartmann	Local Co-ordinate Reference:	Well Upslope Fed Com 211H
Company:	Tap Rock	TVD Reference:	KB @ 3535.00usft
Project:	Eddy County, NM (NAD83 - NM E)	MD Reference:	KB @ 3535.00usft
Site:	Upslope	North Reference:	Grid
Well:	Upslope Fed Com 211H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #1		

Plan Annotations				
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
500.00	500.00	0.00	0.00	Build 1°/100'
3,173.41	3,077.45	576.81	205.92	Hold 26.73° INC
3,671.78	3,522.55	787.96	281.30	Drop 1°/100'
6,345.19	6,100.01	1,364.77	487.22	Hold Vertical
7,845.41	7,600.23	1,364.77	487.22	KOP @ 7845.41' MD
8,413.98	8,062.42	1,365.79	206.51	FTP (330' FEL) @ 8413.98' MD
8,673.22	8,121.00	1,366.69	-43.28	Land @ 8673.22' MD
18,461.96	7,940.00	1,402.16	-9,830.28	LTP (330' FWL) @ 18461.96' MD
18,786.55	7,934.00	1,403.33	-10,154.81	TD at 18786.55' MD

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	Tap Rock Operating LLC
WELL NAME & NO.:	Upslope Fed Com 211H
LOCATION:	Sec 10-25S-25E-NMP
COUNTY:	Eddy County, New Mexico ▼

COA

H ₂ S	<input checked="" type="radio"/> No	<input type="radio"/> Yes
Potash / WIPP	<input checked="" type="radio"/> None <input type="radio"/> Secretary <input type="radio"/> R-111-Q <input type="checkbox"/> Open Annulus <input type="checkbox"/> WIPP	
Cave / Karst	<input type="radio"/> Low <input type="radio"/> Medium <input type="radio"/> High <input checked="" type="radio"/> Critical	
Wellhead	<input type="radio"/> Conventional <input checked="" type="radio"/> Multibowl <input type="radio"/> Both <input type="radio"/> Diverter	
Cementing	<input type="checkbox"/> Primary Squeeze <input type="checkbox"/> Cont. Squeeze <input type="checkbox"/> EchoMeter <input type="checkbox"/> DV Tool	
Special Req	<input type="checkbox"/> Capitan Reef <input type="checkbox"/> Water Disposal <input checked="" type="checkbox"/> COM <input type="checkbox"/> Unit	
Waste Prev.	<input type="radio"/> Self-Certification <input checked="" type="radio"/> Waste Min. Plan <input type="radio"/> APD Submitted prior to 06/10/2024	
Additional Language	<input checked="" type="checkbox"/> Flex Hose <input type="checkbox"/> Casing Clearance <input type="checkbox"/> Pilot Hole <input checked="" type="checkbox"/> Break Testing <input type="checkbox"/> Four-String <input type="checkbox"/> Offline Cementing <input type="checkbox"/> Fluid-Filled	

A. HYDROGEN SULFIDE

Hydrogen Sulfide (H₂S) monitors shall be installed prior to drilling out the surface shoe. If H₂S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet 43 CFR 3176 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.

B. CASING

1. The **11-3/4** inch surface casing shall be set at approximately **350** feet (a minimum of 70 feet (Eddy County) into the Rustler Anhydrite, above the salt, and below usable fresh water) and cemented to the surface. *Set depth adjusted per BLM geologist.*
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or **500 pounds compressive strength**, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.

- d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The minimum required fill of cement behind the **8-5/8** inch intermediate casing (*set at 1450' per BLM geologist*) is:
 - Cement to surface. If cement does not circulate see B.1.a, c-d above. **Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst, Capitan Reef, or potash.**
- ❖ In Critical Cave/Karst Areas cement must come to surface on the first three casing strings.
3. The minimum required fill of cement behind the **5-1/2** inch production casing is:
 - Cement to surface. If cement does not circulate, contact the appropriate BLM office. **Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst, Capitan Reef, or potash.**

C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).
2. Operator has proposed a multi-bowl wellhead assembly. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. If the cement does not circulate and one-inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
 - e. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172 must be followed.

D. SPECIAL REQUIREMENT (S)

Communitization Agreement

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and

lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.

- The operator will submit an as-drilled survey well plat of the well completion, but are not limited to, those specified in 43 CFR 3171 and 3172.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

BOPE Break Testing Variance

- BOPE Break Testing is ONLY permitted for intervals utilizing a 5M BOPE or less. (**Annular preventer must be tested to a minimum of 70% of BOPE working pressure and shall be higher than the MASP.**)
- BOPE Break Testing is NOT permitted to drilling the production hole section.
- Variance only pertains to the intermediate hole-sections and no deeper than the Bone Springs formation.
- While in transfer between wells, the BOPE shall be secured by the hydraulic carrier or cradle.
- Any well control event while drilling require notification to the BLM Petroleum Engineer (**575-706-2779**) prior to the commencement of any BOPE Break Testing operations.
- A full BOPE test is required prior to drilling the first deep intermediate hole section. If any subsequent hole interval is deeper than the first, a full BOPE test will be required. (200' TVD tolerance between intermediate shoes is allowable).
- The BLM is to be contacted (575-361-2822 Eddy County) 4 hours prior to BOPE tests.
- As a minimum, a full BOPE test shall be performed at 21-day intervals.
- In the event any repairs or replacement of the BOPE is required, the BOPE shall test as per **43 CFR 3172**.
- If in the event break testing is not utilized, then a full BOPE test would be conducted.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

Contact Eddy County Petroleum Engineering Inspection Staff:

Email or call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220;

BLM NM CFO DrillingNotifications@BLM.GOV; (575) 361-2822

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - i. Notify the BLM when moving in and removing the Spudder Rig.
 - ii. Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - iii. BOP/BOPE test to be conducted per **43 CFR 3172** as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. For intervals in which cement to surface is required, cement to surface should be verified with a visual check and density or pH check to differentiate cement from spacer and drilling mud. The results should be documented in the driller's log and daily reports.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following

- conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends of both lead and tail cement, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
 4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
 5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
 6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
 7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
 8. Whenever a casing string is cemented in the R-111-Q potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in **43 CFR 3172**.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.

3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - i. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - ii. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - iii. Manufacturer representative shall install the test plug for the initial BOP test.
 - iv. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172.6(b)(9) must be followed.
 - v. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - i. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead cement), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - ii. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the cement plug. The BOPE test can be initiated after bumping the cement plug with the casing valve open. (only applies to single stage cement jobs, prior to the cement setting up.)
 - iii. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer and can be initiated immediately with the casing valve open. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to **43 CFR 3172** with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for 8 hours or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).

- iv. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- v. The results of the test shall be reported to the appropriate BLM office.
- vi. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- vii. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- viii. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per **43 CFR 3172**.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area. Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.



Hydrogen Sulfide Drilling

Operations Plan

Tap Rock Resources

1 H2S safety instructions to the following:

- Characteristics of H2S
- Physical effects and hazards
- Principal and operation of H2S detectors, warning system and briefing areas
- Evacuation procedures, routes and first aid
- Proper use of safety equipment & life support systems
- Essential personnel meeting medical evaluation criteria will receive additional training on the proper use of 30min pressure demand air packs

2 H2S Detection and Alarm Systems:

- H2S sensor/detectors to be located on the drilling rig floor, in the base of the sub structure / cellar area, on the mud pits in the shale shaker area. Additional H2S detectors may be placed as deemed necessary
- An audio alarm system will be installed on the derrick floor and in the doghouse

3 Windssocks and / Wind Streamers:

- Windssocks at mud pit area should be high enough to be visible
- Windssock on the rig floor and / top of doghouse should be high enough to be visible

4 Condition Flags and Signs:

- Warning sign on access road to location
- Flags to be displayed on sign at entrance to location
 - Green Flag – Normal Safe Operation Condition
 - Yellow Flag – Potential Pressure and Danger
 - Red Flag – Danger (H2S present in dangerous concentrations) Only H2S trained personnel admitted on location

5 Well Control Equipment:

- See Drilling Operations Plan Schematics

6 Communication:

- While working under masks chalkboards will be used for communications
- Hand signals will be used where chalk board is inappropriate
- Two way radio will be used to communicate off location in case of emergency help is required. In most cases cellular telephones will be available at most drilling foreman's trailer or living quarters.



7 Drilling Stem Testing:

- No DST cores are planned at this time


8 Drilling contractor supervisor will be required to be familiar with the effects H₂S has on tubulars good and other mechanical equipment

9 If H₂S is encountered, mud system will be altered if necessary to maintain control of formation. A mud gas separator will be brought into service along with H₂S scavengers if necessary


11 Emergency Contacts

Emergency Contacts		
Carlsbad Police Department	575.887.7551	911
Carlsbad Medical Center	575.887.4100	911
Eddy County Fire Service	575.628.5450	911
Eddy County Sherriff	575.887.7551	911
Lea County Fire Service	575.391.2983	911
Lea County Sherriff	575.396.3611	911
Jal Police Department	575.395.2121	911
Jal Fire Department	575.395.2221	911
Tap Rock Resources	720.772.5090	

Rig Diagram
Upslope
Slot 1 Pad
Tap Rock Operating, LLC
10-25S-25E
Eddy County, NM

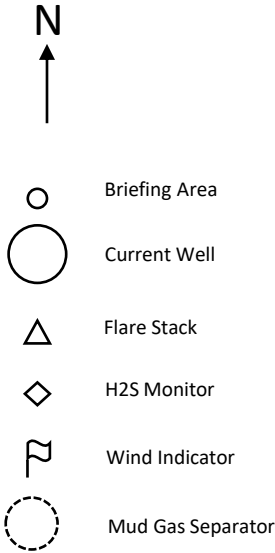

420'

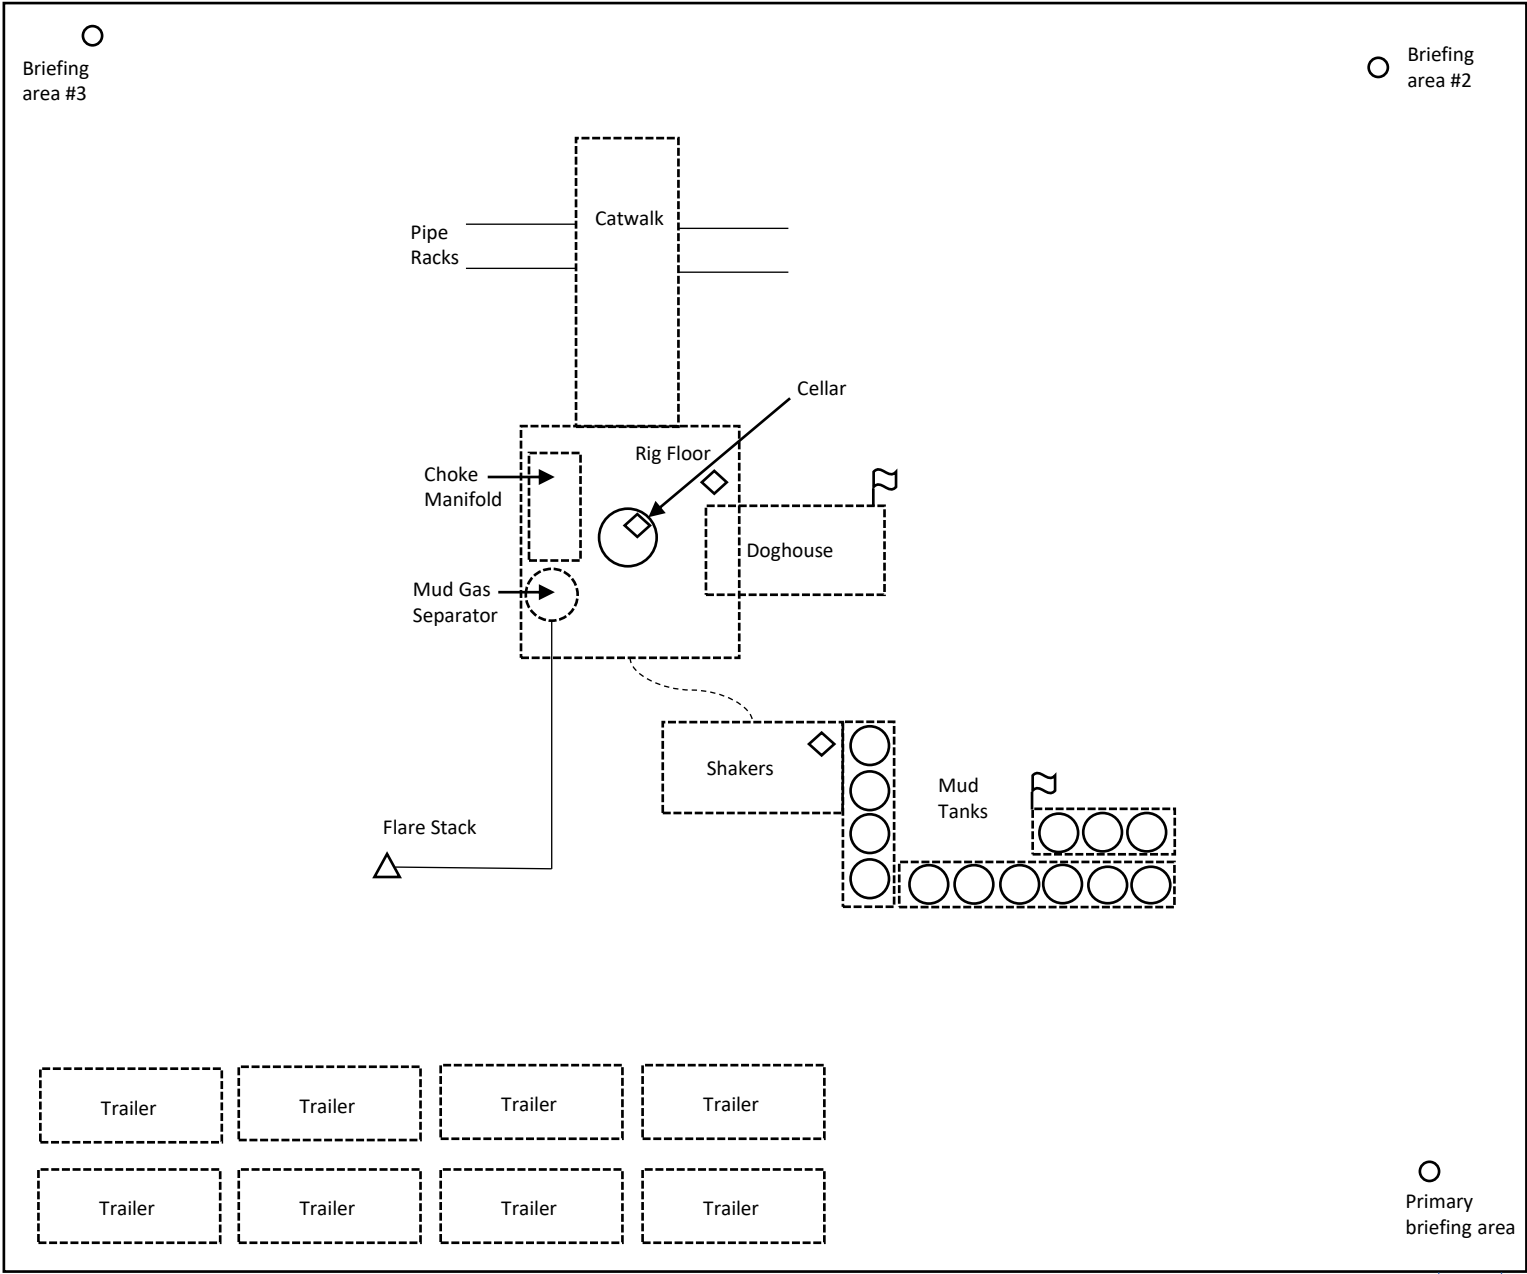


Condition
Warning
Sign



Access
Road



Avant Natural Resources Closed Loop Mud System Schematic

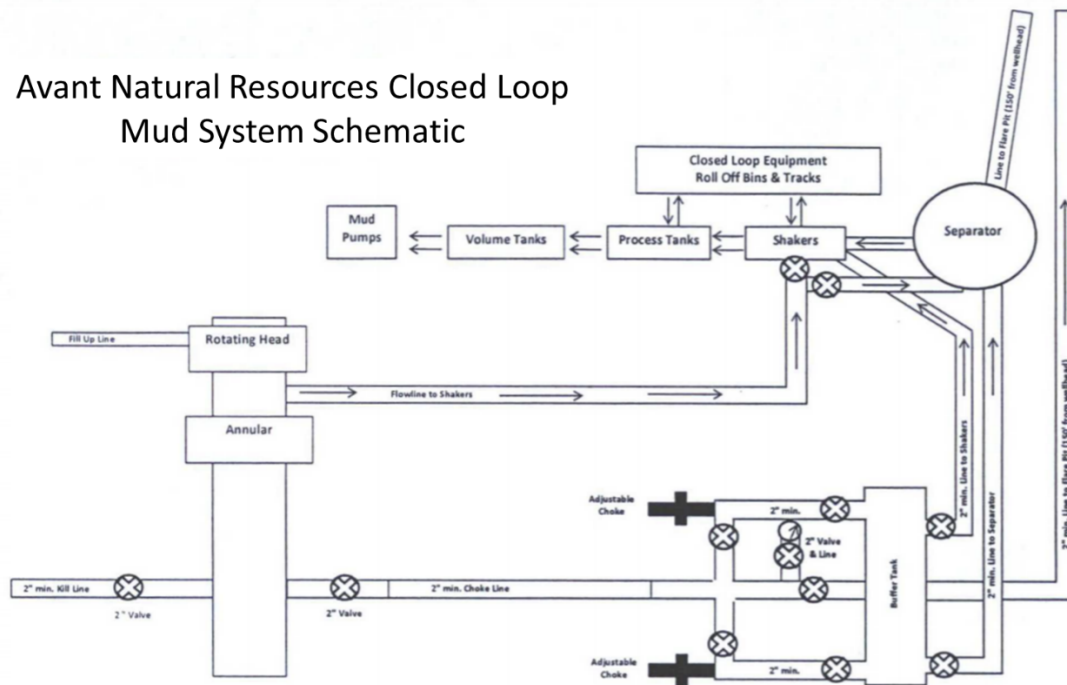

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/oed/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 430232

CONDITIONS

Operator: TAP ROCK OPERATING, LLC 523 Park Point Drive Golden, CO 80401	OGRID: 372043
	Action Number: 430232
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

CONDITIONS

Created By	Condition	Condition Date
bwood	Cement is required to circulate on both surface and intermediate1 strings of casing.	2/10/2025
bwood	If cement does not circulate on any string, a Cement Bond Log (CBL) is required for that string of casing.	2/10/2025
ward.rikala	Notify the OCD 24 hours prior to casing & cement.	2/15/2025
ward.rikala	File As Drilled C-102 and a directional Survey with C-104 completion packet.	2/15/2025
ward.rikala	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string.	2/15/2025
ward.rikala	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system.	2/15/2025
