

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/ocd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

Form C-101
August 1, 2011

Permit 406162

APPLICATION FOR PERMIT TO DRILL, RE-ENTER, DEEPEN, PLUGBACK, OR ADD A ZONE

1. Operator Name and Address Avant Operating II, LLC 1515 Wynkoop Street Denver, CO 80202		2. OGRID Number 332947
		3. API Number 30-025-55849
4. Property Code 337745	5. Property Name QUAIL 16 STATE COM	6. Well No. 205H

7. Surface Location

UL - Lot P	Section 16	Township 20S	Range 34E	Lot Idn	Feet From 264	N/S Line S	Feet From 904	E/W Line E	County Lea
---------------	---------------	-----------------	--------------	---------	------------------	---------------	------------------	---------------	---------------

8. Proposed Bottom Hole Location

UL - Lot A	Section 16	Township 20S	Range 34E	Lot Idn A	Feet From 100	N/S Line N	Feet From 1210	E/W Line E	County Lea
---------------	---------------	-----------------	--------------	--------------	------------------	---------------	-------------------	---------------	---------------

9. Pool Information

LEA;BONE SPRING, SOUTH	37580
------------------------	-------

Additional Well Information

11. Work Type New Well	12. Well Type OIL	13. Cable/Rotary	14. Lease Type State	15. Ground Level Elevation 3638
16. Multiple N	17. Proposed Depth 13911	18. Formation 1st Bone Spring Sand	19. Contractor	20. Spud Date 2/15/2026
Depth to Ground water		Distance from nearest fresh water well		Distance to nearest surface water

☒ We will be using a closed-loop system in lieu of lined pits

21. Proposed Casing and Cement Program

Type	Hole Size	Casing Size	Casing Weight/ft	Setting Depth	Sacks of Cement	Estimated TOC
Surf	14.75	10.75	40.5	1577	765	0
Int1	9.875	8.625	32	5319	825	0
Prod	7.875	5.5	20	13911	890	0

Casing/Cement Program: Additional Comments

--


22. Proposed Blowout Prevention Program

Type	Working Pressure	Test Pressure	Manufacturer
Pipe	10000	5000	CAMERON

23. I hereby certify that the information given above is true and complete to the best of my knowledge and belief. I hereby certify that no additives containing PFAS chemicals will be added to the completion or recompletion of this well. I further certify I have complied with 19.15.14.9 (A) NMAC ☒ and/or 19.15.14.9 (B) NMAC ☒ if applicable. Signature: Printed Name: Electronically filed by Sarah Ferreyros Title: Director of Regulatory Email Address: sarah@avantnr.com Date: 1/7/2026	OIL CONSERVATION DIVISION Approved By: Jeffrey Harrison Title: Petroleum Specialist III Approved Date: 1/26/2026 Expiration Date: 1/26/2028 Conditions of Approval Attached
--	--

C-102 Submit Electronically Via OCD Permitting		State of New Mexico Energy, Minerals & Natural Resources Department OIL CONSERVATION DIVISION				Revised July 9, 2024			
		Submittal Type:		☒ Initial Submittal ☐ Amended Report ☐ As Drilled					
WELL LOCATION INFORMATION									
API Number 30-025-55849		Pool Code 37580		Pool Name Lea; Bone Spring, South					
Property Code 337745		Property Name QUAIL 16 STATE COM				Well Number #205H			
OGRID No. 332947		Operator Name AVANT OPERATING II, LLC				Ground Level Elevation 3638'			
Surface Owner: ☒ State ☐ Fee ☐ Tribal ☐ Federal				Mineral Owner: ☒ State ☐ Fee ☐ Tribal ☐ Federal					
Surface Location									
UL P	Section 16	Township 20 S	Range 34 E	Lot	Ft. from N/S 264' FSL	Ft. from E/W 904' FEL	Latitude 32.566596°	Longitude -103.559594°	County LEA
Bottom Hole Location									
UL A	Section 16	Township 20 S	Range 34 E	Lot	Ft. from N/S 100' FNL	Ft. from E/W 1210' FEL	Latitude 32.580102°	Longitude -103.560590°	County LEA
Dedicated Acres 320.00		Infill or Defining Well Infill		Defining Well API n/a		Overlapping Spacing Unit (Y/N) No		Consolidation Code n/a	
Order Numbers. Pending				Well setbacks are under Common Ownership: ☐ Yes ☒ No					
Kick Off Point (KOP)									
UL P	Section 16	Township 20 S	Range 34 E	Lot	Ft. from N/S 264' FSL	Ft. from E/W 904' FEL	Latitude 32.566596°	Longitude -103.559594°	County LEA
First Take Point (FTP)									
UL P	Section 16	Township 20 S	Range 34 E	Lot	Ft. from N/S 100' FSL	Ft. from E/W 1210' FEL	Latitude 32.566151°	Longitude -103.560588°	County LEA
Last Take Point (LTP)									
UL A	Section 16	Township 20 S	Range 34 E	Lot	Ft. from N/S 100' FNL	Ft. from E/W 1210' FEL	Latitude 32.580102°	Longitude -103.560590°	County LEA
Unitized Area or Area of Uniform Interest Yes				Spacing Unit Type ☒ Horizontal ☐ Vertical			Ground Floor Elevation: 3638'		
OPERATOR CERTIFICATIONS <i>I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and, if the well is a vertical or directional well, that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of a working interest or unleased mineral interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.</i> <i>If this well is a horizontal well, I further certify that this organization has received the consent of at least one lessee or owner of a working interest or unleased mineral interest in each tract (in the target pool or formation) in which any part of the well's completed interval will be located or obtained a compulsory pooling order from the division.</i>  1/5/2026					SURVEYOR CERTIFICATIONS <i>I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.</i>  				
Signature Sarah Ferreyros					Signature and Seal of Professional Surveyor 23203 DECEMBER 18, 2025				
Printed Name sarah@avantnr.com					Certificate Number		Date of Survey		
Email Address									

Note: No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

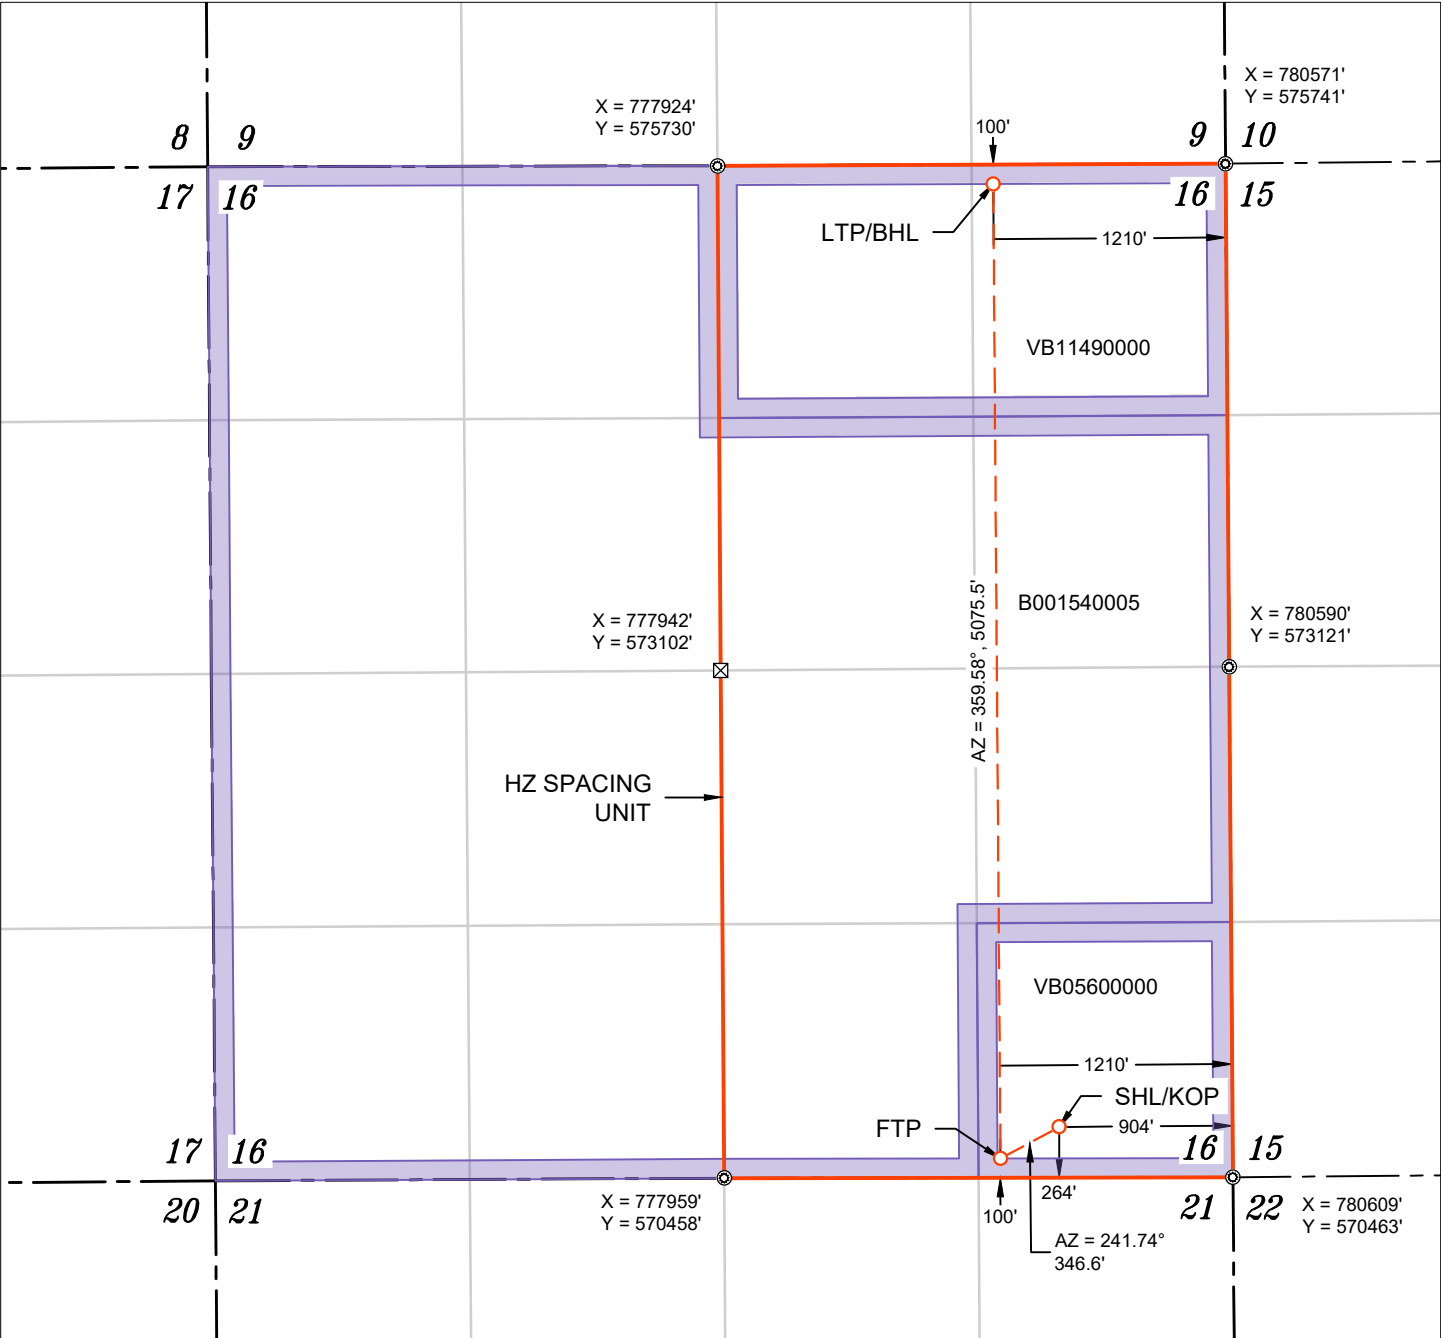

WELL NAME: QUAIL 16 STATE COM #205H
ELEVATION: 3638'

NAD 83 (SHL/KOP) 264' FSL & 904' FEL
LATITUDE = 32.566596°
LONGITUDE = -103.559594°
NAD 27 (SHL/KOP)
LATITUDE = 32.566476°
LONGITUDE = -103.559103°
STATE PLANE NAD 83 (N.M. EAST)
N: 570724.66' E: 779703.98'
STATE PLANE NAD 27 (N.M. EAST)
N: 570663.42' E: 738523.00'

NAD 83 (FTP) 100' FSL & 1210' FEL
LATITUDE = 32.566151°
LONGITUDE = -103.560588°
NAD 27 (FTP)
LATITUDE = 32.566031°
LONGITUDE = -103.560098°
STATE PLANE NAD 83 (N.M. EAST)
N: 570560.56' E: 779398.68'
STATE PLANE NAD 27 (N.M. EAST)
N: 570499.33' E: 738217.70'


NAD 83 (LTP/BHL) 100' FSL & 1210' FEL
LATITUDE = 32.580102°
LONGITUDE = -103.560590°
NAD 27 (LTP/BHL)
LATITUDE = 32.579982°
LONGITUDE = -103.560099°
STATE PLANE NAD 83 (N.M. EAST)
N: 575635.97' E: 779361.25'
STATE PLANE NAD 27 (N.M. EAST)
N: 575574.64' E: 738180.45'

APPROXIMATE WELL BORE DISTANCE FROM FTP TO LTP	
VB05600000	1226.01'
B001540005	2637.77'
VB11490000	1211.77'
TOTAL	5075.55'

NOTES

- ALL COORDINATES, BEARINGS, AND DISTANCES CONTAINED HEREIN ARE GRID, BASED UPON THE NEW MEXICO STATE PLANE COORDINATES SYSTEM, NORTH AMERICAN DATUM 83, NEW MEXICO EAST (3001).
- THIS DOCUMENT IS BASED UPON AN ON THE GROUND SURVEY PERFORMED DURING DECEMBER, 2025. CERTIFICATION OF THIS DOCUMENT IS ONLY TO THE LOCATION OF THIS INFORMATION IN RELATION TO RECORDED MONUMENT OF DEEDS PROVIDED BY THE CLIENT.
- ELEVATIONS MSL, DERIVED FROM G.N.S.S. OBSERVATION AND DERIVED FROM SAID ON-THE-GROUND SURVEY.

FOUND MONUMENT
 CALC. CORNER
 SHL/ KOP/ FTP / PPP/ LTP / BHL
 WELLBORE
 HORIZONTAL SPACING UNIT
 STATE OIL & GAS LEASE
 BLM OIL & GAS LEASE



Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/ocd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

Form APD Conditions

Permit 406162

PERMIT CONDITIONS OF APPROVAL

Operator Name and Address: Avant Operating II, LLC [332947] 1515 Wynkoop Street Denver, CO 80202	API Number: 30-025-55849
	Well: QUAIL 16 STATE COM #205H

OCD Reviewer	Condition
jeffrey.harrison	No additives containing PFAS chemicals will be added to the drilling fluids or completion fluids used during drilling, completions, or recompletions operations.
jeffrey.harrison	NSP required if not included in an existing order or not an infill to an appropriate defining well in the same pool and spacing unit.
jeffrey.harrison	The OCD is currently reviewing the areas containing the Capitan Reef Aquifer and may expand the designated 4-string casing area to encompass additional portions of it in the future.
jeffrey.harrison	This well is within the Capitan Reef aquifer zone. The first intermediate casing string shall be set and cemented back to surface immediately below the Capitan Reef.
jeffrey.harrison	In Capitan Reef areas if lost circulation (50% or greater) occurs below the base of the salt, the operator shall switch to freshwater mud until the intermediate casing is set..
jeffrey.harrison	This well is within the R-111-Q defined boundary. Operator must follow all procedures and requirements listed within the order.
jeffrey.harrison	Designs must align to one of the six options mandated within R-111-Q. No alterations or modifications are permitted to any of the casing design options mandated within order R-111-Q. If you have any questions, please contact Justin.Wrinkle@emnrd.nm.gov.
jeffrey.harrison	Cement is required to circulate on both surface and intermediate1 strings of casing.
jeffrey.harrison	If cement does not circulate on any string, a Cement Bond Log (CBL) is required for that string of casing.
jeffrey.harrison	File As Drilled C-102 and a directional Survey with C-104 completion packet.
jeffrey.harrison	Notify the OCD 24 hours prior to casing & cement.
jeffrey.harrison	A [C-103] Sub. Drilling (C-103N) is required within (10) days of spud.
jeffrey.harrison	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system.
jeffrey.harrison	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string.

WELL DETAILS: Quail 16 State Com #205H


Ground Elev: 3638.0 KB: 3663

+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
0.0	0.0	570724.66	779703.98	32.566596	-103.559594



PROJECT DETAILS: Lea County, NM (NAD 83)

Geodetic System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone: New Mexico Eastern Zone

System Datum: Mean Sea Level

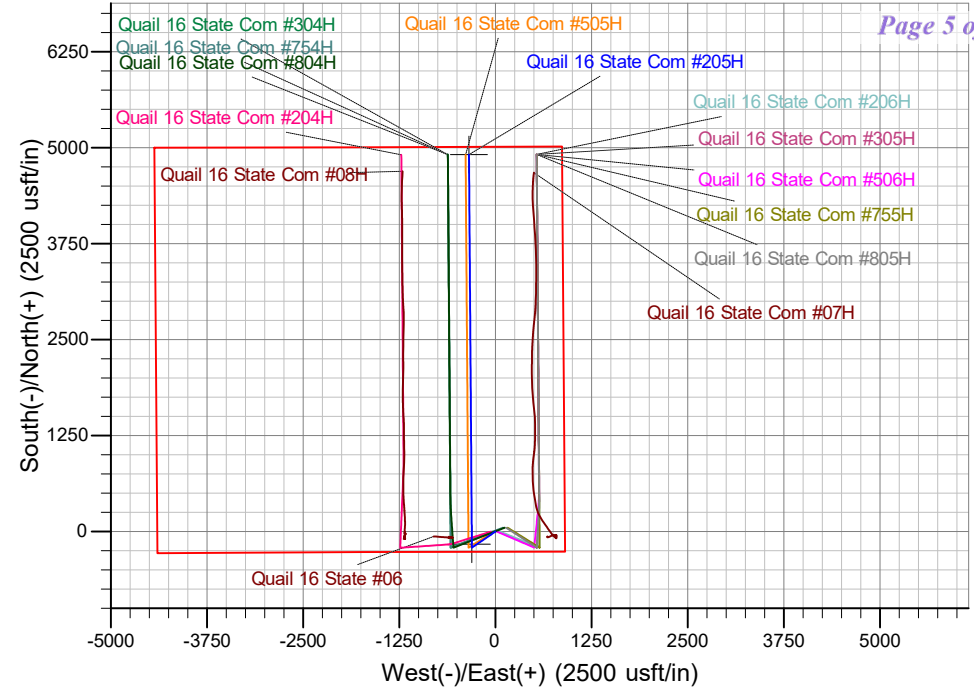**SECTION DETAILS**

Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	Vsect	Annotation
1	0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.0	
2	5000.0	0.00	0.00	5000.0	0.0	0.0	0.00	0.00	0.0	KOP - Start Build 2.00
3	5345.9	6.92	235.59	5345.1	-11.8	-17.2	2.00	235.59	-11.7	Start 2725.7 hold at 5345.9 MD
4	8071.6	6.92	235.59	8050.9	-197.3	-288.1	0.00	0.00	-195.2	Start Drop -2.00
5	8417.5	0.00	0.00	8396.0	-209.1	-305.3	2.00	180.00	-206.9	Start 100.5 hold at 8417.5 MD
6	8518.0	0.00	0.00	8496.5	-209.1	-305.3	0.00	0.00	-206.9	KOP #2 - Start DLS 12.00 TFO 359.58
7	9268.0	90.00	359.58	8974.0	268.3	-308.8	12.00	359.58	270.6	LP - Start 4643.1 hold at 9268.0 MD
8	13911.1	90.00	359.58	8974.0	4911.3	-342.7	0.00	0.00	4913.7	TD at 13911.1

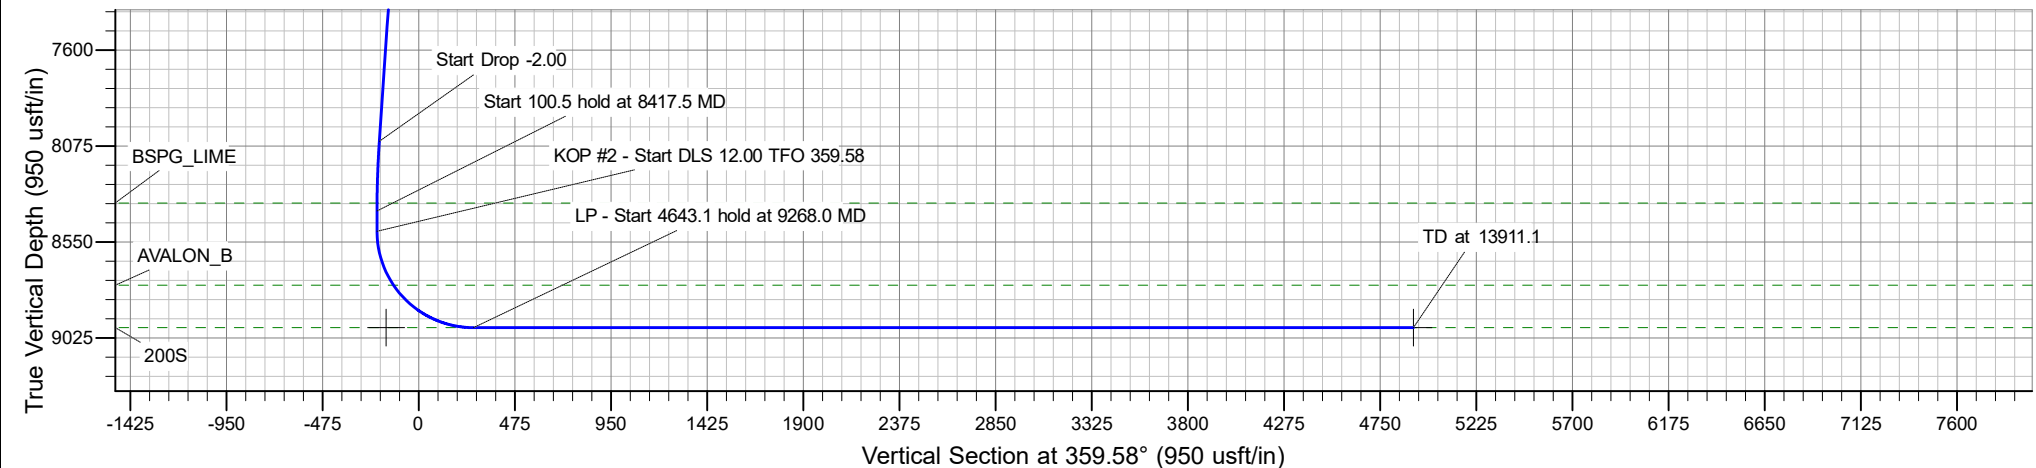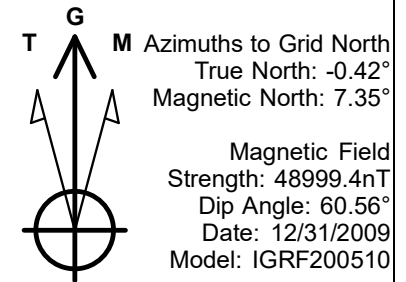

Avant Operating II, LLC

**Lea County, NM (NAD 83)
Quail 16 State Com Pad 2
Quail 16 State Com #205H**

OH

Plan: Plan 0.1

Standard Planning Report

22 December, 2025

Planning Report

Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Quail 16 State Com #205H
Company:	Avant Operating II, LLC	TVD Reference:	Well @ 3663.0usft (3663)
Project:	Lea County, NM (NAD 83)	MD Reference:	Well @ 3663.0usft (3663)
Site:	Quail 16 State Com Pad 2	North Reference:	Grid
Well:	Quail 16 State Com #205H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 0.1		

Project	Lea County, NM (NAD 83)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Quail 16 State Com Pad 2			
Site Position:		Northing:	575,486.84 usft	Latitude: 32.579687
From:	Lat/Long	Easting:	779,592.22 usft	Longitude: -103.559844
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "	

Well	Quail 16 State Com #205H			
Well Position	+N/-S	0.0 usft	Northing:	570,724.66 usft
	+E/-W	0.0 usft	Easting:	779,703.98 usft
Position Uncertainty	0.0 usft		Wellhead Elevation:	usft
Grid Convergence:	0.42 °		Ground Level:	3,638.0 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF200510	12/31/2009	7.77	60.56	48,999.36062279

Design	Plan 0.1			
Audit Notes:				
Version:	Phase:	PROTOTYPE	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0	0.0	0.0	359.58

Plan Survey Tool Program	Date	12/22/2025		
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks
1	0.0	13,911.1 Plan 0.1 (OH)	B001Mb_MWD+HRGM	
			OWSG MWD + HRGM	

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
5,000.0	0.00	0.00	5,000.0	0.0	0.0	0.00	0.00	0.00	0.00	
5,345.9	6.92	235.59	5,345.1	-11.8	-17.2	2.00	2.00	0.00	235.59	
8,071.6	6.92	235.59	8,050.9	-197.3	-288.1	0.00	0.00	0.00	0.00	
8,417.5	0.00	0.00	8,396.0	-209.1	-305.3	2.00	-2.00	0.00	180.00	
8,518.0	0.00	0.00	8,496.5	-209.1	-305.3	0.00	0.00	0.00	0.00	
9,268.0	90.00	359.58	8,974.0	268.3	-308.8	12.00	12.00	-0.06	359.58	
13,911.1	90.00	359.58	8,974.0	4,911.3	-342.7	0.00	0.00	0.00	0.00	Quail 16 State Com #

Planning Report

Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Quail 16 State Com #205H
Company:	Avant Operating II, LLC	TVD Reference:	Well @ 3663.0usft (3663)
Project:	Lea County, NM (NAD 83)	MD Reference:	Well @ 3663.0usft (3663)
Site:	Quail 16 State Com Pad 2	North Reference:	Grid
Well:	Quail 16 State Com #205H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 0.1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00
1,552.0	0.00	0.00	1,552.0	0.0	0.0	0.0	0.00	0.00	0.00
RUSTLER									
1,600.0	0.00	0.00	1,600.0	0.0	0.0	0.0	0.00	0.00	0.00
1,700.0	0.00	0.00	1,700.0	0.0	0.0	0.0	0.00	0.00	0.00
1,800.0	0.00	0.00	1,800.0	0.0	0.0	0.0	0.00	0.00	0.00
1,881.0	0.00	0.00	1,881.0	0.0	0.0	0.0	0.00	0.00	0.00
SOLADO									
1,900.0	0.00	0.00	1,900.0	0.0	0.0	0.0	0.00	0.00	0.00
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.0	0.00	0.00	0.00
2,100.0	0.00	0.00	2,100.0	0.0	0.0	0.0	0.00	0.00	0.00
2,200.0	0.00	0.00	2,200.0	0.0	0.0	0.0	0.00	0.00	0.00
2,300.0	0.00	0.00	2,300.0	0.0	0.0	0.0	0.00	0.00	0.00
2,400.0	0.00	0.00	2,400.0	0.0	0.0	0.0	0.00	0.00	0.00
2,500.0	0.00	0.00	2,500.0	0.0	0.0	0.0	0.00	0.00	0.00
2,600.0	0.00	0.00	2,600.0	0.0	0.0	0.0	0.00	0.00	0.00
2,700.0	0.00	0.00	2,700.0	0.0	0.0	0.0	0.00	0.00	0.00
2,800.0	0.00	0.00	2,800.0	0.0	0.0	0.0	0.00	0.00	0.00
2,900.0	0.00	0.00	2,900.0	0.0	0.0	0.0	0.00	0.00	0.00
3,000.0	0.00	0.00	3,000.0	0.0	0.0	0.0	0.00	0.00	0.00
3,100.0	0.00	0.00	3,100.0	0.0	0.0	0.0	0.00	0.00	0.00
3,200.0	0.00	0.00	3,200.0	0.0	0.0	0.0	0.00	0.00	0.00
3,300.0	0.00	0.00	3,300.0	0.0	0.0	0.0	0.00	0.00	0.00
3,308.0	0.00	0.00	3,308.0	0.0	0.0	0.0	0.00	0.00	0.00
BASE_OF_SALT									
3,400.0	0.00	0.00	3,400.0	0.0	0.0	0.0	0.00	0.00	0.00
3,410.0	0.00	0.00	3,410.0	0.0	0.0	0.0	0.00	0.00	0.00
YATES									
3,500.0	0.00	0.00	3,500.0	0.0	0.0	0.0	0.00	0.00	0.00
3,600.0	0.00	0.00	3,600.0	0.0	0.0	0.0	0.00	0.00	0.00
3,700.0	0.00	0.00	3,700.0	0.0	0.0	0.0	0.00	0.00	0.00
3,800.0	0.00	0.00	3,800.0	0.0	0.0	0.0	0.00	0.00	0.00
3,844.0	0.00	0.00	3,844.0	0.0	0.0	0.0	0.00	0.00	0.00
SVRV									
3,900.0	0.00	0.00	3,900.0	0.0	0.0	0.0	0.00	0.00	0.00
4,000.0	0.00	0.00	4,000.0	0.0	0.0	0.0	0.00	0.00	0.00
4,012.0	0.00	0.00	4,012.0	0.0	0.0	0.0	0.00	0.00	0.00
CAPITAN_REEF									

Planning Report

Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Quail 16 State Com #205H
Company:	Avant Operating II, LLC	TVD Reference:	Well @ 3663.0usft (3663)
Project:	Lea County, NM (NAD 83)	MD Reference:	Well @ 3663.0usft (3663)
Site:	Quail 16 State Com Pad 2	North Reference:	Grid
Well:	Quail 16 State Com #205H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 0.1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
4,100.0	0.00	0.00	4,100.0	0.0	0.0	0.0	0.00	0.00	0.00
4,200.0	0.00	0.00	4,200.0	0.0	0.0	0.0	0.00	0.00	0.00
4,300.0	0.00	0.00	4,300.0	0.0	0.0	0.0	0.00	0.00	0.00
4,400.0	0.00	0.00	4,400.0	0.0	0.0	0.0	0.00	0.00	0.00
4,500.0	0.00	0.00	4,500.0	0.0	0.0	0.0	0.00	0.00	0.00
4,600.0	0.00	0.00	4,600.0	0.0	0.0	0.0	0.00	0.00	0.00
4,700.0	0.00	0.00	4,700.0	0.0	0.0	0.0	0.00	0.00	0.00
4,800.0	0.00	0.00	4,800.0	0.0	0.0	0.0	0.00	0.00	0.00
4,900.0	0.00	0.00	4,900.0	0.0	0.0	0.0	0.00	0.00	0.00
5,000.0	0.00	0.00	5,000.0	0.0	0.0	0.0	0.00	0.00	0.00
KOP - Start Build 2.00									
5,100.0	2.00	235.59	5,100.0	-1.0	-1.4	-1.0	2.00	2.00	0.00
5,200.0	4.00	235.59	5,199.8	-3.9	-5.8	-3.9	2.00	2.00	0.00
5,269.4	5.39	235.59	5,269.0	-7.2	-10.4	-7.1	2.00	2.00	0.00
CPTN_REEF_BASE									
5,300.0	6.00	235.59	5,299.5	-8.9	-12.9	-8.8	2.00	2.00	0.00
5,345.9	6.92	235.59	5,345.1	-11.8	-17.2	-11.7	2.00	2.00	0.00
Start 2725.7 hold at 5345.9 MD									
5,400.0	6.92	235.59	5,398.8	-15.5	-22.6	-15.3	0.00	0.00	0.00
5,500.0	6.92	235.59	5,498.0	-22.3	-32.5	-22.0	0.00	0.00	0.00
5,561.4	6.92	235.59	5,559.0	-26.5	-38.6	-26.2	0.00	0.00	0.00
CHERRY_CNYN									
5,600.0	6.92	235.59	5,597.3	-29.1	-42.5	-28.8	0.00	0.00	0.00
5,700.0	6.92	235.59	5,696.6	-35.9	-52.4	-35.5	0.00	0.00	0.00
5,800.0	6.92	235.59	5,795.9	-42.7	-62.3	-42.2	0.00	0.00	0.00
5,900.0	6.92	235.59	5,895.1	-49.5	-72.3	-49.0	0.00	0.00	0.00
6,000.0	6.92	235.59	5,994.4	-56.3	-82.2	-55.7	0.00	0.00	0.00
6,100.0	6.92	235.59	6,093.7	-63.1	-92.2	-62.4	0.00	0.00	0.00
6,200.0	6.92	235.59	6,192.9	-69.9	-102.1	-69.2	0.00	0.00	0.00
6,300.0	6.92	235.59	6,292.2	-76.7	-112.0	-75.9	0.00	0.00	0.00
6,400.0	6.92	235.59	6,391.5	-83.5	-122.0	-82.6	0.00	0.00	0.00
6,500.0	6.92	235.59	6,490.8	-90.3	-131.9	-89.4	0.00	0.00	0.00
6,600.0	6.92	235.59	6,590.0	-97.1	-141.8	-96.1	0.00	0.00	0.00
6,630.2	6.92	235.59	6,620.0	-99.2	-144.8	-98.1	0.00	0.00	0.00
BRUSHY_CANYON									
6,700.0	6.92	235.59	6,689.3	-104.0	-151.8	-102.8	0.00	0.00	0.00
6,800.0	6.92	235.59	6,788.6	-110.8	-161.7	-109.6	0.00	0.00	0.00
6,900.0	6.92	235.59	6,887.8	-117.6	-171.7	-116.3	0.00	0.00	0.00
7,000.0	6.92	235.59	6,987.1	-124.4	-181.6	-123.0	0.00	0.00	0.00
7,100.0	6.92	235.59	7,086.4	-131.2	-191.5	-129.8	0.00	0.00	0.00
7,200.0	6.92	235.59	7,185.7	-138.0	-201.5	-136.5	0.00	0.00	0.00
7,300.0	6.92	235.59	7,284.9	-144.8	-211.4	-143.2	0.00	0.00	0.00
7,400.0	6.92	235.59	7,384.2	-151.6	-221.3	-150.0	0.00	0.00	0.00
7,500.0	6.92	235.59	7,483.5	-158.4	-231.3	-156.7	0.00	0.00	0.00
7,600.0	6.92	235.59	7,582.7	-165.2	-241.2	-163.4	0.00	0.00	0.00
7,700.0	6.92	235.59	7,682.0	-172.0	-251.2	-170.2	0.00	0.00	0.00
7,800.0	6.92	235.59	7,781.3	-178.8	-261.1	-176.9	0.00	0.00	0.00
7,900.0	6.92	235.59	7,880.6	-185.6	-271.0	-183.6	0.00	0.00	0.00
8,000.0	6.92	235.59	7,979.8	-192.4	-281.0	-190.4	0.00	0.00	0.00
8,071.6	6.92	235.59	8,050.9	-197.3	-288.1	-195.2	0.00	0.00	0.00
Start Drop -2.00									
8,100.0	6.35	235.59	8,079.1	-199.2	-290.8	-197.0	2.00	-2.00	0.00
8,200.0	4.35	235.59	8,178.7	-204.4	-298.5	-202.2	2.00	-2.00	0.00

Planning Report

Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Quail 16 State Com #205H
Company:	Avant Operating II, LLC	TVD Reference:	Well @ 3663.0usft (3663)
Project:	Lea County, NM (NAD 83)	MD Reference:	Well @ 3663.0usft (3663)
Site:	Quail 16 State Com Pad 2	North Reference:	Grid
Well:	Quail 16 State Com #205H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 0.1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
8,300.0	2.35	235.59	8,278.5	-207.7	-303.3	-205.5	2.00	-2.00	0.00
8,378.5	0.78	235.59	8,357.0	-208.9	-305.1	-206.7	2.00	-2.00	0.00
BSPG_LIME									
8,400.0	0.35	235.59	8,378.5	-209.1	-305.3	-206.8	2.00	-2.00	0.00
8,417.5	0.00	0.00	8,396.0	-209.1	-305.3	-206.9	2.00	-2.00	0.00
Start 100.5 hold at 8417.5 MD									
8,500.0	0.00	0.00	8,478.5	-209.1	-305.3	-206.9	0.00	0.00	0.00
8,518.0	0.00	0.00	8,496.5	-209.1	-305.3	-206.9	0.00	0.00	0.00
KOP #2 - Start DLS 12.00 TFO 359.58									
8,600.0	9.84	359.58	8,578.1	-202.1	-305.4	-199.8	12.00	12.00	0.00
8,700.0	21.84	359.58	8,674.1	-174.8	-305.6	-172.6	12.00	12.00	0.00
8,800.0	33.84	359.58	8,762.4	-128.2	-305.9	-126.0	12.00	12.00	0.00
8,802.0	34.07	359.58	8,764.0	-127.1	-305.9	-124.9	12.00	12.00	0.00
AVALON_B									
8,900.0	45.84	359.58	8,839.0	-64.3	-306.4	-62.0	12.00	12.00	0.00
8,904.9	46.43	359.58	8,842.4	-60.7	-306.4	-58.5	12.00	12.00	0.00
Quail 16 State Com #205H FTP									
9,000.0	57.84	359.58	8,900.7	14.2	-306.9	16.4	12.00	12.00	0.00
9,100.0	69.84	359.58	8,944.7	103.8	-307.6	106.0	12.00	12.00	0.00
9,200.0	81.84	359.58	8,969.1	200.6	-308.3	202.8	12.00	12.00	0.00
9,268.0	90.00	359.58	8,974.0	268.3	-308.8	270.6	12.00	12.00	0.00
LP - Start 4643.1 hold at 9268.0 MD									
9,300.0	90.00	359.58	8,974.0	300.3	-309.0	302.6	0.00	0.00	0.00
9,400.0	90.00	359.58	8,974.0	400.3	-309.8	402.6	0.00	0.00	0.00
9,500.0	90.00	359.58	8,974.0	500.3	-310.5	502.6	0.00	0.00	0.00
9,600.0	90.00	359.58	8,974.0	600.3	-311.2	602.6	0.00	0.00	0.00
9,700.0	90.00	359.58	8,974.0	700.3	-311.9	702.6	0.00	0.00	0.00
9,800.0	90.00	359.58	8,974.0	800.3	-312.7	802.6	0.00	0.00	0.00
9,900.0	90.00	359.58	8,974.0	900.3	-313.4	902.6	0.00	0.00	0.00
10,000.0	90.00	359.58	8,974.0	1,000.3	-314.1	1,002.6	0.00	0.00	0.00
10,100.0	90.00	359.58	8,974.0	1,100.3	-314.9	1,102.6	0.00	0.00	0.00
10,200.0	90.00	359.58	8,974.0	1,200.3	-315.6	1,202.6	0.00	0.00	0.00
10,300.0	90.00	359.58	8,974.0	1,300.3	-316.3	1,302.6	0.00	0.00	0.00
10,400.0	90.00	359.58	8,974.0	1,400.3	-317.1	1,402.6	0.00	0.00	0.00
10,500.0	90.00	359.58	8,974.0	1,500.3	-317.8	1,502.6	0.00	0.00	0.00
10,600.0	90.00	359.58	8,974.0	1,600.3	-318.5	1,602.6	0.00	0.00	0.00
10,700.0	90.00	359.58	8,974.0	1,700.3	-319.3	1,702.6	0.00	0.00	0.00
10,800.0	90.00	359.58	8,974.0	1,800.3	-320.0	1,802.6	0.00	0.00	0.00
10,900.0	90.00	359.58	8,974.0	1,900.3	-320.7	1,902.6	0.00	0.00	0.00
11,000.0	90.00	359.58	8,974.0	2,000.3	-321.5	2,002.6	0.00	0.00	0.00
11,100.0	90.00	359.58	8,974.0	2,100.3	-322.2	2,102.6	0.00	0.00	0.00
11,200.0	90.00	359.58	8,974.0	2,200.3	-322.9	2,202.6	0.00	0.00	0.00
11,300.0	90.00	359.58	8,974.0	2,300.3	-323.6	2,302.6	0.00	0.00	0.00
11,400.0	90.00	359.58	8,974.0	2,400.3	-324.4	2,402.6	0.00	0.00	0.00
11,500.0	90.00	359.58	8,974.0	2,500.3	-325.1	2,502.6	0.00	0.00	0.00
11,600.0	90.00	359.58	8,974.0	2,600.3	-325.8	2,602.6	0.00	0.00	0.00
11,700.0	90.00	359.58	8,974.0	2,700.3	-326.6	2,702.6	0.00	0.00	0.00
11,800.0	90.00	359.58	8,974.0	2,800.3	-327.3	2,802.6	0.00	0.00	0.00
11,900.0	90.00	359.58	8,974.0	2,900.3	-328.0	2,902.6	0.00	0.00	0.00
12,000.0	90.00	359.58	8,974.0	3,000.3	-328.8	3,002.6	0.00	0.00	0.00
12,100.0	90.00	359.58	8,974.0	3,100.2	-329.5	3,102.6	0.00	0.00	0.00
12,200.0	90.00	359.58	8,974.0	3,200.2	-330.2	3,202.6	0.00	0.00	0.00
12,300.0	90.00	359.58	8,974.0	3,300.2	-331.0	3,302.6	0.00	0.00	0.00

Planning Report

Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Quail 16 State Com #205H
Company:	Avant Operating II, LLC	TVD Reference:	Well @ 3663.0usft (3663)
Project:	Lea County, NM (NAD 83)	MD Reference:	Well @ 3663.0usft (3663)
Site:	Quail 16 State Com Pad 2	North Reference:	Grid
Well:	Quail 16 State Com #205H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 0.1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
12,400.0	90.00	359.58	8,974.0	3,400.2	-331.7	3,402.6	0.00	0.00	0.00	
12,500.0	90.00	359.58	8,974.0	3,500.2	-332.4	3,502.6	0.00	0.00	0.00	
12,600.0	90.00	359.58	8,974.0	3,600.2	-333.1	3,602.6	0.00	0.00	0.00	
12,700.0	90.00	359.58	8,974.0	3,700.2	-333.9	3,702.6	0.00	0.00	0.00	
12,800.0	90.00	359.58	8,974.0	3,800.2	-334.6	3,802.6	0.00	0.00	0.00	
12,900.0	90.00	359.58	8,974.0	3,900.2	-335.3	3,902.6	0.00	0.00	0.00	
13,000.0	90.00	359.58	8,974.0	4,000.2	-336.1	4,002.6	0.00	0.00	0.00	
13,100.0	90.00	359.58	8,974.0	4,100.2	-336.8	4,102.6	0.00	0.00	0.00	
13,200.0	90.00	359.58	8,974.0	4,200.2	-337.5	4,202.6	0.00	0.00	0.00	
13,300.0	90.00	359.58	8,974.0	4,300.2	-338.3	4,302.6	0.00	0.00	0.00	
13,400.0	90.00	359.58	8,974.0	4,400.2	-339.0	4,402.6	0.00	0.00	0.00	
13,500.0	90.00	359.58	8,974.0	4,500.2	-339.7	4,502.6	0.00	0.00	0.00	
13,600.0	90.00	359.58	8,974.0	4,600.2	-340.5	4,602.6	0.00	0.00	0.00	
13,700.0	90.00	359.58	8,974.0	4,700.2	-341.2	4,702.6	0.00	0.00	0.00	
13,800.0	90.00	359.58	8,974.0	4,800.2	-341.9	4,802.6	0.00	0.00	0.00	
13,900.0	90.00	359.58	8,974.0	4,900.2	-342.6	4,902.6	0.00	0.00	0.00	
13,911.1	90.00	359.58	8,974.0	4,911.3	-342.7	4,913.7	0.00	0.00	0.00	
TD at 13911.1 - 200S - Quail 16 State Com #205H LTP/BHL										

Design Targets									
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
- hit/miss target									
- Shape									
Quail 16 State Com #20:	0.00	0.00	8,974.0	4,911.3	-342.7	575,635.97	779,361.25	32.580102	-103.560591
- plan hits target center									
- Point									
Quail 16 State Com #20:	0.00	0.00	8,974.0	-164.1	-305.3	570,560.56	779,398.68	32.566151	-103.560589
- plan misses target center by 167.3usft at 8904.9usft MD (8842.4 TVD, -60.7 N, -306.4 E)									
- Point									

Formations						
Measured Depth (usft)	Vertical Depth (usft)	Name	Lithology	Dip (°)	Dip Direction (°)	
1,552.0	1,552.0	RUSTLER				
1,881.0	1,881.0	SOLADO				
3,308.0	3,308.0	BASE_OF_SALT				
3,410.0	3,410.0	YATES				
3,844.0	3,844.0	SVRV				
4,012.0	4,012.0	CAPTAN_REEF				
5,269.4	5,269.0	CPTN_REEF_BASE				
5,561.4	5,559.0	CHERRY_CNYN				
6,630.2	6,620.0	BRUSHY_CANYON				
8,378.5	8,357.0	BSPG_LIME				
8,802.0	8,764.0	AVALON_B				
13,911.1	8,974.0	200S				

Planning Report

Database:	EDM 5000.16 Single User Db	Local Co-ordinate Reference:	Well Quail 16 State Com #205H
Company:	Avant Operating II, LLC	TVD Reference:	Well @ 3663.0usft (3663)
Project:	Lea County, NM (NAD 83)	MD Reference:	Well @ 3663.0usft (3663)
Site:	Quail 16 State Com Pad 2	North Reference:	Grid
Well:	Quail 16 State Com #205H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan 0.1		

Plan Annotations					
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment	
		+N/-S (usft)	+E/-W (usft)		
5,000.0	5,000.0	0.0	0.0	KOP - Start Build 2.00	
5,345.9	5,345.1	-11.8	-17.2	Start 2725.7 hold at 5345.9 MD	
8,071.6	8,050.9	-197.3	-288.1	Start Drop -2.00	
8,417.5	8,396.0	-209.1	-305.3	Start 100.5 hold at 8417.5 MD	
8,518.0	8,496.5	-209.1	-305.3	KOP #2 - Start DLS 12.00 TFO 359.58	
9,268.0	8,974.0	268.3	-308.8	LP - Start 4643.1 hold at 9268.0 MD	
13,911.1	8,974.0	4,911.3	-342.7	TD at 13911.1	

AFE: NM1361



Quail 16 State Com #205H

API:

REGULATORY: NM State

PERMIT #

RIG:

KB: 3664.5 (26.5')

GL: 3638'

Avalon

Lea County, NM

Sec. 16, T-20S, R-34E; 264 FSL, 904 FEL

SHL:

Lat: 32.566596, Long: -103.559594 (NAD83)

HOLE SIZE	MD	FORMATION	TVD	MUD	CASING	CEMENT	SPECIAL INSTRUCTIONS
	120	20" Conductor	120				
14 3/4 "				SPUD MW 8.4 ppg	10 3/4 " 40.5# J-55 BTC	LEAD: 12.8 PPG Top of Lead: 0 50% Excess	Circ cement to surface is a NMOCD requirement
	1,552	Rustler	1,552	Fresh	+/- 13 Bowsprings 1 20' pup jt	TAIL: 14.8 PPG Top of Tail: 1262' 20% Excess	Casing must be set 25' into the Rustler
	1,577	SURF CSG PT	1,577	9.9 ppg	1 joint shoe track		MUD: Fresh water only
9 7/8 "	1,881	Solado	1,881	DRLOUT MW 10 ppg	8 5/8 " 32# L-80 HC BK	2 STAGE CEMENT	Circ cement to surface is a NMOCD requirement
	3,410	Yates	3,410			1st STAGE LEAD: 12.5 PPG Top of Lead: 0' 20% excess TAIL: 14.5 PPG Top of Tail: 4255' 20% Excess	
	3,800	DV TOOL & PACKER	3,800	Brine	1 20' pup jt		
	4,012	Capitan Reef	4,012			2nd STAGE LEAD: 12.5 PPG Top of Lead: 0' 20% Excess TAIL: 14.2 PPG Top of Tail: 3200' no excess	
	5,269	Base of Capitan	5,269	TD MW 10 ppg	+/- 9 Bowsprings 1 joint shoe track		
	5,319	INTRM CSG PT	5,319				
7 7/8 " VERTICAL	5,561	Cherry Canyon	5,559	DRLOUT MW 9			R-111-Q FIGURE B Set production cement >500' short of Int1 shoe and perform post-frac bullhead cement job.
	6,630	Brushy Canyon	6,620	Cut Brine			
	8,379	Bone Spring	8,357	KOP MW 9.2			
7 7/8 " CURVE	8,518	KOP	8,497	EOC MW 9.2	Lat MW 9.2	TD MW 9.2	
	8,802	Avalon	8,764	OBM	OBM		
	9,268	EOC	8,974				
7 7/8 " LATERAL							13,911 ' MD
							4,914 ' VS
							8,974 ' TVD
DIRECTIONAL PLAN				Lat. Azi = VS Azi. = 359.58° Est BHST = 155°F, Est BHCT = 138°F			
	MD	INC	INC	TVD	ANNOTATION		BHL: 100 FNL, 1210 FEL
							Expected BH Pressure: 4128
							POST FRAC:
							SQUEEZE CEMENT TO TIE IN 5.5" STRING. FINAL TOP OF CEMENT 500' ABOVE PREVIOUS SHOE WITH ≈47BBLs

DIRECTIONS TO LOCATION:

Drilling Engineer: Ryan Harris

Quail 16 State Com #205H ()

Date: 12/23/2025

State of New Mexico
Energy, Minerals and Natural Resources Department

Submit Electronically
Via E-permitting

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description

Effective May 25, 2021

I. Operator: Avant Operating II, LLC **OGRID:** 332947 **Date:** 09/29/2025

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
Quail 16 State Com 204H		P-16-T20S-R34E	263FSL/964FEL	1200 BBL/D	3600 MCF/D	6000 BBL/D
Quail 16 State Com 205H		P-16-T20S-R34E	264FSL/904FEL	1200 BBL/D	3600 MCF/D	6000 BBL/D
Quail 16 State Com 206H		P-16-T20S-R34E	264FSL/844FEL	1200 BBL/D	3600 MCF/D	6000 BBL/D
Quail 16 State Com 303H		P-16-T20S-R34E	263FSL/1004FEL	950 BBL/D	2000 MCF/D	6650 BBL/D
Quail 16 State Com 304H		P-16-T20S-R34E	263FSL/944FEL	950 BBL/D	2000 MCF/D	6650 BBL/D
Quail 16 State Com 305H		P-16-T20S-R34E	264FSL/864FEL	950 BBL/D	2000 MCF/D	6650 BBL/D
Quail 16 State Com 504H		P-16-T20S-R34E	263FSL/984FEL	1400 BBL/D	2400 MCF/D	7500 BBL/D
Quail 16 State Com 505H		P-16-T20S-R34E	264FSL/924FEL	1400 BBL/D	2400 MCF/D	7500 BBL/D
Quail 16 State Com 506H		P-16-T20S-R34E	264FSL/884FEL	1400 BBL/D	2400 MCF/D	7500 BBL/D
Quail 16 State Com 754H		P-16-T20S-R34E	314FSL/803FEL	1250 BBL/D	2600 MCF/D	7500 BBL/D
Quail 16 State Com 755H		P-16-T20S-R34E	314FSL/743FEL	1250 BBL/D	2600 MCF/D	7500 BBL/D
Quail 16 State Com 804H		P-16-T20S-R34E	314FSL/783FEL	1200 BBL/D	2500 MCF/D	6000 BBL/D
Quail 16 State Com 805H		P-16-T20S-R34E	314FSL/763FEL	1200 BBL/D	2500 MCF/D	6000 BBL/D

IV. Central Delivery Point Name: Quail 16 State CTB [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Quail 16 State Com 204H		02/15/2026	03/30/2026	05/01/2026	07/01/2026	07/01/2026
Quail 16 State Com 205H		02/15/2026	03/30/2026	05/01/2026	07/01/2026	07/01/2026
Quail 16 State Com 206H		02/15/2026	03/30/2026	05/01/2026	07/01/2026	07/01/2026
Quail 16 State Com 303H		02/15/2026	03/30/2026	05/01/2026	07/01/2026	07/01/2026
Quail 16 State Com 304H		02/15/2026	03/30/2026	05/01/2026	07/01/2026	07/01/2026
Quail 16 State Com 305H		02/15/2026	03/30/2026	05/01/2026	07/01/2026	07/01/2026
Quail 16 State Com 504H		02/15/2026	03/30/2026	05/01/2026	07/01/2026	07/01/2026
Quail 16 State Com 505H		02/15/2026	03/30/2026	05/01/2026	07/01/2026	07/01/2026
Quail 16 State Com 506H		02/15/2026	03/30/2026	05/01/2026	07/01/2026	07/01/2026
Quail 16 State Com 754H		02/15/2026	03/30/2026	05/01/2026	07/01/2026	07/01/2026
Quail 16 State Com 755H		02/15/2026	03/30/2026	05/01/2026	07/01/2026	07/01/2026
Quail 16 State Com 804H		02/15/2026	03/30/2026	05/01/2026	07/01/2026	07/01/2026
Quail 16 State Com 805H		02/15/2026	03/30/2026	05/01/2026	07/01/2026	07/01/2026

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 2 – Enhanced Plan **EFFECTIVE APRIL 1, 2022**

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature:



Printed Name: John Harper

Title: SVP – Assets and Exploration

E-mail Address: John@avantnr.com

Date: 08/15/25

Phone: 678-988-6644

OIL CONSERVATION DIVISION
(Only applicable when submitted as a standalone form)

Approved By:

Title:

Approval Date:

Conditions of Approval:

Avant Operating II, LLC Natural Gas Management Plan

VI. Separation equipment will be sized by construction engineering staff based on stated manufacturer daily throughput capacities and anticipated daily production rates to ensure adequate capacity. Closed vent system piping, compression needs, and VRUs will be sized utilizing ProMax modelling software to ensure adequate capacity for anticipated production volumes and conditions.

VII. Avant Operating, LLC (Avant) will take the following actions to comply with the regulations listed in 19.15.27.8:

- A. Avant will maximize the recovery of natural gas by minimizing the waste, as defined by 19.15.2 NMAC, of natural gas through venting and flaring. Avant will ensure that well(s) will be connected to a natural gas gathering system with sufficient capacity to transport natural gas.
- B. All drilling operations will be equipped with a rig flare located at least 100' from the nearest surface hole. Rig flare will be utilized to combust any natural gas that is brought to surface during normal drilling operations. In the case of emergency venting or flaring the volumes will be estimated and reported appropriately.
- C. During completion operations any natural gas brought to surface will be flared. Immediately following the finish of completion operations, all well flowback will be directed to permanent separation equipment. Produced natural gas from separation equipment will be sent to sales. Avant will ensure that the flare is sized properly and is equipped with automatic igniter or continuous pilot. The gas sample will be analyzed twice per week, and the gas will be routed into a gathering system as soon as pipeline specifications are met.
- D. Avant will comply with the performance standards requirements and provisions listed in 19.15.27.8 (1) through (8). All equipment will be designed and sized to handle maximum anticipated pressures and throughputs to minimize the waste. Production storage tanks constructed after May 25, 2021, will be equipped with automatic gauging system. Flares constructed after May 25, 2021, will be equipped with automatic igniter or continuous pilot. Flares will be located at least 100' from the well and storage tanks unless otherwise approved by the division. Avant will conduct AVO inspections as described in 19.15.27.8 E (5) (a) with frequencies specified in 19.15.27.8 E (5) (b) and (c). All emergencies will be resolved as quickly and safely as feasible to minimize waste.
- E. The volume of natural gas that is vented or flared as the result of malfunction or emergency during drilling and completions operations will be estimated. The volume of natural gas that is vented, flared, or beneficially used during production operations, will be measured, or estimated. Avant will install equipment to measure
- F. Measurement meters will be in place for low- and high-pressure gas that is flared due to not being able to use for reuse or sales. Equipment will be installed off tanks to reduce vented gas and the gas will be measured with a meter.

VIII. Best Management Practices: Avant plans to communicate consistently with midstream partners to ensure sufficient takeaway capacity is available and understand planned maintenance to minimize venting. Avant will depressurize equipment and capture vented gases for reuse before any maintenance occurs. Avant will use vapor recovery units for the vented gas off the tanks to capture for reuse or sales to minimize venting during active operations. Avant will be proactive on inspections to identify and fix leaks before they escalate.

Intent ☐ As Drilled ☐

API #		
Operator Name:	Property Name:	Well Number

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

First Take Point (FTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Is this well the defining well for the Horizontal Spacing Unit? ☐Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018
