


|          |               |          |                    |
|----------|---------------|----------|--------------------|
| Well     | WEBB 3 - 23   | Client   | SHELL OIL COMPANY  |
| Field    | 30-019-20135  | SIR No.  |                    |
| Engineer |               | Job Type | CEM SURFACE CASING |
| Country  | United States | Job Date | 06-27-2008         |

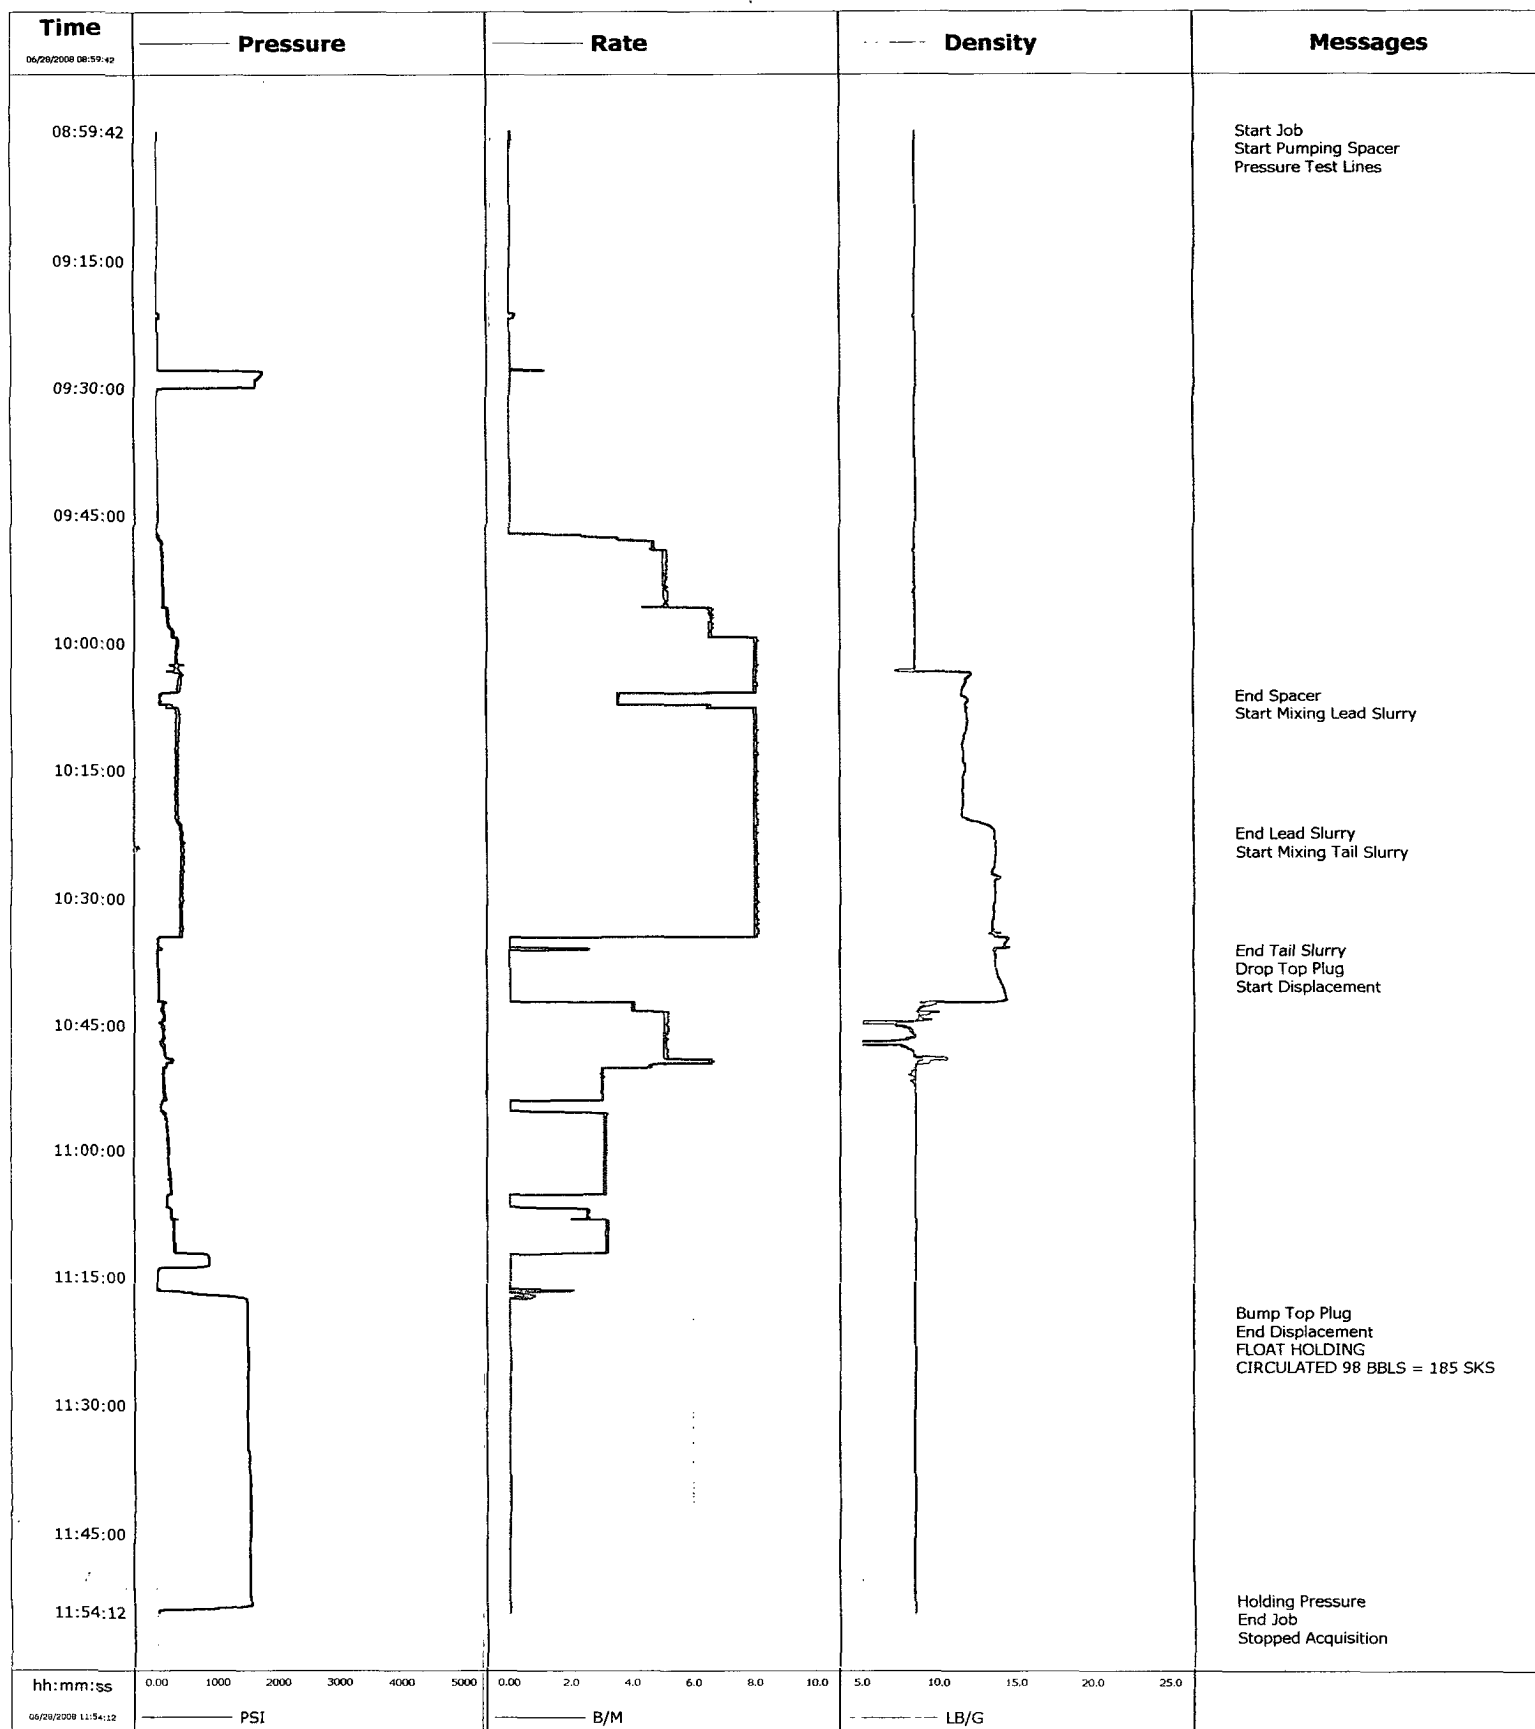

## Cementing Service Report

|                                                           |                        |                                                                              |                     |                                           |               |                                |  |                          |  |
|-----------------------------------------------------------|------------------------|------------------------------------------------------------------------------|---------------------|-------------------------------------------|---------------|--------------------------------|--|--------------------------|--|
|                                                           |                        |                                                                              |                     | Customer<br>SHELL OIL COMPANY             |               |                                |  | Job Number<br>2201756968 |  |
| Well<br>WEBB 3 - 23                                       |                        |                                                                              | Location (legal)    |                                           |               | Schlumberger Location<br>HOBBS |  | Job Start<br>Jun/27/2008 |  |
| Field<br>WILDCAT                                          |                        | Formation Name/Type                                                          |                     | Deviation                                 |               | Bit Size<br>14.8 in            |  | Well MD<br>981.0 ft      |  |
| County<br>GUADALUPE                                       |                        | State/Province<br>NEW MEXICO                                                 |                     | BHP                                       |               | BHST                           |  | BHCT                     |  |
| Well Master<br>0631034156                                 |                        | API/UWI                                                                      |                     |                                           |               |                                |  | Pore Press. Gradient     |  |
| Rig Name<br>NABORS M43                                    |                        | Drilled For<br>Oil                                                           |                     | Service Via<br>Land                       |               | Casing/Liner                   |  |                          |  |
|                                                           |                        |                                                                              |                     |                                           |               | Depth, ft                      |  | Size, in                 |  |
|                                                           |                        |                                                                              |                     |                                           |               | Weight, lb/ft                  |  | Grade                    |  |
| Offshore Zone                                             |                        | Well Class<br>NEW                                                            |                     | Well Type<br>New Well Completion          |               | 981.0                          |  | 10.750                   |  |
|                                                           |                        |                                                                              |                     |                                           |               | 0.0                            |  | 0.000                    |  |
| Drilling Fluid Type                                       |                        | Max. Density                                                                 |                     | Plastic Viscosity                         |               | Tubing/Drill Pipe              |  |                          |  |
|                                                           |                        |                                                                              |                     |                                           |               | Depth,                         |  | Size,                    |  |
|                                                           |                        |                                                                              |                     |                                           |               | Weight,                        |  | Grade                    |  |
| Service Line<br>Cementing                                 |                        | Job Type<br>Cem Surface Casing                                               |                     |                                           |               |                                |  |                          |  |
|                                                           |                        |                                                                              |                     |                                           |               |                                |  |                          |  |
| Max. Allowed Tubing Press                                 |                        | Max. Allowed Ann. Press                                                      |                     | WellHead Connection<br>Single Cement head |               | Perforations/Open Hole         |  |                          |  |
|                                                           |                        |                                                                              |                     |                                           |               | Top,                           |  | Bottom,                  |  |
|                                                           |                        |                                                                              |                     |                                           |               |                                |  | No. of Shots             |  |
|                                                           |                        |                                                                              |                     |                                           |               |                                |  | Total Interval           |  |
| Service Instructions                                      |                        |                                                                              |                     |                                           |               |                                |  | Diameter                 |  |
|                                                           |                        |                                                                              |                     |                                           |               |                                |  |                          |  |
|                                                           |                        |                                                                              |                     |                                           |               |                                |  |                          |  |
|                                                           |                        |                                                                              |                     |                                           |               |                                |  |                          |  |
|                                                           |                        |                                                                              |                     |                                           |               |                                |  |                          |  |
| Treat Down<br>Casing                                      |                        | Displacement<br>93.0 bbl                                                     |                     | Packer Type                               |               | Packer Depth                   |  |                          |  |
| Tubing Vol.                                               |                        | Casing Vol.                                                                  |                     | Annular Vol.<br>125.0 bbl                 |               | Openhole Vol.                  |  |                          |  |
| Casing/Tubing Secured <input checked="" type="checkbox"/> |                        | 1 Hole Volume Circulated prior to Cement <input checked="" type="checkbox"/> |                     | Casing Tools                              |               | Squeeze Job                    |  |                          |  |
| Lift Pressure<br>300 psi                                  |                        | Shoe Type<br>Guide                                                           |                     | Squeeze Type                              |               |                                |  |                          |  |
| Pipe Rotated <input type="checkbox"/>                     |                        | Pipe Reciprocated <input type="checkbox"/>                                   |                     | Shoe Depth<br>981.0 ft                    |               | Tool Type                      |  |                          |  |
| No. Centralizers                                          |                        | Top Plugs<br>1                                                               |                     | Bottom Plugs<br>1                         |               | Stage Tool Type                |  | Tool Depth               |  |
| Cement Head Type<br>Single                                |                        | Stage Tool Depth                                                             |                     | Tail Pipe Size                            |               |                                |  |                          |  |
| Job Scheduled For<br>Jun/27/2008                          |                        | Arrived on Location<br>Jun/27/2008                                           |                     | Leave Location<br>Jun/27/2008             |               | Collar Type<br>Guide           |  | Tail Pipe Depth          |  |
|                                                           |                        |                                                                              |                     |                                           |               | Collar Depth<br>938.0 ft       |  | Sqz. Total Vol.          |  |
| Date                                                      | Time<br>24-hr<br>clock | Treating<br>Pressure<br>PSI                                                  | Flow<br>Rate<br>B/M | Density<br>LB/G                           | Volume<br>BSL | Message                        |  |                          |  |
| 01/01/1970                                                | 00:00:00               |                                                                              |                     |                                           |               | Started Acquisition            |  |                          |  |
| 01/01/1970                                                | 00:00:00               |                                                                              |                     |                                           |               | Stopped Acquisition            |  |                          |  |
| 06/28/2008                                                | 07:34:14               |                                                                              |                     |                                           |               | Started Acquisition            |  |                          |  |
| 06/28/2008                                                | 08:59:42               | 6                                                                            | 0.1                 | 8.40                                      | 0.0           |                                |  |                          |  |
| 06/28/2008                                                | 08:59:43               |                                                                              |                     |                                           |               | Start Job                      |  |                          |  |
| 06/28/2008                                                | 08:59:43               | 6                                                                            | 0.0                 | 8.40                                      | 0.0           |                                |  |                          |  |
| 06/28/2008                                                | 08:59:45               |                                                                              |                     |                                           |               | Start Pumping Spacer           |  |                          |  |
| 06/28/2008                                                | 08:59:45               | 6                                                                            | 0.0                 | 8.40                                      | 0.0           |                                |  |                          |  |
| 06/28/2008                                                | 08:59:47               |                                                                              |                     |                                           |               | Pressure Test Lines            |  |                          |  |
| 06/28/2008                                                | 08:59:47               | 6                                                                            | 0.1                 | 8.40                                      | 0.0           |                                |  |                          |  |
| 06/28/2008                                                | 09:00:00               | 6                                                                            | 0.1                 | 8.40                                      | 0.0           |                                |  |                          |  |
| 06/28/2008                                                | 09:03:20               | 7                                                                            | 0.0                 | 8.40                                      | 0.1           |                                |  |                          |  |
| 06/28/2008                                                | 09:06:40               | 7                                                                            | 0.0                 | 8.40                                      | 0.1           |                                |  |                          |  |
| 06/28/2008                                                | 09:10:00               | 7                                                                            | 0.0                 | 8.40                                      | 0.1           |                                |  |                          |  |
| 06/28/2008                                                | 09:13:20               | 8                                                                            | 0.0                 | 8.40                                      | 0.1           |                                |  |                          |  |
| 06/28/2008                                                | 09:16:40               | 8                                                                            | 0.0                 | 8.40                                      | 0.1           |                                |  |                          |  |
| 06/28/2008                                                | 09:20:00               | 8                                                                            | 0.0                 | 8.40                                      | 0.1           |                                |  |                          |  |
| 06/28/2008                                                | 09:23:20               | 20                                                                           | 0.0                 | 8.40                                      | 0.2           |                                |  |                          |  |
| 06/28/2008                                                | 09:26:40               | 20                                                                           | 0.0                 | 8.40                                      | 0.2           |                                |  |                          |  |
| 06/28/2008                                                | 09:30:00               | 53                                                                           | 0.0                 | 8.40                                      | 0.3           |                                |  |                          |  |
| 06/28/2008                                                | 09:33:20               | 7                                                                            | 0.0                 | 8.40                                      | 0.3           |                                |  |                          |  |
| 06/28/2008                                                | 09:36:40               | 7                                                                            | 0.0                 | 8.40                                      | 0.3           |                                |  |                          |  |

| Well        |                  |                       | Field   |               | Job Start    |  | Customer          |  | Job Number                   |  |
|-------------|------------------|-----------------------|---------|---------------|--------------|--|-------------------|--|------------------------------|--|
| WEBB 3 v 23 |                  |                       | WILDCAT |               | Jun/27/2008  |  | SHELL OIL COMPANY |  | 2201756968                   |  |
| Date        | Time 24-hr clock | Treating Pressure PSI |         | Flow Rate B/M | Density LB/G |  | Volume BBL        |  | Message                      |  |
| 06/28/2008  | 09:40:00         | 7                     |         | 0.0           | 8.40         |  | 0.3               |  |                              |  |
| 06/28/2008  | 09:43:20         | 7                     |         | 0.0           | 8.40         |  | 0.3               |  |                              |  |
| 06/28/2008  | 09:46:40         | 14                    |         | 0.0           | 8.40         |  | 0.3               |  |                              |  |
| 06/28/2008  | 09:50:00         | 110                   |         | 5.1           | 8.40         |  | 13.3              |  |                              |  |
| 06/28/2008  | 09:53:20         | 105                   |         | 5.1           | 8.40         |  | 30.2              |  |                              |  |
| 06/28/2008  | 09:56:40         | 170                   |         | 6.6           | 8.39         |  | 48.5              |  |                              |  |
| 06/28/2008  | 10:00:00         | 332                   |         | 8.0           | 8.39         |  | 71.5              |  |                              |  |
| 06/28/2008  | 10:03:20         | 343                   |         | 8.0           | 11.42        |  | 98.1              |  |                              |  |
| 06/28/2008  | 10:06:08         |                       |         |               |              |  |                   |  | End Spacer                   |  |
| 06/28/2008  | 10:06:08         | 81                    |         | 3.5           | 11.58        |  | 118.7             |  |                              |  |
| 06/28/2008  | 10:06:10         |                       |         |               |              |  |                   |  | Start Mixing Lead Slurry     |  |
| 06/28/2008  | 10:06:10         | 81                    |         | 3.5           | 11.64        |  | 118.8             |  |                              |  |
| 06/28/2008  | 10:06:40         | 77                    |         | 3.5           | 11.90        |  | 120.6             |  |                              |  |
| 06/28/2008  | 10:10:00         | 340                   |         | 8.0           | 11.75        |  | 144.7             |  |                              |  |
| 06/28/2008  | 10:13:20         | 321                   |         | 8.0           | 11.56        |  | 171.4             |  |                              |  |
| 06/28/2008  | 10:16:40         | 319                   |         | 8.0           | 11.60        |  | 198.1             |  |                              |  |
| 06/28/2008  | 10:20:00         | 337                   |         | 8.0           | 11.53        |  | 224.8             |  |                              |  |
| 06/28/2008  | 10:22:25         |                       |         |               |              |  |                   |  | End Lead Slurry              |  |
| 06/28/2008  | 10:22:25         | 415                   |         | 8.0           | 13.64        |  | 244.2             |  |                              |  |
| 06/28/2008  | 10:22:27         |                       |         |               |              |  |                   |  | Start Mixing Tail Slurry     |  |
| 06/28/2008  | 10:22:27         | 439                   |         | 8.0           | 13.64        |  | 244.4             |  |                              |  |
| 06/28/2008  | 10:23:20         | 416                   |         | 8.0           | 13.62        |  | 251.5             |  |                              |  |
| 06/28/2008  | 10:26:40         | 397                   |         | 8.0           | 13.44        |  | 278.2             |  |                              |  |
| 06/28/2008  | 10:30:00         | 404                   |         | 8.0           | 13.57        |  | 304.9             |  |                              |  |
| 06/28/2008  | 10:33:20         | 418                   |         | 8.0           | 13.49        |  | 331.6             |  |                              |  |
| 06/28/2008  | 10:36:07         |                       |         |               |              |  |                   |  | End Tail Slurry              |  |
| 06/28/2008  | 10:36:07         | 37                    |         | 0.0           | 13.63        |  | 341.9             |  |                              |  |
| 06/28/2008  | 10:36:09         |                       |         |               |              |  |                   |  | Drop Top Plug                |  |
| 06/28/2008  | 10:36:09         | 33                    |         | 0.0           | 13.64        |  | 341.9             |  |                              |  |
| 06/28/2008  | 10:36:10         |                       |         |               |              |  |                   |  | Start Displacement           |  |
| 06/28/2008  | 10:36:10         | 34                    |         | 0.0           | 13.63        |  | 341.9             |  |                              |  |
| 06/28/2008  | 10:36:40         | 29                    |         | 0.0           | 13.69        |  | 341.9             |  |                              |  |
| 06/28/2008  | 10:40:00         | 33                    |         | 0.0           | 14.01        |  | 341.9             |  |                              |  |
| 06/28/2008  | 10:43:20         | 106                   |         | 5.1           | 8.62         |  | 347.1             |  |                              |  |
| 06/28/2008  | 10:46:40         | 121                   |         | 5.0           | 7.43         |  | 364.0             |  |                              |  |
| 06/28/2008  | 10:50:00         | 113                   |         | 3.0           | 8.42         |  | 381.2             |  |                              |  |
| 06/28/2008  | 10:53:20         | 137                   |         | 3.0           | 8.40         |  | 391.3             |  |                              |  |
| 06/28/2008  | 10:56:40         | 165                   |         | 3.1           | 8.40         |  | 397.5             |  |                              |  |
| 06/28/2008  | 11:00:00         | 196                   |         | 3.1           | 8.40         |  | 407.8             |  |                              |  |
| 06/28/2008  | 11:03:20         | 233                   |         | 3.1           | 8.40         |  | 418.2             |  |                              |  |
| 06/28/2008  | 11:06:40         | 179                   |         | 0.1           | 8.40         |  | 424.0             |  |                              |  |
| 06/28/2008  | 11:10:00         | 283                   |         | 3.2           | 8.40         |  | 433.5             |  |                              |  |
| 06/28/2008  | 11:13:20         | 854                   |         | 0.0           | 8.40         |  | 440.5             |  |                              |  |
| 06/28/2008  | 11:16:40         | 423                   |         | 0.5           | 8.40         |  | 440.9             |  |                              |  |
| 06/28/2008  | 11:19:07         |                       |         |               |              |  |                   |  | Bump Top Plug                |  |
| 06/28/2008  | 11:19:07         | 1490                  |         | 0.0           | 8.40         |  | 441.3             |  |                              |  |
| 06/28/2008  | 11:19:08         |                       |         |               |              |  |                   |  | End Displacement             |  |
| 06/28/2008  | 11:19:08         | 1491                  |         | 0.0           | 8.40         |  | 441.3             |  |                              |  |
| 06/28/2008  | 11:19:17         |                       |         |               |              |  |                   |  | FLOAT HOLDING                |  |
| 06/28/2008  | 11:19:17         | 1491                  |         | 0.0           | 8.40         |  | 441.3             |  |                              |  |
| 06/28/2008  | 11:20:00         | 1490                  |         | 0.0           | 8.40         |  | 441.3             |  |                              |  |
| 06/28/2008  | 11:20:15         |                       |         |               |              |  |                   |  | CIRCULATED 98 BBLS = 185 SKS |  |
| 06/28/2008  | 11:20:15         | 1489                  |         | 0.0           | 8.40         |  | 441.3             |  |                              |  |
| 06/28/2008  | 11:23:20         | 1489                  |         | 0.0           | 8.40         |  | 441.3             |  |                              |  |
| 06/28/2008  | 11:26:40         | 1489                  |         | 0.0           | 8.40         |  | 441.3             |  |                              |  |

| Well       |                  |                       | Field   |               |              | Job Start   |            | Customer            |  | Job Number |  |
|------------|------------------|-----------------------|---------|---------------|--------------|-------------|------------|---------------------|--|------------|--|
| WEBB 3- 23 |                  |                       | WILDCAT |               |              | Jun/27/2008 |            | SHELL OIL COMPANY   |  | 2201756968 |  |
| Date       | Time 24-hr clock | Treating Pressure PSI |         | Flow Rate B/M | Density LB/G |             | Volume BBL | Message             |  |            |  |
| 06/28/2008 | 11:30:00         | 1493                  |         | 0.0           | 8.40         |             | 441.3      |                     |  |            |  |
| 06/28/2008 | 11:33:20         | 1496                  |         | 0.0           | 8.40         |             | 441.3      |                     |  |            |  |
| 06/28/2008 | 11:36:40         | 1501                  |         | 0.0           | 8.40         |             | 441.3      |                     |  |            |  |
| 06/28/2008 | 11:40:00         | 1507                  |         | 0.0           | 8.40         |             | 441.3      |                     |  |            |  |
| 06/28/2008 | 11:43:20         | 1514                  |         | 0.0           | 8.39         |             | 441.3      |                     |  |            |  |
| 06/28/2008 | 11:46:40         | 1521                  |         | 0.0           | 8.39         |             | 441.3      |                     |  |            |  |
| 06/28/2008 | 11:50:00         | 1529                  |         | 0.0           | 8.39         |             | 441.3      |                     |  |            |  |
| 06/28/2008 | 11:52:48         |                       |         |               |              |             |            | Holding Pressure    |  |            |  |
| 06/28/2008 | 11:52:48         | 1536                  |         | 0.0           | 8.39         |             | 441.3      |                     |  |            |  |
| 06/28/2008 | 11:53:20         | 1538                  |         | 0.0           | 8.39         |             | 441.3      |                     |  |            |  |
| 06/28/2008 | 11:54:08         |                       |         |               |              |             |            | End Job             |  |            |  |
| 06/28/2008 | 11:54:08         | 28                    |         | 0.0           | 8.39         |             | 441.3      |                     |  |            |  |
| 06/28/2008 | 11:54:14         |                       |         |               |              |             |            | Stopped Acquisition |  |            |  |

### Post Job Summary

| Average Pump Rates,                                      |                                     |         |                                        |                           | Volume of Fluid Injected, bbl                                     |                                           |                                                   |    |
|----------------------------------------------------------|-------------------------------------|---------|----------------------------------------|---------------------------|-------------------------------------------------------------------|-------------------------------------------|---------------------------------------------------|----|
| Slurry                                                   | N2                                  | Mud     | Maximum Rate                           |                           | Total Slurry<br>226.0                                             | Mud                                       | Spacer<br>50.0                                    | N2 |
| Treating Pressure Summary, psi                           |                                     |         |                                        |                           | Breakdown Fluid                                                   |                                           |                                                   |    |
| Maximum<br>1500                                          | Final<br>300                        | Average | Bump Plug to<br>1500                   | Breakdown                 | Type<br>FreshWater                                                | Volume                                    | Density<br>8.34 lb/gal                            |    |
| Avg. N2 Percent                                          | Designed Slurry Volume<br>226.0 bbl |         | Displacement<br>93.0 bbl               | Mix Water Temp<br>60 degF | Cement Circulated to Surface? <input checked="" type="checkbox"/> | Volume 98.0 bbl                           |                                                   |    |
|                                                          |                                     |         |                                        |                           | Washed Thru Perfs <input type="checkbox"/>                        | To                                        |                                                   |    |
| Customer or Authorized Representative<br>GEORGE STAMPLEY |                                     |         | Schlumberger Supervisor<br>J, ANTILLON |                           |                                                                   | Circulation Lost <input type="checkbox"/> | Job Completed <input checked="" type="checkbox"/> |    |
|                                                          |                                     |         |                                        |                           |                                                                   | -                                         | -                                                 |    |
