

3R - 434

2012 AGWMR

02/19/2013



**CONESTOGA-ROVERS
& ASSOCIATES**

6121 Indian School Rd., NE Suite 200
Albuquerque, NM, USA 87110
Telephone: (505) 884-0672 Fax: (505) 884-4932
<http://www.craworld.com>

February 19, 2013

Reference No. 074925, 074927, 074928
074929, 074932, 074934
075038

Mr. Glenn von Gonten
New Mexico Oil Conservation Division
1220 South Saint Francis Dr.
Santa Fe, NM 87505

Dear Mr. von Gonten:

Re: Groundwater Monitoring Reports - 2012

Enclosed, please find a copy of the reports listed below compiled by Conestoga-Rovers and Associates, Inc.

- ✓ 3R434 1. Farmington B Com No. 1E Annual Groundwater Monitoring Report - September 2012
- ✓ 3R434 2. Faye Burdette No. 1 Annual Groundwater Monitoring Report - September 2012
- ✓ 3R469 3. Hampton No. 4M Annual Groundwater Monitoring Report - September 2012
- ✓ 3R431 4. Howell K No. 1 Annual Groundwater Monitoring Report - September 2012
- ✓ 3R471 5. Johnston Federal No. 4 Metering Station Annual Groundwater Monitoring Report - September 2012
- ✓ 3R426 6. San Juan 27-5 No. 34A Annual Groundwater Monitoring Report - September 2012
- 3R428 7. Sategna No. 2E Quarterly Groundwater Monitoring Report - September 2012

If you have any questions or require additional information, please contact me at (505) 884-0672 or keblanchard@craworld.com.

Sincerely,
CONESTOGA-ROVERS & ASSOCIATES

Kelly E. Blanchard

Kelly E. Blanchard
Project Manager

JP/cjg/1
Encl.

cc: Brandon Powell, NMOCD
Terry Lauck, ConocoPhillips (electronic only)

Equal
Employment Opportunity
Employer



SEPTEMBER 2012 ANNUAL GROUNDWATER MONITORING REPORT

CONOCOPHILLIPS FAYE BURDETTE No. 1
SAN JUAN COUNTY, NEW MEXICO
API# 30-045-09725
NMOCD# 3R-434

Prepared For:

CONOCOPHILLIPS COMPANY
Risk Management and Remediation
420 South Keeler Avenue
Bartlesville, OK, 74004

RECEIVED OGD
2013 FEB 20 A 11:20

DECEMBER 2012
REF. NO. 074929-95(4)

This report is printed on recycled paper.

Prepared by:
Conestoga-Rovers
& Associates

6121 Indian School Rd Ste. 200
Albuquerque, New Mexico 87110

Office: (505) 884-0672
Fax: (505) 884-4932

web: <http://www.CRAworld.com>

TABLE OF CONTENTS

	<u>Page</u>
1.0 INTRODUCTION	1
1.1 BACKGROUND	1
2.0 GROUNDWATER MONITORING SUMMARY, METHODOLOGY, AND ANALYTICAL RESULTS	3
2.1 GROUNDWATER MONITORING SUMMARY	3
2.2 GROUNDWATER MONITORING METHODOLOGY	3
2.3 GROUNDWATER MONITORING ANALYTICAL RESULTS	3
3.0 CONCLUSIONS AND RECOMMENDATIONS	4

LIST OF FIGURES

FIGURE 1	SITE VICINITY MAP
FIGURE 2	SITE DETAIL MAP
FIGURE 3	GEOLOGICAL CROSS SECTION
FIGURE 4	SEPTEMBER 2012 GROUNDWATER POTENTIOMETRIC SURFACE MAP

LIST OF TABLES

TABLE 1	SITE HISTORY TIMELINE
TABLE 2	MONITORING WELL SPECIFICATIONS AND GROUNDWATER ELEVATIONS (OCTOBER 2008 – SEPTEMBER 2012)
TABLE 3	GROUNDWATER ANALYTICAL RESULTS SUMMARY (OCTOBER 2008 – SEPTEMBER 2012)

LIST OF APPENDICES

APPENDIX A	SEPTEMBER 2012 ANNUAL GROUNDWATER SAMPLING FIELD FORMS
APPENDIX B	SEPTEMBER 2012 ANNUAL GROUNDWATER LABORATORY ANALYTICAL REPORT

1.0 INTRODUCTION

This report presents the results of quarterly groundwater monitoring completed by Conestoga-Rovers & Associates (CRA) on September 17, 2012, at the ConocoPhillips Company (ConocoPhillips) Faye Burdette No. 1 site, located on private land in Unit Letter G, Section 9, Township 30N, Range 11W of San Juan County, New Mexico (Site). Geographical coordinates for the Site are 36° 49' 47.71" North, 107° 59' 31.50" West. This event represents the first annual sampling event conducted at the Site, which follows 12 consecutive quarters of groundwater sampling at the Site.

The Site is located near the intersection of Highway 550 and Pioneer Avenue in Aztec, NM. The Site consists of a gas wellhead and associated equipment and installations. The location and general features of the Site are presented as **Figures 1 and 2**, respectively. A generalized geologic cross section of the Site is included as **Figure 3**.

1.1 BACKGROUND

The Faye Burdette No. 1 wellhead was spudded by Southwest Production Company in April 1962. Ownership was transferred to Beta Development Company in September 1963 and again to Mesa Operating Limited Partnership in August 1988. Conoco Inc., predecessor to ConocoPhillips Company, acquired the well in July 1991. A release occurred in May 2007 from a rusted portion of the on-Site produced water tank. Evidence of pre-existing hydrocarbon impacted soil was encountered during excavation, possibly related to a former earthen pit. Temporary Monitor Well MW-1 was drilled by Envirotech in September 2007. Groundwater samples from MW-1 indicated that benzene, toluene, ethylbenzene, and xylenes (BTEX) were below the New Mexico Water Quality Control Commission (NMWQCC) standards.

To complete additional investigation of the Site, as requested by the New Mexico Oil Conservation Division (NMOCD), Monitor Wells MW-2, MW-3, and MW-4 were installed under the supervision of Tetra Tech, Inc. (Tetra Tech) during January 2009. All four monitor wells were incorporated into a quarterly monitoring program that was initiated on January 29, 2009. On June 15, 2011, Site consulting responsibilities were transferred from Tetra Tech to CRA of Albuquerque, NM. Site history is outlined in **Table 1**.

After 10 consecutive quarters of sampling with BTEX constituents below New Mexico Water Quality Control Commission (NMWQCC) standards, BTEX analysis was discontinued following the March 2011 sampling event. Following the September 2011 sampling event, annual monitoring for dissolved manganese only was initiated.

2.0 GROUNDWATER MONITORING SUMMARY, METHODOLOGY, AND ANALYTICAL RESULTS

2.1 GROUNDWATER MONITORING SUMMARY

Prior to sampling on September 17, 2012, groundwater elevation measurements were obtained for Monitor Wells MW-1, MW-2, MW-3, and MW-4 using an oil/water interface probe. Groundwater elevations are detailed in **Table 2**. A groundwater potentiometric surface map is presented as **Figure 4**. Based on the September 2012 monitoring event data, groundwater flow is to the northwest and is consistent with historical monitoring event records for this Site. The Animas River is approximately 1/3 mile from the site and flows west.

2.2 GROUNDWATER MONITORING METHODOLOGY

Monitor Wells MW-1, MW-2, MW-3, and MW-4 were sampled during the September 2012 quarterly sampling event. Approximately three well volumes were purged from each monitor well with a dedicated, polyethylene, 1.5-inch disposable bailer prior to sampling. Purge water was placed in the on-Site produced water tank. Groundwater samples were placed in laboratory prepared bottles, packed on ice, and shipped under chain-of-custody documentation to Pace Analytical Services, Inc. in Lenexa, Kansas. The samples were analyzed for the presence of dissolved manganese according to EPA Method 6010. Groundwater sampling field forms are included as **Appendix A**.

2.3 GROUNDWATER MONITORING ANALYTICAL RESULTS

The NMWQCC standard for dissolved manganese is 0.2 milligrams per liter (mg/L). Laboratory analysis of groundwater samples collected during the September 17, 2012 monitoring event revealed that the sample from Monitor Well MW-1 exceeded the NMWQCC standard for dissolved manganese with a concentration of 0.73 mg/L. **Table 3** summarizes the laboratory analytical results for the September 2012 groundwater sampling event. The corresponding laboratory analytical report is included in **Appendix B**.


3.0 CONCLUSIONS AND RECOMMENDATIONS

Analysis for BTEX constituents, which were below both NMWQCC standards and laboratory detection limits for 10 consecutive quarters, was discontinued following the March 2011 sampling event.

Groundwater samples collected from MW-1 have continually exceeded the NMWQCC groundwater quality standard for dissolved manganese from October 2008 to September 2012.

Annual analysis for dissolved manganese will continue for all Site wells. Remediation Site closure will be requested when groundwater quality results begin to indicate that all monitored groundwater quality parameters are consistently below NMWQCC groundwater quality standards, are stable, or are representative of background conditions at the Site.

FIGURES

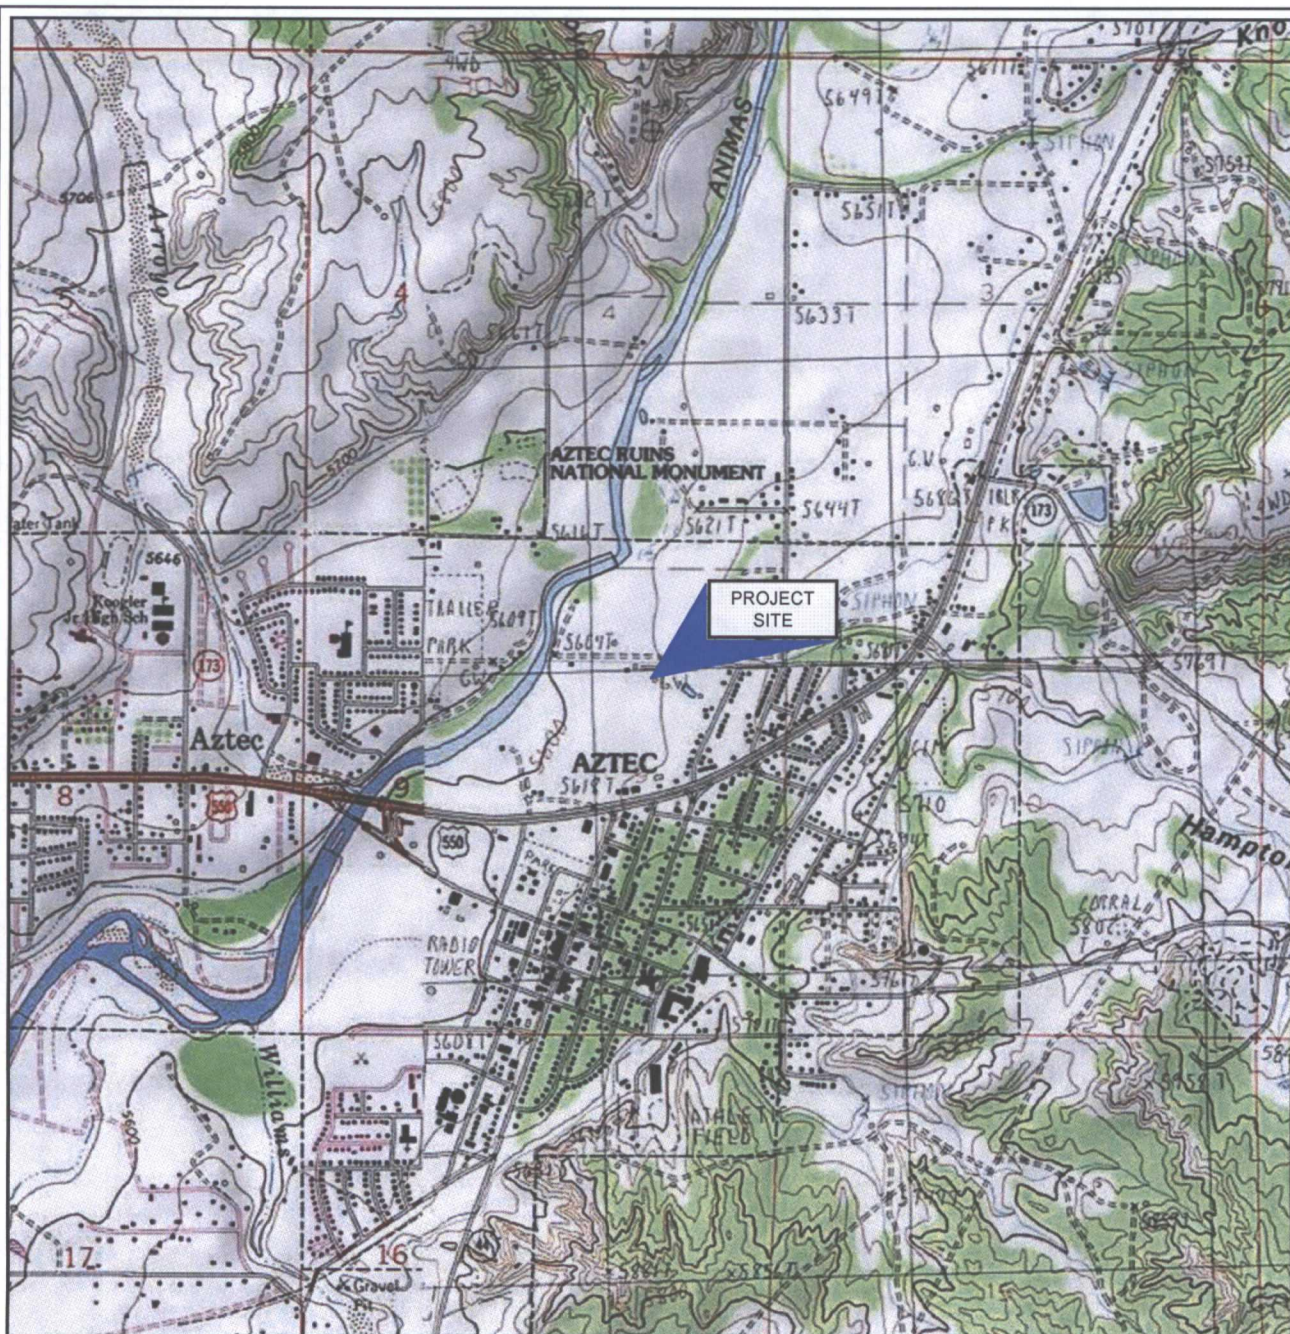

SOURCE: USGS 7.5 MINUTE QUADS
 "AZTEC AND FLORA VISTA, NEW MEXICO"




Figure 1


SITE VICINITY MAP
 FAYE BURDETTE No. 1 GAS WELL SITE
 SECTION 22, T30N-R12W, SAN JUAN COUNTY, NEW MEXICO
ConocoPhillips Company





Figure 2
 SITE DETAIL MAP
 FAYE BURDETTE No. 1 GAS WELL SITE
 SECTION 09, T30N-R11W, SAN JUAN COUNTY, NEW MEXICO
 ConocoPhillips Company



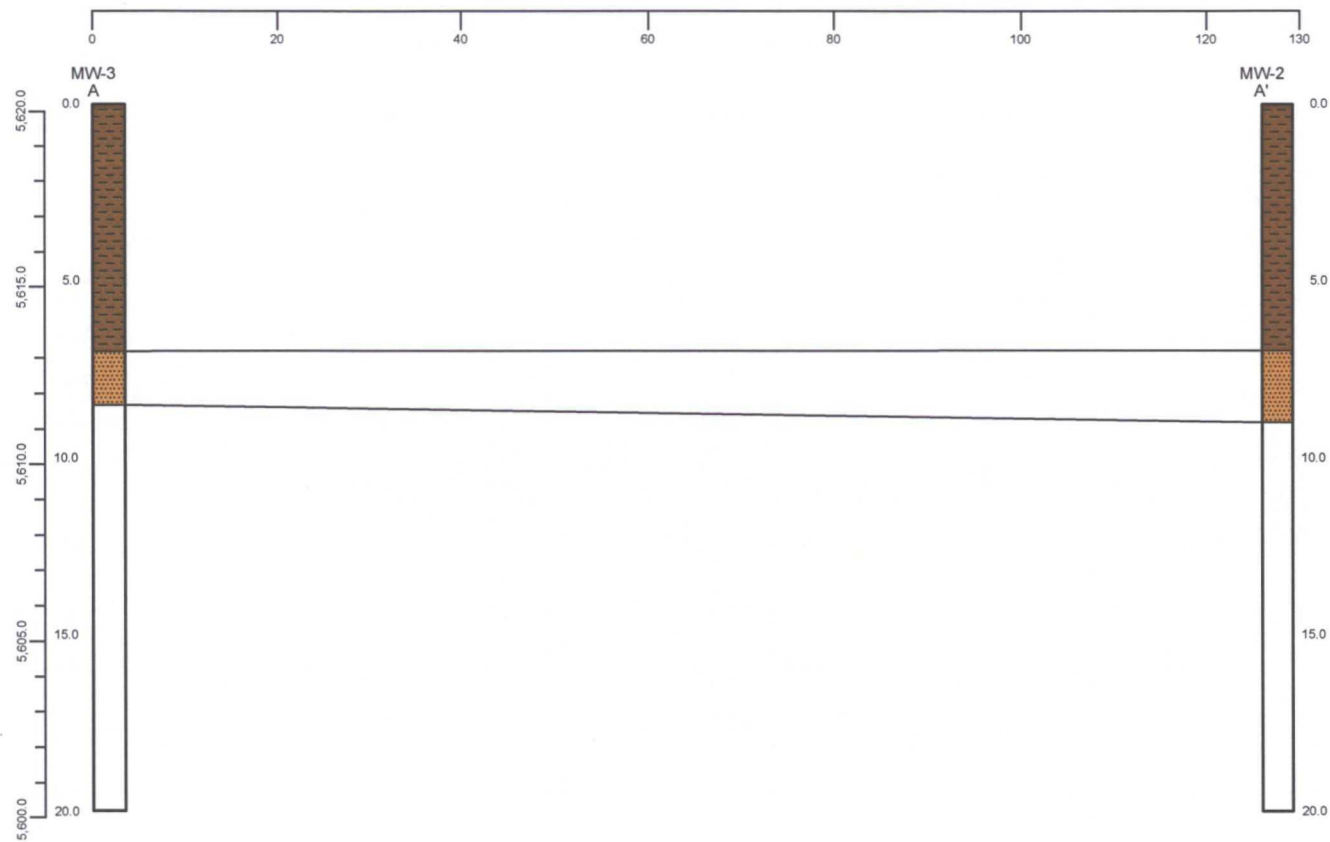

H: 1"= 20'
V: 1"= 10'

 Silty Sand
 Medium Grained Sand



Figure 3
GEOLOGICAL CROSS SECTION
FAYE BURDETTE No. 1 GAS WELL SITE
SECTION 09, T30N-R11W, SAN JUAN COUNTY, NEW MEXICO
ConocoPhillips Company

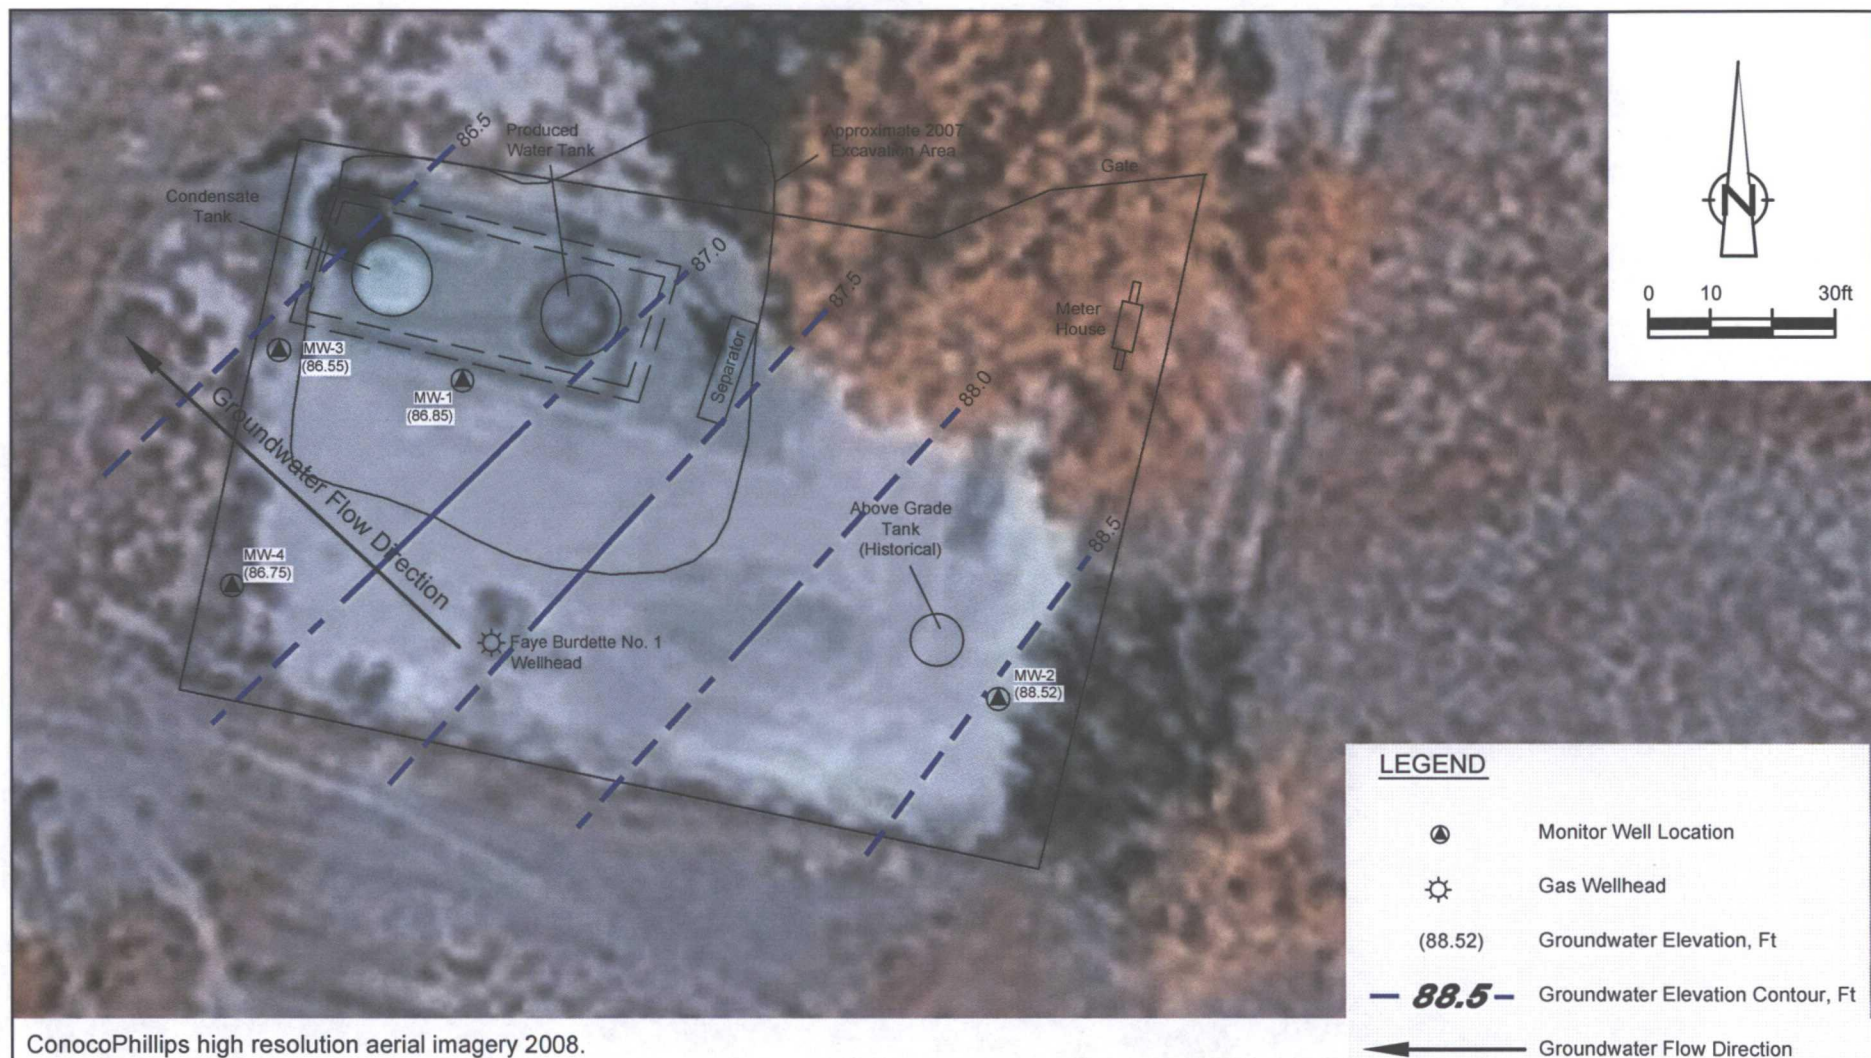


Figure 4

SEPTEMBER 2012 GROUNDWATER POTENTIOMETRIC SURFACE MAP
FAYE BURDETTE No. 1 GAS WELL SITE
SECTION 09, T30N-R11W, SAN JUAN COUNTY, NEW MEXICO
ConocoPhillips Company



TABLES

TABLE 1

1 of 2

**SITE HISTORY TIMELINE
CONOCOPHILLIPS COMPANY
FAYE BURDETTE No. 1
SAN JUAN COUNTY, NEW MEXICO**

DATE	Event/Action	ACTIVITY
April 29, 1962	Well spudded	Well was spudded by Southwest Production Company.
September 1, 1963	Ownership transfer	Ownership of well transferred to Beta Development Company.
February 21, 1983	NMOCD inspection	NMOCD inspection noted a leaky 2-inch valve on a storage tank.
August 15, 1988	Ownership transfer	Ownership of well transferred to Mesa Operating Limited Partnership.
July 1, 1991	Ownership transfer	Ownership of well transferred to Conoco Inc.
May 24, 2007	Release from produced water tank	A small (<25 gallons) release occurred from the produced water tank after a rusty spot was scraped off. Follow-up excavation encountered evidence of pre-existing hydrocarbon-impacted soil, apparently related to a former earthen pit beneath the tank.
July 1, 2007	Initial site assessment	Contaminated soil excavated from the Site. Two ground water samples were obtained at the time of this excavation, and one (1) of these samples was found to contain total xylenes above the State of New Mexico drinking water standard.
September 26, 2007	Monitor well installation/Site assessment	Ground water monitor well installed to a depth of 15 feet below ground surface (bgs) by Envirotech Inc. of Farmington, NM (Envirotech). A soil sample obtained from the well boring was analyzed for benzene, toluene, ethylbenzene, and xylenes (BTEX) and total petroleum hydrocarbons (TPH). Results were below NMOCD regulations of 10 parts per million (ppm), 50 ppm, and 100 ppm, respectively.
	Site assessment	A ground water sample was collected from the temporary Monitor Well (MW-1) and analyzed for BTEX; results were below the State of New Mexico drinking water standard for this constituent. Depth to ground water recorded at 9.5 feet bgs.
November 1, 2007	Envirotech recommendation	Envirotech report recommends plugging and abandonment of the temporary ground water monitor well and a no further action determination for the Site (Envirotech, 2007).
April 8, 2008	Additional monitoring requested by OCD	Oil Conservation Division of NM Energy, Minerals, and Resources Dept. indicates additional investigation and sampling is necessary for closure consideration during a meeting between Tetra Tech and Glenn Von Gonten.
October 22, 2008	Groundwater monitoring	1st quarter sampling of MW-1 conducted by Tetra Tech.
January 9, 2009	Installation of additional monitor wells	WDC Exploration and Wells of Peralta, NM installed additional Monitor Wells MW-2, MW-3 and MW-4 under the supervision of Tetra Tech.
January 29, 2009	Groundwater monitoring	Second quarter sampling of MW-1 conducted by Tetra Tech. Initial sampling of Monitor Wells MW-2, MW-3, and MW-4.
March 31, 2009	Groundwater monitoring	Third consecutive quarter of sampling MW-1 conducted by Tetra Tech. Second quarter sampling of Monitor Wells MW-2, MW-3, and MW-4.
June 17, 2009	Groundwater monitoring	Fourth consecutive quarter of sampling MW-1 conducted by Tetra Tech. Third quarter of sampling Monitor Wells MW-2, MW-3, and MW-4.
September 22, 2009	Groundwater monitoring	Fifth consecutive quarter of sampling MW-1 by Tetra Tech. Fourth consecutive quarter of sampling Monitor Wells MW-2, MW-3, and MW-4. Sampling for total metals discontinued as approved by NMOCD. Sampling for select dissolved metals based on total metals analyses begins.
December 16, 2009	Groundwater monitoring	Sixth consecutive quarter sampling of MW-1 conducted by Tetra Tech. Fifth consecutive quarter sampling of Monitor Wells MW-2, MW-3, and MW-4 for BTEX and dissolved manganese only.
April 1, 2010	Groundwater monitoring	Seventh consecutive quarter sampling of MW-1 conducted by Tetra Tech. Sixth consecutive quarter sampling of Monitor Wells MW-2, MW-3, and MW-4 for BTEX and dissolved manganese only.
June 9, 2010	Groundwater monitoring	Eighth consecutive quarter sampling of MW-1 conducted by Tetra Tech. Seventh consecutive quarter sampling of Monitor Wells MW-2, MW-3, and MW-4 for BTEX and dissolved manganese only.
September 20, 2010	Groundwater monitoring	Ninth consecutive quarter sampling of MW-1 conducted by Tetra Tech. Eighth consecutive quarter sampling of Monitor Wells MW-2, MW-3, and MW-4 for BTEX and dissolved manganese only.

SITE HISTORY TIMELINE
 CONOCOPHILLIPS COMPANY
 FAYE BURDETTE No. 1
 SAN JUAN COUNTY, NEW MEXICO

DATE	Event/Action	ACTIVITY
December 17, 2010	Groundwater monitoring	Tenth consecutive quarter sampling of MW-1 conducted by Tetra Tech. Ninth consecutive quarter sampling of Monitor Wells MW-2, MW-3, and MW-4 for BTEX and dissolved manganese only.
March 16, 2011	Groundwater monitoring	11th consecutive quarter sampling of MW-1 conducted by Tetra Tech. Tenth consecutive quarter sampling of Monitor Wells MW-2, MW-3, and MW-4 for BTEX and dissolved manganese only. Tetra Tech recommended that sampling for BTEX be discontinued.
June 15, 2011	Transfer of site consulting responsibilities	On June 15, 2011, Site consulting responsibilities were transferred from Tetra Tech of Albuquerque, NM to Conestoga-Rovers & Associates (CRA) of Albuquerque, NM.
June 22, 2011	Groundwater monitoring	12th consecutive quarter sampling of MW-1. 11th consecutive quarter sampling of Monitor Wells MW-2, MW-3, and MW-4. Samples analyzed for dissolved manganese only.
September 27, 2011	Groundwater monitoring	13th consecutive quarter sampling of MW-1. 12th consecutive quarter sampling of Monitor Wells MW-2, MW-3, and MW-4. Samples analyzed for dissolved manganese only.
September 17, 2012	Groundwater monitoring	Annual groundwater sampling event. Samples analyzed for dissolved manganese only.

TABLE 2

1 of 2

MONITOR WELL SPECIFICATIONS AND GROUNDWATER ELEVATIONS
 OCT 2008 - SEPT 2011
 CONOCOPHILLIPS COMPANY
 FAYE BURDETTE No. 1
 SAN JUAN COUNTY, NM

Well ID	Total Depth (ft below TOC)	Elevation*	Screen Interval (ft bgs)	Date Measured	Depth to Groundwater (ft below TOC)	Relative Water Level
MW-1	17.52	97.66	4.8 - 14.8	10/22/2008	10.91	86.75
				1/29/2009	11.72	85.94
				3/31/2009	11.88	85.78
				6/17/2009	11.24	86.42
				9/22/2009	10.87	86.79
				12/16/2009	11.56	86.10
				4/1/2010	11.91	85.75
				6/9/2010	11.31	86.35
				9/20/2010	11.39	86.27
				12/17/2010	11.06	86.60
				3/16/2011	11.39	86.27
				6/22/2011	10.73	86.93
				9/27/2011	10.68	86.98
MW-2	19.45	98.54	5 - 20	9/17/2012	10.81	86.85
				1/29/2009	10.91	87.63
				3/31/2009	11.12	87.42
				6/17/2009	10.48	88.06
				9/22/2009	10.76	87.78
				12/16/2009	10.61	87.93
				4/1/2010	11.20	87.34
				6/9/2010	10.35	88.19
				9/20/2010	10.35	88.19
				12/17/2010	10.10	88.44
				3/16/2011	10.70	87.84
MW-3	22.96	97.16	5 - 20	6/22/2011	9.69	88.85
				9/27/2011	9.63	88.91
				9/17/2012	10.02	88.52
				1/29/2009	11.44	85.72
				3/31/2009	11.62	85.54
				6/17/2009	10.97	86.19
				9/22/2009	10.57	86.59
				12/16/2009	11.32	85.84
				4/1/2010	11.66	85.50
				6/9/2010	11.10	86.06
				9/20/2010	11.17	85.99
				12/17/2010	10.84	86.32
				3/16/2011	11.16	86.00
				6/22/2011	10.54	86.62
				9/27/2011	10.50	86.66
				9/17/2012	10.61	86.55

TABLE 2

2 of 2

MONITOR WELL SPECIFICATIONS AND GROUNDWATER ELEVATIONS
OCT 2008 - SEPT 2011
CONOCOPHILLIPS COMPANY
FAYE BURDETTE No. 1
SAN JUAN COUNTY, NM

MW-4	22.28	97.06	5 - 20	1/29/2009	11.02	86.04
				3/31/2009	11.18	85.88
				6/17/2009	10.59	86.47
				9/22/2009	10.16	86.90
				12/16/2009	10.87	86.19
				4/1/2010	11.04	86.02
				6/9/2010	10.65	86.41
				9/20/2010	10.72	86.34
				12/17/2010	10.46	86.60
				3/16/2011	10.84	86.22
				6/22/2011	10.15	86.91
				9/27/2011	10.10	86.96
				9/17/2012	10.31	86.75

Notes:

1. ft = Feet
2. TOC = Top of casing
3. bgs = below ground surface
4. * Elevation relative to an arbitrary point set at 100 feet

TABLE 3

GROUNDWATER ANALYTICAL RESULTS SUMMARY
OCTOBER 2008 - SEPTEMBER 2012
CONOCOPHILLIPS COMPANY
FAYE BURDETTE No. 1
SAN JUAN COUNTY, NEW MEXICO

Well ID	Sample ID	Date	Sample Type	Benzene (mg/L)	Toluene (mg/L)	Ethylbenzene (mg/L)	Xylenes (total) (mg/L)	Iron (dissolved) (mg/L)	Manganese (dissolved) (mg/L)
MW-1	MW-1	10/22/2008	(orig)	< 0.005	< 0.005	< 0.005	< 0.005	--	--
	MW-1	1/29/2009	(orig)	< 0.005	< 0.005	< 0.005	< 0.005	--	--
	MW-1 Duplicate	1/29/2009	Duplicate	< 0.005	< 0.005	< 0.005	< 0.005	--	--
	MW-1	3/31/2009	(orig)	< 0.005	< 0.005	< 0.005	< 0.005	--	--
	MW-1 Duplicate	3/31/2009	Duplicate	< 0.005	< 0.005	< 0.005	< 0.005	--	--
	MW-1	6/17/2009	(orig)	< 0.005	< 0.005	< 0.005	< 0.005	--	--
	MW-1 Duplicate	6/17/2009	Duplicate	< 0.005	< 0.005	< 0.005	< 0.005	--	--
	MW-1	9/22/2009	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	0.445	1.44
	MW-1 Duplicate	9/22/2009	Duplicate	< 0.001	< 0.001	< 0.001	< 0.001	--	--
	MW-1	12/16/2009	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	0.732
	MW-1 Duplicate	12/16/2009	Duplicate	< 0.001	< 0.001	< 0.001	< 0.001	--	--
	MW-1	4/1/2010	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	1.71
	MW-1 Duplicate	4/1/2010	Duplicate	< 0.001	< 0.001	< 0.001	< 0.001	--	--
	MW-1	6/9/2010	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	1.61
	MW-1 Duplicate	6/9/2010	Duplicate	< 0.001	< 0.001	< 0.001	< 0.001	--	--
	MW-1	9/20/2010	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	0.895
	MW-1 Duplicate	9/20/2010	Duplicate	< 0.001	< 0.001	< 0.001	< 0.001	--	--
	MW-1	12/17/2010	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	0.773
	MW-1 Duplicate	12/17/2010	Duplicate	< 0.001	< 0.001	< 0.001	< 0.001	--	--
	MW-1	3/16/2011	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	2.23
	MW-1 Duplicate	3/16/2011	Duplicate	< 0.001	< 0.001	< 0.001	< 0.001	--	--
MW-2	GW-74929-062211-PG-04	6/22/2011	(orig)	--	--	--	--	--	0.368
	GW-074929-092711-CM-009	9/27/2011	(orig)	--	--	--	--	--	0.624
	GW-074929-091712-CM-MW-1	9/17/2012	(orig)	--	--	--	--	--	0.73
	GW-074929-091712-CM-DUP	9/17/2012	Duplicate	--	--	--	--	--	0.38
	MW-2	1/29/2009	(orig)	< 0.005	< 0.005	< 0.005	< 0.005	--	--
	MW-2	3/31/2009	(orig)	< 0.005	< 0.005	< 0.005	< 0.005	--	--
	MW-2	6/17/2009	(orig)	< 0.005	< 0.005	< 0.005	< 0.005	--	--
	MW-2	9/22/2009	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	< 0.02	0.0264
	MW-2	12/16/2009	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	0.0654
	MW-2	4/1/2010	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	0.16
	MW-2	6/9/2010	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	0.0323
	MW-2	9/20/2010	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	0.0455
	MW-2	12/17/2010	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	0.0332
	MW-2	3/16/2011	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	0.0265
	GW-74929-062211-PG-01	6/22/2011	(orig)	--	--	--	--	--	0.0232
	GW-074929-092711-CM-006	9/27/2011	(orig)	--	--	--	--	--	0.0142
	GW-074929-091712-CM-MW-2	9/17/2012	(orig)	--	--	--	--	--	< 0.005

TABLE 3

GROUNDWATER ANALYTICAL RESULTS SUMMARY
OCTOBER 2008 - SEPTEMBER 2012
CONOCOPHILLIPS COMPANY
FAYE BURDETTE No. 1
SAN JUAN COUNTY, NEW MEXICO

Well ID	Sample ID	Date	Sample Type	Benzene (mg/L)	Toluene (mg/L)	Ethylbenzene (mg/L)	Xylenes (total) (mg/L)	Iron (dissolved) (mg/L)	Manganese (dissolved) (mg/L)
MW-3	MW-3	1/29/2009	(orig)	< 0.005	< 0.005	< 0.005	< 0.005	--	--
	MW-3	3/31/2009	(orig)	< 0.005	< 0.005	< 0.005	< 0.005	--	--
	MW-3	6/17/2009	(orig)	< 0.005	< 0.005	< 0.005	< 0.005	--	--
	MW-3	9/22/2009	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	0.0291	0.0201
	MW-3	12/16/2009	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	0.0607
	MW-3	4/1/2010	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	0.0232
	MW-3	6/9/2010	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	< 0.005
	MW-3	9/20/2010	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	< 0.005
	MW-3	12/17/2010	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	0.178
	MW-3	3/16/2011	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	0.0424
	GW-74929-062211-PG-03	6/22/2011	(orig)	--	--	--	--	--	0.0311
	GW-074929-092711-CM-008	9/27/2011	(orig)	--	--	--	--	--	0.0244
MW-4	GW-074929-091712-CM-MW-3	9/17/2012	(orig)	--	--	--	--	--	0.015
	MW-4	1/29/2009	(orig)	< 0.005	< 0.005	< 0.005	< 0.005	--	--
	MW-4	3/31/2009	(orig)	< 0.005	< 0.005	< 0.005	< 0.005	--	--
	MW-4	6/17/2009	(orig)	< 0.005	< 0.005	< 0.005	< 0.005	--	--
	MW-4	9/22/2009	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	0.108	0.476
	MW-4	12/16/2009	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	0.0149
	MW-4	4/1/2010	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	< 0.005
	MW-4	6/9/2010	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	< 0.005
	MW-4	9/20/2010	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	0.0152
	MW-4	12/17/2010	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	0.0502
	MW-4	3/16/2011	(orig)	< 0.001	< 0.001	< 0.001	< 0.001	--	< 0.005
	GW-74929-062211-PG-02	6/22/2011	(orig)	--	--	--	--	--	< 0.015
	GW-074929-092711-CM-007	9/27/2011	(orig)	--	--	--	--	--	0.182
	GW-074929-091712-CM-MW-4	9/17/2012	(orig)	--	--	--	--	--	0.090
NMWQCC Groundwater Quality Standards				0.01	0.75	0.75	0.62	1	0.2

Notes:

1. MW = monitoring well
2. NMWQCC = New Mexico Water Quality Control Commission
3. Constituents in **BOLD** are in excess of NMWQCC groundwater quality standards
4. mg/L = milligrams per liter (parts per million)
5. < 1.0 = Below laboratory detection limit of 1.0 mg/L

APPENDIX A

SEPTEMBER 2012 ANNUAL GROUNDWATER SAMPLING FIELD FORMS

WELL SAMPLING FIELD INFORMATION FORM

FE/PROJECT NAME:

Faye Burdett No 1

JOB#

074929

SAMPLE ID:

QW-074929-091712-CM-MW1

WELL#

MW-1

WELL PURGING INFORMATION

9.17.12

PURGE DATE
(MM DD YY)

9.17.12

SAMPLE DATE
(MM DD YY)

1730

SAMPLE TIME
(24 HOUR)

1.05

WATER VOL IN CASING
(GALLONS)

3.5

ACTUAL VOL PURGED
(GALLONS)

PURGING AND SAMPLING EQUIPMENT

PURGING EQUIPMENT.....DEDICATED

☒ Y ☐ N

(CIRCLE ONE)

SAMPLING EQUIPMENT.....DEDICATED

☒ Y ☐ N

(CIRCLE ONE)

PURGING DEVICE

☒ G

A - SUBMERSIBLE PUMP

D - GAS LIFT PUMP

G - BAILER

X=

B - PERISTALTIC PUMP

E - PURGE PUMP

H - WATERRA®

PURGING DEVICE OTHER (SPECIFY)

SAMPLING DEVICE

☒ G

C - BLADDER PUMP

F - DIPPER BOTTLE

X - OTHER

X=

SAMPLING DEVICE OTHER (SPECIFY)

PURGING MATERIAL

☒ E

A - TEFLON

D - PVC

X=

B - STAINLESS STEEL

E - POLYETHYLENE

PURGING MATERIAL OTHER (SPECIFY)

SAMPLING MATERIAL

☒ E

C - POLYPROPYLENE

X - OTHER

X=

SAMPLING MATERIAL OTHER (SPECIFY)

PURGE TUBING

☒ C

A - TEFLON

D - POLYPROPYLENE

G - COMBINATION

X=

B - TYGON

E - POLYETHYLENE

TEFLON/POLYPROPYLENE

PURGE TUBING OTHER (SPECIFY)

SAMPLING TUBING

☒ C

C - ROPE

F - SILICONE

X - OTHER

X=

SAMPLING TUBING OTHER (SPECIFY)

FILTERING DEVICES 0.45

☒ A

A - IN-LINE DISPOSABLE

B - PRESSURE

C - VACUUM

FIELD MEASUREMENTS

DEPTH TO WATER

10.81

(feet)

WELL ELEVATION

97.66

(feet)

WELL DEPTH

17.35

(feet)

GROUNDWATER ELEVATION

86.85

(feet)

TEMPERATURE

PH

TDS

CONDUCTIVITY

ORP

VOLUME

18.80 (°C)

6.88 (std)

0.699 (g/L)

949 (µS/cm)

25.5 (mV)

2.75 (gal)

18.85 (°C)

6.86 (std)

0.708 (g/L)

961 (µS/cm)

9.3 (mV)

3.25 (gal)

18.95 (°C)

6.85 (std)

0.714 (g/L)

972 (µS/cm)

2.7 (mV)

3.5 (gal)

_____ (°C)

_____ (std)

_____ (g/L)

_____ (µS/cm)

_____ (mV)

_____ (gal)

_____ (°C)

_____ (std)

_____ (g/L)

_____ (µS/cm)

_____ (mV)

_____ (gal)

FIELD COMMENTS

SAMPLE APPEARANCE:

cloudy

ODOR:

None

COLOR:

brown

SHEEN Y/☒ N

WEATHER CONDITIONS:

TEMPERATURE

~80°

WIND ☒ Y ☐ N

PRECIPITATION Y/☒ N (IF Y TYPE)

SPECIFIC COMMENTS:

V.I x 3 = 3.14

Dup @ 1735

I CERTIFY THAT SAMPLING PROCEDURES WERE IN ACCORDANCE WITH APPLICABLE CRA PROTOCOLS

9.17.12

DATE

Jason Ploss

PRINT

[Signature]

SIGNATURE

WELL SAMPLING FIELD INFORMATION FORM

TE/PROJECT NAME:

Faye B. de la 1

JOB#

074929

SAMPLE ID:

Ch 074929-091712-CM-MW-2

WELL#

MW-2

WELL PURGING INFORMATION

9.17.12

PURGE DATE
(MM DD YY)

9.17.12

SAMPLE DATE
(MM DD YY)

1715

SAMPLE TIME
(24 HOUR)

1.51

WATER VOL IN CASING
(GALLONS)

5.0

ACTUAL VOL PURGED
(GALLONS)

PURGING AND SAMPLING EQUIPMENT

PURGING EQUIPMENT.....DEDICATED ☒ N

(CIRCLE ONE)

SAMPLING EQUIPMENT.....DEDICATED ☒ N

(CIRCLE ONE)

PURGING DEVICE

☒ G

A - SUBMERSIBLE PUMP

D - GAS LIFT PUMP

G - BAILER

X=

B - PERISTALTIC PUMP

E - PURGE PUMP

H - WATERA®

PURGING DEVICE OTHER (SPECIFY)

SAMPLING DEVICE

☒ G

C - BLADDER PUMP

F - DIPPER BOTTLE

X - OTHER

X=

SAMPLING DEVICE OTHER (SPECIFY)

PURGING MATERIAL

☒ E

A - TEFLON

D - PVC

X=

B - STAINLESS STEEL

E - POLYETHYLENE

PURGING MATERIAL OTHER (SPECIFY)

SAMPLING MATERIAL

☒ E

C - POLYPROPYLENE

X - OTHER

X=

SAMPLING MATERIAL OTHER (SPECIFY)

PURGE TUBING

☒ C

A - TEFLON

D - POLYPROPYLENE

G - COMBINATION

X=

B - TYGON

E - POLYETHYLENE

TEFLON/POLYPROPYLENE

PURGE TUBING OTHER (SPECIFY)

SAMPLING TUBING

☒ C

C - ROPE

F - SILICONE

X - OTHER

X=

SAMPLING TUBING OTHER (SPECIFY)

FILTERING DEVICES 0.45

☒ A

A - IN-LINE DISPOSABLE

B - PRESSURE

C - VACUUM

FIELD MEASUREMENTS

DEPTH TO WATER

10.02

(feet)

WELL ELEVATION

98.54

(feet)

WELL DEPTH

19.45

(feet)

GROUNDWATER ELEVATION

88.52

(feet)

TEMPERATURE

pH

TDS

CONDUCTIVITY

ORP

VOLUME

16.24 (°C)

6.52 (std)

0.691 (g/L)

885 (µS/cm)

99.9 (mV)

4.0 (gal)

16.31 (°C)

6.22 (std)

0.688 (g/L)

882 (µS/cm)

109.0 (mV)

4.5 (gal)

16.14 (°C)

6.19 (std)

0.692 (g/L)

884 (µS/cm)

108.5 (mV)

5.0 (gal)

_____ (°C)

_____ (std)

_____ (g/L)

_____ (µS/cm)

_____ (mV)

_____ (gal)

_____ (°C)

_____ (std)

_____ (g/L)

_____ (µS/cm)

_____ (mV)

_____ (gal)

FIELD COMMENTS

SAMPLE APPEARANCE:

cloudy

ODOR:

None

COLOR:

brown

SHEEN Y/N

N

WEATHER CONDITIONS:

TEMPERATURE

~80

WIND

0/N

PRECIPITATION Y/N (TYPE)

SPECIFIC COMMENTS:

V/LX3=4.53

I CERTIFY THAT SAMPLING PROCEDURES WERE IN ACCORDANCE WITH APPLICABLE CRA PROTOCOLS

9.17.12

DATE

PRINT

SIGNATURE

WELL SAMPLING FIELD INFORMATION FORM

TE/PROJECT NAME: Faye B. Little Vol JOB# 074929
 SAMPLE ID: GW-074929-091712-CM-1623 WELL# 1623

WELL PURGING INFORMATION

9.17.12 9.17.12 1710 1.96 6.0
 PURGE DATE (MM DD YY) SAMPLE DATE (MM DD YY) SAMPLE TIME (24 HOUR) WATER VOL. IN CASING (GALLONS) ACTUAL VOL. PURGED (GALLONS)

PURGING AND SAMPLING EQUIPMENT

PURGING EQUIPMENT.....DEDICATED ☒ N (CIRCLE ONE) SAMPLING EQUIPMENT.....DEDICATED ☒ N (CIRCLE ONE)

PURGING DEVICE	[G]	A - SUBMERSIBLE PUMP	D - GAS LIFT PUMP	G - BAILER	X=
		B - PERISTALTIC PUMP	E - PURGE PUMP	H - WATERA®	PURGING DEVICE OTHER (SPECIFY)
SAMPLING DEVICE	[G]	C - BLADDER PUMP	F - DIPPER BOTTLE	X - OTHER	X=
					SAMPLING DEVICE OTHER (SPECIFY)
PURGING MATERIAL	[E]	A - TEFLON	D - PVC		X=
		B - STAINLESS STEEL	E - POLYETHYLENE		PURGING MATERIAL OTHER (SPECIFY)
SAMPLING MATERIAL	[E]	C - POLYPROPYLENE	X - OTHER		X=
					SAMPLING MATERIAL OTHER (SPECIFY)
PURGE TUBING	[C]	A - TEFLON	D - POLYPROPYLENE	G - COMBINATION	X=
		B - TYGON	E - POLYETHYLENE	TEFLON/POLYPROPYLENE	PURGE TUBING OTHER (SPECIFY)
SAMPLING TUBING	[C]	C - ROPE	F - SILICONE	X - OTHER	X=
					SAMPLING TUBING OTHER (SPECIFY)

FILTERING DEVICES 0.45 A A - IN-LINE DISPOSABLE B - PRESSURE C - VACUUM

FIELD MEASUREMENTS

DEPTH TO WATER	<u>10.61</u>	(feet)	WELL ELEVATION	<u>97.16</u>	(feet)
WELL DEPTH	<u>22.85</u>	(feet)	GROUNDWATER ELEVATION	<u>86.55</u>	(feet)

TEMPERATURE	pH	TDS	CONDUCTIVITY	ORP	VOLUME
<u>18.40</u> (°C)	<u>6.50</u> (std)	<u>0.691</u> (g/L)	<u>929</u> (µS/cm)	<u>111.0</u> (mV)	<u>5.0</u> (gal)
<u>18.43</u> (°C)	<u>6.21</u> (std)	<u>6.691</u> (g/L)	<u>9.31</u> (µS/cm)	<u>108.9</u> (mV)	<u>5.5</u> (gal)
<u>17.90</u> (°C)	<u>6.20</u> (std)	<u>0.692</u> (g/L)	<u>921</u> (µS/cm)	<u>106.8</u> (mV)	<u>6.0</u> (gal)
(°C)	(std)	(g/L)	(µS/cm)	(mV)	(gal)
(°C)	(std)	(g/L)	(µS/cm)	(mV)	(gal)

FIELD COMMENTS

SAMPLE APPEARANCE: cloudy ODOR: None COLOR: brown SHEEN Y/☒ N
 WEATHER CONDITIONS: TEMPERATURE ~80° WIND 0 N PRECIPITATION Y/☒ N (IF Y TYPE) _____
 SPECIFIC COMMENTS: _____

V₀/x3 = 5.88

I CERTIFY THAT SAMPLING PROCEDURES WERE IN ACCORDANCE WITH APPLICABLE CRA PROTOCOLS

DATE 9-17-12

PRINCE Christine Matthews

SIGNATURE [Signature]

WELL SAMPLING FIELD INFORMATION FORM

TE/PROJECT NAME: Page Bunker No. 1

JOB# 074929

SAMPLE ID: GW-074929-091712-CM-MW-4

WELL# MW-4

WELL PURGING INFORMATION

9.17.12 PURGE DATE (MM DD YY)
 9.17.12 SAMPLE DATE (MM DD YY)
 1720 SAMPLE TIME (24 HOUR)
 1.65 WATER VOL. IN CASING (GALLONS)
 5.75 ACTUAL VOL. PURGED (GALLONS)

PURGING AND SAMPLING EQUIPMENT

PURGING EQUIPMENT.....DEDICATED ☒ N

SAMPLING EQUIPMENT.....DEDICATED ☒ N

(CIRCLE ONE)

(CIRCLE ONE)

PURGING DEVICE	[G]	A - SUBMERSIBLE PUMP	D - GAS LIFT PUMP	G - BAILER	X=	
		B - PERISTALTIC PUMP	E - PURGE PUMP	H - WATERRA®		PURGING DEVICE OTHER (SPECIFY)
SAMPLING DEVICE	[G]	C - BLADDER PUMP	F - DIPPER BOTTLE	X - OTHER	X=	
						SAMPLING DEVICE OTHER (SPECIFY)
PURGING MATERIAL	[E]	A - TEFLON	D - PVC		X=	
		B - STAINLESS STEEL	E - POLYETHYLENE			PURGING MATERIAL OTHER (SPECIFY)
SAMPLING MATERIAL	[E]	C - POLYPROPYLENE	X - OTHER		X=	
						SAMPLING MATERIAL OTHER (SPECIFY)
PURGE TUBING	[C]	A - TEFLON	D - POLYPROPYLENE	G - COMBINATION	X=	
		B - TYGON	E - POLYETHYLENE	TEFLON/POLYPROPYLENE		PURGE TUBING OTHER (SPECIFY)
SAMPLING TUBING	[C]	C - ROPE	F - SILICONE	X - OTHER	X=	
						SAMPLING TUBING OTHER (SPECIFY)

FILTERING DEVICES 0.45 [A] A - IN-LINE DISPOSABLE B - PRESSURE C - VACUUM

FIELD MEASUREMENTS

DEPTH TO WATER	<u>10.31</u>	(feet)	WELL ELEVATION	<u>97.06</u>	(feet)
WELL DEPTH	<u>20.65</u>	(feet)	GROUNDWATER ELEVATION	<u>86.75</u>	(feet)

TEMPERATURE	pH	TDS	CONDUCTIVITY	ORP	VOLUME
<u>17.12</u> (°C)	<u>6.58</u> (std)	<u>0.711</u> (g/L)	<u>929</u> (µS/cm)	<u>101.1</u> (mV)	<u>5.25</u> (gal)
<u>16.98</u> (°C)	<u>6.72</u> (std)	<u>0.709</u> (g/L)	<u>923</u> (µS/cm)	<u>85.1</u> (mV)	<u>5.50</u> (gal)
<u>16.95</u> (°C)	<u>6.38</u> (std)	<u>0.710</u> (g/L)	<u>925</u> (µS/cm)	<u>103.5</u> (mV)	<u>5.75</u> (gal)
(°C)	(std)	(g/L)	(µS/cm)	(mV)	(gal)
(°C)	(std)	(g/L)	(µS/cm)	(mV)	(gal)

FIELD COMMENTS

SAMPLE APPEARANCE: cloudy ODOR: none COLOR: light brown SHEEN Y N
 WEATHER CONDITIONS: TEMPERATURE 85° WIND Y N PRECIPITATION Y N (IF Y, TYPE) _____
 SPECIFIC COMMENTS: _____

Vol x 3 = 4.96

I CERTIFY THAT SAMPLING PROCEDURES WERE IN ACCORDANCE WITH APPLICABLE CRA PROTOCOLS

DATE 9-17-12

PRINT Christine Matthews

SIGNATURE [Signature]

APPENDIX B

SEPTEMBER 2012 ANNUAL GROUNDWATER LABORATORY ANALYTICAL REPORT



Pace Analytical Services, Inc.
9608 Loiret Blvd.
Lenexa, KS 66219
(913)599-5665

October 02, 2012

Christine Matthews
CRA
6121 Indian School Rd NE
Suite 200
Albuquerque, NM 87110

RE: Project: 074929 FAYE BURDETTE NO 1
Pace Project No.: 60129288

Dear Christine Matthews:

Enclosed are the analytical results for sample(s) received by the laboratory on September 19, 2012. The results relate only to the samples included in this report. Results reported herein conform to the most current TNI standards and the laboratory's Quality Assurance Manual, where applicable, unless otherwise noted in the body of the report.

If you have any questions concerning this report, please feel free to contact me.

Sincerely,

Alice Flanagan

alice.flanagan@pacelabs.com
Project Manager

Enclosures

cc: Kelly Blanchard, COP Conestoga-Rovers & Associa
Angela Bown, COP Conestoga-Rovers & Associa
Cassie Brown, COP Conestoga-Rovers & Associa



REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, Inc..

Page 1 of 13

Pace Package 1 of 15

CERTIFICATIONS

Project: 074929 FAYE BURDETTE NO 1

Pace Project No.: 60129288

Kansas Certification IDs

9608 Loiret Boulevard, Lenexa, KS 66219

A2LA Certification #: 2456.01

Arkansas Certification #: 12-019-0

Illinois Certification #: 002885

Iowa Certification #: 118

Kansas/NELAP Certification #: E-10116

Louisiana Certification #: 03055

Nevada Certification #: KS000212008A

Oklahoma Certification #: 9205/9935

Texas Certification #: T104704407-12-3

Utah Certification #: KS000212012-2

REPORT OF LABORATORY ANALYSIS

Page 2 of 13

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, Inc..

SAMPLE SUMMARY

Project: 074929 FAYE BURDETTE NO 1
Pace Project No.: 60129288

Lab ID	Sample ID	Matrix	Date Collected	Date Received
60129288001	GW-074929-091712-CM-MW-3	Water	09/17/12 17:10	09/19/12 08:00
60129288002	GW-074929-091712-CM-MW-4	Water	09/17/12 17:20	09/19/12 08:00
60129288003	GW-074929-091712-CM-MW-2	Water	09/17/12 17:15	09/19/12 08:00
60129288004	GW-074929-091712-CM-MW-1	Water	09/17/12 17:30	09/19/12 08:00
60129288005	GW-074929-091712-CM-DUP	Water	09/17/12 17:35	09/19/12 08:00

REPORT OF LABORATORY ANALYSIS

Page 3 of 13

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, Inc..

SAMPLE ANALYTE COUNT

Project: 074929 FAYE BURDETTE NO 1

Pace Project No.: 60129288

Lab ID	Sample ID	Method	Analysts	Analytes Reported
60129288001	GW-074929-091712-CM-MW-3	EPA 6010	JGP	1
60129288002	GW-074929-091712-CM-MW-4	EPA 6010	JGP	1
60129288003	GW-074929-091712-CM-MW-2	EPA 6010	JGP	1
60129288004	GW-074929-091712-CM-MW-1	EPA 6010	JGP	1
60129288005	GW-074929-091712-CM-DUP	EPA 6010	JGP	1

REPORT OF LABORATORY ANALYSIS

Page 4 of 13

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, Inc..

PROJECT NARRATIVE

Project: 074929 FAYE BURDETTE NO 1
Pace Project No.: 60129288

Method: EPA 6010
Description: 6010 MET ICP, Dissolved
Client: COP Conestoga-Rovers & Associates, Inc. NM
Date: October 02, 2012

General Information:

5 samples were analyzed for EPA 6010. All samples were received in acceptable condition with any exceptions noted below.

Hold Time:

The samples were analyzed within the method required hold times with any exceptions noted below.

Sample Preparation:

The samples were prepared in accordance with EPA 3010 with any exceptions noted below.

Initial Calibrations (including MS Tune as applicable):

All criteria were within method requirements with any exceptions noted below.

Continuing Calibration:

All criteria were within method requirements with any exceptions noted below.

Method Blank:

All analytes were below the report limit in the method blank with any exceptions noted below.

Laboratory Control Spike:

All laboratory control spike compounds were within QC limits with any exceptions noted below.

Matrix Spikes:

All percent recoveries and relative percent differences (RPDs) were within acceptance criteria with any exceptions noted below.

Additional Comments:

This data package has been reviewed for quality and completeness and is approved for release.

REPORT OF LABORATORY ANALYSIS

Page 5 of 13

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, Inc..



Pace Analytical Services, Inc.
9608 Loiret Blvd.
Lenexa, KS 66219
(913)599-5665

ANALYTICAL RESULTS

Project: 074929 FAYE BURDETTE NO 1

Pace Project No.: 60129288

Sample: GW-074929-091712-CM-MW-3 Lab ID: 60129288001 Collected: 09/17/12 17:10 Received: 09/19/12 08:00 Matrix: Water

Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
6010 MET ICP, Dissolved									
Analytical Method: EPA 6010 Preparation Method: EPA 3010									
Manganese, Dissolved	0.015	mg/L	0.0050	0.00060	1	09/24/12 13:45	10/01/12 11:20	7439-96-5	

Date: 10/02/2012 04:15 PM

REPORT OF LABORATORY ANALYSIS

Page 6 of 13

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, Inc..

ANALYTICAL RESULTS

Project: 074929 FAYE BURDETTE NO 1

Pace Project No.: 60129288

Sample: **GW-074929-091712-CM-MW-4** Lab ID: **60129288002** Collected: 09/17/12 17:20 Received: 09/19/12 08:00 Matrix: Water

Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
6010 MET ICP, Dissolved									
Analytical Method: EPA 6010 Preparation Method: EPA 3010									
Manganese, Dissolved	0.090	mg/L	0.0050	0.00060	1	09/24/12 13:45	10/01/12 11:22	7439-96-5	

ANALYTICAL RESULTS

Project: 074929 FAYE BURDETTE NO 1

Pace Project No.: 60129288

Sample: **GW-074929-091712-CM-MW-2** Lab ID: **60129288003** Collected: 09/17/12 17:15 Received: 09/19/12 08:00 Matrix: Water

Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
6010 MET ICP, Dissolved									
Analytical Method: EPA 6010 Preparation Method: EPA 3010									
Manganese, Dissolved	ND	mg/L	0.0050	0.00060	1	09/24/12 13:45	10/01/12 11:25	7439-96-5	

ANALYTICAL RESULTS

Project: 074929 FAYE BURDETTE NO 1

Pace Project No.: 60129288

Sample: GW-074929-091712-CM-MW-1 Lab ID: 60129288004 Collected: 09/17/12 17:30 Received: 09/19/12 08:00 Matrix: Water

Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
6010 MET ICP, Dissolved									
Analytical Method: EPA 6010 Preparation Method: EPA 3010									
Manganese, Dissolved	0.73	mg/L	0.0050	0.00060	1	09/24/12 13:45	10/01/12 11:27	7439-96-5	

ANALYTICAL RESULTS

Project: 074929 FAYE BURDETTE NO 1

Pace Project No.: 60129288

Sample: **GW-074929-091712-CM-DUP** Lab ID: **60129288005** Collected: 09/17/12 17:35 Received: 09/19/12 08:00 Matrix: Water

Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
6010 MET ICP, Dissolved									
Analytical Method: EPA 6010 Preparation Method: EPA 3010									
Manganese, Dissolved	0.38	mg/L	0.0050	0.00060	1	09/24/12 13:45	10/01/12 11:29	7439-96-5	

QUALITY CONTROL DATA

Project: 074929 FAYE BURDETTE NO 1
Pace Project No.: 60129288

QC Batch: MPRP/19622 Analysis Method: EPA 6010
QC Batch Method: EPA 3010 Analysis Description: 6010 MET Dissolved
Associated Lab Samples: 60129288001, 60129288002, 60129288003, 60129288004, 60129288005

METHOD BLANK: 1066225 Matrix: Water
Associated Lab Samples: 60129288001, 60129288002, 60129288003, 60129288004, 60129288005

Parameter	Units	Blank Result	Reporting Limit	Analyzed	Qualifiers
Manganese, Dissolved	mg/L	ND	0.0050	10/01/12 11:09	

LABORATORY CONTROL SAMPLE: 1066226

Parameter	Units	Spike Conc.	LCS Result	LCS % Rec	% Rec Limits	Qualifiers
Manganese, Dissolved	mg/L	1	1.0	100	80-120	

MATRIX SPIKE & MATRIX SPIKE DUPLICATE: 1066227 1066228

Parameter	Units	60129643004 Result	MS Spike Conc.	MSD Spike Conc.	MS Result	MSD Result	MS % Rec	MSD % Rec	% Rec Limits	Max RPD	Qual
Manganese, Dissolved	mg/L	1320 ug/L	1	1	2.3	2.3	95	95	75-125	0	20

QUALIFIERS

Project: 074929 FAYE BURDETTE NO 1
Pace Project No.: 60129288

DEFINITIONS

DF - Dilution Factor, if reported, represents the factor applied to the reported data due to changes in sample preparation, dilution of the sample aliquot, or moisture content.

ND - Not Detected at or above adjusted reporting limit.

J - Estimated concentration above the adjusted method detection limit and below the adjusted reporting limit.

MDL - Adjusted Method Detection Limit.

PRL - Pace Reporting Limit.

RL - Reporting Limit.

S - Surrogate

1,2-Diphenylhydrazine (8270 listed analyte) decomposes to Azobenzene.

Consistent with EPA guidelines, unrounded data are displayed and have been used to calculate % recovery and RPD values.

LCS(D) - Laboratory Control Sample (Duplicate)

MS(D) - Matrix Spike (Duplicate)

DUP - Sample Duplicate

RPD - Relative Percent Difference

NC - Not Calculable.

SG - Silica Gel - Clean-Up

U - Indicates the compound was analyzed for, but not detected.

N-Nitrosodiphenylamine decomposes and cannot be separated from Diphenylamine using Method 8270. The result reported for each analyte is a combined concentration.

Pace Analytical is TNI accredited. Contact your Pace PM for the current list of accredited analytes.

TNI - The NELAC Institute.

QUALITY CONTROL DATA CROSS REFERENCE TABLE

Project: 074929 FAYE BURDETTE NO 1

Pace Project No.: 60129288

Lab ID	Sample ID	QC Batch Method	QC Batch	Analytical Method	Analytical Batch
60129288001	GW-074929-091712-CM-MW-3	EPA 3010	MPRP/19622	EPA 6010	ICP/16166
60129288002	GW-074929-091712-CM-MW-4	EPA 3010	MPRP/19622	EPA 6010	ICP/16166
60129288003	GW-074929-091712-CM-MW-2	EPA 3010	MPRP/19622	EPA 6010	ICP/16166
60129288004	GW-074929-091712-CM-MW-1	EPA 3010	MPRP/19622	EPA 6010	ICP/16166
60129288005	GW-074929-091712-CM-DUP	EPA 3010	MPRP/19622	EPA 6010	ICP/16166

Sample Condition Upon Receipt – ESI Tech Specs

Client Name: COP- CAA NM

Project #: 66129288

Courier: Fed Ex ☒ UPS ☐ USPS ☐ Client ☐ Commercial ☐ Pace ☐ Other ☐

Optional
Proj Due Date: 10/03
Proj Name: _____

Tracking #: 80069527 0905 Pace Shipping Label Used? Yes ☐ No ☒

Custody Seal on Cooler/Box Present: Yes ☒ No ☐ Seals intact: Yes ☒ No ☐

Packing Material: Bubble Wrap ☐ Bubble Bags ☐ Foam ☐ None ☐ Other ☒ 2plc

Thermometer Used: T-191 / T-194

Type of Ice: Wet Blue ☐ None ☐ Samples received on ice, cooling process has begun.
(circle one)

Cooler Temperature: 1.1

Date and Initials of person examining contents: 9/19/12 AS

Temperature should be above freezing to 6°C

Chain of Custody present:	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A	1.
Chain of Custody filled out:	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A	2.
Chain of Custody relinquished:	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A	3.
Sampler name & signature on COC:	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A	4.
Samples arrived within holding time:	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A	5.
Short Hold Time analyses (<72hr):	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No <input type="checkbox"/> N/A	6.
Rush Turn Around Time requested:	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No <input type="checkbox"/> N/A	7.
Sufficient volume:	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A	8.
Correct containers used:	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A	
-Pace containers used:	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A	9.
Containers intact:	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A	10.
Unpreserved 5035A soils frozen w/in 48hrs?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input checked="" type="checkbox"/> N/A	11.
Filtered volume received for dissolved tests?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input checked="" type="checkbox"/> N/A	12.
Sample labels match COC:	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A	
-Includes date/time/ID/analyses Matrix: <u>WT</u>		13.
All containers needing preservation have been checked.	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A	
All containers needing preservation are found to be in compliance with EPA recommendation.	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A	14.
Exceptions: VOA, coliform, TOC, O&G, WI-DRO (water), Phenolics	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	Initial when completed
Trip Blank present:	<input type="checkbox"/> Yes <input type="checkbox"/> No <input checked="" type="checkbox"/> N/A	Lot # of added preservative
Pace Trip Blank lot # (if purchased):		15.
Headspace in VOA vials (>6mm):	<input type="checkbox"/> Yes <input type="checkbox"/> No <input checked="" type="checkbox"/> N/A	16.
Project sampled in USDA Regulated Area:	<input type="checkbox"/> Yes <input type="checkbox"/> No <input checked="" type="checkbox"/> N/A	17. List State: <u>h</u>

Client Notification/ Resolution: Copy COC to Client? Y ☒ N ☐ Field Data Required? Y / N

Person Contacted: _____ Date/Time: _____

Comments/ Resolution: _____

Temp Log: Record start and finish times when unpacking cooler, if >20 min, recheck sample temps.
Start: 0936 Start: _____
End: 0940 End: _____
Temp: _____ Temp: _____

Project Manager Review: MT Date: 9/20/12

Note: Whenever there is a discrepancy affecting North Carolina compliance samples, a copy of this form will be sent to the NCDENR Certification Office (i.e. out of hold, incorrect preservative, out of temp, incorrect containers).
