


200  
400  
BWP

TEXAS PACIFIC OIL CO., INC.  
STATE A ACCT. 1 WELL NO. 42  
SEC. 4, T-23-S, R-36-E  
660' FNL AND 660' FEL  
LANGLIE MATTIX POOL  
LEA COUNTY, NEW MEXICO  
COMPLETION DATE 12/14/57

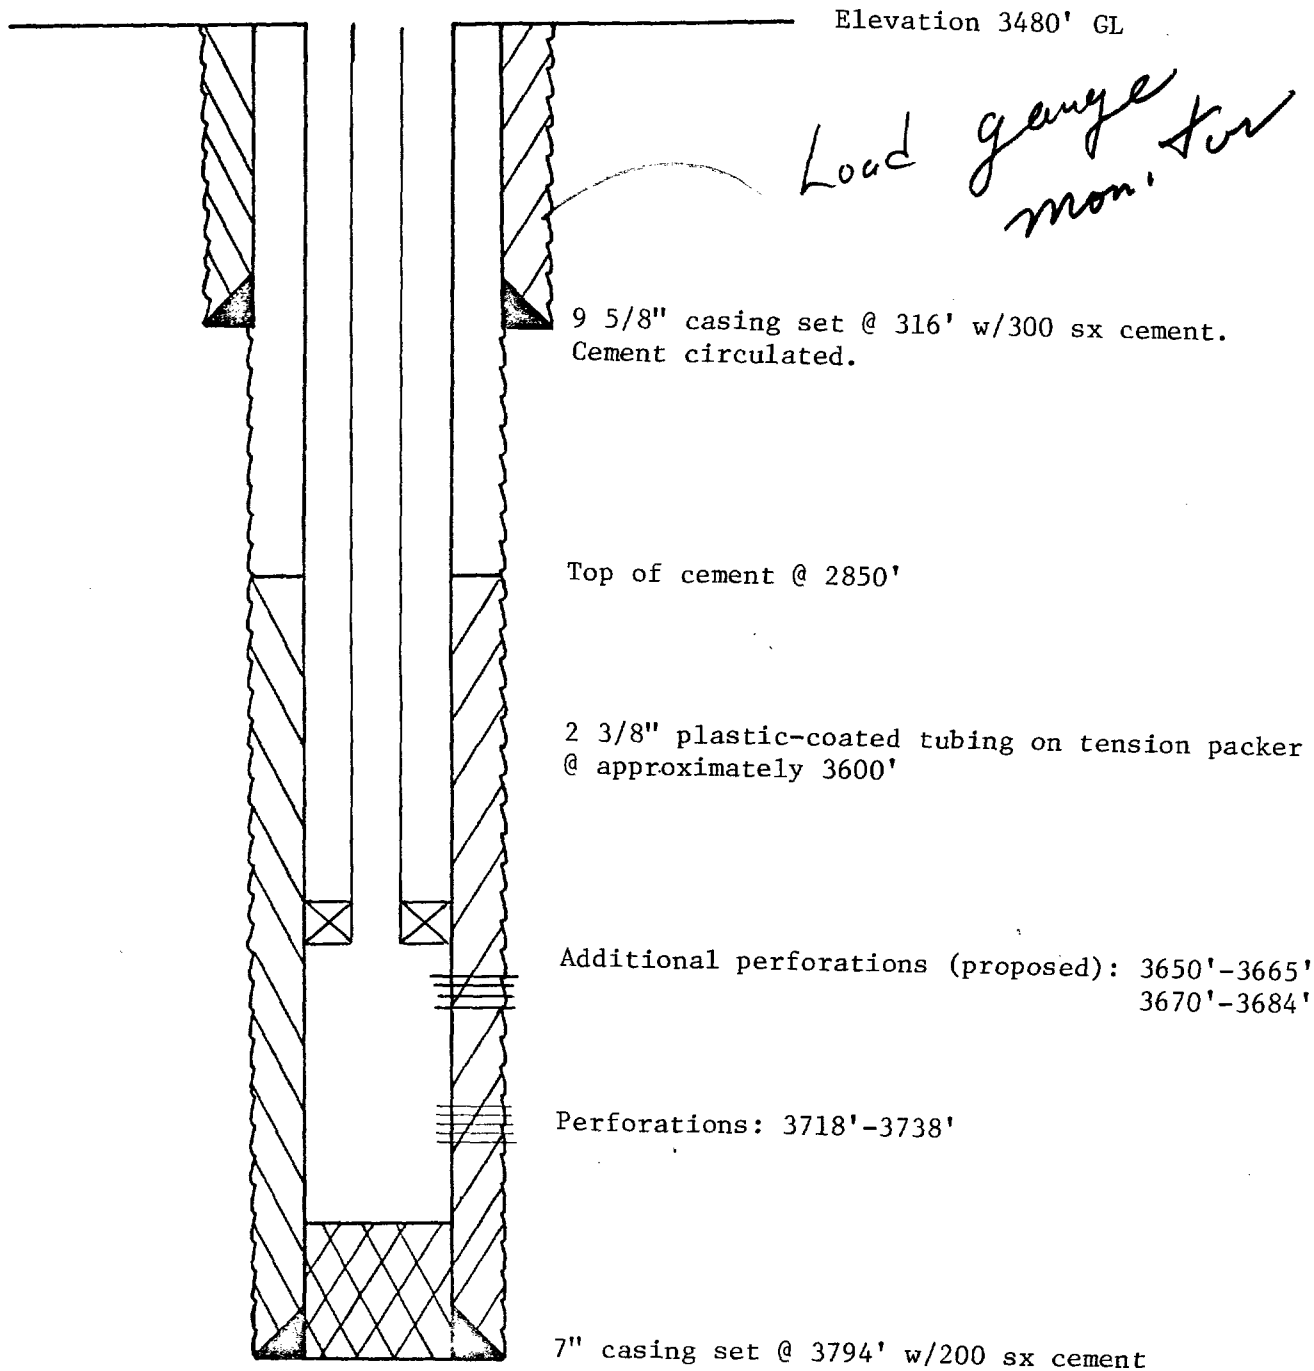

PBTD: 3772'

TD: 3795'

BEFORE EXAMINER STAMETS  
OIL CONSERVATION COMMISSION  
APPN EXHIBIT NO. 3  
CASE NO. 5258  
Submitted by TP  
Hearing Date 6/19/74

TEXAS PACIFIC OIL CO., INC.  
STATE A ACCT. 1 WELL NO. 44  
SEC. 4, T-23-S, R-36-E  
660' FNL AND 1980' FEL  
LANGLIE MATTIX POOL  
LEA COUNTY, NEW MEXICO  
COMPLETION DATE: 1/27/59

Elevation 3462' GL

8 5/8" casing set @ 328' w/300 sx cement.  
Cement circulated.

Top of cement @ 2785'

2 3/8" tubing w/SN @ 3700'

Additional perforations (proposed): 3628'-3634'  
3646'-3658'

Perforations 3700'-3712'  
3740'-3750'

5 1/2" casing set @ 3800' w/250 sx cement.

PBTD: 3790'

TD: 3800'

BEFORE EXAMINER STAMETS  
OIL CONSERVATION COMMISSION  
APPN EXHIBIT NO. 4  
CASE NO. 5258  
Submitted by TF  
Hearing Date 6/19/74

TEXAS PACIFIC OIL CO., INC.  
STATE A ACCT. 1 WELL NO. 45  
SEC. 4, T-23-S, R-36-E  
1980' FNL AND 660' FEL  
LANGLIE MATTIX POOL  
LEA COUNTY, NEW MEXICO  
COMPLETION DATE: 2/21/59

Elevation 3467' GL

9 5/8" casing set @ 315' w/300 sx cement  
Cement circulated

Top of cement @ 2315'

2 3/8" tubing w/SN @ 3710'

Additional perforations (proposed): 3636'-3644'  
3654'-3668'

Perforations 3706'-3722'  
3740'-3750'

7" casing set @ 3799' w/250 sx cement

PBTD: 3786'

TD: 3800'

BEFORE EXAMINER STAMETS  
OIL CONSERVATION COMMISSION


APPN EXHIBIT NO. 5  
CASE NO. 5258

Submitted by TP

Hearing Date 6/19/74

TEXAS PACIFIC OIL CO., INC.  
STATE A ACCT. 1 WELL NO. 87  
SEC. 4, T-23-S, R-36-E  
1980' FNL AND 1980' FEL  
JALMAT OIL POOL  
LEA COUNTY, NEW MEXICO  
COMPLETION DATE: 7/4/60

Elevation 3476' GL

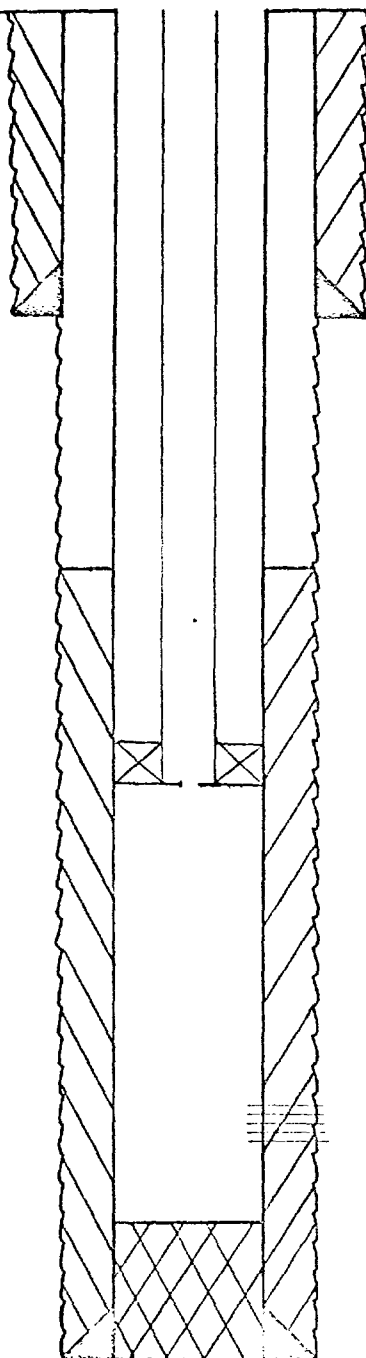

9 5/8" casing @ 316' w/300 sx cement  
Cement circulated

Top of cement @ 2360'

2 7/8" tubing on tension anchor w/SN @ 2300'

*Jalmat  
only*

Perforations 3646'-3655'  
3666'-3675'

Perforations @ 3763'-3768' were squeezed off  
w/250 sx cement.

7" casing set @ 3777' w/250 sx cement

PBTD: 3754'

TD: 3777'

BEFORE EXAMINER STAMETS  
OIL CONSERVATION COMMISSION

APPN EXHIBIT NO. 6  
CASE NO. 5258

Submitted by T.P.

Hearing Date 6/17/74
