




Western Drilling, Inc.
415 W. Wall Street, Suite 1750, Midland, TX 79701
Ph. (432) 683-1700 Fax (432) 683-1703

INCLINATION REPORT

DATE: 04/19/2011


WELL NAME AND NUMBER: East Turkey Track Fed Com #6H
API NUMBER: 30-015-38416
COUNTY: Eddy
STATE: New Mexico
LOCATION: Section 26-T18S-R29E
OPERATOR: MYCO Industries, Inc.
DRILLING CONTRACTOR: Western Drilling, Inc.



The undersigned hereby certifies that they are an authorized representative of the drilling contractor who drilled the above described well and that he has conducted deviation tests and obtained the following results:

DEV.:	DIR.:	DEPTH:	DEV.:	DIR.:	DEPTH:
2.00		286'	91.43	260.06	8,452'
1.00		830'	91.78	270.66	8,829'
1.75		1,303'	92.13	270.77	9,302'
1.00		1,776'	91.78	268.29	9,771'
0.25		2,275'	94.17	268.05	10,242'
1.00		2,742'	93.61	268.02	10,336'
1.00		3,001'	91.50	267.90	10,714'
1.00		3,513'	91.36	269.51	11,092'
0.75		4,012'	92.00	269.13	11,238'
0.50		4,455'	91.36	271.03	11,712'
1.25		5,021'	91.95	270.40	11,965'
3.75		5,522'	92.20	270.00	12,250'
3.75		5,707'	91.99	271.46	12,625'
2.70	240.04	6,234'	92.13	271.56	12,730'
2.64	227.32	6,517'			
0.21	296.09	7,081'			
0.54	234.47	7,364'			
30.56	268.71	7,854'			
51.80	269.56	8,042'			
70.41	268.46	8,167'			

Drilling Contractor:




Western Drilling, Inc.

By:
Marty K. Green
Contract Administrator

Subscribed and sworn to before me on this 19th day of April, 2011.

By:



MYCO

Santo Nino
Eddy County, NM
East Turkey Track Federal Com #6H
VH - Job #32K0311228

Survey: Actual

SDI Standard Survey Report

15 April, 2011

This survey is correct to the best of my knowledge and is supported by actual field data.

Hubert

Notarized this date 14th of April, 2011.

Carrie Reed

Notary Signature
County of Midland
State of Texas



Scientific Drilling
Directional Drilling Operations

Scientific Drilling International, Inc.

SDI Standard Survey Report



Company:	MYCO	Local Co-ordinate Reference:	Well East Turkey Track Federal Com #6H
Project:	Santo Nino	TVD Reference:	WELL @ 0 0usft (Original Well Elev)
Site:	Eddy County, NM	MD Reference:	WELL @ 0 0usft (Original Well Elev)
Well:	East Turkey Track Federal Com #6H	North Reference:	Grid
Wellbore:	VH - Job #32K0311228	Survey Calculation Method:	Minimum Curvature
Design:	VH - Job #32K0311228	Database:	EDM-Regulatory

Project	Santo Nino		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Site		Eddy County, NM			
Site Position:		Northing:	624,568 16 usft	Latitude:	32° 43' 0 059 N
From:	Lat/Long	Easting:	591,330 94 usft	Longitude:	104° 2' 10.968 W
Position Uncertainty:	0 0 usft	Slot Radius:	13-3/16"	Grid Convergence:	0 16 °

Well	East Turkey Track Federal Com #6H, Directional (Weatherford)					
Well Position	+N/-S	0 0 usft	Northing:	624,568 16 usft	Latitude:	32° 43' 0 059 N
	+E/-W	0 0 usft	Easting:	591,330 94 usft	Longitude:	104° 2' 10 968 W
Position Uncertainty		0 0 usft	Wellhead Elevation:	usft	Ground Level:	0 0 usft

Wellbore		VH - Job #32K0311228				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)	
-	IGRF2010	3/12/2011	7 87	60 57	-	48.913

Design	VH - Job #32K0311228			
Audit Notes:				
Version:	1 0	Phase:	ACTUAL	Tie On Depth: 0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0 0	0 0	0 0	269 00

Survey Program		Date 3/16/2011		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description
100 0	5,723 0	Actual (VH - Job #32K0311228)	Keeper	Keeper Gyro

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	True Vertical Depth	North/South (usft)	East/West (usft)	Closure Azimuth (°)	Closure Distance (usft)		
0 0	0 00	0 00	0.0	0 0	0 0	0 0	0 00		0 0
100 0	0 36	339.65	100 0	0 3	-0 1	339 65			0.3
200 0	1 70	40 88	200.0	1 7	0 8	23 74			1 9
300 0	1 42	42 75	299 9	3 7	2 6	34 42			4 5
400 0	1 27	43 15	399 9	5 5	4 2	37 32			6 9
500 0	1 25	49.74	499 9	7 0	5 8	39 52			9 0
600.0	1 28	51 07	599 9	8 4	7 5	41 65			11 2
700 0	1 33	50 87	699.8	9 8	9 2	43.22			13 5
800 0	1 58	56 90	799 8	11 3	11 3	44 95			16 0
900 0	2 00	68 07	899 8	12 7	14 1	47 88			18 9
1,000 0	2 29	68 96	999 7	14 1	17 5	51 25			22.5
1,100 0	2 35	69 86	1,099 6	15 5	21 3	53 99			26 4

Scientific Drilling International, Inc.
SDI Standard Survey Report



Company:	MYCO	Local Co-ordinate Reference:	Well East Turkey Track Federal Com #6H
Project:	Santo Nino	TVD Reference:	WELL @ 0 0usft (Original Well Elev)
Site:	Eddy County, NM	MD Reference:	WELL @ 0 0usft (Original Well Elev)
Well:	East Turkey Track Federal Com #6H	North Reference:	Grid
Wellbore:	VH - Job #32K0311228	Survey Calculation Method:	Minimum Curvature
Design:	VH - Job #32K0311228	Database:	EDM-Regulatory

Survey								
Measured Depth (usft)	Inclination (°)	Azimuth (°)	True Vertical Depth	North/South (usft)	East/West (usft)	Closure Azimuth (°)	Closure Distance (usft)	
1,200 0	2 33	70 37	1,199 5	16 9	25 2	56 14	30 3	
1,300 0	2 32	72 92	1,299 4	18 2	29 0	57 95	34 2	
1,400 0	2 11	75 31	1,399 4	19 2	32 7	59 57	38 0	
1,500 0	1 85	75 30	1,499 3	20 1	36 1	60 87	41 3	
1,600 0	1 58	75 07	1,599 3	20 9	39 0	61 83	44 2	
1,700 0	1 30	72 40	1,699 2	21 6	41 4	62 47	46 7	
1,800 0	1 13	71 01	1,799 2	22 2	43 4	62 88	48 8	
1,900 0	1 02	73 01	1,899 2	22 8	45 2	63 21	50 6	
2,000 0	0 98	74 60	1,999 2	23 3	46 9	63 56	52 3	
2,100 0	0 96	82 44	2,099 2	23 6	48 5	64 02	54 0	
2,200 0	1 01	82 37	2,199 1	23 9	50 2	64 58	55 6	
2,300 0	0 93	80 97	2,299 1	24 1	51 9	65 08	57 2	
2,400 0	1 05	81 56	2,399 1	24 4	53 6	65 55	58 9	
2,500 0	0 93	86 95	2,499 1	24 5	55 3	66 07	60 5	
2,600 0	0 79	85 60	2,599 1	24 6	56 8	66 55	61 9	
2,700 0	0 77	87 48	2,699 1	24 7	58 2	66 97	63 2	
2,800 0	0 74	92 76	2,799 1	24 7	59 5	67 43	64 4	
2,900 0	0 62	83 83	2,899 1	24 7	60 7	67 81	65 5	
3,000 0	0 67	86 83	2,999 1	24 8	61 8	68 10	66 6	
3,100 0	0 55	48 88	3,099 1	25 2	62 7	68 12	67 6	
3,200 0	0 69	40 55	3,199 1	26 0	63 5	67 76	68 6	
3,300 0	0 72	53 18	3,299 0	26 8	64 4	67 40	69 7	
3,400 0	0 68	40 82	3,399 0	27 6	65 3	67 06	70 9	
3,500 0	0 65	50 83	3,499 0	28 4	66 1	66 73	72 0	
3,600 0	0 49	70 42	3,599 0	28 9	66 9	66 63	72 9	
3,700 0	0 46	56 46	3,699 0	29 3	67 7	66 60	73 7	
3,800 0	0 53	51 96	3,799 0	29 8	68 4	66 45	74 6	
3,900 0	0 46	56 03	3,899 0	30 3	69 1	66 31	75 4	
4,000 0	0 35	47 90	3,999 0	30 7	69 6	66 18	76 1	
4,100 0	0 26	33 41	4,099 0	31 1	70 0	66 02	76 6	
4,200 0	0 10	160 28	4,199 0	31 2	70 1	65 99	76 8	
4,300 0	0 42	227 77	4,299 0	30 9	69 9	66 14	76 4	
4,400 0	0 57	244 94	4,399 0	30 5	69 2	66 24	75 6	
4,500 0	0 85	232 94	4,499 0	29 8	68 1	66 38	74 4	
4,600 0	0 99	256 52	4,599 0	29 1	66 7	66 39	72 8	
4,700 0	1 11	251 56	4,699 0	28 6	64 9	66 20	71 0	
4,800 0	1 32	245 38	4,798 9	27 9	63 0	66 14	68 9	
4,900 0	1 16	257 19	4,898 9	27 2	60 9	65 99	66 7	
5,000 0	1 27	259 51	4,998 9	26 7	58 9	65 58	64 6	
5,100 0	1 48	253 89	5,098 9	26 2	56 5	65 17	62 3	
5,200 0	1 73	246 49	5,198 8	25 2	53 9	64 94	59 5	
5,300 0	1 75	246 83	5,298 8	24 0	51 1	64 85	56 5	
5,400 0	2 38	240 45	5,398 7	22 4	47 9	64 97	52 9	
5,500 0	3 10	257 94	5,498 6	20 8	43 5	64 44	48 2	

Scientific Drilling International, Inc.

SDI Standard Survey Report



Company:	MYCO	Local Co-ordinate Reference:	Well East Turkey Track Federal Com #6H
Project:	Santo Nino	TVD Reference:	WELL @ 0 0usft (Original Well Elev)
Site:	Eddy County, NM	MD Reference:	WELL @ 0 0usft (Original Well Elev)
Well:	East Turkey Track Federal Com #6H	North Reference:	Grid
Wellbore:	VH - Job #32K0311228	Survey Calculation Method:	Minimum Curvature
Design:	VH - Job #32K0311228	Database:	EDM-Regulatory

Survey							
Measured Depth (usft)	Inclination (°)	Azimuth (°)	True Vertical Depth	North/South (usft)	East/West (usft)	Closure Azimuth (°)	Closure Distance (usft)
5,600 0	3 34	264 39	5,598 4	19 9	37 9	62 27	42 8
5,700 0	3 13	262 04	5,698 3	19 3	32 3	59 19	37 6
5,723 0	3 07	262 51	5,721 3	19 1	31 1	58 42	36 5




Project: Santo Nino
Eddy County, NM
Well: East Turley Track Federal Com #6H
Wellbore: VH - Job #32K0311228
Design: VH - Job #32K0311228



Azimuths to Grid North
True North: -0 16°
Magnetic North: 7 77°
Magnetic Field
Strength: 48945 1snT
Dip Angle: 60 58°
Date: 3/12/2011
Model: BGM2010

WELL DETAILS: East Turley Track Federal Com #6H
WELL @ 0.0usft (Original Well Elev)

+N/-S	+E/-W	Northing	Easting	Latitude	Longitude	Slot
0.0	0.0	624568.16	591330.94	32° 43' 0.059 N	104° 2' 10.968 W	

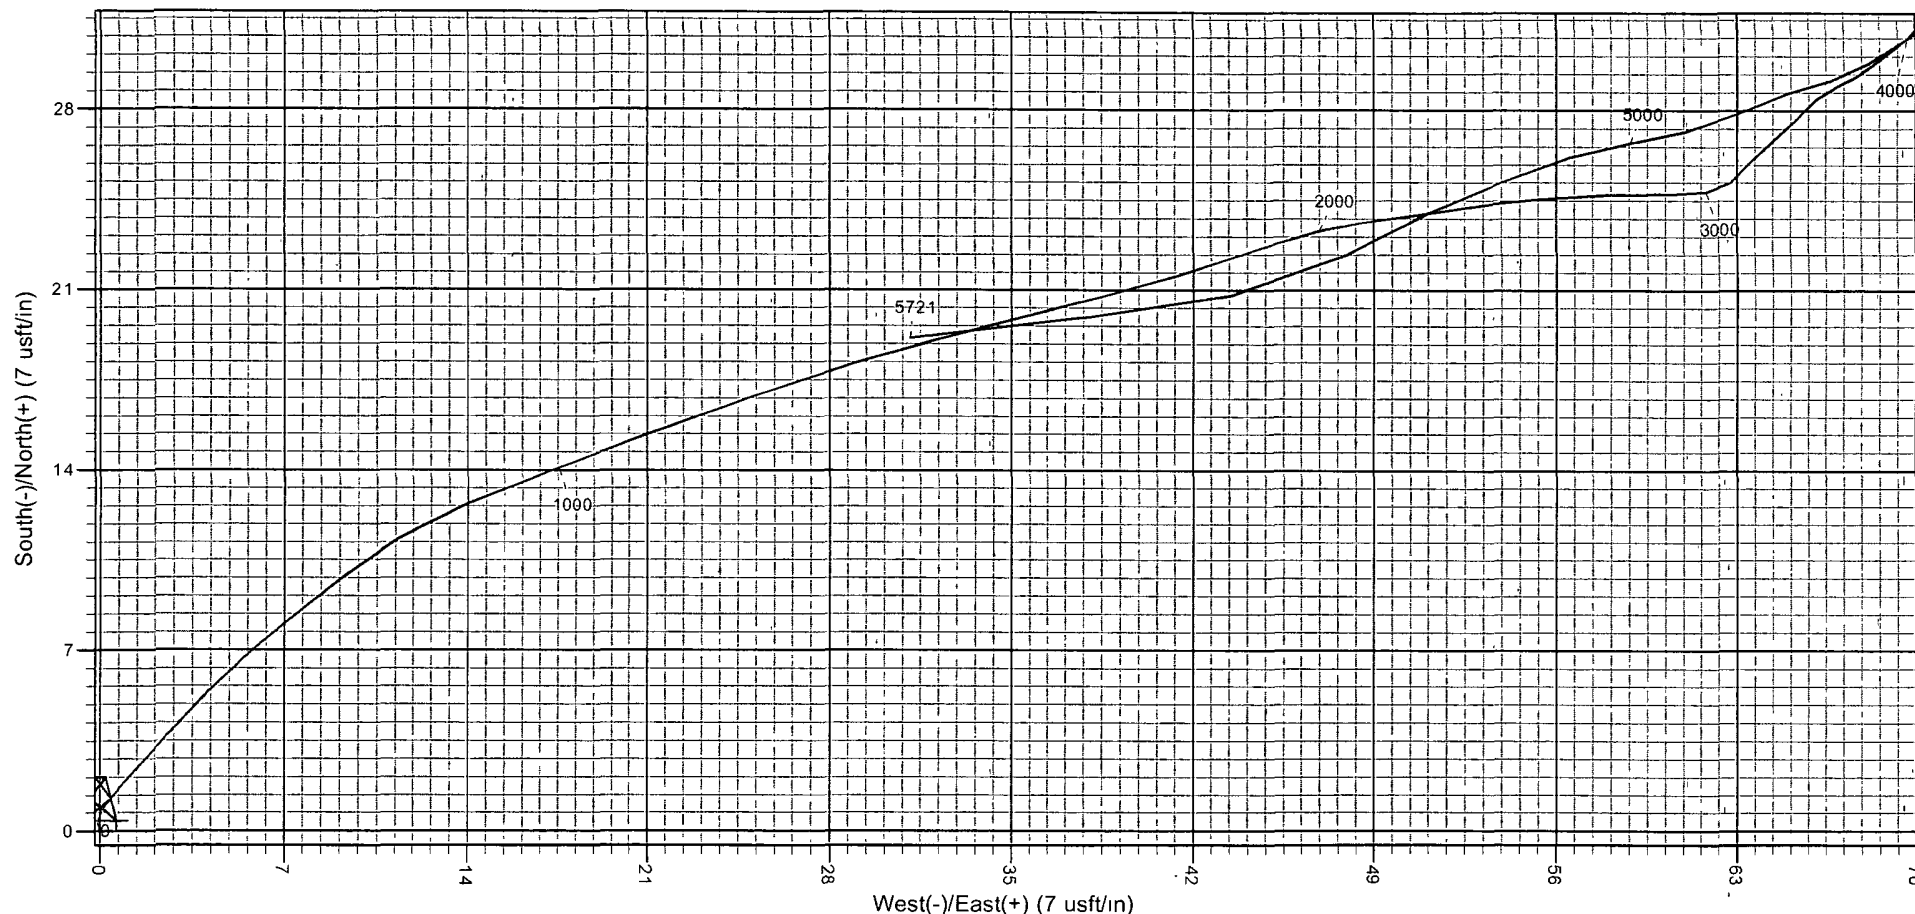

PROJECT DETAILS: Santo Nino
Geodetic System: US State Plane 1927 (Exact solution)
Datum: NAD 1927 (NADCON CONUS)
Ellipsoid: Clarke 1866
Zone: New Mexico East 3001
System Datum: Mean Sea Level

SITE DETAILS: Eddy County, NM
Site Centre Latitude: 32° 43' 0.059 N
Longitude: 104° 2' 10.968 W
Positional Uncertainty: 0.0
Convergence: 0 16
Local North: Grid



Weatherford®

SURVEY REPORT

Report Date: 4/8/2011

Customer: MYCO Industries

Field: Eddy County

Job Name: East Turkey Track Fed

Rig: Western Drilling # 3

Well Name: East Turkey Track Federal

Rig Loc: Eddy County

Survey Calculation Method: Minimum Curvature						
Magnetic Reference	Target Direction	Total Magnetic Field	Magnetic Dip Angle	Magnetic Declination	Grid Convergence	Total Correction
Grid North	269.22 deg	48908 nT	60.57 deg	7.87 deg	0.16 deg	7.71 deg
Survey Tie-On	Depth	INC	AZ	TVD	NS	EW
	5723.00 ft	3.07 deg	262.51 deg	5721.26 ft	19.10 ft	31.09 ft

Depth (ft)	Inc (deg)	Azm (deg)	TVD (ft)	Well Head		VSect (ft)	Dogleg (deg/100ft)
				NS (ft)	EW (ft)		
5827.00	2.72	272.81	5825.13	18.86	25.86	-26.12	0.60
5890.00	2.71	266.64	5888.06	18.84	22.88	-23.14	0.46
5984.00	3.13	256.36	5981.94	18.11	18.17	-18.41	0.72
6045.00	3.30	256.08	6042.84	17.29	14.84	-15.08	0.28
6140.00	2.82	255.73	6137.70	16.06	9.93	-10.14	0.51
6234.00	2.70	240.04	6231.60	14.38	5.77	-5.96	0.81
6328.00	2.97	241.80	6325.48	12.12	1.70	-1.87	0.30
6423.00	2.81	231.54	6420.36	9.51	-2.29	2.16	0.57
6517.00	2.64	227.32	6514.25	6.61	-5.69	5.60	0.28
6612.00	1.44	218.21	6609.19	4.19	-8.04	7.98	1.31
6707.00	1.75	217.73	6704.16	2.11	-9.66	9.63	0.33
6800.00	1.16	196.85	6797.13	0.09	-10.80	10.80	0.84
6895.00	0.69	227.68	6892.11	-1.22	-11.51	11.52	0.70
6988.00	0.60	243.89	6985.11	-1.81	-12.36	12.38	0.22
7081.00	0.25	296.09	7078.11	-1.93	-12.97	13.00	0.52
7176.00	0.27	280.11	7173.10	-1.81	-13.37	13.40	0.08
7270.00	0.33	273.70	7267.10	-1.75	-13.86	13.88	0.08
7364.00	0.54	234.47	7361.10	-1.99	-14.49	14.52	0.37
7460.00	0.54	203.63	7457.10	-2.66	-15.04	15.07	0.30
7554.00	0.27	197.90	7551.09	-3.27	-15.28	15.32	0.29
7603.00	0.25	194.55	7600.09	-3.48	-15.34	15.39	0.05
7665.00	5.50	258.52	7662.00	-4.20	-18.29	18.34	8.70
7696.00	9.31	265.17	7692.73	-4.71	-22.24	22.31	12.60
7728.00	13.68	262.61	7724.08	-5.41	-28.58	28.65	13.74
7759.00	17.91	262.00	7753.91	-6.55	-36.94	37.03	13.66
7791.00	21.86	263.74	7783.99	-7.88	-47.74	47.84	12.46
7823.00	26.17	267.88	7813.22	-8.80	-60.72	60.84	14.47
7854.00	30.56	268.71	7840.49	-9.23	-75.44	75.56	14.21
7885.00	35.16	269.90	7866.52	-9.42	-92.26	92.37	14.99
7916.00	37.62	269.87	7891.47	-9.46	-110.65	110.76	7.91
7948.00	39.89	270.04	7916.43	-9.47	-130.67	130.79	7.10
7979.00	43.81	270.49	7939.51	-9.37	-151.35	151.47	12.68
8011.00	47.18	270.40	7961.94	-9.20	-174.17	174.28	10.54
8042.00	51.80	269.56	7982.07	-9.21	-197.73	197.84	15.06
8074.00	56.44	268.85	8000.82	-9.57	-223.65	223.76	14.60


Depth (ft)	Inc (deg)	Azm (deg)	TVD (ft)	Well Head		VSect (ft)	Dogleg (deg/100ft)
				NS (ft)	EW (ft)		
8104.00	60.37	267.97	8016.54	-10.29	-249.19	249.31	13.34
8135.00	65.18	268.72	8030.72	-11.08	-276.74	276.86	15.64
8167.00	70.41	268.46	8042.81	-11.81	-306.34	306.47	16.38
8198.00	75.97	269.21	8051.77	-12.41	-336.00	336.14	18.07
8230.00	82.10	270.04	8057.85	-12.62	-367.40	367.54	19.33
8261.00	86.82	269.81	8060.85	-12.66	-398.24	398.38	15.25
8356.00	89.83	269.35	8063.63	-13.36	-493.19	493.33	3.20
8388.00	90.24	269.10	8063.61	-13.80	-525.19	525.33	1.52
8420.00	91.08	268.24	8063.24	-14.54	-557.18	557.32	3.74
8452.00	91.43	268.06	8062.53	-15.57	-589.15	589.31	1.24
8483.00	92.06	267.30	8061.59	-16.83	-620.11	620.28	3.17
8513.00	92.56	267.18	8060.38	-18.27	-650.05	650.24	1.69
8543.00	93.04	267.89	8058.91	-19.56	-679.99	680.19	2.88
8575.00	93.11	267.86	8057.20	-20.74	-711.92	712.14	0.24
8607.00	92.55	268.34	8055.61	-21.80	-743.86	744.09	2.31
8638.00	92.48	269.06	8054.25	-22.51	-774.83	775.06	2.33
8670.00	92.48	268.87	8052.87	-23.08	-806.79	807.03	0.58
8701.00	91.92	269.40	8051.67	-23.55	-837.76	838.01	2.46
8734.00	92.48	269.07	8050.41	-23.99	-870.74	870.98	1.95
8765.00	91.92	269.73	8049.21	-24.31	-901.71	901.96	2.79
8797.00	91.92	270.57	8048.14	-24.23	-933.69	933.94	2.61
8829.00	91.78	270.66	8047.10	-23.89	-965.67	965.91	0.51
8860.00	91.78	270.33	8046.14	-23.62	-996.66	996.89	1.05
8892.00	91.92	270.40	8045.10	-23.42	-1028.64	1028.86	0.49
8923.00	92.06	270.48	8044.03	-23.18	-1059.62	1059.84	0.52
8954.00	92.20	270.58	8042.87	-22.89	-1090.60	1090.81	0.55
8986.00	91.71	270.70	8041.78	-22.54	-1122.58	1122.78	1.57
9018.00	91.64	270.92	8040.84	-22.08	-1154.56	1154.75	0.74
9080.00	92.00	270.53	8038.87	-21.30	-1216.52	1216.70	0.85
9144.00	91.57	270.93	8036.88	-20.48	-1280.49	1280.65	0.91
9176.00	91.50	270.81	8036.02	-19.99	-1312.47	1312.62	0.43
9239.00	91.92	271.07	8034.13	-18.96	-1375.43	1375.57	0.78
9270.00	91.99	270.87	8033.07	-18.44	-1406.41	1406.53	0.69
9302.00	92.13	270.77	8031.92	-17.98	-1438.39	1438.50	0.53
9333.00	92.41	270.93	8030.69	-17.52	-1469.36	1469.46	1.04
9365.00	91.79	270.98	8029.52	-16.98	-1501.33	1501.43	1.96
9397.00	91.22	270.66	8028.68	-16.53	-1533.32	1533.40	2.03
9428.00	91.85	271.26	8027.85	-16.01	-1564.30	1564.38	2.82
9460.00	91.50	270.33	8026.91	-15.56	-1596.29	1596.35	3.12
9492.00	91.36	269.90	8026.11	-15.50	-1628.28	1628.34	1.40
9555.00	91.66	270.50	8024.45	-15.28	-1691.25	1691.30	1.06
9586.00	91.93	269.56	8023.48	-15.26	-1722.24	1722.29	3.16
9616.00	92.13	269.41	8022.41	-15.53	-1752.22	1752.27	0.85
9647.00	91.71	269.02	8021.37	-15.96	-1783.20	1783.25	1.86
9679.00	91.64	268.26	8020.43	-16.72	-1815.17	1815.23	2.39
9709.00	91.78	268.49	8019.54	-17.57	-1845.15	1845.22	0.90
9741.00	91.36	268.24	8018.66	-18.48	-1877.12	1877.20	1.53
9771.00	91.78	268.29	8017.83	-19.39	-1907.10	1907.19	1.41
9803.00	90.74	267.46	8017.13	-20.58	-1939.07	1939.17	4.19
9834.00	89.97	267.22	8016.94	-22.02	-1970.03	1970.15	2.60

Depth (ft)	Inc (deg)	Azm (deg)	TVD (ft)	Well Head		VSect (ft)	Dogleg (deg/100ft)
				NS (ft)	EW (ft)		
9866.00	89.76	267.04	8017.02	-23.62	-2001.99	2002.13	0.86
9897.00	90.52	266.74	8016.94	-25.30	-2032.95	2033.10	2.67
9929.00	91.57	266.77	8016.36	-27.11	-2064.89	2065.07	3.28
9960.00	92.56	266.51	8015.24	-28.93	-2095.82	2096.02	3.28
9991.00	92.91	266.46	8013.76	-30.83	-2126.72	2126.95	1.14
10023.00	93.11	266.52	8012.08	-32.78	-2158.62	2158.87	0.68
10054.00	93.18	266.30	8010.38	-34.72	-2189.51	2189.78	0.75
10086.00	92.90	266.82	8008.68	-36.64	-2221.41	2221.70	1.85
10117.00	92.83	267.17	8007.13	-38.26	-2252.33	2252.64	1.14
10148.00	93.25	266.90	8005.49	-39.86	-2283.24	2283.57	1.61
10180.00	93.75	266.94	8003.53	-41.57	-2315.14	2315.49	1.54
10211.00	93.96	267.84	8001.45	-42.98	-2346.03	2346.40	2.96
10242.00	94.17	268.05	7999.25	-44.09	-2376.94	2377.32	0.95
10273.00	93.46	267.96	7997.19	-45.17	-2407.85	2408.24	2.29
10305.00	93.54	268.08	7995.24	-46.28	-2439.77	2440.17	0.45
10336.00	93.61	268.02	7993.31	-47.33	-2470.69	2471.11	0.29
10367.00	93.54	267.53	7991.38	-48.53	-2501.61	2502.04	1.61
10399.00	93.53	267.89	7989.41	-49.81	-2533.52	2533.96	1.15
10430.00	93.18	267.92	7987.59	-50.94	-2564.45	2564.90	1.13
10461.00	92.34	268.11	7986.10	-52.01	-2595.39	2595.86	2.79
10493.00	91.92	268.35	7984.90	-53.00	-2627.35	2627.83	1.50
10525.00	92.06	268.08	7983.79	-53.99	-2659.32	2659.81	0.94
10556.00	92.20	268.33	7982.64	-54.96	-2690.28	2690.78	0.91
10587.00	92.06	268.09	7981.48	-55.93	-2721.25	2721.76	0.87
10618.00	91.64	268.04	7980.48	-56.98	-2752.21	2752.73	1.37
10650.00	91.01	268.06	7979.74	-58.07	-2784.19	2784.72	1.97
10682.00	91.22	268.11	7979.11	-59.14	-2816.16	2816.71	0.68
10714.00	91.50	267.90	7978.35	-60.25	-2848.13	2848.69	1.09
10746.00	91.79	267.72	7977.43	-61.47	-2880.10	2880.67	1.04
10777.00	91.36	268.14	7976.58	-62.59	-2911.06	2911.65	1.91
10809.00	90.80	268.66	7975.98	-63.49	-2943.05	2943.64	2.39
10840.00	90.87	268.62	7975.52	-64.22	-2974.03	2974.63	0.27
10872.00	91.15	268.94	7974.95	-64.91	-3006.02	3006.63	1.34
10903.00	91.29	269.23	7974.29	-65.40	-3037.01	3037.62	1.05
10935.00	91.71	269.25	7973.45	-65.83	-3069.00	3069.61	1.31
10966.00	92.07	269.26	7972.43	-66.23	-3099.98	3100.59	1.13
10998.00	92.28	269.23	7971.22	-66.65	-3131.95	3132.57	0.66
11028.00	92.48	269.28	7969.97	-67.04	-3161.92	3162.54	0.72
11060.00	91.43	269.42	7968.88	-67.40	-3193.90	3194.52	3.31
11092.00	91.36	269.51	7968.10	-67.70	-3225.89	3226.51	0.34
11123.00	91.44	269.29	7967.34	-68.02	-3256.88	3257.50	0.74
11154.00	91.54	269.40	7966.53	-68.38	-3287.87	3288.49	0.49
11184.00	91.71	268.94	7965.68	-68.81	-3317.85	3318.48	1.63
11216.00	91.99	268.94	7964.65	-69.40	-3349.83	3350.46	0.87
11238.00	92.00	269.13	7963.88	-69.77	-3371.81	3372.45	0.88
11269.00	92.20	269.52	7962.75	-70.14	-3402.79	3403.43	1.41
11301.00	92.21	269.20	7961.51	-70.49	-3434.76	3435.41	1.01
11332.00	91.64	269.37	7960.47	-70.88	-3465.74	3466.39	1.90
11364.00	91.08	269.40	7959.71	-71.23	-3497.73	3498.38	1.75
11396.00	91.15	269.33	7959.09	-71.58	-3529.72	3530.37	0.31

Depth (ft)	Inc (deg)	Azm (deg)	TVD (ft)	Well Head		Vsect (ft)	Dogleg (deg/100ft)
				NS (ft)	EW (ft)		
11427.00	89.89	269.77	7958.80	-71.83	-3560.72	3561.37	4.30
11459.00	89.55	270.01	7958.96	-71.89	-3592.72	3593.37	1.33
11490.00	89.68	270.04	7959.17	-71.88	-3623.72	3624.36	0.46
11522.00	89.48	270.79	7959.40	-71.65	-3655.72	3656.35	2.44
11554.00	89.69	271.02	7959.63	-71.14	-3687.71	3688.34	0.97
11585.00	90.32	271.33	7959.63	-70.51	-3718.71	3719.32	2.26
11616.00	91.31	271.40	7959.19	-69.77	-3749.69	3750.30	3.23
11648.00	91.85	271.24	7958.31	-69.03	-3781.67	3782.26	1.75
11680.00	91.72	270.97	7957.31	-68.41	-3813.65	3814.23	0.95
11712.00	91.36	271.03	7956.45	-67.86	-3845.64	3846.20	1.11
11744.00	91.29	271.24	7955.71	-67.22	-3877.62	3878.18	0.71
11776.00	91.09	271.19	7955.05	-66.54	-3909.61	3910.15	0.67
11808.00	90.94	270.96	7954.48	-65.94	-3941.60	3942.13	0.84
11839.00	90.94	271.11	7953.97	-65.38	-3972.59	3973.11	0.49
11871.00	91.43	270.82	7953.31	-64.84	-4004.57	4005.09	1.79
11902.00	91.68	270.43	7952.46	-64.50	-4035.56	4036.07	1.50
11934.00	91.92	270.52	7951.46	-64.24	-4067.54	4068.04	0.81
11965.00	91.85	270.40	7950.43	-63.99	-4098.53	4099.02	0.44
11997.00	91.78	270.44	7949.42	-63.76	-4130.51	4130.99	0.26
12028.00	91.85	270.41	7948.44	-63.53	-4161.49	4161.97	0.25
12060.00	91.64	270.16	7947.46	-63.37	-4193.48	4193.95	1.02
12091.00	91.78	269.93	7946.53	-63.34	-4224.46	4224.93	0.87
12123.00	91.78	269.94	7945.53	-63.38	-4256.45	4256.92	0.04
12155.00	91.93	269.68	7944.50	-63.49	-4288.43	4288.90	0.93
12186.00	92.06	269.91	7943.42	-63.60	-4319.41	4319.88	0.87
12218.00	92.14	269.73	7942.25	-63.70	-4351.39	4351.85	0.63
12250.00	92.20	270.00	7941.04	-63.77	-4383.37	4383.83	0.88
12281.00	92.41	270.23	7939.79	-63.71	-4414.34	4414.80	1.00
12312.00	92.55	270.31	7938.44	-63.57	-4445.31	4445.77	0.52
12344.00	92.69	270.22	7936.98	-63.42	-4477.28	4477.73	0.52
12374.00	92.91	269.90	7935.51	-63.39	-4507.24	4507.69	1.29
12405.00	92.63	270.25	7934.02	-63.35	-4538.21	4538.65	1.46
12436.00	92.00	270.65	7932.77	-63.10	-4569.18	4569.62	2.41
12468.00	91.99	270.63	7931.65	-62.75	-4601.16	4601.59	0.08
12499.00	92.06	270.61	7930.56	-62.41	-4632.14	4632.56	0.23
12531.00	92.70	270.86	7929.23	-62.00	-4664.11	4664.52	2.13
12562.00	92.98	271.24	7927.69	-61.43	-4695.06	4695.47	1.53
12594.00	92.62	271.26	7926.13	-60.74	-4727.02	4727.41	1.13
12625.00	91.99	271.46	7924.88	-60.00	-4757.98	4758.36	2.14
12657.00	92.07	271.42	7923.75	-59.20	-4789.95	4790.32	0.26
12688.00	92.00	271.47	7922.65	-58.41	-4820.92	4821.27	0.27
12719.00	92.06	271.59	7921.55	-57.58	-4851.89	4852.23	0.43
12730.00	92.13	271.56	7921.15	-57.28	-4862.88	4863.21	0.71

Depth (ft)	Inc (deg)	Azm (deg)	TVD (ft)	Well Head		VSect (ft)	Dogleg (deg/100ft)
				NS (ft)	EW (ft)		

Vertical Section is 16194.65 ft along the target direction of 269.22 deg at a measured depth of 24078.77 ft
Horizontal Displacement is 16201.53 ft along the well bore azimuth of 270.89 deg.
The total correction is 7.71 deg relative to Grid North

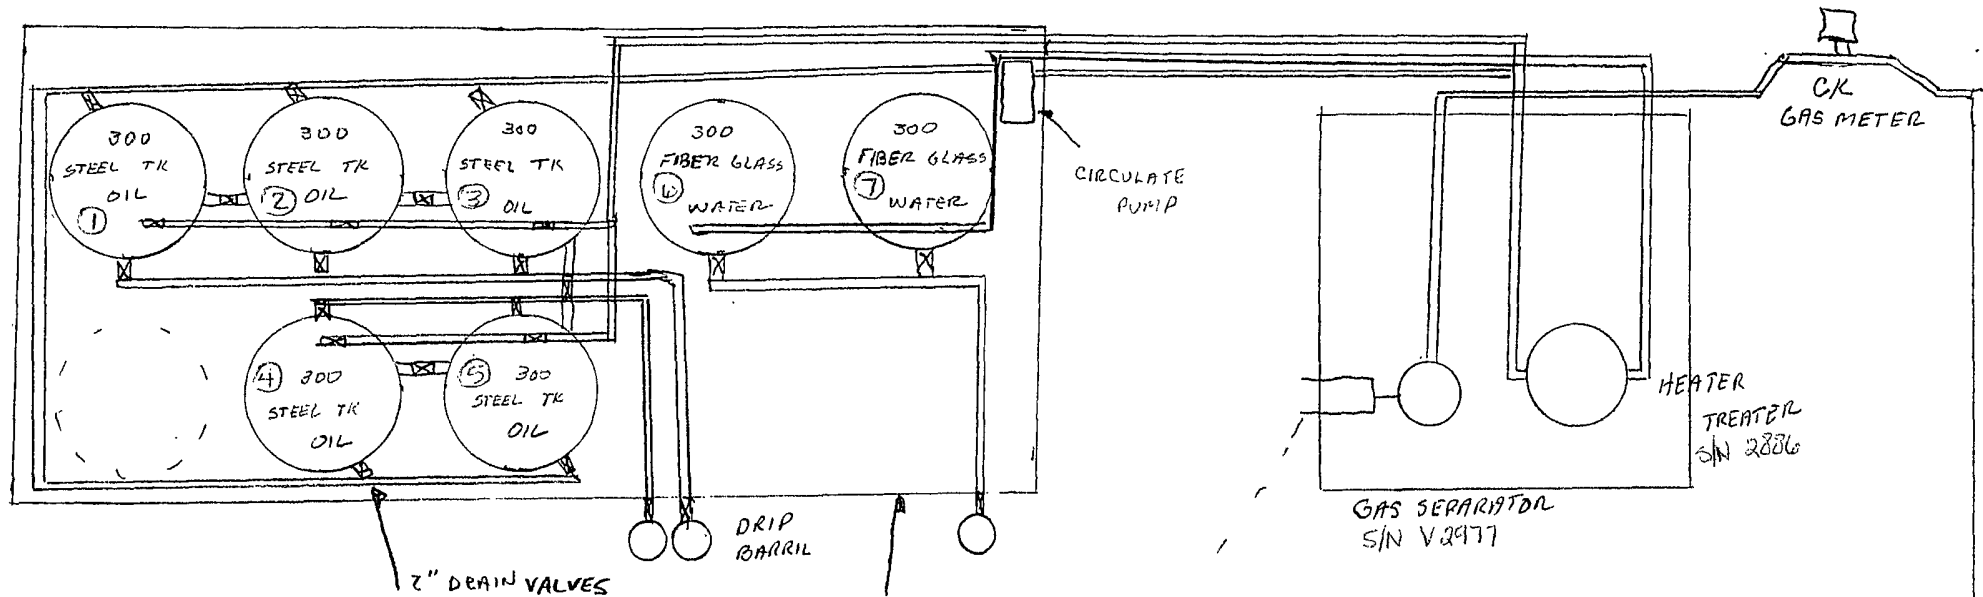

3" Ball VALVES - ISOLATED & SEALED DURING SALES
 FILL LINES
 EQUALIZE
 SALES

SECONDARY CONTAINMENT

1) - S/N 4074
 Tank # 284
 2) - S/N 4381
 Tank # 285
 3) - S/N 3622
 Tank # 286
 4) - S/N 4073
 Tank # 287
 5) - S/N 4430
 Tank # 288

6) - S/N 3282-06
 7) - S/N 3321-05

PUMP UNIT

WELL

FLOW LINE

MYCO INDUSTRIES, INC.
 EAST TURKEY TRACK FED. COM. 5-6H

COMMON TANK BATTERY

T18S - R29E - SEC 26

EDDY COUNTY, NM

API: 30-015-38415 #5H

API: 30-015-38416 #6H

GAS SALES

DCP
