

RECEIVED

JAN 29 2014

Daily Wellbore Schematics Report

1

ID: 30-015-27358


NMOCD ARTESIA

Well Name: G J WEST COOP UNIT #113

Event#: 800

Report Dates: 06/10/2013

WEST COOP UNIT #113 MD (ft)

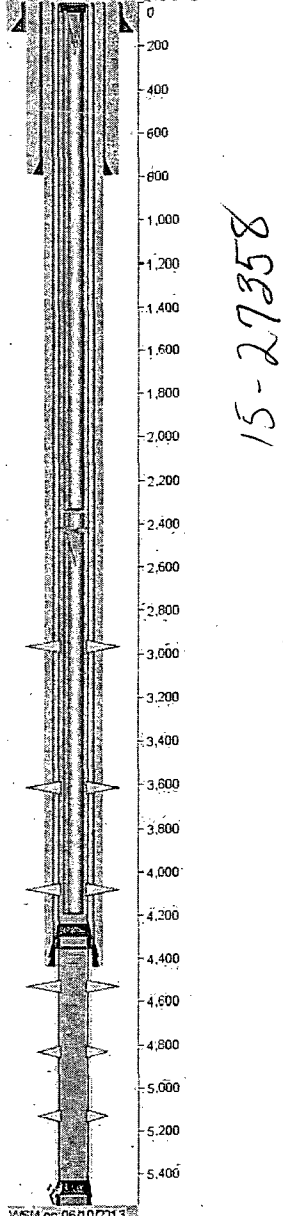

PIPE SPECIFICATION

STRING NAME	SECTION NAME	JOINT COUNT	START DEPTH	END DEPTH	LENGTH	OD SIZE	ID SIZE	WT GRDNT	GRD	CONN
SURFACE	CASING		0.00	132.00	132.00	13.38	12.71	48.0	H-40	
INTERMEDIATE #1	CASING		0.00	789.00	789.00	8.63	8.10	24.0	J-55	
PRODUCTION	FLOAT SHOE		4432.50	4434.00	1.50	5.50	4.89	17.0	J-55	
PRODUCTION	CASING	1	4390.50	4432.50	42.00	5.50	4.89	17.0	J-55	
PRODUCTION	FLOAT COLLAR	1	4389.00	4390.50	1.50	5.50	4.89	17.0	J-55	
PRODUCTION	CASING	1	0.00	4389.00	4389.00	5.50	4.89	17.0	J-55	
TUBING	SEAT NIPPLE		4235.90	4237.00	1.10	2.88	2.23	6.5	SEATIN	
TUBING	TUBING CERAMIC	1	4204.40	4235.90	31.50	2.88	2.44	6.5	J-55	
TUBING	TUBING	1	2418.40	4204.40	1786.00	2.88	2.44	6.5	J-55	
TUBING	TUBING ANCHOR	1	2415.40	2418.40	3.00	5.50	2.44	17.0	TUBING	
TUBING	TUBING	1	2352.40	2415.40	63.00	2.88	2.44	6.5	J-55	
TUBING	MARKER JOINT	1	2350.40	2352.40	2.00	2.88	2.44	6.5	J-55	
TUBING	TUBING	1	0.00	2350.40	2350.40	2.88	2.44	6.5	J-55	
PRODUCTION LINER	FLOAT SHOE		5543.55	5545.00	1.45	4.00	3.43	11.6	UTFJ L-	UTFJ
PRODUCTION LINER	CASING	1	5499.60	5543.55	43.95	4.00	3.43	11.6	UTFJ L-	UTFJ
PRODUCTION LINER	FLOAT COLLAR		5497.95	5499.60	1.65	4.00	3.43	11.6	UTFJ L-	UTFJ
PRODUCTION LINER	CASING	27	4351.07	5497.95	1146.88	4.00	3.43	11.6	UTFJ L-	UTFJ
PRODUCTION LINER	CENTRALIZER		4349.70	4351.07	1.37	4.00	3.43	11.6	UTFJ L-	UTFJ
PRODUCTION LINER	CASING	1	4306.16	4349.70	43.54	4.00	3.43	11.6	UTFJ L-	UTFJ
PRODUCTION LINER	STAGE TOOL		4303.11	4306.16	3.05	4.00	3.43	11.6	UTFJ L-	UTFJ
PRODUCTION LINER	CASING	1	6.00	4303.11	4297.11	4.00	3.43	11.6	UTFJ L-	UTFJ
PRODUCTION LINER	CROSS OVER UP		10.00	13.07	3.07	4.00	3.43	11.6	UTFJ L-	UTFJ
PRODUCTION LINER	KB		0.00	10.00	10.00					

CEMENTING

STRING NAME	STAGE #	LEAD TOP (est) (ft)	LEAD TOP (ver) (ft)	TAIL TOP (est) (ft)	TAIL TOP (ver) (ft)
SURFACE	1	0.0	0.0		
INTERMEDIATE #1	1	0.0	0.0		
PRODUCTION	1	0.0	0.0		
PRODUCTION LINER	1	4303.0	4303.0		
PRODUCTION LINER	2				

BHA STRING

DRILL EQUIP CODE	DESCRIPTION	LENGTH	OD SIZE	ID SIZE
------------------	-------------	--------	---------	---------

PERFORATION

ZONE	JOB REPORT DATE	ZONE NAME	TOP DEPTH	BOTTOM DEPTH	HOLE SIZE	PEN SIZE	SQUEEZED
1	04/29/1993	SAN ANDRES	2599.00	3330.00			N
2	04/29/1993	LOWER BLINEBRY	3613.00	3619.00			N

ID: 30-015-27358

Well Name: G J WEST COOP UNIT #113

Event#: 800

Report Dates: 06/10/2013

PERFORATION							
ZONE	JOB REPORT DATE	ZONE NAME	TOP DEPTH	BOTTOM DEPTH	HOLE SIZE	PEN SIZE	SQUEEZED
2	04/29/1993	LOWER BLINEBRY	3962.00	4200.00			N
2	05/28/2013	LOWER BLINEBRY	5030.00	5230.00	0.41	13.00	N
3	05/30/2013	MIDDLE BLINEBRY	4730.00	4930.00	0.41	13.00	N
4	05/30/2013	UPPER BLINEBRY	4430.00	4630.00	0.41	13.00	N
