

Submit 3 Copies To Appropriate District
Office
District I
1625 N French Dr., Hobbs, NM 88240
District II
1301 W Grand Ave., Artesia, NM 88210
District III
1000 Rio Brazos Rd., Aztec, NM 87410
District IV
1220 S St. Francis Dr., Santa Fe, NM
87505

State of New Mexico
Energy, Minerals and Natural Resources

Form C-103
May 27, 2004

OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505



WELL API NO. 30-015-36651
5. Indicate Type of Lease STATE ☐ FEE ☒
6. State Oil & Gas Lease No.
7. Lease Name or Unit Agreement Name Cass Draw 30
8. Well Number 2
9. OGRID Number 14744
10. Pool name or Wildcat Dublin Ranch Morrow

SUNDRY NOTICES AND REPORTS ON WELLS
(DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS)

1. Type of Well: Oil Well ☐ Gas Well ☒ Other

2. Name of Operator
Mewbourne Oil Company

3. Address of Operator
PO Box 5270 Hobbs, NM 88241

4. Well Location
Unit Letter O : 660 feet from the South line and 1473 feet from the E line
Section 30 Township 22S Range 28E NMPM Eddy County

11. Elevation (Show whether DR, RKB, RT, GR, etc.)
3039' GL

Pit or Below-grade Tank Application ☐ or Closure ☐

Pit type _____ Depth to Groundwater _____ Distance from nearest fresh water well _____ Distance from nearest surface water _____

Pit Liner Thickness: _____ mil Below-Grade Tank: Volume _____ bbls; Construction Material _____

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:

PERFORM REMEDIAL WORK ☐ PLUG AND ABANDON ☐
TEMPORARILY ABANDON ☐ CHANGE PLANS ☐
PULL OR ALTER CASING ☐ MULTIPLE COMPL ☐
OTHER: ☐

SUBSEQUENT REPORT OF:

REMEDIAL WORK ☐ ALTERING CASING ☐
COMMENCE DRILLING OPNS. ☐ P AND A ☐
CASING/CEMENT JOB ☒
OTHER: ☐

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 1103. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

12/25/08...MI & spud 17 1/2" hole. TD hole at 313'. Ran 313' 13 3/8" 48# H40 ST&C csg. Cmt w/350 sks Class C with additives. Mixed @ 14.8 #/g w/ 1.34 yd. Plug down @ 2:15 pm 12/26/08. Lift pressure 124# @ 3 BPM. Did not circ cmt. Ran Temp Survey TOC @ 90'. TIH w/1" pipe Tag @ 114'. Ran 1" pipe in 2 stages with 100 sks Class C w/CaCl2. Mixed @ 14.8 #/g w/ 1.34 yd. Circ 15 sks to pits. WOC 18 hrs. Drilled out with 12 1/4" bit.

01/02/09..TD 12 1/4" hole. Ran 4502' 9 5/8" 40# N80/K55 LT&C Csg. Cemented with 1100 sks BJ Lite Class C (35:65:6) with additives. Mixed @ 12.5# /g w/ 2.04 yd. Tail w/400 sks Class C. Mixed @ 14.8 #/g w/ 1.34 yd. Plug down @ 3:00 pm 01/04/09. Circ 93 sks to pit. WOC 18 hrs. Test BOPE to 5000# & annular to 2500#. At 7:15 pm on 01/05/09, tested casing to 1500# for 20 minutes, held OK. Test csg shoe to 12.5 MWE. Charts and schematic attached. Drilled out with 8 3/4" bit.

ACCEPTED FOR RECORD

JAN 12 2009

I hereby certify that the information above is true and complete to the best of my knowledge and belief. I further certify that any pit or below-grade tank has been/will be constructed or closed according to NMOCD guidelines ☐, a general permit ☐ or an attached permit plan ☐.


SIGNATURE Jackie Lathan TITLE Hobbs Regulatory DATE 01/07/09

Type or print name Jackie Lathan E-mail address: jlathan@mewbourne.com Telephone No. 575-393-5905
For State Use Only

APPROVED BY: _____ TITLE _____ DATE _____

Conditions of Approval (if any):

PRINTED IN U.S.A.

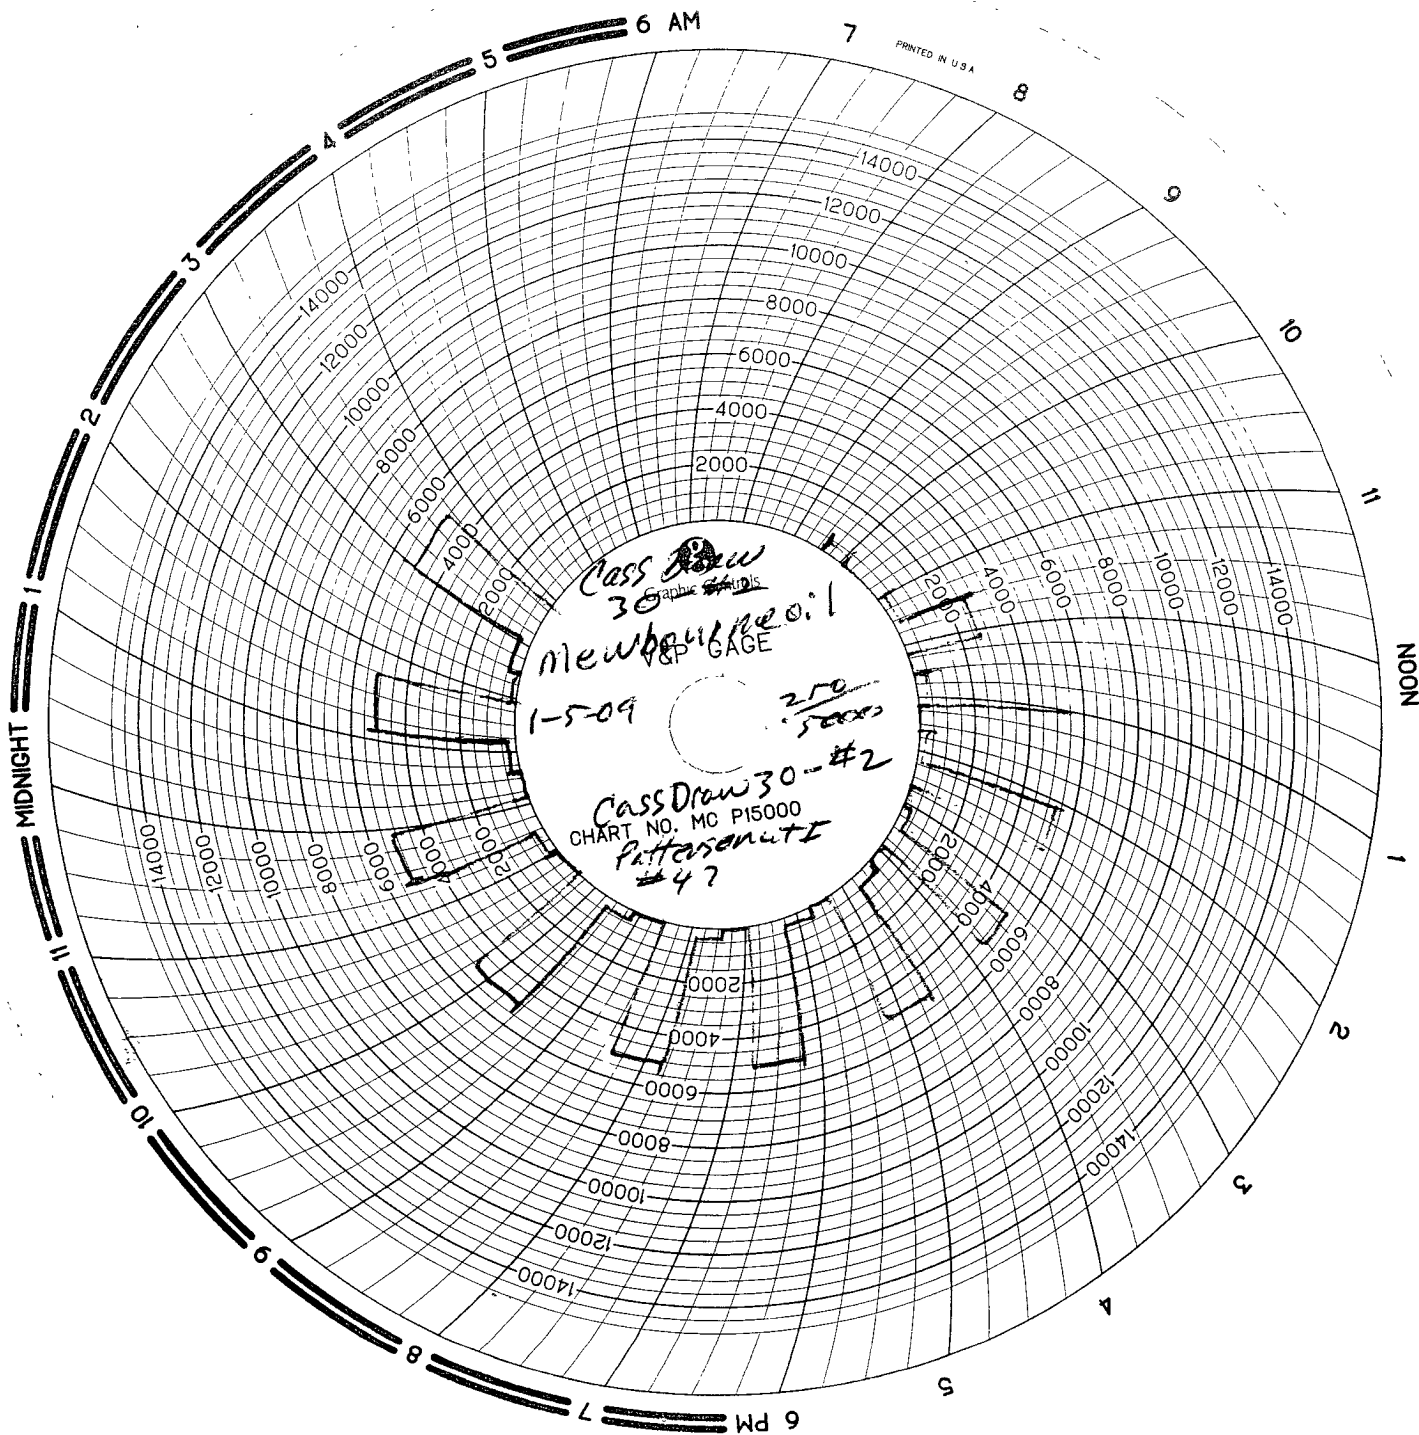

MAN WELDING SERVICES, INC

Company Mewbourne Oil Corp. Date 1-5-08

Lease Cass Draw 30-#2 County Eddy

Drilling Contractor Patterson HTE Plug & Drill Pipe Size 11" 4 1/2 x 4

Accumulator Function Test - OO&GO#2

To Check - USABLE FLUID IN THE NITROGEN BOTTLES (III.A.2.c.i. or ii or iii)

- Make sure all rams and annular are open and if applicable HCR is closed.
- Ensure accumulator is pumped up to working pressure! **(Shut off all pumps)**
 1. Open HCR Valve. (If applicable)
 2. Close annular.
 3. Close **all** pipe rams.
 4. Open one set of the pipe rams to simulate closing the blind ram.
 5. For 3 ram stacks, open the annular to achieve the 50+ % safety factor. (5M and greater systems).
 6. **Record remaining pressure 1400 psi. Test Fails if pressure is lower than required.**
 - a. {950 psi for a 1500 psi system} b. {1200 psi for a 2000 & 3000 psi system }
 7. If annular is closed, open it at this time and close HCR.

To Check - PRECHARGE ON BOTTLES OR SPHERICAL (III.A.2.d.)

- Start with manifold pressure at, or above, maximum acceptable pre-charge pressure:
 - a. {800 psi for a 1500 psi system} b. {1100 psi for 2000 and 3000 psi system}
- 1. Open bleed line to the tank, slowly. **(gauge needle will drop at the lowest bottle pressure)**
 2. Close bleed line. Barely bump electric pump and see what pressure the needle jumps up to.
 3. **Record pressure drop 1000 psi. Test fails if pressure drops below minimum.**
- **Minimum:** a. {700 psi for a 1500 psi system} b. {900 psi for a 2000 & 3000 psi system}

To Check - THE CAPACITY OF THE ACCUMULATOR PUMPS (III.A.2.f.)


- Isolate the accumulator bottles or spherical from the pumps & manifold.
- Open the bleed off valve to the tank, {manifold psi should go to 0 psi} close bleed valve.
 1. Open the HCR valve, {if applicable}
 2. Close annular
 3. With **pumps** only, time how long it takes to regain the required manifold pressure.
 4. **Record elapsed time 30 sec. Test fails if it takes over 2 minutes.**
 - a. {950 psi for a 1500 psi system} b. {1200 psi for a 2000 & 3000 psi system}



INVOICE

ME B09795

ANNULAR 15

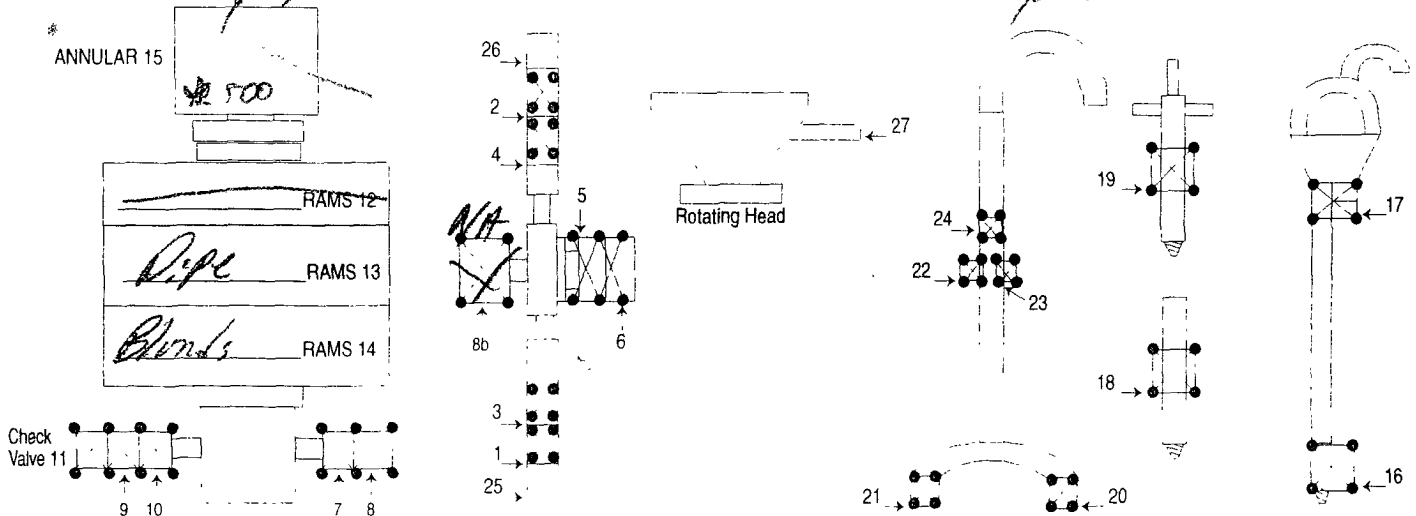[illegible]

8.0 HR @ \$200.00
1.0 HR @ \$800.00
Mileage 2300 @ \$1.50 = \$345.00
MASTER PRINTERS 575 396 3661 Mr. Hurd \$200.00

SUB TOTAL	2545.00
TAX	136.80
TOTAL	2681.80
