


Well ID: 30-015-26838

Well Name: G J WEST COOP UNIT #101

Event#: 6.00

Report Dates: 06/17/2011

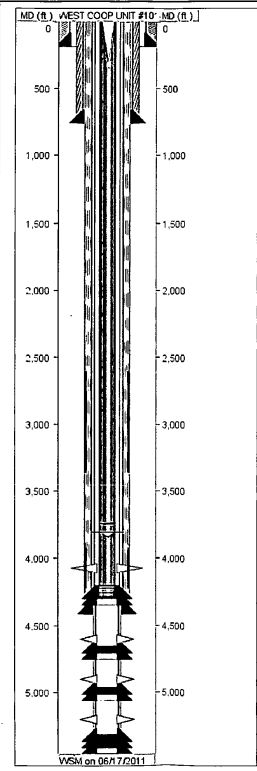

PIPE SPECIFICATION

STRING NAME	SECTION NAME	JOINT COUNT	START DEPTH	END DEPTH	LENGTH	OD SIZE	ID SIZE	WT GRDNT	GRD	CONN
SURFACE	CASING		0.00	184.00	184.00	13.38	12.71	48.0	H-40	
INTERMEDIATE #1	CASING	18	0.00	758.00	758.00	8.63	7.51	49.0	C-90	
PRODUCTION	CASING	110	0.00	4418.00	4418.00	5.50	3.75	43.1	C-90	
TUBING	BULL PLUG		4290.86	4291.36	0.50	2.88	2.44	6.5	J-55	
TUBING	TUBING		4258.54	4291.36	32.82	2.88	2.44	6.5	MA	
TUBING	TUBING		4225.54	4258.54	33.00	2.88	2.44	6.5	MA	
TUBING	DE-SANDER	2	4206.26	4225.54	19.28	2.88	2.44	6.5	DS	
TUBING	SEAT NIPPLE		4205.06	4206.26	1.20	2.88	2.44	6.5	SN	
TUBING	TUBING	12	3809.18	4205.06	395.88	2.88	2.44	6.5	J-55	
TUBING	TUBING ANCHOR		3805.88	3809.18	3.30	5.50	2.44	6.5	TAC	
TUBING	TUBING	2	3743.25	3805.88	62.63	2.88	2.44	6.5	J-55	
TUBING	MARKER JOINT		3741.25	3743.25	2.00	2.88	2.44	6.5	MJ	
TUBING	TUBING	119	1.00	3741.25	3740.25	2.88	2.44	6.5	J-55	
PRODUCTION LINER	FLOAT SHOE		5458.98	5460.35	1.37	4.00	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CASING	1	5415.34	5458.98	43.64	4.00	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CENTRALIZER		5413.97	5415.34	1.37	4.75	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	FLOAT COLLAR		5412.60	5413.97	1.37	4.00	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CASING	1	5368.09	5412.60	44.51	4.00	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CENTRALIZER		5366.72	5368.09	1.37	4.75	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CASING	7	5060.39	5366.72	306.33	4.00	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CENTRALIZER		5059.02	5060.39	1.37	4.75	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CASING	1	5015.22	5059.02	43.80	4.00	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CENTRALIZER		5013.85	5015.22	1.37	4.75	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CASING	6	4751.50	5013.85	262.35	4.00	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CENTRALIZER		4750.13	4751.50	1.37	4.75	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CASING	1	4706.33	4750.13	43.80	4.00	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CENTRALIZER		4704.96	4706.33	1.37	4.75	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CASING	8	4351.92	4704.96	353.04	4.00	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CENTRALIZER		4350.55	4351.92	1.37	4.75	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CASING	1	4306.75	4350.55	43.80	4.00	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CENTRALIZER		4305.38	4306.75	1.37	4.75	3.43	11.6	L-80	UTFJ
PRODUCTION LINER	CASING	1	4261.00	4305.38	44.38	4.00	3.43	11.6	L-80	UTFJ

CEMENTING

STRING NAME	STAGE #	LEAD TOP (est) (ft)	LEAD TOP (ver) (ft)	TAIL TOP (est) (ft)	TAIL TOP (ver) (ft)
SURFACE	1			0.0	0.0
INTERMEDIATE #1	1			0.0	0.0
PRODUCTION	1			0.0	0.0
PRODUCTION LINER	1	4284.0	4284.0	4284.0	4284.0

BHA STRING							
DRILL EQUIP CODE		DESCRIPTION		LENGTH	OD SIZE		ID SIZE
PERFORATION							
ZONE	JOB REPORT DATE	ZONE NAME	TOP DEPTH	BOTTOM DEPTH	HOLE SIZE	PEN SIZE	SQUEEZED
1	11/11/2009	LOWER BLINBRY	5100.00	5300.00	0.41	25.00	N
2	11/26/2009	MIDDLE BLINEBRY	4800.00	5000.00	0.41	18.15	N
3	12/02/2009	UPPER BLINBRY	4500.00	4700.00	0.41	18.15	N
5	10/14/1991	SAN ANDRES	2603.00	3362.00			Y
7	06/10/2011	PADDOCK PERFS	3920.00	4232.00	0.25	27.00	N
