

OCD-ARTESIA

Form 3160-3
(August 2007)

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED
OMB No. 1004-0137
Expires July 31, 2010

5. Lease Serial No.
NMNM030453

6. If Indian, Allottee or Tribe Name

7. If Unit or CA Agreement, Name and No.

8. Lease Name and Well No.
PLU BIG SINKS 24-24-30 USA 1H

9. API Well No.

10. Field and Pool, or Exploratory
UNKNOWN Bone Spring

11. Sec., T. R. M. or Blk. and Survey or Area
24-24S-30E

12. County or Parish
EDDY

13. State
NM

1a. Type of work: ☒ DRILL ☐ REENTER

1b. Type of Well: ☒ Oil Well ☐ Gas Well ☐ Other ☐ Single Zone ☐ Multiple Zone

2. Name of Operator CHESAPEAKE OPERATING AGENT FOR BOPCO

3a. Address PO BOX 18496
OKLAHOMA CITY, OK 73154-0496

3b. Phone No. (include area code)
405-935-2411

4. Location of Well (Report location clearly and in accordance with any State requirements *)
At surface NWNE 100' FNL 1980 FEL
At proposed prod. zone SWSE 350 FSL 1980 FEL

14. Distance in miles and direction from nearest town or post office*
30 MILES FROM LOVING POST OFFICE

15. Distance from proposed* location to nearest property or lease line, ft (Also to nearest drig. unit line, if any)
1900' FNL

16. No. of acres in lease
NMNM030453-640 ACRES

17. Spacing Unit dedicated to this well
160

18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft
350' per operator 11-23-11 WWI

19. Proposed Depth
14,020' MD/ 9285' TVD
9304

20. BLM/BIA Bond No. on file
ESB00159

21. Elevations (Show whether DF, KDB, RT, GL, etc.)
3472 GL


22. Approximate date work will start*
04/1/2012

23. Estimated duration
35-45 DAYS

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, must be attached to this form:

- 1: Well plat certified by a registered surveyor.
- 2: A Drilling Plan.
- 3: A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).
- 4: Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- 5: Operator certification
- 6: Such other site specific information and/or plans as may be required by the BLM.

25. Signature


Name (Printed/Typed)
LYNDEE SONGER

Date
11/14/2011

Title
REGULATORY COMPLIANCE ANALYST

Approved by (Signature) /s/George MacDonell

Name (Printed/Typed)

Date
JAN 6 2012

Title
FIELD MANAGER

Office
CARLSBAD FIELD OFFICE

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.


APPROVAL FOR TWO YEARS

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)

Carlsbad Controlled Water Basin



Approval Subject to General Requirements
& Special Stipulations Attached

SEE ATTACHED FOR
CONDITIONS OF APPROVAL

ONSHORE ORDER NO. 1
Chesapeake Agent for BOPCO
PLU Big Sinks 24-24-30 USA 1H
SL: 100' FNL & 1980' FEL
BL: 350' FSL & 1980' FEL
Section 24-24S-30E
Eddy County, NM

CONFIDENTIAL – TIGHT HOLE
OPERATOR CERTIFICATION

SL: Lease No. NMNM 030453
BL: Lease No. NMNM 030453

CERTIFICATION

I hereby certify that I, or someone under my direct supervision, have inspected the drill site and access route proposed herein; that I am familiar with the conditions which currently exist; that I have full knowledge of state and Federal laws applicable to this operation; that the statements made in this APD package are, to the best of my knowledge, true and correct; and, that the work associated with the operations proposed will be performed in conformity with this APD package and the terms and conditions under which it is approved. I also certify that I, or the company I represent, am responsible for the operations conducted under this application. These statements are subject to the provisions of 18 U.S.C. 1001 for the filing of a false statement.

Executed this 9th day of September, 2011

Name: 
Toby Reid - Field Superintendent

Address: 1616 W Bender Blvd Hobbs, NM 88240

Telephone: 575-725-8497

E-mail: toby.reid@chk.com

Additional Operator Remarks:

Chesapeake Operating, Inc. respectfully requests permission to drill a well to 14,020' to test the Bone Spring formation. If productive, casing will be run and the well completed. If dry, the well will be plugged and abandoned as per BLM and New Mexico Oil Conservation Division requirements.

Please find the Surface Use Plan and Drilling Plan as required by Onshore Order No. 1.

Attached are the Exhibit A-1 to A-5 Survey plats, Exhibit B 1 mile radius plat, Exhibit C Production facility, Exhibit D Generic Rig layout, Exhibit F-1 to F-2 BOP & Choke Manifold, Exhibit G Directional Drill Plan, Exhibit H Reclamation Plan and Exhibit I Pipeline Map.

Archeological Survey will be delivered to the BLM when completed.

Chesapeake Operating, Inc. has an agreement with the grazing lessee.

Please be advised that Chesapeake Operating, Inc. is the Designated Agent for BOPCO, the Operator of this unit. Chesapeake Operating, Inc. agrees to be responsible under the terms and conditions of the lease for the operations conducted upon the lease lands.

(CHK PN 639440)

DISTRICT I
1625 N. French Dr., Hobbs, NM 88240


DISTRICT II
1301 W. Grand Avenue, Artesia, NM 88210

DISTRICT III
1000 Rio Brazos Rd., Aztec, NM 87410

DISTRICT IV
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals and Natural Resources Department

OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, New Mexico 87505



WELL LOCATION AND ACREAGE DEDICATION PLAT

☐ AMENDED REPORT

API Number 30-015-39846	Pool Code 96403	Pool Name WILDCAT; BONE SPRING
Property Code 39031	Property Name PLU BIG SINKS 24 24 30 USA	Well Number 1H
OGRD No. 147179	Operator Name CHESAPEAKE OPERATING CO.	Elevation 3472'

Surface Location

UL or lot No.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
B	24	24 S	30 E		100	NORTH	1980	EAST	EDDY

Bottom Hole Location If Different From Surface

UL or lot No.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
O	24	24 S	30 E		350	SOUTH	1980	EAST	EDDY
Dedicated Acres 160		Joint or Infill	Consolidation Code	Order No.					

NO ALLOWABLE WILL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN CONSOLIDATED
OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION

<p>SURFACE LOCATION Lat - N 32.21059824° Long - W 103.8320815° NMSPCE- N 440711.188 E 696364.254 (NAD-83) Lat - N 32.21047487° Long - W 103.83159728° NMSPCE- N 440652.381 E 655180.036 (NAD-27)</p>	<p>Penetration Point 3475.0'</p>	<p>3476.9'</p>	<p>1980'</p>	<p>OPERATOR CERTIFICATION I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division. Signature: <u>Bryan Arrant</u> Date: <u>08/25/2011</u> Printed Name: <u>Bryan Arrant</u> Email Address: <u>bryan.arrant@chk.com</u></p>
<p>PROPOSED BOTTOM HOLE LOCATION Lat - N 32.19706943° Long - W 103.8320937° NMSPCE- N 435789.583 E 696383.399 (NAD-83) Lat - N 32.19694593° Long - W 103.83161018° NMSPCE- N 435730.885 E 655199.015 (NAD-27)</p>	<p>Project Area</p>	<p>Producing Area</p>	<p>350'</p>	<p>SURVEYOR CERTIFICATION I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief. Date Surveyed: <u>August 5, 2011</u> Signature & Seal of Professional Surveyor: <u>GARY L. JONES</u> Certificate No. Gary L. Jones 7977 BASIN SURVEYS 24759</p>

1. FORMATION TOPS

The estimated tops of important geologic markers are as follows: 3480

FORMATION	MD	SUB-SEA	KBTVD
Rustler	2,926'	566'	
Salt	824'	2,668'	
Lamar	-714'	4,206'	
Bell Canyon	-755'	4,247'	
Cherry Canyon	-1,627'	5,119'	
Brushy Canyon	-2,893'	6,385'	
First Bone Spring Lime	-4,451'	8,043'	
First Bone Spring Sand	-5,406'	8,898'	
Second Bone Spring Lime	-5,719'	9,211'	
TOTAL DEPTH			14,020'

2. ESTIMATED DEPTH OF WATER, OIL, GAS & OTHER MINERAL BEARING FORMATIONS

The estimated depths at which the top and bottom of the anticipated water, oil, gas or other mineral bearing formations are expected to be encountered are as follows:

Substance	Formation	Depth
Water	Rustler	566
Oil/Gas	Brushy Canyon	6,385'
Oil/Gas	Bone Spring	8,043

All shows of fresh water and minerals will be reported and protected.

3. BOP EQUIPMENT

Will have a 5000 psi rig stack (see proposed schematic) for drill out below surface casing, but this system will be tested to 3000 psi working pressure and 3000 psi working pressure for the annular preventer; therefore, no shoe tests will be conducted.

Chesapeake Operating Inc.'s minimum specifications for pressure control equipment are as follows:

I. BOP, Annular, Choke Manifold Pressure Test - See Exhibit F-1 and F-2

A. Equipment

1. The equipment to be tested includes all of the following that is installed on the well:
 - (a) Ram-type and annular preventers
 - (b) Choke manifolds and valves
 - (c) Kill lines and valves

(d) Upper and lower kelly cock valves, inside BOP's and safety valves

B. Frequency

1. All tests shall be performed with clear water
 - (a) when installed
 - (b) before drilling out each casing string
 - (c) at any time that there is a repair requiring a pressure seal to be broken in the assembly
 - (d) at least once every 30 days while drilling

C.-Frequency

1. In some drilling operations, the pressures to be used for low and high pressure testing of preventers and casing may be different from those given below due to governmental regulations or approved local practices.
2. If an individual component does not test at the low pressure, do not, test to the high pressure and then drop back down to the low pressure.
3. All valves located downstream of a valve being tested must be placed in the open position.
4. All equipment will be tested with an initial "low pressure" test at 250 psi.
5. The subsequent "high pressure" test will be conducted at the rated working pressure of the equipment for all equipment except the annular preventer unless otherwise stated (see above).
6. The "high pressure" test for the annular preventer will be conducted at 70% of the rated working pressure unless otherwise stated (see above).
7. A record of all pressures will be made on a pressure-recording chart.

II. Accumulator Performance Test

A. Scope

1. The purpose of this test is to check the capabilities of the Bop control systems and to detect deficiencies in the hydraulic oil volume and recharge time.

B. Test Frequency

1. The accumulator is to be tested each time the BOP's are tested, or any time a major repair is performed.

C. Minimum Requirements

1. The accumulator should be of sufficient volume to supply 1.5 times the volume to close and hold all BOP equipment in sequence, without recharging and the pump turned off, and have remaining pressures of 200 psi above the precharge pressure.
2. Minimum precharge pressures for the various accumulator systems per manufacturers recommended specifications are as follows:

DRILLING PROGRAM

Chesapeake Agent for BOPCO.
PLU Big Sinks 24-24-30 USA 1H
Eddy County, New Mexico

CONFIDENTIAL-TIGHT HOLE

System Operating Pressure	Precharge Pressure
1500 psi	750 psi
2000 psi	1000 psi
3000 psi	1000 psi

3. Closing times for the annular preventer should be less than 20 seconds and for the ram-type preventers less than 10 seconds.
4. System recharge time should not exceed 10 minutes

D. Test Procedure

1. Shut accumulator pumps off and record accumulator pressure.
2. In sequence, close the annular and one set of properly sized pipe rams, and open the HCR valve
3. Record time to close or open each element and the remaining accumulator pressure after each operation.
4. Record the remaining accumulator pressure at the end of the test sequence. Per the previous requirement, this pressure should not be less than the following pressures:

System Operating Pressure	Remaining Pressure After Test
1500 psi	950 psi
2000 psi	1200 psi
3000 psi	1200 psi

5. Turn the accumulator pumps on and record the recharge time. This time should not exceed 10 minutes.
6. Open annular and ram-type preventers. Close HCR valve.
7. Place all 4-way control valves in full open or full closed position. Do not leave in neutral position.

4. CASING PROGRAM

- a. The proposed casing program will be as follows:

Purpose	From	To	Hole Size	Csg Size	Weight	Grade	Thread	Condition
Surface	0'	660'	17- 1/2"	13-3/8"	48#	H-40	STC	New
Intermediate	0' <i>4050</i>	<i>4,220'</i>	11"	8-5/8"	32#	J-55	LTC	New
Production	0'	14,020'	7-7/8"	5-1/2"	20#	L-80	LTC	New

*See
COA*

- b. Casing design subject to revision based on geologic conditions encountered.
- c. Casing Safety Factors

Casing String	Min SF Burst	Min SF Collapse	Min SF Tension
Surface	1.37	2.58	2.52
Intermediate	1.37	1.39	1.94
Production	1.2	2.12	1.6

Min SF is the smallest of the group of safety factors that include the following considerations:

DRILLING PROGRAM

Chesapeake Agent for BOPCO.
PLU Big Sinks 24-24-30 USA 1H
Eddy County, New Mexico

CONFIDENTIAL-TIGHT HOLE

Burst Design

	Surf	Int	Prod
Pressure Test- Surface, Int, Prod Csg P external: Water P internal: Test psi + next section heaviest mud in csg	X	X	X
Displace to Gas- Surf Csg P external: Water P internal: Dry Gas from Next Csg Point	X		
Frac at Shoe, Gas to Surf- Int Csg P external: Water P internal: Dry Gas, 15 ppg Frac Gradient		X	
Stimulation (Frac) Pressures- Prod Csg P external: Water P internal: Max inj pressure w/ heaviest injected fluid			X
Tubing leak- Prod Csg P external: Water P internal: Leak just below surf, 8.7 ppg packer fluid			X

Collapse Design

Full Evacuation P external: Water gradient in cement, mud above TOC P internal: none	X	X	X
Cementing- Surf, Int, Prod Csg P external: Wet cement P internal: water	X	X	X

Tension Design

100k lb overpull	X	X	X
------------------	---	---	---

5. CEMENTING PROGRAM

	Type	Top	Btm	Wt (ppg)	Yld (sx/cu ft)	%Exc Open Hole	Sx
Surface							
Single Slurry	C + % Gel	0'	660'	13.5	1.73	150	650
Shallow Int							
Lead	TXI +5% Salt	0'	3,720'	12	1.8	150	1248
Tail	50C/50Poz +5% Salt	3,720'	4,220' 4,050'	14.2	1.37	150	243
Production							
Slurry 1 Lead	35/65Poz H +8% Gel	5,050'	8,000'	12.4	2.09	75	428
Slurry 1 Tail	50H/50Poz	8,000'	14,020'	14.5	1.24	75	1481
Slurry 2 Lead	35/65Poz H +8% Gel	3,720' 3,550'	4,800'	12.4	2.19	200	178
Slurry 2 Tail	50H/50Poz	4,800'	5,050'	14.8	1.33	200	98

1. Final cement volumes will be determined by caliper.
2. Surface casing shall have at least one centralizer installed on each of the bottom three joints starting with the shoe joint.
3. The production casing will be cemented in two stages with the DV tool place at: 5,050'
4. Production casing will have one centralizer on every other joint from TD

to KOP (horizontal type) and from KOP to intermediate casing (bowspring type).

Pilot Hole Plugging Plan:

There will be no pilot hole for this well.

6. MUD PROGRAM

From	To	Type	Weight	F. Vis	FL
Depth		Type	Weight	F. Vis	FL
0'	660'	Spud Mud	8.4 - 8.7	32 - 34	NC - NC
660'	4,220' 4050'	Brine	9.8 - 10.1	28 - 29	NC - NC
4,220'	8,826'	Cut Brine	8.4 - 9	28 - 30	NC - NC
8,826'	9,580'	Cut Brine	8.4 - 9	28 - 30	NC - NC
9,580'	14,020'	Cut Brine	8.4 - 9	28 - 30	NC - NC

A closed system will be utilized consisting of above ground steel tanks. All wastes accumulated during drilling operations will be contained in a portable trash cage and removed from location and deposited

All fluids and cuttings will be disposed of in accordance with New Mexico Oil Conservation Division rules and regulations.

A mud test shall be performed every 24 hours after mudding up to determine, as applicable: density, viscosity, gel strength, filtration, and pH.

7. TESTING, LOGGING, AND CORING *See COA*

The anticipated type and amount of testing, logging, and coring are as follows:

a. Drill stem tests are not planned.

b. The logging program will be as follows:

	Logs	Interval	Timing	Vendor
Mudlog	Mudlog	Int Csg to TD	Drill out Int Csg	Suttles
OH	Triple Combo (Dual Induction)	Curve to Int Csg	After Curve	TBD
LWD	GR/Neutron	Int Csg to Surface	While Drilling	TBD
LWD	MWD/Gamma	Curve/Lateral	While Drilling	TBD

c. Core samples are not planned.

d. A Directional Survey will be run.

8. ABNORMAL PRESSURES AND HYDROGEN SULFIDE

a. No abnormal pressures or temperatures are expected. Estimated BHP is: 4112 psi

b. Hydrogen sulfide gas is not anticipated.

Permian District

Poker Lake

PLU Big Sinks 24-24-30 USA 1H

Well #1

Wellbore #1

Plan: Design #1

Standard Planning Report

29 August, 2011

EXHIBIT 6

Chesapeake Operating

Planning Report

Database:	Drilling Database	Local Co-ordinate Reference:	Well Well #1
Company:	Permian District	TVD Reference:	RKB @ 3497.0usft (Original Well Elev)
Project:	Poker Lake	MD Reference:	RKB @ 3497.0usft (Original Well Elev)
Site:	PLU Big Sinks 24-24-30 USA 1H	North Reference:	Grid
Well:	Well #1	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Project: Poker Lake, Eddy County, NM			
Map System:	US State Plane 1983	System Datum:	Ground Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site: PLU Big Sinks 24-24-30 USA 1H					
Site Position:		Northing:	440,711 19 usft	Latitude:	32.2105982355
From:	Map	Easting:	696,364.25 usft	Longitude:	-103.8320814508
Position Uncertainty:	0.0 usft	Slot Radius:	13.200 in	Grid Convergence:	0.2672098

Well:	Well #1					
Well Position	+N/-S	0.0 usft	Northing:	440,711.19 usft	Latitude:	32.2105982355
	+E/-W	0.0 usft	Easting:	696,364.25 usft	Longitude:	-103.8320814508
Position Uncertainty	0.0 usft	Wellhead Elevation:		Ground Level:	3,472.0 usft	

Wellbore #1					
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF200510	8/29/2011	7.6675057	60.1479255	48,572

Design:	Design #1
---------	-----------

Audit Notes:				
Version:	Phase:	PROTOTYPE	Tie On Depth:	0.0

Vertical Section:	Depth From (TVD)	+N/-S	+E/-W	Direction
	(usft)	(usft)	(usft)	(°)
	0.0	0.0	0.0	179.78

Plan Sections:										
Measured:	Inclination	Azimuth	Vertical	+N/-S	+E/-W	Dogleg	Buid	Turn	TFO	Target
Depth	(°)	(°)	Depth	(usft)	(usft)	Rate	Rate	Rate	(°)	
(usft)			(usft)			(°/100usft)	(°/100usft)	(°/100usft)		
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.0000000	
8,826.4	0.00	0.00	8,826.4	0.0	0.0	0.00	0.00	0.00	0.0000000	
9,580.5	90.50	179.78	9,303.8	-481.6	1.9	12.00	12.00	0.00	79.7771210	
14,020.7	90.50	179.78	9,265.0	-4,921.6	19.1	0.00	0.00	0.00	0.0000000	BHL #1

Chesapeake Operating Planning Report

Database:	Drilling Database	Local Co-ordinate Reference:	Well Well #1
Company:	Permian District	TVD Reference:	RKB @ 3497.0usft (Original Well Elev)
Project:	Poker Lake	MD Reference:	RKB @ 3497.0usft (Original Well Elev)
Site:	PLU Big Sinks 24-24-30 USA 1H	North Reference:	Grid
Well:	Well #1	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/S (usft)	+E/W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00
1,600.0	0.00	0.00	1,600.0	0.0	0.0	0.0	0.00	0.00	0.00
1,700.0	0.00	0.00	1,700.0	0.0	0.0	0.0	0.00	0.00	0.00
1,800.0	0.00	0.00	1,800.0	0.0	0.0	0.0	0.00	0.00	0.00
1,900.0	0.00	0.00	1,900.0	0.0	0.0	0.0	0.00	0.00	0.00
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.0	0.00	0.00	0.00
2,100.0	0.00	0.00	2,100.0	0.0	0.0	0.0	0.00	0.00	0.00
2,200.0	0.00	0.00	2,200.0	0.0	0.0	0.0	0.00	0.00	0.00
2,300.0	0.00	0.00	2,300.0	0.0	0.0	0.0	0.00	0.00	0.00
2,400.0	0.00	0.00	2,400.0	0.0	0.0	0.0	0.00	0.00	0.00
2,500.0	0.00	0.00	2,500.0	0.0	0.0	0.0	0.00	0.00	0.00
2,600.0	0.00	0.00	2,600.0	0.0	0.0	0.0	0.00	0.00	0.00
2,700.0	0.00	0.00	2,700.0	0.0	0.0	0.0	0.00	0.00	0.00
2,800.0	0.00	0.00	2,800.0	0.0	0.0	0.0	0.00	0.00	0.00
2,900.0	0.00	0.00	2,900.0	0.0	0.0	0.0	0.00	0.00	0.00
3,000.0	0.00	0.00	3,000.0	0.0	0.0	0.0	0.00	0.00	0.00
3,100.0	0.00	0.00	3,100.0	0.0	0.0	0.0	0.00	0.00	0.00
3,200.0	0.00	0.00	3,200.0	0.0	0.0	0.0	0.00	0.00	0.00
3,300.0	0.00	0.00	3,300.0	0.0	0.0	0.0	0.00	0.00	0.00
3,400.0	0.00	0.00	3,400.0	0.0	0.0	0.0	0.00	0.00	0.00
3,500.0	0.00	0.00	3,500.0	0.0	0.0	0.0	0.00	0.00	0.00
3,600.0	0.00	0.00	3,600.0	0.0	0.0	0.0	0.00	0.00	0.00
3,700.0	0.00	0.00	3,700.0	0.0	0.0	0.0	0.00	0.00	0.00
3,800.0	0.00	0.00	3,800.0	0.0	0.0	0.0	0.00	0.00	0.00
3,900.0	0.00	0.00	3,900.0	0.0	0.0	0.0	0.00	0.00	0.00
4,000.0	0.00	0.00	4,000.0	0.0	0.0	0.0	0.00	0.00	0.00
4,100.0	0.00	0.00	4,100.0	0.0	0.0	0.0	0.00	0.00	0.00
4,200.0	0.00	0.00	4,200.0	0.0	0.0	0.0	0.00	0.00	0.00
4,300.0	0.00	0.00	4,300.0	0.0	0.0	0.0	0.00	0.00	0.00
4,400.0	0.00	0.00	4,400.0	0.0	0.0	0.0	0.00	0.00	0.00
4,500.0	0.00	0.00	4,500.0	0.0	0.0	0.0	0.00	0.00	0.00
4,600.0	0.00	0.00	4,600.0	0.0	0.0	0.0	0.00	0.00	0.00
4,700.0	0.00	0.00	4,700.0	0.0	0.0	0.0	0.00	0.00	0.00
4,800.0	0.00	0.00	4,800.0	0.0	0.0	0.0	0.00	0.00	0.00
4,900.0	0.00	0.00	4,900.0	0.0	0.0	0.0	0.00	0.00	0.00
5,000.0	0.00	0.00	5,000.0	0.0	0.0	0.0	0.00	0.00	0.00
5,100.0	0.00	0.00	5,100.0	0.0	0.0	0.0	0.00	0.00	0.00
5,200.0	0.00	0.00	5,200.0	0.0	0.0	0.0	0.00	0.00	0.00
5,300.0	0.00	0.00	5,300.0	0.0	0.0	0.0	0.00	0.00	0.00

Chesapeake Operating

Planning Report

Database:	Drilling Database:	Local Co-ordinate Reference:	Well Well #1
Company:	Permian District	TVD Reference:	RKB @ 3497.0usft (Original Well Elev)
Project:	Poker Lake	MD Reference:	RKB @ 3497.0usft (Original Well Elev)
Site:	PLU Big Sinks 24-24-30 USA 1H	North Reference:	Gnd
Well:	Well #1	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	N-S (usft)	E-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
5,400.0	0.00	0.00	5,400.0	0.0	0.0	0.0	0.00	0.00	0.00	
5,500.0	0.00	0.00	5,500.0	0.0	0.0	0.0	0.00	0.00	0.00	
5,600.0	0.00	0.00	5,600.0	0.0	0.0	0.0	0.00	0.00	0.00	
5,700.0	0.00	0.00	5,700.0	0.0	0.0	0.0	0.00	0.00	0.00	
5,800.0	0.00	0.00	5,800.0	0.0	0.0	0.0	0.00	0.00	0.00	
5,900.0	0.00	0.00	5,900.0	0.0	0.0	0.0	0.00	0.00	0.00	
6,000.0	0.00	0.00	6,000.0	0.0	0.0	0.0	0.00	0.00	0.00	
6,100.0	0.00	0.00	6,100.0	0.0	0.0	0.0	0.00	0.00	0.00	
6,200.0	0.00	0.00	6,200.0	0.0	0.0	0.0	0.00	0.00	0.00	
6,300.0	0.00	0.00	6,300.0	0.0	0.0	0.0	0.00	0.00	0.00	
6,400.0	0.00	0.00	6,400.0	0.0	0.0	0.0	0.00	0.00	0.00	
6,500.0	0.00	0.00	6,500.0	0.0	0.0	0.0	0.00	0.00	0.00	
6,600.0	0.00	0.00	6,600.0	0.0	0.0	0.0	0.00	0.00	0.00	
6,700.0	0.00	0.00	6,700.0	0.0	0.0	0.0	0.00	0.00	0.00	
6,800.0	0.00	0.00	6,800.0	0.0	0.0	0.0	0.00	0.00	0.00	
6,900.0	0.00	0.00	6,900.0	0.0	0.0	0.0	0.00	0.00	0.00	
7,000.0	0.00	0.00	7,000.0	0.0	0.0	0.0	0.00	0.00	0.00	
7,100.0	0.00	0.00	7,100.0	0.0	0.0	0.0	0.00	0.00	0.00	
7,200.0	0.00	0.00	7,200.0	0.0	0.0	0.0	0.00	0.00	0.00	
7,300.0	0.00	0.00	7,300.0	0.0	0.0	0.0	0.00	0.00	0.00	
7,400.0	0.00	0.00	7,400.0	0.0	0.0	0.0	0.00	0.00	0.00	
7,500.0	0.00	0.00	7,500.0	0.0	0.0	0.0	0.00	0.00	0.00	
7,600.0	0.00	0.00	7,600.0	0.0	0.0	0.0	0.00	0.00	0.00	
7,700.0	0.00	0.00	7,700.0	0.0	0.0	0.0	0.00	0.00	0.00	
7,800.0	0.00	0.00	7,800.0	0.0	0.0	0.0	0.00	0.00	0.00	
7,900.0	0.00	0.00	7,900.0	0.0	0.0	0.0	0.00	0.00	0.00	
8,000.0	0.00	0.00	8,000.0	0.0	0.0	0.0	0.00	0.00	0.00	
8,100.0	0.00	0.00	8,100.0	0.0	0.0	0.0	0.00	0.00	0.00	
8,200.0	0.00	0.00	8,200.0	0.0	0.0	0.0	0.00	0.00	0.00	
8,300.0	0.00	0.00	8,300.0	0.0	0.0	0.0	0.00	0.00	0.00	
8,400.0	0.00	0.00	8,400.0	0.0	0.0	0.0	0.00	0.00	0.00	
8,500.0	0.00	0.00	8,500.0	0.0	0.0	0.0	0.00	0.00	0.00	
8,600.0	0.00	0.00	8,600.0	0.0	0.0	0.0	0.00	0.00	0.00	
8,700.0	0.00	0.00	8,700.0	0.0	0.0	0.0	0.00	0.00	0.00	
8,800.0	0.00	0.00	8,800.0	0.0	0.0	0.0	0.00	0.00	0.00	
8,826.4	0.00	0.00	8,826.4	0.0	0.0	0.0	0.00	0.00	0.00	
8,900.0	8.84	179.78	8,899.7	-5.7	0.0	5.7	12.00	12.00	0.00	
9,000.0	20.84	179.78	8,996.2	-31.2	0.1	31.2	12.00	12.00	0.00	
9,100.0	32.84	179.78	9,085.3	-76.3	0.3	76.3	12.00	12.00	0.00	
9,200.0	44.84	179.78	9,163.0	-138.9	0.5	138.9	12.00	12.00	0.00	
9,300.0	56.84	179.78	9,226.0	-216.3	0.8	216.3	12.00	12.00	0.00	
9,400.0	68.84	179.78	9,271.6	-305.1	1.2	305.1	12.00	12.00	0.00	
9,500.0	80.84	179.78	9,297.7	-401.4	1.6	401.4	12.00	12.00	0.00	
9,580.5	90.50	179.78	9,303.8	-481.6	1.9	481.6	12.00	12.00	0.00	
9,600.0	90.50	179.78	9,303.6	-501.1	1.9	501.1	0.00	0.00	0.00	
9,700.0	90.50	179.78	9,302.8	-601.1	2.3	601.1	0.00	0.00	0.00	
9,800.0	90.50	179.78	9,301.9	-701.1	2.7	701.1	0.00	0.00	0.00	
9,900.0	90.50	179.78	9,301.0	-801.1	3.1	801.1	0.00	0.00	0.00	
10,000.0	90.50	179.78	9,300.1	-901.1	3.5	901.1	0.00	0.00	0.00	
10,100.0	90.50	179.78	9,299.3	-1,001.1	3.9	1,001.1	0.00	0.00	0.00	
10,200.0	90.50	179.78	9,298.4	-1,101.1	4.3	1,101.1	0.00	0.00	0.00	
10,300.0	90.50	179.78	9,297.5	-1,201.1	4.7	1,201.1	0.00	0.00	0.00	
10,400.0	90.50	179.78	9,296.6	-1,301.1	5.1	1,301.1	0.00	0.00	0.00	
10,500.0	90.50	179.78	9,295.8	-1,401.1	5.5	1,401.1	0.00	0.00	0.00	

Chesapeake Operating

Planning Report

Database:	Drilling Database	Local Co-ordinate Reference:	Well Well #1
Company:	Permian District	TVD Reference:	RKB @ 3497.0usft (Original Well Elev)
Project:	Poker Lake	MD Reference:	RKB @ 3497.0usft (Original Well Elev)
Site:	PLU Big Sinks 24-24-30-USA 1H	North Reference:	Grid
Well:	Well #1	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		


Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
10,600.0	90.50	179.78	9,294.9	-1,501.1	5.8	1,501.1	0.00	0.00	0.00	
10,700.0	90.50	179.78	9,294.0	-1,601.1	6.2	1,601.1	0.00	0.00	0.00	
10,800.0	90.50	179.78	9,293.2	-1,701.1	6.6	1,701.1	0.00	0.00	0.00	
10,900.0	90.50	179.78	9,292.3	-1,801.1	7.0	1,801.1	0.00	0.00	0.00	
11,000.0	90.50	179.78	9,291.4	-1,901.0	7.4	1,901.1	0.00	0.00	0.00	
11,100.0	90.50	179.78	9,290.5	-2,001.0	7.8	2,001.1	0.00	0.00	0.00	
11,200.0	90.50	179.78	9,289.7	-2,101.0	8.2	2,101.1	0.00	0.00	0.00	
11,300.0	90.50	179.78	9,288.8	-2,201.0	8.6	2,201.0	0.00	0.00	0.00	
11,400.0	90.50	179.78	9,287.9	-2,301.0	9.0	2,301.0	0.00	0.00	0.00	
11,500.0	90.50	179.78	9,287.0	-2,401.0	9.3	2,401.0	0.00	0.00	0.00	
11,600.0	90.50	179.78	9,286.2	-2,501.0	9.7	2,501.0	0.00	0.00	0.00	
11,700.0	90.50	179.78	9,285.3	-2,601.0	10.1	2,601.0	0.00	0.00	0.00	
11,800.0	90.50	179.78	9,284.4	-2,701.0	10.5	2,701.0	0.00	0.00	0.00	
11,900.0	90.50	179.78	9,283.6	-2,801.0	10.9	2,801.0	0.00	0.00	0.00	
12,000.0	90.50	179.78	9,282.7	-2,901.0	11.3	2,901.0	0.00	0.00	0.00	
12,100.0	90.50	179.78	9,281.8	-3,001.0	11.7	3,001.0	0.00	0.00	0.00	
12,200.0	90.50	179.78	9,280.9	-3,101.0	12.1	3,101.0	0.00	0.00	0.00	
12,300.0	90.50	179.78	9,280.1	-3,201.0	12.5	3,201.0	0.00	0.00	0.00	
12,400.0	90.50	179.78	9,279.2	-3,301.0	12.8	3,301.0	0.00	0.00	0.00	
12,500.0	90.50	179.78	9,278.3	-3,401.0	13.2	3,401.0	0.00	0.00	0.00	
12,600.0	90.50	179.78	9,277.4	-3,501.0	13.6	3,501.0	0.00	0.00	0.00	
12,700.0	90.50	179.78	9,276.6	-3,601.0	14.0	3,601.0	0.00	0.00	0.00	
12,800.0	90.50	179.78	9,275.7	-3,701.0	14.4	3,701.0	0.00	0.00	0.00	
12,900.0	90.50	179.78	9,274.8	-3,801.0	14.8	3,801.0	0.00	0.00	0.00	
13,000.0	90.50	179.78	9,274.0	-3,901.0	15.2	3,901.0	0.00	0.00	0.00	
13,100.0	90.50	179.78	9,273.1	-4,000.9	15.6	4,001.0	0.00	0.00	0.00	
13,200.0	90.50	179.78	9,272.2	-4,100.9	16.0	4,101.0	0.00	0.00	0.00	
13,300.0	90.50	179.78	9,271.3	-4,200.9	16.3	4,201.0	0.00	0.00	0.00	
13,400.0	90.50	179.78	9,270.5	-4,300.9	16.7	4,301.0	0.00	0.00	0.00	
13,500.0	90.50	179.78	9,269.6	-4,400.9	17.1	4,401.0	0.00	0.00	0.00	
13,600.0	90.50	179.78	9,268.7	-4,500.9	17.5	4,501.0	0.00	0.00	0.00	
13,700.0	90.50	179.78	9,267.8	-4,600.9	17.9	4,601.0	0.00	0.00	0.00	
13,800.0	90.50	179.78	9,267.0	-4,700.9	18.3	4,701.0	0.00	0.00	0.00	
13,900.0	90.50	179.78	9,266.1	-4,800.9	18.7	4,800.9	0.00	0.00	0.00	
14,000.0	90.50	179.78	9,265.2	-4,900.9	19.1	4,900.9	0.00	0.00	0.00	
14,020.7	90.50	179.78	9,265.0	-4,921.6	19.1	4,921.6	0.00	0.00	0.00	

Design Targets										
Target Name	Dip Angle (°)	Dip Dir (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude	
BHL #1	0.00	0.00	9,265.0	-4,921.6	19.1	435,789.58	696,383.39	32.1970694320	-103.8320937413	
- plan hits target center										
- Point										
SHL #1	0.00	0.01	9,308.0	0.0	0.0	440,711.19	696,364.25	32.2105982355	-103.8320814508	
- plan misses target center by 200.8usft at 9200.0usft MD (9163.0 TVD, -138.9 N, 0.5 E)										
- Point										

Project: Poker Lake
 Site: PLU Big Sinks 24-24-30 USA 1H
 Well: Well #1
 Wellbore: Wellbore #1
 Design: Design #1

PROJECT DETAILS: Poker Lake

Geodetic System: US State Plane 1983
 Datum: North American Datum 1983
 Ellipsoid: GRS 1980
 Zone: New Mexico Eastern Zone

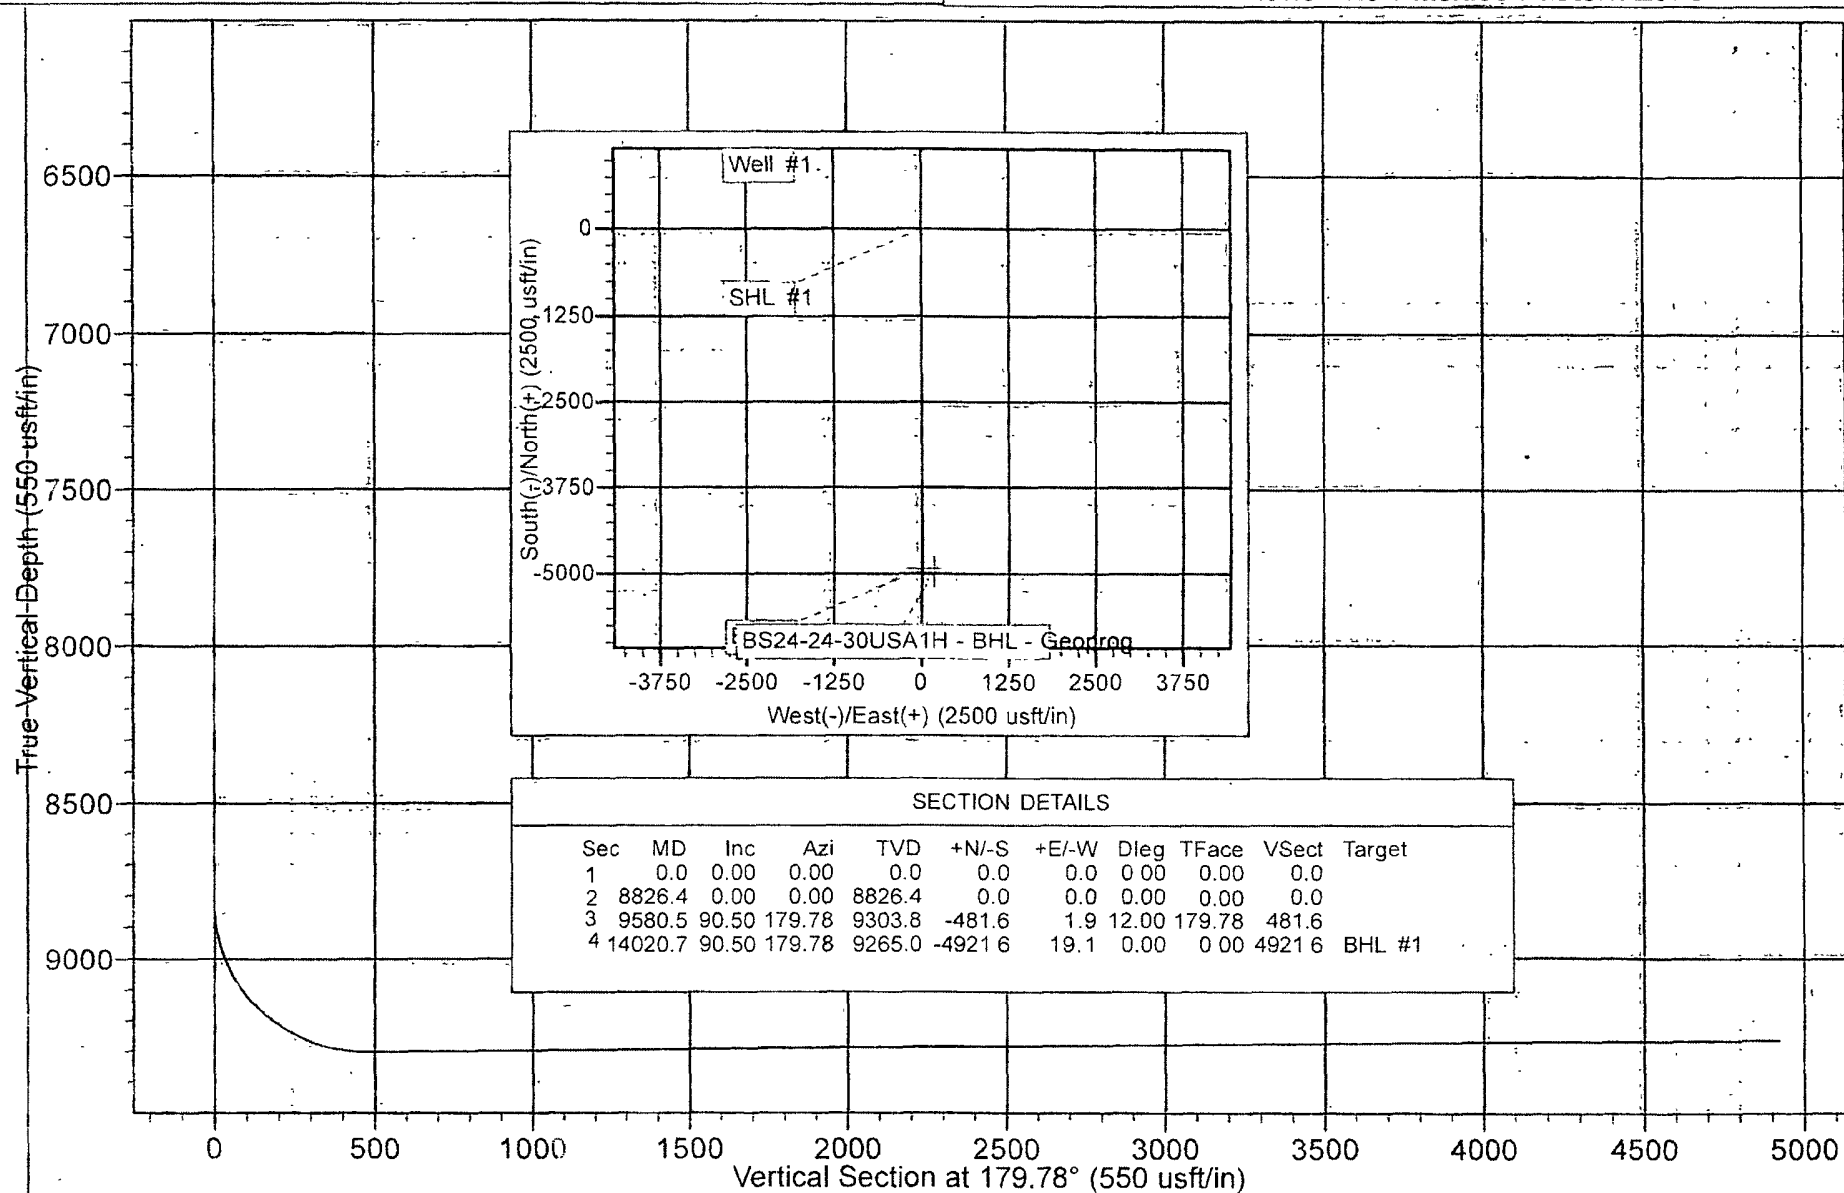

Chesapeake Minimum BOPE Requirements

Wellname: RLU Big Sinks 24-24-30 USA 1H

Operation: Intermediate and Production Hole Sections

BLOWOUT PREVENTER SCHEMATIC CHESAPEAKE OPERATING INC

WELL : Permian District

FIELD : Avalon

RIG :

COUNTY :

OPERATION : Intermediate and Production Hole Sections

STATE :

REVISION : : / /

Component Descriptions

	Size	Pressure	Description
A	13 5/8"	LP	Rotating Head w/ Orbit Valve
B	13 5/8"	5,000 psi	Annular
C	13 5/8"	5,000 psi	Pipe Ram
D	13 5/8"	5,000 psi	Blind Ram
E	13 5/8"	5,000 psi	Mud Cross
F	13 5/8"	5,000 psi	Drilling Spool (as req'd)
G			
DSA (Int)	13 5/8" 3M x 13 5/8" 5M		
DSA (Prod)	11" 5M x 13 5/8" 5M		
B Sec	13 5/8" 3M x 11" 5M w/ 5M Gate Valves		
A Sec	13 5/8" 5OV x 13 5/8" 3M w/ 3M Gate Valve		

Quantity	Features


Trip Tank Required: Yes ☒ No ☐

Kill Line

ID	Pressure	Description
2 1/16"	5,000 psi	Check Valve
2 1/16"	5,000 psi	Gate Valve
2 1/16"	5,000 psi	Gate Valve

Choke Line

ID	Pressure	Description
3 1/16"	5,000 psi	Gate Valve
3 1/16"	5,000 psi	HCR Valve
3 1/16"	5,000 psi	Steel

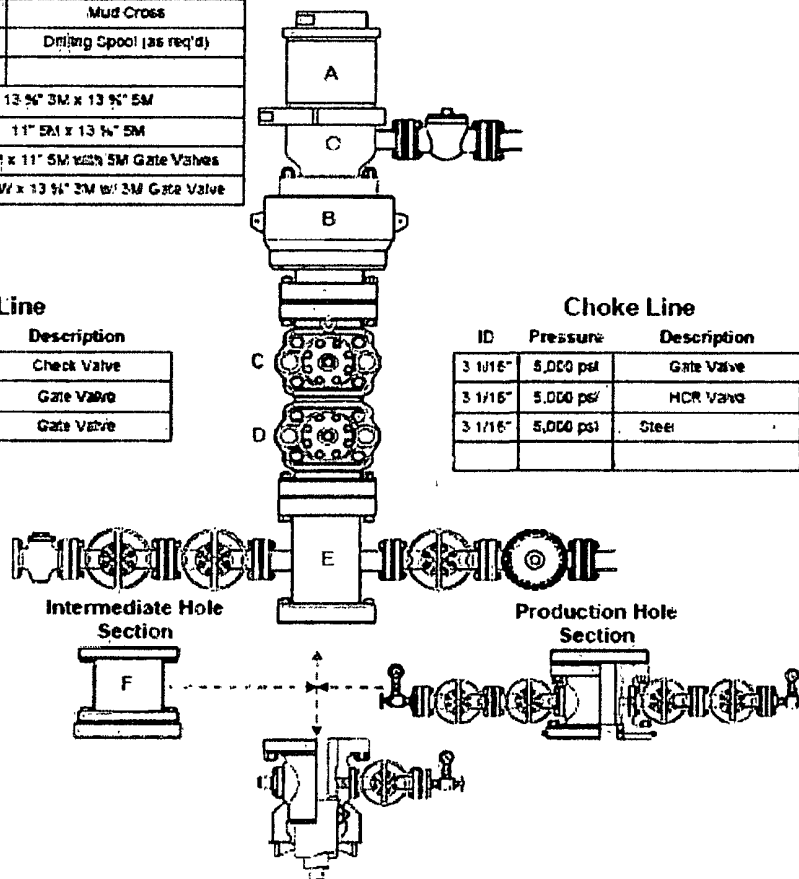

Testing Requirements

Item	Pressure	Frequency
Rotating Head	250 psi	Once prior to DO shoe
Annular	250 / 3,500 psi	Every 21 Days
Rams	250 / 5,000 psi	Every 21 Days
Choke Manifold	250 / 5,000 psi	Every 21 Days

- Function test on trips
- H₂S service trim required

Approved by

Date

CEO	
V.P.	
SEC	

EXHIBIT F1

Chesapeake Minimum BOPE Requirements

Wellname: PLU Big Sinks 24-24-30 USA 1H

Operation: Intermediate and Production Hole Sections

CHOKE MANIFOLD SCHEMATIC CHESAPEAKE OPERATING INC

WELL : Permian District

FIELD : Avalon

RIG :

COUNTY :

OPERATION :


STATE :

REVISION : : / /

Component Descriptions

	Size	Pressure	Description
A	3 1/16"	5,000 psi	Steel
B	3 1/16" x 2 1/16"	5,000 psi	Block Y
C	2 1/16"	5,000 psi	Top Valve
D	3 1/16"	5,000 psi	Gate Valve
E	2 1/16"	5,000 psi	Gate Valve
F	2 1/16"	5,000 psi	Manual Choke
G	2 1/16"	5,000 psi	Hydraulic Choke
H	6" minimum		Buffer Chamber

Equipment	Reference

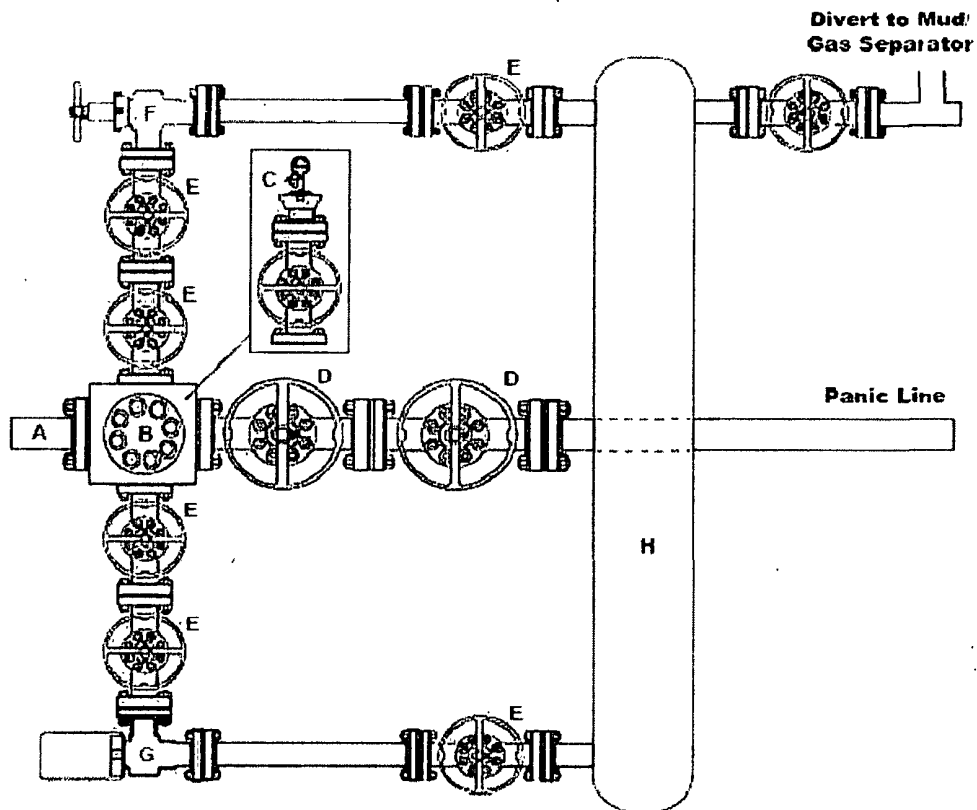

Approved by


Date

CEO	
VP	
ISC	

EXHIBIT F2



Chesapeake Energy

Reclamation
Area

General sealing of valves and sales by tank ganging.
Production phase: all drain valves (D1-D3) and sales valves (I1-I3) sealed closed. Sales phase: the tank from which sales are being made will be isolated by sealing closed the drain, fill, and any equalizer valves during sales. Draining phase: the tank being drained will be isolated by sealing closed the sales, fill, equalizer valves and drain valves on the other tanks.

300 Feet

Reclamation
Area

This lease is subject to
Chesapeake's Site
Security Plan located at
6100 N. Western
Oklahoma City, OK
73148

Drawing not to scale

Prepared by: Jean Ann Dunn
Date: 9-12-11

Approved by: Donny Lowry
Date: 9-12-11

EXHIBIT

H

PECOS DISTRICT CONDITIONS OF APPROVAL

OPERATOR'S NAME:	CHESAPEAKE OPERATING
LEASE NO.:	NM030453
WELL NAME & NO.:	1H PLU BIG SINKS 24-24-30 USA
SURFACE HOLE FOOTAGE:	10' FNL & 1980' FEL
BOTTOM HOLE FOOTAGE:	350' FSL & 1980' FEL
LOCATION:	Section 24, T.24 S., R.30 E., NMPM
COUNTY:	Eddy County, New Mexico

TABLE OF CONTENTS

Standard Conditions of Approval (COA) apply to this APD. If any deviations to these standards exist or special COAs are required, the section with the deviation or requirement will be checked below.

- ☐ **General Provisions**
- ☐ **Permit Expiration**
- ☐ **Archaeology, Paleontology, and Historical Sites**
- ☐ **Noxious Weeds**
- ☒ **Special Requirements**
 - Buried flowline not permitted**
 - Livestock fence**
 - Commercial Well Determination
- ☐ **Construction**
 - Notification
 - Topsoil
 - Closed Loop System
 - Federal Mineral Material Pits
 - Well Pads
 - Roads
- ☐ **Road Section Diagram**
- ☒ **Drilling**
 - Medium Cave/Karst
 - Logging requirements
 - Waste Material and Fluids
- ☐ **Production (Post Drilling)**
 - Well Structures & Facilities
 - Pipelines
 - Electric Lines
- ☒ **Interim Reclamation**
- ☒ **Final Abandonment & Reclamation**

I. GENERAL PROVISIONS

The approval of the Application For Permit To Drill (APD) is in compliance with all applicable laws and regulations: 43 Code of Federal Regulations 3160, the lease terms, Onshore Oil and Gas Orders, Notices To Lessees, New Mexico Oil Conservation Division (NMOCD) Rules, National Historical Preservation Act As Amended, and instructions and orders of the Authorized Officer. Any request for a variance shall be submitted to the Authorized Officer on Form 3160-5, Sundry Notices and Report on Wells.

II. PERMIT EXPIRATION

If the permit terminates prior to drilling and drilling cannot be commenced within 60 days after expiration, an operator is required to submit Form 3160-5, Sundry Notices and Reports on Wells, requesting surface reclamation requirements for any surface disturbance. However, if the operator will be able to initiate drilling within 60 days after the expiration of the permit, the operator must have set the conductor pipe in order to allow for an extension of 60 days beyond the expiration date of the APD. (Filing of a Sundry Notice is required for this 60 day extension.)

III. ARCHAEOLOGICAL, PALEONTOLOGY & HISTORICAL SITES

Any cultural and/or paleontological resource discovered by the operator or by any person working on the operator's behalf shall immediately report such findings to the Authorized Officer. The operator is fully accountable for the actions of their contractors and subcontractors. The operator shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery shall be made by the Authorized Officer to determine the appropriate actions that shall be required to prevent the loss of significant cultural or scientific values of the discovery. The operator shall be held responsible for the cost of the proper mitigation measures that the Authorized Officer assesses after consultation with the operator on the evaluation and decisions of the discovery. Any unauthorized collection or disturbance of cultural or paleontological resources may result in a shutdown order by the Authorized Officer.

IV. NOXIOUS WEEDS

The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes the roads, pads, associated pipeline corridor, and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

V. SPECIAL REQUIREMENT(S)

Buried pipeline is not permitted. The pipeline should be applied for by sundry notice with centerline survey.

Livestock fence

When interim reclamation is conducted, the fence should be constructed back to the original location

Commercial Well Determination

A commercial well determination will need to be submitted, after production has been established for at least six months.

VI. CONSTRUCTION

A. NOTIFICATION

The BLM shall administer compliance and monitor construction of the access road and well pad. Notify the Carlsbad Field Office at (575) 234-6235 at least 3 working days prior to commencing construction of the access road and/or well pad.

When construction operations are being conducted on this well, the operator shall have the approved APD and Conditions of Approval (COA) on the well site and they shall be made available upon request by the Authorized Officer.

B. TOPSOIL

The operator shall stockpile the topsoil in a low profile manner in order to prevent wind/water erosion of the topsoil. The topsoil to be stripped is approximately 4 inches in depth. The topsoil will be used for interim and final reclamation.

C. CLOSED LOOP SYSTEM

Tanks are required for drilling operations: No Pits.

The operator shall properly dispose of drilling contents at an authorized disposal site.

D. FEDERAL MINERAL MATERIALS PIT

Payment shall be made to the BLM prior to removal of any federal mineral materials. Call the Carlsbad Field Office at (575) 234-5972.

E. WELL PAD SURFACING

Surfacing of the well pad is not required.

If the operator elects to surface the well pad, the surfacing material may be required to be removed at the time of reclamation.

The well pad shall be constructed in a manner which creates the smallest possible surface disturbance, consistent with safety and operational needs.

F. ON LEASE ACCESS ROADS

Road Width

The access road shall have a driving surface that creates the smallest possible surface disturbance and does not exceed fourteen (14) feet in width. The maximum width of surface disturbance, when constructing the access road, shall not exceed twenty (20) feet.

Surfacing

Surfacing material is not required on the new access road driving surface. If the operator elects to surface the new access road or pad, the surfacing material may be required to be removed at the time of reclamation.

Where possible, no improvements should be made on the unsurfaced access road other than to remove vegetation as necessary, road irregularities, safety issues, or to fill low areas that may sustain standing water.

The Authorized Officer reserves the right to require surfacing of any portion of the access road at any time deemed necessary. Surfacing may be required in the event the road deteriorates, erodes, road traffic increases, or it is determined to be beneficial for future field development. The surfacing depth and type of material will be determined at the time of notification.

Crowning


Crowning shall be done on the access road driving surface. The road crown shall have a grade of approximately 2% (i.e., a 1" crown on a 14' wide road). The road shall conform to Figure 1; cross section and plans for typical road construction.

Ditching

Ditching shall be required on both sides of the road.

Turnouts

Vehicle turnouts shall be constructed on the road. Turnouts shall be intervisible with interval spacing distance less than 1000 feet. Turnouts shall be constructed on all blind curves. Turnouts shall conform to the following diagram:




Drainage

Drainage control systems shall be constructed on the entire length of road (e.g. ditches, sidehill outsloping and insloping, lead-off ditches, culvert installation, and low water crossings).

A typical lead-off ditch has a minimum depth of 1 foot below and a berm of 6 inches above natural ground level. The berm shall be on the down-slope side of the lead-off ditch.

Cross Section of a Typical Lead-off Ditch



All lead-off ditches shall be graded to drain water with a 1 percent minimum to 3 percent maximum ditch slope. The spacing interval are variable for lead-off ditches and shall be determined according to the formula for spacing intervals of lead-off ditches, but may be amended depending upon existing soil types and centerline road slope (in %);

Formula for Spacing Interval of Lead-off Ditches

Example - On a 4% road slope that is 400 feet long, the water flow shall drain water into a lead-off ditch. Spacing interval shall be determined by the following formula:

$$400 \text{ foot road with } 4\% \text{ road slope: } \frac{400'}{4\%} + 100' = 200' \text{ lead-off ditch interval}$$

Culvert Installations

Appropriately sized culvert(s) shall be installed at the deep waterway channel flow crossing.

Cattleguards

An appropriately sized cattleguard(s) sufficient to carry out the project shall be installed and maintained at fence crossing(s).

Any existing cattleguard(s) on the access road shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattleguard(s) that are in place and are utilized during lease operations.

A gate shall be constructed and fastened securely to H-braces.

Fence Requirement


Where entry is required across a fence line, the fence shall be braced and tied off on both sides of the passageway prior to cutting.

The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fence(s).

Public Access

Public access on this road shall not be restricted by the operator without specific written approval granted by the Authorized Officer.

Figure 1 – Cross Sections and Plans For Typical Road Sections

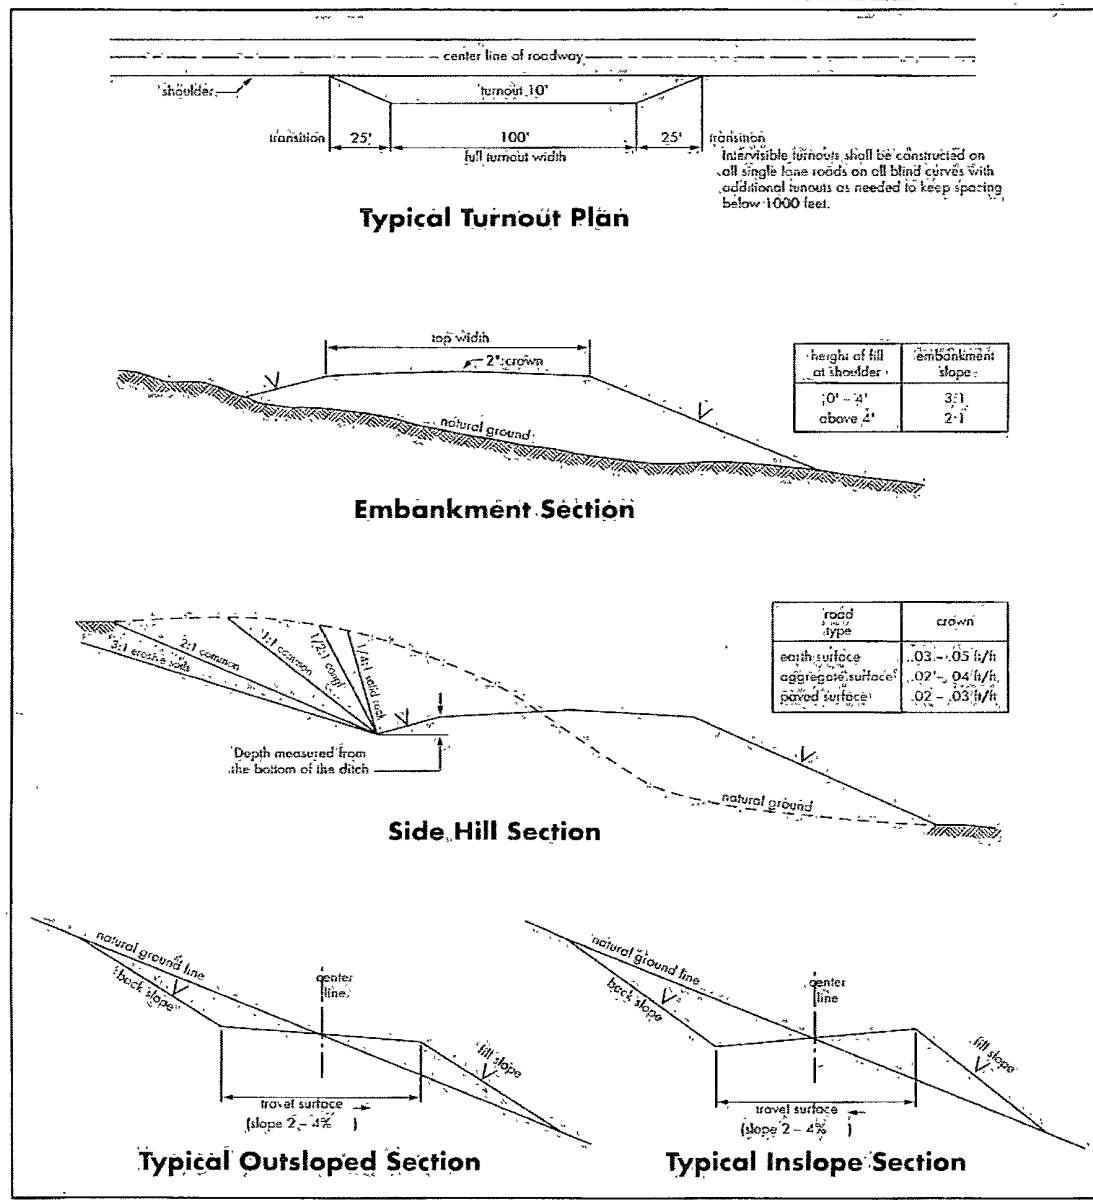

VII. DRILLING

A. DRILLING OPERATIONS REQUIREMENTS

The BLM is to be notified a minimum of 4 hours in advance for a representative to witness:

- a. Spudding well
- b. Setting and/or Cementing of all casing strings
- c. BOPE tests

☒ **Eddy County**

Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
(575) 361-2822

1. **Although Hydrogen Sulfide has not been reported in the area, it is always a potential hazard. If Hydrogen Sulfide is encountered, please report measured amounts and formations to the BLM.**
2. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval. **If the drilling rig is removed without approval – an Incident of Non-Compliance will be written and will be a “Major” violation.**
3. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
4. **The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.**

B. CASING

Changes to the approved APD casing and cement program require submitting a sundry and receiving approval prior to work. Failure to obtain approval prior to work will result in an Incident of Non-Compliance being issued.

Centralizers required on surface casing per Onshore Order 2.III.B.1.f.

Wait on cement (WOC) time prior to drilling out for a primary cement job will be a minimum 18 hours for a water basin, 24 hours in the potash area, or 500 pounds compressive strength, whichever is greater for all casing strings. DURING THIS WOC TIME, NO DRILL PIPE, ETC. SHALL BE RUN IN THE HOLE. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. See individual casing strings for details regarding lead cement slurry requirements.

No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.

Medium cave/karst

**Possible water flows in the Castile, Salado, Delaware and Bone Springs Groups
Possible lost circulation in the Delaware and Bone Spring formations**

1. The 13-3/8 inch surface casing shall be set at **approximately 660 feet (below the Magenta Dolomite member of the Rustler Anhydrite and above the salt)** and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. **Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry.**
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The minimum required fill of cement behind the 8-5/8 inch intermediate casing, **which is to be set in the base of the Castile or Lamar limestone at approximately 4050', is:**
 - ☒ Cement to surface. If cement does not circulate see B.1.a, c-d above. **Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst.**

If 75% or greater lost circulation occurs while drilling the intermediate casing hole, the cement on the production casing must come to surface.

Centralizers required on horizontal leg, must be type for horizontal service and a minimum of one every other joint.

3. The minimum required fill of cement behind the **5-1/2** inch production casing is:
 - a. First stage to DV tool, cement shall:
 - ☒ Cement to circulate. If cement does not circulate, contact the appropriate BLM office before proceeding with second stage cement job. Operator should have plans as to how they will achieve circulation on the next stage.
 - b. Second stage above DV tool, cement shall:
 - ☒ Cement should tie-back at least **500** feet into previous casing string. Operator shall provide method of verification.
4. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.

C. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **3000 (3M)** psi. **Operator installing a 5M and testing as a 3M.**
 - a. **For surface casing only:** If the BOP/BOPE is to be tested against casing, the wait on cement (WOC) time for that casing is to be met (see WOC statement at start of casing section). Independent service company required.
3. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.

- a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
- b. The tests shall be done by an independent service company utilizing a test plug **not a cup or J-packer**. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to Onshore Order 2 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (18 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
- c. The results of the test shall be reported to the appropriate BLM office.
- d. All tests are required to be recorded on a calibrated test chart. **A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.**
- e. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug.

D. DRILL STEM TEST

If drill stem tests are performed, Onshore Order 2.III.D shall be followed.

E. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

CRW 010512

VIII. PRODUCTION (POST DRILLING)

A. WELL STRUCTURES & FACILITIES

Placement of Production Facilities

Production facilities should be placed on the well pad to allow for maximum interim recontouring and revegetation of the well location.

Containment Structures

The containment structure shall be constructed to hold the capacity of the entire contents of the largest tank, plus 24 hour production, unless more stringent protective requirements are deemed necessary by the Authorized Officer.

Painting Requirement

All above-ground structures including meter housing that are not subject to safety requirements shall be painted a flat non-reflective paint color Shale Green, Munsell Soil Color Chart # 5Y 4/2

B. PIPELINES (not permitted)

C. ELECTRIC LINES (not applied for in APD)

IX. INTERIM RECLAMATION

During the life of the development, all disturbed areas not needed for active support of production operations should undergo interim reclamation in order to minimize the environmental impacts of development on other resources and uses.

Within six (6) months of well completion, operators should work with BLM surface management specialists (Jim Amos: 575-234-5909) to devise the best strategies to reduce the size of the location. Interim reclamation should allow for remedial well operations, as well as safe and efficient removal of oil and gas.

During reclamation, the removal of caliche is important to increasing the success of revegetating the site. Removed caliche that is free of contaminants may be used for road repairs, fire walls or for building other roads and locations. In order to operate the well or complete workover operations, it may be necessary to drive, park and operate on restored interim vegetation within the previously disturbed area. Disturbing revegetated areas for production or workover operations will be allowed. If there is significant disturbance and loss of vegetation, the area will need to be revegetated. Communicate with the appropriate BLM office for any exceptions/exemptions if needed.

All disturbed areas after they have been satisfactorily prepared need to be reseeded with the seed mixture provided below.

Seed Mixture for LPC Sand/Shinnery Sites

The holder shall seed all disturbed areas with the seed mixture listed below. The seed mixture shall be planted in the amounts specified in pounds of pure live seed (PLS)* per acre. There shall be no primary or secondary noxious weeds in the seed mixture. Seed will be tested and the viability testing of seed will be done in accordance with State law(s) and within nine (9) months prior to purchase. Commercial seed will be either certified or registered seed. The seed container will be tagged in accordance with State law(s) and available for inspection by the authorized officer.

Seed will be planted using a drill equipped with a depth regulator to ensure proper depth of planting where drilling is possible. The seed mixture will be evenly and uniformly planted over the disturbed area (smaller/heavier seeds have a tendency to drop the bottom of the drill and are planted first). The holder shall take appropriate measures to ensure this does not occur. Where drilling is not possible, seed will be broadcast and the area shall be raked or chained to cover the seed. When broadcasting the seed, the pounds per acre are to be doubled. The seeding will be repeated until a satisfactory stand is established as determined by the authorized officer. Evaluation of growth will not be made before completion of at least one full growing season after seeding.

Species to be planted in pounds of pure live seed* per acre:

<u>Species</u>	<u>lb/acre</u>
Plains Bristlegrass	5lbs/A
Sand Bluestem	5lbs/A
Little Bluestem	3lbs/A
Big Bluestem	6lbs/A
Plains Coreopsis	2lbs/A
Sand Dropseed	1lbs/A

*Pounds of pure live seed:

Pounds of seed x percent purity x percent germination = pounds pure live seed

FEDERAL PERMIT ATTACHED – READ CAREFULLY FOLLOW REQUIREMENTS

DATE: January 12, 2012
TO: DISTRIBUTION
FROM: Lyndee Songer
RE: **APD (Federal Permit) - APPROVED**
PLU Big Sinks 24-24-30 USA 1H
Section 15-25S-30E, Eddy County NM
BLM Lease: NMNM030453 (Surface)

Please be advised this well is subject to Bureau of Land Management (BLM) regulations and Minerals Management Service (MMS) reporting. **A copy of the BLM approved permit to drill must be on location at the date of first surface disturbance and thereafter, including any subsequent sundry notices changing the original APD.** A summary of BLM stipulations is set forth below, but is not a substitute for your review and compliance with all stipulations. In addition, these requirements are not in lieu of any state requirements; we must be in compliance with both state and federal rules and regulations. A copy of the approved federal permit is attached.

- **REVIEW AND COMPLY WITH THE CONDITIONS OF APPROVAL.** All operations, unless otherwise specifically approved in APD, must be conducted in accordance with Onshore Order No. 1 – Surface Use; Onshore Order No. 2 - Drilling Operations and Onshore Order No. 3 – Site Security.
- **REQUIREMENTS PRIOR TO & DURING CONSTRUCTION:**
 1. **Approved APD must be read carefully and followed by all parties involved. A complete copy must be on location at all times.**
 2. **The BLM will monitor construction of this drill site.** Contact the BLM Carlsbad Field Office at 575-234-5972 **at least 3 working days** prior to commencing construction of well pad (COA: V. Construction, A. Notification)
 3. Provide dirt contractor with copy of APD signature page, maps and drilling requirements.
 4. **Maintain existing access road pursuant to BLM standards. The Access road will be maintained with caliche material and shall be compacted to a minimum thickness of 6 inches for entire length of the travelway surface on the access road (Special Drilling Stipulations, Pg. 1, Item II).**
- **STANDARD and SPECIAL ENVIRONMENTAL STIPULATIONS:**
 1. All surface-disturbing activities will be restricted to approved areas. During surface-disturbing activities if any archeological items or foundations are encountered immediately contact BLM Carlsbad Field Office (III. Archaeological, Pg 2).
 2. Review drilling program under Conditions of Approval – VI. Drilling.

3. V-Door – Not stipulated.

4. Re-vegetate all reclaimed areas with desired seed mixture (Seed Mixture 2 Sandy Sites). If dry hole, restore to former land use. Seeding should be done in either late fall (Sep 15 to Nov 15) or early as possible in the spring.

SPECIAL REQUIREMENTS

1. The well pad and any collection facilities that are needed will be bermed to contain/control any spills or leaks on pad.

If questions arise regarding environmental/biological issues, contact BLM Carlsbad Field Office, NM, at 575-234-5972.

REPORTING REQUIREMENTS:

1. Contact **BLM Carlsbad** Field Office, at **575-234-5972**, **within 3 working days (72 hours) before** starting access road and/or well pad construction.
2. The BLM is to be notified a minimum of **4 hours** in advance for a representative to witness:
 - a. Spudding well
 - b. Setting and/or Cementing of all Casing strings
 - c. BOPE tests

Call the Carlsbad Field Office, at 575-361-2822. Daily progress report should include BLM staff that was notified (directly or otherwise).

3. Submit a Sundry Notice for each casing string, and cementing operations. The Sundry shall be submitted **within 15 days** of completion of each casing string. Reports may be combined into same Sundry if they fall within the same 15-day time frame.
4. **Production start-up** must be reported **within 5 business days** of production.
5. **Site Facility Diagram** must be submitted to BLM within **60 days** of production. Diagram should indicate required federal seals. (BOPCO TO SUBMIT)
6. **MMS revenue** must be reported by 4 p.m. Mountain Time **on or before the last day of the month following the month the product was removed from the lease or sold**, unless lease terms state otherwise. If the last day of the month, or the due date, falls on a weekend or Federal holiday, the report and payment are due by 4 p.m. Mountain Time the next business day.

If you have any questions or need additional information, please do not hesitate to call me at 405-935-2411.



New Mexico Energy, Minerals and Natural Resources Department

Susana Martinez
Governor

John H. Barnis
Cabinet Secretary-Designate

Brett F. Woods, Ph.D.
Deputy Cabinet Secretary

Jami Bailey
Division Director
Oil Conservation Division



November 7, 2011

Ocean Munds-Dry, Esq.
P.O. Box 2208
Santa Fe, NM 87504

Administrative Order NSL-6494

Re: Chesapeake Operating, Inc.
PLU Big Sinks 24 24 30 USA Well No. 1H (API No. 30-015-NA)
SHL/PP: 10 FNL 1980 FEL (BILL: 350 FSL 1980 FEL)
Project Area: Units B, G, J, O of Section 24, T24S, R30E
Eddy County, New Mexico

Dear Ms. Munds-Dry:

Reference is made to the following:

(a) your application (administrative application reference No. pTGW11-27028004) submitted to the New Mexico Oil Conservation Division (the Division) in Santa Fe, New Mexico, on behalf of Chesapeake Operating, Inc. (Chesapeake) [OGRID 147179], on September 26, 2011, and

(b) the Division's records pertinent to this request.

Chesapeake has requested to drill the above-referenced well as a horizontal well in the First Bone Spring Shale member of the Bone Spring formation, at a location that will be unorthodox under Division Rule 16.14.B(2) [19.15.16.14.B(2) NMAC].

The W/2 E/2 of Section 24 will be dedicated to the proposed well to form a project area comprising four standard 40-acre spacing units in the Wildcat; Bone Spring Pool. This pool is governed by statewide Rule 15.9 [19.15.15.9 NMAC], which provides for 40-acre units, with wells located at least 330 feet from a unit outer boundary. This location is unorthodox because it penetrates the pool at less than 330 feet from the northern portion of the project area.

The point of penetration of the top of the Bone Spring formation which is the top of the Wildcat; Bone Spring Pool is the same as the above referenced SHL. However, it is our



understanding that the well will be orthodox at the point of penetration of the target member of the Bone Spring formation.

Your application has been duly filed under the provisions of Division Rules 15.13 [19.15.15.13 NMAC] and 4.12.A(2) [19.15.4.12.A(2) NMAC].

It is our understanding that you are seeking this location for engineering reasons, in order to penetrate the maximum amount of the target zone within the producing area.

It is also understood that you have given due notice of this application to all operators or owners who are "affected persons," as defined in Rule 4.12.A(2) [19.15.4.12.A(2) NMAC], in all adjoining units towards which the proposed location encroaches.

Pursuant to the authority conferred by Division Rule 15.13.B [19.15.15.13.B NMAC], the above-described unorthodox location is hereby approved.

This approval is subject to your being in compliance with all other applicable Division rules, including, but not limited to, Division Rule 5.9 [19.15.5.9 NMAC].

Jurisdiction of this case is retained for the entry of such further orders as the Division may deem necessary.

Sincerely,



JAMI BAILEY
Director

JB/wvj

cc: Oil Conservation Division – Artesia
Bureau of Land Management – Carlsbad

DATE 9-26-11 SUSPENSE ENGINEER DB LOGGED 9.27.11 TYPE NSL APP NO 1127028004

ABOVE THIS LINE FOR DIVISION USE ONLY

NEW MEXICO OIL CONSERVATION DIVISION
- Engineering Bureau -
1220 South St. Francis Drive, Santa Fe, NM 87505



Chesapeake
PLU Big Links 24 24 30
USA #1H

ADMINISTRATIVE APPLICATION CHECKLIST

THIS CHECKLIST IS MANDATORY FOR ALL ADMINISTRATIVE APPLICATIONS FOR EXCEPTIONS TO DIVISION RULES AND REGULATIONS WHICH REQUIRE PROCESSING AT THE DIVISION LEVEL IN SANTA FE

Application Acronyms:

[NSL-Non-Standard Location] [NSP-Non-Standard Proration Unit] [SD-Simultaneous Dedication]
[DHC-Downhole Commingling] [CTB-Lease Commingling] [PLC-Pool/Lease Commingling]
[PC-Pool Commingling] [OLS - Off-Lease Storage] [OLM-Off-Lease Measurement]
[WFX-Waterflood Expansion] [PMX-Pressure Maintenance Expansion]
[SWD-Salt Water Disposal] [IPI-Injection Pressure Increase]
[EOR-Qualified Enhanced Oil Recovery Certification] [PPR-Positive Production Response]

[1] TYPE OF APPLICATION - Check Those Which Apply for [A]

- [A] Location - Spacing Unit - Simultaneous Dedication
☒ NSL ☐ NSP ☐ SD

Check One Only for [B] or [C]

- [B] Commingling - Storage - Measurement
☐ DHC ☐ CTB ☐ PLC ☐ PC ☐ OLS ☐ OLM

- [C] Injection - Disposal - Pressure Increase - Enhanced Oil Recovery
☐ WFX ☐ PMX ☐ SWD ☐ IPI ☐ EOR ☐ PPR

- [D] Other: Specify _____

RECEIVED OOD
2011 SEP 26 P 14 08

[2] NOTIFICATION REQUIRED TO: - Check Those Which Apply, or ☐ Does Not Apply

- [A] ☐ Working, Royalty or Overriding Royalty Interest Owners
[B] ☒ Offset Operators, Leaseholders or Surface Owner
[C] ☐ Application is One Which Requires Published Legal Notice
[D] ☐ Notification and/or Concurrent Approval by BLM or SLO
U.S. Bureau of Land Management - Commissioner of Public Lands, State Land Office
[E] ☐ For all of the above, Proof of Notification or Publication is Attached, and/or,
[F] ☐ Waivers are Attached

[3] SUBMIT ACCURATE AND COMPLETE INFORMATION REQUIRED TO PROCESS THE TYPE OF APPLICATION INDICATED ABOVE.

[4] CERTIFICATION: I hereby certify that the information submitted with this application for administrative approval is accurate and complete to the best of my knowledge. I also understand that no action will be taken on this application until the required information and notifications are submitted to the Division.

Note: Statement must be completed by an individual with managerial and/or supervisory capacity.

Ocean Munds Dry Ocean Munds Dry a Thorney 9-22-11
Print or Type Name Signature Title Date
omundsdry@hollandhart.com
e-mail Address

HOLLAND & HART



Ocean Munds-Dry
omundsdry@hollandhart.com

September 22, 2011

HAND-DELIVERED

Jami Bailey, Director
Oil Conservation Division
New Mexico Department of Energy,
Minerals and Natural Resources
1220 South Saint Francis Drive
Santa Fe, New Mexico 87505

Re: Application of Chesapeake Operating, Inc. for administrative approval of an unorthodox well location for its PLU Big Sinks 24 24 30 USA Well No. 1H to be drilled from a surface location and penetration point 10 feet from the North line and 1980 feet from the East line and a bottomhole location 350 feet from the South line and 1980 feet from the East line of Section 24, Township 24 South, Range 30 East, NMPM, Eddy County, New Mexico.

Dear Ms. Bailey:

Chesapeake Operating, Inc. ("Chesapeake") hereby seeks administrative approval pursuant to the provisions of Division Rules 19.15.15.13 and 19.15.16.14 for an unorthodox well location for its PLU Big Sinks 24 24 30 USA Well No. 1H. This wildcat well is located in Section 24, Township 24 South, Range 30 East, N.M.P.M., Eddy County, New Mexico and is to be drilled in the Bone Spring formation at a surface location and a penetration point 10 feet from the North line and 1980 feet from the East line and a bottomhole location 350 feet from the South and 1980 feet from the East line of Section 24, Eddy County, New Mexico. A 160-acre project area has been dedicated to this horizontal well comprised of the W/2 E/2 of Section 24.

This location is unorthodox because the Bone Spring formation under this acreage is governed by the Division's statewide rules which provide for wells on 40-acre spacing units to be located no closer than 330 feet to the outer boundary of the spacing unit. Division Rule 19.15.16.14 defines the "Penetration Point" as "the point where the wellbore penetrates the top of the pool from which it is intended to produce." The wellbore penetrates the Bone Spring formation at a point 10 feet from the North line of Section 24; it is, therefore, closer than allowed by Division rules.

Holland & Hart LLP

Phone [505] 988-4421 Fax [505] 983-6043 www.hollandhart.com

110 North Guadalupe Suite 1 Santa Fe, NM 87501 Mailing Address PO Box 2268 Santa Fe, NM 87504-2208

Aspen Billings Boise Boulder Cheyenne Colorado Springs Denver Denver Tech Center Jackson Hole Salt Lake City Santa Fe Washington, D.C. ☏

HOLLAND & HART

Although the wellbore penetrates the top of the Bone Spring at an unorthodox location, the well will be at a standard location at the producing interval. Chesapeake is targeting the First Bone Spring Shale at approximately 9,192 feet (TVD). Therefore, once Chesapeake reaches the targeted formation, it will be at a standard location.


Exhibit A is a plat showing the location of the well. This location is encroaching to the north of Section 24. This location is within the Poker Lake Unit which is operated by BOPCo. A copy of this application with all attachments was mailed to BOPCo. and OGX and they were advised that if they have an objection to this application it must be filed in writing with the Division's Santa Fe office within twenty days from the date notice was sent. BOPCo. and OGX were also advised that if no objections were received by the Division within twenty days, the Division Director could approve the application.

Exhibit B is the C-102 for this well.

Exhibit C is the notice list.

Your attention to this application is appreciated.

Sincerely,



Ocean Munds-Dry
ATTORNEY FOR
CHESAPEAKE OPERATING, INC.

Enclosures

cc: OCD District Office - Artesia

DISTRICT I --- CHECKLIST FOR INTENTS TO DRILL

"out of compliance"
Ltr 1/17/2012

39031

Operator CHESA POAKO OGRID # 147179
Well Name & # PLU BIG SINKS 24 24 30 Surface Type (F)(S)(P)
Location: UL Sect Township s, RNG e, Sub-surface Type (F)(S)(P)

A. Date C101 rec'd 1/11/2012 C101 reviewed 1/17/2012

B. 1. Check mark, Information is OK on Forms:

OGRID ✓, BONDING ✓, PROP CODE , WELL # , SIGNATURE

2. Inactive Well list as of: 1/17/2012 # wells 748, # Inactive wells 754

a. District Grant APD but see number of inactive wells:

No letter required ; Sent Letter to Operator , to Santa Fe ✓ 1/17/2012

3. Additional Bonding as of: 1/17/2012

a. District Denial because operator needs addition bonding:

No Letter required ✓; Sent Letter to Operator , To Santa Fe

b. District Denial because of inactive well list and Financial Assurance:

No Letter required ✓; Sent Letter to Operator , To Santa Fe

C. C102 YES ✓ NO , Signature ✓

1. Pool WILDCAT; BONE SPMS, Code 96403

a. Dedicated acreage , What Units

b. SUR. Location Standard ; Non-Standard Location

c. Well shares acres: Yes , No , # of wells plus this well #

2. 2nd. Operator in same acreage, Yes , No

Agreement Letter , Disagreement letter

3. Intent to Directional Drill Yes ✓, No

a. Dedicated acreage 160, What Units

b. Bottomhole Location Standard , Non-Standard Bottomhole

4. Downhole Commingle: Yes , No

a. Pool #2 , Code , Acres

Pool #3 , Code , Acres

Pool #4 , Code , Acres

5. POTASH Area Yes , No ✓

D. Blowout Preventer Yes ✓, No

E. H2S Yes ✓, No

F. C144 Pit Registration Yes ✓, No

G. Does APD require Santa Fe Approval:

1. Non-Standard Location: Yes ✓, No , NSL # 6494-0

2. Non-Standard Proration: Yes , No ✓, NSP #

3. Simultaneous Dedication: Yes , No ✓, SD #

Number of wells Plus #

4. Injection order Yes , No ✓; PMX # or WFX #

5. SWD order Yes , NO ✓; SWD #

6. DHC from SF ; DHC-HOB ; Holding

7. OCD Approval Date 1/20/2012

API #30-0 15-39846

8. Reviewers tes
