

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENTN.M. Oil Cons. Div-Dist. 2
1301 W. Grand Avenue
Artesia, NM 88210

SUBMIT IN DUPLICATE

FORM APPROVED

OMB NO. 1004-0137

Expires: February 28, 1995

LEASE DESIGNATION AND SERIAL NO.

NMNM112273

WELL COMPLETION OR RECOMPLETION REPORT AND LOG*

1a. TYPE OF WELL:

OIL
WELLGAS
WELL ☒

DRY

Other

b. TYPE OF COMPLETION:

NEW
WELL ☒WORK
OVERDEEP-
ENPLUG
BACKDIFF.
RES/V

Other

2. NAME OF OPERATOR

MARBOB ENERGY CORPORATION

3. ADDRESS AND TELEPHONE NO.

PO BOX 227, ARTESIA, NM 88211-0227

4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements*)

At surface 1095 FSL 430 FWL, LOT 4

At top prod. interval reported below

At total depth 1650 FSL 660 FWL, LOT 3

14. PERMIT NO.

DATE ISSUED

6. IF INDIAN, ALLOTTEE OR TRIBE NAME

7. UNIT AGREEMENT NAME

8. FARM OR LEASE NAME, WELL NO.

COLLINSOSCOPY FEDERAL #1

9. API WELL NO.

30-015-33758

10. FIELD AND POOL, OR WILDCAT

BURTON FLAT; MORROW, EAST

11. SEC., T., R., M., OR BLOCK AND SURVEY
OR AREA

SEC. 7-T20S-R30E

12. COUNTY OR PARISH

EDDY

NM

15. DATE SPUDDED

12/18/04

16. DATE T.D. REACHED

2/6/05

17. DATE COMPL. (Ready to prod.)

3/16/05

18. ELEVATIONS (DF, RKB, RT, GE, ETC.)*

3310' GL

19. ELEV. CASINGHEAD

20. TOTAL DEPTH, MD & TVD

12400'

21. PLUG, BACK T.D., MD & TVD

11965'

22. IF MULTIPLE COMPL.,
HOW MANY*23. INTERVALS
DRILLED BY

ROTARY TOOLS

0 - 12400'

CABLE TOOLS

24. PRODUCING INTERVAL(S), OF THIS COMPLETION-TOP, BOTTOM, NAME (MD AND TVD)*

11838' - 11932' MORROW

26. TYPE ELECTRIC AND OTHER LOGS RUN

DLL, CSNG

27. WAS WELL CORED

NO

28. CASING RECORD (Report all strings set in well)

CASING SIZE/GRADE	WEIGHT, LB./FT.	DEPTH SET (MD)	HOLE SIZE	TOP OF CEMENT, CEMENTING RECORD	AMOUNT PULLED
20" H40	94#	315'	26"	750 SX	NONE
13 3/8" J55	54.5#	1783'	17 1/2"	1350 SX, CIRC	NONE
8 5/8" J55	32#	3425'	12 1/4"	1400 SX, CIRC	NONE
5 1/2" P110	17#	12400'	7 7/8"	2100 SX, TOC @ 2000'	NONE

29. LINER RECORD

30. TUBING RECORD

SIZE	TOP (MD)	BOTTOM (MD)	SACKS CEMENT*	SCREEN (MD)	SIZE	DEPTH SET (MD)	PACKER SET (MD)
					2 3/8"	11748'	

31. PERFORATION RECORD (Interval, size and number)

12144' - 12199' (64 SHOTS)
12043' - 12053' (11 SHOTS)
11990' - 10994' (10 SHOTS)
11838' - 11932' (168 SHOTS)

32. ACID, SHOT, FRACTURE, CEMENT SQUEEZE, ETC.

DEPTH INTERVAL (MD)	AMOUNT AND KIND OF MATERIAL USED
12144'-12199'	ACDZ W/ 1000 GAL CLAY SAFE H
12144'-12199'	FRAC W/ 30300# VERSAPROP
12043'-12053'	ACDZ W/ 500 GAL CLAY SAFE H
11990'-12053'	SQZ W/ 150 SX PREM CMT

33. PRODUCTION

DATE FIRST PRODUCTION

4/7/05

PRODUCTION METHOD (Flowing, gas lift, pumping--size and type of pump)

FLOWING

WELL STATUS (Producing or
shut-in)

PROD

DATE OF TEST

4/10/05

HOURS TESTED

24

CHOKE SIZE

PROD'N FOR
TEST PERIOD

OIL--BBL.

22

GAS--MCF.

1956

WATER--BBL.

2

GAS-OIL RATIO

FLOW. TUBING PRESS.

CASING PRESSURE

CALCULATED
24-HOUR RATE

OIL--BBL.

GAS--MCF.

WATER--BBL.

OIL GRAVITY-API (CORR.)

RECEIVED

34. DISPOSITION OF GAS (Sold, used for fuel, vented, etc.)

SOLD

MAY 24 2005

TEST WITNESSED BY

OWEN PUCKETT

35. LIST OF ATTACHMENTS

LOGS, DEVIATION SURVEYS

OCD-ARTESIA

36. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records

SIGNED

TITLE

PRODUCTION ANALYST

DATE 5/1/05

*(See Instructions and Spaces for Additional Data on Reverse Side)

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Patriot Drilling, LLC

OPERATOR: Marbob Energy Group
WELL/LEASE: Collinscopy
COUNTY: Eddy County, NM

STATE OF NEW MEXICO


DEVIATION REPORT


<u>Depth</u>	<u>Deviation</u>
10096	1
10585	2
10716	3/4
10972	1
11253	3/4
11526	1
11761	1/2


M. Leroy Peterson

The foregoing instrument was acknowledged before me on this 10th day of February, 2005 by Leroy Peterson, Executive Vice-President of Patriot Drilling, LLC.


My Commission Expires: 5/29/2005




Notary Public for Midland County, Texas

37. SUMMARY OF POROUS ZONES: (Show all important zones of porosity and contents thereof; cored intervals; and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures, and recoveries):

38. GEOLOGICAL MARKERS			38. GEOLOGICAL MARKERS		
NAME	TOP		NAME	TOP	
	MEAS. DEPTH	TRUE VERT. DEPTH		MEAS. DEPTH	TRUE VERT. DEPTH
YATES	1708'				
SEVEN RIVERS	1988'				
CAPITAN	2136'				
DELAWARE	3309'				
BONE SPRING	6468'				
WOLFCAMP	9789'				
STRAWN	10818'				
ATOKA	11200'				
MORROW CLASTICS	11884'				



Scientific Drilling

MARBOB ENERGY

Field: Burton Flat
Site: Eddy County, NM
Well: Collinsoscopy Fed #1
Wellpath: VH - Job #32K0105041
Survey: 01/15/04


This survey is correct to the best of my knowledge
and is supported by actual field data.

Scott N. Naylor Company Representative

Notorized this date 7th of February, 2005.

Deborah Sue Bynum

Notary Signature
County of Midland
State of Texas





Scientific
Drilling

Scientific Drilling International

Survey Report

Company: MARBOB ENERGY
Field: Burton Flat
Site: Eddy County, NM
Well: Collinsoscopy Fed #1
Wellpath: VH - Job #32K0105041

Date: 2/7/2005 Time: 21:12:49 Page: 1
Co-ordinate(NE) Reference: Site: Eddy County, NM, Grid North
Vertical (TVD) Reference: SITE 0.0
Section (VS) Reference: Well (0.00N,0.00E,30.74Azi)
Survey Calculation Method: Minimum Curvature Db: Sybase

Survey: 01/15/04
KSRG 0'-6480'

Start Date: 1/15/2005

Company: Scientific Drilling Internatio
Tool: Keeper;Keeper Gyro

Engineer: Carter w/P&M
Tied-to: From Surface

Survey

MD ft	Incl deg	Azim deg	TVD ft	VS ft	N/S ft	E/W ft	DLS deg/100ft	ClsD ft	ClsA deg
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
100.00	0.32	72.36	100.00	0.21	0.08	0.27	0.32	0.28	72.36
200.00	0.65	47.02	200.00	0.96	0.56	0.95	0.39	1.10	59.58
300.00	0.77	40.41	299.99	2.17	1.46	1.80	0.14	2.32	51.03
400.00	0.68	58.85	399.98	3.36	2.28	2.74	0.25	3.57	50.33
500.00	0.97	65.61	499.97	4.58	2.93	4.02	0.31	4.98	53.92
600.00	1.16	56.10	599.95	6.19	3.85	5.64	0.26	6.82	55.68
700.00	0.85	59.72	699.94	7.75	4.79	7.12	0.31	8.58	56.08
800.00	1.11	76.37	799.92	9.08	5.39	8.70	0.38	10.24	58.23
900.00	1.17	76.60	899.90	10.47	5.85	10.64	0.06	12.14	61.17
1000.00	1.17	66.50	999.88	12.00	6.50	12.56	0.21	14.14	62.65
1100.00	0.79	76.34	1099.87	13.32	7.07	14.17	0.41	15.83	63.49
1200.00	0.88	76.93	1199.86	14.33	7.40	15.59	0.09	17.26	64.60
1300.00	0.68	74.22	1299.85	15.30	7.74	16.92	0.21	18.60	65.41
1400.00	0.71	99.93	1399.84	15.95	7.79	18.10	0.31	19.70	66.70
1500.00	0.66	107.55	1499.83	16.30	7.51	19.26	0.10	20.67	68.69
1600.00	0.71	92.00	1599.83	16.73	7.32	20.43	0.19	21.70	70.29
1700.00	0.85	77.53	1699.82	17.54	7.46	21.77	0.24	23.01	71.09
1800.00	0.90	76.92	1799.80	18.59	7.80	23.26	0.05	24.53	71.47
1900.00	1.05	74.03	1899.79	19.80	8.23	24.91	0.16	26.23	71.73
2000.00	1.35	79.78	1999.77	21.24	8.69	26.95	0.33	28.32	72.13
2100.00	1.60	60.82	2099.74	23.22	9.58	29.33	0.54	30.85	71.92
2200.00	1.66	67.42	2199.70	25.59	10.81	31.89	0.20	33.67	71.27
2300.00	1.94	67.84	2299.65	28.10	12.01	34.79	0.28	36.81	70.96
2400.00	2.08	67.84	2399.58	30.90	13.33	38.04	0.14	40.31	70.69
2500.00	2.14	70.61	2499.52	33.78	14.64	41.48	0.12	43.99	70.57
2600.00	2.10	69.40	2599.45	36.65	15.90	44.96	0.06	47.69	70.52
2700.00	1.78	68.16	2699.39	39.31	17.12	48.12	0.33	51.07	70.41
2800.00	1.65	73.97	2799.35	41.59	18.10	50.94	0.21	54.06	70.44
2900.00	1.67	76.22	2899.30	43.66	18.84	53.74	0.07	56.95	70.68
3000.00	1.41	69.24	2999.27	45.65	19.62	56.30	0.32	59.62	70.78
3100.00	1.38	74.72	3099.24	47.48	20.38	58.62	0.14	62.06	70.83
3200.00	1.53	70.63	3199.21	49.37	21.14	61.04	0.18	64.60	70.90
3300.00	0.96	77.19	3299.18	50.97	21.77	63.12	0.59	66.77	70.97
3400.00	0.89	74.44	3399.17	52.11	22.16	64.68	0.08	68.37	71.09
3500.00	0.91	89.38	3499.16	53.08	22.38	66.22	0.24	69.90	71.33
3600.00	0.98	86.72	3599.14	53.98	22.44	67.88	0.09	71.49	71.71
3700.00	0.93	81.20	3699.13	54.97	22.61	69.53	0.11	73.12	71.99
3800.00	0.69	93.74	3799.12	55.76	22.69	70.93	0.29	74.48	72.26
3900.00	0.50	69.73	3899.11	56.38	22.81	71.94	0.31	75.47	72.41
4000.00	0.54	82.41	3999.11	57.01	23.02	72.82	0.12	76.37	72.46
4100.00	0.59	81.32	4099.11	57.62	23.16	73.79	0.05	77.34	72.58
4200.00	0.75	58.16	4199.10	58.53	23.58	74.86	0.31	78.48	72.51
4300.00	0.66	42.39	4299.09	59.67	24.35	75.80	0.21	79.61	72.19
4400.00	0.65	57.28	4399.08	60.75	25.09	76.67	0.17	80.67	71.88
4500.00	0.58	29.82	4499.08	61.76	25.83	77.40	0.30	81.59	71.54
4600.00	0.28	44.02	4599.08	62.50	26.44	77.82	0.31	82.19	71.23
4700.00	0.43	26.42	4699.07	63.11	26.95	78.15	0.18	82.67	70.97
4800.00	0.41	333.08	4799.07	63.67	27.60	78.16	0.38	82.89	70.55



Scientific
Drilling

Scientific Drilling International

Survey Report

Company: MARBOB ENERGY
Field: Burton Flat
Site: Eddy County, NM
Well: Collinoscopy Fed #1
Wellpath: VH - Job #32K0105041

Date: 2/7/2005 Time: 21:12:49 Page: 2
Co-ordinate(NE) Reference: Site: Eddy County, NM, Grid North
Vertical (TVD) Reference: SITE 0.0
Section (VS) Reference: Well (0.00N,0.00E,30.74Azi)
Survey Calculation Method: Minimum Curvature Db: Sybase



Survey

MD ft	Incl deg	Azim deg	TVD ft	VS ft	N/S ft	E/W ft	DLS deg/100ft	ClsD ft	ClsA deg
4900.00	0.33	332.63	4899.07	64.02	28.18	77.86	0.08	82.80	70.10
5000.00	0.32	349.79	4999.07	64.38	28.71	77.68	0.10	82.81	69.72
5100.00	0.41	3.26	5099.07	64.91	29.34	77.65	0.12	83.01	69.30
5200.00	0.56	3.71	5199.06	65.66	30.19	77.70	0.16	83.36	68.77
5300.00	0.72	351.98	5299.06	66.59	31.30	77.65	0.20	83.72	68.05
5400.00	0.75	339.74	5399.05	67.49	32.53	77.33	0.16	83.90	67.19
5500.00	0.60	2.59	5499.04	68.36	33.66	77.13	0.30	84.16	66.42
5600.00	0.49	320.22	5599.04	68.96	34.51	76.88	0.41	84.28	65.82
5700.00	0.46	338.31	5699.03	69.35	35.22	76.46	0.15	84.18	65.27
5800.00	0.51	349.18	5799.03	69.93	36.03	76.23	0.10	84.32	64.70
5900.00	0.55	342.09	5899.03	70.58	36.92	76.00	0.07	84.49	64.09
6000.00	0.53	318.24	5999.02	71.04	37.72	75.54	0.22	84.44	63.47
6100.00	0.58	343.61	6099.02	71.52	38.55	75.09	0.25	84.41	62.83
6200.00	0.77	274.85	6199.01	71.57	39.09	74.29	0.78	83.94	62.25
6300.00	0.60	342.78	6299.01	71.62	39.64	73.46	0.78	83.48	61.65
6400.00	0.51	318.54	6399.00	72.11	40.48	73.01	0.25	83.48	61.00
6480.00	0.24	297.92	6479.00	72.21	40.82	72.63	0.38	83.31	60.66



Scientific
Drilling

Field: Burton Flat
Site: Eddy County, NM
Well: Collinsoscopy Fed #1
Wellpath: VH - Job #32K0105041
Survey: 01/15/04

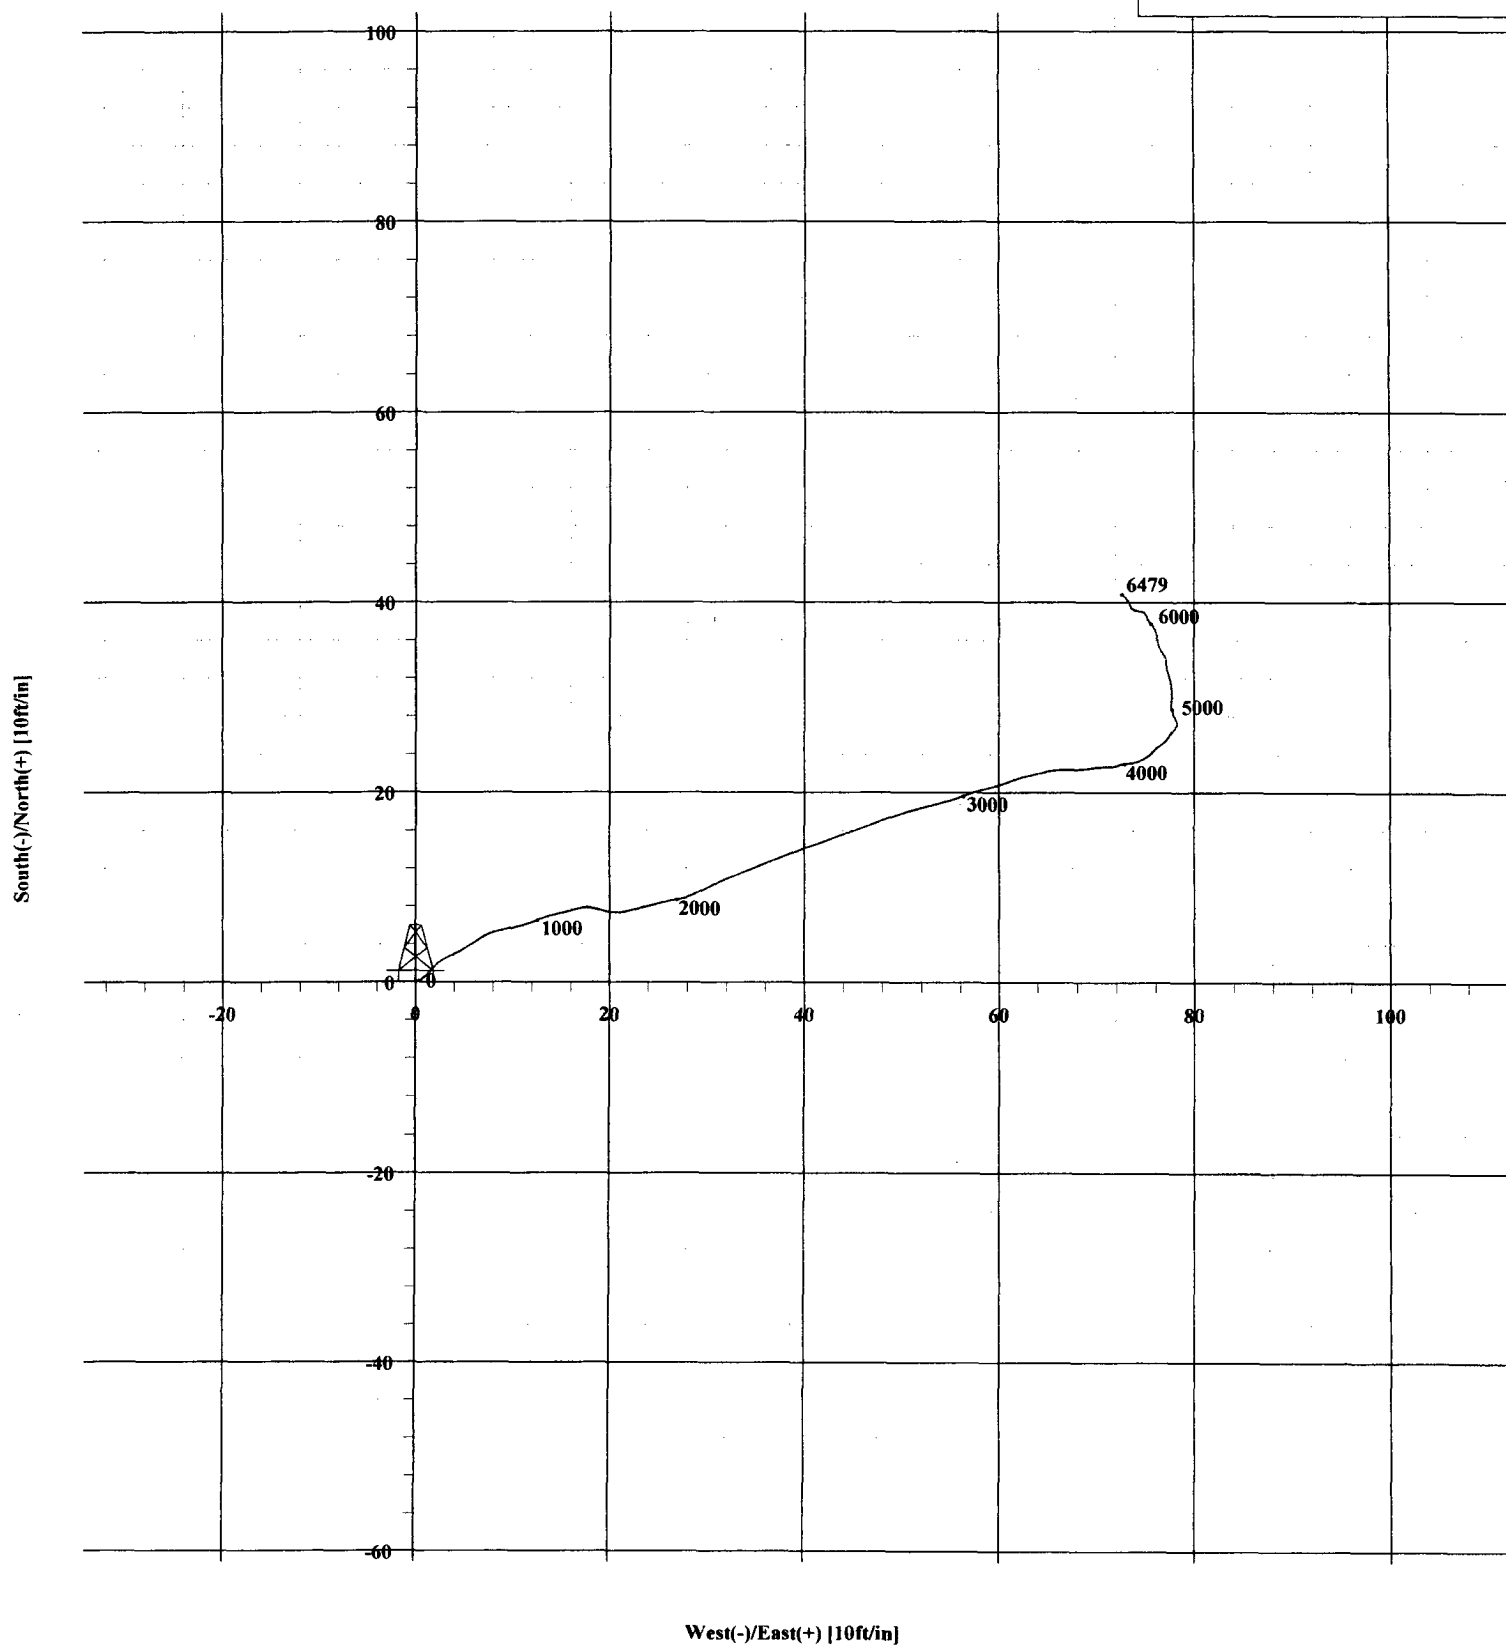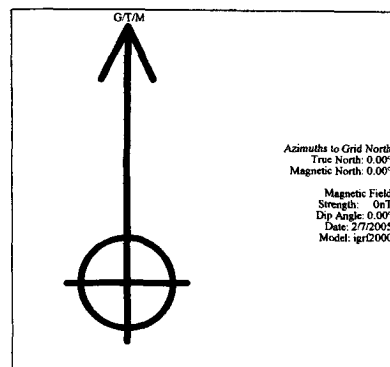

PathFinder

Survey Report

Company: Marbob Energy Field: Collinsoscopy Federal #1 Site: Section 7, T-20S, R-30E Well: Collinsoscopy Federal #1 Wellpath: Original Hole	Date: 2/2/2005 Co-ordinate(NE) Reference: Well: Collinsoscopy Federal #1 Vertical (TVD) Reference: SITE 0.0 Section (VS) Reference: Well (0.00N,0.00E,31.75Azi) Survey Calculation Method: Minimum Curvature	Time: 15:31:35 Page: 1 Db: Sybase
--	---	--

Field: Collinsoscopy Federal #1		
Map System: US State Plane Coordinate System 1927 Geo Datum: NAD27 (Clarke 1866) Sys Datum: Mean Sea Level	Map Zone: New Mexico, Eastern Zone Coordinate System: Well Centre Geomagnetic Model: igrf2005	

Site: Section 7, T-20S, R-30E		
Eddy County, NM		
Site Position: From: Geographic Position Uncertainty: 0.00 ft Ground Level: 3310.00 ft	Northing: 576144.13 ft Easting: 597137.15 ft	Latitude: 32 35 0.710 N Longitude: 104 1 4.690 W North Reference: True Grid Convergence: 0.17 deg

Well: Collinsoscopy Federal #1 Well Position: +N/-S 0.00 ft +E/-W 0.00 ft Position Uncertainty: 0.00 ft	Slot Name: Well Position: +N/-S 0.00 ft +E/-W 0.00 ft Position Uncertainty: 0.00 ft	Latitude: 32 35 0.710 N Longitude: 104 1 4.690 W
---	---	---

Wellpath: Original Hole Current Datum: SITE Magnetic Data: 1/18/2005 Field Strength: 49462 nT Vertical Section: Depth From (TVD) ft	Height 0.00 ft +N/-S ft ft	Drilled From: Surface Tie-on Depth: 0.00 ft Above System Datum: Mean Sea Level Declination: 8.57 deg Mag Dip Angle: 60.60 deg +E/-W Direction deg ft deg ft deg
0.00	0.00	0.00 31.75

Survey: PathFinder MWD Surveys Company: PathFinder Energy Services Tool:	Start Date: 1/18/2005 Engineer: Ron McIntyre Tied-to: From: Definitive Path
---	--

Survey: PathFinder MWD Surveys										
MD ft	Incl deg	Azim deg	TVD ft	+N/-S ft	+E/-W ft	VS ft	DLS deg/100ft	Build deg/100ft	Turn deg/100ft	Tool/Comment
6480.00	0.24	297.92	6479.00	40.84	72.60	72.93	0.00	0.00	0.00	Tie-In to Gyro Begin PathFinder Surveys
6517.00	0.79	9.31	6516.00	41.13	72.57	73.16	2.02	1.49	192.95	
6580.00	1.32	21.26	6578.99	42.23	72.90	74.27	0.91	0.84	18.97	
6644.00	0.88	17.22	6642.98	43.39	73.31	75.47	0.70	-0.69	-6.31	
6708.00	0.88	38.40	6706.97	44.24	73.76	76.44	0.51	0.00	33.09	
6771.00	0.97	42.00	6769.96	45.02	74.42	77.44	0.17	0.14	5.71	
6835.00	1.14	0.78	6833.95	46.06	74.79	78.52	1.19	0.27	-64.41	
6899.00	0.97	344.70	6897.94	47.22	74.66	79.44	0.53	-0.27	-25.13	
6962.00	1.06	0.69	6960.93	48.31	74.53	80.30	0.47	0.14	25.38	
7026.00	0.97	0.52	7024.92	49.45	74.54	81.27	0.14	-0.14	-0.27	
7089.00	1.06	349.09	7087.91	50.55	74.43	82.15	0.35	0.14	-18.14	
7153.00	1.76	348.83	7151.89	52.10	74.13	83.31	1.09	1.09	-0.41	
7216.00	3.17	359.90	7214.83	54.79	73.94	85.50	2.35	2.24	17.57	
7280.00	3.96	356.48	7278.71	58.76	73.80	88.80	1.28	1.23	-5.34	
7343.00	5.63	356.04	7341.48	64.02	73.45	93.09	2.65	2.65	-0.70	
7407.00	6.68	358.58	7405.11	70.87	73.14	98.76	1.69	1.64	3.97	
7471.00	9.50	5.70	7468.47	79.85	73.58	106.62	4.67	4.41	11.13	
7534.00	12.05	10.80	7530.36	91.49	75.33	117.43	4.32	4.05	8.10	
7598.00	14.95	15.20	7592.58	106.02	78.74	131.59	4.80	4.53	6.87	
7661.00	16.36	16.87	7653.25	122.35	83.45	147.95	2.35	2.24	2.65	
7725.00	16.44	14.40	7714.64	139.75	88.32	165.31	1.10	0.12	-3.86	
7788.00	16.53	18.89	7775.06	156.86	93.44	182.56	2.03	0.14	7.13	
7852.00	15.30	17.92	7836.60	173.51	98.98	199.63	1.97	-1.92	-1.52	
7915.00	16.53	22.93	7897.19	189.68	105.03	216.56	2.93	1.95	7.95	

PathFinder Survey Report

Company: Marbob Energy Field: Collinsoscopy Federal #1 Site: Section 7, T-20S, R-30E Well: Collinsoscopy Federal #1 Wellpath: Original Hole	Date: 2/2/2005 Co-ordinate(NE) Reference: Vertical (TVD) Reference: Section (VS) Reference: Survey Calculation Method: Minimum Curvature	Time: 15:31:35 Well: Collinsoscopy Federal #1 SITE: 0.0 Well (0.00N,0.00E,31.75Azi) Db: Sybase	Page: 2
--	---	---	----------------

Survey: PathFinder MWD Surveys

MD ft	Incl deg	Azim deg	TVD ft	+N/-S ft	+E/-W ft	VS ft	DLS deg/100ft	Build deg/100ft	Turn deg/100ft	Tool/Comment
7979.00	17.15	20.82	7958.44	206.88	111.93	234.82	1.36	0.97	-3.30	
8043.00	17.50	25.34	8019.54	224.40	119.40	253.65	2.17	0.55	7.06	
8106.00	16.80	22.67	8079.74	241.36	126.97	272.06	1.67	-1.11	-4.24	
8170.00	16.62	24.07	8141.04	258.25	134.27	290.26	0.69	-0.28	2.19	
8233.00	17.59	30.14	8201.26	274.71	142.72	308.71	3.22	1.54	9.63	
8297.00	19.35	36.03	8261.96	291.66	153.82	328.95	4.00	2.75	9.20	
8361.00	19.70	37.70	8322.28	308.77	166.65	350.25	1.03	0.55	2.61	
8456.00	18.82	39.28	8411.97	333.30	186.14	381.37	1.08	-0.93	1.66	
8520.00	19.43	39.45	8472.43	349.51	199.44	402.15	0.96	0.95	0.27	
8583.00	18.73	37.96	8531.97	365.57	212.32	422.59	1.35	-1.11	-2.37	
8679.00	18.20	37.21	8623.03	389.67	230.87	452.84	0.60	-0.55	-0.78	
8742.00	16.88	38.31	8683.10	404.68	242.49	471.72	2.16	-2.10	1.75	
8806.00	16.18	38.40	8744.45	418.96	253.79	489.81	1.09	-1.09	0.14	
8869.00	16.53	36.90	8804.91	433.01	264.62	507.45	0.87	0.56	-2.38	
8933.00	16.80	35.50	8866.22	447.82	275.46	525.75	0.76	0.42	-2.19	
8997.00	16.71	33.39	8927.50	463.03	285.89	544.18	0.96	-0.14	-3.30	
9060.00	15.48	30.49	8988.03	477.84	295.15	561.64	2.33	-1.95	-4.60	
9124.00	14.16	29.87	9049.90	491.98	303.38	578.00	2.08	-2.06	-0.97	
9187.00	14.51	30.14	9110.94	505.49	311.18	593.59	0.57	0.56	0.43	
9251.00	13.72	30.05	9173.01	519.00	319.00	609.19	1.23	-1.23	-0.14	
9314.00	13.10	33.48	9234.29	531.42	326.68	623.80	1.60	-0.98	5.44	
9379.00	12.57	35.50	9297.67	543.32	334.86	638.22	1.07	-0.82	3.11	
9443.00	12.53	33.65	9360.14	554.77	342.75	652.11	0.63	-0.06	-2.89	
9506.00	12.05	32.69	9421.69	565.99	350.09	665.51	0.83	-0.76	-1.52	
9570.00	11.70	35.59	9484.32	576.89	357.47	678.67	1.08	-0.55	4.53	
9633.00	10.90	36.82	9546.10	586.85	364.76	690.97	1.33	-1.27	1.95	
9697.00	9.32	32.42	9609.11	596.07	371.16	702.18	2.75	-2.47	-6.87	
9760.00	8.53	33.21	9671.34	604.29	376.46	711.96	1.27	-1.25	1.25	
9824.00	7.91	25.66	9734.69	612.23	380.96	721.08	1.94	-0.97	-11.80	
9887.00	4.92	21.17	9797.29	618.66	383.82	728.05	4.81	-4.75	-7.13	
9951.00	2.37	23.81	9861.15	622.43	385.34	732.06	3.99	-3.98	4.12	PathFinder Survey
9997.00	0.56	23.81	9907.14	623.51	385.82	733.22	3.93	-3.93	0.00	Bit Projection

Annotation

MD ft	TVD ft	
6480.00	6479.00	Tie-In to Gyro
6517.00	6516.00	Begin PathFinder Surveys
9951.00	9861.15	PathFinder Survey
9997.00	9907.14	Bit Projection
