




Tubing Summary

15-42670

Well Name RUSTLER BLUFF 33-24-29 FED COM 001H	Lease Rustler Bluffs Unit	Field Name Bone Spring	Business Unit Mid-Continent
Ground Elevation (ft) 2,934.00	Original RKB Elevation (ft) 2,965.00	Current RKB Elevation 2,965.00, 11/26/2014	Mud Line Elevation (ft) Water Depth (ft)
Current KB to Ground (ft) 31.00	Current KB to Mud Line (ft)	Current KB to Csg Flange (ft) 37.00	Current KB to Tubing Head (ft) 31.00

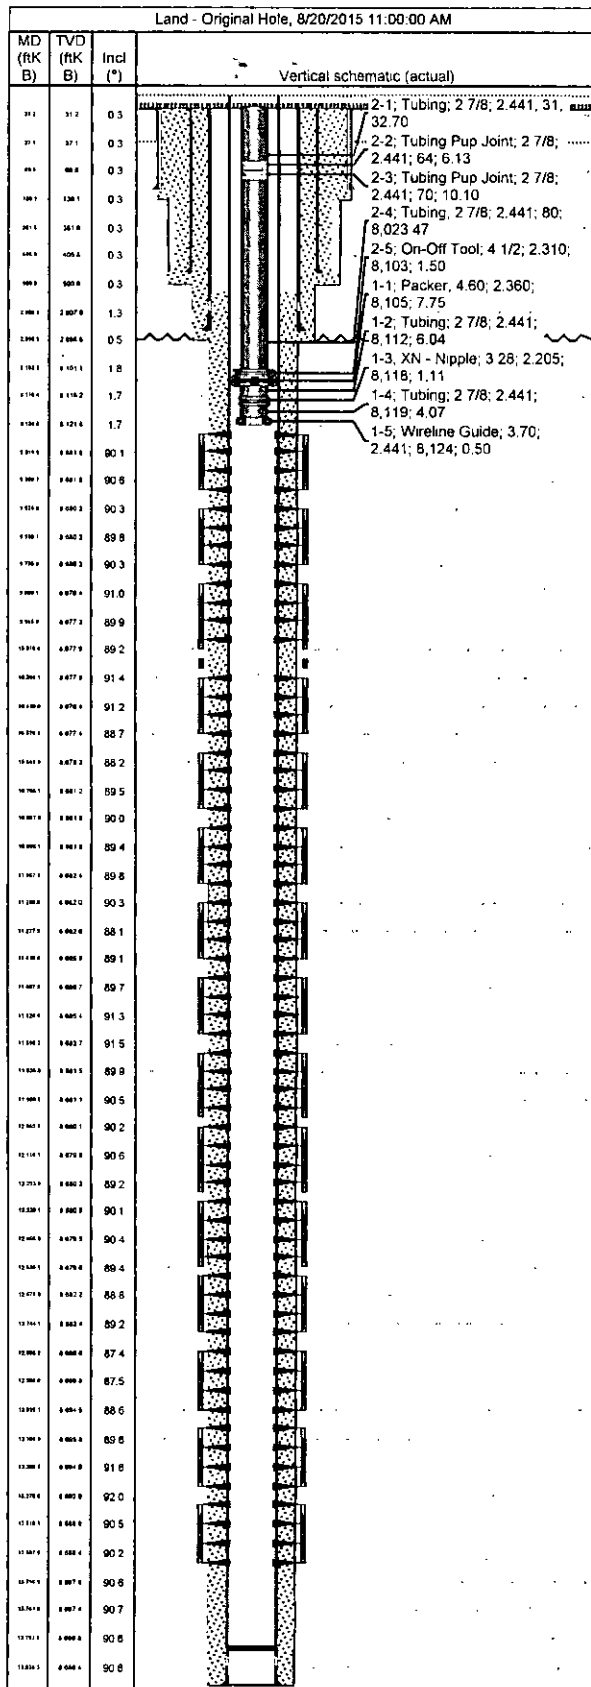


Tubing Strings									
Tubing Description Tubing - Production		Planned Run? N		Set Depth (MD) (ftKB) 8,104.8		Set Depth (TVD) (ftKB) 8,102.6			
Run Date 8/20/2015		Run Job Complete, 3/10/2015 13:00		Pull Date		Pull Job			
Jts	Item Des	OD (in)	ID (in)	Wt (lb/ft)	Grade	Top Thread	Len (ft)	Top (ftKB)	Btm (ftKB)
1	Tubing	2 7/8	2.441	6.50	L-80		32.70	30.9	63.6
1	Tubing Pup Joint	2 7/8	2.441	6.50	L-80		6.13	63.6	69.7
1	Tubing Pup Joint	2 7/8	2.441	6.50	L-80		10.10	69.7	79.8
247	Tubing	2 7/8	2.441	6.50	L-80		8,023.4 7	79.8	8,103.3
1	On-Off Tool	4 1/2	2.310				1.50	8,103.3	8,104.8

Rod Strings			
Rod Description		Planned Run?	Set Depth (ftKB)
Run Date		Run Job	Set Depth (TVD) (ftKB)
		Pull Date	Pull Job

Rod Components							
Jts	Item Des	OD (in)	Grade	Model	Len (ft)	Top (ftKB)	Btm (ftKB)




Wellbore Schematic

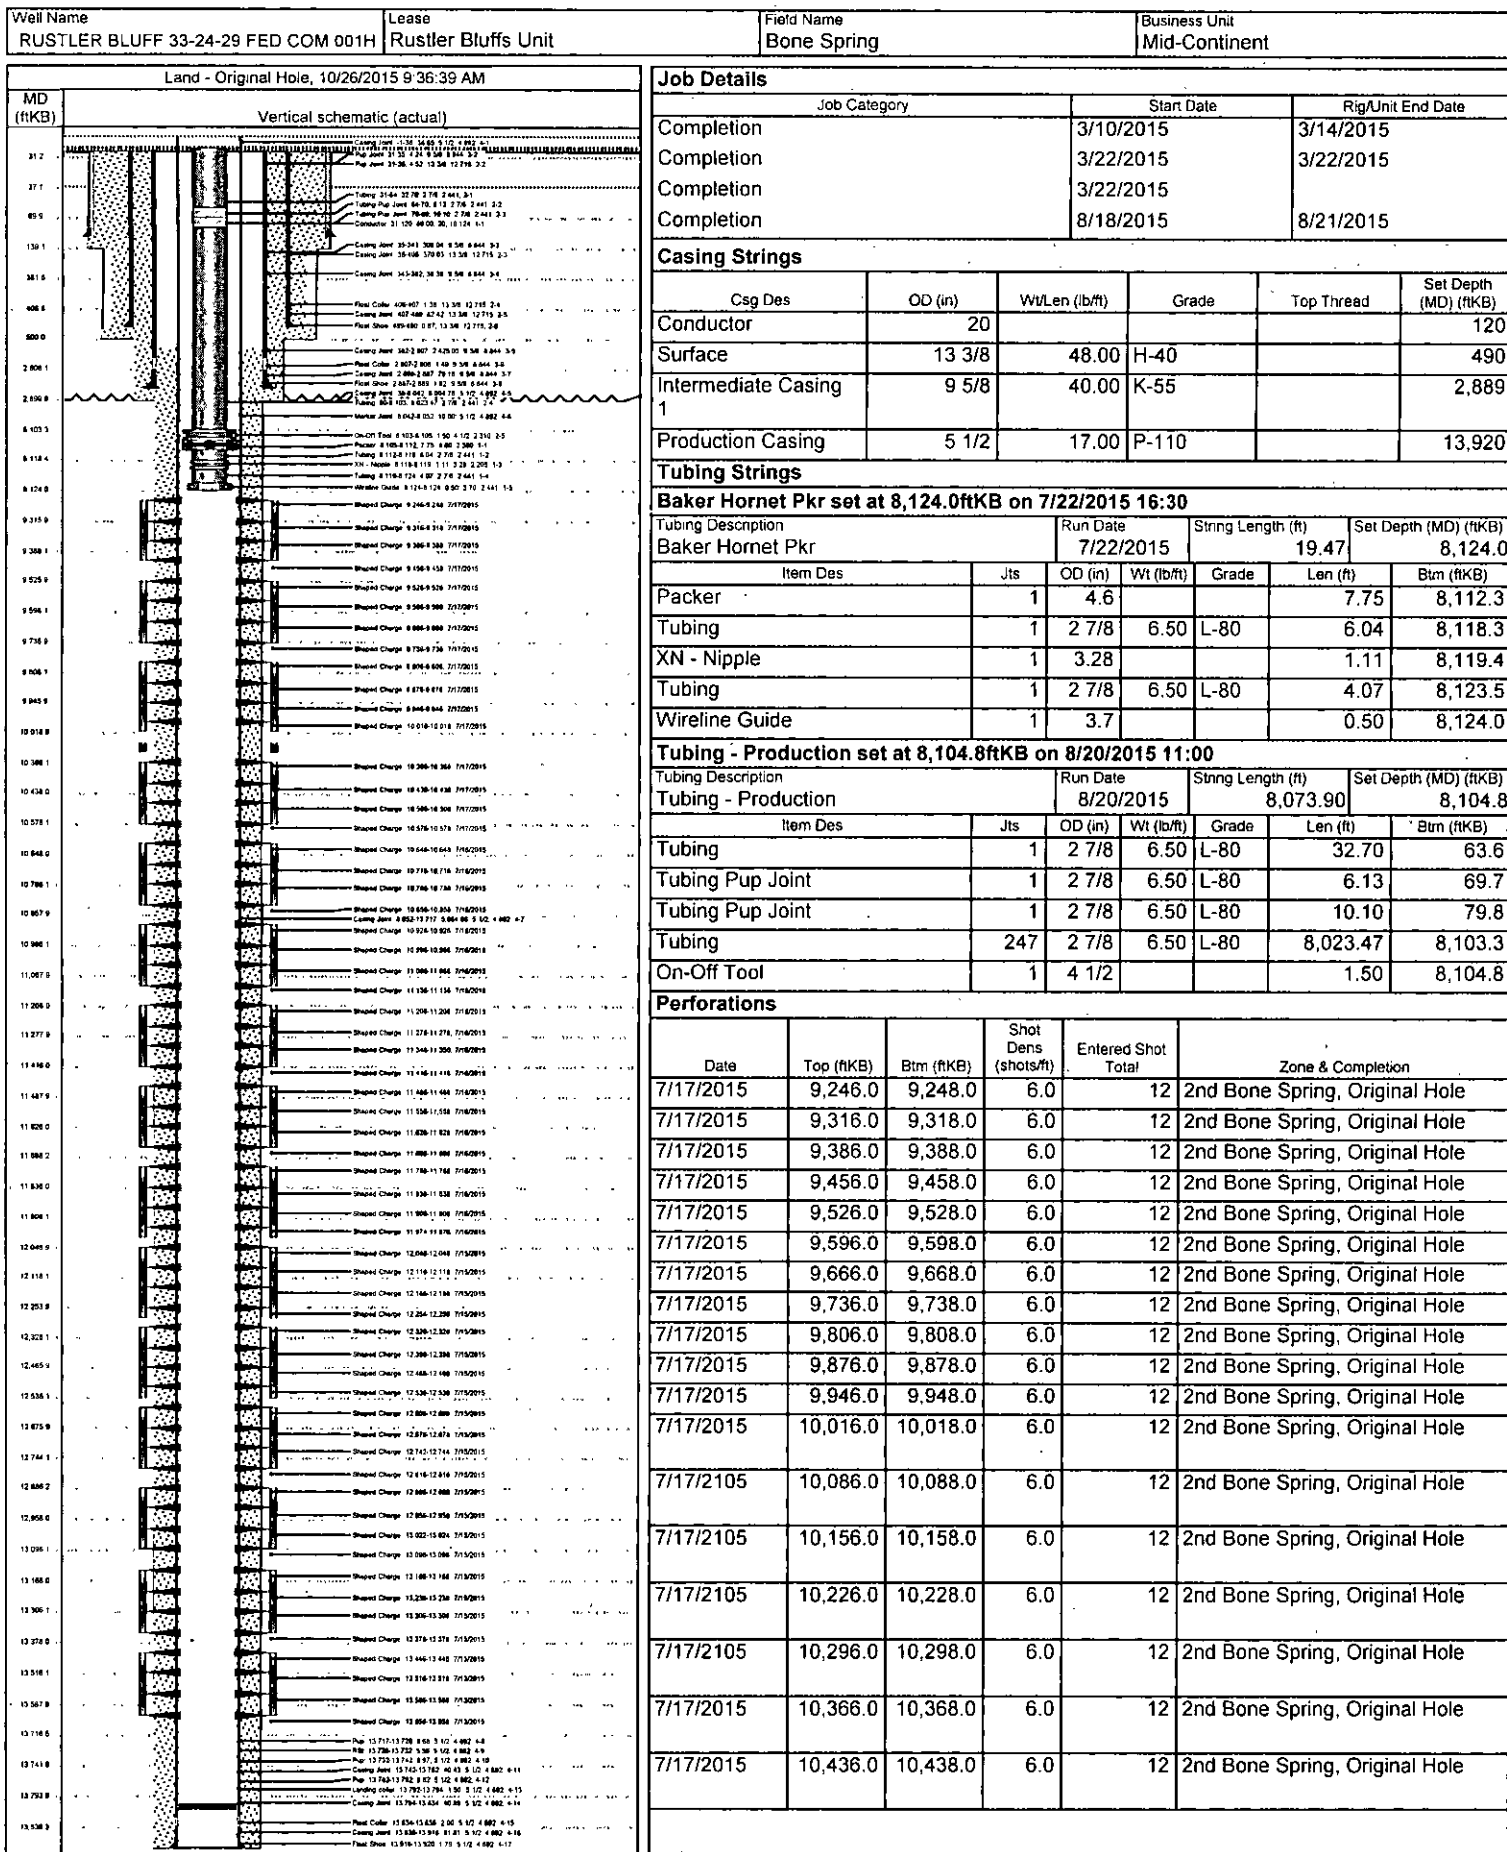



Wellbore Schematic

Well Name RUSTLER BLUFF 33-24-29 FED COM 001H	Lease Rustler Bluffs Unit	Field Name Bone Spring	Business Unit Mid-Continent
--	------------------------------	---------------------------	--------------------------------

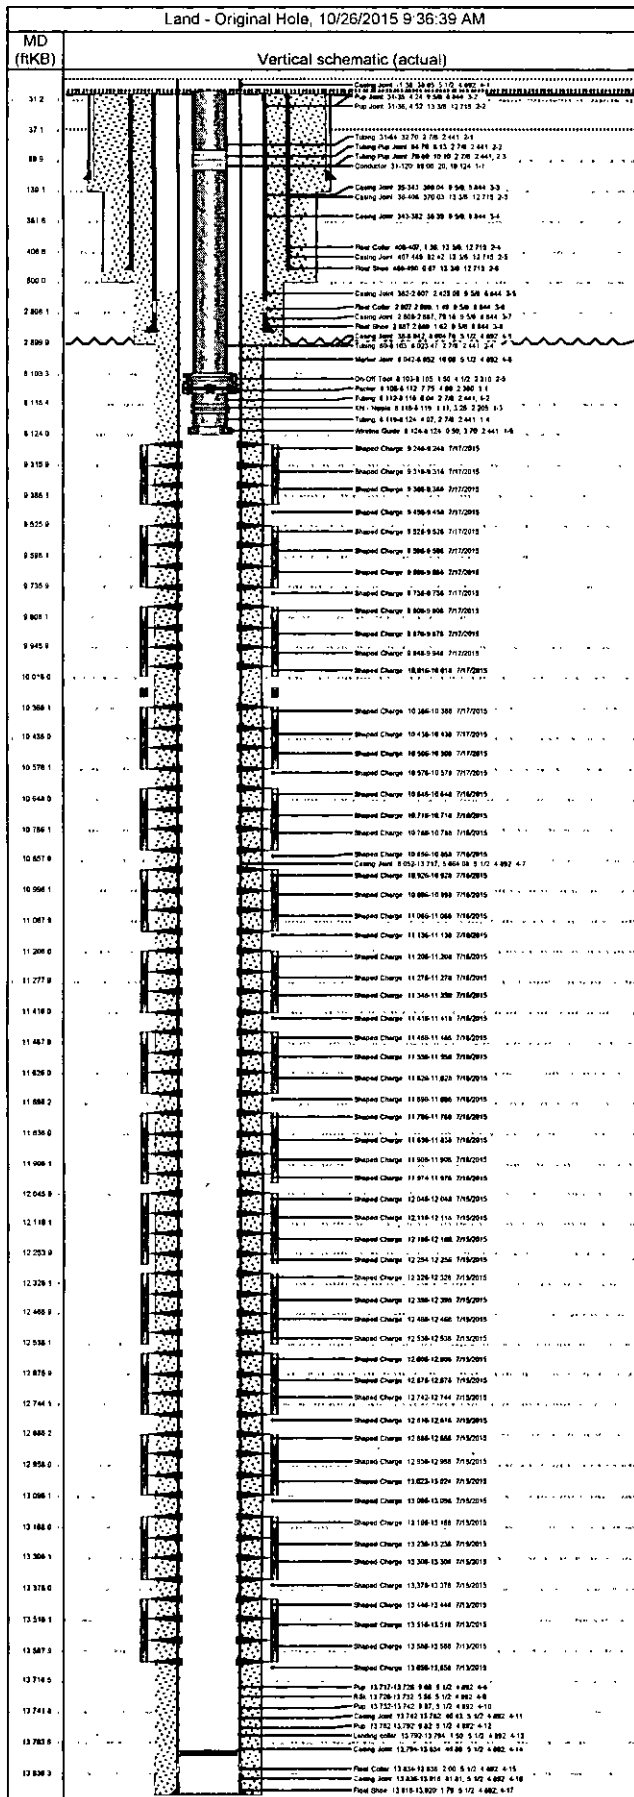


Perforations					
Date	Top (ftKB)	Btm (ftKB)	Shot Dens (shots/ft)	Entered Shot Total	Zone & Completion
7/15/2015	12,606.0	12,608.0	6.0	12	2nd Bone Spring, Original Hole
7/15/2015	12,676.0	12,678.0	6.0	12	2nd Bone Spring, Original Hole
7/15/2015	12,742.0	12,744.0	6.0	12	2nd Bone Spring, Original Hole
7/15/2015	12,816.0	12,818.0	6.0	12	2nd Bone Spring, Original Hole
7/15/2015	12,886.0	12,888.0	6.0	12	2nd Bone Spring, Original Hole
7/15/2015	12,956.0	12,958.0	6.0	12	2nd Bone Spring, Original Hole
7/15/2015	13,022.0	13,024.0	6.0	12	2nd Bone Spring, Original Hole
7/15/2015	13,096.0	13,098.0	6.0	12	2nd Bone Spring, Original Hole
7/15/2015	13,166.0	13,168.0	6.0	12	2nd Bone Spring, Original Hole
7/15/2015	13,236.0	13,238.0	6.0	12	2nd Bone Spring, Original Hole
7/15/2015	13,306.0	13,308.0	6.0	12	2nd Bone Spring, Original Hole
7/15/2015	13,376.0	13,378.0	6.0	12	2nd Bone Spring, Original Hole
7/13/2015	13,446.0	13,448.0	6.0	12	2nd Bone Spring, Original Hole
7/13/2015	13,516.0	13,518.0	6.0	12	2nd Bone Spring, Original Hole
7/13/2015	13,586.0	13,588.0	6.0	12	2nd Bone Spring, Original Hole
7/13/2015	13,656.0	13,658.0	6.0	12	2nd Bone Spring, Original Hole
Other Strings					
Run Date	Pull Date	Set Depth (ftKB)	Com		
Other In Hole					
Des	Top (ftKB)	Btm (ftKB)	Run Date	Pull Date	Com
Composite Frac Plug (drop ball)	9,491.0	9,493.0	7/17/2015	7/18/2015	Stage 16
Composite Frac Plug (drop ball)	9,771.0	9,773.0	7/17/2015	7/18/2015	Stage 15
Composite Frac Plug (drop ball)	10,051.0	10,053.0	7/17/2015	7/18/2015	Stage 14
Composite Frac Plug (drop ball)	10,331.0	10,333.0	7/17/2015	7/18/2015	Stage 13
Composite Frac Plug (drop ball)	10,611.0	10,613.0	7/17/2015	7/18/2015	Stage 12
Composite Frac Plug (drop ball)	10,891.0	10,893.0	7/16/2015	7/18/2015	Stage 11
Composite Frac Plug (drop ball)	11,171.0	11,173.0	7/16/2015	7/19/2015	Stage 10
Composite Frac Plug (drop ball)	11,451.0	11,453.0	7/16/2015	7/19/2015	Stage 9
Composite Frac Plug (drop ball)	11,731.0	11,733.0	7/16/2015	7/19/2015	Stage 8
Composite Frac Plug (drop ball)	12,009.0	12,011.0	7/16/2015	7/19/2015	Stage 7
Composite Frac Plug (drop ball)	12,291.0	12,293.0	7/15/2015	7/19/2015	Stage 6
Composite Frac Plug (drop ball)	12,571.0	12,573.0	7/15/2015	7/19/2015	Stage 5



Wellbore Schematic

Well Name RUSTLER BLUFF 33-24-29 FED COM 001H	Lease Rustler Bluffs Unit	Field Name Bone Spring	Business Unit Mid-Continent
--	------------------------------	---------------------------	--------------------------------

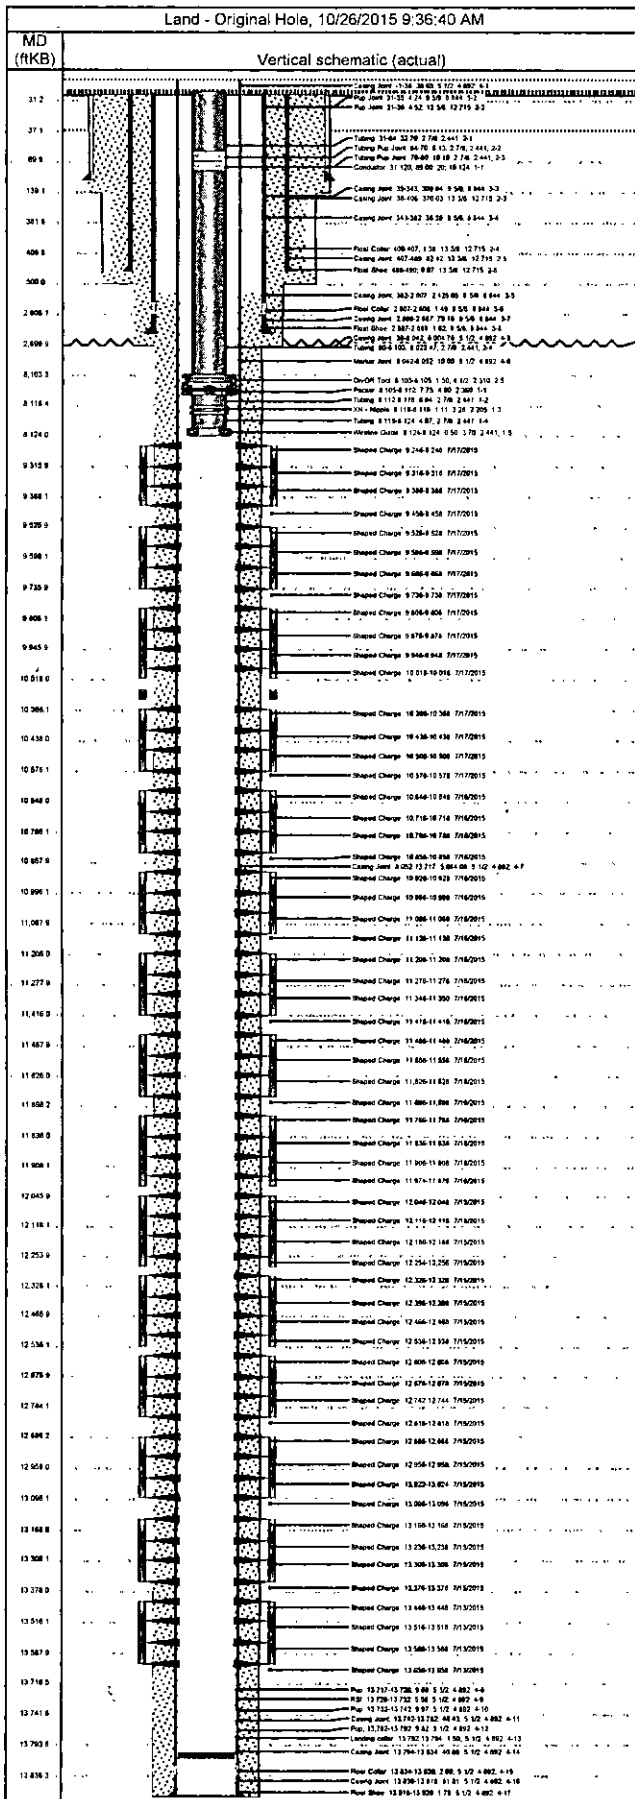

Other In Hole					
Des	Top (ftKB)	Btm (ftKB)	Run Date	Pull Date	Com
Composite Frac Plug (drop ball)	12,851.0	12,853.0	7/15/2015	7/19/2015	Stage 4
Composite Frac Plug (drop ball)	13,131.0	13,133.0	7/15/2015	7/19/2015	Stage 3
Composite Frac Plug (drop ball)	13,411.0	13,413.0	7/15/2015	7/19/2015	Stage 2
