


WPXENERGY

East Pecos Fed 22-6H
Wellbore Diagram
 2nd Bone Spring SS
 Eddy County, New Mexico
 API # 30-015-42281

Wolfcamp Proposed Perf/Frac: 2/24/16

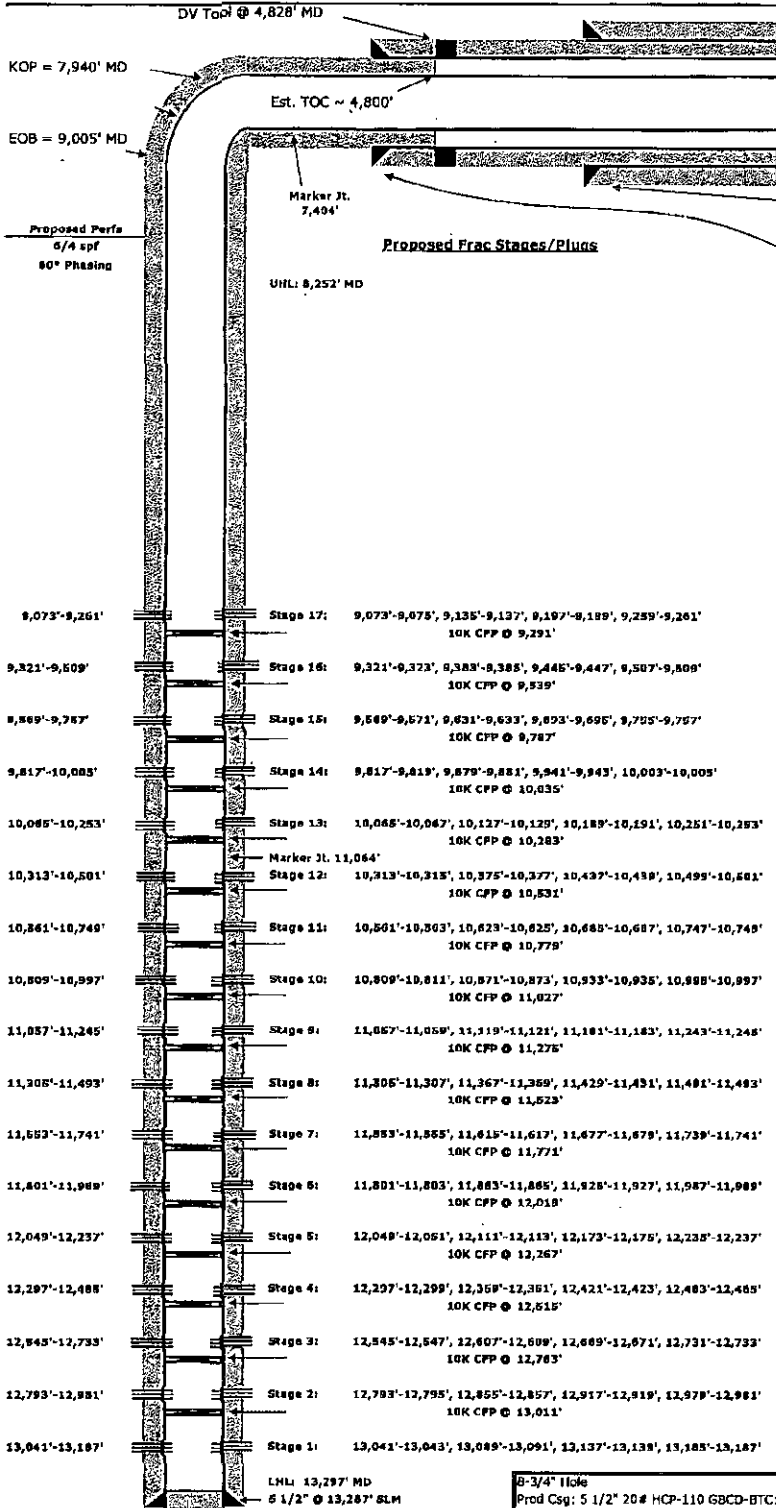

SHL: 250' FSL & 1,840' FEL of Sec 22, T26S, R29E
 BHL: 230' FNL & 1,840' FEL of Sec 22, T26S, R29E
 KB elev = 2,898'
 GL elev = 2,881'
 KB-GL: 17'
 SPUD: 12/16/15
 TD: 1/12/16

17-1/2" Hole
 Surface Casing: 13 3/8" 54.5# J-55 STC: 0' - 382'
 CMT: Tail 400 sks @ 14.8 ppg.
 Bumped plug, floats held, 29 bbls to surf.

12-1/4" Hole
 INT CSG: 9-5/8" 40# HCL-80 LTC: 0' - 6,648'
 CMT: 1st Stage CMT: 800 sks @ 13.0 ppg, bumped plug, floats held. Did not circ any cmt off DV tool.
 2nd Stage Lead: 1,800 sks @ 12.9 ppg, Tail: 175 sks @ 14.9 ppg. Bumped plug, floats held, circ 0 bbls to surface.
 Perf 4,700', sqz 2,800 sks @ 12.9 ppg, no cmt to surf, but good returns. Perf more sqz holes @ 600', pump 600 sks @ 12.9 ppg. Good returns. Perf sqz holes @ 400', sqz 345 sks @ 12.9 ppg, circ 155 bbl to surface.

Proppant Totals/Stage

314,000# 20/40 White Sand
 46,000# 20/40 CRC

9,073'-9,261'	Stage 17:	9,073'-9,075', 9,135'-9,137', 9,197'-9,199', 9,259'-9,261'
		10K CFP @ 9,291'
9,321'-9,509'	Stage 16:	9,321'-9,323', 9,383'-9,385', 9,445'-9,447', 9,507'-9,509'
		10K CFP @ 9,539'
9,569'-9,757'	Stage 15:	9,569'-9,571', 9,631'-9,633', 9,693'-9,695', 9,755'-9,757'
		10K CFP @ 9,787'
9,817'-10,005'	Stage 14:	9,817'-9,819', 9,879'-9,881', 9,941'-9,943', 10,003'-10,005'
		10K CFP @ 10,035'
10,065'-10,253'	Stage 13:	10,065'-10,067', 10,127'-10,129', 10,189'-10,191', 10,251'-10,253'
		10K CFP @ 10,283'
10,313'-10,501'	Marker Jt. 11,064'	
	Stage 12:	10,313'-10,315', 10,375'-10,377', 10,437'-10,439', 10,499'-10,501'
		10K CFP @ 10,531'
10,561'-10,749'	Stage 11:	10,561'-10,563', 10,623'-10,625', 10,685'-10,687', 10,747'-10,749'
		10K CFP @ 10,779'
10,809'-10,997'	Stage 10:	10,809'-10,811', 10,871'-10,873', 10,933'-10,935', 10,995'-10,997'
		10K CFP @ 11,027'
11,057'-11,245'	Stage 9:	11,057'-11,059', 11,119'-11,121', 11,181'-11,183', 11,243'-11,245'
		10K CFP @ 11,275'
11,305'-11,493'	Stage 8:	11,305'-11,307', 11,367'-11,369', 11,429'-11,431', 11,491'-11,493'
		10K CFP @ 11,523'
11,553'-11,741'	Stage 7:	11,553'-11,555', 11,615'-11,617', 11,677'-11,679', 11,739'-11,741'
		10K CFP @ 11,771'
11,801'-11,989'	Stage 6:	11,801'-11,803', 11,863'-11,865', 11,925'-11,927', 11,987'-11,989'
		10K CFP @ 12,019'
12,049'-12,237'	Stage 5:	12,049'-12,051', 12,111'-12,113', 12,173'-12,175', 12,235'-12,237'
		10K CFP @ 12,267'
12,297'-12,485'	Stage 4:	12,297'-12,299', 12,359'-12,361', 12,421'-12,423', 12,483'-12,485'
		10K CFP @ 12,515'
12,545'-12,733'	Stage 3:	12,545'-12,547', 12,607'-12,609', 12,669'-12,671', 12,731'-12,733'
		10K CFP @ 12,763'
12,793'-12,981'	Stage 2:	12,793'-12,795', 12,855'-12,857', 12,917'-12,919', 12,979'-12,981'
		10K CFP @ 13,011'
13,041'-13,187'	Stage 1:	13,041'-13,043', 13,089'-13,091', 13,137'-13,139', 13,185'-13,187'

8-3/4" Hole
 Prod Csg: 5 1/2" 20# HCP-110 GBCD-BTC: 0' - 13,287'
 CMT: Lead 400 sks @ 13.0 ppg, Tail 980 sks @ 13.0 ppg, bump plug, floats held. Est TOC ~ 4,809' per Renegade RBL dated 2/16/16.
