

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
SUNDRY NOTICES AND REPORTS ON WELLS

FORM APPROVED
OMB NO. 1004-0135
EXPIRES: March 31, 2007

Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals

SUBMIT IN TRIPLICATE

1a. Type of Well ☒ Oil Well ☐ Gas Well ☐ Other _____

2. Name of Operator
DEVON ENERGY PRODUCTION COMPANY, LP

3. Address and Telephone No.
20 North Broadway, Oklahoma City, OK 73102 405-235-3611

4. Location of Well (Report location clearly and in accordance with Federal requirements)*
810' FSL 910' FEL P SEC 25 T22S R30E PP: 447' FSL & 1464' FEL
BHL: 430' FSL & 330' FWL Sec 25 T22S R30E

5. Lease Serial No. NM-89052
6. If Indian, Allottee or Tribe Name
7. Unit or CA Agreement Name and No.
8. Well Name and No. Apache 25 Federal 10H
9. API Well No. 30-015-35597
10. Field and Pool, or Exploratory Quahada Ridge Southeast; Delaware
11. County or Parish State Eddy NM

12. CHECK APPROPRIATE BOX(s) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
☐ Notice of Intent	☐ Acidize	☐ Deepen	☐ Production (Start/Resume)	☐ Water Shut-Off
☒ Subsequent Report	☐ Alter Casing	☐ Fracture Treat	☐ Reclamation	☐ Well Integrity
☐ Final Abandonment Notice	☐ Casing Repair	☐ New Construction	☐ Recomplete	☒ Other <u>Completion Report</u>
	☐ Change Plans	☐ Plug and Abandon	☐ Temporarily Abandon	
	☐ Convert to Injection	☐ Plug Back	☐ Water Disposal	

13. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work and approximate duration thereof. If the proposal deepens directionally or recompletes horizontally, give subsurface location and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirement, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection)

9/10/07 - 10/11/07

MIRU Key Well Service. CHC. Displ w/340 bbls 2% KCL. Perf 10136-11332': 23 shots. RU BJ Services pkr @ 10,111' MD pump 500 gals rust buster. Acidize Delaware Brushy Canyon perfs: 10136-11332' w/1400 gals 7 1/2% NEFE acid & 46 BS. Test to 6200#. Rise pkr. ND BOP. NU Frac Valve. Test csg to 1000#, ok. Frac L. Brushy Canyon perfs: 10136-11332' w/249,000 gals Spectra Star 2800 Gel, 7021# 100 Mesh Sd, 302,563# 20/40 White Sd, 81,778# 16/30 SiberProp sd. Flush w/ 13,365 gals 10# Gel. RD frac crew. ND Frac Valve. NU BOP. CHC. Perf heel section of Brushy Canyon w/ 3 1/8" cased hole guns @ 8207-9502': total 23 shots. RU BJ spot 800 gals 7 1/2% NEFE acid across perfs 8207-9502'. Test to 7000#, ok. Acidize L. Brushy Canyon w/1400 gals 7 1/2% HCL acid & 46 BS. RU BJ & frac. Test to 6000#. Frac w/251,961 gals Spectra Star 2800 Gel, 7500# 100 mesh sd, 302,500# 20/40 white sd, 83,750# 16/30 Siberprop sd and flush w/12,096 gals 10# gel. NU BOP. CHC. DO BP. Lost 280 bbls KCL wtr to perfs. ND BOP & install WH. RU Wood Group & TIH w/ submersible pump. ND BOP & NU WH. WO NSL approval from NMOC. RD PU. Start up pump @ 50 htz w/ 125# TP & CP. Well producing dn FL. POP.

14. I hereby certify that the foregoing is true and correct

Signed 

Name Judy A. Barnett
Title Regulatory Analyst


Date 11/13/2007

(This space for Federal or State Office use)

Approved by _____ Title _____ Date _____
Conditions of approval, if any:

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make any department or agency of the United States any false, fictitious or fraudulent statements or representations to any matter within its jurisdiction.

*See Instruction on Reverse Side



Scientific Drilling

DEVON ENERGY

Field: Ingle Wells
Site: Eddy County, NM
Well: Apache 25 Fed #10H
Wellpath: VH - Job #32K0807676
Survey: 08/09/07


This survey is correct to the best of my knowledge
and is supported by actual field data.

Blharth.....Company Representative

Notorized this date 13th of August, 2007.

Deborah Sue Bynum

Notary Signature
County of Midland
State of Texas





Scientific
Drilling

Scientific Drilling International

Survey Report

Company: DEVON ENERGY
Field: Ingle Wells
Site: Eddy County, NM
Well: Apache 25 Fed #10H
Wellpath: VH - Job #32K0807676

Date: 08/10/2007 Time: 10:34:21 Page: 1
Co-ordinate(NE) Reference: Site: Eddy County, NM, Grid North
Vertical (TVD) Reference: SITE 0.0
Section (VS) Reference: Well (0.00N,0.00E,264.59Azi)
Survey Calculation Method: Minimum Curvature Db: Sybase

Survey: 08/09/07 Start Date: 08/09/2007
Company: Scientific Drilling Internatio Engineer: Guebara/Rowe/Lopez
Tool: Keeper, Keeper Gyro Tied-to: From Surface

Survey

MD ft	Incl deg	Azim deg	TVD ft	VS ft	N/S ft	E/W ft	DLS deg/100ft	ClsD ft	ClsA deg
0.00	0.00	359.73	0.00	0.00	0.00	0.00	0.00	0.00	0.00
100.00	0.39	282.90	100.00	0.32	0.08	-0.33	0.39	0.34	282.90
200.00	0.39	282.03	200.00	0.97	0.22	-1.00	0.01	1.02	282.61
300.00	0.51	310.61	299.99	1.60	0.58	-1.67	0.25	1.77	289.28
400.00	0.47	262.94	399.99	2.32	0.82	-2.41	0.40	2.55	288.82
500.00	0.56	269.68	499.99	3.22	0.77	-3.30	0.11	3.39	283.09
600.00	0.65	260.80	599.98	4.27	0.67	-4.35	0.13	4.40	278.82
700.00	0.84	263.23	699.97	5.57	0.50	-5.64	0.19	5.66	275.05
800.00	0.81	251.32	799.96	6.99	0.19	-7.03	0.17	7.04	271.51
900.00	0.96	258.48	899.95	8.51	-0.21	-8.52	0.19	8.53	268.60
1000.00	0.91	256.72	999.94	10.13	-0.56	-10.12	0.06	10.13	266.84
1100.00	0.70	252.03	1099.93	11.51	-0.93	-11.47	0.22	11.51	265.37
1200.00	0.86	242.65	1199.92	12.80	-1.46	-12.72	0.20	12.80	263.45
1300.00	0.90	242.61	1299.91	14.22	-2.17	-14.08	0.04	14.25	261.25
1400.00	1.00	237.67	1399.89	15.73	-2.99	-15.51	0.13	15.80	259.08
1500.00	0.78	241.64	1499.88	17.13	-3.78	-16.85	0.22	17.27	257.34
1600.00	0.99	228.88	1599.87	18.46	-4.68	-18.10	0.28	18.70	255.52
1700.00	0.99	235.33	1699.85	19.91	-5.73	-19.46	0.11	20.29	253.59
1800.00	0.82	229.01	1799.84	21.25	-6.69	-20.71	0.20	21.77	252.09
1900.00	0.85	221.76	1899.83	22.38	-7.72	-21.75	0.11	23.08	250.46
2000.00	1.02	223.82	1999.82	23.59	-8.91	-22.86	0.17	24.53	248.70
2100.00	1.07	217.89	2099.80	24.91	-10.29	-24.04	0.12	26.15	246.83
2200.00	0.81	226.21	2199.79	26.10	-11.52	-25.13	0.29	27.64	245.38
2300.00	0.81	233.04	2299.78	27.26	-12.43	-26.20	0.10	29.00	244.62
2400.00	0.97	214.54	2399.77	28.40	-13.55	-27.25	0.32	30.43	243.56
2500.00	0.88	225.93	2499.75	29.55	-14.78	-28.28	0.20	31.91	242.41
2600.00	0.89	211.06	2599.74	30.61	-15.98	-29.23	0.23	33.31	241.34
2700.00	1.30	214.09	2699.72	31.79	-17.58	-30.27	0.41	35.00	239.85
2800.00	1.49	215.36	2799.69	33.36	-19.58	-31.65	0.19	37.22	238.26
2900.00	1.40	210.17	2899.66	34.92	-21.69	-33.02	0.16	39.51	236.69
3000.00	1.38	216.37	2999.63	36.43	-23.72	-34.35	0.15	41.74	235.37
3100.00	1.48	197.08	3099.60	37.72	-25.92	-35.44	0.49	43.91	233.82
3200.00	1.76	188.38	3199.56	38.58	-28.67	-36.04	0.37	46.05	231.50
3300.00	1.56	191.85	3299.52	39.35	-31.52	-36.54	0.22	48.26	229.22
3400.00	1.58	184.11	3399.48	39.98	-34.23	-36.92	0.21	50.35	227.17
3500.00	1.60	179.65	3499.44	40.34	-37.00	-37.01	0.13	52.34	225.01
3600.00	1.87	173.38	3599.40	40.42	-40.02	-36.82	0.33	54.38	222.61
3700.00	1.87	167.74	3699.34	40.20	-43.23	-36.28	0.18	56.44	220.01
3800.00	1.70	170.45	3799.30	39.89	-46.29	-35.69	0.19	58.45	217.63
3900.00	1.76	163.09	3899.25	39.48	-49.22	-35.00	0.23	60.39	215.41
4000.00	1.69	172.04	3999.21	39.11	-52.15	-34.35	0.28	62.44	213.37
4100.00	1.70	169.04	4099.16	38.90	-55.06	-33.86	0.09	64.64	211.59
4200.00	1.48	164.10	4199.12	38.52	-57.77	-33.22	0.26	66.64	209.90
4300.00	1.58	165.79	4299.09	38.07	-60.35	-32.53	0.11	68.56	208.33
4400.00	1.37	162.43	4399.05	37.61	-62.83	-31.83	0.22	70.43	206.87
4500.00	1.14	166.54	4499.03	37.22	-64.94	-31.24	0.25	72.06	205.69
4600.00	1.35	162.57	4599.01	36.83	-67.03	-30.65	0.22	73.70	204.57
4700.00	1.00	161.04	4698.99	36.39	-68.97	-30.02	0.35	75.22	203.52
4800.00	1.12	163.71	4798.97	36.00	-70.74	-29.46	0.13	76.63	202.61



Scientific Drilling International


Survey Report

Company: DEVON ENERGY
Field: Ingle Wells
Site: Eddy County, NM
Well: Apache 25 Fed #10H
Wellpath: VH - Job #32K0807676

Date: 08/10/2007 Time: 10:34:21 Page: 2
Co-ordinate(NE) Reference: Site: Eddy County, NM, Grid North
Vertical (TVD) Reference: SITE 0.0
Section (VS) Reference: Well (0.00N,0.00E,264.59Azi)
Survey Calculation Method: Minimum Curvature Db: Sybase


Survey

MD ft	Incl deg	Azim deg	TVD ft	VS ft	N/S ft	E/W ft	DLS deg/100ft	ClsD ft	ClsA deg
4900.00	1.37	163.90	4898.94	35.59	-72.82	-28.85	0.25	78.33	201.62
5000.00	1.27	172.38	4998.92	35.33	-75.07	-28.38	0.22	80.25	200.71
5100.00	1.24	164.75	5098.89	35.10	-77.21	-27.94	0.17	82.11	199.90
5200.00	1.14	172.93	5198.87	34.89	-79.24	-27.54	0.20	83.89	199.16
5300.00	1.22	172.65	5298.85	34.82	-81.29	-27.28	0.08	85.74	198.55
5400.00	1.08	170.44	5398.83	34.72	-83.27	-26.99	0.14	87.54	197.96
5500.00	1.01	159.02	5498.81	34.41	-85.03	-26.51	0.22	89.06	197.32
5600.00	1.00	183.80	5598.80	34.31	-86.72	-26.25	0.43	90.61	196.84
5700.00	0.78	179.23	5698.79	34.51	-88.27	-26.30	0.23	92.11	196.59
5800.00	1.05	188.70	5798.77	34.79	-89.86	-26.43	0.31	93.66	196.39
5900.00	1.09	182.68	5898.76	35.14	-91.71	-26.62	0.12	95.49	196.18
6000.00	1.05	185.55	5998.74	35.45	-93.57	-26.75	0.07	97.32	195.95
6100.00	0.85	198.37	6098.73	35.93	-95.19	-27.07	0.29	98.96	195.88
6200.00	1.07	204.01	6198.71	36.68	-96.75	-27.69	0.24	100.63	195.97
6300.00	1.03	197.19	6298.70	37.49	-98.46	-28.33	0.13	102.45	196.05
6400.00	1.04	203.14	6398.68	38.27	-100.15	-28.95	0.11	104.25	196.12
6500.00	1.21	218.26	6498.66	39.43	-101.82	-29.96	0.34	106.13	196.40
6600.00	1.17	210.68	6598.64	40.76	-103.52	-31.14	0.16	108.10	196.74
6700.00	1.22	211.18	6698.62	42.00	-105.31	-32.21	0.05	110.13	197.01
6790.00	1.08	218.33	6788.60	43.15	-106.80	-33.23	0.22	111.85	197.29




Scientific
Drilling

Field: Ingle Wells
Site: Eddy County, NM
Well: Apache 25 Fed #10H
Wellpath: VH - Job #32K0807676
Survey: 08/09/07



Azimuths to Grid North
True North: 0.00°
Magnetic North: 0.00°

Magnetic Field
Strength: 0nT
Dip Angle: 0.00°
Date: 08/10/2007
Model: igrf2000

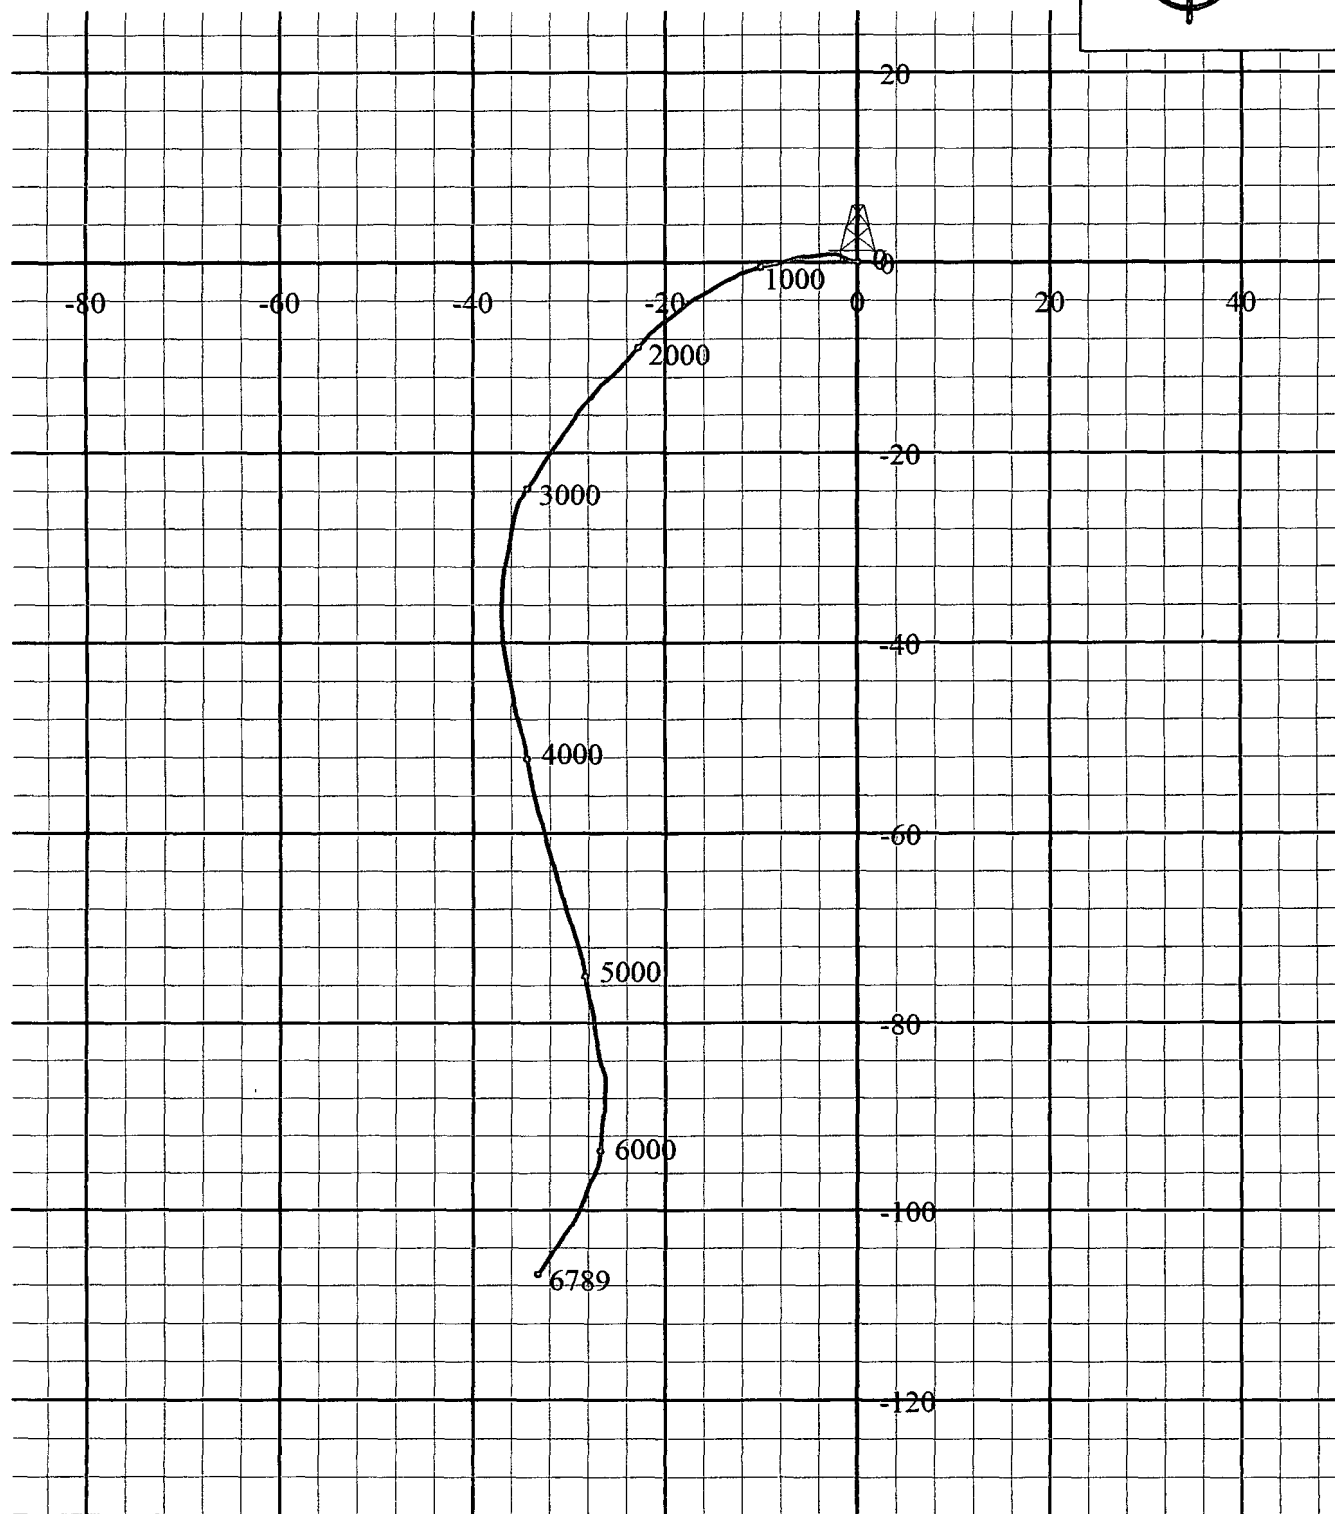


South(-)/North(+) [20ft/in]

West(-)/East(+) [20ft/in]

**McVAY DRILLING COMPANY**

P.O. Box 2450
Hobbs, New Mexico 88241
(505) 397-3311
FAX: 39-DRILL



Well Name and Number: Apache 25 Fed 10H

Location: Sec 25, T22S, R30E, Eddy County, NM

Operator: Devon

Drilling Contractor: McVay Drilling Company

The undersigned certifies that he is an authorized representative of the drilling contractor who drilled the above described well and that he has conducted deviation tests and obtained the following results:

Degrees @ Depth		Degrees @ Depth	
1/2	346	85 3/4	7885
1	637	90.75	7952
1	1137	91	8016
3/4	1614	90.25	8112
3/4	2106	90.1	8144
1	2606	91.2	8207
1.3	3080	88.6	8335
1.42	4359	88.7	8367
1.5	4836	88.7	8367
.84	5336	92.2	8621
1.5	6765	91	8716
1.1	7081	89.5	8748
6.1	7144	88.5	8939
.21	7270	90.75	9258
24.7	7300	90.7	92.98
47.2	7460	89.2	9571
61.6	7587	89.9	9798
64 1/4	7619	93.1	9894
1	7683	93.4	10084
71	7713	93	10180
73 1/4	7750	91.5	10339
81 1/4	7841	90	10433

Drilling Contractor: McVay Drilling Company

By: [Signature]

Subscribed and sworn to before me this 31st day of August, 2007

[Signature]
Notary Public

My Commission Expires: 8-16-09

Lea County, New Mexico



McVAY DRILLING COMPANY

P.O. Box 2450
Hobbs, New Mexico 88241
(505) 397-3311
FAX: 39-DRILL

Well Name and Number: Apache 25 Fed 10H

Location: Sec 25, T22S, R30E, Eddy County, NM

Operator: Devon

Drilling Contractor: McVay Drilling Company

The undersigned certifies that he is an authorized representative of the drilling contractor who drilled the above described well and that he has conducted deviation tests and obtained the following results:

<u>Degrees @ Depth</u>		<u>Degrees @ Depth</u>
88.5	10815	
89.75	10910	
90	11133	
90.4	11228	
91.5	11323	
