

7. **OCD Approval:** ☒ Permit Application (including closure plan) ☐ Closure Plan (only)

OCD Representative Signature: *James D. Dele* Approval Date: 02/22/2010

Title: *Dist H Supervisor* OCD Permit Number: 210023

8. **Closure Report (required within 60 days of closure completion):** Subsection K of 19.15.17.13 NMAC

Instructions: Operators are required to obtain an approved closure plan prior to implementing any closure activities and submitting the closure report. The closure report is required to be submitted to the division within 60 days of the completion of the closure activities. Please do not complete this section of the form until an approved closure plan has been obtained and the closure activities have been completed.

☐ Closure Completion Date: _____

9. **Closure Report Regarding Waste Removal Closure For Closed-loop Systems That Utilize Above Ground Steel Tanks or Haul-off Bins Only:**

Instructions: Please identify the facility or facilities for where the liquids, drilling fluids and drill cuttings were disposed. Use attachment if more than two facilities were utilized.

Disposal Facility Name: _____ Disposal Facility Permit Number: _____

Disposal Facility Name: _____ Disposal Facility Permit Number: _____

Were the closed-loop system operations and associated activities performed on or in areas that *will not* be used for future service and operations?

☐ Yes (If yes, please demonstrate compliance to the items below) ☐ No

Required for impacted areas which will not be used for future service and operations:

☐ Site Reclamation (Photo Documentation)

☐ Soil Backfilling and Cover Installation

☐ Re-vegetation Application Rates and Seeding Technique

10.

Operator Closure Certification:

I hereby certify that the information and attachments submitted with this closure report is true, accurate and complete to the best of my knowledge and belief. I also certify that the closure complies with all applicable closure requirements and conditions specified in the approved closure plan.


Name (Print): _____ Title: _____

Signature: _____ Date: _____

e-mail address: _____ Telephone: _____



Commitment Runs Deep

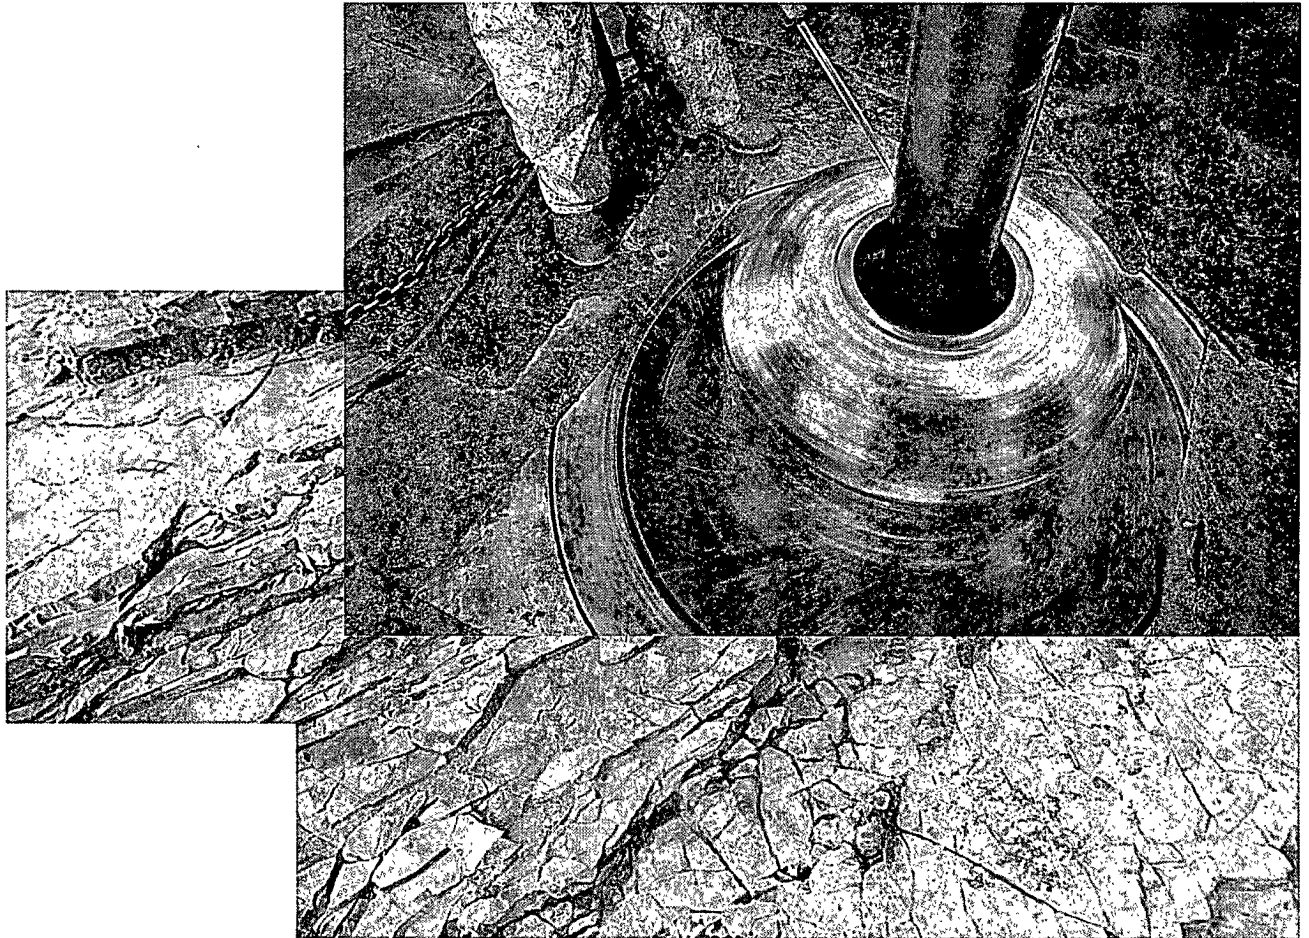

Design Plan
Operation & Maintenance Plan
Closure Plan
Workover Operations

SENM
July 2008

I. Design Plan

Above ground steel tanks will be used for the management of all workover fluids.

II. Operations and Maintenance Plan

Devon will operate and maintain all of the above ground steel tanks involved in workover operations in a prudent manner to prevent any spills. If a leak develops, the appropriate division district office will be notified within 48 hours of the discovery and the leak will be addressed. During an upset condition the source of the spill is isolated and addressed as soon as it is discovered. Free liquids will be removed and loose topsoil will be used to stabilize the spill. The contaminated soil will be either bio-remediated or excavated and taken to an agency approved disposal facility.

III. Closure Plan

All workover fluids will go to above ground steel tanks and will be hauled by various trucking companies to an agency approved disposal facility.

Impacted areas which will not be used for future service or operations will be reclaimed and reseeded as stated in the APD.
