

Wellbore Status as of : **Current**

Spud: 8/25/1986
TD: 9/13/1986 9200'
Completed: 9/26/1986
Current PBTD: 7/14/2001 9089'

Surface Casing:

13 3/8" J-55 54.5# set @ 458' w/450 sx cmt circ


Intermediate Casing:

8 5/8" 24# & 28# set @ 2900' w/1150 sx cmt circ

Production Casing:

5 1/2" 17# J-55 set @ 9200' w/2050 sx cmt TOC @ 900'

Spud: 8/25/1986
TD: 9/13/1986 9200'
Completed: 9/26/1986
Current PBTD: 7/14/2001 9089'

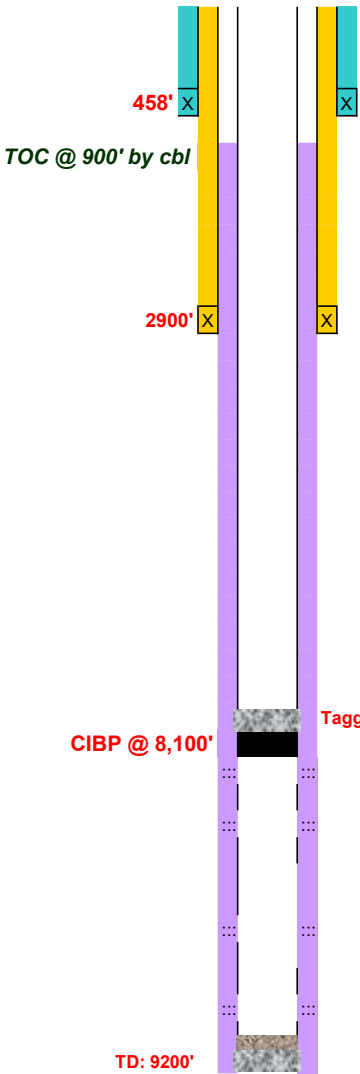

Tagged TOC @ 8,042'

4/21/00 3. Perf 8153.5, 8156.5, 8160, 8169, 8180, 8183 & 8186.5'; acdz

9/23/86 2. Perf 8443-68' w/2 spf; acdz w/500 gals 20%

460 Hornet Packer Mech Bottom X-Over ID 1.998" OD @ 8,562'

9/19/86 1. Perf 8617-28' w/2 spf; acdz w/3000 gals 20%--squeezed 9/23/1986

Second Bone Springs:

3/13/17 4. perf 9,008' - 9,014' 125,417# sand/2056 bbls water (ATP 7427 @ 17.3 bpm)
