

HOE
NOV 05 2013

13-156

OCD Hobbs

RECEIVED

Form 3160-3
(April 2004)

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED
OMB No. 1004-0137
Expires March 31, 2007

1a. Type of work: ☒ DRILL ☐ REENTER		5. Lease Serial No. NMNM-0315712
1b. Type of Well: ☒ Oil Well ☐ Gas Well ☐ Other ☒ Single Zone ☐ Multiple Zone		6. If Indian, Allottee or Tribe Name N/A
2. Name of Operator COG Operating LLC		7. If Unit or CA Agreement, Name and No. N/A
3a. Address One Concho Center, 600 W. Illinois Ave Midland, TX 79701		8. Lease Name and Well No. Sneed 9 Federal Com #1H (40134)
3b. Phone No. (include area code) (432) 685-4385		9. API Well No. 30-025- 41489
4. Location of Well (Report location clearly and in accordance with any State requirements.) At surface SHL: 330' FNL & 150' FWL, UL D At proposed prod. zone BHL: 330' FNL & 330' FEL, UL A		10. Field and Pool, or Exploratory Maljamar; Yeso, West 44500
14. Distance in miles and direction from nearest town or post office* 1.3 miles Southwest of Maljamar		11. Sec., T. R. M. or Blk. and Survey or Area Sec 9, T17S, R32E
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 150'	16. No. of acres in lease 760	17. Spacing Unit dedicated to this well 160
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. 24'	19. Proposed Depth TVD: 6626' MD: 11272'	20. BLM/BIA Bond No. on file NMB000740; NMB000215
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 4089' GL	22. Approximate date work will start* 12/31/2013	23. Estimated duration 15 days

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, shall be attached to this form:

- | | |
|---|--|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the authorized officer. |

25. Signature 	Name (Printed/Typed) Robyn M. Odom	Date 08/15/2013
---	---------------------------------------	--------------------

Title
Regulatory Analyst

Approved by (Signature) /s/ STEPHEN J. CAFFEY	Name (Printed/Typed)	Date OCT 31 2013
--	----------------------	---------------------

Title
FIELD MANAGER

Office
CARLSBAD FIELD OFFICE

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

APPROVAL FOR TWO YEARS

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

*(Instructions on page 2)

Roswell Controlled Water Basin

SEE ATTACHED FOR
CONDITIONS OF APPROVAL

Approval Subject to General Requirements
& Special Stipulations Attached

NOV 07 2013

PM

ATTACHMENT TO FORM 3160-3
COG Operating, LLC
SNEED 9 FEDERAL COM # 1H
SHL: 330' FNL & 330' FWL, Unit D
BHL: 330' FNL & 330' FEL, Unit A
Sec 9, T17S, R32E
Eddy County, NM

1. Proration Unit Spacing: 160 Acres

2. Ground Elevation: 4094'

3. Proposed Depths: EOC (end of curve) TVD = 6700', MD = 6981'
Toe (end of lateral) TVD = 6628', MD = 11108'

4. Estimated tops of geological markers:

Rustler	953'
Top of Salt	1262'
Base of Salt	2115'
Yates	2274'
Seven Rivers	2611'
Queen	3237'
Grayburg	3676'
San Andres	3982'
Glorieta	5474'
Paddock	5557'
Blinbry	5957'
Tubb	6890'

5. Possible mineral bearing formations:

Water Sand	150'	Fresh Water
Grayburg	3676'	
San Andres	3982'	
Glorieta	5474'	
Paddock	5557'	
Blinebry	5957'	
Tubb	6890'	

No other formations are expected to give up oil, gas or fresh water in measurable quantities. Setting 13 3/8" casing to 978' (25' into Rustler) and circulating cement back to the surface will protect the surface fresh water sand. The Salt Section will be protected by setting 9 5/8" casing to 2290' and circulating cement back to surface in a single or multi-stage job and/or with an ECP. Any shallower zones above TD, which contain commercial quantities of oil and/or gas, will have cement circulated across them or be isolated by external casing packers. This will be achieved by cementing from the KOP by single or multi-stage job using ECP & DV Tools as necessary. The 7" portion of the tapered 7" x 5 1/2" production casing will be cemented back to a minimum of 200' into the intermediate casing (although cement volume is actually calculated to surface). At the KOP the 7" casing will be tapered to 5 1/2" casing which will be run thru curve and lateral with external casing packers for zone isolation. If wellbore conditions arise that require immediate action and/or a change to this program, COG Operating LLC personnel will always react to protect the wellbore and/or environment.

See
CORA

ATTACHMENT TO FORM 3160-3
COG Operating, LLC
SNEED 9 FEDERAL COM #1H
Page 2 of 6

6. Proposed Mud System

The well will be drilled to TD with a combination of fresh water, brine, cut brine and polymer mud systems. The applicable depths and properties of these systems are as follows:

DEPTH (MD)	TYPE	WEIGHT	VISCOSITY	WATERLOSS
0-978'	Fresh Water	8.5	28	N.C.
978'-2290'	Brine	10	30	N.C.
2290'-6223'	Cut Brine	8.7-9.2	30	N.C.
6223'-6981'	Cut Brine/polymer mud	8.7-9.2	30	N.C.
6981'-11108'	Cut Brine/polymer mud	8.7-9.2	30	N.C.

Sufficient mud materials will be kept at the well site to maintain mud properties and meet minimum lost circulation and weight increase requirements at all times.

6. Proposed Casing Program

Hole Size	Interval MD	OD Casing	Weight	Grade	Condition	Jt.	brst/clps/ten
17 1/2"	0-978'	13 3/8"	48#	H-40/J-55 Hybrid	New	ST&C	1.77/1.78/7.88
12 1/4"	978'- 2290'	9 5/8"	40#	J/K-55	New	LT&C	1.72/2.16/6.68
8 3/4"	2290'- 6223'	7"	26#	L-80	New	LT&C	1.17/1.83/3.70
8 3/4"	6223'- 6981'	5 1/2"	17#	L-80	New	LT&C	1.55/1.96/3.45
7 7/8"	6981'- 11108'	5 1/2"	17#	L-80	New	LT&C	1.55/1.96/3.45

Production string will be a tapered string with 7" 26# L-80 LTC run from surface to kick off point (6223') and then crossed over to 5 1/2" 17# L-80 LTC.

7. Proposed Cement Program

13 3/8" SURFACE: (Circulate to Surface)

Lead: 0'-500'	400 sks	Class "C" w/4% Gel	1.69 cf/sk	13.5 ppg
Excess 95%		+2% CaCl ₂ + 0.25 pps CF		

Tail: 500'-978'	500 sks	Class C w/2% CaCl ₂	1.32 cf/sk	14.8 ppg
Excess 80%				

9 5/8" INTERMEDIATE:

Option #1: Single Stage (Circulate to Surface)

Lead: 0'-1750'	500 sks	50:50:10 C:Poz:Gel	2.45 cf/sk	11.8 ppg
Excess 100%		w/ 5% Salt+ 0.25% CF		
		+5 pps LCM		

Tail: 1750'-2290'	300 sks	Class C w/2% CaCl ₂	1.32 cf/sk	14.8 ppg
Excess 113%				

Option #2: Multi-stage w/ DV Tool @ +/-1028' (DV Tool 50' below 13 3/8" csg. Shoe) (Circulate to Surface)

Stage #1: Lead: 1028'-1750'	200 sks	50:50:10 C:Poz:Gel	2.45 cf/sk	11.8 ppg
Excess 116%		w/5% Salt + 0.25% CF		
		+ 5 pps LCM		

Tail: 1750'-2290'	300 sks	Class C w/2% CaCl ₂	1.32 cf/sk	14.8 ppg
Excess 134%				

Stage #2 Lead: 0'-1028'	300 sks	50:50:10 C:Poz:Gel w/5% salt+ 0.25% CF +5 pps LCM	2.45 cf/sk	11.8 ppg
Excess 92%				

Note: Multi-stage tool to be set depending on hole conditions at approximately 1028' (50' below the surface casing shoe). Cement volumes will be adjusted proportionately for depth changes of multi-stage tool.

ATTACHMENT TO FORM 3160-3
COG Operating, LLC
SNEED 9 FEDERAL COM #1H
Page 4 of 6

7" X 5 1/2" TAPERED PRODUCTION CASING:

Cement details for 7" portion of tapered casing string as follows:.

**Option #1: Single Stage (Cement cal to Surface)
DV Tool & ECP (external csg. Packer) @ 6223' KOP:**

Lead:	500 sks	35:65:6 C:Poz Gel w/5%	2.05 cf/sk	12.5 ppg
0'-4173'		salt+ 5 pps LCM+ 0.2 %		
(min. tie back 200'		SMS+ 0.3% FL-52A+		
above 9 5/8"shoe)		0.125 pps CF		
Excess 59 %				
Tail:	400 sks	50:50:2 C:Poz Gel w/5%	1.37 cf/sk	14.0 ppg
4173'-6223'		salt+ 3 pps LCM+ 0.6 %		
Excess 78%		SMS+ 0.3% FL-52A+		
		0.125 pps CF+1% FL-25+		
		1% BA-58		

Option #2: Multi-stage (2 Stages) w/DV Tool & ECP@ +/-6223'

Stage #1:

Lead:	400 sks	35:65:6 C:Poz Gel w/5%	2.05 cf/sk	12.5 ppg
2340'-5173'		salt+ 5 pps LCM+ 0.2 %		
Excess 92%		SMS+ 0.3% FL-52A+		
		0.125 pps CF		
Tail:	250 sks	50:50:2 C:Poz Gel w/ 5 %	1.37 cf/sk	14.0 ppg
5173'-6223'		salt+ 3 pps LCM + 0.6%		
Excess 116%		SMS+1 % FL-25+ 1%		
		BA-58+ 0.125 pps CF		

Stage #2: 2nd DV Tool @ 2340' (50' below 9 5/8" csg shoe) (Cement cal to Surface)

Lead:	350 sks	35:65:6 C:Poz Gel w/5%	1.37 cf/sk	14.0 ppg
0'-2340'		salt+ 5 pps LCM+ 0.2 %		
(min. tie back 200'		SMS+ 0.3% FL-52A+		
above 9 5/8" shoe)		0.125 pps CF		
Excess 29%				

ATTACHMENT TO FORM 3160-3
COG Operating, LLC
SNEED 9 FEDERAL COM #1H
Page 5 of 6

Note: 5 ½" casing will be run from KOP at 6223' thru curve and lateral to TD of 11108' MD/6628' TVD. Productive intervals will be isolated by a Peak Packer system or similar.

Note: Assumption for 2nd DV tool is water flow. Cement volumes will be adjusted proportionately for depth changes of multi-stage tool.

Note: FL-52A is fluid loss additive, R-3 is retarder.

Note: Multi-stage tool to be set depending on hole conditions at approximately 2340' Cement volumes will be adjusted proportionately for depth changes of multi-stage tool.

8. Pressure Control Equipment:

The blowout preventer equipment (BOP) shown in Exhibit #9 will consist of a double ram-type (2000 psi WP) preventer, and in some cases possibly a 2000 psi Hydril type annular preventer as provided for in Onshore Order #2. This unit will be hydraulically operated and the ram type preventer will be equipped with blind rams on top and 4 1/2" drill pipe rams on the bottom. A 13-5/8" BOP will be used during the drilling of the well. A 13 5/8" permanent casing head will be installed on the 13 3/8" casing. The BOP will be nipped up on the 13 5/8" permanent casing head and tested to 2000 psig. After setting 9-5/8", permanent "B section" well head will be installed and the BOP will then be nipped up on the permanent B. BOP and well head will be tested by a third party to 2000 psig and used continuously until total depth is reached. Pipe rams will be operationally checked each 24-hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock and floor safety valve, choke lines and a choke manifold with a 2000 psi WP rating all of which will also be tested to working pressure by independent tester also.

SLB
COA

See
COA

9. Production Hole Drilling Summary:

Drill 8 ¾" hole and kick off at +/- 6223', building curve at 12°/100' over +/- 758' to 91° at 6981' MD/6700' TVD, Azm 89.81°. Drill 7 7/8" lateral section at 91° in a easterly direction (Azm 89.81°) for +/-4130' to TD at +/-11108' MD, 6628' TVD. Run 7" x 5-1/2" production casing. 7" to be run from surface to kickoff point and then changed over to 5 ½" with DV Tool and ECP at kickoff point. 5 ½" casing will be run from kickoff point to td and isolation packers set throughout lateral. 7" to be cemented from kickoff point to surface.

10. Auxiliary Well Control and Monitoring Equipment

- A. Kelly cock will be kept in the drill string at all times.
- B. A full opening drill pipe-stabbing valve with proper drill pipe connections will be on the rig floor at all times.

11. Logging, Testing and Coring Program:

- A. The following logs will be run in the vertical portion of the hole to KOP: SLB-PEX/HRLA, HNGS.

ATTACHMENT TO FORM 3160-3
COG Operating, LLC
SNEED 9 FEDERAL COM #1H
Page 6 of 6

- B. The mud logging program will consist of lagged 10' samples from KOP to TD in Horizontal hole.
- C. Drill Stem test is not anticipated.
- D. No conventional coring is anticipated.
- E. Further testing procedures will be determined after the 7" x 5 1/2" production casing has been cemented at TD based on drill shows and log evaluation.

12. Abnormal Conditions, Pressures, Temperatures and Potential Hazards:

No abnormal pressures or temperatures are anticipated. The estimated bottom hole temperature at TD is 99° Fahrenheit and estimated maximum bottom hole pressure is 2948 psi. Wells in the Majamar area will penetrate formations that are known or could reasonably be expected to contain Hydrogen Sulfide. Measurable gas volumes or Hydrogen Sulfide levels have not been encountered during drilling operations in this area, However as per Onshore order No. 6 a H2S drilling operations plan is included with this APD. No major loss of circulation zones has been reported in offsetting wells.

13. Anticipated Starting Date

Drilling operations will commence approximately on December 15, 2012 with drilling and completion operations lasting approximately 90 days.

Plan Proposal

FOR

COG Operating, LLC
Sneed 9 Federal Com #1H
Lea Co., NM

Design #1

Presented By:

Aaron Boger
Account Manager

Bret Wolford
Well Planner

SHL

330' FNL & 150' FWL

Penetration Point

334' FNL & 330' FWL

PBHL

330' FNL & 330' FEL

Sec:1-T17S-R32E

Accepted



Project: Lea County(NM27E)
Site: Sec.9T17S-R32E
Well: Sneed 9 Federal Com #1H
Wellbore: Wellbore #1
Design: Design #1
Lat: 32° 51' 19.398 N
Long: 103° 46' 44.533 W
GL: 4089.00
KB: WELL @ 4103.00usft

Archer

SECTION DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSect	Annotation
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
6179.21	0.00	0.00	6179.21	0.00	0.00	0.00	0.00	0.00	KOP / Start Build 11.00°
7006.48	91.00	91.00	6700.00	-9.25	529.88	11.00	91.00	529.84	EOC / Start DLS 3.00° TFO -89.99
7052.48	91.00	89.62	6699.20	-9.50	575.87	3.00	-89.99	575.83	EOT / Start 4219.16° hold at 7052.48 MD
11271.65	91.00	89.62	6625.56	18.50	4794.30	0.00	0.00	4794.34	TD at 11271.65

WELL DETAILS: Sneed 9 Federal Com #1H

WELL DETAILS: Sneed 9 Federal Com #1H							
+N/-S	+E/-W	Northing	Ground Level:	4089.00			
			Easting	Latitude	Longitude		Slot
0.00	0.00	675348.200	670215.800	32° 51' 19.398 N	103° 46' 44.533 W		

WELLBORE TARGET DETAILS (LAT/LONG)

Name	TVD	+N/-S	+E/-W	Latitude	Longitude	Shape
Sneed 9 Fed Com #1H PBHL	6625.56	18.50	4794.30	32° 51' 19.328 N	103° 45' 48.329 W	Point

PROJECT DETAILS: Lea County(NM27E)






Geodetic System: US State Plane 1927 (Exact solution)
Datum: NAD 1927 (NADCON CONUS)
Ellipsoid: Clarke 1866
Zone: New Mexico East 3001

System Datum: Mean Sea Level

SITE DETAILS: Sec.9T17S-R32E

Site Centre Latitude: 32° 51' 19.398 N
Longitude: 103° 46' 44.533 W

Positional Uncertainty: 0.00
Convergence: 0.30
Local North: Grid

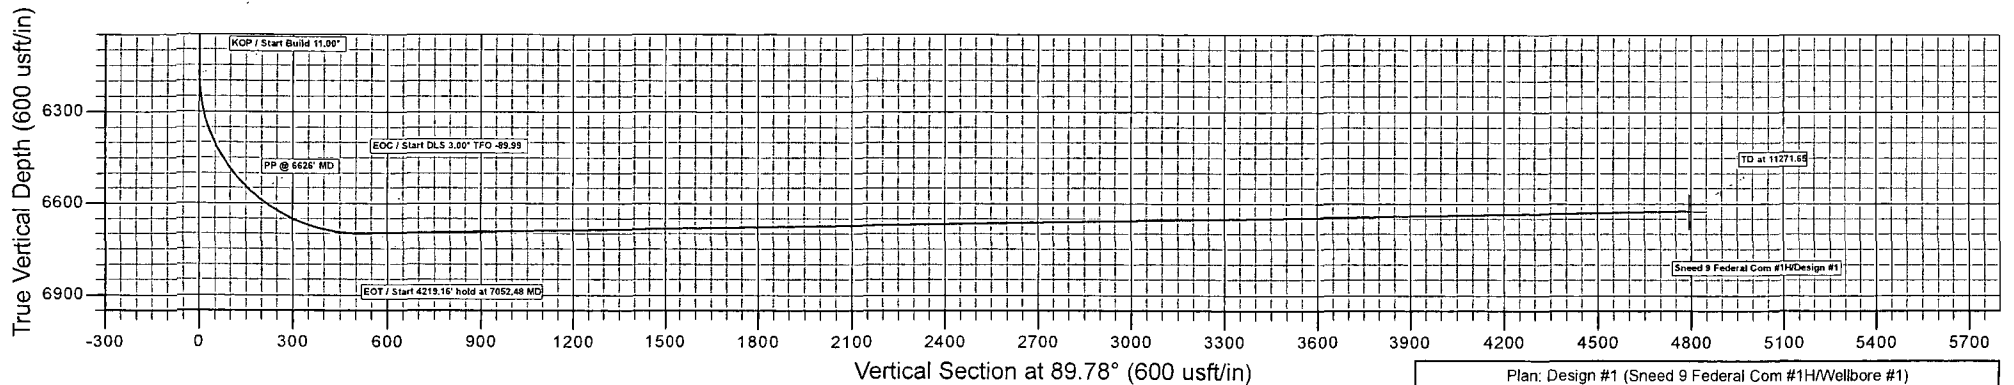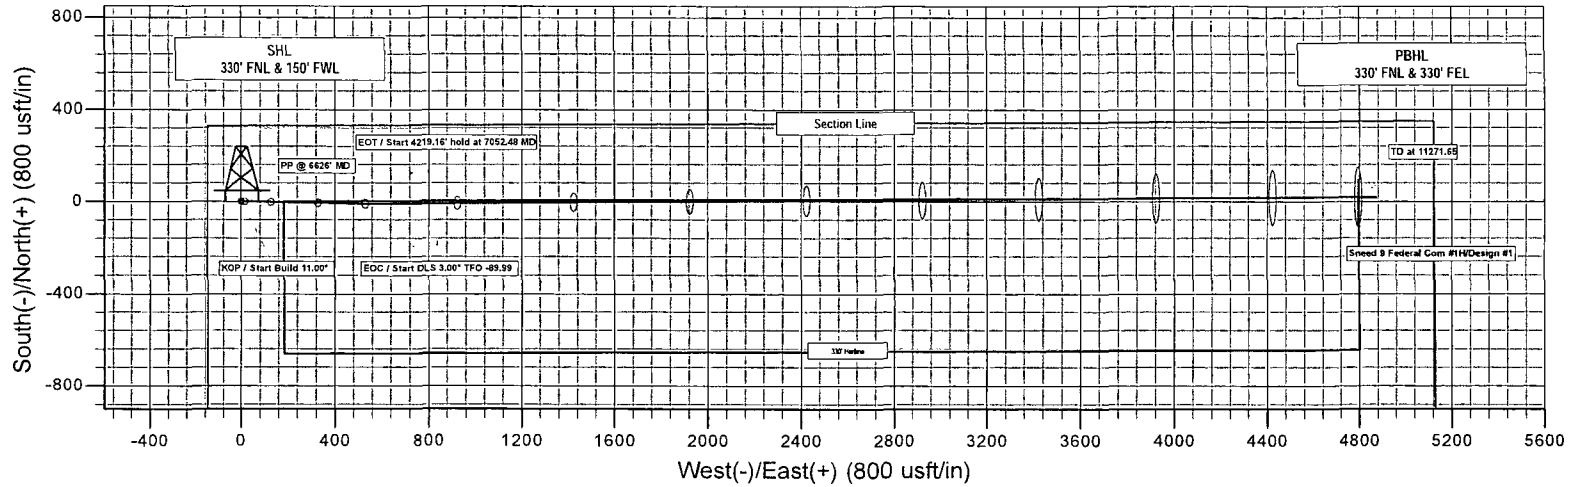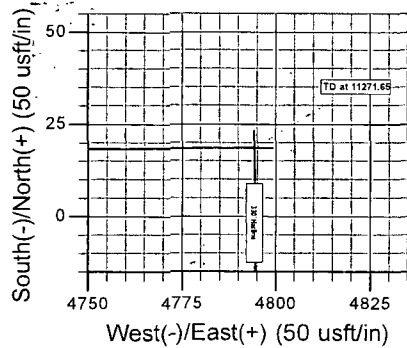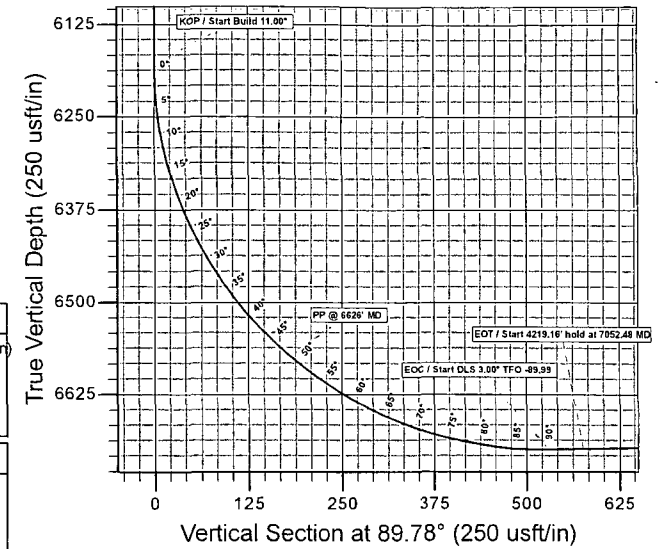

Plan: Design #1 (Sneed 9 Federal Com #1H/Wellbore #1)

Created By: Bret Wolford Date: 12:44, July 05 2013



COG Operating, LLC

Lea County(NM27E)

Sec.9T17S-R32E

Sneed 9 Federal Com #1H

Wellbore #1

Plan: Design #1

Standard Planning Report

05 July, 2013

Archer

Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Sneed 9 Federal Com #1H
Company:	COG Operating, LLC	TVD Reference:	WELL @ 4103.00usft
Project:	Lea County(NM27E)	MD Reference:	WELL @ 4103.00usft
Site:	Sec.9T17S-R32E	North Reference:	Grid
Well:	Sneed 9 Federal Com #1H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Project:	Lea County(NM27E)		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Site:	Sec.9T17S-R32E		
Site Position:		Northing:	675,348.200 usft
From:	Map	Easting:	670,215.800 usft
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16"
		Latitude:	32° 51' 19.398 N
		Longitude:	103° 46' 44.533 W
		Grid Convergence:	0.30 °

Well:	Sneed 9 Federal Com #1H					
Well Position	+N/-S	0.00 usft	Northing:	675,348.200 usft	Latitude:	32° 51' 19.398 N
	+E/-W	0.00 usft	Easting:	670,215.800 usft	Longitude:	103° 46' 44.533 W
Position Uncertainty		0.00 usft	Wellhead Elevation:	usft	Ground Level:	4,089.00 usft

Wellbore		Wellbore #1			
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2010	07/05/13	7.48	60.68	48,763

Design:	Design #1			
Audit Notes:				
Version:	Phase:	PLAN	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD)	+N/-S	+E/-W	Direction
	(usft)	(usft)	(usft)	(°)
	6,625.56	0.00	0.00	89.78

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
6,179.21	0.00	0.00	6,179.21	0.00	0.00	0.00	0.00	0.00	0.00	
7,006.48	91.00	91.00	6,700.00	-9.25	529.88	11.00	11.00	0.00	91.00	
7,052.48	91.00	89.62	6,699.20	-9.50	575.87	3.00	0.00	-3.00	-89.99	Sneed 9 Fed Com #1
11,271.65	91.00	89.62	6,625.56	18.50	4,794.30	0.00	0.00	0.00	0.00	Sneed 9 Fed Com #1

Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Sneed 9 Federal Com #1H
Company:	COG Operating, LLC	TVD Reference:	WELL @ 4103.00usft
Project:	Lea County(NM27E)	MD Reference:	WELL @ 4103.00usft
Site:	Sec.9T17S-R32E	North Reference:	Grid
Well:	Sneed 9 Federal Com #1H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Planned/Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
100.00	0.00	0.00	100.00	0.00	0.00	0.00	0.00	0.00	0.00
200.00	0.00	0.00	200.00	0.00	0.00	0.00	0.00	0.00	0.00
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00	0.00
500.00	0.00	0.00	500.00	0.00	0.00	0.00	0.00	0.00	0.00
600.00	0.00	0.00	600.00	0.00	0.00	0.00	0.00	0.00	0.00
700.00	0.00	0.00	700.00	0.00	0.00	0.00	0.00	0.00	0.00
800.00	0.00	0.00	800.00	0.00	0.00	0.00	0.00	0.00	0.00
900.00	0.00	0.00	900.00	0.00	0.00	0.00	0.00	0.00	0.00
1,000.00	0.00	0.00	1,000.00	0.00	0.00	0.00	0.00	0.00	0.00
1,100.00	0.00	0.00	1,100.00	0.00	0.00	0.00	0.00	0.00	0.00
1,200.00	0.00	0.00	1,200.00	0.00	0.00	0.00	0.00	0.00	0.00
1,300.00	0.00	0.00	1,300.00	0.00	0.00	0.00	0.00	0.00	0.00
1,400.00	0.00	0.00	1,400.00	0.00	0.00	0.00	0.00	0.00	0.00
1,500.00	0.00	0.00	1,500.00	0.00	0.00	0.00	0.00	0.00	0.00
1,600.00	0.00	0.00	1,600.00	0.00	0.00	0.00	0.00	0.00	0.00
1,700.00	0.00	0.00	1,700.00	0.00	0.00	0.00	0.00	0.00	0.00
1,800.00	0.00	0.00	1,800.00	0.00	0.00	0.00	0.00	0.00	0.00
1,900.00	0.00	0.00	1,900.00	0.00	0.00	0.00	0.00	0.00	0.00
2,000.00	0.00	0.00	2,000.00	0.00	0.00	0.00	0.00	0.00	0.00
2,100.00	0.00	0.00	2,100.00	0.00	0.00	0.00	0.00	0.00	0.00
2,200.00	0.00	0.00	2,200.00	0.00	0.00	0.00	0.00	0.00	0.00
2,300.00	0.00	0.00	2,300.00	0.00	0.00	0.00	0.00	0.00	0.00
2,400.00	0.00	0.00	2,400.00	0.00	0.00	0.00	0.00	0.00	0.00
2,500.00	0.00	0.00	2,500.00	0.00	0.00	0.00	0.00	0.00	0.00
2,600.00	0.00	0.00	2,600.00	0.00	0.00	0.00	0.00	0.00	0.00
2,700.00	0.00	0.00	2,700.00	0.00	0.00	0.00	0.00	0.00	0.00
2,800.00	0.00	0.00	2,800.00	0.00	0.00	0.00	0.00	0.00	0.00
2,900.00	0.00	0.00	2,900.00	0.00	0.00	0.00	0.00	0.00	0.00
3,000.00	0.00	0.00	3,000.00	0.00	0.00	0.00	0.00	0.00	0.00
3,100.00	0.00	0.00	3,100.00	0.00	0.00	0.00	0.00	0.00	0.00
3,200.00	0.00	0.00	3,200.00	0.00	0.00	0.00	0.00	0.00	0.00
3,300.00	0.00	0.00	3,300.00	0.00	0.00	0.00	0.00	0.00	0.00
3,400.00	0.00	0.00	3,400.00	0.00	0.00	0.00	0.00	0.00	0.00
3,500.00	0.00	0.00	3,500.00	0.00	0.00	0.00	0.00	0.00	0.00
3,600.00	0.00	0.00	3,600.00	0.00	0.00	0.00	0.00	0.00	0.00
3,700.00	0.00	0.00	3,700.00	0.00	0.00	0.00	0.00	0.00	0.00
3,800.00	0.00	0.00	3,800.00	0.00	0.00	0.00	0.00	0.00	0.00
3,900.00	0.00	0.00	3,900.00	0.00	0.00	0.00	0.00	0.00	0.00
4,000.00	0.00	0.00	4,000.00	0.00	0.00	0.00	0.00	0.00	0.00
4,100.00	0.00	0.00	4,100.00	0.00	0.00	0.00	0.00	0.00	0.00
4,200.00	0.00	0.00	4,200.00	0.00	0.00	0.00	0.00	0.00	0.00
4,300.00	0.00	0.00	4,300.00	0.00	0.00	0.00	0.00	0.00	0.00
4,400.00	0.00	0.00	4,400.00	0.00	0.00	0.00	0.00	0.00	0.00
4,500.00	0.00	0.00	4,500.00	0.00	0.00	0.00	0.00	0.00	0.00
4,600.00	0.00	0.00	4,600.00	0.00	0.00	0.00	0.00	0.00	0.00
4,700.00	0.00	0.00	4,700.00	0.00	0.00	0.00	0.00	0.00	0.00
4,800.00	0.00	0.00	4,800.00	0.00	0.00	0.00	0.00	0.00	0.00
4,900.00	0.00	0.00	4,900.00	0.00	0.00	0.00	0.00	0.00	0.00
5,000.00	0.00	0.00	5,000.00	0.00	0.00	0.00	0.00	0.00	0.00
5,100.00	0.00	0.00	5,100.00	0.00	0.00	0.00	0.00	0.00	0.00
5,200.00	0.00	0.00	5,200.00	0.00	0.00	0.00	0.00	0.00	0.00
5,300.00	0.00	0.00	5,300.00	0.00	0.00	0.00	0.00	0.00	0.00

Database:	EDM 5000.1-Single User Db	Local Co-ordinate Reference:	Well Sneed 9 Federal Com #1H
Company:	COG Operating, LLC	TVD Reference:	WELL @ 4103.00usft
Project:	Lea County(NM27E)	MD Reference:	WELL @ 4103.00usft
Site:	Sec:9T17S-R32E	North Reference:	Grid
Well:	Sneed 9 Federal Com #1H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
5,400.00	0.00	0.00	5,400.00	0.00	0.00	0.00	0.00	0.00	0.00
5,500.00	0.00	0.00	5,500.00	0.00	0.00	0.00	0.00	0.00	0.00
5,600.00	0.00	0.00	5,600.00	0.00	0.00	0.00	0.00	0.00	0.00
5,700.00	0.00	0.00	5,700.00	0.00	0.00	0.00	0.00	0.00	0.00
5,800.00	0.00	0.00	5,800.00	0.00	0.00	0.00	0.00	0.00	0.00
5,900.00	0.00	0.00	5,900.00	0.00	0.00	0.00	0.00	0.00	0.00
6,000.00	0.00	0.00	6,000.00	0.00	0.00	0.00	0.00	0.00	0.00
6,100.00	0.00	0.00	6,100.00	0.00	0.00	0.00	0.00	0.00	0.00
KOP / Start Build 11.00°									
6,179.21	0.00	0.00	6,179.21	0.00	0.00	0.00	0.00	0.00	0.00
6,200.00	2.29	91.00	6,199.99	-0.01	0.41	0.41	11.00	11.00	0.00
6,250.00	7.79	91.00	6,249.78	-0.08	4.80	4.80	11.00	11.00	0.00
6,300.00	13.29	91.00	6,298.92	-0.24	13.94	13.94	11.00	11.00	0.00
6,350.00	18.79	91.00	6,346.96	-0.48	27.75	27.74	11.00	11.00	0.00
6,400.00	24.29	91.00	6,393.45	-0.80	46.09	46.09	11.00	11.00	0.00
6,450.00	29.79	91.00	6,437.97	-1.20	68.81	68.80	11.00	11.00	0.00
6,500.00	35.29	91.00	6,480.10	-1.67	95.69	95.68	11.00	11.00	0.00
6,550.00	40.79	91.00	6,519.47	-2.21	126.48	126.47	11.00	11.00	0.00
6,600.00	46.29	91.00	6,555.70	-2.81	160.90	160.89	11.00	11.00	0.00
PP @ 6626' MD									
6,626.00	49.15	91.00	6,573.19	-3.14	180.13	180.12	11.00	11.00	0.00
6,650.00	51.79	91.00	6,588.47	-3.47	198.64	198.62	11.00	11.00	0.00
6,700.00	57.29	91.00	6,617.46	-4.18	239.34	239.32	11.00	11.00	0.00
6,750.00	62.79	91.00	6,642.43	-4.93	282.63	282.61	11.00	11.00	0.00
6,800.00	68.29	91.00	6,663.12	-5.73	328.12	328.10	11.00	11.00	0.00
6,850.00	73.79	91.00	6,679.36	-6.55	375.38	375.35	11.00	11.00	0.00
6,900.00	79.29	91.00	6,691.00	-7.40	423.98	423.95	11.00	11.00	0.00
6,950.00	84.79	91.00	6,697.92	-8.26	473.47	473.44	11.00	11.00	0.00
7,000.00	90.29	91.00	6,700.07	-9.14	523.40	523.36	11.00	11.00	0.00
EOC / Start DLS 3.00° TFO -89.99									
7,006.48	91.00	91.00	6,700.00	-9.25	529.88	529.84	11.00	11.00	0.00
EOT / Start 4219.16' hold at 7052.48 MD									
7,052.48	91.00	89.62	6,699.20	-9.50	575.87	575.83	3.00	0.00	-3.00
7,100.00	91.00	89.62	6,698.37	-9.18	623.38	623.34	0.00	0.00	0.00
7,200.00	91.00	89.62	6,696.62	-8.52	723.36	723.33	0.00	0.00	0.00
7,300.00	91.00	89.62	6,694.88	-7.86	823.35	823.31	0.00	0.00	0.00
7,400.00	91.00	89.62	6,693.13	-7.19	923.33	923.30	0.00	0.00	0.00
7,500.00	91.00	89.62	6,691.39	-6.53	1,023.31	1,023.28	0.00	0.00	0.00
7,600.00	91.00	89.62	6,689.64	-5.86	1,123.29	1,123.26	0.00	0.00	0.00
7,700.00	91.00	89.62	6,687.90	-5.20	1,223.28	1,223.25	0.00	0.00	0.00
7,800.00	91.00	89.62	6,686.15	-4.54	1,323.26	1,323.23	0.00	0.00	0.00
7,900.00	91.00	89.62	6,684.41	-3.87	1,423.24	1,423.22	0.00	0.00	0.00
8,000.00	91.00	89.62	6,682.66	-3.21	1,523.23	1,523.20	0.00	0.00	0.00
8,100.00	91.00	89.62	6,680.92	-2.55	1,623.21	1,623.19	0.00	0.00	0.00
8,200.00	91.00	89.62	6,679.17	-1.88	1,723.19	1,723.17	0.00	0.00	0.00
8,300.00	91.00	89.62	6,677.42	-1.22	1,823.17	1,823.15	0.00	0.00	0.00
8,400.00	91.00	89.62	6,675.68	-0.56	1,923.16	1,923.14	0.00	0.00	0.00
8,500.00	91.00	89.62	6,673.93	0.11	2,023.14	2,023.12	0.00	0.00	0.00
8,600.00	91.00	89.62	6,672.19	0.77	2,123.12	2,123.11	0.00	0.00	0.00
8,700.00	91.00	89.62	6,670.44	1.43	2,223.10	2,223.09	0.00	0.00	0.00
8,800.00	91.00	89.62	6,668.70	2.10	2,323.09	2,323.08	0.00	0.00	0.00
8,900.00	91.00	89.62	6,666.95	2.76	2,423.07	2,423.06	0.00	0.00	0.00
9,000.00	91.00	89.62	6,665.21	3.43	2,523.05	2,523.05	0.00	0.00	0.00

Database:	EDM 5000.1 Single User Db	Local Coordinate Reference:	Well Sneed 9 Federal Com #1H
Company:	COG Operating, LLC	TVD Reference:	WELL @ 4103.00usft
Project:	Lea County(NM27E)	MD Reference:	WELL @ 4103.00usft
Site:	Sec.9T17S-R32E	North Reference:	Grid
Well:	Sneed 9 Federal Com #1H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		


Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
9,100.00	91.00	89.62	6,663.46	4.09	2,623.03	2,623.03	0.00	0.00	0.00	
9,200.00	91.00	89.62	6,661.72	4.75	2,723.02	2,723.01	0.00	0.00	0.00	
9,300.00	91.00	89.62	6,659.97	5.42	2,823.00	2,823.00	0.00	0.00	0.00	
9,400.00	91.00	89.62	6,658.23	6.08	2,922.98	2,922.98	0.00	0.00	0.00	
9,500.00	91.00	89.62	6,656.48	6.74	3,022.96	3,022.97	0.00	0.00	0.00	
9,600.00	91.00	89.62	6,654.74	7.41	3,122.95	3,122.95	0.00	0.00	0.00	
9,700.00	91.00	89.62	6,652.99	8.07	3,222.93	3,222.94	0.00	0.00	0.00	
9,800.00	91.00	89.62	6,651.25	8.73	3,322.91	3,322.92	0.00	0.00	0.00	
9,900.00	91.00	89.62	6,649.50	9.40	3,422.89	3,422.90	0.00	0.00	0.00	
10,000.00	91.00	89.62	6,647.76	10.06	3,522.88	3,522.89	0.00	0.00	0.00	
10,100.00	91.00	89.62	6,646.01	10.73	3,622.86	3,622.87	0.00	0.00	0.00	
10,200.00	91.00	89.62	6,644.27	11.39	3,722.84	3,722.86	0.00	0.00	0.00	
10,300.00	91.00	89.62	6,642.52	12.05	3,822.82	3,822.84	0.00	0.00	0.00	
10,400.00	91.00	89.62	6,640.77	12.72	3,922.81	3,922.83	0.00	0.00	0.00	
10,500.00	91.00	89.62	6,639.03	13.38	4,022.79	4,022.81	0.00	0.00	0.00	
10,600.00	91.00	89.62	6,637.28	14.04	4,122.77	4,122.80	0.00	0.00	0.00	
10,700.00	91.00	89.62	6,635.54	14.71	4,222.75	4,222.78	0.00	0.00	0.00	
10,800.00	91.00	89.62	6,633.79	15.37	4,322.74	4,322.76	0.00	0.00	0.00	
10,900.00	91.00	89.62	6,632.05	16.03	4,422.72	4,422.75	0.00	0.00	0.00	
11,000.00	91.00	89.62	6,630.30	16.70	4,522.70	4,522.73	0.00	0.00	0.00	
11,100.00	91.00	89.62	6,628.56	17.36	4,622.68	4,622.72	0.00	0.00	0.00	
11,200.00	91.00	89.62	6,626.81	18.02	4,722.67	4,722.70	0.00	0.00	0.00	
TD at 11271.65 - Sneed 9 Fed Com #1H PBHL										
11,271.65	91.00	89.62	6,625.56	18.50	4,794.30	4,794.34	0.00	0.00	0.00	

Design Targets										
Target Name	Dip Angle (°)	Dip Dir (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude	
- hit/miss target										
- Shape										
Sneed 9 Fed Com #1H F	0.00	0.00	6,625.56	18.50	4,794.30	675,366.700	675,010.100	32° 51' 19.328 N	103° 45' 48.329 W	
- plan hits target center										
- Point										

Plan Annotations					
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates			
		+N/-S (usft)	+E/-W (usft)	Comment	
6,179.21	6,179.21	0.00	0.00	KOP / Start Build 11.00°	
6,626.00	6,573.19	-3.14	180.13	PP @ 6626' MD	
7,006.48	6,700.00	-9.25	529.88	EOC / Start DLS 3.00° TFO -89.99	
7,052.48	6,699.20	-9.50	575.87	EOT / Start 4219.16' hold at 7052.48 MD	
11,271.65	6,625.56	18.50	4,794.30	TD at 11271.65	

COG Operating LLC

Sneed 9 Fed Com #1H - H2S Safety Equipment Diagram

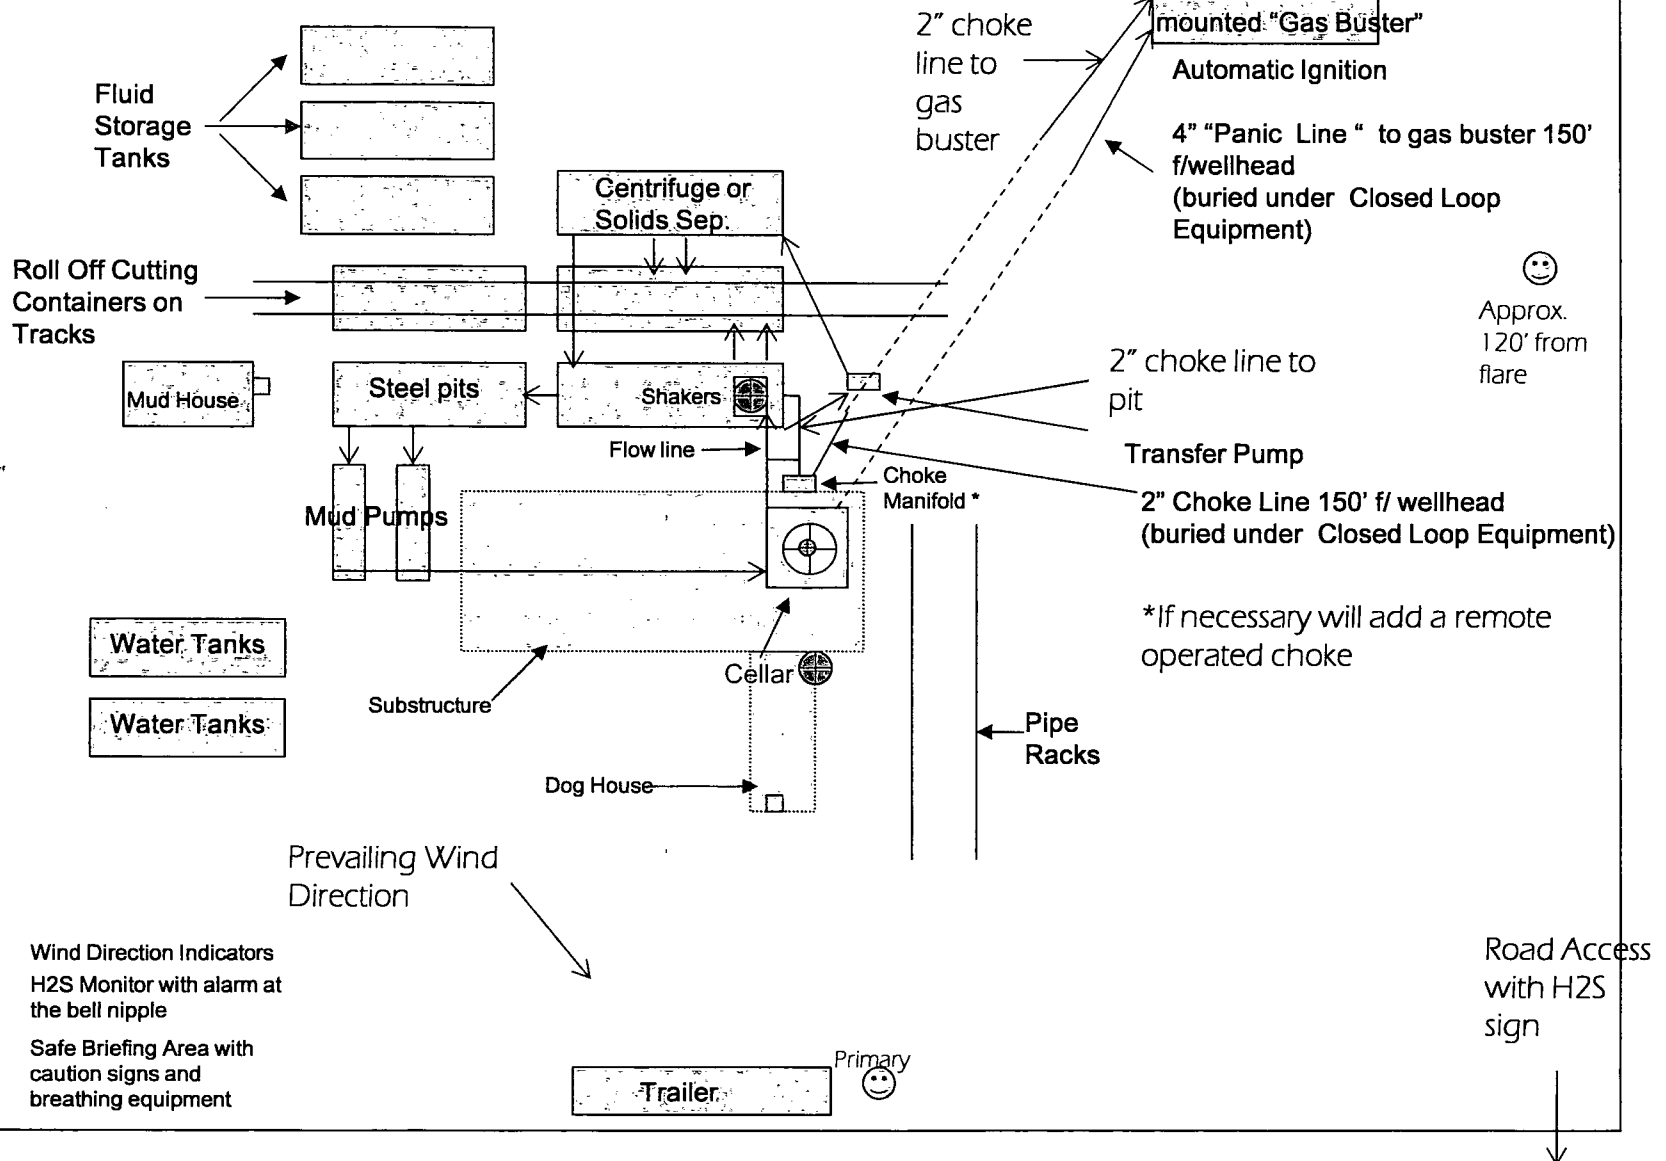


NOTES REGARDING THE BLOWOUT PREVENTERS

**Master Drilling Plan
Eddy County, New Mexico**

1. Drilling nipple to be so constructed that it can be removed without use of a welder through rotary table opening, with minimum I.D. equal to preventer bore.
2. Wear ring to be properly installed in head.
3. Blow out preventer and all fittings must be in good condition, 2000 psi WP minimum.
4. All fittings to be flanged.
5. Safety valve must be available on rig floor at all times with proper connections, valve to be full 2000 psi WP minimum.
6. All choke and fill lines to be securely anchored especially ends of choke lines
7. Equipment through which bit must pass shall be at least as large as the diameter of the casing being drilled through.
8. Kelly cock on Kelly.
9. Extension wrenches and hands wheels to be properly installed.
10. Blow out preventer control to be located as close to driller's position as feasible.
11. Blow out preventer closing equipment to include minimum 40-gallon accumulator, two independent sources of pump power on each closing unit installation all API specifications.

13 5/8" 2K ANNULAR

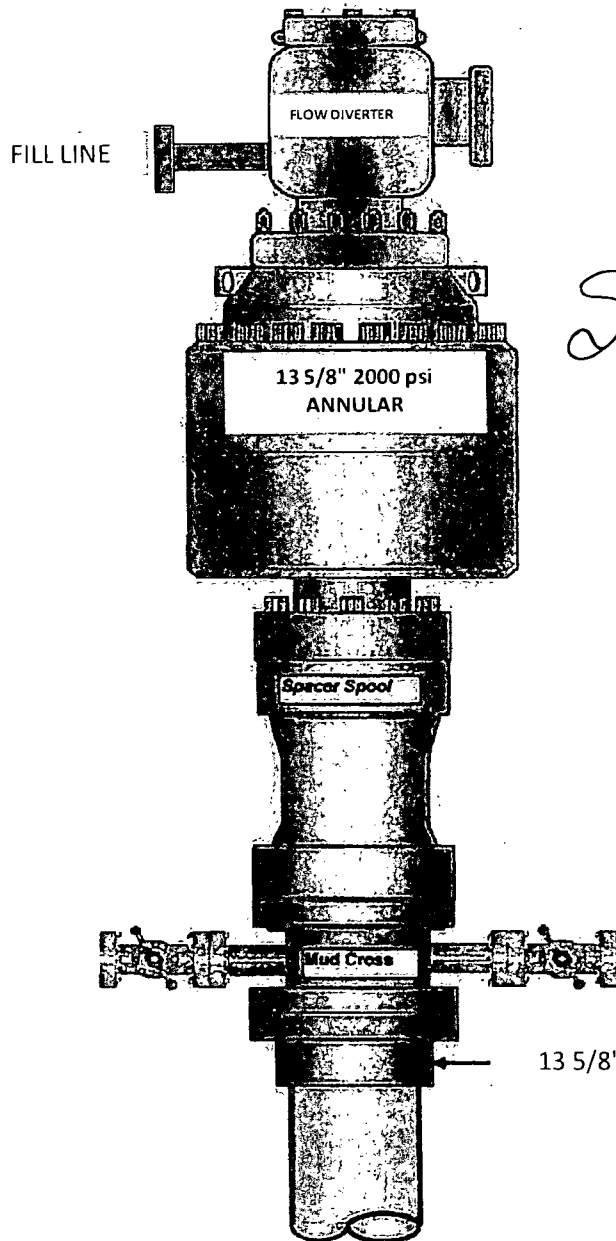

See
CWP


4-1/16", 2K VALVES

13 5/8" 3K "A" SECTION


COG Operating LLC

Exhibit #9

BOPE and Choke Schematic

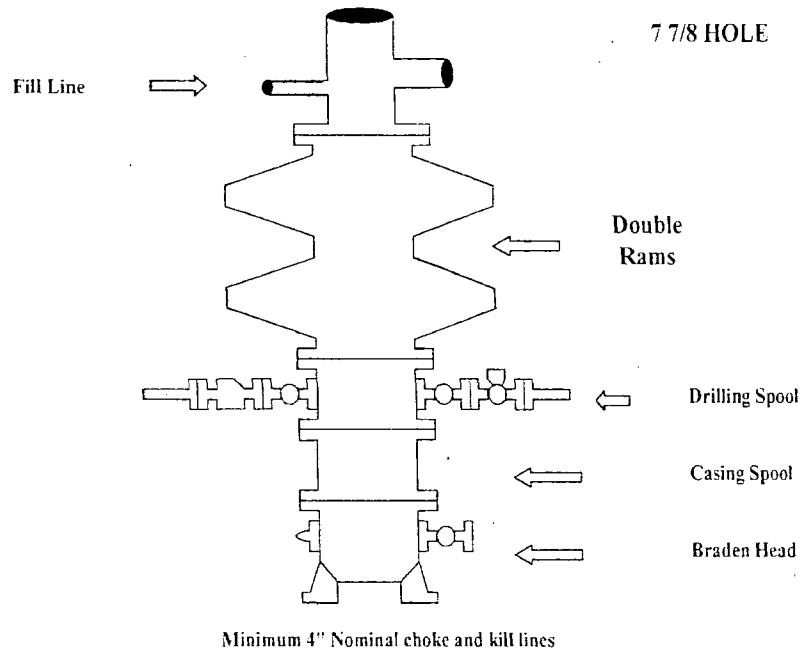


Choke Manifold Requirement (2000 psi WP)
No Annular Required

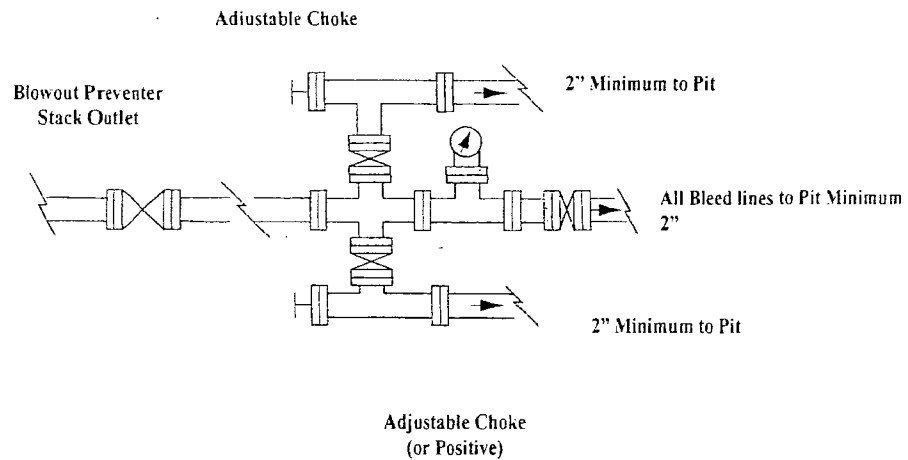

COG Operating LLC

Closed Loop Equipment Diagram

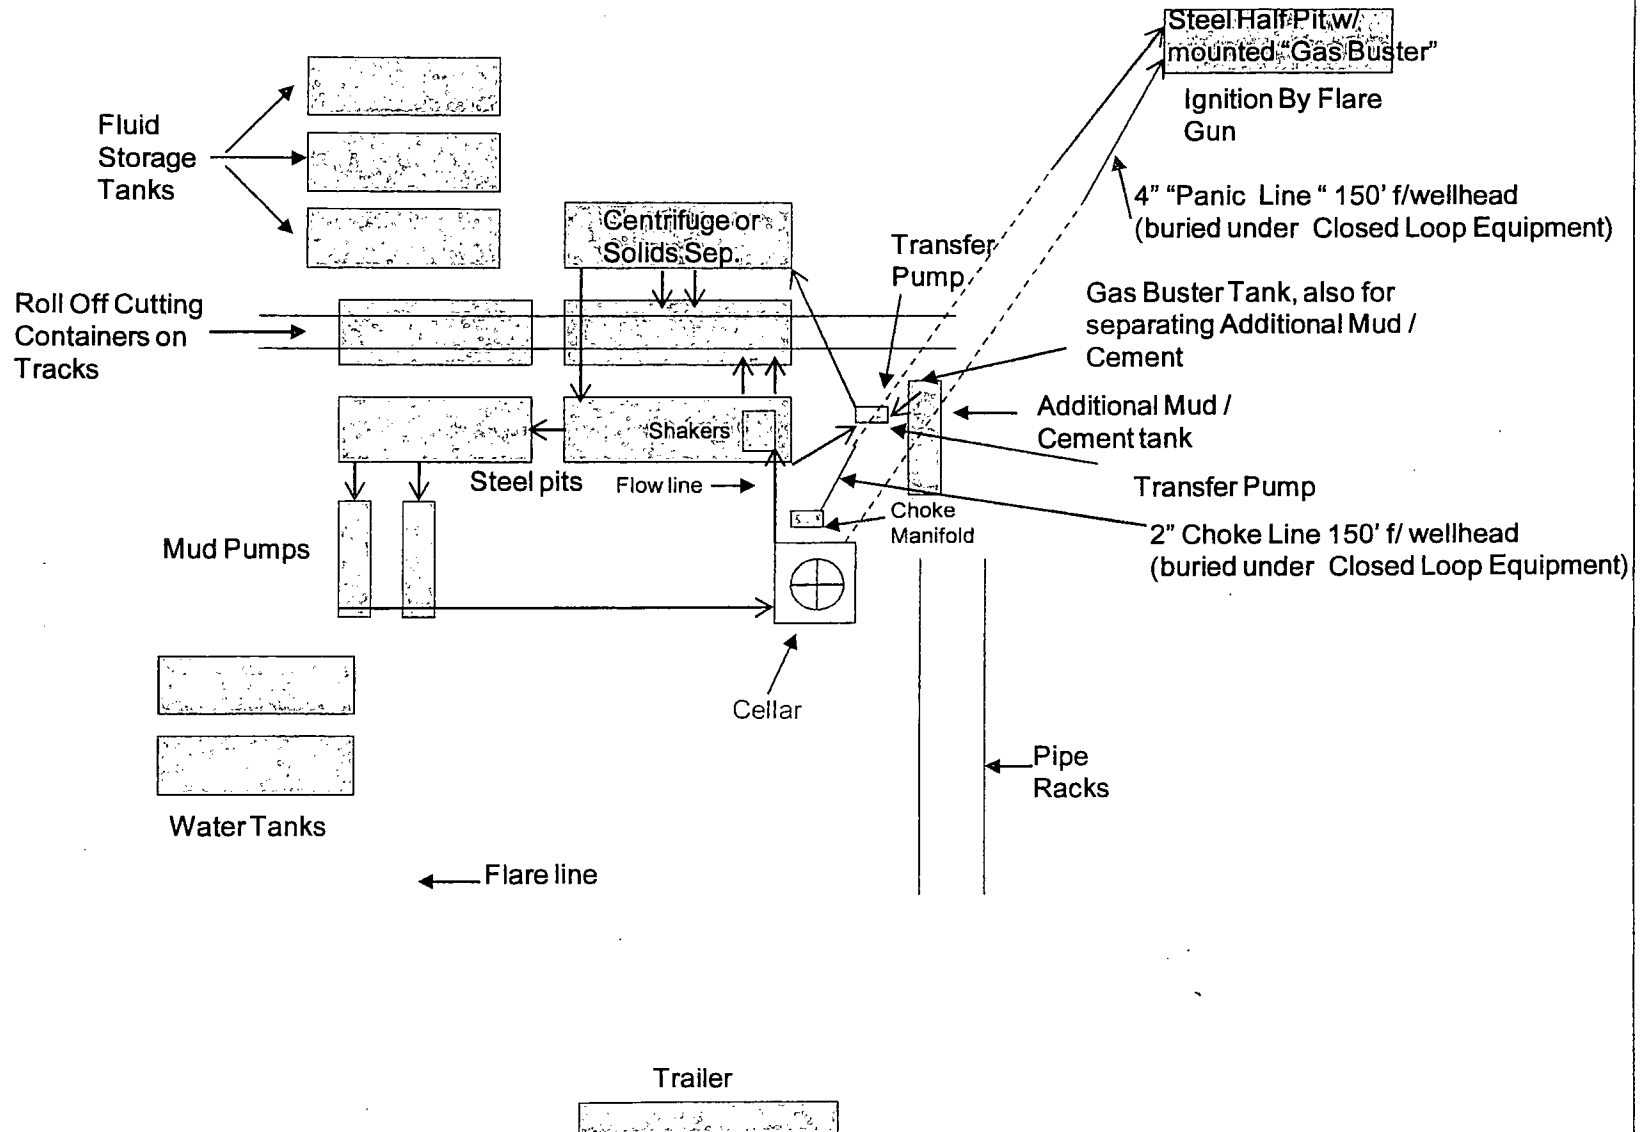

Closed Loop Operation & Maintenance Procedure

All drilling fluid circulated over shaker(s) with cuttings discharged into roll off container.

Fluid and fines below shaker(s) are circulated with transfer pump through centrifuge(s) or solids separator with cuttings and fines discharged into roll off container.

Fluid is continuously re-circulated through equipment with polymer added to aid separation of cutting fines.

Roll off containers are lined and de-watered with fluids re-circulated into system.

Additional tank is used to capture unused drilling fluid or cement returns from casing jobs.

This equipment will be maintained 24 hrs./day by solids control personnel and or rig crews that stay on location.

Cuttings will be hauled to either:

CRI (permit number R9166)

or

GMI (permit number 711-019-001)

dependent upon which rig is available to drill this well.
