

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

OCD Hobbs

HOBBS OCD

FORM APPROVED
OMB NO. 1004-0135
Expires: July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter abandoned well. Use form 3160-3 (APD) for such proposals.

JAN 07 2014

5. Lease Serial No.
NMNM077004

6. If Indian, Allottee or Tribe Name

7. If Unit or CA/Agreement, Name and/or No.

SUBMIT IN TRIPLICATE - Other instructions on reverse side

RECEIVED

1. Type of Well
 Oil Well Gas Well Other

8. Well Name and No.
EXCALIBUR 17 MP FED COM 1H

2. Name of Operator
MEWBOURNE OIL COMPANY
Contact: JACKIE LATHAN
E-Mail: jlathan@mewbourne.com

9. API Well No.
30-025-41255-00-X1

3a. Address
HOBBS, NM 88241

3b. Phone No. (include area code)
Ph: 575-393-5905
Fx: 575-397-6252

10. Field and Pool, or Exploratory
TONTON

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
Sec 17 T19S R33E SWSW 500FSL 20FWL
32.391592 N Lat, 103.413758 W Lon

11. County or Parish, and State
LEA COUNTY, NM

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Deepen
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Fracture Treat
	<input type="checkbox"/> Production (Start/Resume)
	<input type="checkbox"/> Reclamation
	<input type="checkbox"/> Water Shut-Off
	<input type="checkbox"/> Well Integrity
	<input checked="" type="checkbox"/> Other
	Drilling Operations
	<input type="checkbox"/> Change Plans
	<input type="checkbox"/> New Construction
	<input type="checkbox"/> Recomplete
	<input type="checkbox"/> Plug and Abandon
	<input type="checkbox"/> Temporarily Abandon
	<input type="checkbox"/> Convert to Injection
	<input type="checkbox"/> Plug Back
	<input type="checkbox"/> Water Disposal

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

11/15/13 TD 12 1/4" hole @ 5116'. Ran 5116' of 9 5/8" 40 & 36# J55 & N80 LT&C csg. Cemented with 1400 sks Class C (35:65:6) w/additives. Mixed @ 12.6 #/g w/1.99 yd. Tail w/200 sks Class C w/additives. Mixed @ 14.8#/g w/1.37 yd. Plug down @ 3:45 PM 11/15/13. Test BOPE to 3000# & Annular to 1500#. At 8:00 P.M. 11/16/13, tested csg to 1500# for 30 minutes, held OK. Circ 119 sks of cement to pit.

Chart & schematic attached.


Bonds on file: NM1693 nationwide & NMB000919

14. I hereby certify that the foregoing is true and correct.

**Electronic Submission #229770 verified by the BLM Well Information System
For MEWBOURNE OIL COMPANY, sent to the Hobbs
Committed to AFMSS for processing by JOHNNY DICKERSON on 12/18/2013 (14JLD1017SE)**

Name (Printed/Typed) JACKIE LATHAN	Title AUTHORIZED REPRESENTATIVE
Signature (Electronic Submission)	Date 12/17/2013

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved By ACCEPTED	JAMES A AMOS Title SUPERVISORY EPS	Date 12/28/2013
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.		Office Hobbs 

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

**** BLM REVISED ** BLM REVISED ** BLM REVISED ** BLM REVISED ** BLM REVISED ****

FEB 12 2014



PO Box 7
Lovington, NM 88260
(575) 224-2345 (575) 942-9472

Company Newberry Oil Co Date 11/16/13
Lease EXPLOR 17 MP Fed com 1# County Lea County
Drilling Contractor Patterson TS Plug & Drill Pipe Size 11" C27 / 4 1/2 XH

Accumulator Function Test - OO&GO#2 To Check - USABLE FLUID IN THE NITROGEN BOTTLES (III.A.2.c.i. or ii or iii)

- Make sure all rams and annular are open and if applicable HCR is closed.
 - Ensure accumulator is pumped up to working pressure! (Shut off all pumps)
1. Open HCR Valve. (If applicable)
 2. Close annular.
 3. Close **all** pipe rams.
 4. Open one set of the pipe rams to simulate closing the blind ram.
 5. For 3 ram stacks, open the annular to achieve the 50+ % safety factor. (5M and greater systems).
 6. Record remaining pressure 1350 psi. Test fails if pressure is lower than required.
a. {950 psi for a 1500 psi system} b. {1200 psi for a 2000 & 3000 psi system}
 7. If annular is closed, open it at this time and close HCR.


To Check - PRECHARGE ON BOTTLES OR SPHERICAL (III.A.2.d.)


- Start with manifold pressure at, or above, maximum acceptable pre-charge pressure.
a. {800 psi for a 1500 psi system} b. {1100 psi for 2000 and 3000 psi system}
1. Open bleed line to the tank, slowly. (gauge needle will drop at the lowest bottle pressure)
 2. Close bleed line. Barely bump electric pump and see what pressure the needle jumps up to.
 3. Record pressure drop 1000 psi. Test fails if pressure drops below minimum.
- Minimum: a. {700 psi for a 1500 psi system} b. {900 psi for a 2000 & 3000 psi system}

To Check - THE CAPACITY OF THE ACCUMULATOR PUMPS (III.A.2.f.)

- Isolate the accumulator bottles or spherical from the pumps & manifold.
 - Open the bleed off valve to the tank, {manifold psi should go to 0 psi} close bleed valve.
1. Open the HCR valve, {if applicable}
 2. Close annular.
 3. With pumps only, time how long it takes to regain the required manifold pressure.
 4. Record elapsed time 65 sec. Test fails if it takes over 2 minutes.
a. {950 psi for a 1500 psi system} b. {1200 psi for a 2000 & 3000 psi system}


GRAPHIC W. DATA

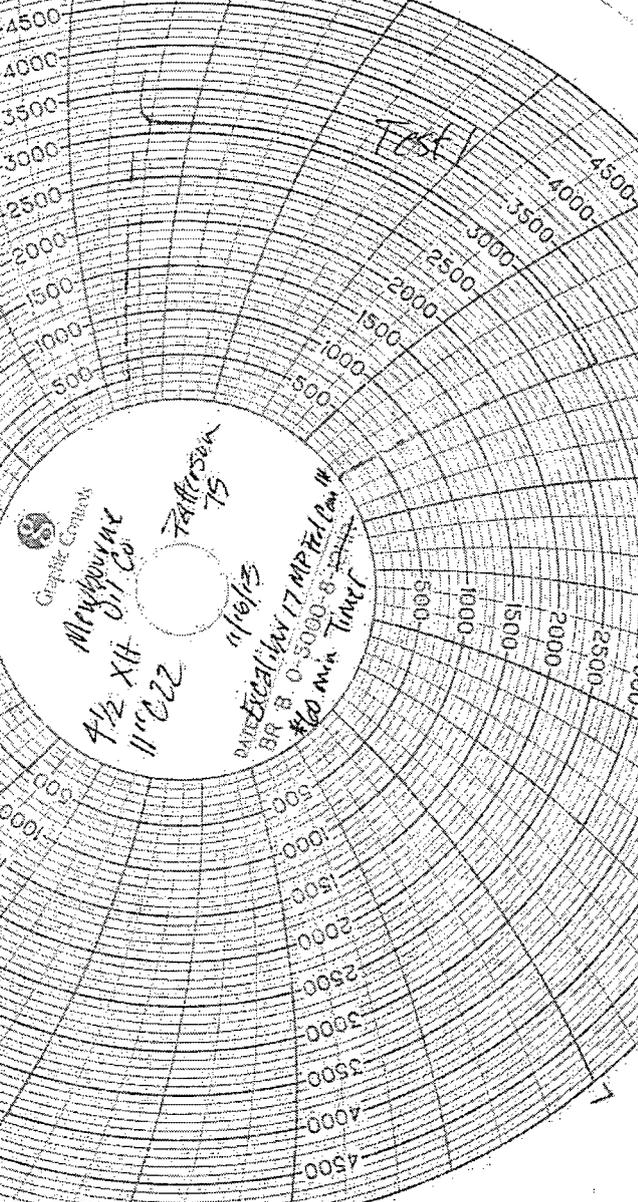

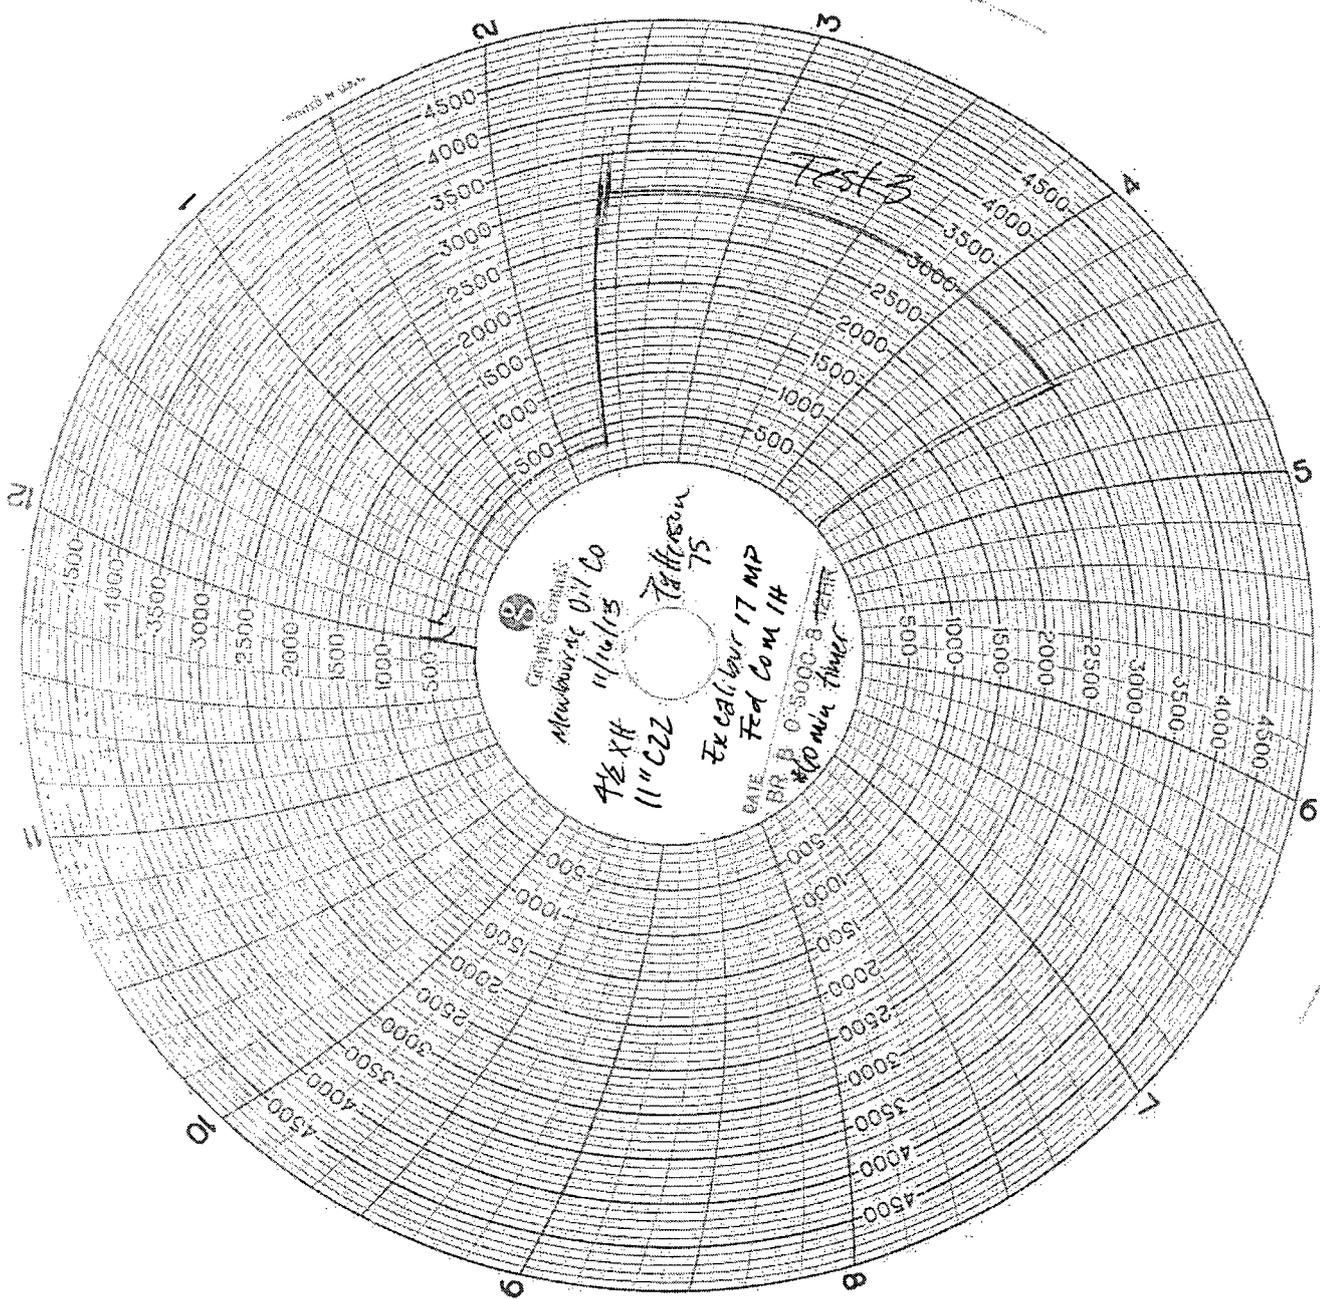

McLoughlin Oil Co
7 1/2 x 11
11" O.D.
Tullahoma
TS
Ex Cal. by 17 MP
Fed Com 14
DATE BR 0.5000-8
#10 min. timer

Test 8

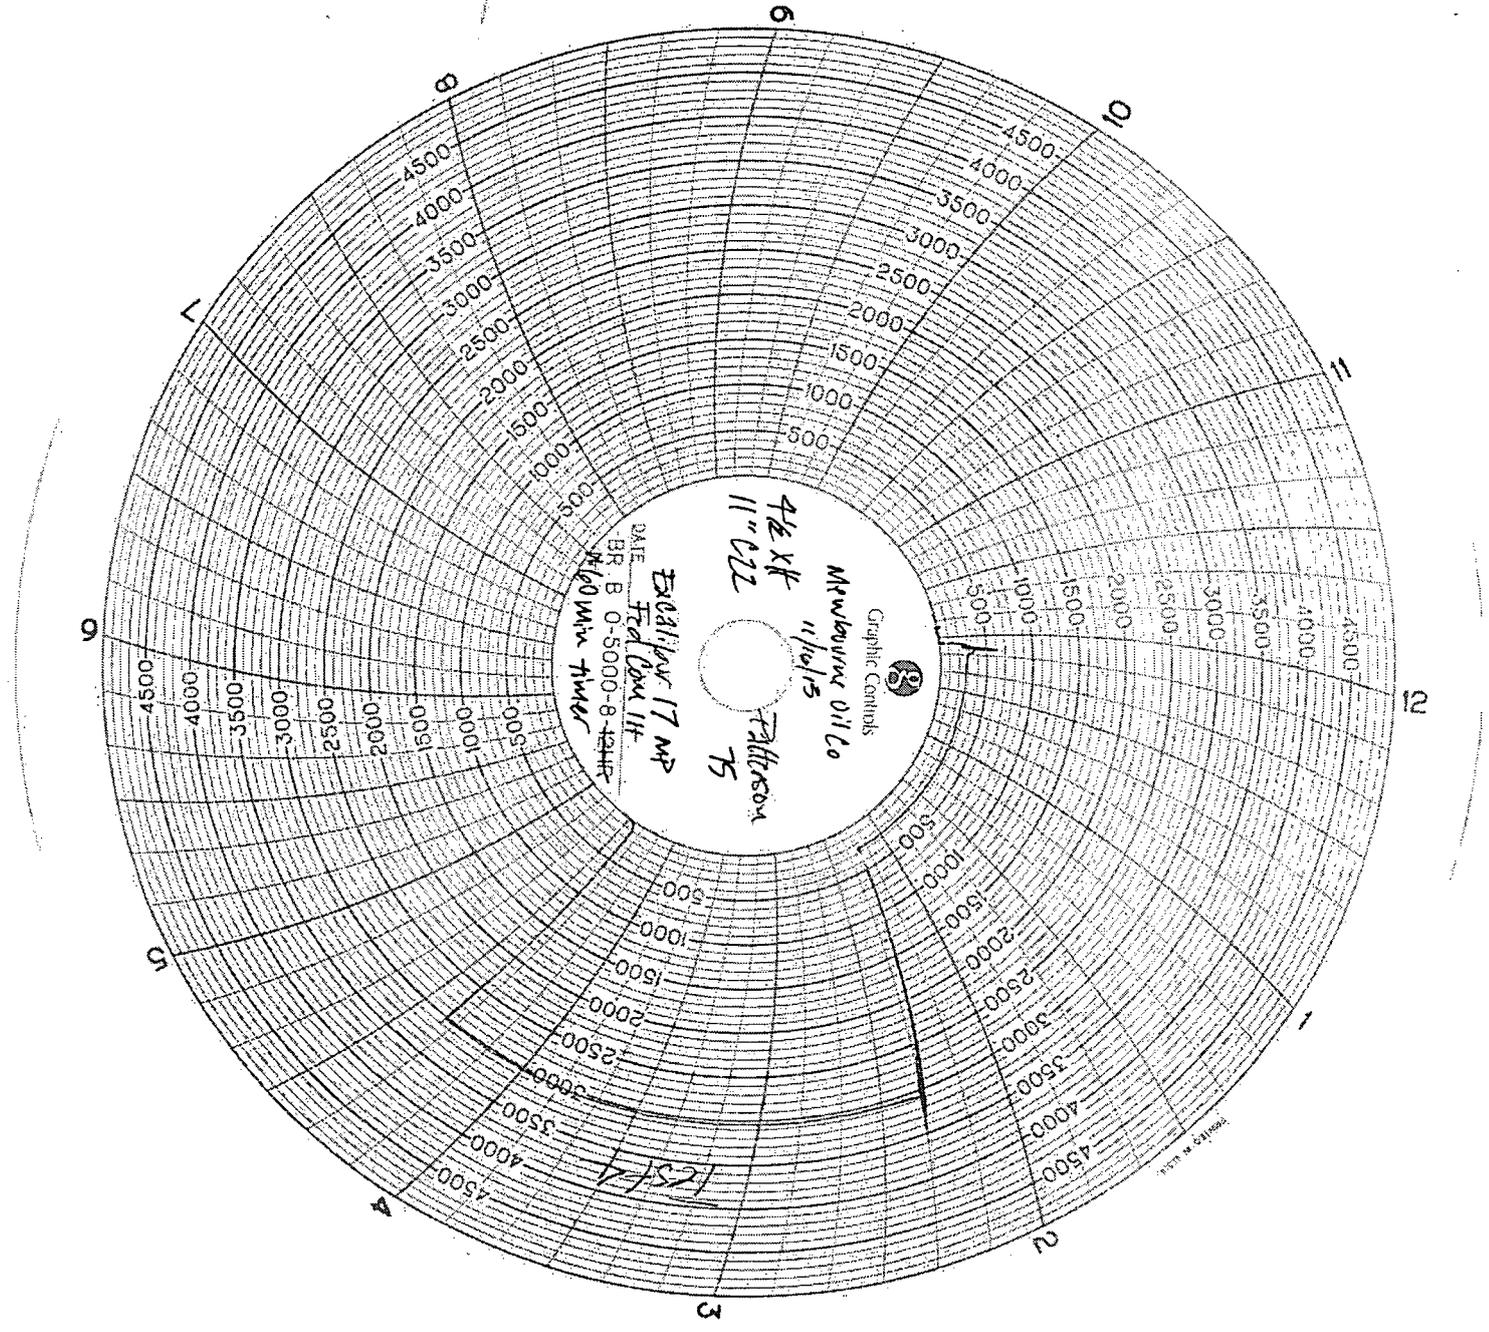

Graphic Controls

Merrimack Oil Co

11 inch C12

4 1/2 X 11 inch C12

Fallston 75

Excavator 17 MP


DATE Fed. Law 11

BR B 0-5000-8-1241R

110mm times

125/1


Reading in U.S.

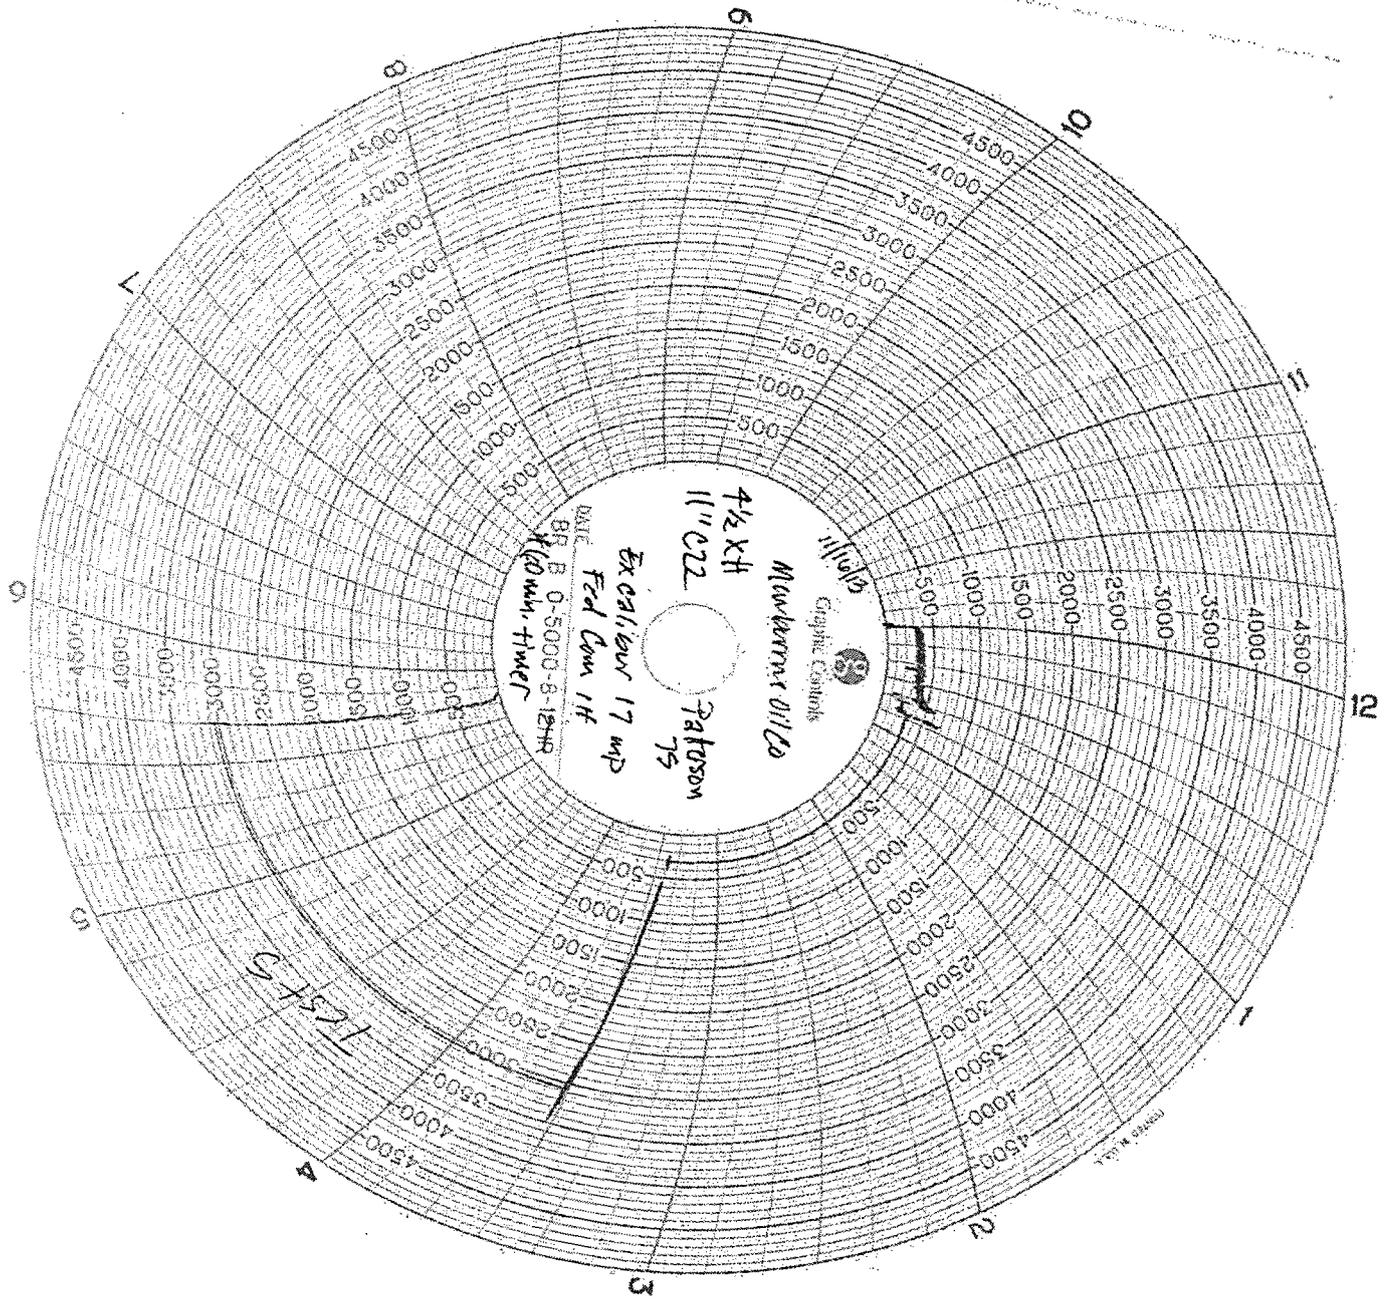

4 1/2 XH
 11" C22
 Fatsom
 75
 Maderman Oil Co
 Graphic Controls
 DATE 0-5000-8-12-48
 Ex calibur 17 mps
 Fed Com 1H
 100 m/h timer

7257 S


1948

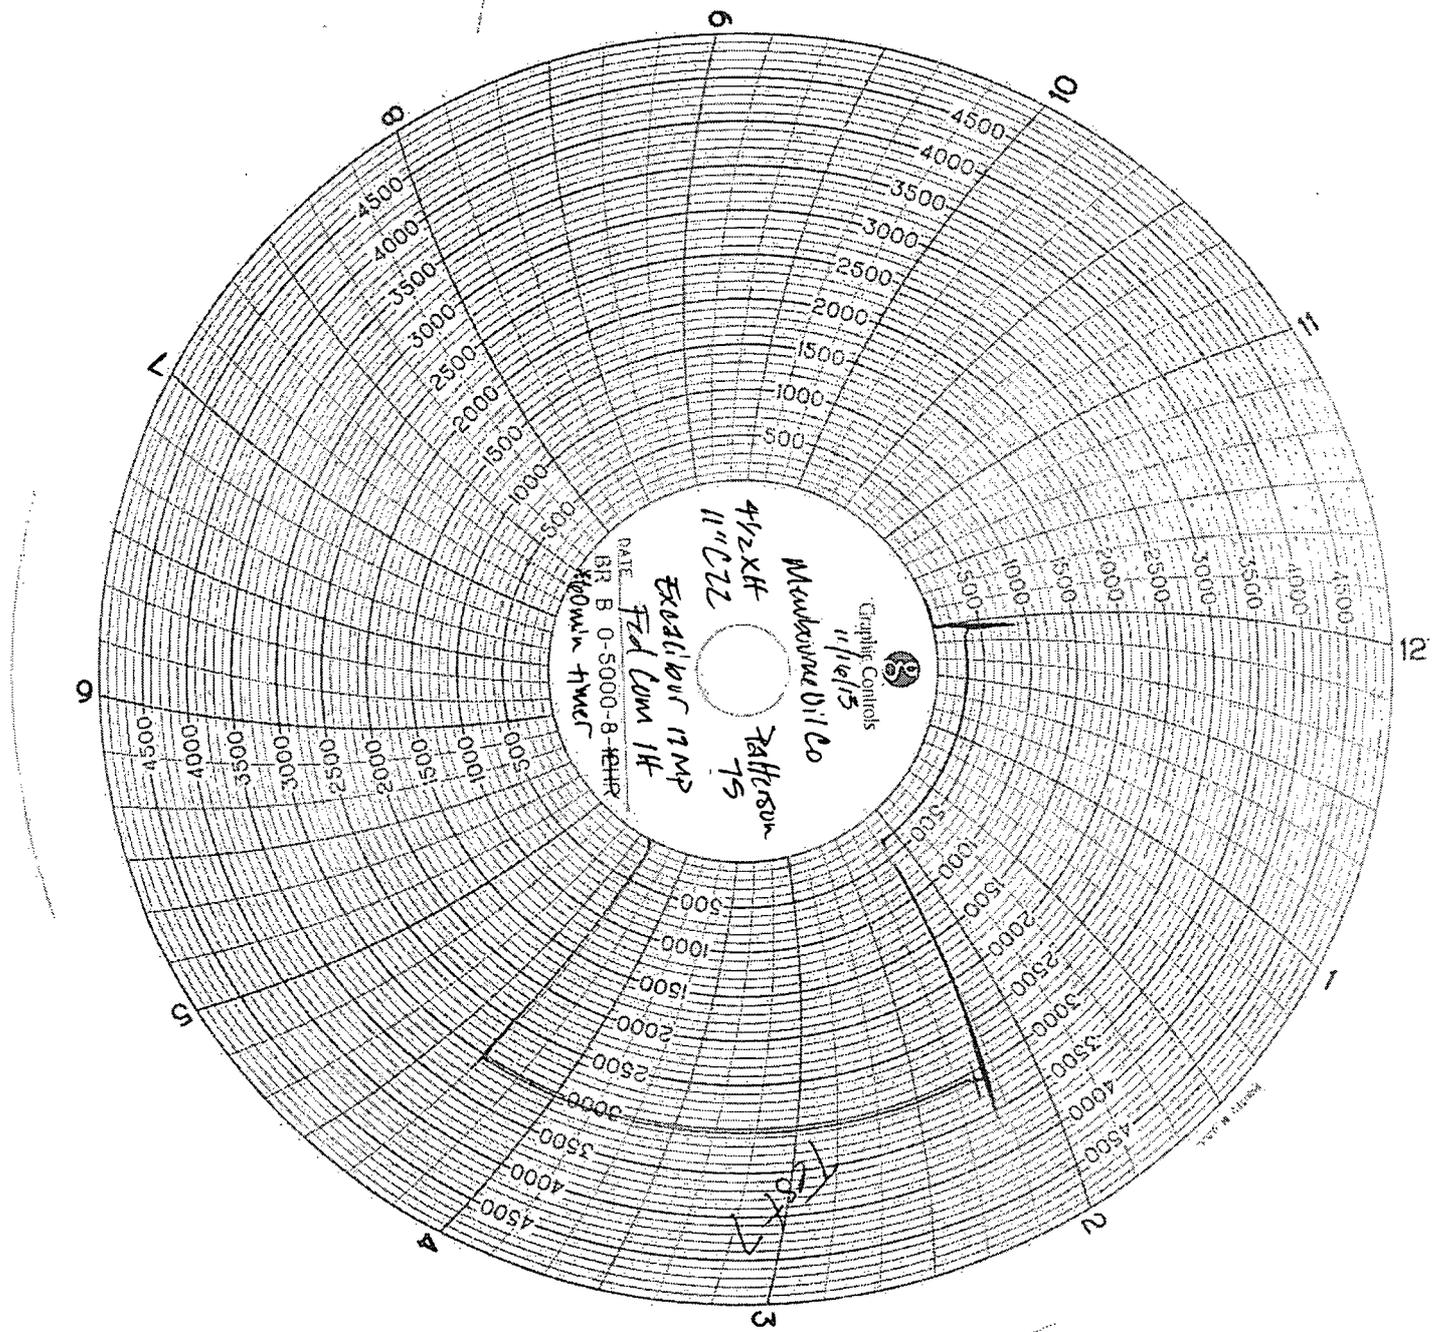

Graphic Controls
Machinist Oil Co
4 1/2 x 14
11/16/15
EXHAUST RAMP
FD LUM 14
DATE
BR B 0-5000-8-14HR
KIDWIN 4WAC

75
75

Model No. 1000

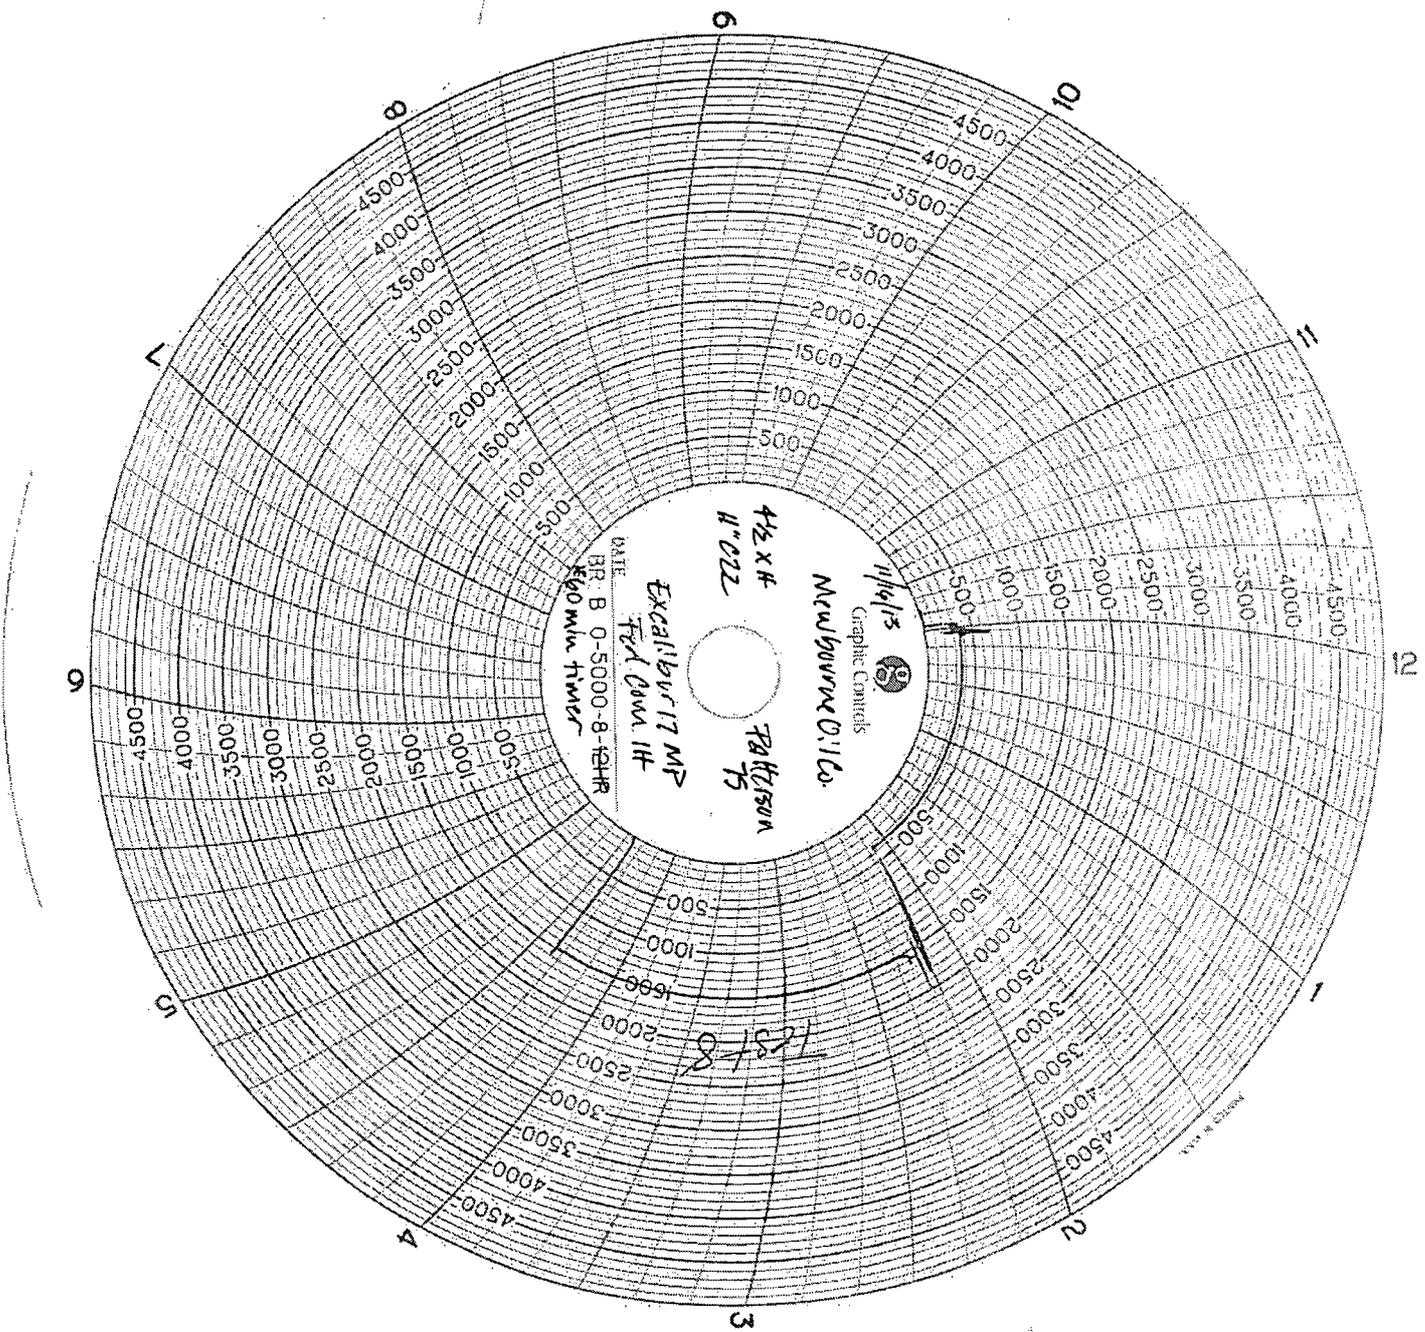

Graphic Calculators
11/6/75
McWhorter Oil Co.
4 1/2 x 4
11" O.D.
FAH/1500
75
EXCALIBUR 17 MP
FDL Osm. IH
DATE
RP: B 0-5000-8-12HR
K60 min timer

12/8/75
17 MP

McWhorter Oil Co.

MADE IN U.S.A.



Graphic Controls

11/16/13

Memboverre Oil Co

Patterson

75

4 1/2 x 4

11" CZZ

Excelsior 17 MP

Fed Com Int

DATE

BR. B 0-5000-6-12HR

#100 min. timer

7510

12

11

10

9

8

7


6


5

4

3

2

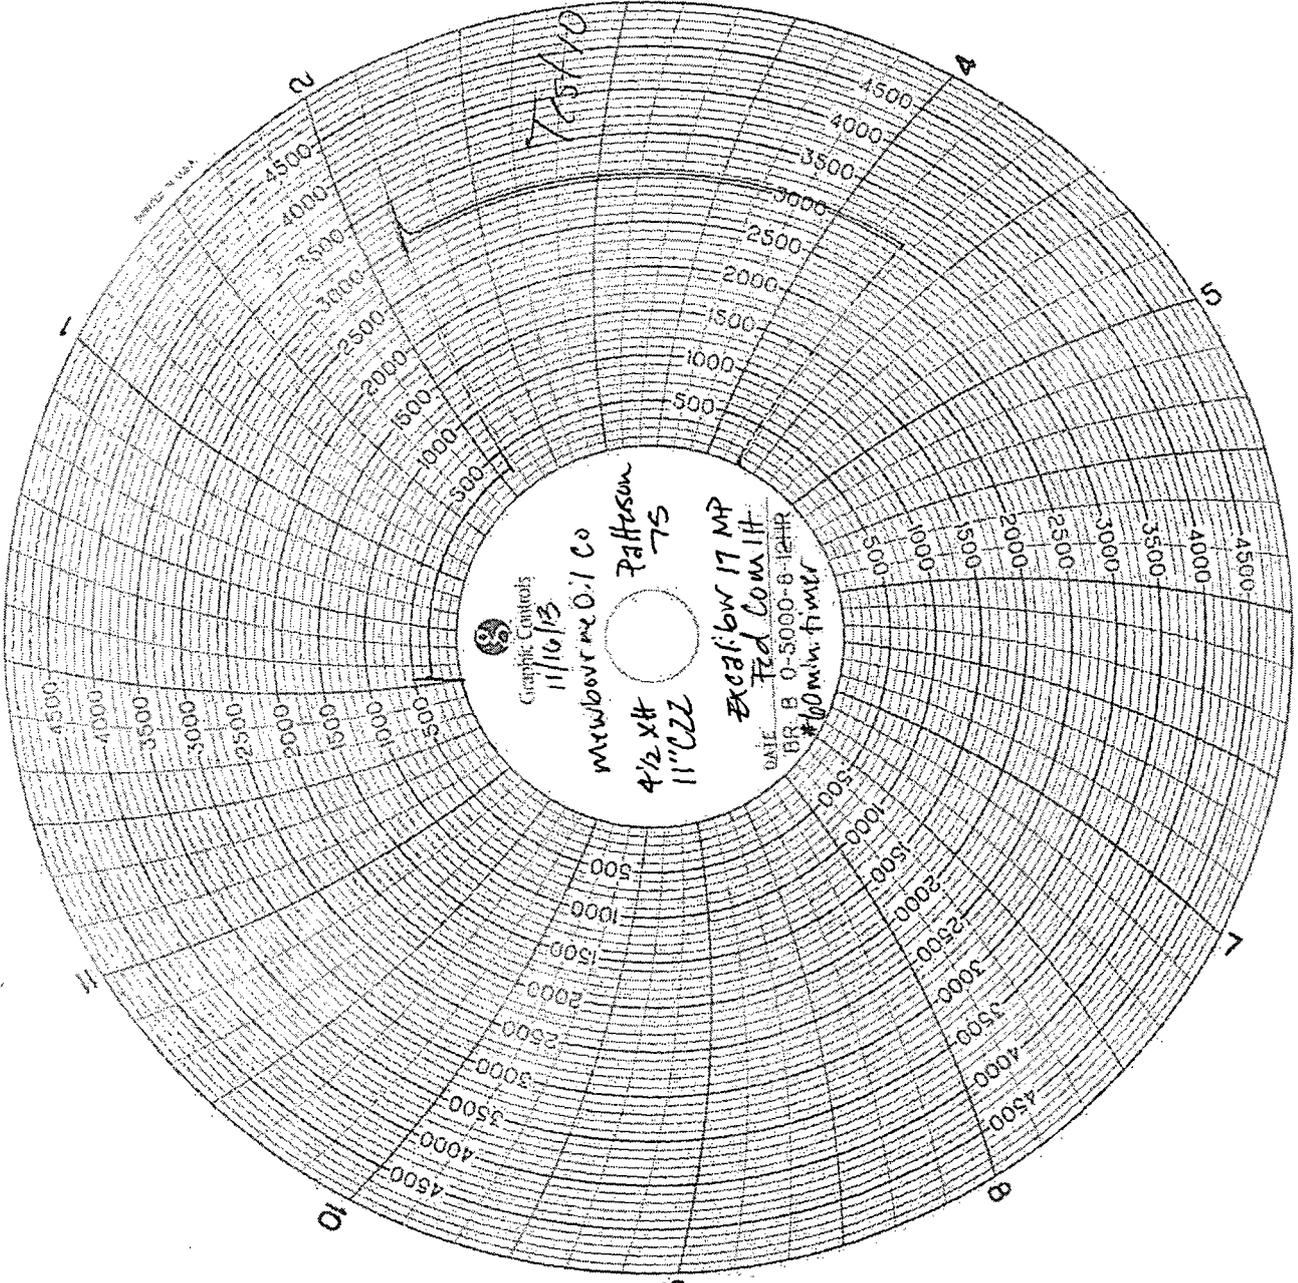

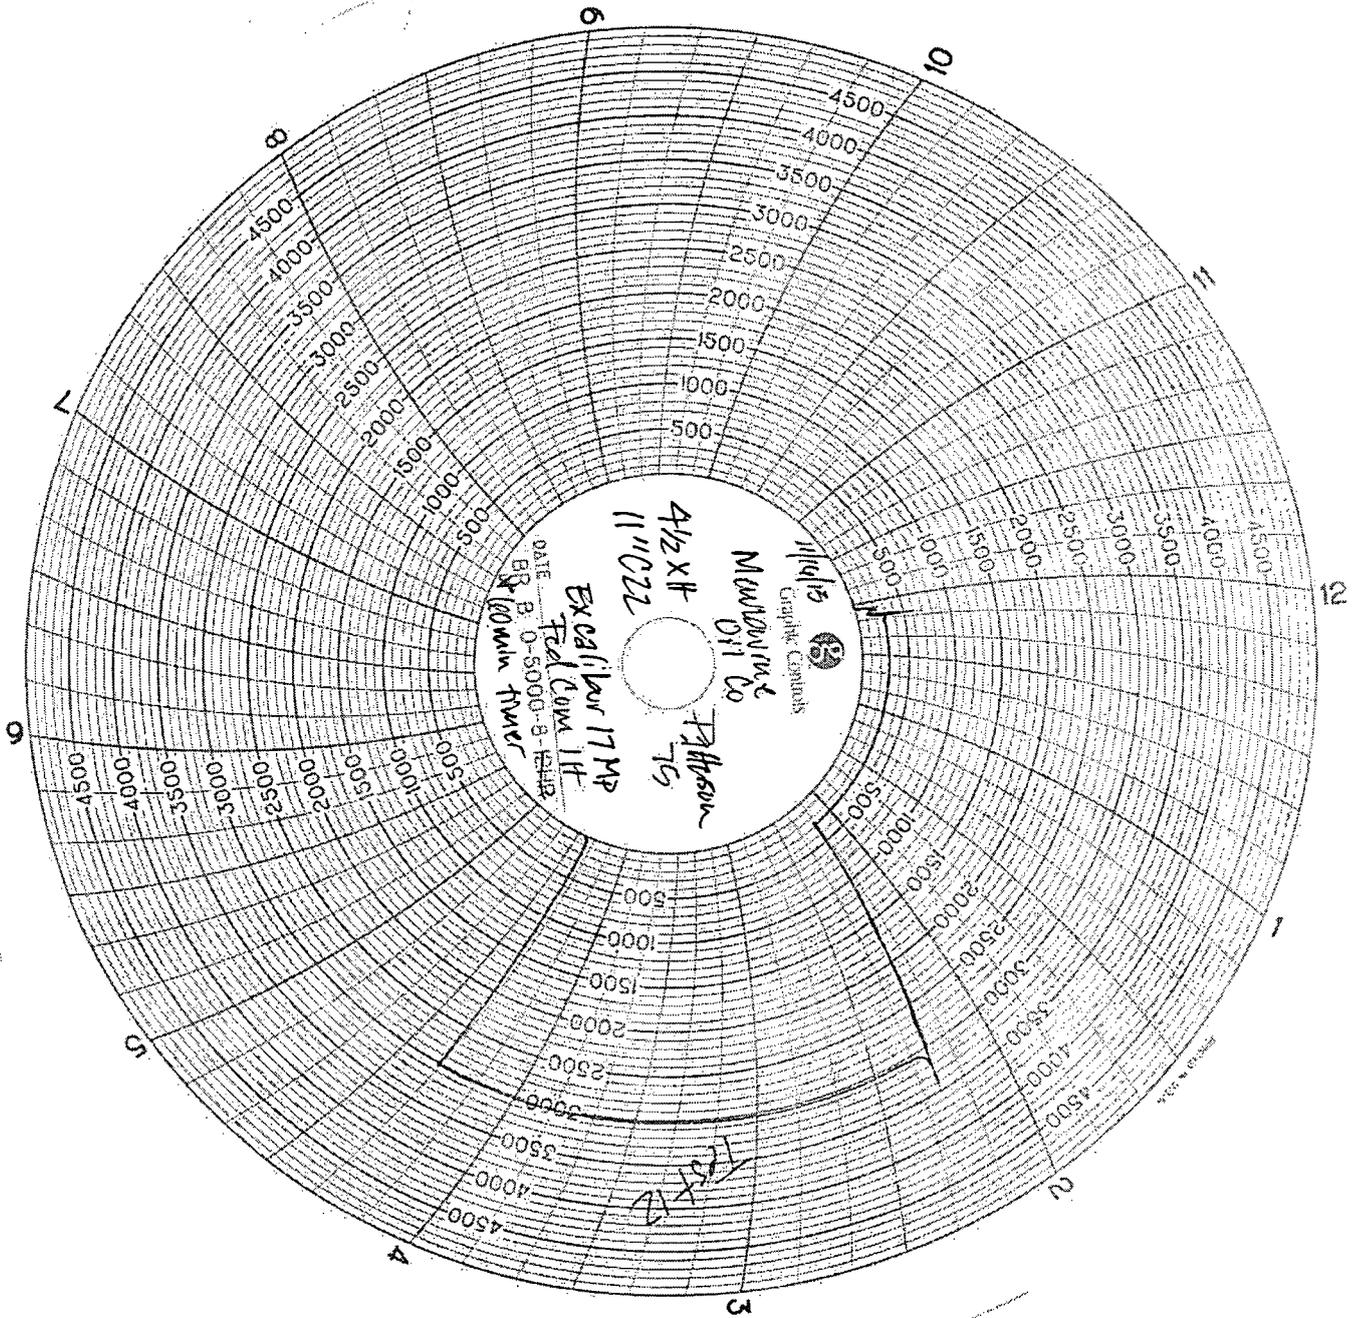

11/11/22
 12/12
