

HOBBS STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

OCD Hobbs

ATS-14-714

FORM APPROVED
OMB NO. 1004-0137
Expires October 31, 2014


APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of Work ☒ DRILL ☐ REENTER		5. Lease Serial No. NMNM19858
1b. Type of Well ☒ Oil Well ☐ Gas Well ☐ Other ☒ Single Zone ☐ Multiple Zone		6. If Indian, Allottee or Tribe Name
2. Name of Operator EOG Resources, Inc.		7. Unit or CA Agreement Name and No.
3a. Address P.O. Box 2267 Midland, TX 79702		8. Lease Name and Well No. Hawk 26 Fed 2H <314177>
3b. Phone No. (include area code) 432-686-3689		9. API Well No. 30-025-42395
4. Location of Well (Report location clearly and in accordance with any State requirements)* At surface 500 FSL & 715 FWL, SWSW (M), Sec 26, T24S, R33E At proposed prod. zone 230 FSL & 876 FWL, SWSW (M), Sec 35, T24S, R33E		10. Field and Pool, or Exploratory Red Hills; Upper BS Shale <97900>
11. Sec., T., R., M., or Blk. and Survey or Area Sec 26, T24S, R33E		
14. Distance in miles and direction from nearest town or post office* Approximately +/- 21 miles Northwest from Jal, NM		12. County or Parish Lea
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drg. unit line, if any) 10'		13. State NM
16. No. of Acres in lease 1440		17. Spacing Unit dedicated to this well 160 ac
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. 30' from 1H		20. BLM/BIA Bond No. on file NM 2308
19. Proposed Depth 14814 MD - 9494 TVD		
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 3514' GL		22. Approximate date work will start* 12/1/14
		23. Estimated duration 25 days

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, must be attached to this form:

- | | |
|--|---|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification. |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the BLM |

25. Signature 	Name (Printed/Typed) Stan Wagner	Date 4/7/14
Title Regulatory Analyst		
Approved by (Signature) 	Name (Printed/Typed) Steve Caffey	Date JAN 26 2015
Title FIELD MANAGER		
Office CARLSBAD FIELD OFFICE		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

APPROVAL FOR TWO YEARS

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)

Carlsbad Controlled Water Basin

Approval Subject to General Requirements
& Special Stipulations AttachedSEE ATTACHED FEB 3 2015
CONDITIONS OF APPROVAL

EOG RESOURCES, INC.
HAWK 26 FED NO. 2H

1. GEOLOGIC NAME OF SURFACE FORMATION:

Permian

2. ESTIMATED TOPS OF IMPORTANT GEOLOGICAL MARKERS:

Rustler	1,213'
Top of Salt	1,700'
Base of Salt / Top Anhydrite	4,955'
Base Anhydrite	5,203'
Lamar	5,203'
Bell Canyon	5,234'
Cherry Canyon	6,238'
Brushy Canyon	7,690'
Bone Spring Lime	9,220'
TD	9,494'

3. ESTIMATED DEPTHS OF ANTICIPATED FRESH WATER, OIL OR GAS:

Upper Permian Sands	0- 400'	Fresh Water
Cherry Canyon	6,238'	Oil
Brushy Canyon	7,690'	Oil
Bone Spring Lime	9,220'	Oil

No other Formations are expected to give up oil, gas or fresh water in measurable quantities.
Surface fresh water sands will be protected by setting 13.375" casing at ~~1,240'~~ and circulating cement back to surface. *1300'*

4. CASING PROGRAM - NEW

See COT

Hole Size	Interval	Csg OD	Weight	Grade	Conn	DF _{min} Collapse	DF _{min} Burst	DF _{min} Tension
17.5"	0 - 1,240'	13.375"	54.5#	J55	STC	1.125	1.25	1.60
12.25"	0-4,000'	9.625"	40#	J55	LTC	1.125	1.25	1.60
12.25"	4,000' - 5,100'	9.625"	40#	HCK55	LTC	1.125	1.25	1.60
8.75"	0'-14,814'	5.500"	17#	P110 or HCP110	LTC	1.125	1.25	1.60

EOG RESOURCES, INC.
HAWK 26 FED NO. 2H

Cementing Program:

Depth	No. Sacks	Wt. lb/gal	Yld Ft ³ /ft	Mix Water Gal/sk	Slurry Description
13-3/8" 1,240'	600	13.5	1.73	9.13	Lead: Class C + 4.0% Bentonite + 0.6% CD-32 + 0.5% CaCl ₂ + 0.25 lb/sk Cello-Flake (TOC @ surface)
	300	14.8	1.34	6.34	Tail: Class C + 0.005 pps Static Free + 2% CaCl ₂ + 0.25 pps CelloFlake + 0.005 gps FP-6L
9-5/8" 5,100'	1000	12.7	2.22	12.38	Lead: Class 'C' + 1.50% R-3 + 0.25 lb/sk Cello-Flake + 2.0% Sodium Metasilicate + 10% Salt + 0.005 lb/sk Static Free (TOC @ surface)
	200	14.8	1.32	6.33	Tail: Class 'C' + 0.25 lb/sk Cello Flake + 0.005 lb/sk Static Free
5-1/2" 14,814'	375	10.8	3.67	21.7	Lead: 60:40:0 Class 'C' + 15.00 lb/sk BA-90 + 4.00% MPA-5 + 3.00% SMS + 5.00% A-10 + 1.00% BA-10A + 0.80% ASA-301 + 2.90% R-21 + 8.00 lb/sk LCM-1 + 0.005 lb/sk Static Free (TOC @ 4600')
	400	11.8	2.38	13.25	Middle: 50:50:10 Class 'H' + 0.80% FL-52 + 0.45% ASA-301 + 0.40% SMS + 2.00% Salt + 3.00 lb/sx LCM-1 + 0.20% R-21 + 0.25 lb/sk Cello Flake + 0.005 lb/sk Static Free
	1425	14.2	1.28	5.75	Tail: 50:50:2 Class 'H' + 0.65% FL-52 + 0.20% CD-32 + 0.15% SMS + 2.00% Salt + 0.10% R-3 + 0.005 lb/sk Static Free

Note: Cement volumes based on bit size plus at least 25% excess in the open hole plus 10% excess in the cased-hole overlap section.

5. MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:

See COA

Variance is requested to use a co-flex line between the BOP and choke manifold (instead of using a 4" OD steel line).

The minimum blowout preventer equipment (BOPE) shown in Exhibit #1 will consist of a double ram-type (10,000 psi WP) preventer and an annular preventer (5000-psi WP). Both units will be hydraulically operated and the ram-type will be equipped with blind rams on bottom and drill pipe rams on top. All BOPE will be tested in accordance with Onshore Oil & Gas order No. 2.

3000 psi BOPE is adequate for this application. Due to the 3000 psi BOPE requirement no FIT tests are planned.

EOG RESOURCES, INC.
HAWK 26 FED NO. 2H

Before drilling out of the surface casing, the ram-type BOP and accessory equipment will be tested to 2000/ 250 psig and the annular preventer to 2000/ 250 psig. The surface casing will be tested to 1500 psi for 30 minutes.

Before drilling out of the intermediate casing, the ram-type BOP and accessory equipment will be tested to 3000/ 250 psig and the annular preventer to 3000/ 250 psig. The intermediate casing will be tested to 2000 psi for 30 minutes.

Pipe rams will be operationally checked each 24-hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets.

A hydraulically operated choke will be installed prior to drilling out of the intermediate casing shoe.

6. TYPES AND CHARACTERISTICS OF THE PROPOSED MUD SYSTEM:

During this procedure we plan to use a Closed-Loop System and haul contents to the required disposal.

The applicable depths and properties of the drilling fluid systems are as follows.

See COA

Depth	Type	Weight (ppg)	Viscosity	Water Loss
0 - 1,240'	Fresh Water Gel	8.6-8.8	28-34	N/c
1,240' - 5,100'	Saturated Brine	10.0-10.2	28-34	N/c
5,100' - 8,972'	Fresh Water	8.4-8.6	28-34	N/c
8,972' - 14,814'	Cut Brine Water	9.0-9.5	28-34	N/c
Lateral				

An electronic pit volume totalizer (PVT) will be utilized on the circulating system, to monitor pit volume, flow rate, pump pressure and stroke rate.

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept at the wellsite at all times.

7. AUXILIARY WELL CONTROL AND MONITORING EQUIPMENT:

(A) A kelly cock will be kept in the drill string at all times.

(B) A full opening drill pipe-stabbing valve (inside BOP) with proper drill pipe connections will be on the rig floor at all times.

See COA (C) H₂S monitoring and detection equipment will be utilized from surface casing point to TD.

EOG RESOURCES, INC.
HAWK 26 FED NO. 2H

8. LOGGING, TESTING AND CORING PROGRAM:

*See
cont*

Open-hole logs are not planned for this well.

GR-CCL Will be run in cased hole during completions phase of operations.

**9. ABNORMAL CONDITIONS, PRESSURES, TEMPERATURES AND
POTENTIAL HAZARDS:**

The estimated bottom-hole temperature (BHT) at TD is 155 degrees F with an estimated maximum bottom-hole pressure (BHP) at TD of 4111 psig. No hydrogen sulfide or other hazardous gases or fluids have been encountered, reported or are known to exist at this depth in this area. No major loss circulation zones have been reported in offsetting wells.

10. ANTICIPATED STARTING DATE AND DURATION OF OPERATIONS:


The drilling operation should be finished in approximately one month. If the well is productive, an additional 60-90 days will be required for completion and testing before a decision is made to install permanent facilities.

Hawk 26 Fed #2H
Lea County, New Mexico
Proposed Wellbore

500' FSL
715' FWL
Section 26
T-24-S, R-33-E

API: 30-025-*****

KB: 3,544'
GL: 3,514'

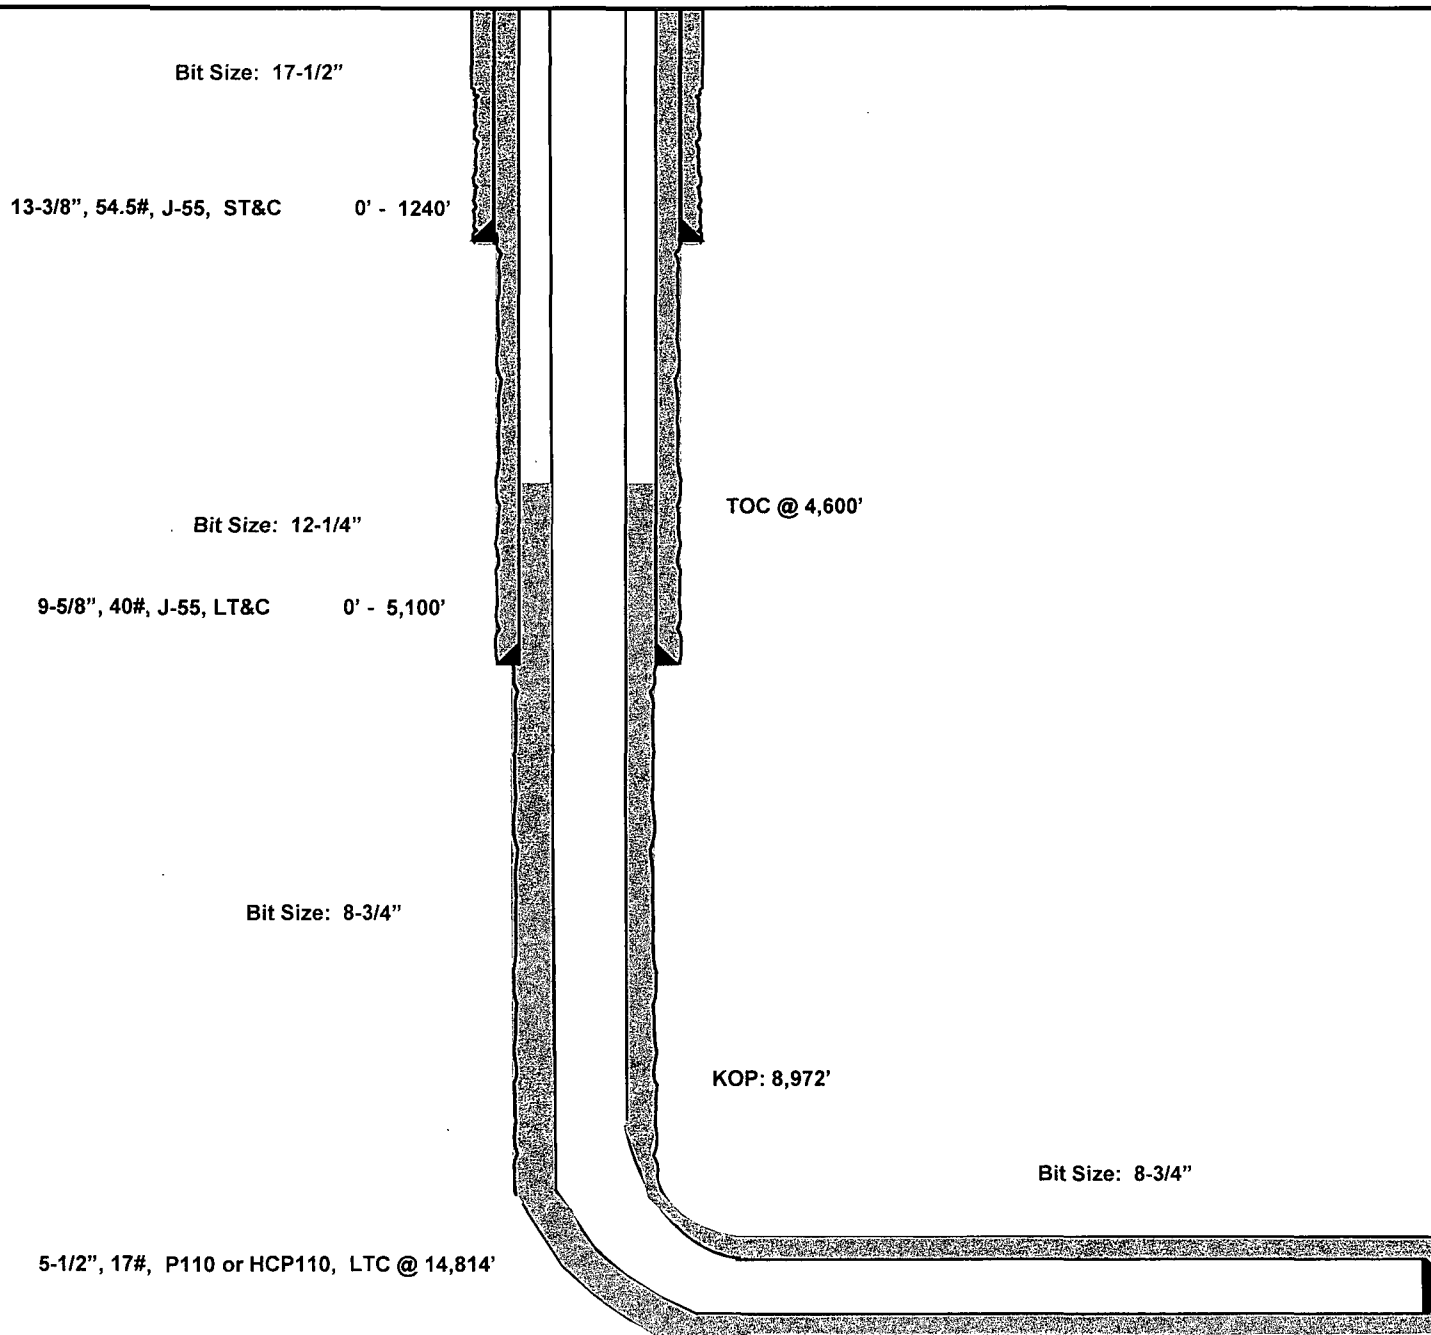

Lateral:
14,814' MD, 9,494' TVD
Upper Most Perf:
10' FNL & 884' FWL
Lower Most Perf:
330' FSL & 876' FWL
BH Location: 230' FSL & 876' FWL
Section 35
T-24-S, R-33-E



Lea County, NM

Hawk 26 Fed #2H

GL 3514' + Cactus 123 KB

Plan #1

PROJECT DETAILS: Lea County, NM

Geodetic System: US State Plane 1927 (Exact solution)
Datum: NAD 1927 (NADCON CONUS)
Ellipsoid: Clarke 1866
Zone: New Mexico East 3001
System Datum: Mean Sea Level

WELL DETAILS: Hawk 26 Fed #2H







Ground Level: 3514.00
Northing 431034.00 Easting 742897.00 Latitude 32° 10' 57.348 N Longitude 103° 32' 55.963 W

SECTION DETAILS

Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	Vsect	Target	Annotation
1	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		
2	8972.55	0.00	0.00	8972.55	0.00	0.00	0.00	0.00	0.00		
3	9718.38	89.50	185.85	9450.00	-458.94	115.70	12.00	165.85	462.91		KOP, Build @ 12° DLS
4	10176.69	89.50	179.80	9454.01	-912.45	173.60	3.00	96.06	918.26		LP, Turn @ 3° DLS
5	14814.53	89.50	179.60	9494.42	-5550.00	206.00	0.00	5553.82			Hold 89.50° Inc; 179.60° AZI; TD 14814.53' MD; 9494.42' TVD

WELLBORE TARGET DETAILS (MAP CO-ORDINATES)

Name	TVD	+N/-S	+E/-W	Northing	Easting	Shape
U Perf - Hawk 26 Fed #2H	9450.45	-509.00	171.00	430525.00	742868.00	Point
L Perf - Hawk 26 Fed #2H	9453.55	-5450.00	205.00	425584.00	742902.00	Point
BHL - Hawk 26 Fed #2H	9494.42	-5550.00	206.00	425484.00	742903.00	Point

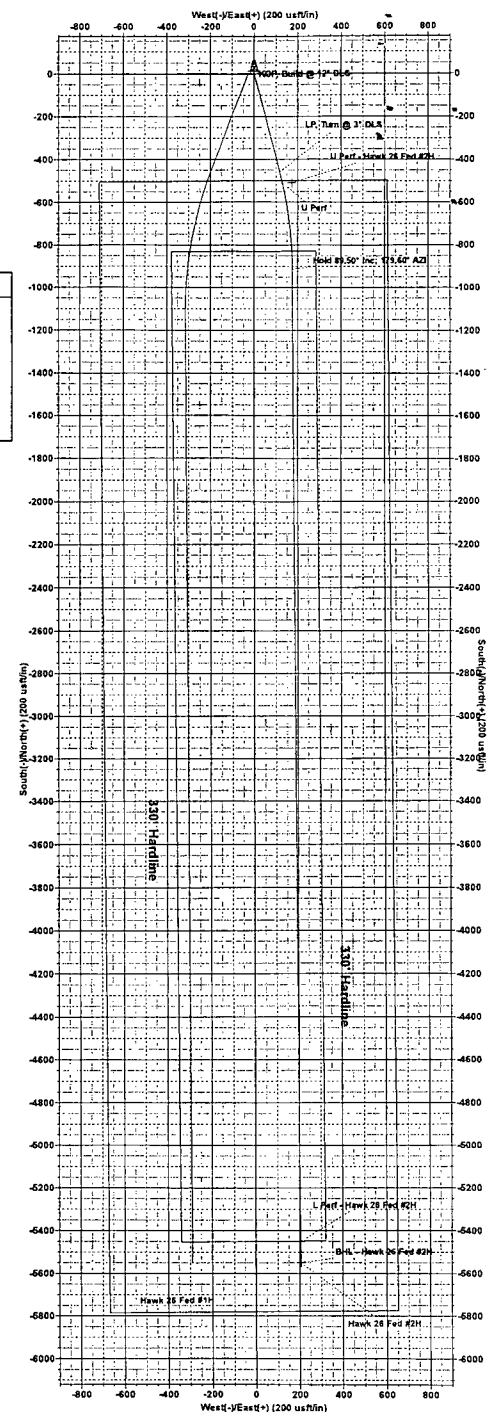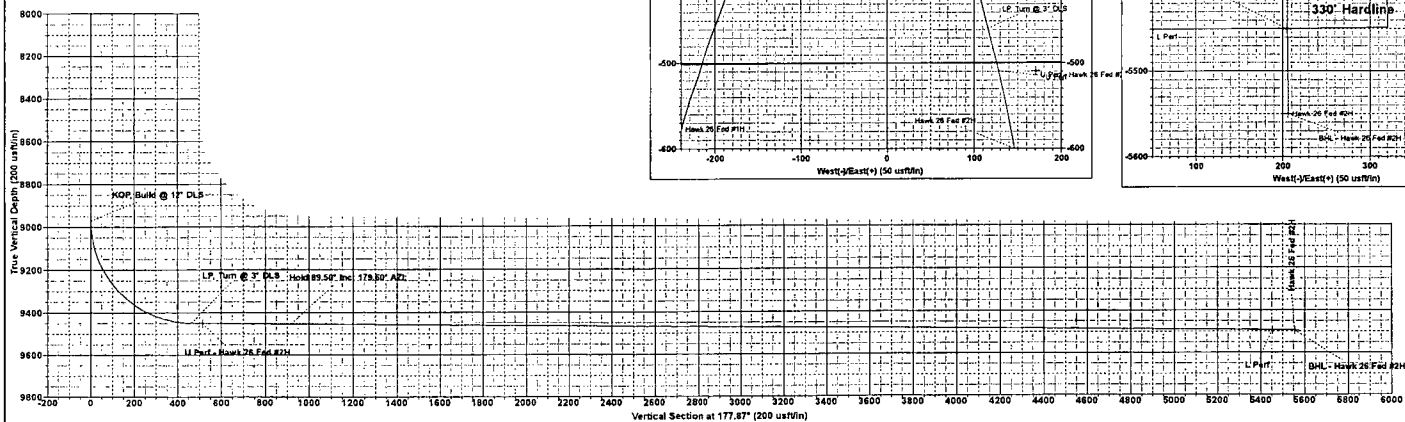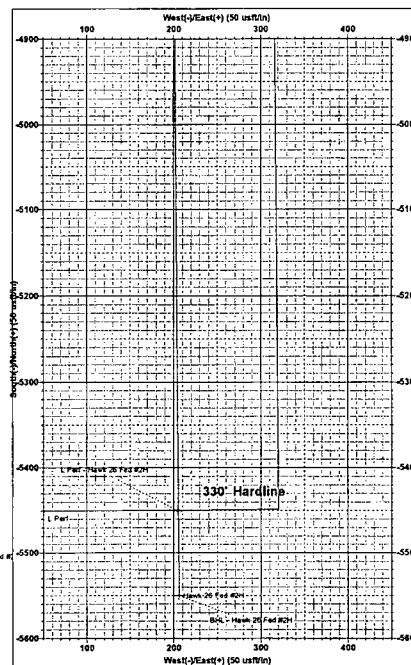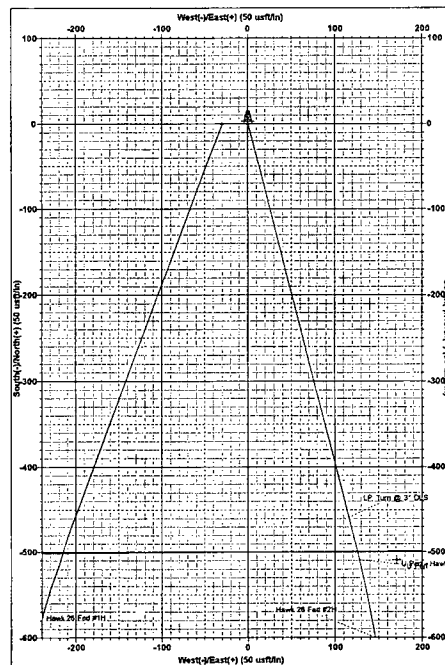



EOG Resources - Midland

Lea County, NM

Hawk 26 Fed

Hawk 26 Fed #2H

OH

Plan: Plan #1

Standard Survey Report

20 March, 2014



EOG Resources, Inc.

Survey Report

Company: EOG Resources - Midland
 Project: Lea County, NM
 Site: Hawk 26 Fed
 Well: Hawk 26 Fed #2H
 Wellbore: OH
 Design: Plan #1

Local Co-ordinate Reference: Well Hawk 26 Fed #2H
 TVD Reference: WELL @ 3544.00usft (GL 3514' + Cactus 123 KB)
 MD Reference: WELL @ 3544.00usft (GL 3514' + Cactus 123 KB)
 North Reference: Grid
 Survey Calculation Method: Minimum Curvature
 Database: EDM 5000.1 Single User Db

Project	Lea County, NM		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Site	Hawk 26 Fed		
Site Position:		Northing:	431,034.00 usft
From:	Map	Easting:	742,667.00 usft
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16 "
		Latitude:	32° 10' 57.351 N
		Longitude:	103° 32' 56.312 W
		Grid Convergence:	0.42 °

Well	Hawk 26 Fed #2H		
Well Position	+N/-S	0.00 usft	Northing:
	+E/-W	0.00 usft	Easting:
Position Uncertainty	0.00 usft	Wellhead Elevation:	usft
		Latitude:	32° 10' 57.348 N
		Longitude:	103° 32' 55.963 W
		Ground Level:	3,514.00 usft

Wellbore	OH		
Magnetics	Model Name	Sample Date	Declination
	IGRF2010	3/19/2014	(°)
			Dip Angle
			(°)
			Field Strength
			(nT)
			7.23
			60.08
			48,317

Design	Plan #1		
Audit Notes:			
Version:	Phase:	PLAN	Tie On Depth:
			0.00
Vertical Section:	Depth From (TVD)	+N/-S	+E/-W
	(usft)	(usft)	(usft)
	0.00	0.00	0.00
			Direction
			(°)
			177.87

Survey Tool Program	Date 3/20/2014		
From	To	Survey (Wellbore)	Tool Name
(usft)	(usft)		
0.00	14,811.87	Plan #1 (OH)	MWD
			Description
			MWD - Standard

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
100.00	0.00	0.00	100.00	0.00	0.00	0.00	0.00	0.00	0.00	
200.00	0.00	0.00	200.00	0.00	0.00	0.00	0.00	0.00	0.00	
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00	
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00	0.00	
500.00	0.00	0.00	500.00	0.00	0.00	0.00	0.00	0.00	0.00	
600.00	0.00	0.00	600.00	0.00	0.00	0.00	0.00	0.00	0.00	
700.00	0.00	0.00	700.00	0.00	0.00	0.00	0.00	0.00	0.00	
800.00	0.00	0.00	800.00	0.00	0.00	0.00	0.00	0.00	0.00	



EOG Resources, Inc.

Survey Report

Company: EOG Resources - Midland
Project: Lea County, NM
Site: Hawk 26 Fed
Well: Hawk 26 Fed #2H
Wellbore: OH
Design: Plan #1

Local Co-ordinate Reference: Well Hawk 26 Fed #2H
TVD Reference: WELL @ 3544.00usft (GL 3514' + Cactus 123 KB)
MD Reference: WELL @ 3544.00usft (GL 3514' + Cactus 123 KB)
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: EDM 5000.1 Single User Db

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
900.00	0.00	0.00	900.00	0.00	0.00	0.00	0.00	0.00	0.00
1,000.00	0.00	0.00	1,000.00	0.00	0.00	0.00	0.00	0.00	0.00
1,100.00	0.00	0.00	1,100.00	0.00	0.00	0.00	0.00	0.00	0.00
1,200.00	0.00	0.00	1,200.00	0.00	0.00	0.00	0.00	0.00	0.00
1,300.00	0.00	0.00	1,300.00	0.00	0.00	0.00	0.00	0.00	0.00
1,400.00	0.00	0.00	1,400.00	0.00	0.00	0.00	0.00	0.00	0.00
1,500.00	0.00	0.00	1,500.00	0.00	0.00	0.00	0.00	0.00	0.00
1,600.00	0.00	0.00	1,600.00	0.00	0.00	0.00	0.00	0.00	0.00
1,700.00	0.00	0.00	1,700.00	0.00	0.00	0.00	0.00	0.00	0.00
1,800.00	0.00	0.00	1,800.00	0.00	0.00	0.00	0.00	0.00	0.00
1,900.00	0.00	0.00	1,900.00	0.00	0.00	0.00	0.00	0.00	0.00
2,000.00	0.00	0.00	2,000.00	0.00	0.00	0.00	0.00	0.00	0.00
2,100.00	0.00	0.00	2,100.00	0.00	0.00	0.00	0.00	0.00	0.00
2,200.00	0.00	0.00	2,200.00	0.00	0.00	0.00	0.00	0.00	0.00
2,300.00	0.00	0.00	2,300.00	0.00	0.00	0.00	0.00	0.00	0.00
2,400.00	0.00	0.00	2,400.00	0.00	0.00	0.00	0.00	0.00	0.00
2,500.00	0.00	0.00	2,500.00	0.00	0.00	0.00	0.00	0.00	0.00
2,600.00	0.00	0.00	2,600.00	0.00	0.00	0.00	0.00	0.00	0.00
2,700.00	0.00	0.00	2,700.00	0.00	0.00	0.00	0.00	0.00	0.00
2,800.00	0.00	0.00	2,800.00	0.00	0.00	0.00	0.00	0.00	0.00
2,900.00	0.00	0.00	2,900.00	0.00	0.00	0.00	0.00	0.00	0.00
3,000.00	0.00	0.00	3,000.00	0.00	0.00	0.00	0.00	0.00	0.00
3,100.00	0.00	0.00	3,100.00	0.00	0.00	0.00	0.00	0.00	0.00
3,200.00	0.00	0.00	3,200.00	0.00	0.00	0.00	0.00	0.00	0.00
3,300.00	0.00	0.00	3,300.00	0.00	0.00	0.00	0.00	0.00	0.00
3,400.00	0.00	0.00	3,400.00	0.00	0.00	0.00	0.00	0.00	0.00
3,500.00	0.00	0.00	3,500.00	0.00	0.00	0.00	0.00	0.00	0.00
3,600.00	0.00	0.00	3,600.00	0.00	0.00	0.00	0.00	0.00	0.00
3,700.00	0.00	0.00	3,700.00	0.00	0.00	0.00	0.00	0.00	0.00
3,800.00	0.00	0.00	3,800.00	0.00	0.00	0.00	0.00	0.00	0.00
3,900.00	0.00	0.00	3,900.00	0.00	0.00	0.00	0.00	0.00	0.00
4,000.00	0.00	0.00	4,000.00	0.00	0.00	0.00	0.00	0.00	0.00
4,100.00	0.00	0.00	4,100.00	0.00	0.00	0.00	0.00	0.00	0.00
4,200.00	0.00	0.00	4,200.00	0.00	0.00	0.00	0.00	0.00	0.00
4,300.00	0.00	0.00	4,300.00	0.00	0.00	0.00	0.00	0.00	0.00
4,400.00	0.00	0.00	4,400.00	0.00	0.00	0.00	0.00	0.00	0.00
4,500.00	0.00	0.00	4,500.00	0.00	0.00	0.00	0.00	0.00	0.00
4,600.00	0.00	0.00	4,600.00	0.00	0.00	0.00	0.00	0.00	0.00
4,700.00	0.00	0.00	4,700.00	0.00	0.00	0.00	0.00	0.00	0.00
4,800.00	0.00	0.00	4,800.00	0.00	0.00	0.00	0.00	0.00	0.00
4,900.00	0.00	0.00	4,900.00	0.00	0.00	0.00	0.00	0.00	0.00
5,000.00	0.00	0.00	5,000.00	0.00	0.00	0.00	0.00	0.00	0.00



EOG Resources, Inc.

Survey Report

Company: EOG Resources - Midland
Project: Lea County, NM
Site: Hawk 26 Fed
Well: Hawk 26 Fed #2H
Wellbore: OH
Design: Plan #1

Local Co-ordinate Reference: Well Hawk 26 Fed #2H
TVD Reference: WELL @ 3544.00usft (GL 3514' + Cactus 123 KB)
MD Reference: WELL @ 3544.00usft (GL 3514' + Cactus 123 KB)
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: EDM 5000.1 Single User Db

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
5,100.00	0.00	0.00	5,100.00	0.00	0.00	0.00	0.00	0.00	0.00
5,200.00	0.00	0.00	5,200.00	0.00	0.00	0.00	0.00	0.00	0.00
5,300.00	0.00	0.00	5,300.00	0.00	0.00	0.00	0.00	0.00	0.00
5,400.00	0.00	0.00	5,400.00	0.00	0.00	0.00	0.00	0.00	0.00
5,500.00	0.00	0.00	5,500.00	0.00	0.00	0.00	0.00	0.00	0.00
5,600.00	0.00	0.00	5,600.00	0.00	0.00	0.00	0.00	0.00	0.00
5,700.00	0.00	0.00	5,700.00	0.00	0.00	0.00	0.00	0.00	0.00
5,800.00	0.00	0.00	5,800.00	0.00	0.00	0.00	0.00	0.00	0.00
5,900.00	0.00	0.00	5,900.00	0.00	0.00	0.00	0.00	0.00	0.00
6,000.00	0.00	0.00	6,000.00	0.00	0.00	0.00	0.00	0.00	0.00
6,100.00	0.00	0.00	6,100.00	0.00	0.00	0.00	0.00	0.00	0.00
6,200.00	0.00	0.00	6,200.00	0.00	0.00	0.00	0.00	0.00	0.00
6,300.00	0.00	0.00	6,300.00	0.00	0.00	0.00	0.00	0.00	0.00
6,400.00	0.00	0.00	6,400.00	0.00	0.00	0.00	0.00	0.00	0.00
6,500.00	0.00	0.00	6,500.00	0.00	0.00	0.00	0.00	0.00	0.00
6,600.00	0.00	0.00	6,600.00	0.00	0.00	0.00	0.00	0.00	0.00
6,700.00	0.00	0.00	6,700.00	0.00	0.00	0.00	0.00	0.00	0.00
6,800.00	0.00	0.00	6,800.00	0.00	0.00	0.00	0.00	0.00	0.00
6,900.00	0.00	0.00	6,900.00	0.00	0.00	0.00	0.00	0.00	0.00
7,000.00	0.00	0.00	7,000.00	0.00	0.00	0.00	0.00	0.00	0.00
7,100.00	0.00	0.00	7,100.00	0.00	0.00	0.00	0.00	0.00	0.00
7,200.00	0.00	0.00	7,200.00	0.00	0.00	0.00	0.00	0.00	0.00
7,300.00	0.00	0.00	7,300.00	0.00	0.00	0.00	0.00	0.00	0.00
7,400.00	0.00	0.00	7,400.00	0.00	0.00	0.00	0.00	0.00	0.00
7,500.00	0.00	0.00	7,500.00	0.00	0.00	0.00	0.00	0.00	0.00
7,600.00	0.00	0.00	7,600.00	0.00	0.00	0.00	0.00	0.00	0.00
7,700.00	0.00	0.00	7,700.00	0.00	0.00	0.00	0.00	0.00	0.00
7,800.00	0.00	0.00	7,800.00	0.00	0.00	0.00	0.00	0.00	0.00
7,900.00	0.00	0.00	7,900.00	0.00	0.00	0.00	0.00	0.00	0.00
8,000.00	0.00	0.00	8,000.00	0.00	0.00	0.00	0.00	0.00	0.00
8,100.00	0.00	0.00	8,100.00	0.00	0.00	0.00	0.00	0.00	0.00
8,200.00	0.00	0.00	8,200.00	0.00	0.00	0.00	0.00	0.00	0.00
8,300.00	0.00	0.00	8,300.00	0.00	0.00	0.00	0.00	0.00	0.00
8,400.00	0.00	0.00	8,400.00	0.00	0.00	0.00	0.00	0.00	0.00
8,500.00	0.00	0.00	8,500.00	0.00	0.00	0.00	0.00	0.00	0.00
8,600.00	0.00	0.00	8,600.00	0.00	0.00	0.00	0.00	0.00	0.00
8,700.00	0.00	0.00	8,700.00	0.00	0.00	0.00	0.00	0.00	0.00
8,800.00	0.00	0.00	8,800.00	0.00	0.00	0.00	0.00	0.00	0.00
8,900.00	0.00	0.00	8,900.00	0.00	0.00	0.00	0.00	0.00	0.00
8,972.55	0.00	0.00	8,972.55	0.00	0.00	0.00	0.00	0.00	0.00
KOP, Build @ 12° DLS									
8,975.00	0.29	165.85	8,975.00	-0.01	0.00	0.01	12.00	12.00	0.00



EOG Resources, Inc.

Survey Report

Company: EOG Resources - Midland
 Project: Lea County, NM
 Site: Hawk 26 Fed
 Well: Hawk 26 Fed #2H
 Wellbore: OH
 Design: Plan #1

Local Co-ordinate Reference: Well Hawk 26 Fed #2H
 TVD Reference: WELL @ 3544.00usft (GL 3514' + Cactus 123 KB)
 MD Reference: WELL @ 3544.00usft (GL 3514' + Cactus 123 KB)
 North Reference: Grid
 Survey Calculation Method: Minimum Curvature
 Database: EDM 5000.1 Single User Db

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
9,000.00	3.29	165.85	8,999.99	-0.76	0.19	0.77	12.00	12.00	0.00
9,025.00	6.29	165.85	9,024.89	-2.79	0.70	2.81	12.00	12.00	0.00
9,050.00	9.29	165.85	9,049.66	-6.08	1.53	6.13	12.00	12.00	0.00
9,075.00	12.29	165.85	9,074.22	-10.62	2.68	10.71	12.00	12.00	0.00
9,100.00	15.29	165.85	9,098.49	-16.40	4.13	16.54	12.00	12.00	0.00
9,125.00	18.29	165.85	9,122.42	-23.40	5.90	23.60	12.00	12.00	0.00
9,150.00	21.29	165.85	9,145.94	-31.61	7.97	31.88	12.00	12.00	0.00
9,175.00	24.29	165.85	9,168.99	-41.00	10.34	41.35	12.00	12.00	0.00
9,200.00	27.29	165.85	9,191.49	-51.55	13.00	51.99	12.00	12.00	0.00
9,225.00	30.29	165.85	9,213.40	-63.22	15.94	63.77	12.00	12.00	0.00
9,250.00	33.29	165.85	9,234.65	-75.99	19.16	76.65	12.00	12.00	0.00
9,275.00	36.29	165.85	9,255.18	-89.82	22.65	90.60	12.00	12.00	0.00
9,300.00	39.29	165.85	9,274.93	-104.68	26.39	105.58	12.00	12.00	0.00
9,325.00	42.29	165.85	9,293.85	-120.51	30.38	121.56	12.00	12.00	0.00
9,350.00	45.29	165.85	9,311.90	-137.29	34.61	138.48	12.00	12.00	0.00
9,375.00	48.29	165.85	9,329.01	-154.95	39.07	156.30	12.00	12.00	0.00
9,400.00	51.29	165.85	9,345.15	-173.47	43.73	174.97	12.00	12.00	0.00
9,425.00	54.29	165.85	9,360.26	-192.77	48.60	194.44	12.00	12.00	0.00
9,450.00	57.29	165.85	9,374.31	-212.82	53.65	214.66	12.00	12.00	0.00
9,475.00	60.29	165.85	9,387.27	-233.55	58.88	235.57	12.00	12.00	0.00
9,500.00	63.29	165.85	9,399.08	-254.91	64.27	257.12	12.00	12.00	0.00
9,525.00	66.29	165.85	9,409.73	-276.84	69.79	279.24	12.00	12.00	0.00
9,550.00	69.29	165.85	9,419.17	-299.28	75.45	301.87	12.00	12.00	0.00
9,575.00	72.29	165.85	9,427.40	-322.17	81.22	324.96	12.00	12.00	0.00
9,600.00	75.29	165.85	9,434.37	-345.45	87.09	348.44	12.00	12.00	0.00
9,625.00	78.29	165.85	9,440.08	-369.04	93.04	372.24	12.00	12.00	0.00
9,650.00	81.29	165.85	9,444.51	-392.90	99.05	396.30	12.00	12.00	0.00
9,675.00	84.29	165.85	9,447.65	-416.95	105.12	420.56	12.00	12.00	0.00
9,700.00	87.29	165.85	9,449.48	-441.12	111.21	444.94	12.00	12.00	0.00
9,718.38	89.50	165.85	9,450.00	-458.94	115.70	462.91	12.00	12.00	0.00
LP, Turn @ 3° DLS									
9,769.85	89.50	167.39	9,450.45	-509.00	127.61	513.39	3.00	0.00	3.00
U Perf									
9,800.00	89.50	168.30	9,450.71	-538.48	133.96	543.08	3.00	0.00	3.00
9,900.00	89.50	171.30	9,451.59	-636.88	151.67	642.07	3.00	0.00	3.00
10,000.00	89.50	174.30	9,452.47	-736.08	164.20	741.66	3.00	0.00	3.00
10,100.00	89.50	177.30	9,453.34	-835.79	171.52	841.58	3.00	0.00	3.00
10,176.69	89.50	179.60	9,454.01	-912.45	173.60	918.26	3.00	0.00	3.00
Hold 89.50° Inc; 179.60° AZI;									
10,200.00	89.50	179.60	9,454.22	-935.76	173.76	941.56	0.00	0.00	0.00
10,300.00	89.50	179.60	9,455.09	-1,035.75	174.46	1,041.51	0.00	0.00	0.00
10,400.00	89.50	179.60	9,455.96	-1,135.74	175.16	1,141.46	0.00	0.00	0.00



EOG Resources, Inc.

Survey Report

Company: EOG Resources - Midland
Project: Lea County, NM

Site: Hawk 26 Fed

Well: Hawk 26 Fed #2H

Wellbore: OH

Design: Plan #1

Local Co-ordinate Reference: Well Hawk 26 Fed #2H
TVD Reference: WELL @ 3544.00usft (GL 3514' + Cactus 123 KB)
MD Reference: WELL @ 3544.00usft (GL 3514' + Cactus 123 KB)
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: EDM 5000.1 Single User Db

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
10,500.00	89.50	179.60	9,456.83	-1,235.74	175.86	1,241.41	0.00	0.00	0.00
10,600.00	89.50	179.60	9,457.70	-1,335.73	176.56	1,341.36	0.00	0.00	0.00
10,700.00	89.50	179.60	9,458.57	-1,435.72	177.25	1,441.31	0.00	0.00	0.00
10,800.00	89.50	179.60	9,459.44	-1,535.72	177.95	1,541.26	0.00	0.00	0.00
10,900.00	89.50	179.60	9,460.31	-1,635.71	178.65	1,641.21	0.00	0.00	0.00
11,000.00	89.50	179.60	9,461.19	-1,735.71	179.35	1,741.16	0.00	0.00	0.00
11,100.00	89.50	179.60	9,462.06	-1,835.70	180.05	1,841.12	0.00	0.00	0.00
11,200.00	89.50	179.60	9,462.93	-1,935.69	180.75	1,941.07	0.00	0.00	0.00
11,300.00	89.50	179.60	9,463.80	-2,035.69	181.45	2,041.02	0.00	0.00	0.00
11,400.00	89.50	179.60	9,464.67	-2,135.68	182.15	2,140.97	0.00	0.00	0.00
11,500.00	89.50	179.60	9,465.54	-2,235.67	182.84	2,240.92	0.00	0.00	0.00
11,600.00	89.50	179.60	9,466.41	-2,335.67	183.54	2,340.87	0.00	0.00	0.00
11,700.00	89.50	179.60	9,467.28	-2,435.66	184.24	2,440.82	0.00	0.00	0.00
11,800.00	89.50	179.60	9,468.16	-2,535.66	184.94	2,540.77	0.00	0.00	0.00
11,900.00	89.50	179.60	9,469.03	-2,635.65	185.64	2,640.72	0.00	0.00	0.00
12,000.00	89.50	179.60	9,469.90	-2,735.64	186.34	2,740.67	0.00	0.00	0.00
12,100.00	89.50	179.60	9,470.77	-2,835.64	187.04	2,840.62	0.00	0.00	0.00
12,200.00	89.50	179.60	9,471.64	-2,935.63	187.73	2,940.57	0.00	0.00	0.00
12,300.00	89.50	179.60	9,472.51	-3,035.63	188.43	3,040.53	0.00	0.00	0.00
12,400.00	89.50	179.60	9,473.38	-3,135.62	189.13	3,140.48	0.00	0.00	0.00
12,500.00	89.50	179.60	9,474.25	-3,235.61	189.83	3,240.43	0.00	0.00	0.00
12,600.00	89.50	179.60	9,475.13	-3,335.61	190.53	3,340.38	0.00	0.00	0.00
12,700.00	89.50	179.60	9,476.00	-3,435.60	191.23	3,440.33	0.00	0.00	0.00
12,800.00	89.50	179.60	9,476.87	-3,535.59	191.93	3,540.28	0.00	0.00	0.00
12,900.00	89.50	179.60	9,477.74	-3,635.59	192.62	3,640.23	0.00	0.00	0.00
13,000.00	89.50	179.60	9,478.61	-3,735.58	193.32	3,740.18	0.00	0.00	0.00
13,100.00	89.50	179.60	9,479.48	-3,835.58	194.02	3,840.13	0.00	0.00	0.00
13,200.00	89.50	179.60	9,480.35	-3,935.57	194.72	3,940.08	0.00	0.00	0.00
13,300.00	89.50	179.60	9,481.22	-4,035.56	195.42	4,040.03	0.00	0.00	0.00
13,400.00	89.50	179.60	9,482.10	-4,135.56	196.12	4,139.99	0.00	0.00	0.00
13,500.00	89.50	179.60	9,482.97	-4,235.55	196.82	4,239.94	0.00	0.00	0.00
13,600.00	89.50	179.60	9,483.84	-4,335.54	197.52	4,339.89	0.00	0.00	0.00
13,700.00	89.50	179.60	9,484.71	-4,435.54	198.21	4,439.84	0.00	0.00	0.00
13,800.00	89.50	179.60	9,485.58	-4,535.53	198.91	4,539.79	0.00	0.00	0.00
13,900.00	89.50	179.60	9,486.45	-4,635.53	199.61	4,639.74	0.00	0.00	0.00
14,000.00	89.50	179.60	9,487.32	-4,735.52	200.31	4,739.69	0.00	0.00	0.00
14,100.00	89.50	179.60	9,488.19	-4,835.51	201.01	4,839.64	0.00	0.00	0.00
14,200.00	89.50	179.60	9,489.07	-4,935.51	201.71	4,939.59	0.00	0.00	0.00
14,300.00	89.50	179.60	9,489.94	-5,035.50	202.41	5,039.54	0.00	0.00	0.00
14,400.00	89.50	179.60	9,490.81	-5,135.49	203.10	5,139.49	0.00	0.00	0.00
14,500.00	89.50	179.60	9,491.68	-5,235.49	203.80	5,239.44	0.00	0.00	0.00
14,600.00	89.50	179.60	9,492.55	-5,335.48	204.50	5,339.40	0.00	0.00	0.00



EOG Resources, Inc.

Survey Report

Company: EOG Resources - Midland
Project: Lea County, NM
Site: Hawk 26 Fed
Well: Hawk 26 Fed #2H
Wellbore: OH
Design: Plan #1

Local Co-ordinate Reference: Well Hawk 26 Fed #2H
TVD Reference: WELL @ 3544.00usft (GL 3514' + Cactus 123 KB)
MD Reference: WELL @ 3544.00usft (GL 3514' + Cactus 123 KB)
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: EDM 5000.1 Single User Db

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
14,700.00	89.50	179.60	9,493.42	-5,435.48	205.20	5,439.35	0.00	0.00	0.00
14,712.53	89.50	179.60	9,493.53	-5,448.00	205.29	5,451.87	0.00	0.00	0.00
L Perf									
14,800.00	89.50	179.60	9,494.29	-5,535.47	205.90	5,539.30	0.00	0.00	0.00
14,814.53	89.50	179.60	9,494.42	-5,550.00	206.00	5,553.82	0.00	0.00	0.00
TD 14814.53' MD; 9494.42' TVD									

Design Targets

Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
hit/miss target									
Shape									
U Perf - Hawk 26 Fed #2	0.00	0.01	9,450.45	-509.00	171.00	430,525.00	742,868.00	32° 10' 52.299 N	103° 32' 54.016 W
- plan misses target center by 42.37usft at 9778.98usft MD (9450.53 TVD, -517.92 N, 129.58 E)									
- Point									
L Perf - Hawk 26 Fed #2	0.00	0.00	9,493.55	-5,450.00	205.00	425,584.00	742,902.00	32° 10' 3.403 N	103° 32' 54.040 W
- plan misses target center by 0.30usft at 14714.52usft MD (9493.55 TVD, -5450.00 N, 205.30 E)									
- Point									
BHL - Hawk 26 Fed #2H	0.00	0.00	9,494.42	-5,550.00	206.00	425,484.00	742,903.00	32° 10' 2.413 N	103° 32' 54.037 W
- plan hits target center									
- Point									

Plan Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
8973	8973	0	0	KOP, Build @ 12° DLS
9718	9450	-459	116	LP, Turn @ 3° DLS
9770	9450	-509	128	U Perf
10,177	9454	-912	174	Hold 89.50° Inc; 179.60° AZI;
14,713	9494	-5448	205	L Perf
14,815	9494	-5550	206	TD 14814.53' MD; 9494.42' TVD

Checked By: _____ Approved By: _____ Date: _____

Exhibit 1

EOG Resources

5M BOPE

Rig Floor

1. 13 5/8" Rotating Head
2. Hydril 13 5/8" 5,000 PSI WP GK Annular Preventor
3. 13 5/8" Cameron Type "U" 10,000 PSI WP Ram Preventors
4. 2 1/16" - 10,000 PSI WP Check Valve
5. 10,000 PSI WP - 1502 Union to kill line
6. 2 1/16" - 10,000 PSI WP Manual Valves
7. 13 5/8" 3,000 PSI WP x 13 5/8" 5,000 PSI WP Spacer Spool
8. 4 1/16" 10,000 PSI WP HCR Valve
9. 4 1/16" 10,000 PSI WP Manual Valve
10. 8" OD x 4" ID 10,000 PSI WP Flex Choke Line
11. DSA - 13 5/8" 10,000 PSI WP x 13 5/8" 5,000 PSI WP
12. Mud Cross - 13 5/8" 10,000 PSI WP
13. Blind Rams
14. Pipe Rams
15. 13 5/8" 5,000 PSI WP Spacer Spools
16. Flow Line
17. 2" Fill Line


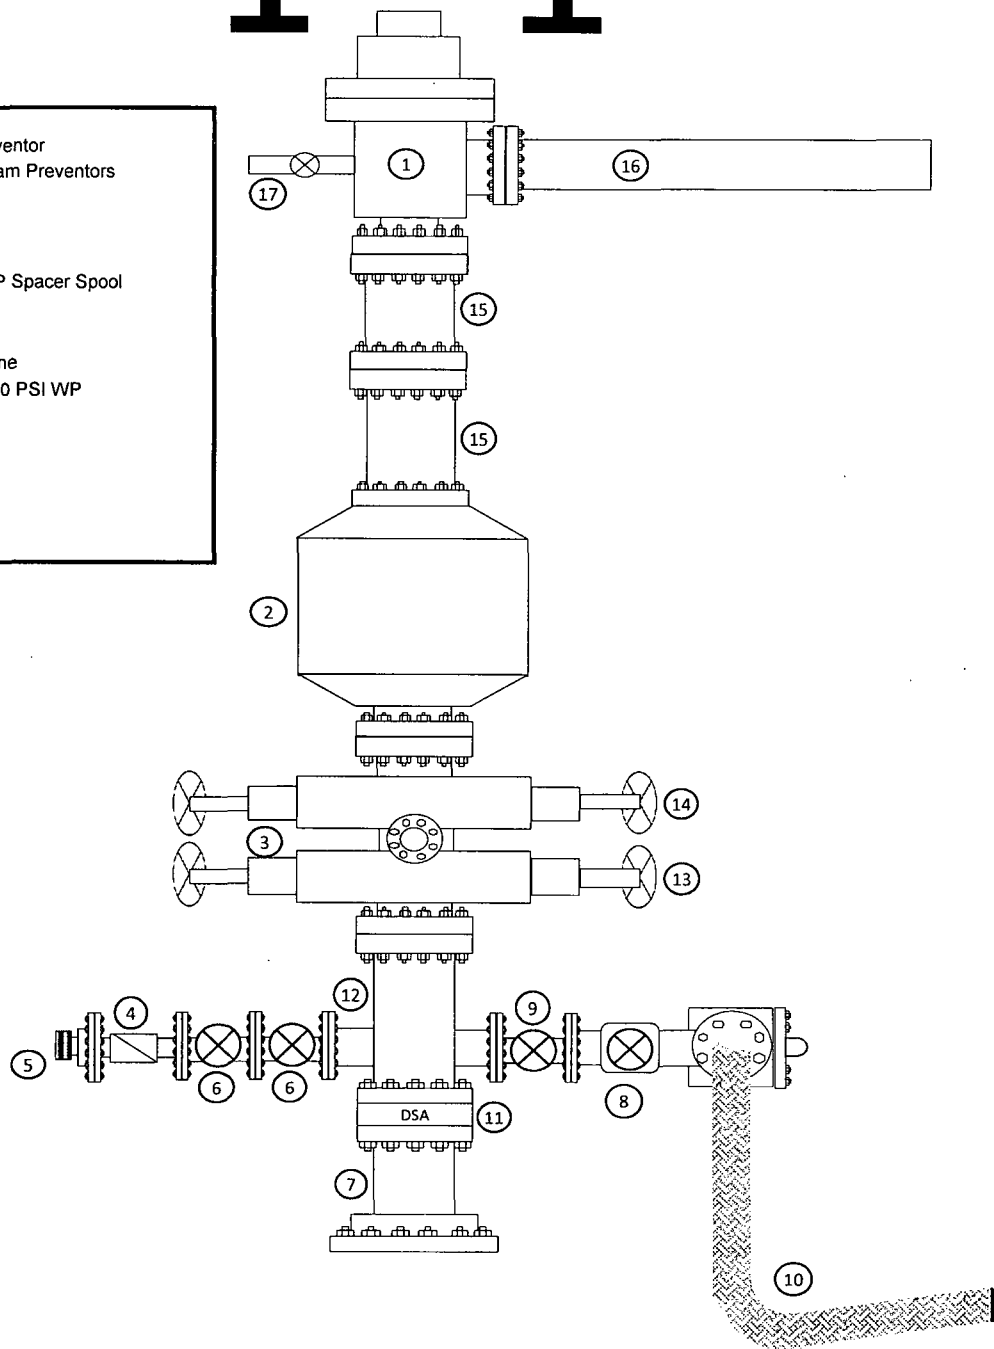


Exhibit 1a

EOG Resources 5M BOPE

1. Cameron 2 1/16" 10,000 PSI WP Gate Valve
2. 4 1/16" 10,000 PSI WP Manual Choke
3. Cameron 4 1/16" 10,000 PSI WP Manual Valve
4. 8" OD x 4" ID 10,000 PSI WP Flex Choke Line
5. Cameron 4 1/16" 10,000 PSI WP Manual Valve & Pressure Gauge on Pressure Block
6. 10,000 PSI WP Hydraulic Choke Valve
7. 8" Expansion Chamber
8. LP Butterfly Valve
9. LP Valve
10. 4" Panic Line
11. 6" Butterfly Valve
12. 10-3/4" Butterfly Valve
13. 6" Butterfly Valve

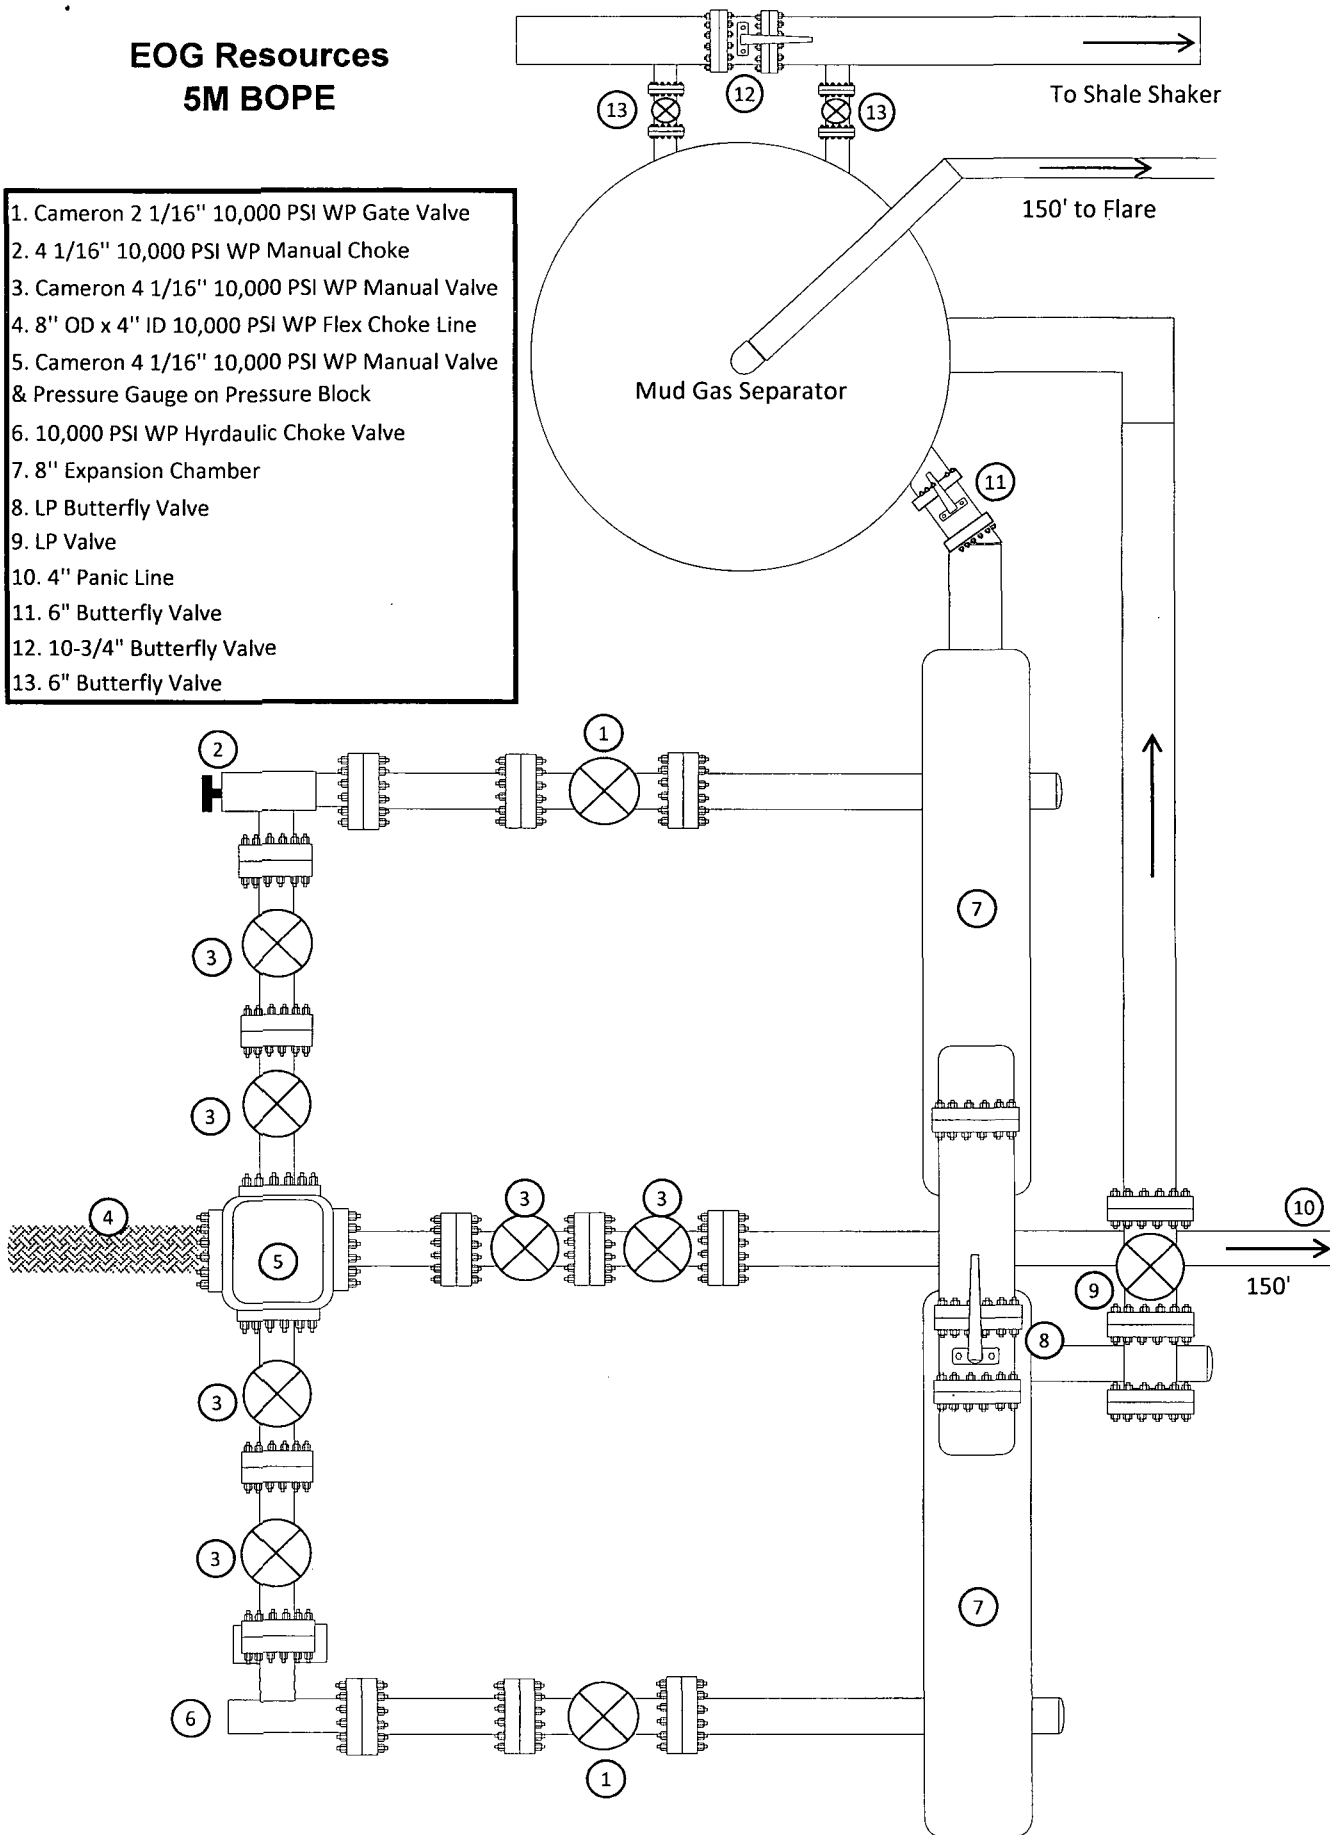

Manufacturer: Midwest Hose & Specialty

Serial Number: SN#90067

Length: 35'

Size: OD = 8" ID = 4"

Ends: Flanges Size: 4-1/16"

WP Rating: 10,000 psi Anchors required by manufacturer: No

M I D W E S T
HOSE AND SPECIALTY INC.

INTERNAL HYDROSTATIC TEST REPORT			
Customer: CACTUS		P.O. Number: RIG #123	
Asset # M10761			
HOSE SPECIFICATIONS			
Type: CHOKER LINE		Length: 35'	
I.D. 4" INCHES		O.D. 8" INCHES	
WORKING PRESSURE 10,000 PSI	TEST PRESSURE 15,000 PSI		BURST PRESSURE PSI
COUPLINGS			
Type of End Fitting 4 1/16 10K FLANGE			
Type of Coupling: SWEDGED		MANUFACTURED BY MIDWEST HOSE & SPECIALTY	
PROCEDURE			
<i>Hose assembly pressure tested with water at ambient temperature.</i>			
TIME HELD AT TEST PRESSURE 1 MIN.		ACTUAL BURST PRESSURE: 0 PSI	
COMMENTS: SN#90067 M10761 Hose is covered with stainless steel armour cover and wrapped with fire resistant vermiculite coated fiberglass insulation rated for 1500 degrees complete with lifting eyes			
Date: 6/6/2011	Tested By: BOBBY FINK		Approved: MENDI JACKSON



Midwest Hose
& Specialty, Inc.

Internal Hydrostatic Test Graph

September 10, 2011

Customer: CACTUS


SALES ORDER# 90067

Hose Specifications

<u>Hose Type</u>	<u>Length</u>
C & K	35'
<u>I.D.</u>	<u>O.D.</u>
4"	8"
<u>Working Pressure</u>	<u>Burst Pressure</u>
10000 PSI	Standard Safety Multiplier Applies

Verification

<u>Type of Fitting</u>	<u>Coupling Method</u>
4 1/16 10K	Swage
<u>Die Size</u>	<u>Final O.D.</u>
6.62"	6.68"
<u>Hose Serial #</u>	<u>Hose Assembly Serial #</u>
	90067

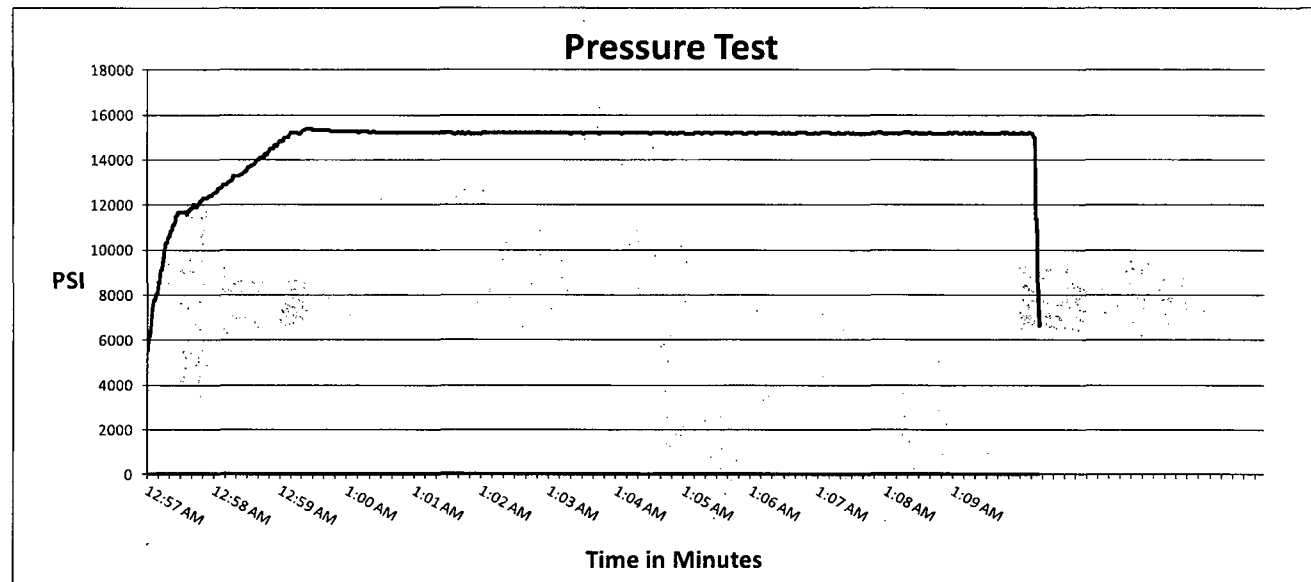

Test Pressure
15000 PSI

Time Held at Test Pressure
11 1/4 Minutes

Actual Burst Pressure

Peak Pressure
15439 PSI

Comments: Hose assembly pressure tested with water at ambient temperature.

Tested By: Bobby Fink

Approved By: Mendi Jackson

Exhibit 4
EOG Resources
Hawk 26 Fed #2H

Well Site Diagram

