

OCD Hobbs
HOBBS OCD

ATS-15-608

FORM APPROVED
OMB No. 1004-0137
Expires July 31, 2010

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SEP 21 2015

APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: ☒ DRILL ☐ REENTER		7. If Unit or CA Agreement, Name and No.
1b. Type of Well: ☒ Oil Well ☐ Gas Well ☐ Other ☐ Single Zone ☐ Multiple Zone		8. Lease Name and Well No. (715271)
2. Name of Operator CHEVRON USA INC (4323)		9. API Well No. 30-025-42807
3a. Address 1616 W. BENDER BLVD HOBBBS, NM 88240	3b. Phone No. (include area code) 575-263-0431	10. Field and Pool, or Exploratory (97838) JENNINGS; UPPER BONE SPRING SH
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface 10' FSL & 648' FWL (u) At proposed prod. zone 180" FSL & 330" FWL (u)		11. Sec., T. R. M. or Blk. and Survey or Area SEC 14 T26S, R32E, UL M (SHL) SEC 23 T26S, R32E, UL M (BHL)
14. Distance in miles and direction from nearest town or post office* 50 MILES SOUTH FROM JAL, NEW MEXICO		12. County or Parish LEA
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 10' FSL		13. State NM
16. No. of acres in lease 1,280 ACRES		17. Spacing Unit dedicated to this well 160 ACRES
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. 1650 ft - RED HILLS W 22 AP FED COM 1		20. BLM/BIA Bond No. on file CA 0329
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 3157' GL		22. Approximate date work will start* 12/01/2015
		23. Estimated duration 30 days

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. I, must be attached to this form:

- | | |
|--|---|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the BLM. |

25. Signature <i>Cindy Herrera-Murillo</i>	Name (Printed/Typed) CINDY HERRERA-MURILLO	Date 04/28/2015
---	---	--------------------

Title

PERMITTING SPECIALIST

Approved by (Signature) <i>/s/George MacDoneil</i>	Name (Printed/Typed)	Date SEP 14 2015
---	----------------------	---------------------

Title

FIELD MANAGER

Office

CARLSBAD FIELD OFFICE

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

APPROVAL FOR TWO YEARS

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)

SEE ATTACHED FOR
CONDITIONS OF APPROVAL

Ka
09/21/15

APPROVAL SUBJECT TO
GENERAL REQUIREMENTS AND
SPECIAL STIPULATIONS
ATTACHED

CARLSBAD CONTROLLED WATER BASIN

WITNESS SURFACE CASING

SEP 23 2015

1. FORMATION TOPS

The estimated tops of important geologic markers are as follows:

FORMATION	SUB-SEA TVD	KBTVD	MD
Rustler	2516	650	
Castile	166	3000	
Lamar	-1484	4650	
Bell Canyon	-1514	4680	
Cherry Canyon	-2634	5800	
Brushy Canyon	-4184	7350	
Bone Spring Limestone	-5564	8730	
Upr. Avalon	-5634	8800	
Lateral TD (Upper Avalon)	-5784	8950	13856

2. ESTIMATED DEPTH OF WATER, OIL, GAS & OTHER MINERAL BEARING FORMATIONS

The estimated depths at which the top and bottom of the anticipated water, oil, gas, or other mineral bearing formations are expected to be encountered are as follows:

Substance	Formation	Depth
Deepest Expected Base of Fresh Water		800
Water	Rustler	650
Water	Bell Canyon	4680
Water	Cherry Canyon	5800
Oil/Gas	Brushy Canyon	7350
Oil/Gas	Bone Spring Limestone	8730
Oil/Gas	Upr. Avalon	8800

All shows of fresh water and minerals will be reported and protected.

3. BOP EQUIPMENT

Will have a minimum of a 5000 psi rig stack (see proposed schematic) for drill out below surface casing.
Stack will be tested as specified in the attached testing requirements.

see cont

Chevron requests a variance to use a GE/Vetco SH-2 ~~Multibowl~~ wellhead, which will be run through the rig floor on surface casing. BOPE will be nipped up and tested after cementing surface casing. Subsequent tests will be performed as needed, not to exceed 30 days. The field report from GE/Vetco and BOP test information will be provided in a subsequent report at the end of the well. Please see the attached wellhead schematic. An installation manual has been placed on file with the BLM office and remains unchanged from previous submittal.

4. CASING PROGRAM

a. The proposed casing program will be as follows:

Purpose	From	To	Hole Size	Csg Size	Weight	Grade	Thread	Condition
Surface	0'	670' 850'	17-1/2"	13-3/8"	48 #	H-40	STC	New
Intermediate	0'	4530' 4740'	12-1/4"	9-5/8"	40 #	HCK-55	LTC	New
Production	0'	13,856'	8-3/4"	5-1/2"	20.0 #	HCP-110	TXP BTC S	New

b. Casing design subject to revision based on geologic conditions encountered.

c. ***A "Worst Case" casing design for wells in a particular area is used below to calculate the Casing Safety Factors. If for any reason the casing design for a particular well requires setting casing deeper than the following "worst case" design, then the Casing Safety Factors will be recalculated & sent to the BLM prior to drilling.

d. Chevron will fill casing at a minimum of every 20 jts (840') while running for intermediate and production casing in order to maintain collapse SF.

SF Calculations based on the following "Worst Case" casing design:

Surface Casing: 1000'

Intermediate Casing: 5000'

Production Casing: 15,000' MD/9,135' TVD (6400' VS @ 90 deg inc)

Casing String	Min SF Burst	Min SF Collapse	Min SF Tension	Min SF Tri-Axial
Surface	1.42	1.63	2.29	1.8
Intermediate	1.2	1.44	2.09	1.44
Production	1.26	1.71	2.2	1.46

Min SF is the smallest of a group of safety factors that include the following considerations:

	Surf	Int	Prod
Burst Design			
Pressure Test- Surface, Int, Prod Csg P external: Water P internal: Test psi + next section heaviest mud in csg	X	X	X
Displace to Gas- Surf Csg P external: Water P internal: Dry Gas from Next Csg Point	X		
Frac at Shoe, Gas to Surf- Int Csg P external: Water P internal: Dry Gas, 15 ppg Frac Gradient		X	
Stimulation (Frac) Pressures- Prod Csg P external: Water P internal: Max inj pressure w/ heaviest injected fluid			X
Tubing leak- Prod Csg (packer at KOP) P external: Water P internal: Leak just below surf, 8.7 ppg packer fluid			X
Collapse Design			
Full Evacuation P external: Water gradient in cement, mud above TOC P internal: none	X	X	X
Cementing- Surf, Int, Prod Csg P external: Wet cement P internal: water	X	X	X
Tension Design			
100k lb overpull	X	X	X

5. CEMENTING PROGRAM

Slurry	Type	Top	Bottom	Weight	Yield	%Excess	Sacks	Water
Surface			620	(ppg)	(sx/cu ft)	Open Hole		gal/sk
Tail	Class C+2%CaCl	0'	850'	14.8	1.35	125	1011	6.57
Intermediate								
Lead	EconoCem C + 3 lb/sk Kol-Seal + 0.125 lb/sk PolyFlake + 0.1% HR-601 + 0.25% D-Air 5000	0'	3,740'	11.9	2.46	150	1050	14.21
Tail	HalCem C	3,740'	4,740'	14.8	1.33	85	464	6.37
Production			4530					
1st Lead	VariCem-PB1 + 0.1% FWCA + 3 lb/sk Kol-Seal + 0.1% HR-601	3,890'	8,487'	11.3	2.54	50	646	15.51
2nd Lead	VariCem-PB2 + 0.5% Halad-344 + 0.3% CFR-3 + 3 lb/sk KolSeal + 0.05% FE-2 + 0.1% HR-601	8,487'	12,856'	12.5	1.79	35	836	9.64
Tail	SoluCem H + 0.25 lb/sk D-Air 5000	12,856'	13,856'	15	2.63	0	96	11.42

1. Final cement volumes will be determined by caliper.
2. Surface casing shall have at least one centralizer installed on each of the bottom three joints starting with the shoe joint.
3. Production casing will have one horizontal type centralizer on every joint for the first 1000' from TD, then every other joint to EOB, and then every third joint to KOP. Bowspring type centralizers will be run from KOP to intermediate casing.

6. MUD PROGRAM

From	To	Type	Weight	F. Vis	Filtrate
0'	850'	Spud Mud	8.3 - 8.7	32 - 34	NC - NC
850'	4,740'	Brine	9.5 - 10.1	28 - 30	NC - NC
4,740'	8,487'	FW/Cut Brine	8.3 - 9.6	28 - 30	NC - NC
8,487'	9,231'	Cut Brine	8.3 - 9.6	28 - 30	15 - 25
9,231'	13,856'	FW/Cut Brine	8.3 - 9.6	28 - 30	15 - 25

A closed system will be utilized consisting of above ground steel tanks. All wastes accumulated during drilling operations will be contained in a portable trash cage and removed from location and deposited in an approved sanitary landfill. Sanitary wastes will be contained in a chemical porta-toilet and then hauled to an approved sanitary landfill.

All fluids and cuttings will be disposed of in accordance with New Mexico Oil Conservation Division rules and regulations.

A mud test shall be performed every 24 hours after mudding up to determine, as applicable: density, viscosity, gel strength, filtration, and pH.

Visual mud monitoring equipment shall be in place to detect volume changes indicating loss or gain of circulating fluid volume. When abnormal pressures are anticipated -- a pit volume totalizer (PVT), stroke counter, and flow sensor will be used to detect volume changes indicating loss or gain of circulating fluid volume.

A weighting agent and lost circulating material (LCM) will be onsite to mitigate pressure or lost circulation as hole conditions dictate.

7. TESTING, LOGGING, AND CORING

The anticipated type and amount of testing, logging, and coring are as follows:

- Drill stem tests are not planned.
- The logging program will be as follows:

TYPE	Logs	Interval	Timing	Vendor
Mudlogs	2 man mudlog	Int Csg to TD	Drillout of Int Csg	TBD
LWD	MWD Gamma	Int. and Prod. Hole	While Drilling	TBD

- Conventional whole core samples are not planned.
- A Directional Survey will be run.

8. ABNORMAL PRESSURES AND HYDROGEN SULFIDE


- No abnormal pressures or temperatures are expected. Estimated BHP is: 4500 psi
- Hydrogen sulfide gas is not anticipated. An H2S Contingency plan is attached with this APD in the event that H2S is encountered



Project: Lea County, NM (NAD27 NME)
Site: SD WE
Well: 23 Fed P5 1H
Wellbore: Wellbore #1
Design: Plan 1 04-06-15
Rig: TBD



Azimuths to Grid North
True North: -0.36°
Magnetic North: 6.70°
Magnetic Field
Strength: 48115.5nT
Dip Angle: 59.77°
Date: 4/8/2015
Model: HDGM

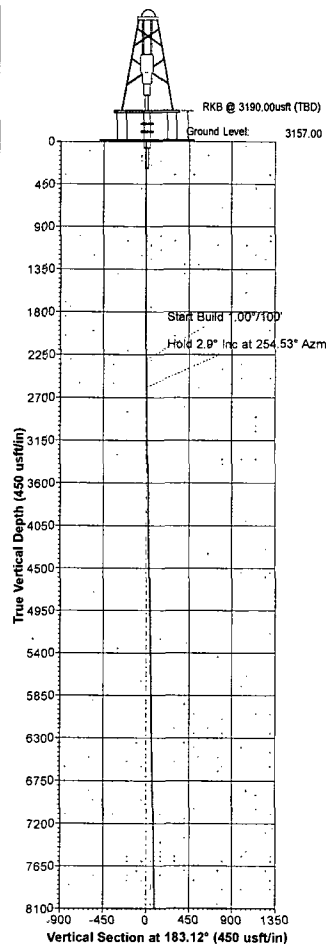

WELL DETAILS						
			Ground Level:	3157.00		
+N-S	+E-W	Northing	Easting	Latitude	Longitude	
1.00	25.00	377312.00	711242.00	32° 2' 7.84596 N	103° 39' 5.90418 W	

SECTION DETAILS											
Sec	MD	Inc	Azi	TVD	+N-S	+E-W	Dleg	TFace	VSec	Target	Annotation
1	0.00	0.00	0.00	0.00	1.00	25.00	0.00	0.00	0.00		Start Build 1.00°/100'
2	2300.00	0.00	0.00	2300.00	1.00	25.00	0.00	0.00	0.00		Hold 2.9° Inc at 254.53° Azm
3	2590.09	2.90	254.53	2589.96	-0.96	17.92	1.00	254.53	2.34		KOP: Start Build-Turn 12°/100'
4	8487.06	2.90	254.53	8479.38	-80.54	-269.70	0.00	0.00	97.48		LP: 90° Inc at 179.61° Azm
5	9230.78	90.00	179.61	8950.00	-558.11	-289.48	12.00	-74.94	575.42		TD at 13855.78
6	13855.78	90.00	179.61	8950.00	-5183.00	-258.00	0.00	0.00	5191.72	BHL 23 Fed P5 1H	





DESIGN TARGET DETAILS									
Name	TVD	+N-S	+E-W	Northing	Easting	Latitude	Longitude	Shape	
BHL 23 Fed P5 1H	8950.00	-5183.00	-258.00	372128.00	710958.00	32° 1' 16.56274 N	103° 38' 9.57116 W	Point	
plan hits target center									


Map System: US State Plane 1927 (Exact solution)
Datum: NAD 1927 (NADCON CONUS)
Ellipsoid: Clarke 1866
Zone Name: New Mexico East 3001
Local Origin: Site SD WE, Grid North
Latitude: 32° 2' 7.83756 N
Longitude: 103° 39' 6.19467 W
Grid East: 711217.00
Grid North: 377311.00
Scale Factor: 1.000

Geomagnetic Model: HDGM
Sample Date: 06-Apr-15
Magnetic Declination: 7.07°
Dip Angle from Horizontal: 59.77°
Magnetic Field Strength: 48116
To convert a Magnetic Direction to a Grid Direction, Add 6.71°
To convert a Magnetic Direction to a True Direction, Add 7.07° East
To convert a True Direction to a Grid Direction, Subtract 0.36°

LEGEND

- 23 Fed P5 2H, Wellbore #1, Plan 1 04-06-15 V0
- 14 Fed P5 1H, Wellbore #1, Plan 1 04-06-15 V0
- 14 Fed P5 2H, Wellbore #1, Plan 1 04-06-15 V0
- Plan 1 04-06-15

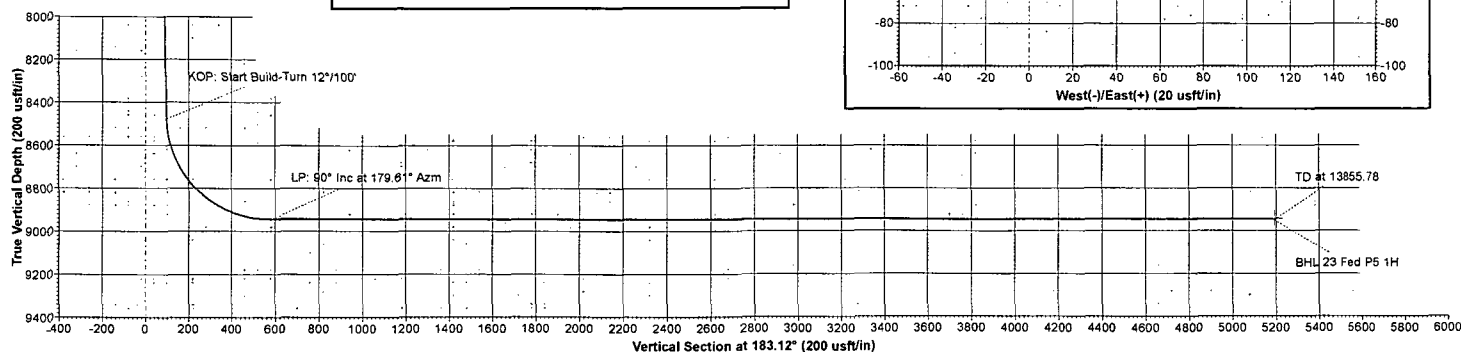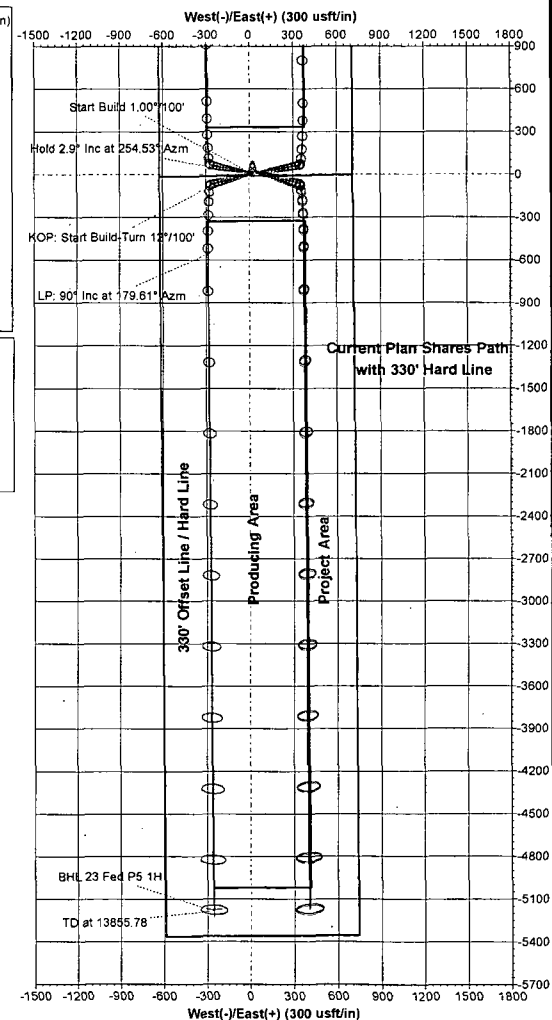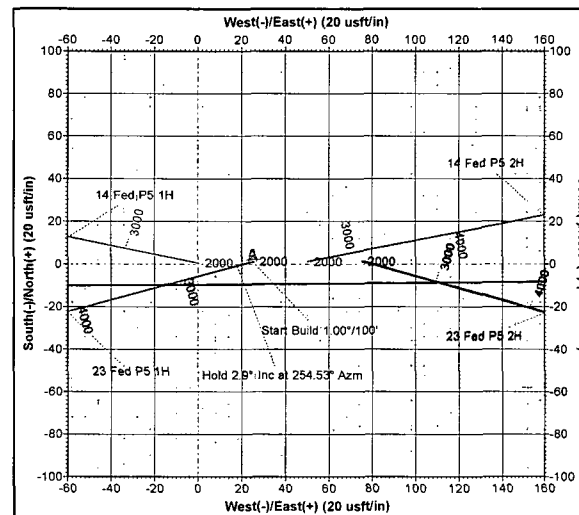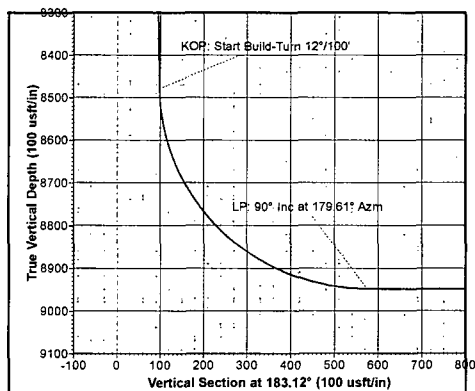



Chevron

Lea County, NM (NAD27 NME)

SD WE

23 Fed P5 1H

Wellbore #1

Plan: Plan 1 04-06-15

Standard Planning Report

06 April, 2015





Planning Report



Database: Compass 5000 GCR
Company: Chevron
Project: Lea County, NM (NAD27 NME)
Site: SD WE
Well: 23 Fed P5 1H
Wellbore: Wellbore #1
Design: Plan 1 04-06-15

Local Co-ordinate Reference: Site SD WE
TVD Reference: RKB @ 3190.00usft (TBD)
MD Reference: RKB @ 3190.00usft (TBD)
North Reference: Grid
Survey Calculation Method: Minimum Curvature

Project	Lea County, NM (NAD27 NME)		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Site	SD WE			
Site Position:		Northing:	377,311.00 usft	Latitude: 32° 2' 7.83756 N
From: Map		Easting:	711,217.00 usft	Longitude: 103° 39' 6.19467 W
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16"	Grid Convergence: 0.36°

Well	23 Fed P5 1H			
Well Position	+N/-S	1.00 usft	Northing:	377,312.00 usft
	+E/-W	25.00 usft	Easting:	711,242.00 usft
Position Uncertainty	0.00 usft	Wellhead Elevation:	0.00 usft	Ground Level: 3,157.00 usft

Wellbore	Wellbore #1				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	HDGM	4/6/2015	7.07	59.77	48,116

Design	Plan 1 04-06-15			
Audit Notes:				
Version:	Phase:	PROTOTYPE	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.00	1.00	25.00	183.12

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.00	0.00	0.00	0.00	1.00	25.00	0.00	0.00	0.00	0.00	
2,300.00	0.00	0.00	2,300.00	1.00	25.00	0.00	0.00	0.00	0.00	
2,590.09	2.90	254.53	2,589.96	-0.96	17.92	1.00	1.00	0.00	254.53	
8,487.06	2.90	254.53	8,479.38	-80.54	-269.70	0.00	0.00	0.00	0.00	
9,230.78	90.00	179.61	8,950.00	-558.11	-289.48	12.00	11.71	-10.07	-74.94	
13,855.78	90.00	179.61	8,950.00	-5,183.00	-258.00	0.00	0.00	0.00	0.00	BHL 23 Fed P5 1H



Planning Report



Database: Compass 5000 GCR
Company: Chevron
Project: Lea County, NM (NAD27 NME)
Site: SD WE
Well: 23 Fed P5 1H
Wellbore: Wellbore #1
Design: Plan 1 04-06-15

Local Co-ordinate Reference: Site SD WE
TVD Reference: RKB @ 3190.00usft (TBD)
MD Reference: RKB @ 3190.00usft (TBD)
North Reference: Grid
Survey Calculation Method: Minimum Curvature

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.00	0.00	0.00	0.00	1.00	25.00	0.00	0.00	0.00	0.00
100.00	0.00	0.00	100.00	1.00	25.00	0.00	0.00	0.00	0.00
200.00	0.00	0.00	200.00	1.00	25.00	0.00	0.00	0.00	0.00
300.00	0.00	0.00	300.00	1.00	25.00	0.00	0.00	0.00	0.00
400.00	0.00	0.00	400.00	1.00	25.00	0.00	0.00	0.00	0.00
500.00	0.00	0.00	500.00	1.00	25.00	0.00	0.00	0.00	0.00
600.00	0.00	0.00	600.00	1.00	25.00	0.00	0.00	0.00	0.00
700.00	0.00	0.00	700.00	1.00	25.00	0.00	0.00	0.00	0.00
800.00	0.00	0.00	800.00	1.00	25.00	0.00	0.00	0.00	0.00
900.00	0.00	0.00	900.00	1.00	25.00	0.00	0.00	0.00	0.00
1,000.00	0.00	0.00	1,000.00	1.00	25.00	0.00	0.00	0.00	0.00
1,100.00	0.00	0.00	1,100.00	1.00	25.00	0.00	0.00	0.00	0.00
1,200.00	0.00	0.00	1,200.00	1.00	25.00	0.00	0.00	0.00	0.00
1,300.00	0.00	0.00	1,300.00	1.00	25.00	0.00	0.00	0.00	0.00
1,400.00	0.00	0.00	1,400.00	1.00	25.00	0.00	0.00	0.00	0.00
1,500.00	0.00	0.00	1,500.00	1.00	25.00	0.00	0.00	0.00	0.00
1,600.00	0.00	0.00	1,600.00	1.00	25.00	0.00	0.00	0.00	0.00
1,700.00	0.00	0.00	1,700.00	1.00	25.00	0.00	0.00	0.00	0.00
1,800.00	0.00	0.00	1,800.00	1.00	25.00	0.00	0.00	0.00	0.00
1,900.00	0.00	0.00	1,900.00	1.00	25.00	0.00	0.00	0.00	0.00
2,000.00	0.00	0.00	2,000.00	1.00	25.00	0.00	0.00	0.00	0.00
2,100.00	0.00	0.00	2,100.00	1.00	25.00	0.00	0.00	0.00	0.00
2,200.00	0.00	0.00	2,200.00	1.00	25.00	0.00	0.00	0.00	0.00
2,300.00	0.00	0.00	2,300.00	1.00	25.00	0.00	0.00	0.00	0.00
Start Build 1.00°/100'									
2,400.00	1.00	254.53	2,399.99	0.77	24.16	0.28	1.00	1.00	0.00
2,500.00	2.00	254.53	2,499.96	0.07	21.64	1.11	1.00	1.00	0.00
2,590.09	2.90	254.53	2,589.96	-0.96	17.92	2.34	1.00	1.00	0.00
Hold 2.9° Inc at 254.53° Azm									
2,600.00	2.90	254.53	2,599.86	-1.09	17.44	2.50	0.00	0.00	0.00
2,700.00	2.90	254.53	2,699.74	-2.44	12.56	4.11	0.00	0.00	0.00
2,800.00	2.90	254.53	2,799.61	-3.79	7.69	5.73	0.00	0.00	0.00
2,900.00	2.90	254.53	2,899.48	-5.14	2.81	7.34	0.00	0.00	0.00
3,000.00	2.90	254.53	2,999.35	-6.49	-2.07	8.95	0.00	0.00	0.00
3,100.00	2.90	254.53	3,099.22	-7.84	-6.95	10.57	0.00	0.00	0.00
3,200.00	2.90	254.53	3,199.09	-9.19	-11.82	12.18	0.00	0.00	0.00
3,300.00	2.90	254.53	3,298.97	-10.54	-16.70	13.79	0.00	0.00	0.00
3,400.00	2.90	254.53	3,398.84	-11.89	-21.58	15.41	0.00	0.00	0.00
3,500.00	2.90	254.53	3,498.71	-13.24	-26.46	17.02	0.00	0.00	0.00
3,600.00	2.90	254.53	3,598.58	-14.59	-31.34	18.63	0.00	0.00	0.00
3,700.00	2.90	254.53	3,698.45	-15.94	-36.21	20.25	0.00	0.00	0.00
3,800.00	2.90	254.53	3,798.33	-17.29	-41.09	21.86	0.00	0.00	0.00
3,900.00	2.90	254.53	3,898.20	-18.64	-45.97	23.47	0.00	0.00	0.00
4,000.00	2.90	254.53	3,998.07	-19.98	-50.85	25.09	0.00	0.00	0.00
4,100.00	2.90	254.53	4,097.94	-21.33	-55.72	26.70	0.00	0.00	0.00
4,200.00	2.90	254.53	4,197.81	-22.68	-60.60	28.31	0.00	0.00	0.00
4,300.00	2.90	254.53	4,297.69	-24.03	-65.48	29.93	0.00	0.00	0.00
4,400.00	2.90	254.53	4,397.56	-25.38	-70.36	31.54	0.00	0.00	0.00
4,500.00	2.90	254.53	4,497.43	-26.73	-75.23	33.15	0.00	0.00	0.00
4,600.00	2.90	254.53	4,597.30	-28.08	-80.11	34.77	0.00	0.00	0.00
4,700.00	2.90	254.53	4,697.17	-29.43	-84.99	36.38	0.00	0.00	0.00
4,800.00	2.90	254.53	4,797.04	-30.78	-89.87	37.99	0.00	0.00	0.00
4,900.00	2.90	254.53	4,896.92	-32.13	-94.74	39.61	0.00	0.00	0.00
5,000.00	2.90	254.53	4,996.79	-33.48	-99.62	41.22	0.00	0.00	0.00



Planning Report



Database: Compass 5000 GCR
 Company: Chevron
 Project: Lea County, NM (NAD27 NME)
 Site: SD WE
 Well: 23 Fed P5 1H
 Wellbore: Wellbore #1
 Design: Plan 1 04-06-15

Local Co-ordinate Reference: Site SD WE
 TVD Reference: RKB @ 3190.00usft (TBD)
 MD Reference: RKB @ 3190.00usft (TBD)
 North Reference: Grid
 Survey Calculation Method: Minimum Curvature

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
5,100.00	2.90	254.53	5,096.66	-34.83	-104.50	42.83	0.00	0.00	0.00
5,200.00	2.90	254.53	5,196.53	-36.18	-109.38	44.45	0.00	0.00	0.00
5,300.00	2.90	254.53	5,296.40	-37.53	-114.25	46.06	0.00	0.00	0.00
5,400.00	2.90	254.53	5,396.28	-38.88	-119.13	47.68	0.00	0.00	0.00
5,500.00	2.90	254.53	5,496.15	-40.23	-124.01	49.29	0.00	0.00	0.00
5,600.00	2.90	254.53	5,596.02	-41.58	-128.89	50.90	0.00	0.00	0.00
5,700.00	2.90	254.53	5,695.89	-42.93	-133.76	52.52	0.00	0.00	0.00
5,800.00	2.90	254.53	5,795.76	-44.28	-138.64	54.13	0.00	0.00	0.00
5,900.00	2.90	254.53	5,895.63	-45.63	-143.52	55.74	0.00	0.00	0.00
6,000.00	2.90	254.53	5,995.51	-46.97	-148.40	57.36	0.00	0.00	0.00
6,100.00	2.90	254.53	6,095.38	-48.32	-153.27	58.97	0.00	0.00	0.00
6,200.00	2.90	254.53	6,195.25	-49.67	-158.15	60.58	0.00	0.00	0.00
6,300.00	2.90	254.53	6,295.12	-51.02	-163.03	62.20	0.00	0.00	0.00
6,400.00	2.90	254.53	6,394.99	-52.37	-167.91	63.81	0.00	0.00	0.00
6,500.00	2.90	254.53	6,494.87	-53.72	-172.78	65.42	0.00	0.00	0.00
6,600.00	2.90	254.53	6,594.74	-55.07	-177.66	67.04	0.00	0.00	0.00
6,700.00	2.90	254.53	6,694.61	-56.42	-182.54	68.65	0.00	0.00	0.00
6,800.00	2.90	254.53	6,794.48	-57.77	-187.42	70.26	0.00	0.00	0.00
6,900.00	2.90	254.53	6,894.35	-59.12	-192.29	71.88	0.00	0.00	0.00
7,000.00	2.90	254.53	6,994.23	-60.47	-197.17	73.49	0.00	0.00	0.00
7,100.00	2.90	254.53	7,094.10	-61.82	-202.05	75.10	0.00	0.00	0.00
7,200.00	2.90	254.53	7,193.97	-63.17	-206.93	76.72	0.00	0.00	0.00
7,300.00	2.90	254.53	7,293.84	-64.52	-211.80	78.33	0.00	0.00	0.00
7,400.00	2.90	254.53	7,393.71	-65.87	-216.68	79.94	0.00	0.00	0.00
7,500.00	2.90	254.53	7,493.58	-67.22	-221.56	81.56	0.00	0.00	0.00
7,600.00	2.90	254.53	7,593.46	-68.57	-226.44	83.17	0.00	0.00	0.00
7,700.00	2.90	254.53	7,693.33	-69.92	-231.32	84.78	0.00	0.00	0.00
7,800.00	2.90	254.53	7,793.20	-71.27	-236.19	86.40	0.00	0.00	0.00
7,900.00	2.90	254.53	7,893.07	-72.62	-241.07	88.01	0.00	0.00	0.00
8,000.00	2.90	254.53	7,992.94	-73.97	-245.95	89.62	0.00	0.00	0.00
8,100.00	2.90	254.53	8,092.82	-75.31	-250.83	91.24	0.00	0.00	0.00
8,200.00	2.90	254.53	8,192.69	-76.66	-255.70	92.85	0.00	0.00	0.00
8,300.00	2.90	254.53	8,292.56	-78.01	-260.58	94.46	0.00	0.00	0.00
8,400.00	2.90	254.53	8,392.43	-79.36	-265.46	96.08	0.00	0.00	0.00
8,487.06	2.90	254.53	8,479.38	-80.54	-269.70	97.48	0.00	0.00	0.00
KOP: Start Build-Turn 12°/100'									
8,500.00	3.63	230.11	8,492.30	-80.89	-270.33	97.86	12.00	5.62	-188.77
8,525.00	6.00	207.36	8,517.21	-82.56	-271.54	99.60	12.00	9.48	-91.01
8,550.00	8.76	198.12	8,542.00	-85.53	-272.73	102.63	12.00	11.06	-36.98
8,575.00	11.64	193.35	8,566.61	-89.79	-273.91	106.95	12.00	11.52	-19.09
8,600.00	14.57	190.46	8,590.95	-95.34	-275.06	112.55	12.00	11.71	-11.55
8,625.00	17.52	188.52	8,614.97	-102.16	-276.19	119.42	12.00	11.81	-7.74
8,650.00	20.49	187.13	8,638.61	-110.22	-277.29	127.54	12.00	11.86	-5.56
8,675.00	23.47	186.08	8,661.79	-119.52	-278.36	136.87	12.00	11.90	-4.21
8,700.00	26.44	185.26	8,684.45	-130.01	-279.40	147.41	12.00	11.92	-3.31
8,725.00	29.43	184.59	8,706.54	-141.68	-280.40	159.12	12.00	11.93	-2.68
8,750.00	32.41	184.03	8,727.98	-154.49	-281.37	171.96	12.00	11.95	-2.23
8,775.00	35.40	183.56	8,748.73	-168.40	-282.29	185.90	12.00	11.95	-1.89
8,800.00	38.39	183.15	8,768.72	-183.39	-283.16	200.91	12.00	11.96	-1.63
8,825.00	41.38	182.79	8,787.90	-199.40	-283.99	216.94	12.00	11.97	-1.43
8,850.00	44.38	182.48	8,806.22	-216.39	-284.77	233.95	12.00	11.97	-1.27
8,875.00	47.37	182.19	8,823.62	-234.32	-285.50	251.89	12.00	11.97	-1.14
8,900.00	50.36	181.93	8,840.06	-253.13	-286.18	270.72	12.00	11.97	-1.03
8,925.00	53.36	181.70	8,855.50	-272.78	-286.80	290.37	12.00	11.98	-0.95



Planning Report



Database: Compass 5000 GCR
 Company: Chevron
 Project: Lea County, NM (NAD27 NME)
 Site: SD WE
 Well: 23 Fed P5 1H
 Wellbore: Wellbore #1
 Design: Plan 1 04-06-15

Local Co-ordinate Reference: Site SD WE
 TVD Reference: RKB @ 3190.00usft (TBD)
 MD Reference: RKB @ 3190.00usft (TBD)
 North Reference: Grid
 Survey Calculation Method: Minimum Curvature

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
8,950.00	56.35	181.48	8,869.89	-293.21	-287.36	310.80	12.00	11.98	-0.88
8,975.00	59.35	181.27	8,883.19	-314.37	-287.87	331.96	12.00	11.98	-0.82
9,000.00	62.34	181.08	8,895.37	-336.20	-288.32	353.77	12.00	11.98	-0.77
9,025.00	65.34	180.90	8,906.39	-358.63	-288.71	376.20	12.00	11.98	-0.73
9,050.00	68.33	180.72	8,916.22	-381.61	-289.03	399.16	12.00	11.98	-0.69
9,075.00	71.33	180.56	8,924.84	-405.07	-289.29	422.60	12.00	11.98	-0.67
9,100.00	74.33	180.40	8,932.22	-428.95	-289.49	446.46	12.00	11.98	-0.64
9,125.00	77.32	180.24	8,938.34	-453.19	-289.62	470.67	12.00	11.98	-0.62
9,150.00	80.32	180.09	8,943.19	-477.71	-289.70	495.16	12.00	11.99	-0.61
9,175.00	83.31	179.94	8,946.75	-502.46	-289.70	519.86	12.00	11.99	-0.60
9,200.00	86.31	179.79	8,949.01	-527.35	-289.64	544.72	12.00	11.99	-0.59
9,225.00	89.31	179.64	8,949.97	-552.33	-289.52	569.65	12.00	11.99	-0.59
9,230.78	90.00	179.61	8,950.00	-558.11	-289.48	575.42	12.00	11.99	-0.59
LP: 90° Inc at 179.61° Azm									
9,300.00	90.00	179.61	8,950.00	-627.33	-289.01	644.51	0.00	0.00	0.00
9,400.00	90.00	179.61	8,950.00	-727.32	-288.33	744.32	0.00	0.00	0.00
9,500.00	90.00	179.61	8,950.00	-827.32	-287.65	844.13	0.00	0.00	0.00
9,600.00	90.00	179.61	8,950.00	-927.32	-286.97	943.95	0.00	0.00	0.00
9,700.00	90.00	179.61	8,950.00	-1,027.32	-286.29	1,043.76	0.00	0.00	0.00
9,800.00	90.00	179.61	8,950.00	-1,127.32	-285.61	1,143.57	0.00	0.00	0.00
9,900.00	90.00	179.61	8,950.00	-1,227.31	-284.93	1,243.38	0.00	0.00	0.00
10,000.00	90.00	179.61	8,950.00	-1,327.31	-284.25	1,343.19	0.00	0.00	0.00
10,100.00	90.00	179.61	8,950.00	-1,427.31	-283.56	1,443.00	0.00	0.00	0.00
10,200.00	90.00	179.61	8,950.00	-1,527.31	-282.88	1,542.82	0.00	0.00	0.00
10,300.00	90.00	179.61	8,950.00	-1,627.30	-282.20	1,642.63	0.00	0.00	0.00
10,400.00	90.00	179.61	8,950.00	-1,727.30	-281.52	1,742.44	0.00	0.00	0.00
10,500.00	90.00	179.61	8,950.00	-1,827.30	-280.84	1,842.25	0.00	0.00	0.00
10,600.00	90.00	179.61	8,950.00	-1,927.30	-280.16	1,942.06	0.00	0.00	0.00
10,700.00	90.00	179.61	8,950.00	-2,027.29	-279.48	2,041.88	0.00	0.00	0.00
10,800.00	90.00	179.61	8,950.00	-2,127.29	-278.80	2,141.69	0.00	0.00	0.00
10,900.00	90.00	179.61	8,950.00	-2,227.29	-278.12	2,241.50	0.00	0.00	0.00
11,000.00	90.00	179.61	8,950.00	-2,327.29	-277.44	2,341.31	0.00	0.00	0.00
11,100.00	90.00	179.61	8,950.00	-2,427.29	-276.76	2,441.12	0.00	0.00	0.00
11,200.00	90.00	179.61	8,950.00	-2,527.28	-276.08	2,540.94	0.00	0.00	0.00
11,300.00	90.00	179.61	8,950.00	-2,627.28	-275.40	2,640.75	0.00	0.00	0.00
11,400.00	90.00	179.61	8,950.00	-2,727.28	-274.72	2,740.56	0.00	0.00	0.00
11,500.00	90.00	179.61	8,950.00	-2,827.28	-274.04	2,840.37	0.00	0.00	0.00
11,600.00	90.00	179.61	8,950.00	-2,927.27	-273.35	2,940.18	0.00	0.00	0.00
11,700.00	90.00	179.61	8,950.00	-3,027.27	-272.67	3,040.00	0.00	0.00	0.00
11,800.00	90.00	179.61	8,950.00	-3,127.27	-271.99	3,139.81	0.00	0.00	0.00
11,900.00	90.00	179.61	8,950.00	-3,227.27	-271.31	3,239.62	0.00	0.00	0.00
12,000.00	90.00	179.61	8,950.00	-3,327.26	-270.63	3,339.43	0.00	0.00	0.00
12,100.00	90.00	179.61	8,950.00	-3,427.26	-269.95	3,439.24	0.00	0.00	0.00
12,200.00	90.00	179.61	8,950.00	-3,527.26	-269.27	3,539.06	0.00	0.00	0.00
12,300.00	90.00	179.61	8,950.00	-3,627.26	-268.59	3,638.87	0.00	0.00	0.00
12,400.00	90.00	179.61	8,950.00	-3,727.26	-267.91	3,738.68	0.00	0.00	0.00
12,500.00	90.00	179.61	8,950.00	-3,827.25	-267.23	3,838.49	0.00	0.00	0.00
12,600.00	90.00	179.61	8,950.00	-3,927.25	-266.55	3,938.30	0.00	0.00	0.00
12,700.00	90.00	179.61	8,950.00	-4,027.25	-265.87	4,038.11	0.00	0.00	0.00
12,800.00	90.00	179.61	8,950.00	-4,127.25	-265.19	4,137.93	0.00	0.00	0.00
12,900.00	90.00	179.61	8,950.00	-4,227.24	-264.51	4,237.74	0.00	0.00	0.00
13,000.00	90.00	179.61	8,950.00	-4,327.24	-263.83	4,337.55	0.00	0.00	0.00
13,100.00	90.00	179.61	8,950.00	-4,427.24	-263.14	4,437.36	0.00	0.00	0.00



Planning Report



Database: Compass 5000 GCR
Company: Chevron
Project: Lea County, NM (NAD27 NME)
Site: SD WE
Well: 23 Fed P5 1H
Wellbore: Wellbore #1
Design: Plan 1 04-06-15

Local Co-ordinate Reference: Site SD WE
TVD Reference: RKB @ 3190.00usft (TBD)
MD Reference: RKB @ 3190.00usft (TBD)
North Reference: Grid
Survey Calculation Method: Minimum Curvature

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
13,200.00	90.00	179.61	8,950.00	-4,527.24	-262.46	4,537.17	0.00	0.00	0.00
13,300.00	90.00	179.61	8,950.00	-4,627.23	-261.78	4,636.99	0.00	0.00	0.00
13,400.00	90.00	179.61	8,950.00	-4,727.23	-261.10	4,736.80	0.00	0.00	0.00
13,500.00	90.00	179.61	8,950.00	-4,827.23	-260.42	4,836.61	0.00	0.00	0.00
13,600.00	90.00	179.61	8,950.00	-4,927.23	-259.74	4,936.42	0.00	0.00	0.00
13,700.00	90.00	179.61	8,950.00	-5,027.23	-259.06	5,036.23	0.00	0.00	0.00
13,800.00	90.00	179.61	8,950.00	-5,127.22	-258.38	5,136.05	0.00	0.00	0.00
13,855.78	90.00	179.61	8,950.00	-5,183.00	-258.00	5,191.72	0.00	0.00	0.00
TD at 13855.78									

Design Targets

Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
- hit/miss target									
- Shape									
BHL 23 Fed P5 1H	0.00	0.00	8,950.00	-5,183.00	-258.00	372,128.00	710,959.00	32° 1' 16.56274 N	103° 39' 9.57116 W
- plan hits target center									
- Point									

Plan Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
2,300.00	2,300.00	1.00	25.00	Start Build 1.00°/100'
2,590.09	2,589.96	-0.96	17.92	Hold 2.9° Inc at 254.53° Azm
8,487.06	8,479.38	-80.54	-269.70	KOP: Start Build-Turn 12°/100'
9,230.78	8,950.00	-558.11	-289.48	LP: 90° Inc at 179.61° Azm
13,855.78	8,950.00	-5,183.00	-258.00	TD at 13855.78

BLOWOUT PREVENTOR SCHEMATIC

Minimum Requirements

OPERATION : Intermediate and Production Hole Sections

Minimum System

Pressure Rating : 5,000 psi


SIZE	PRESSURE	DESCRIPTION
A	N/A	Bell Nipple
B	13 5/8" 5,000 psi	Annular
C	13 5/8" 5,000 psi	Pipe Ram
D	13 5/8" 5,000 psi	Blind Ram
E	13 5/8" 5,000 psi	Mud Cross
F		
DSA	As required for each hole size	
C-Sec		
B-Sec	13-5/8" 5K x 11" 5K	
A-Sec	13-3/8" SOW x 13-5/8" 5K	

Kill Line

SIZE	PRESSURE	DESCRIPTION
2"	5,000 psi	Gate Valve
2"	5,000 psi	Gate Valve
2"	5,000 psi	Check Valve

Choke Line

SIZE	PRESSURE	DESCRIPTION
3"	5,000 psi	Gate Valve
3"	5,000 psi	HCR Valve

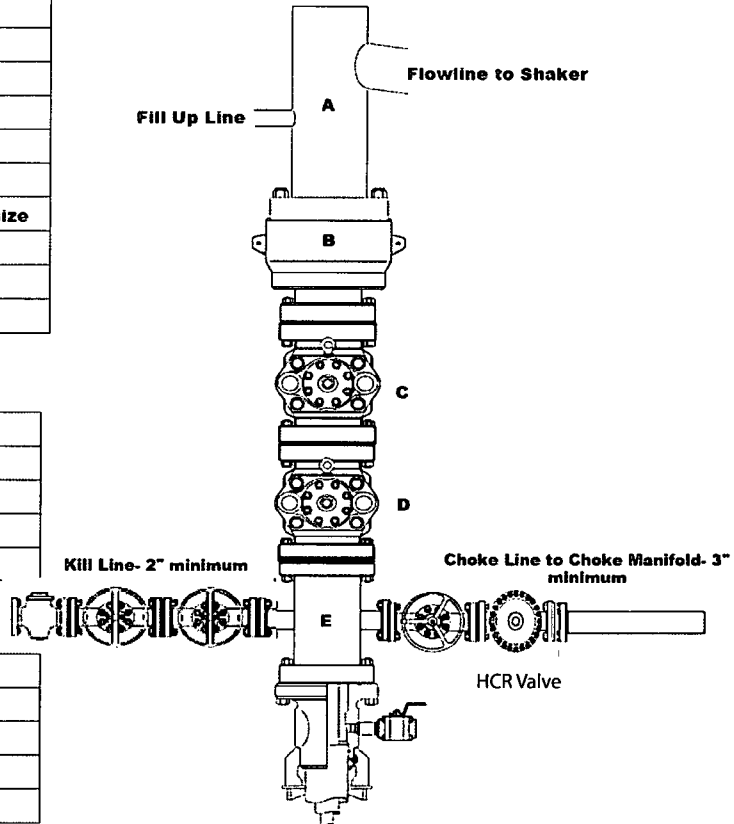

Installation Checklist

The following item must be verified and checked off prior to pressure testing of BOP equipment.

- ☐ The installed BOP equipment meets at least the minimum requirements (rating, type, size, configuration) as shown on this schematic. Components may be substituted for equivalent equipment rated to higher pressures. Additional components may be put into place as long as they meet or exceed the minimum pressure rating of the system.
- ☐ All valves on the kill line and choke line will be full opening and will allow straight through flow.
- ☐ The kill line and choke line will be straight unless turns use tee blocks or are targeted with running tress, and will be anchored to prevent whip and reduce vibration.
- ☐ Manual (hand wheels) or automatic locking devices will be installed on all ram preventers. Hand wheels will also be installed on all manual valves on the choke line and kill line.
- ☐ A valve will be installed in the closing line as close as possible to the annular preventer to act as a locking device. This valve will remain open unless accumulator is inoperative.
- ☐ Upper kelly cock valve with handle will be available on rig floor along with safety valve and subs to fit all drill string connections in use.

After Installation Checklist is complete, fill out the information below and email to Superintendent and Drilling Engineer

Wellname: _____

Representative: _____

Date: _____

CHOKE MANIFOLD SCHEMATIC


Minimum Requirements

OPERATION : Intermediate and Production Hole Sections

Minimum System : 5,000 psi
Pressure Rating :

Choke Manifold

SIZE	PRESSURE	DESCRIPTION
3"	5,000 psi	Panic Line Valves
2"	5,000 psi	Valves on Choke Lines

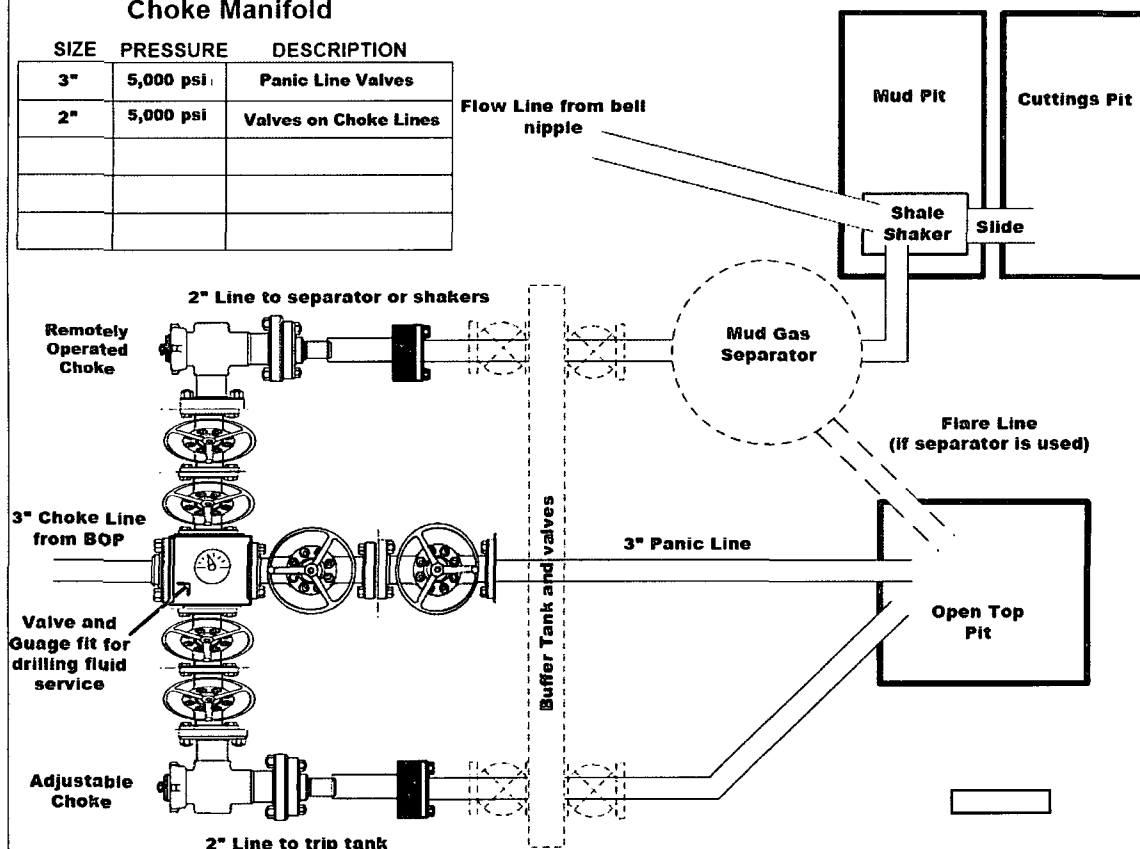

Installation Checklist

The following item must be verified and checked off prior to pressure testing of BOP equipment.

- ☐ The installed BOP equipment meets at least the minimum requirements (rating, type, size, configuration) as shown on this schematic. Components may be substituted for equivalent equipment rated to higher pressures. Additional components may be put into place as long as they meet or exceed the minimum pressure rating of the system.
- ☐ Adjustable Chokes may be Remotely Operated but will have backup hand pump for hydraulic actuation in case of loss of rig air pressure or power.
- ☐ Flare and Panic lines will terminate a minimum of 150' from the wellhead. These lines will terminate at a location as per approved APD.
- ☐ The choke line, kill line, and choke manifold lines will be straight unless turns use tee blocks or are targeted with running tress, and will be anchored to prevent whip and reduce vibration. This excludes the line between mud gas separator and shale shaker.
- ☐ All valves (except chokes) on choke line, kill line, and choke manifold will be full opening and will allow straight through flow. This excludes any valves between mud gas separator and shale shakers.
- ☐ All manual valves will have hand wheels installed.
- ☐ If used, flare system will have effective method for ignition
- ☐ All connections will be flanged, welded, or clamped (no threaded connections like hammer unions)
- ☐ If buffer tank is used, a valve will be used on all lines at any entry or exit point to or from the buffer tank.

After Installation Checklist is complete, fill out the information below and email to Superintendent and Drilling Engineer

Wellname: _____

Representative: _____

Date: _____

BOPE Testing

Minimum Requirements

Closing Unit and Accumulator Checklist

The following item must be performed, verified, and checked off at least once per well prior to low/high pressure testing of BOP equipment. This must be repeated after 6 months on the same well.

- ☐ Precharge pressure for each accumulator bottle must fall within the range below. Bottles may be further charged with nitrogen gas only. Tested precharge pressures must be recorded for each individual bottle and kept on location through the end of the well. Test will be conducted prior to connecting unit to BOP stack.

Check one that applies	Accumulator working pressure rating	Minimum acceptable operating pressure	Desired precharge pressure	Maximum acceptable precharge pressure	Minimum acceptable precharge pressure
☐	1500 psi	1500 psi	750 psi	800 psi	700 psi
☐	2000 psi	2000 psi	1000 psi	1100 psi	900 psi
☐	3000 psi	3000 psi	1000 psi	1100 psi	900 psi

- ☐ Accumulator will have sufficient capacity to open the hydraulically-controlled choke line valve (if used), close all rams, close the annular preventer, and retain a minimum of 200 psi above the maximum acceptable precharge pressure (see table above) on the closing manifold without the use of the closing pumps. This test will be performed with test pressure recorded and kept on location through the end of the well.
- ☐ Accumulator fluid reservoir will be double the usable fluid volume of the accumulator system capacity. Fluid level will be maintained at manufacturer's recommendations. Usable fluid volume will be recorded. Reservoir capacity will be recorded. Reservoir fluid level will be recorded along with manufacturer's recommendation. All will be kept on location through the end of the well.
- ☐ Closing unit system will have two independent power sources (not counting accumulator bottles) to close the preventers.
- ☐ Power for the closing unit pumps will be available to the unit at all times so that the pumps will automatically start when the closing valve manifold pressure decreases to the pre-set level. It is recommended to check that air line to accumulator pump is "ON" during each tour change.
- ☐ With accumulator bottles isolated, closing unit will be capable of opening the hydraulically-operated choke line valve (if used) plus close the annular preventer on the smallest size drill pipe within 2 minutes and obtain a minimum of 200 psi above maximum acceptable precharge pressure (see table above) on the closing manifold. Test pressure and closing time will be recorded and kept on location through the end of the well.
- ☐ Master controls for the BOPE system will be located at the accumulator and will be capable of opening and closing all preventer and the choke line valve (if used)
- ☐ Remote controls for the BOPE system will be readily accessible (clear path) to the driller and located on the rig floor (not in the dog house). Remote controls will be capable of closing all preventers.
- ☐ Record accumulator tests in drilling reports and IADC sheet

BOPE Test Checklist

The following item must be checked off prior to beginning test

- ☐ BLM will be given at least 4 hour notice prior to beginning BOPE testing
- ☐ Valve on casing head below test plug will be open
- ☐ Test will be performed using clear water.

The following item must be performed during the BOPE testing and then checked off

- ☐ BOPE will be pressure tested when initially installed, whenever any seal subject to test pressure is broken, following related repairs, and at a minimum of 30 days intervals. Test pressure and times will be recorded by a 3rd party on a test chart and kept on location through the end of the well.
- ☐ Test plug will be used
- ☐ Ram type preventer and all related well control equipment will be tested to 250 psi (low) and 5,000 psi (high).
- ☐ Annular type preventer will be tested to 250 psi (low) and 3,500 psi (high).
- ☐ Valves will be tested from the working pressure side with all down stream valves open. The check valve will be held open to test the kill line valve(s)
- ☐ Each pressure test will be held for 10 minutes with no allowable leak off.
- ☐ Master controls and remote controls to the closing unit (accumulator) must be function tested as part of the BOP testing
- ☐ Record BOP tests and pressures in drilling reports and IADC sheet

After Installation Checklist is complete, fill out the information below and email to Superintendent and Drilling Engineer along with any/all BOP and accumulator test charts and reports from 3rd parties.


Wellname: _____

Representative: _____

Date: _____



GE Oil & Gas

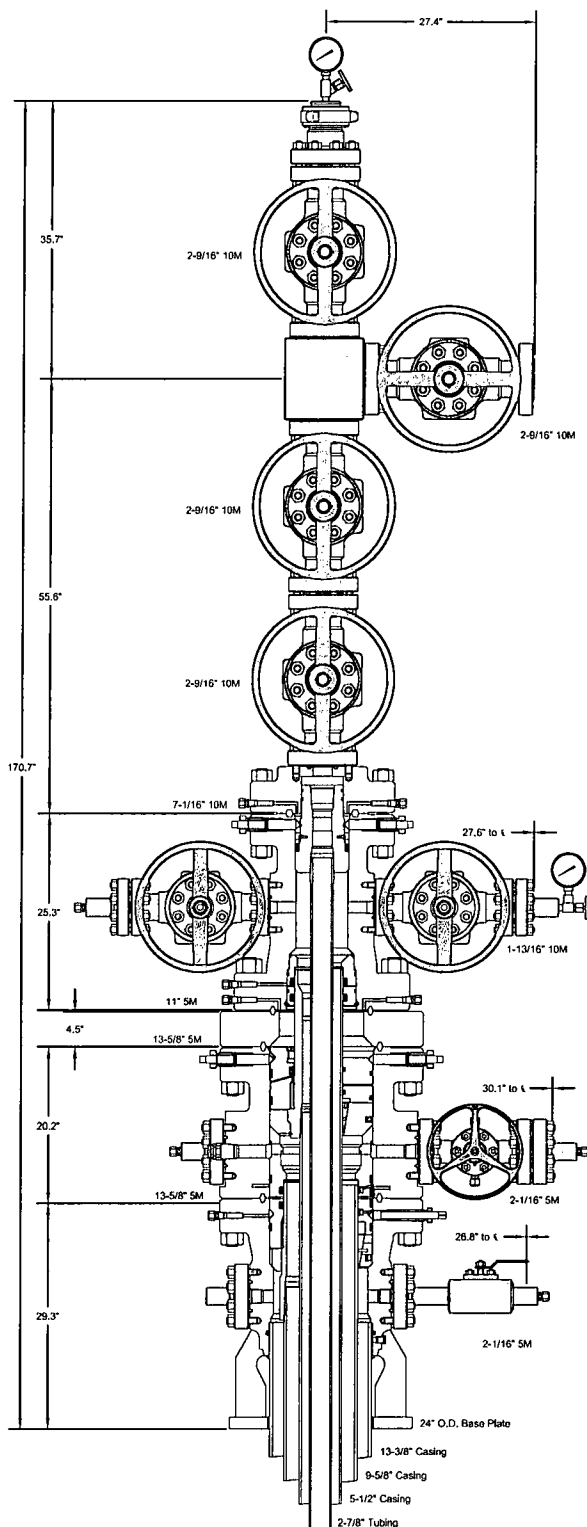

This drawing is the property of GE Oil & Gas Pressure Control LP and is considered confidential. Unless otherwise approved in writing, neither it nor its contents may be used, copied, transmitted or reproduced except for the sole purpose of GE Oil & Gas Pressure Control LP.

CHEVRON USA, INC.
DELAWARE BASIN

13-3/8" x 9-5/8" x 5-1/2" x 2-7/8" 10M SH2/Conventional
Wellhead Assembly, With DSA, T-EBS-F Tubing Head,
T-EN Tubing Hanger and A5PEN Adapter Flange

DRAWN	VJK	19MAR13
APPRV	KN	19MAR13

FOR REFERENCE ONLY

DRAWING NO.

AE23705

Nabors Pace X Section 14 - 23 5th Pad

Exhibit D

