

ATS-15-1009

Form 3160-3
(March 2012)UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT**UNORTHODOX
LOCATION****APPLICATION FOR PERMIT TO DRILL OR REENTER**FORM APPROVED
OMB No. 1004-0137
Expires October 31, 20145. Lease Serial No. Units J&O: LC-054687
SL:LC-029509B; BL:NM-3157126. If Indian, Allottee or Tribe Name
N/A7. If Unit or CA Agreement, Name and No.
N/A8. Lease Name and Well No.
Ragnar Federal Com #15H

9. API Well No.

30-025-43114

10. Field and Pool, or Exploratory
Maljamar; Yeso, West11. Sec., T. R. M. or Blk. and Survey or Area
Sec 22 & 15, T17S, R32E12. County or Parish
LEA13. State
NM1a. Type of work: ☒ DRILL ☐ REENTER1b. Type of Well: ☒ Oil Well ☐ Gas Well ☐ Other ☒ Single Zone ☐ Multiple Zone

2. Name of Operator COG Operating LLC (229137)

3a. Address One Concho Center, 600 W. Illinois Ave
Midland, TX 797013b. Phone No. (include area code)
432-685-4285

4. Location of Well (Report location clearly and in accordance with any State requirements.)*

At surface SHL: 205' FNL & 2498' FEL, Unit B, Sec 22

At proposed prod. zone BHL: 330' FNL & 2304' FEL, Unit B, Sec 15

14. Distance in miles and direction from nearest town or post office*
2 miles from Loco Hills, NM15. Distance from proposed*
location to nearest
property or lease line, ft.
(Also to nearest drig. unit line, if any)
205'16. No. of acres in lease
SHL: 520; Units J&O: 400;
BHL: 76017. Spacing Unit dedicated to this well
16018. Distance from proposed location*
to nearest well, drilling, completed,
applied for, on this lease, ft.
738.319. Proposed Depth
TVD: 5669' MD: 10709'
EOC: 5750' TVD20. BLM/BIA Bond No. on file
NMB000740; NMB00021521. Elevations (Show whether DF, KDB, RT, GL, etc.)
4015' GL22. Approximate date work will start*
12/30/201523. Estimated duration
15 Days

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. I, must be attached to this form:

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).
- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification
- Such other site specific information and/or plans as may be required by the BLM.

25. Signature

Name (Printed Typed)
Kelly J. HollyDate
08/28/2015

Title

Permitting Tech

Approved by (Signature) /Cody Layton

Name (Printed Typed)

Date
NOV 17 2015

Title

FIELD MANAGER

Office

CARLSBAD FIELD OFFICE

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.**APPROVAL FOR TWO YEARS**

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)

Roswell Controlled Water Basin

K2
03/09/16

E-PERM K2

MAR 09 2016

**COG Operating LLC
Ragnar Federal Com #15H**

HOBBS OCD

MAR 09 2016

1. Geologic Formations

TVD of target	5750'	Pilot hole depth	NA
MD at TD:	10709'	Deepest expected fresh water:	132'

RECEIVED

Back Reef

Formation	Depth (TVD) from KB	Water/Mineral Bearing/ Target Zone?	Hazards*
Quaternary Fill	Surface	Fresh Water	
Rustler	850'	Brackish Water	
Top of Salt	1063'	Salt	
Tansill	2063'	Barren	
Yates	2170'	Oil/Gas	
Seven Rivers	2529'	Oil/Gas	
Queen	3126'	Oil/Gas	
Grayburg	3525'	Oil/Gas	
San Andres	3911'	Oil/Gas	
Glorieta	5410'	Oil/Gas	
Paddock	5489'	Target	
Blinberry	5985'	Will Not Penetrate	

*H2S, water flows, loss of circulation, abnormal pressures, etc.

2. Casing Program

Hole Size	Casing Interval		Csg. Size	Weight (lbs)	Grade	Conn.	SF Collapse	SF Burst	SF Tension
	From	To							
17.5"	0	875'	13.375"	48	H40/J55	STC	1.85	1.60	7.67
12.25"	0	2083'	9.625"	40	J55	STC	2.37	1.44	5.42
8.75"	0	5229'	5.5"	17	L80	LTC	2.51	1.33	3.28
8.75"	5229'	6057'	5.5"	17	L80	LTC	2.29	1.33	3.63
7.875"	6057'	10709'	5.5"	17	L80	LTC	2.29	1.33	4.27
BLM Minimum Safety Factor							1.125	1	1.6 Dry 1.8 Wet

All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h

BLM standard formulas where used on all SF calculations

Assumed 9.2 ppg MW equivalent pore pressure from 9 5/8" shoe to Deepest TVD in wellbore.

COG Operating LLC
Ragnar Federal Com #15H

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	Y
Is casing API approved? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	N
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	N
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is well within the designated 4 string boundary.	N
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	N
If yes, are the first three strings cemented to surface?	
Is 2 nd string set 100' to 600' below the base of salt?	
Is well located in high Cave/Karst?	N
If yes, are there two strings cemented to surface?	
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	

3. Cementing Program

Casing	# Sks	Wt. lb/gal	Yld ft3/sk	H ₂ O gal/sk	500 psi Comp. Strength (hours)	Slurry Description
Surf. Single Stage	275	13.5	1.75	9.2	13	Lead: Class C + 4% Gel + 2% CaCl ₂ + 0.25 pps CF
	375	14.8	1.32	6.3	6	Tail: Class C + 2% CaCl ₂ + 0.25 pps Celloflake
Inter. Single stage	325	11.8	2.45	14.4	72	Lead: 50:50:10 C: Poz:Gel w/ 5% Salt + 5 pps LCM + 0.25 pps Cello flake
	250	14.8	1.32	6.3	6	Tail: Class C w/ 2% CaCl ₂

**COG Operating LLC
Ragnar Federal Com #15H**

IF DV Tool +/- 925'						
Inter. Multi- Stage	150	11.8	2.45	14.4	72	1 st stage Lead: 50:50:10 C: Poz:Gel w/ 5% Salt + 5 pps Lcm + 0.25 pps Cello flake
	225	14.8	1.32	6.3	6	1 st stage Tail: Class C w/ 2% CaCl2
	200	11.8	2.45	14.4	72	2nd stage Lead: 50:50:10 C: Poz:Gel w/ 5% Salt + 5 pps LCM + 0.25 pps Cello flake
Prod. Single Stage	900	12.5	2.01	11.4	22	Lead: 35:65:6 C:Poz Gel w/5% salt + 5 pps LCM + 0.2% SMS + 1% FL-25 + 1% Ba-58+0.3% FL-52A + 0.125 pps CF
	1000	14	1.37	6.4	10	Tail: 50:50:2 C:Pox Gel w/5% salt+3 pps LCM + 0.6% SMS + 1% FL-25 +1% BA-58+ 0.125 pps CF
IF DV/ECP Tool +/- 4011'						
Prod Multi- Stage	700	12.5	2.01	11.4	22	2 nd Stage Lead: 35:65:6 C:Poz Gel w/5% salt+5 pps LCM+0.2% SMS + 1% FL-25+1% BA-58+0.3% FL-52A+ 0.125 pps CF
	150	16.8	.99	4.8	6	2 nd Stage Tail: Class"C" w/0.3% R-3 + 1.5% CD-32
	200	12.5	2.01	11.4	22	1 st stage Lead: 35:65:6 C: PozGel w/5% salt + 5 pps LCM + 0.2% SMS + 1% FL-25+ 1% BA-58 + 0.3% FL-52A + 0.125 pps CF
	1000	14	1.37	6.4	10	1 st stage Tail: 50:50:2 C: PozGel w/5% salt + 3 pps LCM + 0.6% SMS + 1% FL-25 + 1% BA-58 + 0.125 pps CF

Casing String	TOC	% Excess
Surface	0'	50%
Intermediate	0'	50%
Production	0'	35%

4. Pressure Control Equipment * See attachment for further details*****

No	A variance is requested for the use of a diverter on the surface casing. See attached for schematic.
----	--

COG Operating LLC
Ragnar Federal Com #15H

BOP installed and tested before drilling which hole?	Size?	Min Required WP	Type	✓	Tested to:
12-1/4"	13-5/8"	2M	Annular	X	2000 psi
			Blind Ram		
			Pipe Ram		
			Double Ram		
			Other*		
8-3/4" & 7 7/8"	13-5/8"	2M	Annular	X	2000 psi
			Blind Ram		
			Pipe Ram		
			Double Ram		
			Other*		

*Specify if additional ram is utilized.

BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all the components installed will be functional and tested.

Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold. See attached schematics.

NA	Formation integrity test will be performed per Onshore Order #2. On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i.
NA	A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart.
NA	Are anchors required by manufacturer?
NA	A multibowl wellhead is being used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested. Provide description here See attached schematic.

COG Operating LLC
Ragnar Federal Com #15H

5. Mud Program

Depth		Type	Weight (ppg)	Viscosity	Water Loss
From	To				
0	Surf. shoe	FW Gel	8.6-8.8	28-34	N/C
Surf shoe	Int shoe	Saturated Brine	10.0-10.2	28-34	N/C
Int shoe	TD	FW-Cut Brine	8.5-9.2	28-34	N/C

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times.

What will be used to monitor the loss or gain of fluid?	PVT/Pason/Visual Monitoring
---	-----------------------------

6. Logging and Testing Procedures

Logging, Coring and Testing	
X	Will run Cased hole GR/CNL/CCL from KOP to surface. Stated logs run will be in the Completion Report and submitted to the BLM.
No	Open hole logs are planned from KOP to Intermediate casing shoe.
No	Drill stem test? If yes, explain
No	Coring? If yes, explain

Additional logs planned	Interval
	Resistivity
	Density
	CBL
X	Mud log
	PEX/HRLA/HNGS
	Int. shoe to KOP
	Int. shoe to KOP
	Production casing
	Intermediate shoe to TD
	Intermediate shoe to KOP

7. Drilling Conditions

Condition	Specify what type and where?
BH Pressure at deepest TVD	2530 psi
Abnormal Temperature	No

Mitigation measure for abnormal conditions.

**COG Operating LLC
Ragnar Federal Com #15H**

Hydrogen Sulfide (H2S) monitors will be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the operator will comply with the provisions of Onshore Oil and Gas Order #6. If Hydrogen Sulfide is encountered, measured values and formations will be provided to the BLM.	
NO	H2S is present
Yes	H2S Plan attached

8. Other facets of operation

Is this a walking operation? No.
Will be pre-setting casing? No

Attachments:
Directional Plan
Multi-stage Cement details
BOP description

**COG Operating LLC
Ragnar Federal Com #15H**

Multi-stage Cement details:

Discussion of DV Tool cement options:

9 5/8" DV tool cement option is proposed for approval. This may become necessary if lost circulation occurs while drilling the 12 1/4" intermediate hole. DV tool depth will be based on hole conditions. Cement volumes will be adjusted proportionally. DV Tool will be set a minimum of 50 feet below previous casing and a minimum of 200 feet above current shoe.

7" DV tool cement option is proposed for approval. This may become necessary if water flows in the San Andres are encountered. These water flows normally occur in areas where produced water disposal is happening. This dense cement is used to combat water flows. This cement recipe also has a right angle set time and is mixed a little under saturated so the water flow will be absorbed by cement. DV tool depth will be based on hole conditions. Cement volumes will be adjusted proportionally. DV tool will be set a minimum of 50 feet below previous casing and a minimum of 200 feet above current shoe.

Discussion of Pressure Control Equipment:

A 13 5/8" 3000 psi Double ram BOP or 13 5/8" 3000 psi Hydril type annular preventor will be used depending on the rig selected.

The majority of the rigs currently in use by COG have 13 5/8" 3000 psi BOPs (double ram or hydril type) but due to the vagaries of rig scheduling one of the few rigs with 11" BOPs might be used if the intermediate hole size is 11"; therefore, COG Operating LLC requests variance to the requirement of 13 5/8" BOPS on 13 3/8" casing. When the circumstance occurs that a 11" BOP is used on 13 3/8" casing a special flange will be utilized to allow testing the entire BOP with a test plug, without subjecting the casing to test pressure. The special flange also allows return to full-open capability if desired.

In every case COG Operating LLC will use BOP equipment which will meet or exceed well control requirements of Onshore Oil and Gas Order No. 2.

GEG 7/23/15



COG Operating LLC
NEW MEXICO SHELF

LEA COUNTY, NM
MALJAMAR
RAGNAR FED COM #15H

OWB

Plan: PWP0

SHL: 205' FNL, 2498' FEL, SEC. 22, T17S, R32E, UNIT B

PP: 568' FSL, 2310' FEL, SEC. 15, T17S, R32E, UNIT O

BHL: 330' FNL, 2304' FEL, SEC. 15, T17S, R32E, UNIT B

Standard Planning Report

25 March, 2015



COG Operating LLC

Planning Report

Database:	EDM_Users	Local Co-ordinate Reference:	Well RAGNAR FED COM #15H
Company:	NEW MEXICO SHELF	TVD Reference:	RKB=4015+12 @ 4027.0usft (TBD)
Project:	LEA COUNTY, NM	MD Reference:	RKB=4015+12 @ 4027.0usft (TBD)
Site:	MALJAMAR	North Reference:	Grid
Well:	RAGNAR FED COM #15H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Project	LEA COUNTY, NM		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Site	MALJAMAR			
Site Position:		Northing:	675,386.60 usft	Latitude: 32° 51' 19.093 N
From:	Map	Easting:	682,929.80 usft	Longitude: 103° 44' 15.489 W
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "	Grid Convergence: 0.32 °

Well	RAGNAR FED COM #15H			
Well Position	+N/-S	-10,445.4 usft	Northing:	664,941.20 usft
	+E/-W	-4,755.1 usft	Easting:	678,174.70 usft
Position Uncertainty		3.0 usft	Wellhead Elevation:	0.0 usft
			Ground Level:	4,015.0 usft

Wellbore	OWB				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	WMM_2005	12/31/2009	7.88	60.76	49,126

Design	PWP0			
Audit Notes:				
Version:	Phase:	PROTOTYPE	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	5,669.0	0.0	0.0	1.80

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
5,229.1	0.00	0.00	5,229.1	0.0	0.0	0.00	0.00	0.00	0.00	
6,056.5	91.00	15.00	5,750.0	512.0	137.2	11.00	11.00	0.00	15.00	
6,439.5	91.00	359.68	5,743.3	890.7	186.0	4.00	0.00	-4.00	-89.88	
10,708.8	91.00	359.68	5,669.0	5,159.2	162.0	0.00	0.00	0.00	0.00	PBHL-Ragnar Fed Cc



COG Operating LLC

Planning Report

Database:	EDM_Users	Local Co-ordinate Reference:	Well RAGNAR FED COM #15H
Company:	NEW MEXICO SHELF	TVD Reference:	RKB=4015+12 @ 4027.0usft (TBD)
Project:	LEA COUNTY, NM	MD Reference:	RKB=4015+12 @ 4027.0usft (TBD)
Site:	MALJAMAR	North Reference:	Grid
Well:	RAGNAR FED COM #15H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00
1,600.0	0.00	0.00	1,600.0	0.0	0.0	0.0	0.00	0.00	0.00
1,700.0	0.00	0.00	1,700.0	0.0	0.0	0.0	0.00	0.00	0.00
1,800.0	0.00	0.00	1,800.0	0.0	0.0	0.0	0.00	0.00	0.00
1,900.0	0.00	0.00	1,900.0	0.0	0.0	0.0	0.00	0.00	0.00
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.0	0.00	0.00	0.00
2,100.0	0.00	0.00	2,100.0	0.0	0.0	0.0	0.00	0.00	0.00
2,200.0	0.00	0.00	2,200.0	0.0	0.0	0.0	0.00	0.00	0.00
2,300.0	0.00	0.00	2,300.0	0.0	0.0	0.0	0.00	0.00	0.00
2,400.0	0.00	0.00	2,400.0	0.0	0.0	0.0	0.00	0.00	0.00
2,500.0	0.00	0.00	2,500.0	0.0	0.0	0.0	0.00	0.00	0.00
2,600.0	0.00	0.00	2,600.0	0.0	0.0	0.0	0.00	0.00	0.00
2,700.0	0.00	0.00	2,700.0	0.0	0.0	0.0	0.00	0.00	0.00
2,800.0	0.00	0.00	2,800.0	0.0	0.0	0.0	0.00	0.00	0.00
2,900.0	0.00	0.00	2,900.0	0.0	0.0	0.0	0.00	0.00	0.00
3,000.0	0.00	0.00	3,000.0	0.0	0.0	0.0	0.00	0.00	0.00
3,100.0	0.00	0.00	3,100.0	0.0	0.0	0.0	0.00	0.00	0.00
3,200.0	0.00	0.00	3,200.0	0.0	0.0	0.0	0.00	0.00	0.00
3,300.0	0.00	0.00	3,300.0	0.0	0.0	0.0	0.00	0.00	0.00
3,400.0	0.00	0.00	3,400.0	0.0	0.0	0.0	0.00	0.00	0.00
3,500.0	0.00	0.00	3,500.0	0.0	0.0	0.0	0.00	0.00	0.00
3,600.0	0.00	0.00	3,600.0	0.0	0.0	0.0	0.00	0.00	0.00
3,700.0	0.00	0.00	3,700.0	0.0	0.0	0.0	0.00	0.00	0.00
3,800.0	0.00	0.00	3,800.0	0.0	0.0	0.0	0.00	0.00	0.00
3,900.0	0.00	0.00	3,900.0	0.0	0.0	0.0	0.00	0.00	0.00
4,000.0	0.00	0.00	4,000.0	0.0	0.0	0.0	0.00	0.00	0.00
4,100.0	0.00	0.00	4,100.0	0.0	0.0	0.0	0.00	0.00	0.00
4,200.0	0.00	0.00	4,200.0	0.0	0.0	0.0	0.00	0.00	0.00
4,300.0	0.00	0.00	4,300.0	0.0	0.0	0.0	0.00	0.00	0.00
4,400.0	0.00	0.00	4,400.0	0.0	0.0	0.0	0.00	0.00	0.00
4,500.0	0.00	0.00	4,500.0	0.0	0.0	0.0	0.00	0.00	0.00
4,600.0	0.00	0.00	4,600.0	0.0	0.0	0.0	0.00	0.00	0.00
4,700.0	0.00	0.00	4,700.0	0.0	0.0	0.0	0.00	0.00	0.00
4,800.0	0.00	0.00	4,800.0	0.0	0.0	0.0	0.00	0.00	0.00
4,900.0	0.00	0.00	4,900.0	0.0	0.0	0.0	0.00	0.00	0.00
5,000.0	0.00	0.00	5,000.0	0.0	0.0	0.0	0.00	0.00	0.00
5,100.0	0.00	0.00	5,100.0	0.0	0.0	0.0	0.00	0.00	0.00
5,200.0	0.00	0.00	5,200.0	0.0	0.0	0.0	0.00	0.00	0.00
5,229.1	0.00	0.00	5,229.1	0.0	0.0	0.0	0.00	0.00	0.00



COG Operating LLC
Planning Report

Database:	EDM_Users	Local Co-ordinate, Reference:	Well RAGNAR FED COM #15H
Company:	NEW MEXICO SHELF	TVD Reference:	RKB=4015+12 @ 4027.0usft (TBD)
Project:	LEA COUNTY, NM	MD Reference:	RKB=4015+12 @ 4027.0usft (TBD)
Site:	MALJAMAR	North Reference:	Grid
Well:	RAGNAR FED COM #15H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
EST. KOP 5229.1' MD, 5750' TVD, 11°/100'									
5,300.0	7.80	15.00	5,299.8	4.7	1.2	4.7	11.00	11.00	0.00
5,400.0	18.80	15.00	5,397.0	26.8	7.2	27.0	11.00	11.00	0.00
5,500.0	29.79	15.00	5,488.0	66.5	17.8	67.0	11.00	11.00	0.00
5,600.0	40.79	15.00	5,569.5	122.2	32.8	123.2	11.00	11.00	0.00
5,700.0	51.79	15.00	5,638.4	191.9	51.4	193.5	11.00	11.00	0.00
5,800.0	62.79	15.00	5,692.4	273.1	73.2	275.3	11.00	11.00	0.00
5,900.0	73.78	15.00	5,729.4	362.7	97.2	365.6	11.00	11.00	0.00
6,000.0	84.78	15.00	5,747.9	457.5	122.6	461.1	11.00	11.00	0.00
6,056.5	91.00	15.00	5,750.0	512.0	137.2	516.0	11.00	11.00	0.00
EOC, 6056.5' MD, 91° INC, 15° AZI									
6,100.0	91.00	13.26	5,749.2	554.1	147.8	558.5	4.00	0.02	-4.00
6,200.0	91.01	9.26	5,747.5	652.2	167.3	657.1	4.00	0.00	-4.00
6,300.0	91.01	5.26	5,745.7	751.3	180.0	756.6	4.00	0.00	-4.00
6,322.0	91.01	4.38	5,745.3	773.3	181.8	778.6	4.00	0.00	-4.00
PP 6322' MD									
6,400.0	91.00	1.26	5,744.0	851.1	185.6	856.6	4.00	-0.01	-4.00
6,439.5	91.00	359.68	5,743.3	890.7	186.0	896.1	4.00	-0.01	-4.00
6,500.0	91.00	359.68	5,742.2	951.1	185.6	956.5	0.00	0.00	0.00
6,600.0	91.00	359.68	5,740.5	1,051.1	185.1	1,056.4	0.00	0.00	0.00
6,700.0	91.00	359.68	5,738.8	1,151.1	184.5	1,156.3	0.00	0.00	0.00
6,800.0	91.00	359.68	5,737.0	1,251.1	183.9	1,256.2	0.00	0.00	0.00
6,900.0	91.00	359.68	5,735.3	1,351.1	183.4	1,356.2	0.00	0.00	0.00
7,000.0	91.00	359.68	5,733.5	1,451.0	182.8	1,456.1	0.00	0.00	0.00
7,100.0	91.00	359.68	5,731.8	1,551.0	182.3	1,556.0	0.00	0.00	0.00
7,200.0	91.00	359.68	5,730.1	1,651.0	181.7	1,655.9	0.00	0.00	0.00
7,300.0	91.00	359.68	5,728.3	1,751.0	181.1	1,755.8	0.00	0.00	0.00
7,400.0	91.00	359.68	5,726.6	1,851.0	180.6	1,855.7	0.00	0.00	0.00
7,500.0	91.00	359.68	5,724.8	1,951.0	180.0	1,955.6	0.00	0.00	0.00
7,600.0	91.00	359.68	5,723.1	2,050.9	179.4	2,055.6	0.00	0.00	0.00
7,700.0	91.00	359.68	5,721.4	2,150.9	178.9	2,155.5	0.00	0.00	0.00
7,800.0	91.00	359.68	5,719.6	2,250.9	178.3	2,255.4	0.00	0.00	0.00
7,900.0	91.00	359.68	5,717.9	2,350.9	177.8	2,355.3	0.00	0.00	0.00
8,000.0	91.00	359.68	5,716.1	2,450.9	177.2	2,455.2	0.00	0.00	0.00
8,100.0	91.00	359.68	5,714.4	2,550.9	176.6	2,555.1	0.00	0.00	0.00
8,200.0	91.00	359.68	5,712.7	2,650.8	176.1	2,655.1	0.00	0.00	0.00
8,300.0	91.00	359.68	5,710.9	2,750.8	175.5	2,755.0	0.00	0.00	0.00
8,400.0	91.00	359.68	5,709.2	2,850.8	175.0	2,854.9	0.00	0.00	0.00
8,500.0	91.00	359.68	5,707.4	2,950.8	174.4	2,954.8	0.00	0.00	0.00
8,600.0	91.00	359.68	5,705.7	3,050.8	173.8	3,054.7	0.00	0.00	0.00
8,700.0	91.00	359.68	5,704.0	3,150.8	173.3	3,154.6	0.00	0.00	0.00
8,800.0	91.00	359.68	5,702.2	3,250.7	172.7	3,254.6	0.00	0.00	0.00
8,900.0	91.00	359.68	5,700.5	3,350.7	172.2	3,354.5	0.00	0.00	0.00
9,000.0	91.00	359.68	5,698.7	3,450.7	171.6	3,454.4	0.00	0.00	0.00
9,100.0	91.00	359.68	5,697.0	3,550.7	171.0	3,554.3	0.00	0.00	0.00
9,200.0	91.00	359.68	5,695.3	3,650.7	170.5	3,654.2	0.00	0.00	0.00
9,300.0	91.00	359.68	5,693.5	3,750.7	169.9	3,754.1	0.00	0.00	0.00
9,400.0	91.00	359.68	5,691.8	3,850.6	169.3	3,854.1	0.00	0.00	0.00
9,500.0	91.00	359.68	5,690.0	3,950.6	168.8	3,954.0	0.00	0.00	0.00
9,600.0	91.00	359.68	5,688.3	4,050.6	168.2	4,053.9	0.00	0.00	0.00
9,700.0	91.00	359.68	5,686.6	4,150.6	167.7	4,153.8	0.00	0.00	0.00
9,800.0	91.00	359.68	5,684.8	4,250.6	167.1	4,253.7	0.00	0.00	0.00
9,900.0	91.00	359.68	5,683.1	4,350.6	166.5	4,353.6	0.00	0.00	0.00



COG Operating LLC

Planning Report

Database:	EDM_Users	Local Co-ordinate Reference:	Well RAGNAR FED COM #15H
Company:	NEW MEXICO SHELF	TVD Reference:	RKB=4015+12 @ 4027.0usft (TBD)
Project:	LEA COUNTY, NM	MD Reference:	RKB=4015+12 @ 4027.0usft (TBD)
Site:	MALJAMAR	North Reference:	Grid
Well:	RAGNAR FED COM #15H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/S (usft)	+E/W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
10,000.0	91.00	359.68	5,681.3	4,450.5	166.0	4,453.6	0.00	0.00	0.00	
10,100.0	91.00	359.68	5,679.6	4,550.5	165.4	4,553.5	0.00	0.00	0.00	
10,200.0	91.00	359.68	5,677.9	4,650.5	164.9	4,653.4	0.00	0.00	0.00	
10,300.0	91.00	359.68	5,676.1	4,750.5	164.3	4,753.3	0.00	0.00	0.00	
10,400.0	91.00	359.68	5,674.4	4,850.5	163.7	4,853.2	0.00	0.00	0.00	
10,500.0	91.00	359.68	5,672.6	4,950.5	163.2	4,953.1	0.00	0.00	0.00	
10,600.0	91.00	359.68	5,670.9	5,050.4	162.6	5,053.1	0.00	0.00	0.00	
10,700.0	91.00	359.68	5,669.2	5,150.4	162.0	5,153.0	0.00	0.00	0.00	
10,708.8	91.00	359.68	5,669.0	5,159.2	162.0	5,161.7	0.00	0.00	0.00	
PBHL 10,708.8' MD, 5669' TVD										

Design Targets										
Target Name	Dip Angle (°)	Dip Dir (°)	TVD (usft)	+N/S (usft)	+E/W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude	
- hit/miss target										
- Shape										
PBHL-Ragnar Fed Com	0.00	0.00	5,669.0	5,159.2	162.0	670,100.40	678,336.70	32° 50' 27.039 N	103° 45' 9.672 W	
- plan hits target center										
- Point										

Plan Annotations					
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment	
		+N/S (usft)	+E/W (usft)		
5,229.1	5,229.1	0.0	0.0	EST. KOP 5229.1' MD, 5750' TVD, 11°/100'	
6,056.5	5,750.0	512.0	137.2	EOC, 6056.5' MD, 91° INC, 15° AZI	
6,322.0	5,745.3	773.3	181.8	PP 6322' MD	
10,708.8	5,669.0	5,159.2	162.0	PBHL 10,708.8' MD, 5669' TVD	



Project: LEA COUNTY, NM
 Site: MALJAMAR
 Well: RAGNAR FED COM #15H
 Wellbore: OWB
 Design: PWFO

Sec	MD	Inc	Azi	TVD	+N/S	+E/W	SECTION DETAILS			Annotation
							TFace	VSecl	Target	
1	0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.0	0.0	
2	5229.1	0.00	0.00	5229.1	0.0	0.0	0.00	0.0	0.0	EST. KOP 5229.1' MD, 5750' TVD, 11°100'
3	6056.5	91.00	15.00	5750.0	512.0	137.2	0.00	0.0	0.0	EOC, 6056.5' MD, 91° INC, 15° AZI
4	6439.5	91.00	359.68	5743.3	890.7	186.0	0.00	-89.88	896.1	
5	10708.8	91.00	359.68	5669.0	5159.2	162.0	0.00	0.00	5161.7	PBHL 10,708.8' MD, 5669' TVD

LEGEND
 — PWFO



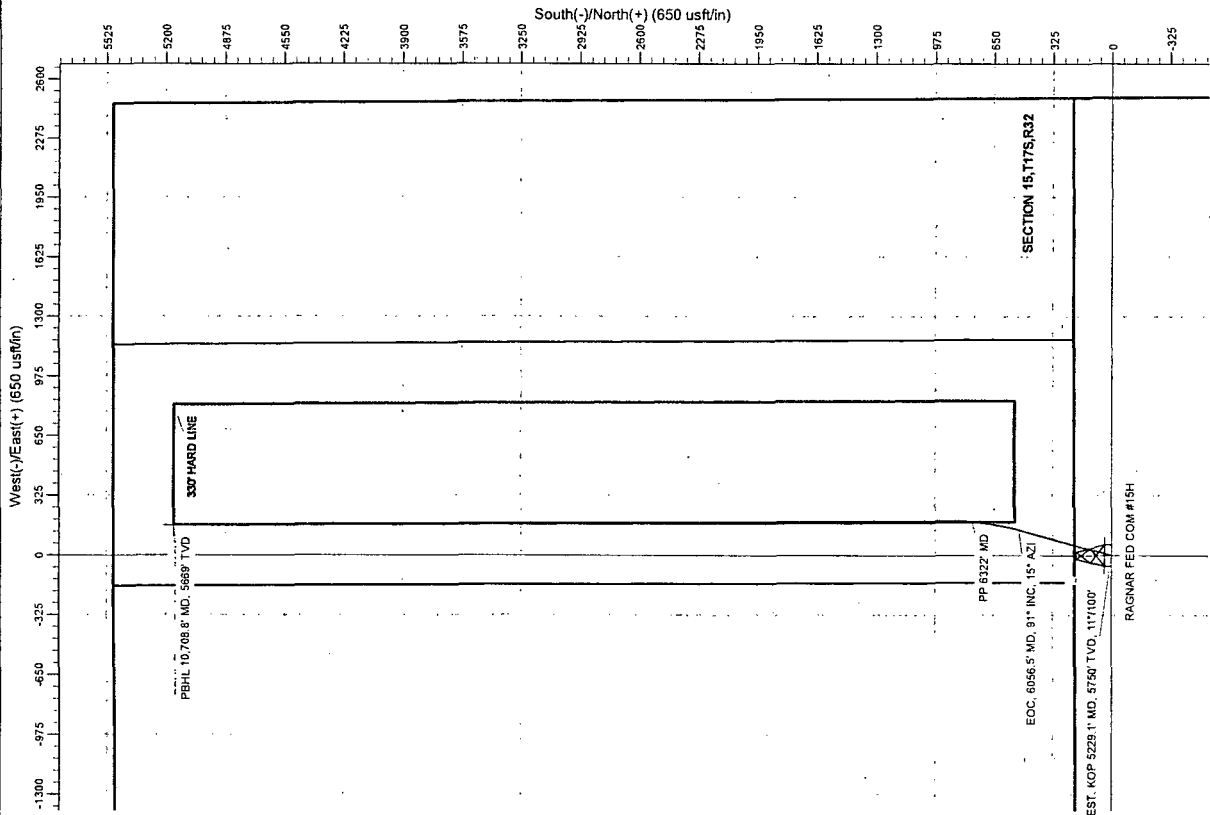


Exhibit #10


(Choke Manifold Schematic same as Exhibit #9)

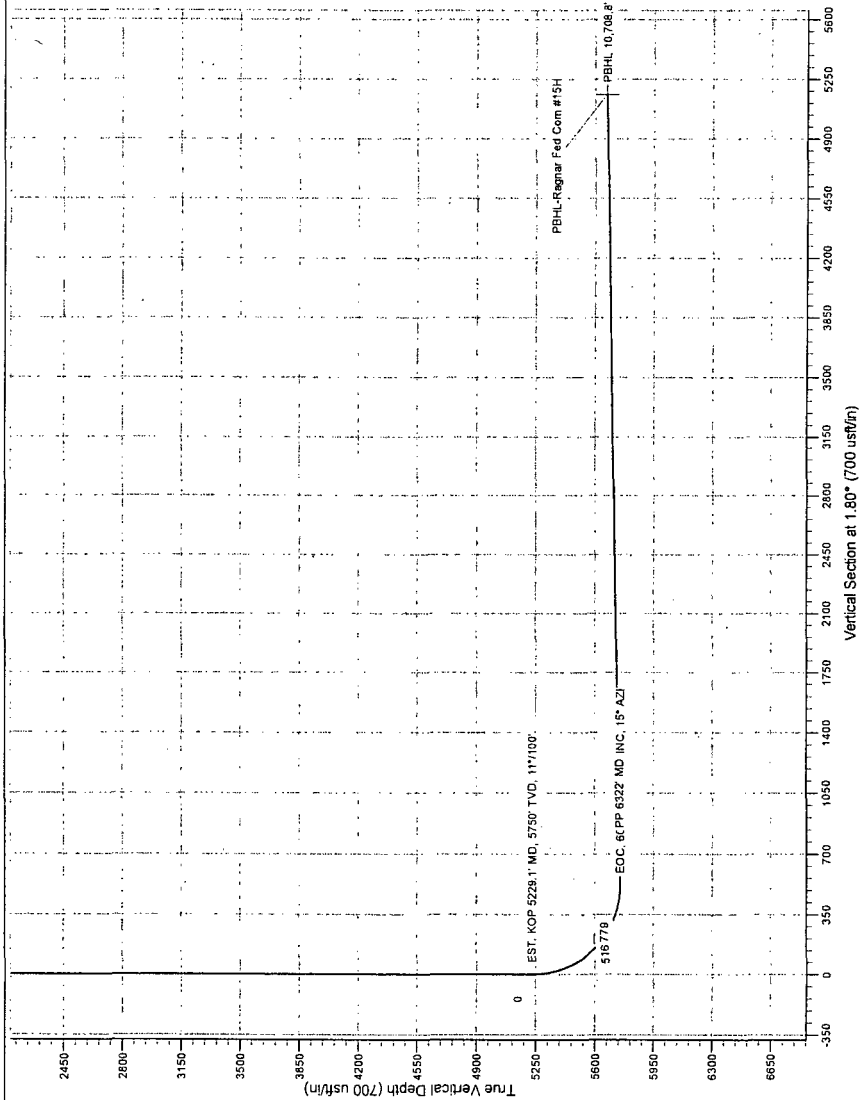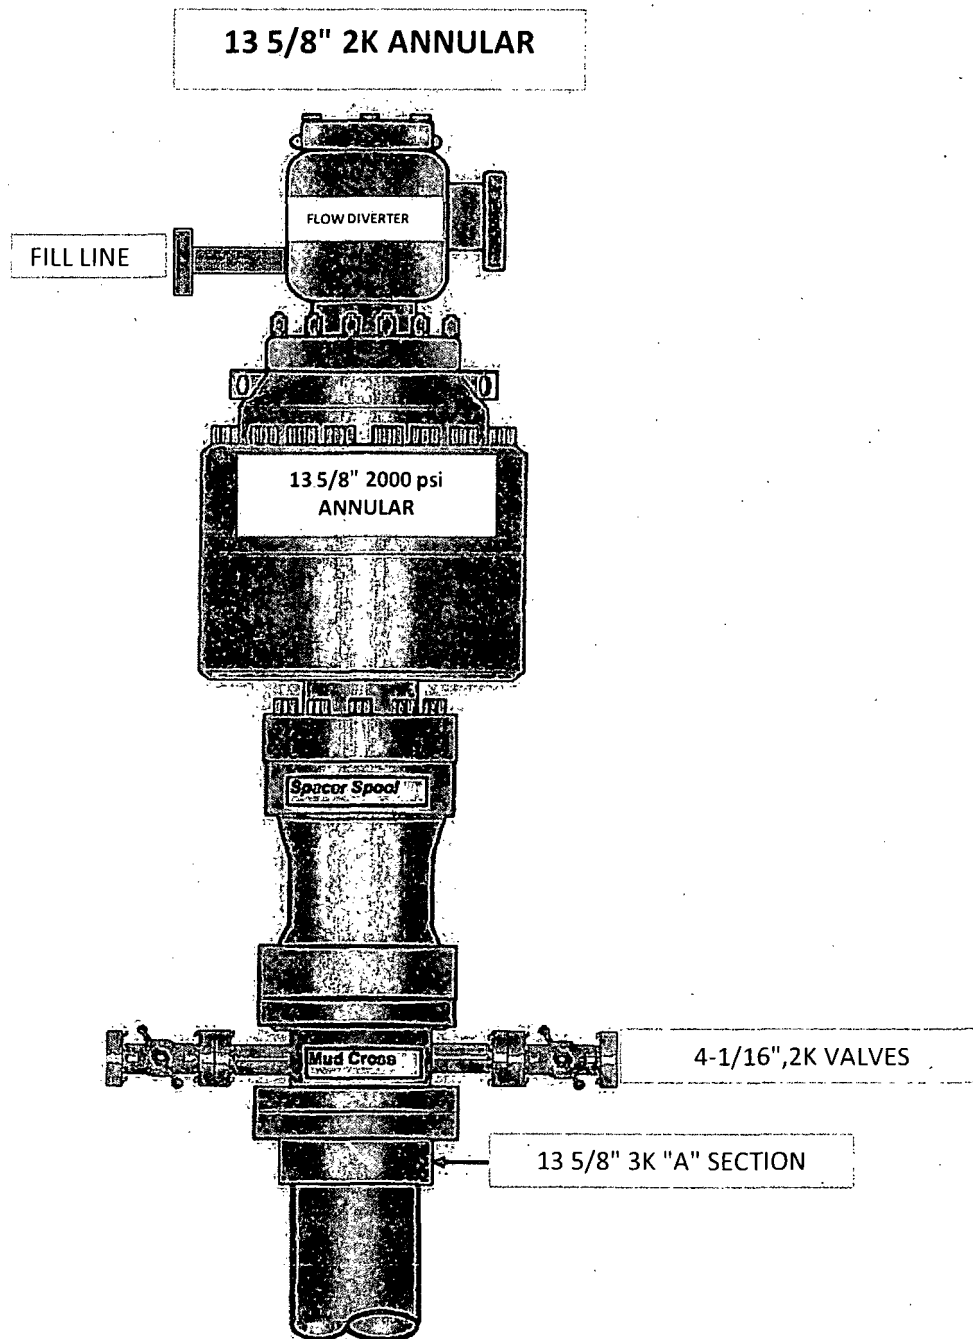


COG Operating LLC

Exhibit #9

BOPE and Choke Schematic

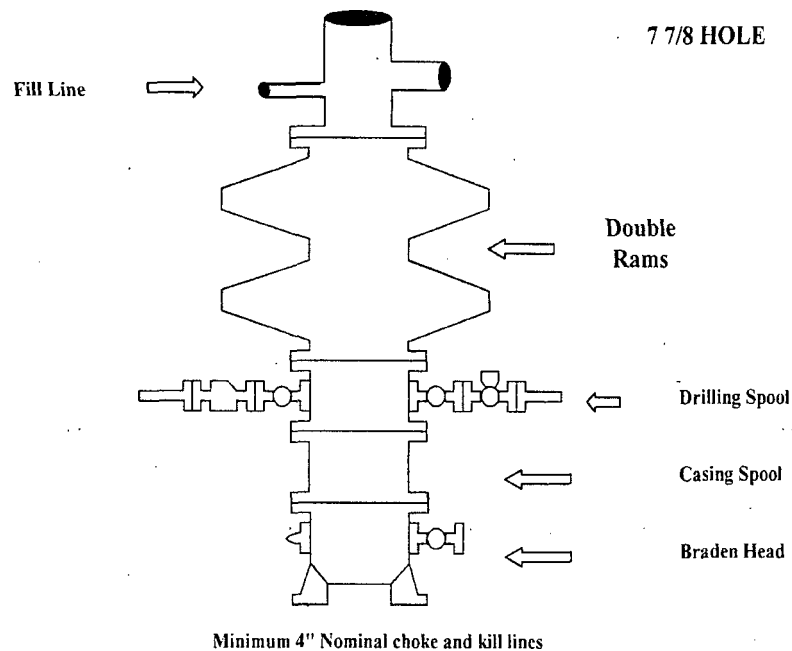

Choke Manifold Requirement (2000 psi WP)
No Annular Required

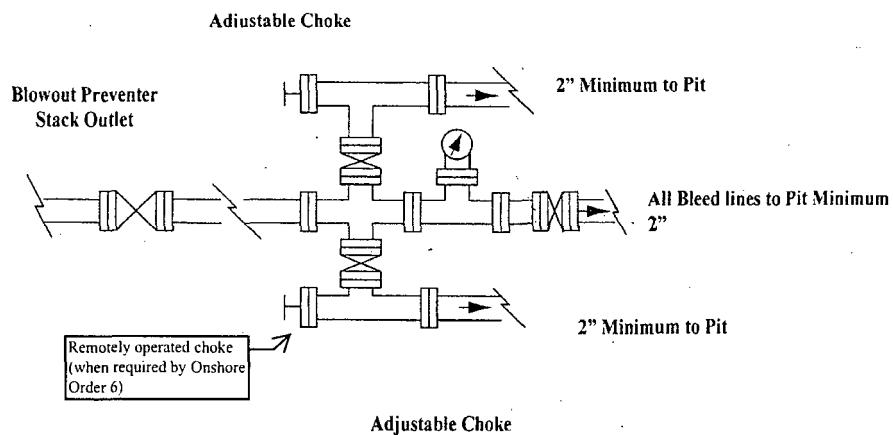

NOTES REGARDING THE BLOWOUT PREVENTERS

**Master Drilling Plan
Eddy County, New Mexico**

1. Drilling nipple to be so constructed that it can be removed without use of a welder through rotary table opening, with minimum I.D. equal to preventer bore.
2. Wear ring to be properly installed in head.
3. Blow out preventer and all fittings must be in good condition, 2000 psi WP minimum.
4. All fittings to be flanged.
5. Safety valve must be available on rig floor at all times with proper connections, valve to be full 2000 psi WP minimum.
6. All choke and fill lines to be securely anchored especially ends of choke lines.
7. Equipment through which bit must pass shall be at least as large as the diameter of the casing being drilled through.
8. Kelly cock on Kelly.
9. Extension wrenches and hands wheels to be properly installed.
10. Blow out preventer control to be located as close to driller's position as feasible.
11. Blow out preventer closing equipment to include minimum 40-gallon accumulator, two independent sources of pump power on each closing unit installation all API specifications.

Closed Loop Operation & Maintenance Procedure

All drilling fluid circulated over shaker(s) with cuttings discharged into roll off container.

Fluid and fines below shaker(s) are circulated with transfer pump through centrifuge(s) or solids separator with cuttings and fines discharged into roll off container.

Fluid is continuously re-circulated through equipment with polymer added to aid separation of cutting fines.

Roll off containers are lined and de-watered with fluids re-circulated into system.

Additional tank is used to capture unused drilling fluid or cement returns from casing jobs.

This equipment will be maintained 24 hrs./day by solids control personnel and or rig crews that stay on location.

Cuttings will be hauled to either:

CRI (permit number R9166)

or

GMI (permit number 711-019-001)

dependent upon which rig is available to drill this well.

COG Operating LLC

Closed Loop Equipment Diagram

