

Submit 1 Copy To Appropriate District
Office
District I - (575) 393-6161
1625 N. French Dr., Hobbs, NM 88240
District II - (575) 748-1283
811 S. First St., Artesia, NM 88210
District III - (505) 334-6178
1000 Rio Brazos Rd., Aztec, NM 87410
District IV - (505) 476-3460
1220 S. St. Francis Dr., Santa Fe, NM
87505

State of New Mexico
Energy, Minerals and Natural Resources

Form C-103
Revised July 18, 2013

OIL CONSERVATION DIVISION

1220 South St. Francis Dr.
Santa Fe, NM 87505

WELL API NO. 30-025-01461
5. Indicate Type of Lease STATE ☒ FEE ☐
6. State Oil & Gas Lease No.
7. Lease Name or Unit Agreement Name CAPROCK MALJAMAR UNIT
8. Well Number 7
9. OGRID Number 269324
10. Pool name or Wildcat MALJAMAR;GRAYBURG-SAN ANDRES
11. Elevation (Show whether DR, RKB, RT, GR, etc.) 4210 GL

SUNDRY NOTICES AND REPORTS ON WELLS

(DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)

1. Type of Well: Oil Well ☐ Gas Well ☒ Other INJECTION

2. Name of Operator
LINN OPERATING, INC.

3. Address of Operator
600 TRAVIS, SUITE 5100, HOUSTON, TEXAS 77002

4. Well Location

Unit Letter G: 1980 feet from the N line and 2080 feet from the E line
Section 18 Township 17S Range 33E NMPM LEA County

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:

PERFORM REMEDIAL WORK ☐ PLUG AND ABANDON ☐
TEMPORARILY ABANDON ☐ C
PULL OR ALTER CASING ☐ M
DOWNHOLE COMMINGLE ☐ INT TO PA
CLOSED-LOOP SYSTEM ☐ P&A NR PM ✓
OTHER: ☐ FAILED MIT P&A R

SUBSEQUENT REPORT OF:

REMEDIAL WORK ☐ ALTERING CASING ☐
COMMENCE DRILLING OPNS. ☐ P AND A ☒
CASING/CEMENT JOB ☐
OTHER: ☐ RETURN TO PRODUCTION

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

LINN PA'd the above mentioned well on 7/25/16. Please see attached Plugging Procedure and Final Well Bore Diagram.

Spud Date:

Rig Release Da

Approved for Plugging of wellbore only. Liability under bond is retained pending restoration and completion of the C-103, Specific for Subsequent Report of Well Plugging, which may be found on the OCD web page under forms.

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE Laura A. Moreno TITLE REGULATORY ADVISOR DATE 7-28-2016

Type or print name LAURA A. MORENO E-mail address: lmoreno@linnenergy.com PHONE: 713-904-6657

For State Use Only

APPROVED BY: M. L. P. S. TITLE P.E.S. DATE 8/2/2016

Conditions of Approval (if any):

CAPROCK MALJAMAR UNIT #007

(30-025-01461)

PA PROCEDURE

7/15/16: MIRU plugging equipment, dug out cellar.

7/18/16: POH 125 jts of 5 ½ csg. Set 5 ½ CIBP @ 4147'. Circulate hole w/mud laden fluid. Spot 25 sx cmt @ 4147 & displaced @3907'.

7/19/16: Perf csg @ 2552', pressured up on perfs. Spot 25 sx cmt @2583-2343 (per Mark Whitaker's approval). WOC. Tag plug @ 2430'. Perf csg @1400', pressure up on perfs. Spot 25 sx cmt @ 1435-1195' (per Mark Whitaker's approval). WOC. Tag plug @ 1240'. Perf csg @ 340'. Sqz 50 sx cmt @ 340 & displaced to 240'. WOC.


7/20/16: Tag plug @ 220'. Perf csg @ 200, pressure up on perfs. Spot 25 sx cmt @ 220 & circulate to surface. RDMO

7/25/16: Move in welder & backhoe. Dug out cellar. Cut off wellhead. Welded on above ground dry hole marker. Backfilled cellar. Removed deadmen, cleaned location, moved off.

Well Name: CAPROCK MALJAMAR UNIT 007

API/UWI 3002501461	Field Name PBNM - PB - CAPROCK MALJAMAR	County Lea	State/Province NM	Section 18	Township 017-S	Range 033-E	Survey	Block
Ground Elevation (ft) 4,225.00	Orig KB Elev (ft) 4,233.00	KB-Grd (ft) 8.00	Initial Spud Date 11/7/1958	Rig Release Date 11/22/1958	TD Date 11/22/1958	Latitude (°) 32° 50' 10.946" N	Longitude (°) 103° 42' 2.73" W	Operated? Yes

Original Hole, 7/27/2016 3:24:46 PM

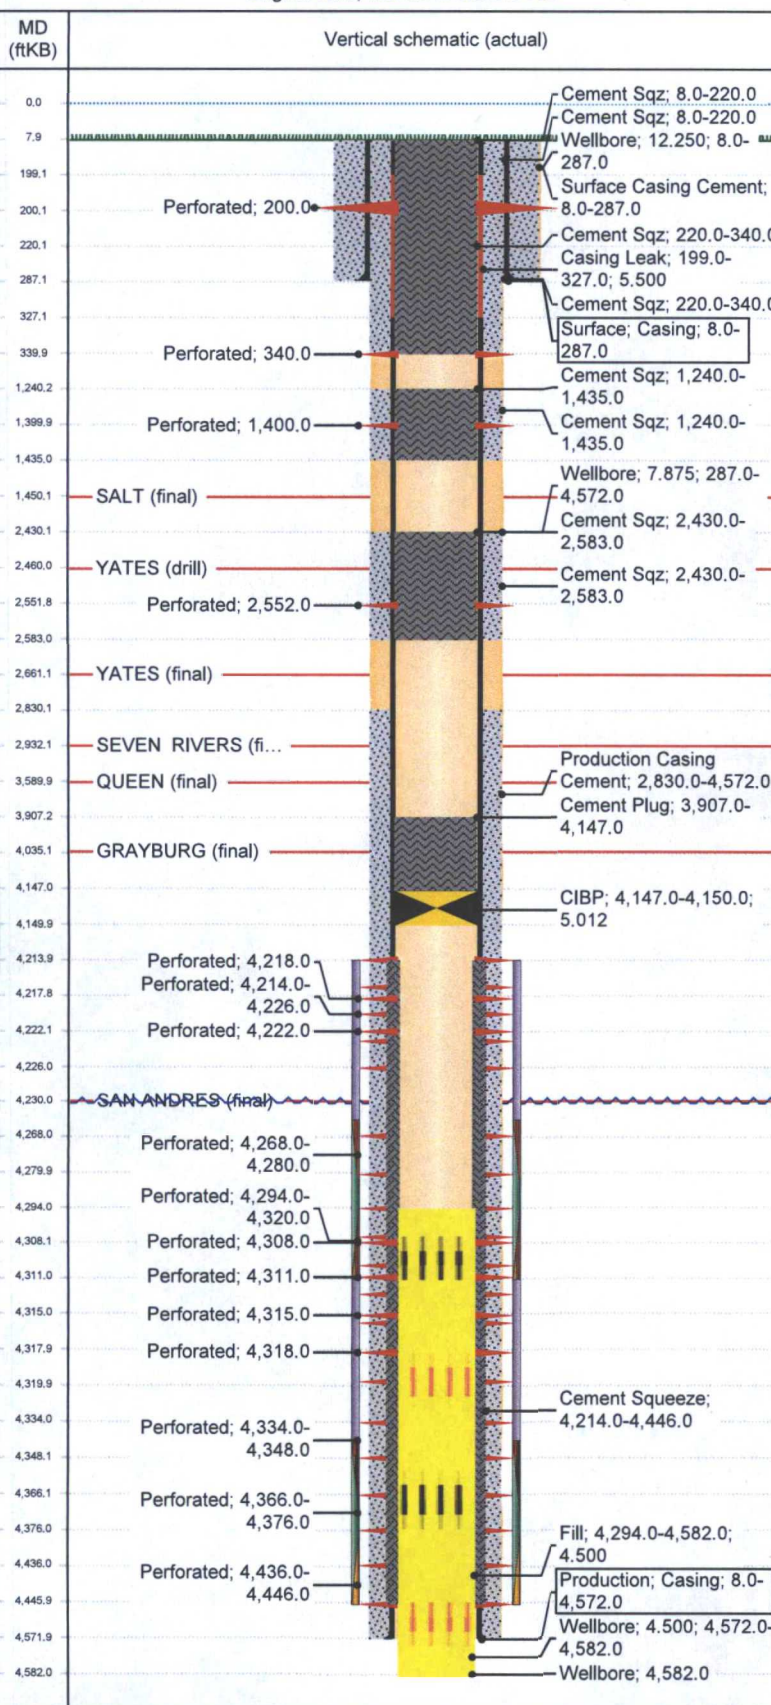

Original Hole Data

Wellbores

North-South Distance (ft) 1,980.0	NS Flag FSL	East-West Distance (ft) 2,080.0	EW Flag FEL
--------------------------------------	----------------	------------------------------------	----------------

Casing Strings

Csg Des	Set Dept...	OD Nom...	ID Nom...	W/Len (l...	String Grade	Run Date
Surface	287.0	8 5/8	8.097	24.00	J-55	11/7/1958
Csg Des	Set Dept...	OD Nom...	ID Nom...	W/Len (l...	String Grade	Run Date
Production	4,572.0	5 1/2	5.012	14.00	J-55	11/22/1958

Cement Stages

Description	Top (ftKB)	Btm (ftKB)	Eval Method	Comment
Production Casing Cement	2,830.0	4,572.0	Calculated	150 sx cmt + 1200 gals Cealment
Casing Cement				filled hole with mud and cement
Production Casing Cement	2,430.0	2,583.0	Calculated	Sqz 25 sks cmt 2583-2430 (Tagged TOC)
Production Casing Cement	1,240.0	1,435.0	Calculated	Sqz 25 sks cmt 1435-1240 (Tagged TOC)
Production Casing Cement	220.0	340.0	Calculated	Sqz 50 sks cmt 340-220 (Tagged TOC)
Production Casing Cement	8.0	220.0	Calculated	Sqz 25 sks cmt 220 - surface
Surface Casing Cement	8.0	287.0	Returns to Surface	150 sx 10.3 ppg mud
Cement Squeeze	4,214.0	4,446.0	Calculated	circ to surface
Cement Plug	3,907.0	4,147.0	Calculated	Comment: CIBP @ 4147' Cap w/ 25 sks cmt plug TOC @ 3907'
Cement Plug	2,430.0	2,583.0	Calculated	Comment: Sqz 25 sks cmt 2583-2430 (Tagged TOC)
Cement Plug	1,240.0	1,435.0	Calculated	Comment: Sqz 25 sks cmt 1435-1240 (Tagged TOC)
Cement Plug	220.0	340.0	Calculated	Comment: Sqz 50 sks cmt 340-220 (Tagged TOC)
Cement Plug	8.0	220.0	Calculated	Comment: Sqz 25 sks cmt 220 - surface

Tubing Strings

Tubing Description	Set Depth...	Run Date	Pull Date
Tubing	4,118.8	3/12/2010	3/10/2015
Tubing Description	Set Depth...	Run Date	Pull Date
Tubing - Production	4,064.0	3/19/2015	3/31/2015

Perforations


Top (ftKB)	Btm (ftKB)	Comment
200.0	200.0	
Top (ftKB)	Btm (ftKB)	Comment
340.0	340.0	
Top (ftKB)	Btm (ftKB)	Comment
1,400.0	1,400.0	
Top (ftKB)	Btm (ftKB)	Comment
2,552.0	2,552.0	
Top (ftKB)	Btm (ftKB)	Comment
4,214.0	4,226.0	

Well Name: CAPROCK MALJAMAR UNIT 007

API/UVI 3002501461	Field Name PBNM - PB - CAPROCK MALJAMAR	County Lea	State/Province NM	Section 18	Township 017-S	Range 033-E	Survey	Block
Ground Elevation (ft) 4,225.00	Orig KB Elev (ft) 4,233.00	KB-Grd (ft) 8.00	Initial Spud Date 11/7/1958	Rig Release Date 11/22/1958	TD Date 11/22/1958	Latitude (°) 32° 50' 10.946" N	Longitude (°) 103° 42' 2.73" W	Operated? Yes

Original Hole, 7/27/2016 3:24:46 PM

Original Hole Data

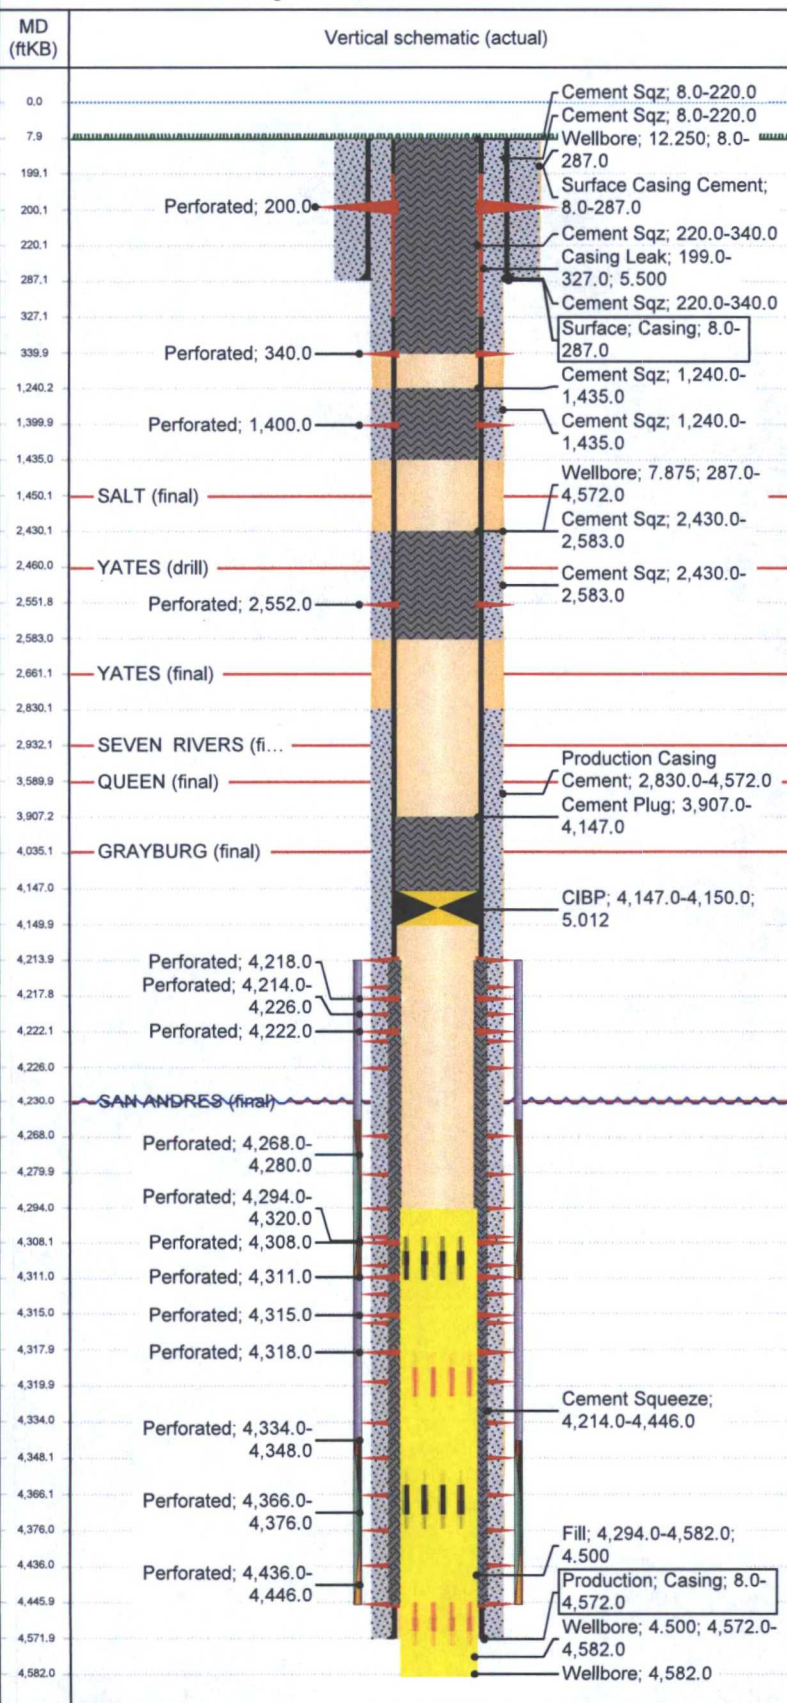

Perforations

Top (ftKB)	Btm (ftKB)	Comment
4,218.0	4,218.0	
4,222.0	4,222.0	
4,268.0	4,280.0	
4,294.0	4,320.0	
4,308.0	4,308.0	
4,311.0	4,311.0	
4,315.0	4,315.0	
4,318.0	4,318.0	
4,334.0	4,348.0	
4,366.0	4,376.0	
4,436.0	4,446.0	

Other In Hole

Des	Top (ftKB)	Btm (ftKB)	Run Date	Com
Fill	4,294.0	4,582.0	3/5/2015	Tagged up @ 4294'
Casing Leak	199.0	327.0	3/6/2015	Shallow casing leak isolated from 199'-327' (1.2 bpm @ 250#). Sqz w/ 22 sx class C cmt in 2010 Sqz w/ 65 sks class C cmt and w/ 150 sks cmt in 2015
CIBP	4,147.0	4,150.0	7/15/2016	

Formations

Formation	Final Top...	Final Btm...	Comment
SALT	1,450.0	2,460.0	
YATES	2,661.0	2,932.0	
SEVEN RIVERS	2,932.0	3,590.0	
QUEEN	3,590.0	4,035.0	
GRAYBURG	4,035.0	4,230.0	
SAN ANDRES	4,230.0		
