




Wellbore Schematic

Well Name SALADO DRAW WE 23 FED P7 004H	Lease SD 23 FED P7	Field Name JENNINGS	Business Unit Mid-Continent
--	-----------------------	------------------------	--------------------------------

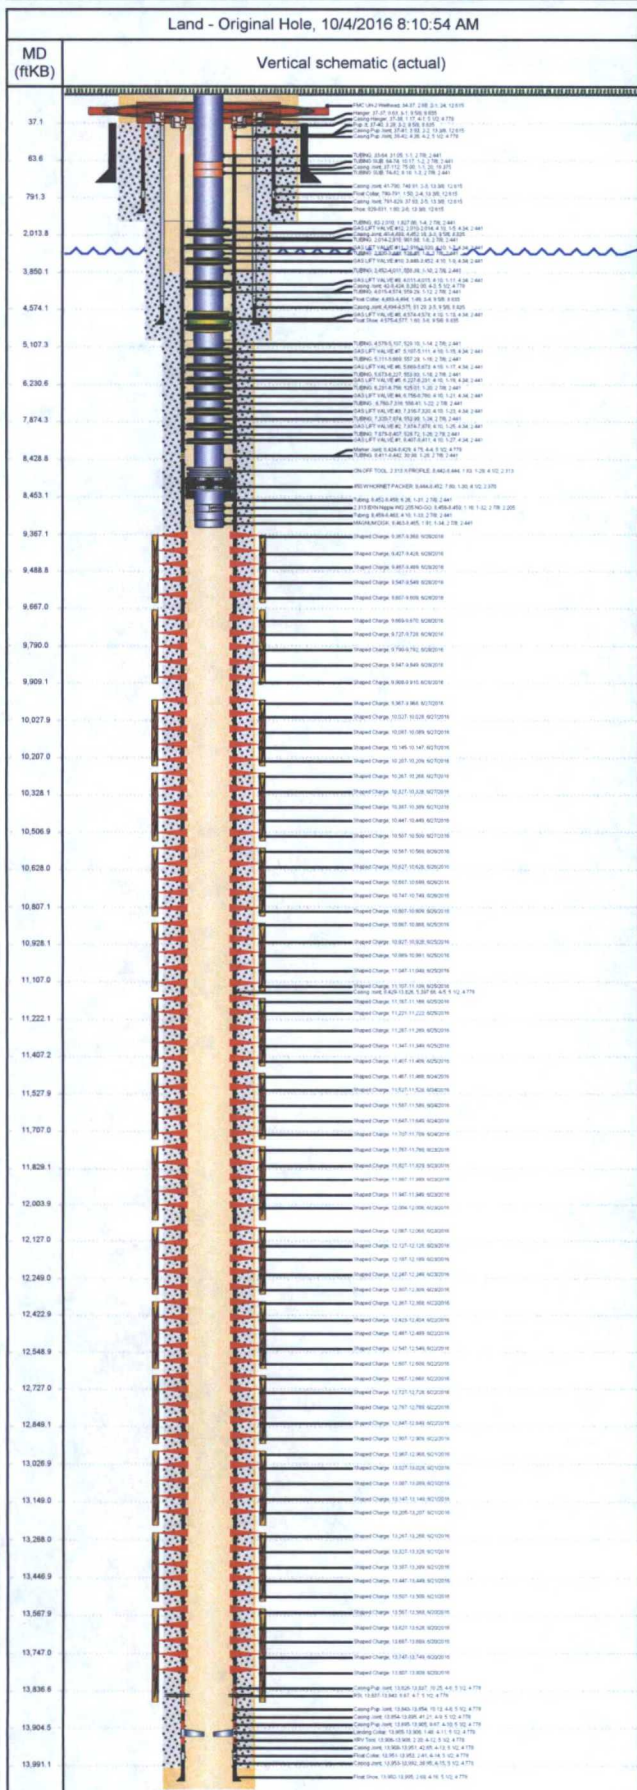


Job Details						
Job Category			Start Date		Rig/Unit End Date	
Completion			6/20/2016		6/30/2016	
Completion			6/30/2016		7/8/2016	
Completion			7/6/2016		7/8/2016	
Casing Strings						
Csg Des	OD (in)	Wt/Len (lb/ft)	Grade		Top Thread	Set Depth (MD) (ftKB)
Conductor	20	169.00	K-55			112
Surface	13 3/8	54.50	J-55		ST&C	831
Intermediate Casing 1	9 5/8	40.00	HCK-55		LT&C	4,577
Production Casing	5 1/2	20.00	P-110IC		TXP BTC-S	13,995
Tubing Strings						
TUBING set at 8,465.2ftKB on 7/7/2016 15:00						
Tubing Description			Run Date		String Length (ft)	Set Depth (MD) (ftKB)
TUBING			7/7/2016		8,432.65	8,465.2
Item Des	Jts	OD (in)	Wt (lb/ft)	Grade	Len (ft)	Btm (ftKB)
TUBING	1	2 7/8	6.50	L-80	31.05	63.6
TUBING SUB	1	2 7/8	6.50	L-80	10.17	73.8
TUBING SUB	1	2 7/8	6.50	L-80	8.18	82.0
TUBING	62	2 7/8	6.50	L-80	1,927.86	2,009.8
GAS LIFT VALVE #12	1	4.335			4.10	2,013.9
TUBING	17	2 7/8	6.50	L-80	901.68	2,915.6
GAS LIFT VALVE #11	1	4.335			4.10	2,919.7
TUBING	18	2 7/8	6.50	L-80	528.45	3,448.1
GAS LIFT VALVE #10	1	4.335			4.10	3,452.2
TUBING	18	2 7/8	6.50	L-80	558.38	4,010.6
GAS LIFT VALVE #9	1	4.335			4.10	4,014.7
TUBING	17	2 7/8	6.50	L-80	559.29	4,574.0
GAS LIFT VALVE #8	1	4.335			4.10	4,578.1
TUBING	18	2 7/8	6.50	L-80	529.10	5,107.2
GAS LIFT VALVE #7	1	4.335			4.10	5,111.3
TUBING	18	2 7/8	6.50	L-80	557.29	5,668.6
GAS LIFT VALVE #6	1	4.335			4.10	5,672.7
TUBING	18	2 7/8	6.50	L-80	553.83	6,226.5
GAS LIFT VALVE #5	1	4.335			4.10	6,230.6
TUBING	17	2 7/8	6.50	L-80	525.01	6,755.6
GAS LIFT VALVE #4	1	4.335			4.10	6,759.7
TUBING	18	2 7/8	6.50	L-80	556.41	7,316.2
GAS LIFT VALVE #3	1	4.335			4.10	7,320.3
TUBING	18	2 7/8	6.50	L-80	553.99	7,874.2
GAS LIFT VALVE #2	1	4.335			4.10	7,878.3
TUBING	17	2.785	6.50	L-80	528.72	8,407.1
GAS LIFT VALVE #1	1	4.335			4.10	8,411.2
TUBING	1	2 7/8	6.50	L-80	30.98	8,442.1
ON-OFF TOOL, 2.313 X PROFILE	1	4 1/2			1.83	8,444.0
450 W HORNET PACKER	1	4 1/2			7.80	8,451.8
Tubing	1	2 7/8	6.50	L-80	6.26	8,458.0
2.313 BXN Nipple W/2.205 NO-GO	1	2 7/8			1.16	8,459.2
Tubing	1	2 7/8	6.50	L-80	4.10	8,463.3
MAGNUM DISK	1	2 7/8			1.91	8,465.2
Perforations						
Date	Top (ftKB)	Btm (ftKB)	Shot Dens (shots/ft)	Entered Shot Total	Linked Zone	
6/28/2016	9,367.0	9,368.0	6.0	6	Avalon, Original Hole	
6/28/2016	9,427.0	9,428.0	6.0	6	Avalon, Original Hole	
6/28/2016	9,487.0	9,489.0	6.0	12	Avalon, Original Hole	
6/28/2016	9,547.0	9,549.0	6.0	12	Avalon, Original Hole	
6/28/2016	9,607.0	9,609.0	6.0	12	Avalon, Original Hole	
6/28/2016	9,669.0	9,670.0	6.0	6	Avalon, Original Hole	



Wellbore Schematic

Well Name SALADO DRAW WE 23 FED P7 004H	Lease SD 23 FED P7	Field Name JENNINGS	Business Unit Mid-Continent
--	-----------------------	------------------------	--------------------------------

Land - Original Hole, 10/4/2016 8:10:54 AM

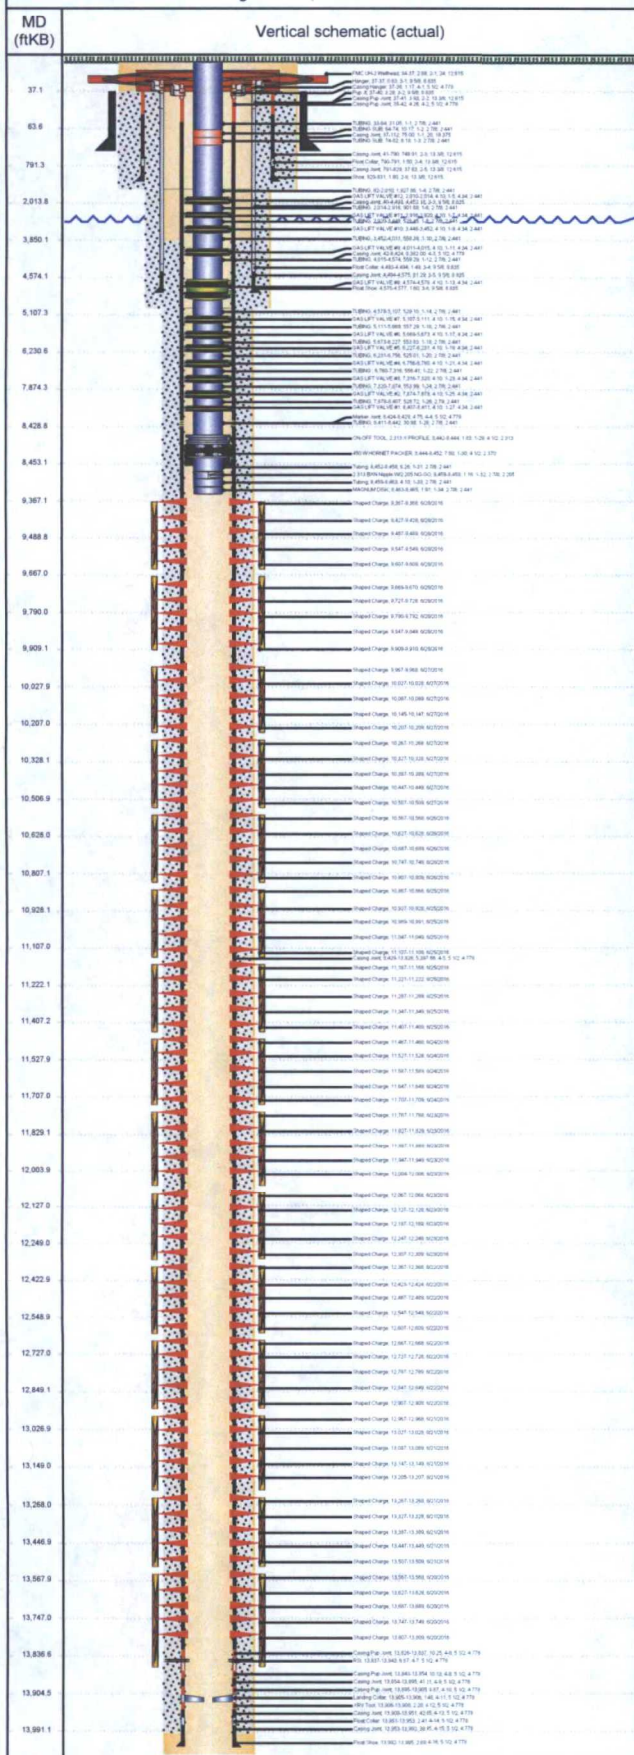

Perforations


Date	Top (ftKB)	Blm (ftKB)	Shot Dens (shots/ft)	Entered Shot Total	Linked Zone
6/28/2016	9,727.0	9,728.0	6.0	6	Avalon, Original Hole
6/28/2016	9,790.0	9,792.0	6.0	12	Avalon, Original Hole
6/28/2016	9,847.0	9,849.0	6.0	12	Avalon, Original Hole
6/28/2016	9,908.0	9,910.0	6.0	12	Avalon, Original Hole
6/27/2016	9,967.0	9,968.0	6.0	6	Avalon, Original Hole
6/27/2016	10,027.0	10,028.0	6.0	6	Avalon, Original Hole
6/27/2016	10,087.0	10,089.0	6.0	12	Avalon, Original Hole
6/27/2016	10,145.0	10,147.0	6.0	12	Avalon, Original Hole
6/27/2016	10,207.0	10,209.0	6.0	12	Avalon, Original Hole
6/27/2016	10,267.0	10,268.0	6.0	6	Avalon, Original Hole
6/27/2016	10,327.0	10,328.0	6.0	6	Avalon, Original Hole
6/27/2016	10,387.0	10,389.0	6.0	12	Avalon, Original Hole
6/27/2016	10,447.0	10,449.0	6.0	12	Avalon, Original Hole
6/27/2016	10,507.0	10,509.0	6.0	12	Avalon, Original Hole
6/26/2016	10,567.0	10,568.0	6.0	6	Avalon, Original Hole
6/26/2016	10,627.0	10,628.0	6.0	6	Avalon, Original Hole
6/26/2016	10,687.0	10,689.0	6.0	12	Avalon, Original Hole
6/26/2016	10,747.0	10,749.0	6.0	12	Avalon, Original Hole
6/26/2016	10,807.0	10,809.0	6.0	12	Avalon, Original Hole
6/25/2016	10,867.0	10,868.0	6.0	6	Avalon, Original Hole
6/25/2016	10,927.0	10,928.0	6.0	6	Avalon, Original Hole
6/25/2016	10,989.0	10,991.0	6.0	12	Avalon, Original Hole
6/25/2016	11,047.0	11,049.0	6.0	12	Avalon, Original Hole
6/25/2016	11,107.0	11,109.0	6.0	12	Avalon, Original Hole
6/25/2016	11,167.0	11,168.0	6.0	6	Avalon, Original Hole
6/25/2016	11,221.0	11,222.0	6.0	6	Avalon, Original Hole
6/25/2016	11,287.0	11,289.0	6.0	12	Avalon, Original Hole
6/25/2016	11,347.0	11,349.0	6.0	12	Avalon, Original Hole
6/25/2016	11,407.0	11,409.0	6.0	12	Avalon, Original Hole
6/24/2016	11,467.0	11,468.0	6.0	6	Avalon, Original Hole
6/24/2016	11,527.0	11,528.0	6.0	6	Avalon, Original Hole
6/24/2016	11,587.0	11,589.0	6.0	12	Avalon, Original Hole
6/24/2016	11,647.0	11,649.0	6.0	12	Avalon, Original Hole
6/24/2016	11,707.0	11,709.0	6.0	12	Avalon, Original Hole
6/23/2016	11,767.0	11,768.0	6.0	6	Avalon, Original Hole
6/23/2016	11,827.0	11,829.0	6.0	12	Avalon, Original Hole
6/23/2016	11,887.0	11,889.0	6.0	12	Avalon, Original Hole
6/23/2016	11,947.0	11,949.0	6.0	12	Avalon, Original Hole
6/23/2016	12,004.0	12,006.0	6.0	12	Avalon, Original Hole
6/23/2016	12,067.0	12,068.0	6.0	6	Avalon, Original Hole
6/23/2016	12,127.0	12,128.0	6.0	6	Avalon, Original Hole
6/23/2016	12,187.0	12,189.0	6.0	12	Avalon, Original Hole
6/23/2016	12,247.0	12,249.0	6.0	12	Avalon, Original Hole
6/23/2016	12,307.0	12,309.0	6.0	12	Avalon, Original Hole
6/22/2016	12,367.0	12,368.0	6.0	6	Avalon, Original Hole
6/22/2016	12,423.0	12,424.0	6.0	6	Avalon, Original Hole
6/22/2016	12,487.0	12,489.0	6.0	12	Avalon, Original Hole
6/22/2016	12,547.0	12,549.0	6.0	12	Avalon, Original Hole
6/22/2016	12,607.0	12,609.0	6.0	12	Avalon, Original Hole
6/22/2016	12,667.0	12,668.0	6.0	6	Avalon, Original Hole
6/22/2016	12,727.0	12,728.0	6.0	6	Avalon, Original Hole
6/22/2016	12,787.0	12,789.0	6.0	12	Avalon, Original Hole
6/22/2016	12,847.0	12,849.0	6.0	12	Avalon, Original Hole
6/22/2016	12,907.0	12,909.0	6.0	12	Avalon, Original Hole
6/21/2016	12,967.0	12,968.0	6.0	6	Avalon, Original Hole
6/21/2016	13,027.0	13,028.0	6.0	6	Avalon, Original Hole
6/21/2016	13,087.0	13,089.0	6.0	12	Avalon, Original Hole
6/21/2016	13,147.0	13,149.0	6.0	12	Avalon, Original Hole



Wellbore Schematic

Well Name SALADO DRAW WE 23 FED P7 004H	Lease SD 23 FED P7	Field Name JENNINGS	Business Unit Mid-Continent
--	-----------------------	------------------------	--------------------------------

Land - Original Hole, 10/4/2016 8:10:55 AM

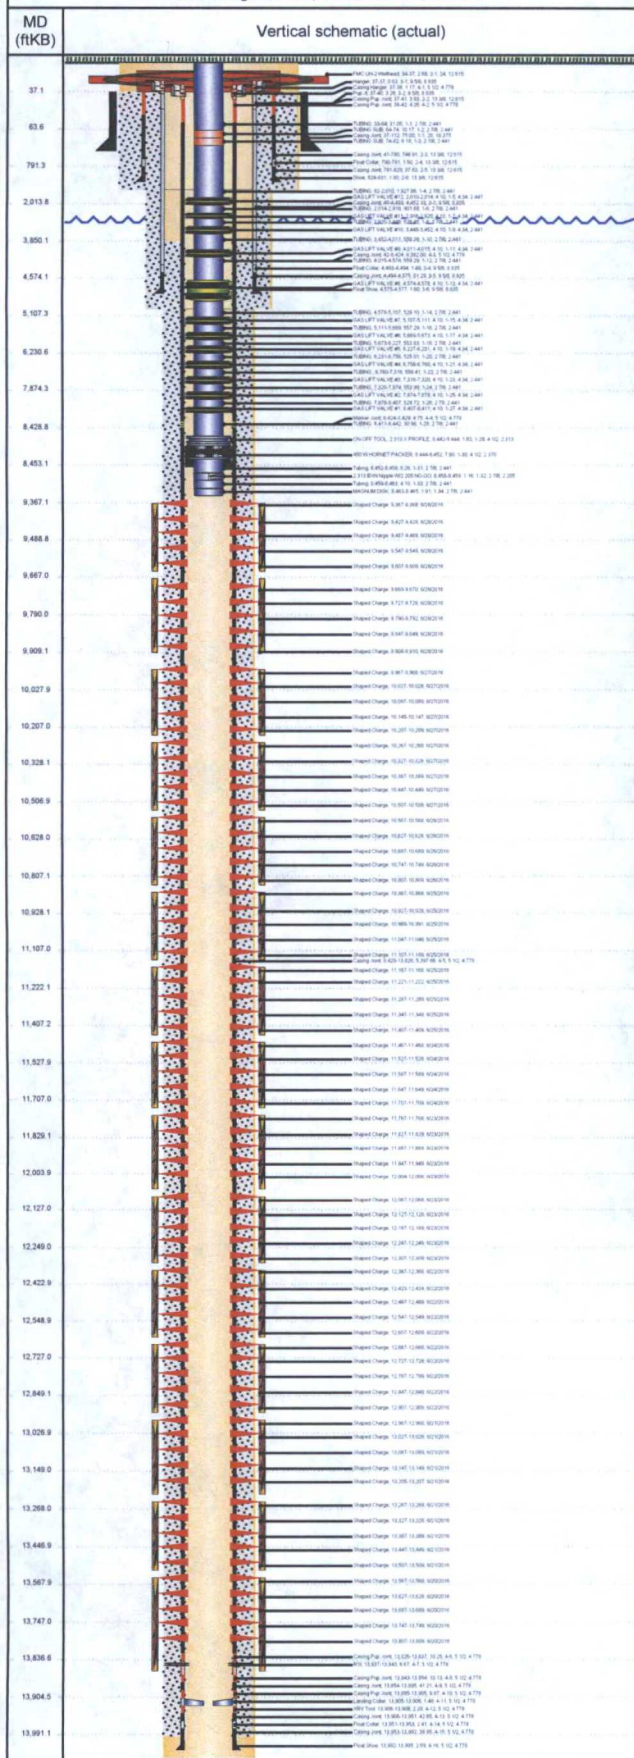

Perforations

Date	Top (ftKB)	Btm (ftKB)	Shot Dens (shots/ft)	Entered Shot Total	Linked Zone
6/21/2016	13,205.0	13,207.0	6.0	12	Avalon, Original Hole
6/21/2016	13,267.0	13,268.0	6.0	6	Avalon, Original Hole
6/21/2016	13,327.0	13,328.0	6.0	6	Avalon, Original Hole
6/21/2016	13,387.0	13,389.0	6.0	12	Avalon, Original Hole
6/21/2016	13,447.0	13,449.0	6.0	12	Avalon, Original Hole
6/21/2016	13,507.0	13,509.0	6.0	12	Avalon, Original Hole
6/20/2016	13,567.0	13,568.0	6.0	6	Avalon, Original Hole
6/20/2016	13,627.0	13,628.0	6.0	6	Avalon, Original Hole
6/20/2016	13,687.0	13,689.0	6.0	12	Avalon, Original Hole
6/20/2016	13,747.0	13,749.0	6.0	12	Avalon, Original Hole
6/20/2016	13,807.0	13,809.0	6.0	12	Avalon, Original Hole

Other Strings

Run Date	Pull Date	Set Depth (ftKB)	Com

Other In Hole

Des	Top (ftKB)	Btm (ftKB)	Run Date	Pull Date	Com
Packer	8,445.0	8,453.0	7/4/2016		Baker Hornet Retrieveable
Composite Frac Plug (drop ball)	9,637.0	9,639.0	6/28/2016	7/2/2016	Stage 15
Composite Frac Plug (drop ball)	9,937.0	9,939.0	6/28/2016	7/2/2016	Stage 14
Composite Frac Plug (drop ball)	10,238.0	10,240.0	6/27/2016	7/2/2016	Stage 13
Composite Frac Plug (drop ball)	10,537.0	10,539.0	6/27/2016	7/2/2016	Stage 12
Composite Frac Plug (drop ball)	10,837.0	10,839.0	6/26/2016	7/2/2016	Stage 11
Composite Frac Plug (drop ball)	11,137.0	11,139.0	6/25/2016	7/3/2016	Stage 10
Composite Frac Plug (drop ball)	11,445.0	11,447.0	6/25/2016	7/3/2016	Stage 9
Composite Frac Plug (drop ball)	11,737.0	11,739.0	6/24/2016	7/3/2016	Stage 8
Composite Frac Plug (drop ball)	12,037.0	12,039.0	6/23/2016	7/3/2016	Stage 7
Composite Frac Plug (drop ball)	12,337.0	12,339.0	6/23/2016	7/3/2016	Stage 6
Composite Frac Plug (drop ball)	12,627.0	12,629.0	6/22/2016	7/3/2016	Stage 5
Composite Frac Plug (drop ball)	12,937.0	12,939.0	6/22/2016	7/3/2016	Stage 4
Composite Frac Plug (drop ball)	13,237.0	13,239.0	6/21/2016	7/3/2016	Stage 3
Composite Frac Plug (drop ball)	13,530.0	13,532.0	6/21/2016	7/3/2016	Stage 2
