

Submit 1 Copy to Appropriate District Office
 District I - (575) 393-6161
 1625 N. French Dr., Hobbs, NM 88240
 District II - (575) 748-1283
 811 S. First St., Artesia, NM 88210
 District III - (505) 334-6178
 1000 Rio Brazos Rd., Aztec, NM 87410
 District IV - (505) 476-3460
 1220 S. St. Francis Dr., Santa Fe, NM 87505

HOBBS OGD

State of New Mexico
 Energy, Minerals and Natural Resources

Form C-103
 Revised July 18, 2013

JAN 25 2017

RECEIVED

OIL CONSERVATION DIVISION
 1220 South St. Francis Dr.
 Santa Fe, NM 87505

WELL API NO. 30-025-42207
5. Indicate Type of Lease STATE <input type="checkbox"/> FEE <input checked="" type="checkbox"/>
6. State Oil & Gas Lease No. NM 0149956
7. Lease Name or Unit Agreement Name N/A
8. Well Number D2
9. OGRID Number 025575
10. Pool name or Wildcat DEVONIAN EXPL.
11. Elevation (Show whether DR, RKB, RT, GR, etc.) 3548 ft. Ground Level

SUNDRY NOTICES AND REPORTS ON WELLS
 (DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)

1. Type of Well: Oil Well Gas Well Other: Acid Gas Injection

2. Name of Operator
DCP MIDSTREAM LP

3. Address of Operator
370 17TH STREET, SUITE 2500, DENVER, CO 80202

4. Well Location
 Unit Letter L : 1893 feet from the South line and 950 feet from the West line
 Section 19 Township 19S Range 32E NMPM County LEA

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:		SUBSEQUENT REPORT OF:	
PERFORM REMEDIAL WORK <input type="checkbox"/>	PLUG AND ABANDON <input type="checkbox"/>	REMEDIAL WORK <input type="checkbox"/>	ALTERING CASING <input type="checkbox"/>
TEMPORARILY ABANDON <input type="checkbox"/>	CHANGE PLANS <input type="checkbox"/>	COMMENCE DRILLING OPNS. <input type="checkbox"/>	P AND A <input type="checkbox"/>
PULL OR ALTER CASING <input type="checkbox"/>	MULTIPLE COMPL <input type="checkbox"/>	CASING/CEMENT JOB <input type="checkbox"/>	
DOWNHOLE COMMINGLE <input type="checkbox"/>			
CLOSED-LOOP SYSTEM <input type="checkbox"/>			
OTHER: <input type="checkbox"/>		OTHER: Subsequent MIT and Bradenhead <input checked="" type="checkbox"/>	

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

The MIT and Braden head Test were conducted on Wednesday, January 2, 2017 at 8:18 am. In order to conduct the MIT, the annular space pressure was adjusted to 560 psig by adding a small amount of diesel immediately before the test.

- Initially the starting injection pressure and the annular space pressure between casing and tubing was 280 psig
- Placed chart on annular space and began recording annular space pressure.
- Bled off annular fluid (diesel) to bring observed annular space pressure to zero psig.
- Slowly raised annular pressure by introducing diesel to the annulus to bring pressure to 560 psig.
- When annulus pressure reached 560 psig closed valves to pumping truck and recorded annular space pressure for 30 minutes.
- The DCP Zia AGI D #2 is not yet in service so there is no injection pressure on the tubing.
- After 30 minutes bled off annular fluid to reduce observed pressure to zero psig.
- Stopped recording TEST COMPLETE.
- Restored annular pressure to normal psig.

The Braden head Test was conducted concurrent with the MIT, which included bleeding off the pressure and keeping the valve open during the MIT.

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

Spud Date: November 2, 2016

Rig Release Date:


I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE Jared Smith TITLE CONSULTANT TO DCP MIDSTREM LP DATE 01/25/2017

Type or print name JARED R. SMITH E-mail address: JSMITH@GEOLEX.COM PHONE: 505-842-8000

For State Use Only

APPROVED BY [Signature] TITLE Compliance Officer DATE 1/25/2017

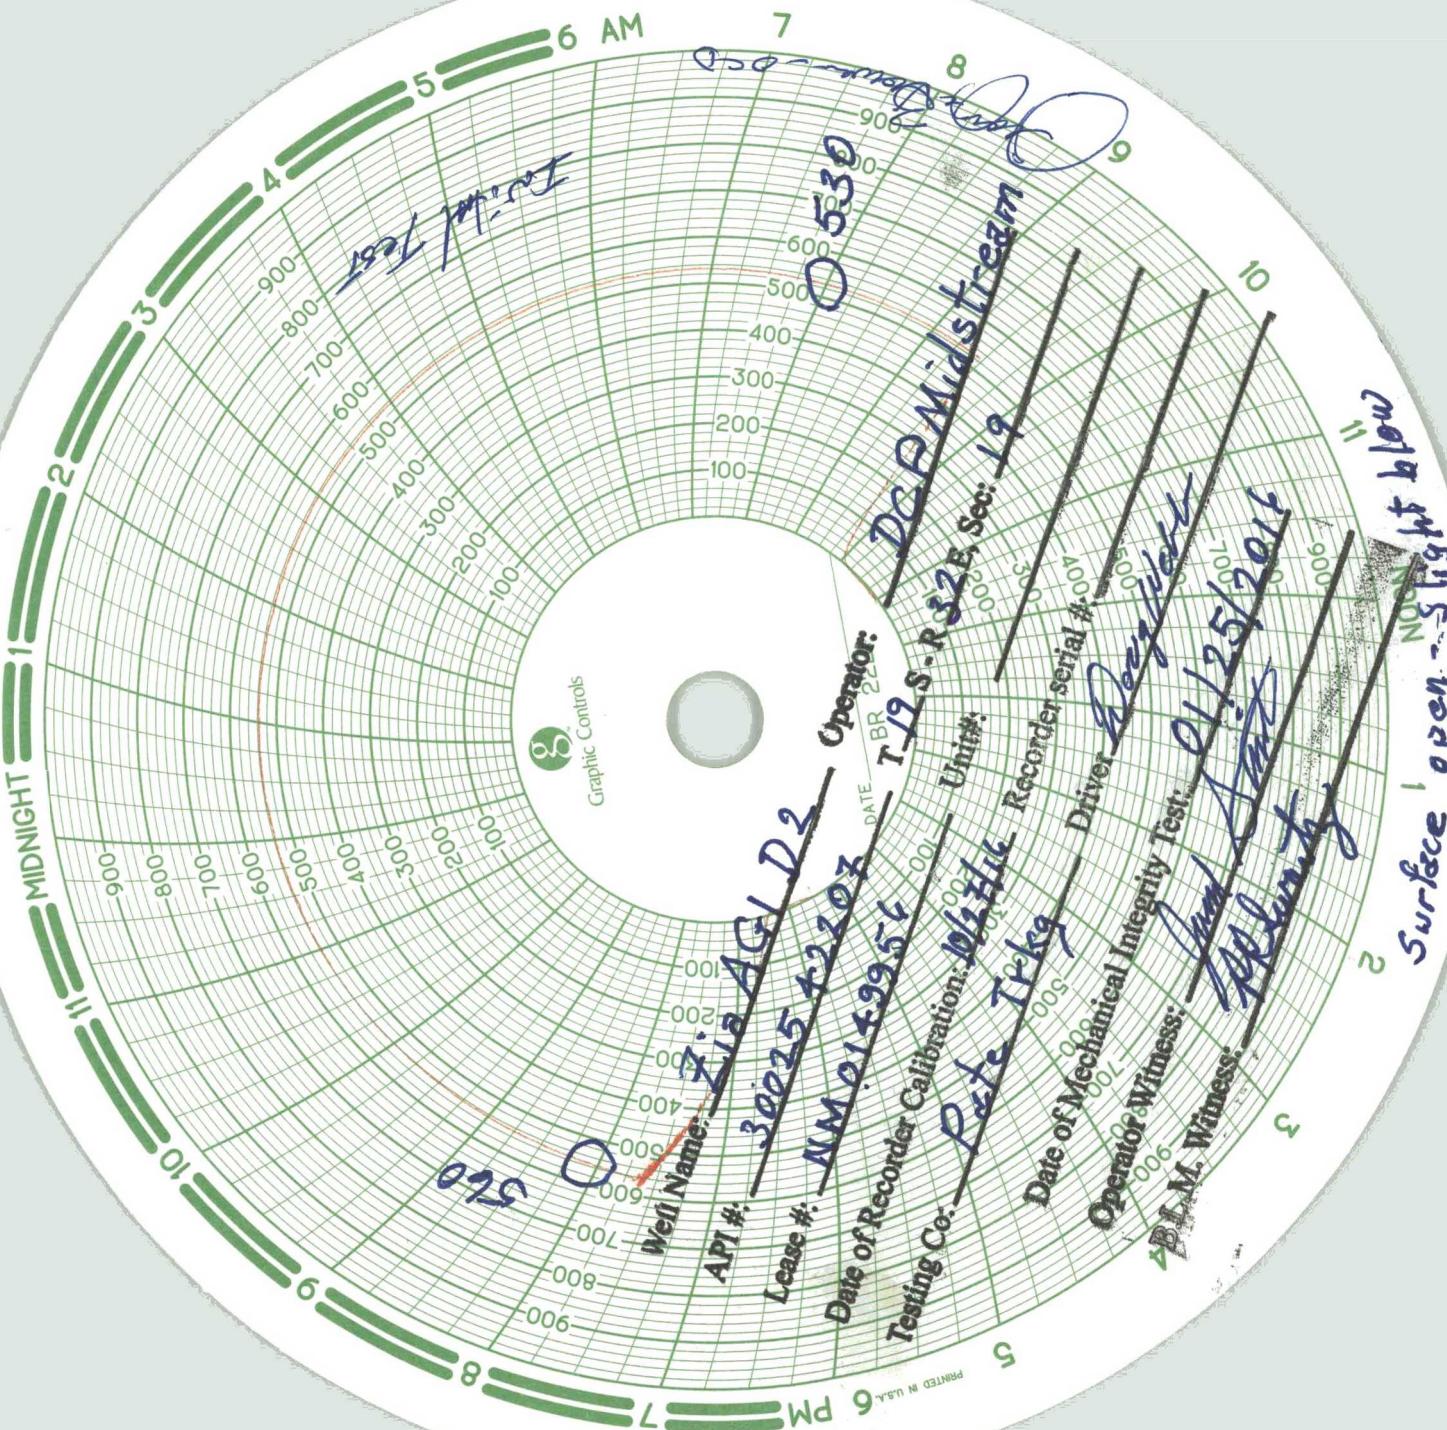

Well Name: Z.18 AGL D2 Operator: DCP Midstream
 API #: 3002542207 DATE: T 19 S. R. 22 E. Sec: 19
 Lease #: AM0149956 Unit#: _____
 Date of Recorder Calibration: 03/16/16 Recorder serial #: 00047
 Testing Co.: Pete Trkg Driver: Edy Water
 Date of Mechanical Integrity Test: _____
 Operator Witness: Paul Jant
 P.M. Witness: AR Smith

NOON
 Surface open - slight blow
