



30-025-44112

Cementing Job Report

Personel and Equipment

Personel	Tractor Number	Trailer Number
Service Supervisor: Donald Gregory		
Pump Operator: Tramain Faris		1520479
Operator: Eddie Traijllo		1323082
Operator: George Carter		1322860
Operator: James O		1323005
Operator: Xavian Marshall	1322970	1322970
Operator:		
Operator:		
Operator:		
Operator:		
Operator:		

1322970

MAR 16 2018

RECEIVED

Job Timeline

Time (24:00)	Comments	Pressure (psi)	Rate (bpm)	Vol. bbl	Weight lb/gal
0315A	arived on loc. 155joints on rack				
0330A	pre job jsa rigging up				
230P	JSA				
257P	pre job dinso test	40	4.0		
340P	fill lines pressure test	3000	5.0		
345P	fresh water ahead		5.0		
352P	start lead cement		8.0	464.0	11.8
400P	66 bbls away	950	8.0		
408P	132	605	8.0		
418P	198	470	8.0		
428P	264	517	8.0		
437P	330	514	8.0		
449P	396	398	8.0		
457P	464	400	8.0		
457P	start tail 13.3 bbls		3.0	13.3	14.4
509P	shut down wash up				
514P	droplug start displacement		9.0		
522P	100	375	9.0		
533P	200	630	9.0		
544P	300	850	9.0		
600P	380	1020-850	9-6.5		
602P	400	840	6.5		
607P	430	880	6.5		
619P	500	1030-885	6.5-4		
629P	544.3 LANDED PLUG	1000-1500	4.0		
631P	CHECK FLOATS OT 2 BBLS BACK	1500-0			
	RIGG DOWN				

Customer Representative

UPP Representative

[Signature]



Cementing Job Report

Company:	ImPetro Operating	Service Supervisor:	Donald Gregory
Well:	Wildhog BWX State Com #2	Total Pumping Time:	3.5
Job Type:	Cement 7 5/8" 2nd Intermediate Casing	Total Time on Location:	16HRS.
County:	Lea	UPP Down Time:	3HRS.
State:	New Mexico	Third Party Down Time:	0
Salesman:	Mark Acklin	Total Down Time:	3
Invoice #:	1115008699	Number of Personel on Job:	7
Job Date:		Hours on Job:	16

Well Data				Capacities	
Depth (TMD):	12265 ft	Liner Size:		Casing:	
Vertical Depth (TVD):	12265 ft	Top of Liner:		Open Hole:	
Hole Size:	9 7/8 in	Hole at:		Open Hole Annulus:	
Casing Size:	7 5/8 in 29.7 #/ft	Perfs at:		Cased Hole Annulus:	
Previous Casing Size:	10 3/4 in 45.5 #/ft	Retainer at:		Tubing/Drill Pipe:	
Prev. Casing Depth:	5325 ft	Packer at:		Liner:	
DV Tool Depth:		Tubing/Pipe:			

Pre-Flush, Spacer, and Displacement Fluids

Pre-flush	30 Bbls	Type:	Fresh Water
Displacement	TBD	Type:	Displacement Fluid

Cement

Lead	Premium 50/50 Poz + 5% Salt + 10% Gel + 2# Kol-Seal + 1/4# Celloflake + 0.3% CAS-1 + 0.6% CR-1					
	Sacks:	1055 sk	Yield:	2.47 cuft/sk	Slurry Volume:	464.96 Bbl
	Weight:	11.80 ppg	Mix Water:	14.05 gal/sk	Slurry Mix Water:	352.85 Bbl
Tail	Premium 50/50 Poz + 3% Salt + 2% Gel + 2# Kol-Seal + 0.3% CD-1 + 0.5% CFL-3 + 0.1% CR-1					
	Sacks:	80 sk	Yield:	1.25 cuft/sk	Slurry Volume:	17.80 Bbl
	Weight:	14.40 ppg	Mix Water:	5.37 gal/sk	Slurry Mix Water:	10.22 Bbl

Totals


Total Cement Pumped: 481.81 bbl

Total Displacement Pumped: 544.3 bbl

Pumping Data

Cement Circulated:	0	Maximum Pressure:	1500 PSI	Maximum Rate:	10.00 BPM
Minimum STP:		Operator's Max Pressure:	3000 PSI	Minimum Rate:	3.50 BPM
ISDP:		Average Pressure:	500 PSI	Average Rate:	6.50 BPM

Customer Representative


UPP Representative



Cement 7 5/8" 2nd Intermediate Casing

Company:	ImPetro Operating	Date:	
Well:	Wildhog BWX State Com #2	County:	Lea
Rig Name:	Trinidad 117	State:	New Mexico

Well Information

Depth (TMD):	12265 ft	Tubing/Drill Pipe:		Hole at:	
Vert. Depth (TVD):	12265 ft	Tubing/Drill Pipe Length:		Liner Size:	
Hole Size:	9 7/8 in	Casing Size:	7 5/8 in	Top of Liner:	
DV Tool at:		Prev. Casing Depth:	5325 ft	Liner Length:	
Additional Info:				Plug:	
				Packer at:	

Planned Pre-Flush, Spacer, and Displacement Fluids

Pre-flush 30 Bbls Type: Fresh Water

Displacement TBD Type: Displacement Fluid

Planned Cement

Lead	Premium 50/50 Poz + 5% Salt + 10% Gel + 2# Kol-Seal + 1/4# Celloflake + 0.3% CAS-1 + 0.6% CR-1			
1055 sk	Weight: 11.80 ppg	Yield: 2.47 cuft/sk	Mixing Water: 14.05 gal/sk	
	Slurry Volume: 464.96 Bbl	Slurry Mixing Water: 352.85 Bbl		
Tail	Premium 50/50 Poz + 3% Salt + 2% Gel + 2# Kol-Seal + 0.3% CD-1 + 0.5% CFL-3 + 0.1% CR-1			
80 sk	Weight: 14.40 ppg	Yield: 1.25 cuft/sk	Mixing Water: 5.37 gal/sk	
	Slurry Volume: 17.80 Bbl	Slurry Mixing Water: 10.22 Bbl		

Totals

Total Volume: 482.76 Bbl

Total Mix Water: 363.07 Bbl

Total Displacement:

Planned Pump Rates

Max Pressure:

Max Rate:

Min Rate:


Service Supervisor Signature

Company Representative Signature




impetro 2nd inter_2018-2-23 15-52-39

Job Name

Page 1 of 1

2/23/2018 7:02:20 PM

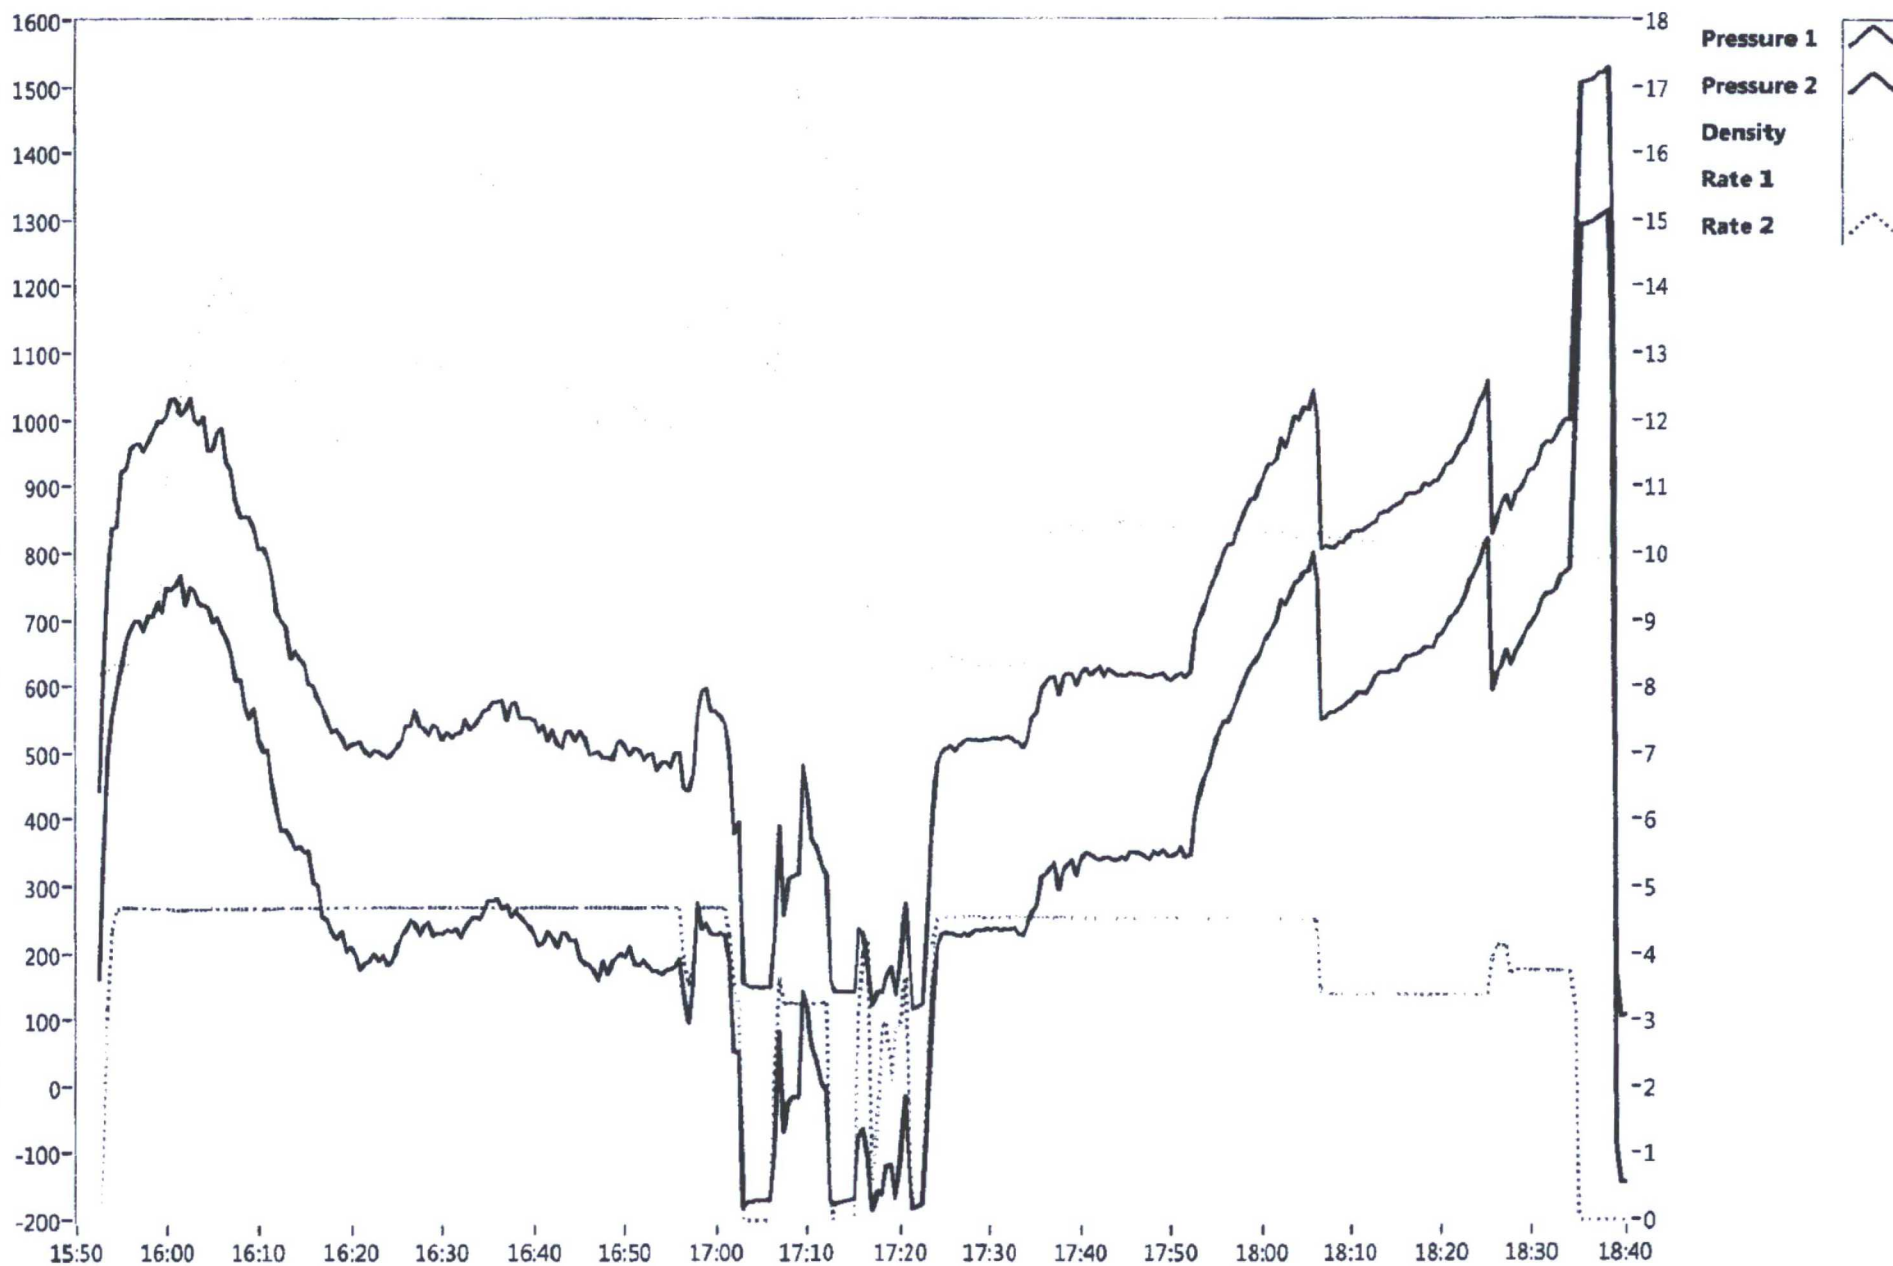




impetro 2nd inter_2018-2-23 14-52-42

Job Name

Page 1 of 1

2/23/2018 7:02:39 PM

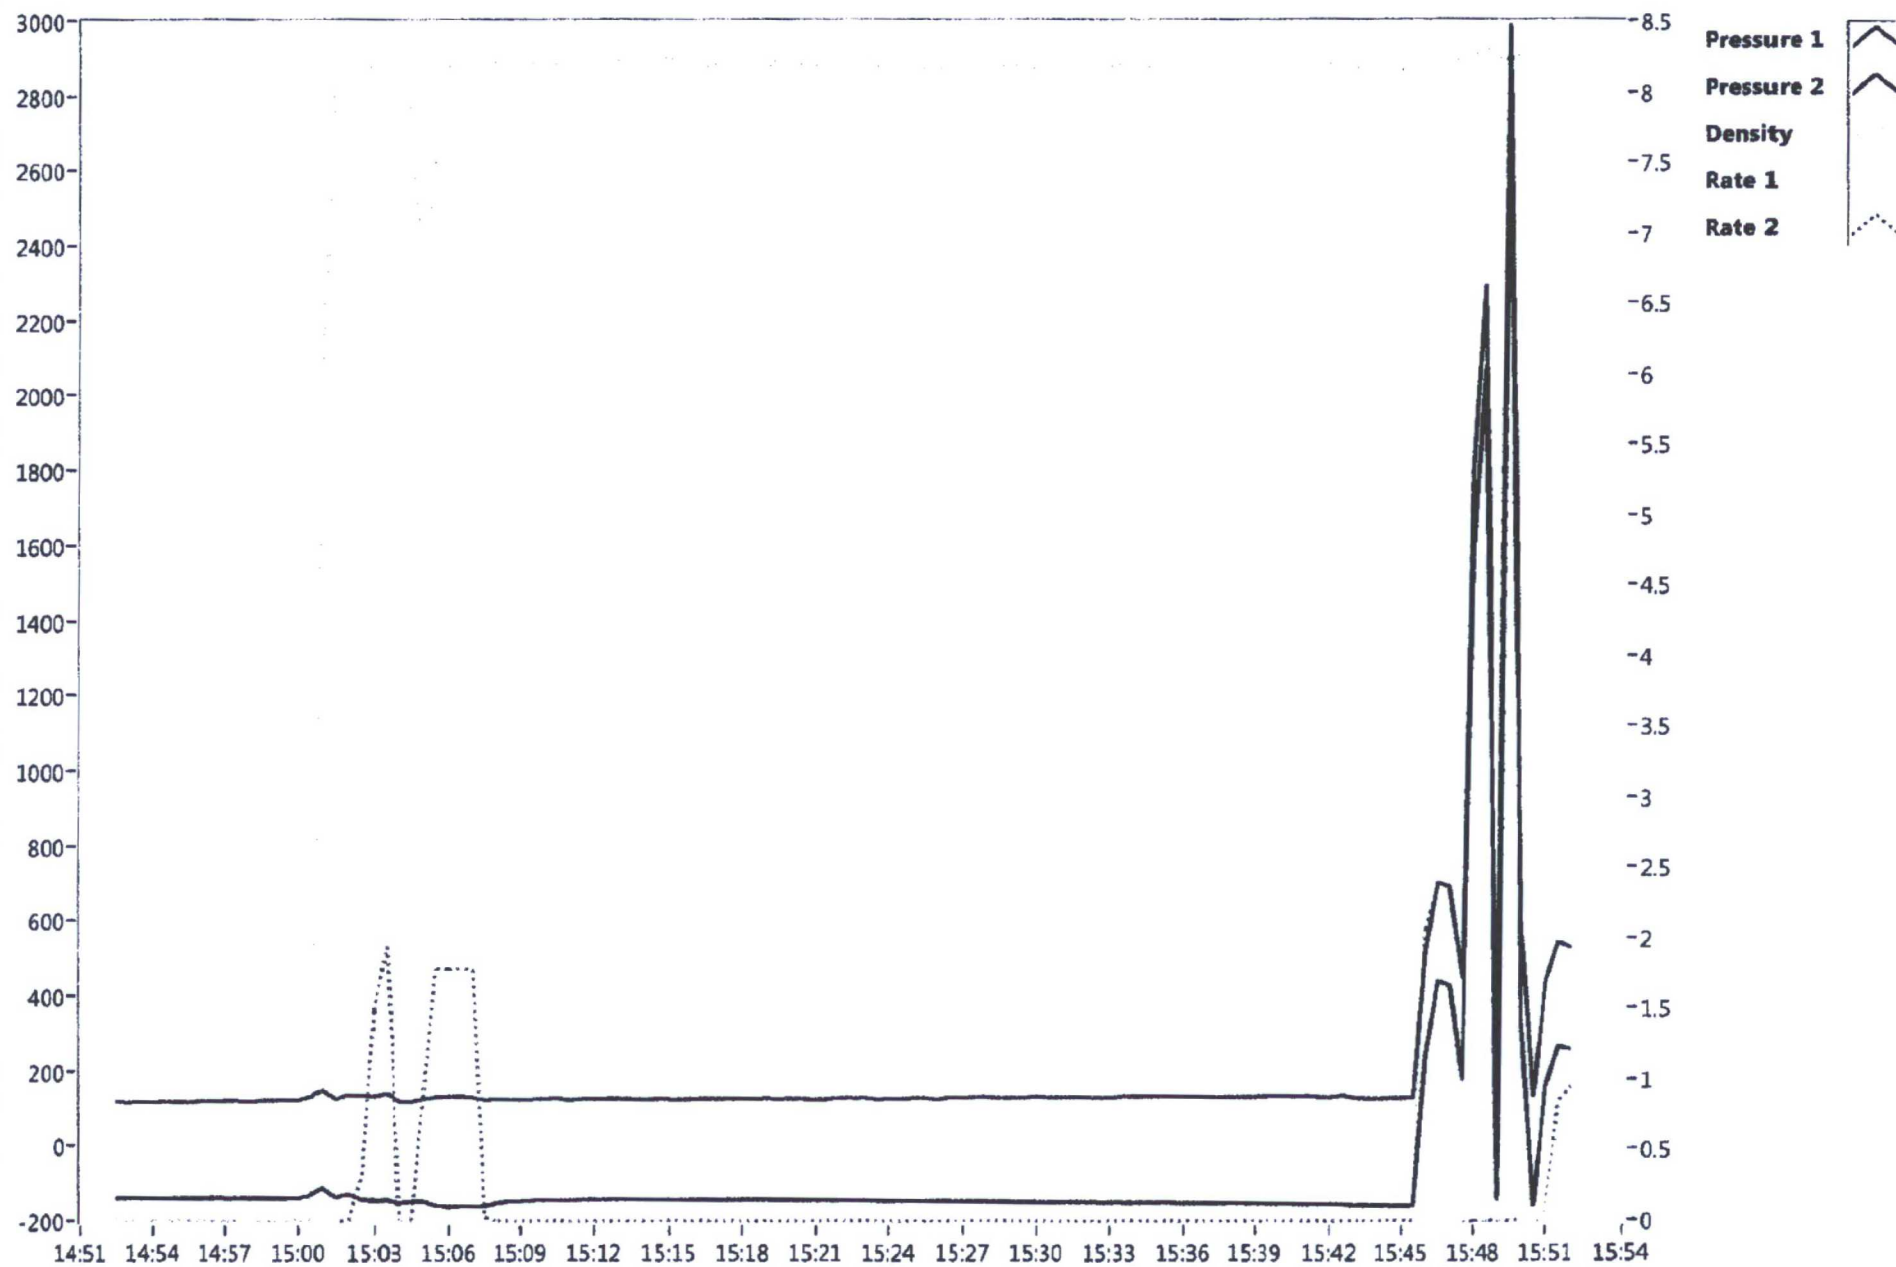




impetro 2nd inter_2018-2-23 15-52-39

Job Name

Page 1 of 1

2/23/2018 7:02:23 PM

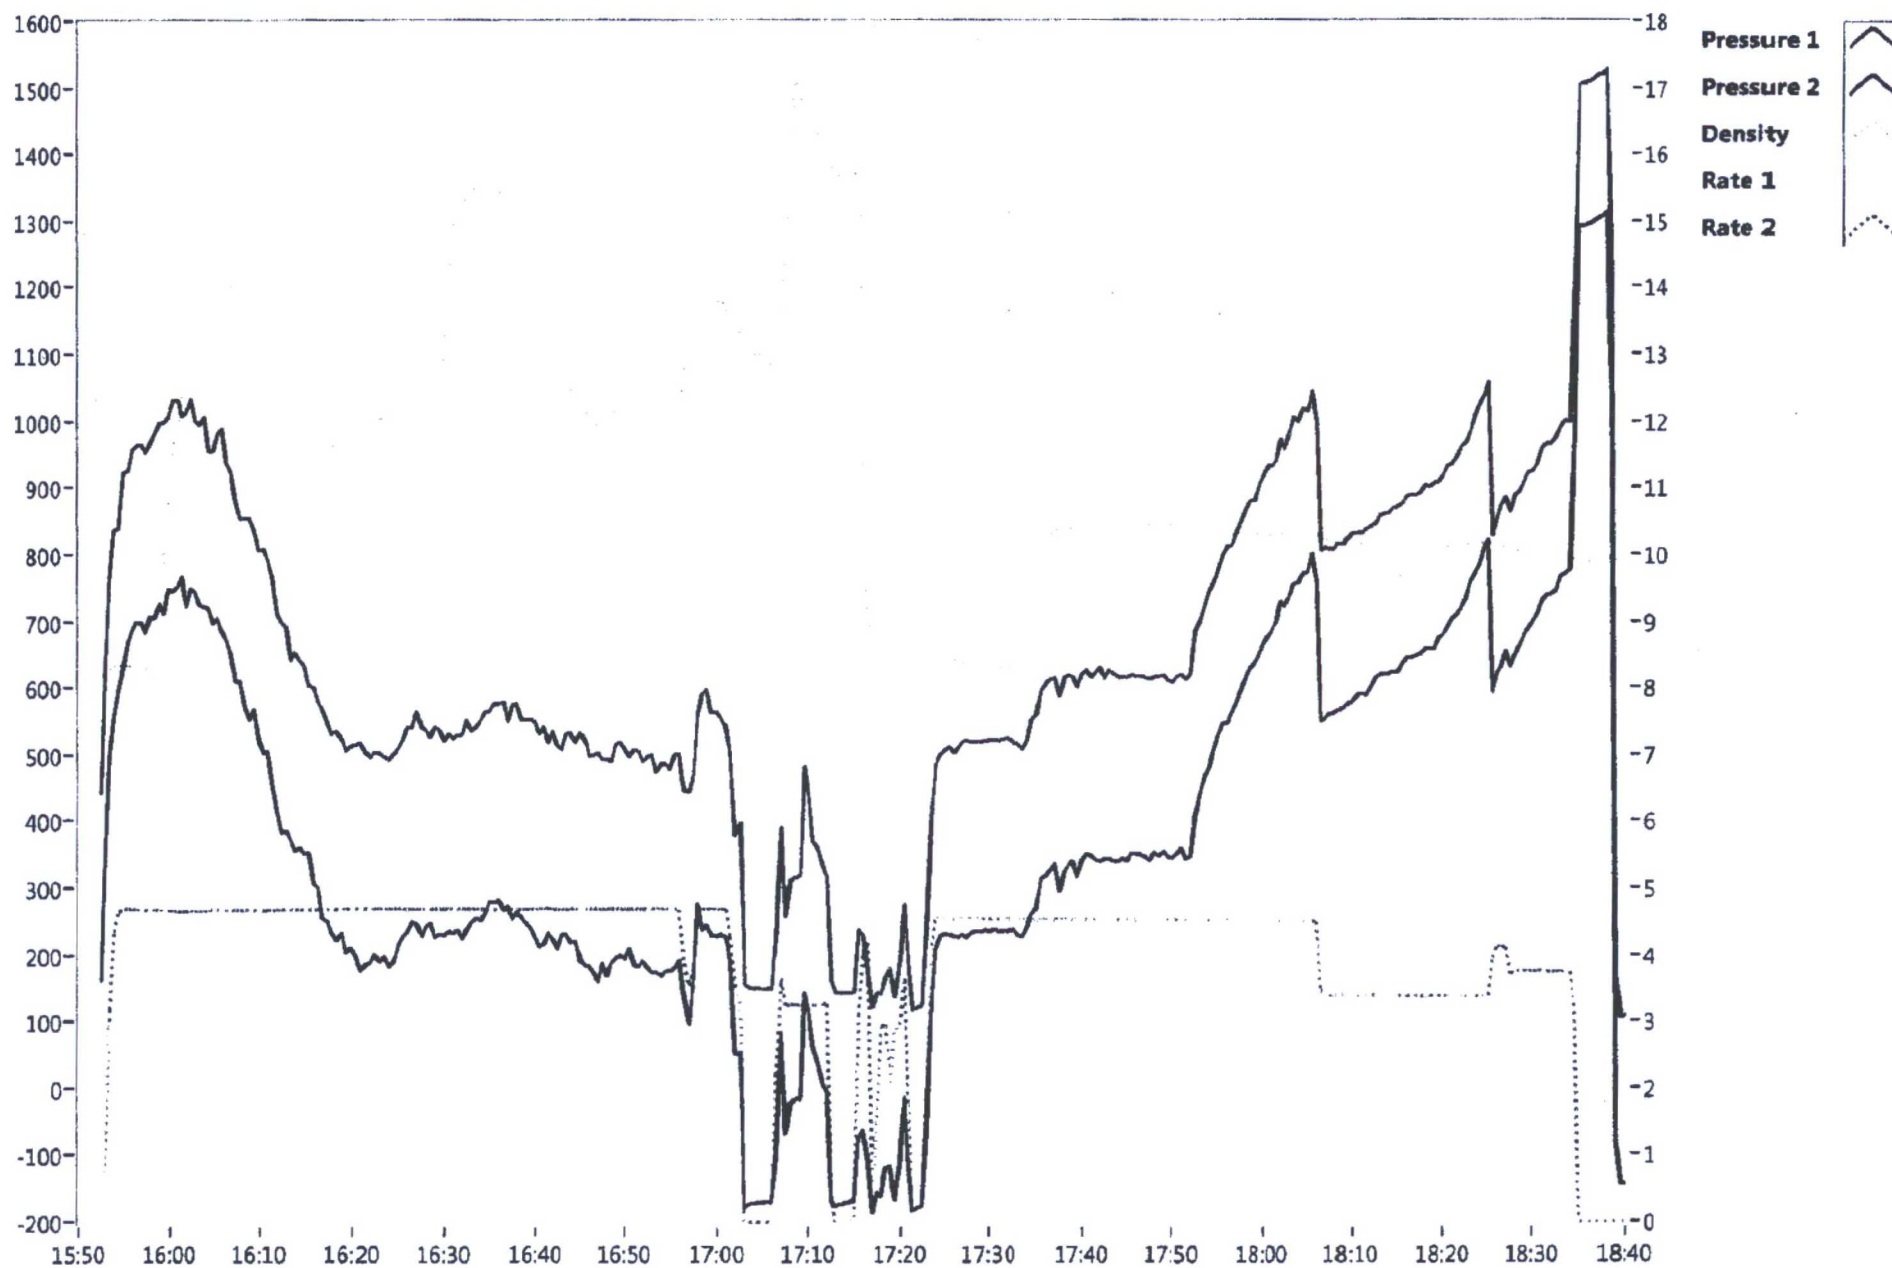



impetro 2nd Inter_2018-2-23 10-39-46

Job Name

Page 1 of 1

2/23/2018 7:03:14 PM

