

Carlsbad Field Office

FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: ☒ DRILL ☐ REENTER
1b. Type of Well: ☐ Oil Well ☒ Gas Well ☐ Other
1c. Type of Completion: ☐ Hydraulic Fracturing ☒ Single Zone ☐ Multiple Zone

2. Name of Operator
MARATHON OIL PERMIAN LLC (372098)

3a. Address
5555 San Felipe St. Houston TX 77056

3b. Phone No. (include area code)
(713)629-6600

4. Location of Well (Report location clearly and in accordance with any State requirements. *)
At surface SESW / 230 FSL / 1584 FWL / LAT 32.2980041 / LONG -103.6312897
At proposed prod. zone NWNW / 330 FNL / 1323 FWL / LAT 32.310982 / LONG -103.6321424

14. Distance in miles and direction from nearest town or post office*
17.33 miles

12. County or Parish
LEA

13. State
NM

15. Distance from proposed* location to nearest property or lease line, ft.
(Also to nearest drig. unit line, if any)
330 feet

16. No of acres in lease
800

17. Spacing Unit dedicated to this well
320

18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.
30 feet

19. Proposed Depth
12508 feet / 17218 feet

20. BLM/BIA Bond No. in file
FED: WYB002107

21. Elevations (Show whether DE, KDB, RT, GL, etc.)
3714 feet

22. Approximate date work will start*
03/16/2018

23. Estimated duration
30 days

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).

- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification.
- Such other site specific information and/or plans as may be requested by the BLM.

25. Signature
(Electronic Submission)

Name (Printed/Typed)
Jennifer Van Curen / Ph: (713)296-2500

Date
02/09/2018

Title

Sr. Regulatory Compliance Rep

Approved by (Signature)
(Electronic Submission)

Name (Printed/Typed)
Cody Layton / Ph: (575)234-5959

Date
09/11/2018

Title

Assistant Field Manager Lands & Minerals

Office
CARLSBAD

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

ECF Rec 09/26/18

APPROVED WITH CONDITIONS
Approval Date: 09/11/2018

KZ
09/26/18
Regulatory NSL

(Continued on page 2)

*(Instructions on page 2)

Double sided

INSTRUCTIONS

GENERAL: This form is designed for submitting proposals to perform certain well operations, as indicated on Federal and Indian lands and leases for action by appropriate Federal agencies, pursuant to applicable Federal laws and regulations. Any necessary special instructions concerning the use of this form and the number of copies to be submitted, particularly with regard to local, area, or regional procedures and practices, either are shown below or will be issued by, or may be obtained from local Federal offices.

ITEM 1: If the proposal is to redrill to the same reservoir at a different subsurface location or to a new reservoir, use this form with appropriate notations. Consult applicable Federal regulations concerning subsequent work proposals or reports on the well.

ITEM 4: Locations on Federal or Indian land should be described in accordance with Federal requirements. Consult local Federal offices for specific instructions.

ITEM 14: Needed only when location of well cannot readily be found by road from the land or lease description. A plat, or plats, separate or on the reverse side, showing the roads to, and the surveyed location of, the well, and any other required information, should be furnished when required by Federal agency offices.

ITEMS 15 AND 18: If well is to be, or has been directionally drilled, give distances for subsurface location of hole in any present or objective productive zone.

ITEM 22: Consult applicable Federal regulations, or appropriate officials, concerning approval of the proposal before operations are started.

ITEM 24: If the proposal will involve hydraulic fracturing operations, you must comply with 43 CFR 3162.3-3, including providing information about the protection of usable water. Operators should provide the best available information about all formations containing water and their depths. This information could include data and interpretation of resistivity logs run on nearby wells. Information may also be obtained from state or tribal regulatory agencies and from local BLM offices.

NOTICES

The Privacy Act of 1974 and regulation in 43 CFR 2.48(d) provide that you be furnished the following information in connection with information required by this application.

AUTHORITY: 30 U.S.C. 181 et seq., 25 U.S.C. 396; 43 CFR 3160

PRINCIPAL PURPOSES: The information will be used to: (1) process and evaluate your application for a permit to drill a new oil, gas, or service well or to reenter a plugged and abandoned well; and (2) document, for administrative use, information for the management, disposal and use of National Resource Lands and resources including (a) analyzing your proposal to discover and extract the Federal or Indian resources encountered; (b) reviewing procedures and equipment and the projected impact on the land involved; and (c) evaluating the effects of the proposed operation on the surface and subsurface water and other environmental impacts.

ROUTINE USE: Information from the record and/or the record will be transferred to appropriate Federal, State, and local or foreign agencies, when relevant to civil, criminal or regulatory investigations or prosecution, in connection with congressional inquiries and for regulatory responsibilities.

EFFECT OF NOT PROVIDING INFORMATION: Filing of this application and disclosure of the information is mandatory only if you elect to initiate a drilling or reentry operation on an oil and gas lease.

The Paperwork Reduction Act of 1995 requires us to inform you that:

The BLM collects this information to allow evaluation of the technical, safety, and environmental factors involved with drilling for oil and/or gas on Federal and Indian oil and gas leases. This information will be used to analyze and approve applications. Response to this request is mandatory only if the operator elects to initiate drilling or reentry operations on an oil and gas lease. The BLM would like you to know that you do not have to respond to this or any other Federal agency-sponsored information collection unless it displays a currently valid OMB control number.

BURDEN HOURS STATEMENT: Public reporting burden for this form is estimated to average 8 hours per response, including the time for reviewing instructions, gathering and maintaining data, and completing and reviewing the form. Direct comments regarding the burden estimate or any other aspect of this form to U.S. Department of the Interior, Bureau of Land Management (1004-0137), Bureau Information Connection Clearance Officer (WO-630), 1849 C Street, N.W., Mail Stop 401 LS, Washington, D.C. 20240.

Additional Operator Remarks

Location of Well

1. SHL: SESW / 230 FSL / 1584 FWL / TWSP: 23S / RANGE: 32E / SECTION: 13 / LAT: 32.2980041 / LONG: -103.6312897 (TVD: 0 feet, MD: 0 feet)
PPP: NWNW / 1320 FNL / 1323 FWL / TWSP: 23S / RANGE: 32E / SECTION: 13 / LAT: 32.3073547 / LONG: -103.6321403 (TVD: 12531 feet, MD: 15898 feet)
PPP: SWSW / 330 FSL / 1322 FWL / TWSP: 23S / RANGE: 32E / SECTION: 13 / LAT: 32.2982761 / LONG: -103.632136 (TVD: 12483 feet, MD: 12577 feet)
BHL: NWNW / 330 FNL / 1323 FWL / TWSP: 23S / RANGE: 32E / SECTION: 13 / LAT: 32.310982 / LONG: -103.6321424 (TVD: 12508 feet, MD: 17218 feet)

BLM Point of Contact

Name: Priscilla Perez

Title: Legal Instruments Examiner

Phone: 5752345934

Email: pperez@blm.gov

Review and Appeal Rights

A person contesting a decision shall request a State Director review. This request must be filed within 20 working days of receipt of the Notice with the appropriate State Director (see 43 CFR 3165.3). The State Director review decision may be appealed to the Interior Board of Land Appeals, 801 North Quincy Street, Suite 300, Arlington, VA 22203 (see 43 CFR 3165.4). Contact the above listed Bureau of Land Management office for further information.



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Operator Certification Data Report

09/12/2018

Operator Certification

I hereby certify that I, or someone under my direct supervision, have inspected the drill site and access route proposed herein; that I am familiar with the conditions which currently exist; that I have full knowledge of state and Federal laws applicable to this operation; that the statements made in this APD package are, to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein will be performed in conformity with this APD package and the terms and conditions under which it is approved. I also certify that I, or the company I represent, am responsible for the operations conducted under this application. These statements are subject to the provisions of 18 U.S.C. 1001 for the filing of false statements.

NAME: Jennifer Van Curen

Signed on: 02/07/2018

Title: Sr. Regulatory Compliance Rep

Street Address: 5555 San Felipe St.

City: Houston

State: TX

Zip: 77056

Phone: (713)296-2500

Email address: jvancuren@marathonoil.com

Field Representative

Representative Name:

Street Address:

City:

State:

Zip:

Phone:

Email address:



U. S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Application Data Report

09/12/2018

APD ID: 10400027053

Submission Date: 02/09/2018

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

Well Type: CONVENTIONAL GAS WELL

Well Work Type: Drill



[Show Final Text](#)

Section 1 - General

APD ID: 10400027053

Tie to previous NOS?

Submission Date: 02/09/2018

BLM Office: CARLSBAD

User: Jennifer Van Curen

Title: Sr. Regulatory Compliance Rep

Federal/Indian APD: FED

Is the first lease penetrated for production Federal or Indian? FED

Lease number: NMNM084728

Lease Acres: 800

Surface access agreement in place?

Allotted?

Reservation:

Agreement in place? NO

Federal or Indian agreement:

Agreement number:

Agreement name:

Keep application confidential? YES

Permitting Agent? NO

APD Operator: MARATHON OIL PERMIAN LLC

Operator letter of designation:

Operator Info

Operator Organization Name: MARATHON OIL PERMIAN LLC

Operator Address: 5555 San Felipe St.

Zip: 77056

Operator PO Box:

Operator City: Houston

State: TX

Operator Phone: (713)629-6600

Operator Internet Address:

Section 2 - Well Information

Well in Master Development Plan? NO

Mater Development Plan name:

Well in Master SUPO? NO

Master SUPO name:

Well in Master Drilling Plan? NO

Master Drilling Plan name:

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

Well API Number:

Field/Pool or Exploratory? Field and Pool

Field Name: DIAMONDTAIL;
WOLFCAMP

Pool Name: DIAMONDTAIL;
WOLFCAMP

Is the proposed well in an area containing other mineral resources? USEABLE WATER

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

Describe other minerals:

Is the proposed well in a Helium production area? N

Use Existing Well Pad? NO

New surface disturbance?

Type of Well Pad: MULTIPLE WELL

Multiple Well Pad Name:
BALLISTA FEDERAL 23 32 13

Number: 214-1

Well Class: HORIZONTAL

Number of Legs: 1

Well Work Type: Drill

Well Type: CONVENTIONAL GAS WELL

Describe Well Type:

Well sub-Type: INFILL

Describe sub-type:

Distance to town: 17.33 Miles

Distance to nearest well: 30 FT

Distance to lease line: 330 FT

Reservoir well spacing assigned acres Measurement: 320 Acres

Well plat: signed_BALLISTA_FEDERAL_23_32_13_WA_6H_REV1_CERTIFIED_FORM_C_102_2018020713153
3.pdf
APP_2_3160_3_BALLISTA_FEDERAL_23_32_13_WA_6H_20180711115252.pdf

Well work start Date: 03/16/2018

Duration: 30 DAYS

Section 3 - Well Location Table

Survey Type: RECTANGULAR

Describe Survey Type:

Datum: NAD27

Vertical Datum: NAVD88

Survey number: 21653

	NS-Foot	NS Indicator	EW-Foot	EW Indicator	Twsp	Range	Section	Aliquot/Lot/Tract	Latitude	Longitude	County	State	Meridian	Lease Type	Lease Number	Elevation	MD	TVD
SHL Leg #1	230	FSL	158 4	FWL	23S	32E	13	Aliquot SESW	32.29800 41	- 103.6312 897	LEA	NEW MEXI CO	NEW MEXI CO	F	NMNM 084728	371 4	0	0
KOP Leg #1	100	FSL	132 2	FWL	23S	32E	13	Aliquot SWS W	32.29759 61	- 103.6321 344	LEA	NEW MEXI CO	NEW MEXI CO	F	NMNM 084728	- 829 6	120 20	120 10

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

	NS-Foot	NS Indicator	EW-Foot	EW Indicator	Twsp	Range	Section	Aliquot/Lot/Tract	Latitude	Longitude	County	State	Meridian	Lease Type	Lease Number	Elevation	MD	TVD
PPP Leg #1	330	FSL	132 2	FWL	23S	32E	13	Aliquot SWS W	32.29827 61	- 103.6321 36	LEA	NEW MEXI CO	NEW MEXI CO	F	NMNM 084728	- 876 9	125 77	124 83
PPP Leg #1	132 0	FNL	132 3	FWL	23S	32E	13	Aliquot NWN W	32.30735 47	- 103.6321 403	LEA	NEW MEXI CO	NEW MEXI CO	F	NMNM 077062	- 881 7	158 98	125 31
EXIT Leg #1	330	FNL	132 3	FWL	23S	32E	13	Aliquot NWN W	32.31098 2	- 103.6321 424	LEA	NEW MEXI CO	NEW MEXI CO	F	NMNM 077062	- 879 4	172 18	125 08
BHL Leg #1	330	FNL	132 3	FWL	23S	32E	13	Aliquot NWN W	32.31098 2	- 103.6321 424	LEA	NEW MEXI CO	NEW MEXI CO	F	NMNM 077062	- 879 4	172 18	125 08

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED
OMB No. 1094-0137
Expires October 31, 2014

1a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. NMNM084728
1b. Type of Well: <input type="checkbox"/> Oil Well <input checked="" type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name
2. Name of Operator MARATHON OIL PERMIAN LLC		7. If Unit or CA Agreement, Name and No.
3a. Address 5555 San Felipe St. Houston TX 77056	3b. Phone No. (include area code) (713)629-6600	8. Lease Name and Well No. BALLISTA FEDERAL 23 32 13 WA 6H
4. Location of Well (Report location clearly and in accordance with any State requirements.) At surface SESW / 230 FSL / 1584 FWL / LAT 32.2980041 / LONG -103.6312897 At proposed prod. zone NWNW / 330 FNL / 1323 FWL / LAT 32.310982 / LONG -103.6321424		9. API Well No.
10. Field and Pool, or Exploratory DIAMONDTAIL; WOLFCAMP / DIAMON		11. Sec., T. R. M. or Blk. and Survey or Arca SEC 13 / T23S / R32E / NMP
14. Distance in miles and direction from nearest town or post office* 17.33 miles		12. County or Parish LEA
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 330 feet		13. State NM
16. No. of acres in lease 800		17. Spacing Unit dedicated to this well 320
18. Distance from proposed location* to nearest well, drilling, completed, 30 feet applied for, on this lease, ft. 30 feet		20. BLM/BIA Bond No. on file FED: WYB002107
21. Elevations (Show whether DF, KDB, RT, Gl., etc.) 3714 feet		22. Approximate date work will start* 03/16/2018
		23. Estimated duration 30 days

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, must be attached to this form:

- | | |
|--|---|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the BLM. |

25. Signature (Electronic Submission)	Name (Printed Typed) Jennifer Van Curen / Ph: (713)296-2500	Date 02/09/2018
Title Sr. Regulatory Compliance Rep		
Approved by (Signature)	Name (Printed Typed)	Date
Title Office CARLSBAD		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Drilling Plan Data Report

09/12/2018

APD ID: 10400027053

Submission Date: 02/09/2018

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

Well Type: CONVENTIONAL GAS WELL

Well Work Type: Drill

Highlighted data
reflects the most
recent changes

[Show Final Text](#)

Section 1 - Geologic Formations

Formation ID	Formation Name	Elevation	True Vertical Depth	Measured Depth	Lithologies	Mineral Resources	Producing Formation
1	RUSTLER	2468	1246	1246	DOLOMITE, ANHYDRITE	OTHER : Brine	No
2	SALADO	-1126	1718	1718	SALT, ANHYDRITE	OTHER : Brine	No
3	CASTILE	-2999	3591	3594	SALT	OTHER : Brine	No
4	BASE OF SALT	-4273	4865	4872	OTHER : Limy Sands	OTHER : Brine	No
5	LAMAR	-4382	4974	4981	OTHER : Sand/Shales	OIL	No
6	BELL CANYON	-4434	5026	5033	OTHER : Sands/Shale	OIL	No
7	CHERRY CANYON	-5562	6154	6165	OTHER : Sands/Carbonates	OIL	No
8	BRUSHY CANYON	-6626	7218	7231	OTHER : Sands/Carbonate	OIL	No
9	BONE SPRING	-8202	8794	8807	OTHER : Sands/Carbonate	OIL	No
10	WOLFCAMP	-11621	12213	12230	SHALE, SANDSTONE, OTHER : Carbonates	NATURAL GAS, OIL	Yes

Section 2 - Blowout Prevention

Pressure Rating (PSI): 10M

Rating Depth: 15000

Equipment: 13 5/8 5M Annular, 10M pipe ram, and 10M double ram will be installed and tested for each of the 12 1/4, 8 3/4 and 6 1/8 hole sections.

Requesting Variance? YES

Variance request: A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart. BOP variance is requested for the annular to be 5000 psi on 10000 psi BOP stack. Testing Procedure: - BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table attached. If the system is upgraded all the components installed will be functional and tested. The Annular will be tested to 70% of 5000 working pressure (see attached BOP plan). The working pressure of 10000 for the Double Ram and Pipe Ram will be tested to 10000 psi. - Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock, full opening safety valve / inside BOP and choke lines and

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

choke manifold. See attached schematics. - Formation integrity test will be performed per Onshore Order #2. On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i. - A multibowl wellhead is being used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested. See attached schematic.

Choke Diagram Attachment:

Drill_Plan___Choke_Line_Test_Chart_SN_63393___Ballista_Federal_23_32_13_PAD_20180207095559.pdf

Drill_Plan___Choke_and_Kill_Hose_SN_663393___Ballista_Federal_23_32_13_PAD_20180207095756.pdf

Drill_Plan___Choke_Line_System_Flex_III_Rig___Ballista_Federal_23_32_13_PAD_20180207095634.pdf

Drill_Plan___5M_10M.TWO_CHOKE_MANIFOLD.BLM___Ballista_Federal_23_32_13_PAD_20180207095618.pdf

BOP Diagram Attachment:

Drill_Plan___WH_TH_Design_1B_5K_10K_7in_x_4.5in___Ballista_Federal_23_32_13_PAD_20180207095926.pdf

Drill_Plan___5M_Flex_BOPE_Well_Head___Ballista_Federal_23_32_13_PAD_20180207095844.pdf

Marathon_Permian___Drilling_Well_Control_Plan_06_05_2018_20180710131315.pdf

Section 3 - Casing

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE	17.5	13.375	NEW	API	N	0	1250	0	1250	3714	2464	1250	J-55	54.5	STC	3.28	1.69	BUOY	2.77	BUOY	2.77
2	INTERMEDIATE	12.25	9.625	NEW	API	N	0	5000	0	5000	3714	1286	5000	J-55	40	LTC	1.16	1.36	BUOY	2.55	BUOY	2.55
3	INTERMEDIATE	8.75	7.0	NEW	API	N	0	12900	0	12600	3714	-8886	12900	P-110	29	BUTT	2.11	1.18	BUOY	2.11	BUOY	2.11
4	PRODUCTION	6.125	4.5	NEW	API	N	12000	17218	12000	12508	-8286	-8794	5218	P-110	13.5	BUTT	1.36	1.56	BUOY	2.39	BUOY	2.39

Casing Attachments

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

Casing Attachments

Casing ID: 1 **String Type:** SURFACE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Drill_Plan___Red_Hills_3_csg___liner___Surface_Csg___Ballista_Federal_23_32_13_WA_6H_20180207133559.pdf

Casing ID: 2 **String Type:** INTERMEDIATE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Drill_Plan___Red_Hills_3_csg___liner___Int_I_Csg___Ballista_Federal_23_32_13_WA_6H_20180207133643.pdf

Casing ID: 3 **String Type:** INTERMEDIATE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Drill_Plan___Red_Hills_3_csg___liner___Int_II_Csg___Ballista_Federal_23_32_13_WA_6H_20180207134229.pdf

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

Casing Attachments

Casing ID: 4 String Type: PRODUCTION

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Drill_Plan___Red_Hills_3_csg___liner___Prod_Liner___Ballista_Federal_23_32_13_WA_6H_20180207134356.pdf

Section 4 - Cement

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
PRODUCTION	Lead		0	0	0	0	0	758	0	N/A. No lead, tail only.	N/A. No lead, tail only.
PRODUCTION	Tail		1200 0	1721 8	524	1.22	14.5	639	30	Class H	0.15% retarder + 3.5% extender + 0.25% fluid loss
SURFACE	Lead		0	1000	795	1.75	13.5	1389	100	Class C	3 lbm/sk granular LCM + 0.1250 lbm/sk Poly-E-Flake
SURFACE	Tail		1000	1250	255	1.36	14.8	347	100	Class C	0.25 % Accelerator
INTERMEDIATE	Lead		0	4000	1267	1.73	12.8	2192	75	Class C	0.02 Gal/Sx Defoamer + 0.5% Extender + 1% Accelerator
INTERMEDIATE	Tail		4000	5000	353	1.33	14.8	470	50	Class C	0.07 % Retarder
INTERMEDIATE	Lead		3000	1190 0	842	2.7	11	2275	70	Class C	0.8% retarder + 10% extender + 0.02 gal/sk + 2.0% Extender + 0.15% Viscosifier
INTERMEDIATE	Tail		1190 0	1290 0	179	1.09	15.6	195	30	Class H	3% extender + 0.1% Dispersant + 0.2% retarder

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

Section 5 - Circulating Medium

Mud System Type: Closed

Will an air or gas system be Used? NO

Description of the equipment for the circulating system in accordance with Onshore Order #2:

Diagram of the equipment for the circulating system in accordance with Onshore Order #2:

Describe what will be on location to control well or mitigate other conditions: The necessary mud products for additional weight and fluid loss control will be on location at all times.

Describe the mud monitoring system utilized: Losses or gains in the mud system will be monitored visually/manually as well as with an electronic PVT.

Circulating Medium Table

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
1290 0	1721 8	OIL-BASED MUD	12	12.5							
1250	5000	OTHER : Brine	9.9	10.2							
0	1250	WATER-BASED MUD	8.4	8.8							
5000	1290 0	OTHER : Cut Brine	9	9.4							

Section 6 - Test, Logging, Coring

List of production tests including testing procedures, equipment and safety measures:

None Planned.

List of open and cased hole logs run in the well:

GR,MUDLOG

Coring operation description for the well:

None Planned.

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

Section 7 - Pressure

Anticipated Bottom Hole Pressure: 6130

Anticipated Surface Pressure: 5378.18

Anticipated Bottom Hole Temperature(F): 188

Anticipated abnormal pressures, temperatures, or potential geologic hazards? NO

Describe:

Contingency Plans geohazards description:

Contingency Plans geohazards attachment:

Hydrogen Sulfide drilling operations plan required? YES

Hydrogen sulfide drilling operations plan:

Drill_Plan___H2S_Contingency_Plan___Ballista_Federal_23_32_13_PAD_20180207113226.pdf

Pad_Flex_III_Rev1_20180711100133.pdf

Drill_Plan___Plat___H2S_Map___Ballista_Federal_23_32_13_PAD_20180207113651_20180711110559.pdf

GCP___Ballista_Federal_23_32_13_Pad___2_6_2018_20180711110614.pdf

Section 8 - Other Information

Proposed horizontal/directional/multi-lateral plan submission:

Ballista_Federal_6H_Directional_Plans_20180207135201.pdf

Plat___Ballista_Federal_23_32_13_Pad___Federal_Minerals_Map_20180207135219.pdf

Plat___Ballista_Federal_23_32_13_Pad___Mineral_Ownership_Map_20180207135248.pdf

Other proposed operations facets description:

- Kelly cock will be in the drill string at all times.
- A full opening drill pipe stabbing valve having the appropriate connections will be on the rig floor unobstructed and readily accessible at all times.
- Hydrogen Sulfide detection equipment will be in operation after drilling out the surface casing shoe until the production casing is cemented. Breathing equipment will be on location upon drilling the surface casing shoe until total depth is reached. If Hydrogen Sulfide is encountered, measured amounts and formations will be reported to the BLM.

Potential Hazards:

- H2S detection equipment will be in operation after drilling out the surface casing shoe until the production casing has been cemented. Breathing equipment will be on location from drilling out the surface shoe until production casing is cemented. If H2S is encountered the operator will comply with Onshore Order #6.
- No abnormal temperatures or pressures are anticipated. All personnel will be familiar with all aspects of safe operation of equipment being used to drill this well. Adequate flare lines will be installed off the mud/gas separator where gas may be flared safely.
- No losses are anticipated at this time.
- All personnel will be familiar with all aspects of safe operation of equipment being used to drill this well.
- Adequate flare lines will be installed off the mud/gas separator where gas may be flared safely.

Other proposed operations facets attachment:

Batch_Drilling_Plan_and_Surface_Rig_Request_20180710131332.pdf

Ballista_Federal_23_32_13_WA_6H_Drilling_APD_Information_20180711110632.doc


Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

Other Variance attachment:

Certificate of Conformity



ContiTech

Certificate Number 953233-4	COM Order Reference 953233	Customer Name & Address HELMERICH & PAYNE DRILLING CO 1434 SOUTH BOULDER AVE TULSA, OK 74119 USA	
Customer Purchase Order No: 740053080			
Project:			
Test Center Address ContiTech Oil & Marine Corp. 11535 Brittmoore Park Drive Houston, TX 77041 USA	Accepted by GOM Inspection Signed: Roger Suarez Date: 5/11/17	Accepted by Client Inspection	

We certify that the items detailed below meet the requirements of the customer's Purchase Order referenced above, and are in conformance with the specifications given below.

Item	Part No.	Description	Qty	Serial Number	Specifications
------	----------	-------------	-----	---------------	----------------

30

RECERTIFICATION - 3" ID 10K Choke and Kill Hose x 35 ft OAL

1

63393

ContiTech Standard

Hydrostatic Test Certificate

Continental

ContiTech

Certificate Number 953233-4	COM Order Reference 953233	Customer Name & Address HELMERICH & PAYNE DRILLING CO 1434 SOUTH BOULDER AVE TULSA, OK 74119 USA	
Customer Purchase Order No: 740053080			
Project:			
Test Center/Address ContiTech Oil & Marine Corp. 11535 Brittmoore Park Drive Houston, TX 77041 USA	Accepted by GOM Inspection Signed: Roger Suarez Date: 5/11/17	Accepted by Client Inspection	

We certify that the goods detailed hereon have been inspected as described below by our Quality Management System, and to the best of our knowledge are found to conform the requirements of the above referenced purchase order as issued to ContiTech Oil & Marine Corporation.

Item	Part No.	Description	Qty	Serial Number	Work Press.	Test Press.	Test Time (minutes)
30		RECERTIFICATION - 3" ID 10K Choke and Kill Hose x 35 ft OAL	1	63393	10,000 psi	15,000 psi	60

63393

6 AM

JOB # 48-20-10-81
PBC# 955233
HOSE DESCRIPTION: 3" ID 100' Chlor. 1/2"
TEST PRESSURE: 1500 psi
CHART RECORDER #: 1042162208
CHART SETTING: 911m
CBC REPRESENTATIVE: G. Kae Hahn
DATE: 5-5-70



CHART NO. MD MP-20000-150F

METER

CHART PUT ON

LOCATION

REMARKS

TAKEN OFF

NOON

6 PM

QUALITY CONTROL	No.: QC-DB- 380 / 2012
	Page : 1 / 61
Hose No.: 63389, 63390, 63391 63392, 63393	Revision : 0
	Date: 28. August 2012.
	Prepared by : <i>Szabolcs Lőrincz</i>
	Appr. by: <i>Szabolcs Lőrincz</i>
<h1>CHOKE AND KILL HOSES</h1> <p>id.: 3" 69 MPa x 35 ft (10,67 m)</p> <h2>DATA BOOK</h2> <p>Purchaser: H & P</p> <p>Purchaser Order No.:</p> <p>ContiTech Rubber Order No.: 531895</p> <p>ContiTech Beattie Co. Order No.: 006227</p> <p>NOT DESIGNED FOR WELL TESTING</p>	

CONTENT

	<u>Page</u>
1. API QMS Certificate (No.: 0760)	3.
2. American Petroleum Institute Certificate of Authority To Use the Official API Monogram (No.: 16C-0004)	4.
3. Quality Control Inspection and Test Certificates (No.: 1595, 1596, 1597, 1598, 1599)	5-9.
4. Hose Data Sheet	10.
5. Metal Parts	
5.1. Raw Material Quality Certificates (No.: EUR-240960, EUR-251871, 81687/12-0)	11-14.
5.2. Hardness Test Reports (No.: HB 2150/12, HB 2151/12, HB 2159/12)	15-17.
5.3. Ultrasonic Test Reports (No.: U12/124, U12/126, U12/129, U12/127)	18-21.
5.4. NDT Examiner Certificate (Name: Joó Imre)	22-23.
5.5. Welding Procedure Specification (No.: 140-60)	24-27.
5.6. Welding Procedure Qualification Record (No.: BUD 0600014/1)	28-29.
5.7. Welder's Approval Test Certificates (No.: RK-1894628-A1-X2, RK-1894628-A1-X-1, RK-2096656-B, RK-1894628-A1-X3, RK1079715-A1-X)	30-41.
5.8. Welding Log Sheets (No.: 240, 241)	42-43.
5.9. Visual Examination Record (No.: 696/12)	44.
5.10. NDT Examiner Certificate (Name: Benkő Péter)	45-46.
5.11. Radiographic Test Certificates (No.: 1458/12, 1459/12, 1460/12, 1461/12, 1462/12)	47-51.
5.12. NDT Examiner Certificate (Name: Ménesi István)	52-53.
5.13. MP Examination Record (No.: 1262/12)	54.
5.14. NDT Examiner Certificate (Name: Oravecz Gábor)	55-56.
6. Steel Cord	
6.1. Inspection Certificate (No.: 437089)	57.
7. Outside Stripwound Tube	
7.1. Inspection Certificate (No.: 917781/001)	58.
8. Certificate of Calibration (Manometer Serial No.: 0227-073)	59-61.



 ContiTech Rubber
 Industrial Kft.
 Quality Control Dept.
 (1)



Certificate of Registration

APIQR REGISTRATION NUMBER
0760

This certifies that the quality management system of
CONTITECH RUBBER INDUSTRIAL LTD.
Budapesti ut 10
Szeged
Hungary

*has been assessed by the American Petroleum Institute Quality Registrar (APIQR®) and
found it to be in conformance with the following standard:*

ISO 9001:2008

The scope of this registration and the approved quality management system applies to the
Design and Manufacture of High Pressure Hoses

APIQR® approves the organization's justification for excluding:
No Exclusions Identified as Applicable

COPY

Effective Date: October 15, 2010
Expiration Date: October 15, 2013
Registered Since: October 15, 2007

W. Dan Whitaker
Manager of Operations, APIQR


Accredited by Member of
the International
Accreditation Forum
Manufacture Registration
Arrangement for Quality
Management Systems




This certificate is valid for the period specified herein. The registered organization must continually meet all requirements of APIQR's Registration Program and the requirements of the Registration Agreement. Registration is maintained and regularly monitored through annual full system audits. Further clarifications regarding the scope of this certificate and the applicability of ISO 9001 standard requirements may be obtained by consulting the registered organization. This certificate has been issued from APIQR offices located at 1220 L Street, N.W., Washington, D.C. 20005-4070, U.S.A.. It is the property of APIQR, and must be returned upon request. To verify the authenticity of this certificate, go to www.apiqr.com/compositelists.



2007-11-15 03:29:13



**American
Petroleum
Institute**



2010 1120

Certificate of Authority to use the Official API Monogram

License Number: 16C-0004

ORIGINAL

The American Petroleum Institute hereby grants to

CONTITECH RUBBER INDUSTRIAL LTD.

Budapesti ut 10

Szeged

Hungary

the right to use the Official API Monogram® on manufactured products under the conditions in the official publications of the American Petroleum Institute entitled API Spec Q1® and API Spec 16C and in accordance with the provisions of the License Agreement.

In all cases where the Official API Monogram is applied, the API Monogram should be used in conjunction with this certificate number: **16C-0004**

The American Petroleum Institute reserves the right to revoke this authorization to use the Official API Monogram for any reason satisfactory to the Board of Directors of the American Petroleum Institute.

The scope of this license includes the following product: Flexible Choke and Kill Lines

QMS Exclusions: No Exclusions Identified as Applicable

COPY

Effective Date: OCTOBER 15, 2010

Expiration Date: OCTOBER 15, 2013

To verify the authenticity of this license, go to www.api.org/compositelist.

American Petroleum Institute

Director of Global Industry Services

**CONTITECH RUBBER
Industrial Kft.**


**No: QC-DB- 380 /2012
Page: 4 /61**

QUALITY CONTROL INSPECTION AND TEST CERTIFICATE				CERT. N°: 1599	
PURCHASER: ContiTech Beattie Co.				P.O. N°: 006227	
CONTITECH ORDER N°: 531895		HOSE TYPE: 3" ID Choke and Kill Hose			
HOSE SERIAL N°: 63393		NOMINAL / ACTUAL LENGTH: 10,67 m / 10,72 m			
W.P. 68,9 MPa 10000 psi		T.P. 103,4 MPa 15000 psi		Duration: 60 min.	
<p>Pressure test with water at ambient temperature</p> <p style="text-align: center;">See attachment. (1 page)</p> <p>↑ 10 mm = 10 Min. → 10 mm = 20 MPa</p>					
COUPLINGS Type		Serial N°		Quality	
3" coupling with		2156 2153		AISI 4130	
4 1/16" 10K API Flange end				AISI 4130	
				Heat N°	
				20231	
				34031	
NOT DESIGNED FOR WELL TESTING				API Spec 16 C	
				Temperature rate:"B"	
All metal parts are flawless					
WE CERTIFY THAT THE ABOVE HOSE HAS BEEN MANUFACTURED IN ACCORDANCE WITH THE TERMS OF THE ORDER INSPECTED AND PRESSURE TESTED AS ABOVE WITH SATISFACTORY RESULT.					
STATEMENT OF CONFORMITY: We hereby certify that the above items/equipment supplied by us are in conformity with the terms, conditions and specifications of the above Purchaser Order and that these items/equipment were fabricated inspected and tested in accordance with the referenced standards, codes and specifications and meet the relevant acceptance criteria and design requirements.					
COUNTRY OF ORIGIN HUNGARY/EU					
Date:		Inspector		Quality Control	
23. August 2012.				ContiTech Rubber Industrial Kft. Quality Control Dept. (1)	




Hose Data Sheet

CRI Order No.	531895
Customer	ContiTech Beattie Co.
Customer Order No	PO6227 Pbc13080-H&P
Item No.	1
Hose Type	Flexible Hose
Standard	API SPEC 16 C
Inside dia in inches	3
Length	35 ft
Type of coupling one end	FLANGE 4 1/16" API SPEC 6A TYPE 6BX FOR 10000 PSI C/W BX155RING GROOVE
Type of coupling other end	FLANGE 4 1/16" API SPEC 6A TYPE 6BX FOR 10000 PSI C/W BX155 RING GROOVE
H2S service NACE MR0175	Yes
Working Pressure	10 000 psi
Design Pressure	10 000 psi
Test Pressure	15 000 psi
Safety Factor	2,25
Marking	USUAL PHOENIX
Cover	NOT FIRE RESISTANT
Outside protection	St. steel outer wrap
Internal stripwound tube	No
Lining	OIL RESISTANT
Safety clamp	No
Lifting collar	No
Element C	No
Safety chain	No
Safety wire rope	No
Max. design temperature [°C]	100
Min. design temperature [°C]	-20
MBR operating [m]	1,60
MBR storage [m]	1,40
Type of packing	WOODEN CRATE ISPM-15

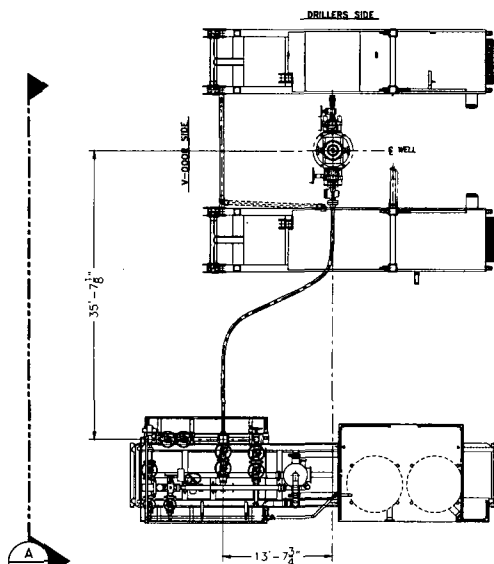

PLAN VIEW

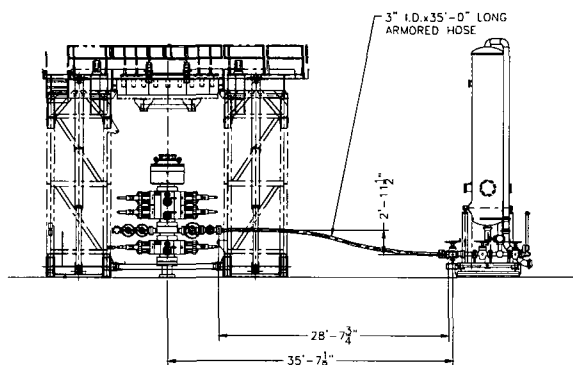

SECTION "A"

**ISSUED FOR
FABRICATION**
December-19-2007
DRAFTSMAN _____
ENGINEER _____

PROPRIETARY


THIS DRAWING AND THE IDEAS AND INFORMATION INCLUDED
HEREIN ARE PROPRIETARY AND ARE NOT TO BE
REPRODUCED, DISTRIBUTED OR DISCLOSED IN ANY MANNER
WITHOUT THE WRITTEN CONSENT OF A QUALIFIED
OFFICER OF HELMERICH & PAYNE INT'L DRILLING CO.

**HELMERICH & PAYNE
INTERNATIONAL DRILLING CO.**

**CHOKE LINE SYSTEM
FLEXRIG3**

ENGINEERING APPROVAL		DATE	TITLE
△			
△			
△			
△			
12/18/07	REMOVED SHEET TOTAL CALLOUT	JAY	
REV	DATE	DESCRIPTION	BY

CUSTOMER			
PROJECT			
DRAWN	JBG	DATE	4-10-07
SCALE	3/16"=1'	SHEET	2 OF 3
DWG NO	210-P1-07		
REV	A		

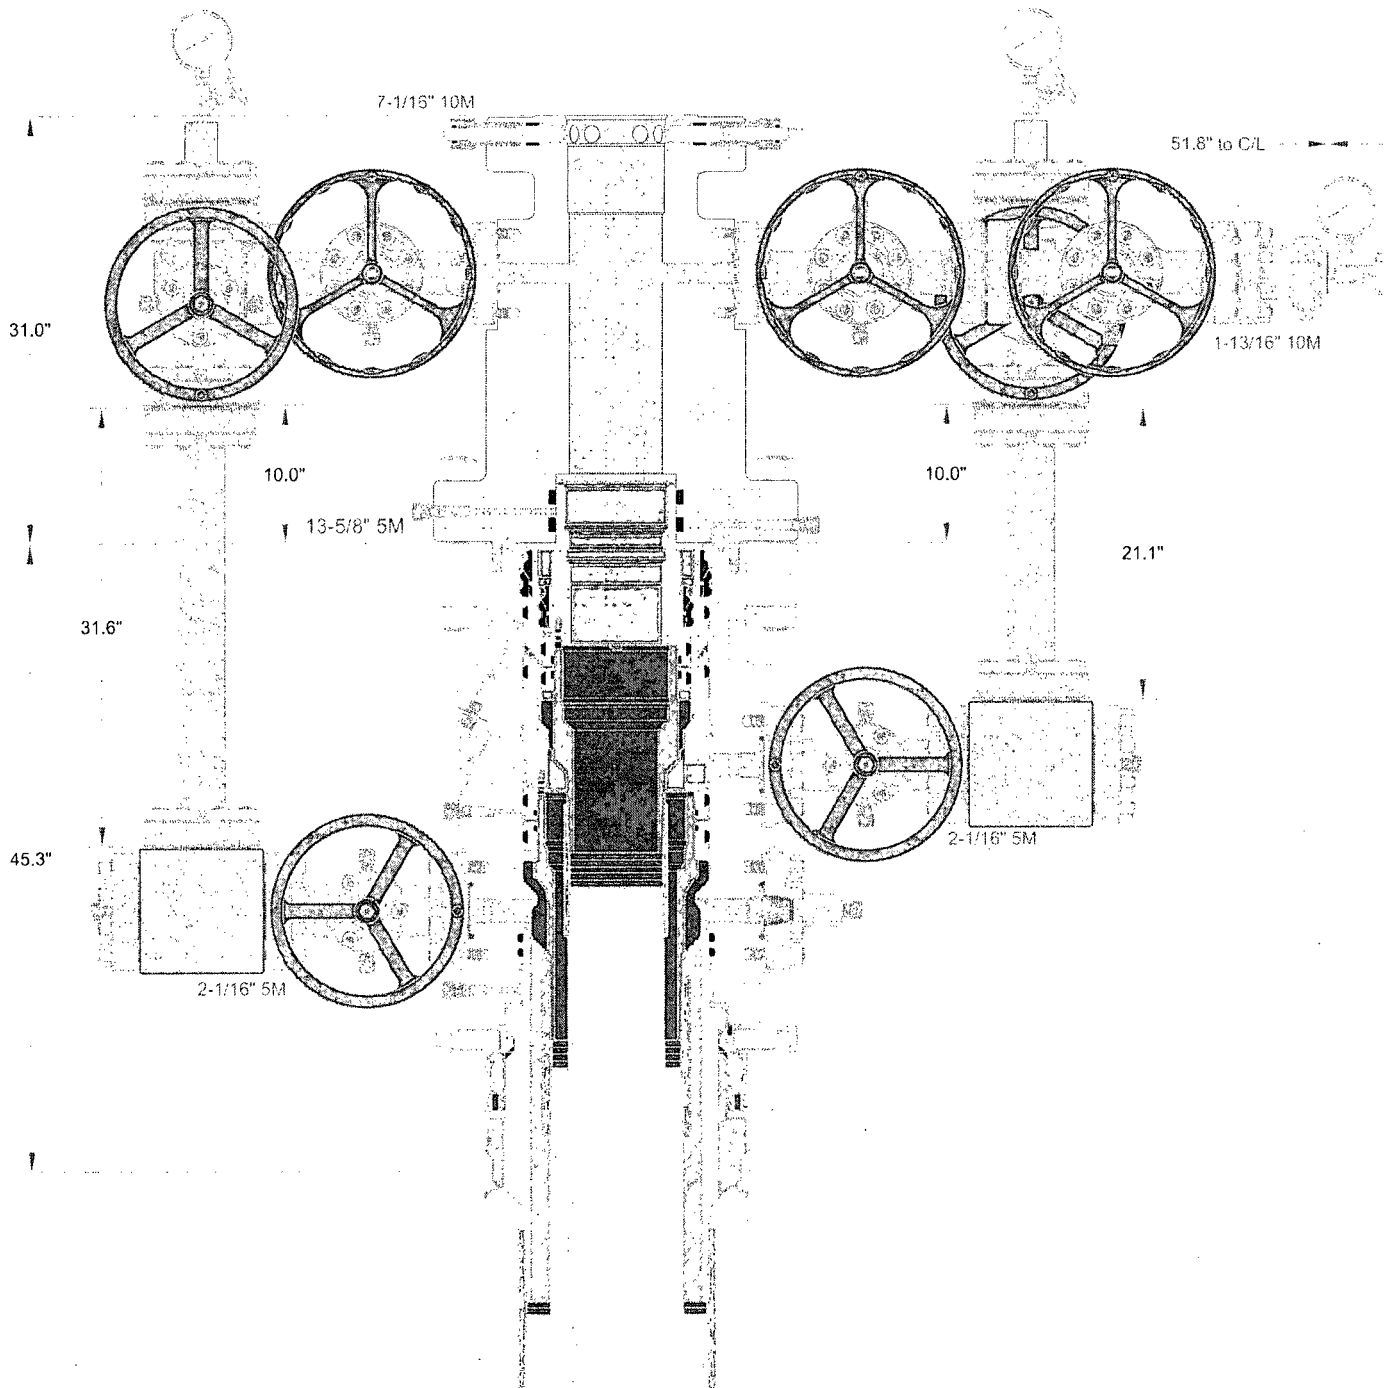

INFORMATION CONTAINED HEREIN IS THE PROPERTY OF CACTUS WELLHEAD, LLC. REPRODUCTION, DISCLOSURE, OR USE THEREOF IS PERMISSIBLE ONLY AS PROVIDED BY CONTRACT OR AS EXPRESSLY AUTHORIZED BY CACTUS WELLHEAD, LLC.


CACTUS WELLHEAD LLC

MARATHON OIL COMPANY

20" x 13-3/8" x 9-5/8" x 7" MBU-3T-CFL-R-DBLO Wellhead
With 13-5/8" 5M x 7-1/16" 10M CTH-DBLHPS Tubing Head (31" LG)
Utilizing Pin Down Mandrel Casing Hangers

DRAWN	DLE	24JUL17
APPRV		
DRAWING NO.	ODE0001624	

Operator: Marathon Oil
5M BOPE

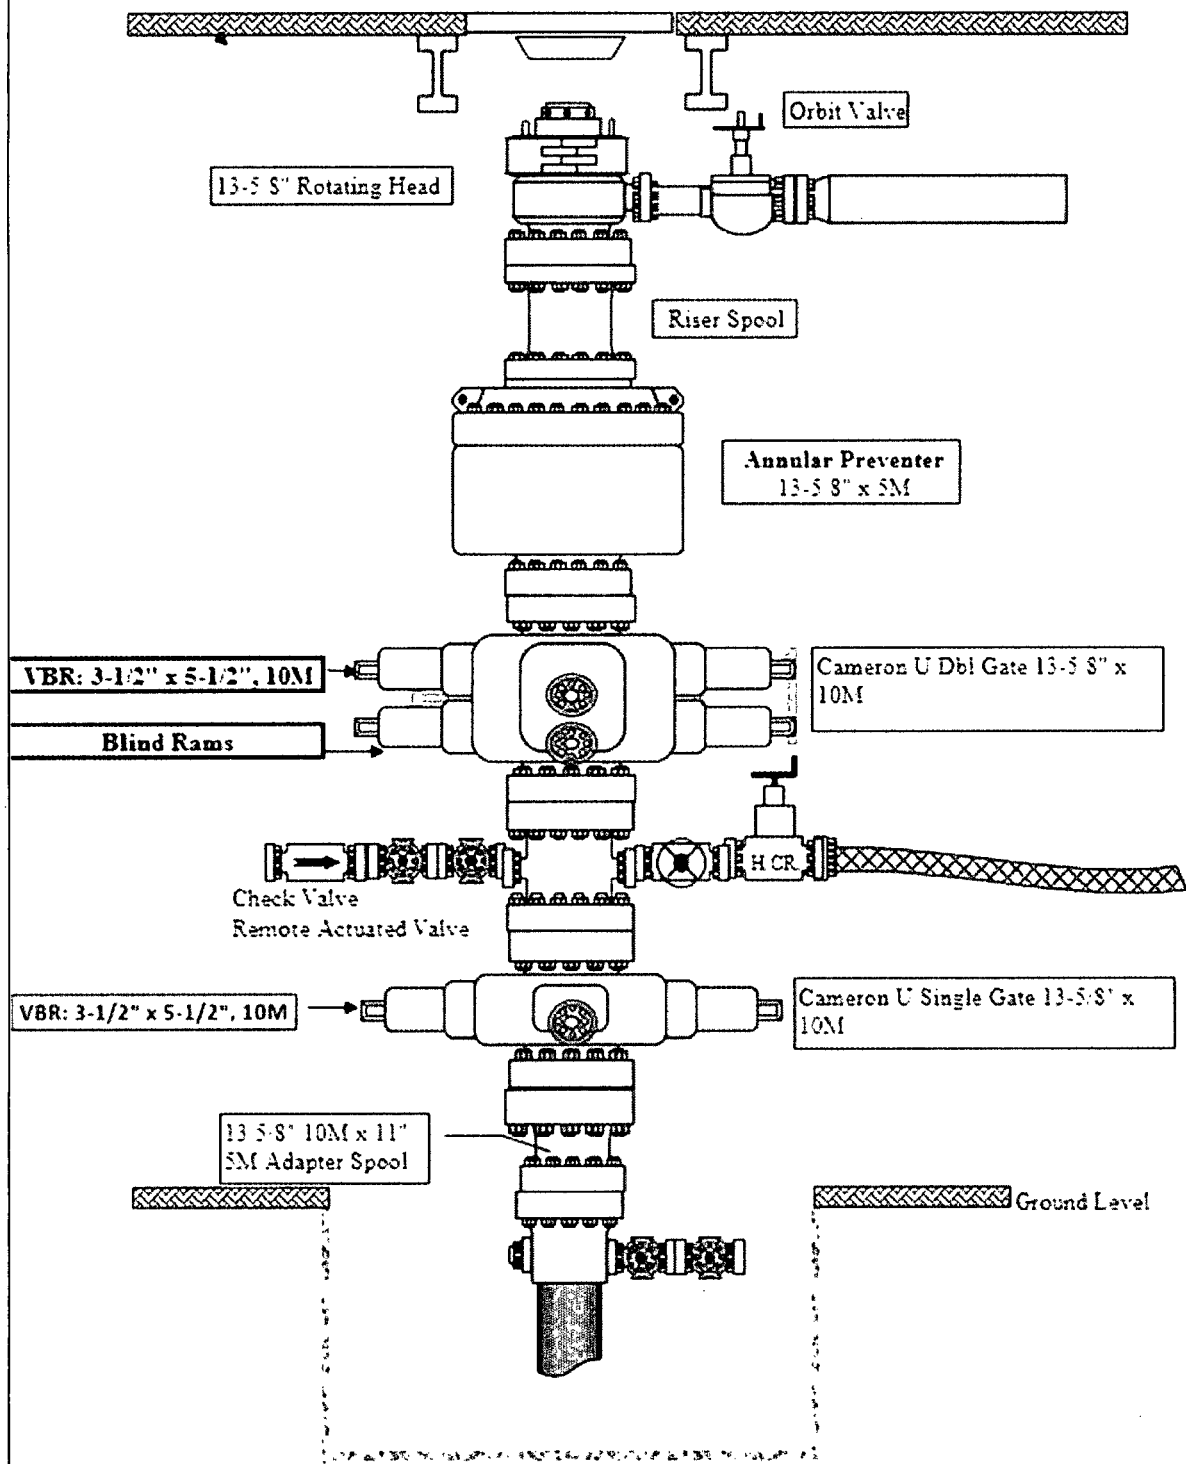

1. DRILLING WELL CONTROL PLAN

1.1 WELL CONTROL - CERTIFICATIONS

Required IADC/IWCF Well Control Certifications Supervisor Level:

Any personnel who supervises or operates the BOP must possess a valid current IADC training certification and photo identification. This would include the onsite drilling supervisor, tool pusher/rig manager, driller, and any personnel that will be acting in these capacities. Another example of this may be a wireline or snubbing crew rigged up on the rig to assist the rig, the operator of each system must also have a valid control certification for their level of operation.

BLM recognizes IADC training as the industry approved accredited training. Online self-certifications will not be acceptable. Enforcement actions for the lack of a valid Supervisory Level certificate shall be prompt action to correct the deficiency. **Enforcement actions include but are not limited to immediate replacement of personnel lacking certifications, drilling operations being shut down or installment of a 10M annular.**

IADC Driller Level for all Drillers and general knowledge for the Assistant Driller, Derrick Hands, Floor Hands and Motor Hands is recognized by the BLM; however, a Driller Level certification will need to be presented only if acting in a temporary Driller Level certification capacity.

Well Control-Position/Roles

IADC Well control training and certification is targeted toward each role, e.g., Supervisor Level toward those who direct, Driller Level to those who act, Introductory to those who need to know.

- **Supervisor Level**
 - Specifies and has oversight that the correct actions are carried out
 - Role is to supervise well control equipment, training, testing, and well control events
 - Directs the testing of BOP and other well control equipment
 - Regularly direct well control crew drills
 - Land based rigs – usually runs the choke during a well kill operation
 - Due to role on the rig, training and certification is targeted more toward management of well control and managing an influx out of the well
- **Driller Level**
 - Performs an action to prevent or respond to well control accident
 - Role is to monitor the well via electronic devices while drilling and detect unplanned influxes
 - Assist with the testing of BOP and other well control equipment
 - Regularly assist with well control crew drills
 - When influx is detected, responsible to close the BOP
 - Due to role on the rig, training and certification is targeted more toward monitoring and shutting the well in (closing the BOP) when an influx is detected

(Well Control-Positions/Roles Continued)

- **Derrick Hand, Assistant Driller Introductory Level**
 - Role is to assist Driller with kick detection by physically monitoring the well at the mixing pits/tanks
 - Regularly record mud weights/viscosity for analysis by the Supervisor level and mud engineer so pre-influx signs can be detected
 - Mix required kill fluids as directed by Supervisor or Driller
 - Due to role on the rig, training and certification is targeted more toward monitoring for influxes, either via mud samples or visual signs on the pits/tanks
- **Motorman, Floor Hand Introductory Level**
 - Role is to assist the Supervisor, Driller, or Derrick Hand with detecting influxes
 - Be certain all valves are aligned for proper well control as directed by Supervisor
 - Perform Supervisor or Driller assigned tasks during a well control event
 - Due to role on the rig, training and certification is targeted more toward monitoring for influxes

1.2 WELL CONTROL-COMPONENT AND PREVENTER COMPATIBILITY CHECKLIST

The table below, which covers the drilling and casing of the 10M Stack portion of the well, outlines the tubulars and the compatible preventers in use. This table, combined with the mud program, documents that two barriers to flow can be maintained at all times, independent of the rating of the annular preventer.

- Example 6-1/8" Production hole section, 10M requirement

Component	OD	Preventer	RWP
Drill pipe	4"	Upper and Lower 3.5-5.5" VBRs	10M
HWDP	4"	Upper and Lower 3.5-5.5" VBRs	10M
Drill collars and MWD tools	4.75-5"	Upper and Lower 3.5-5.5" VBRs	10M
Mud Motor	4.75-5.25"	Upper and Lower 3.5-5.5" VBRs	10M
Production casing	4.5"	Upper and Lower 3.5-5.5" VBRs	10M
ALL	0-13-5/8"	Annular	5M
Open-hole	-	Blind Rams	10M

- VBR = Variable Bore Ram. Compatible range listed in chart.

1.3 WELL CONTROL-BOP TESTING

BOP Test will be completed per Onshore Oil and Gas Order #2 Well Control requirements. The 5M Annular Preventer on a required 10M BOP stack will be tested to 70 % of rated working

pressure including a 10 minute low pressure test. Pressure shall be maintained at least 10 minutes.

1.4 WELL CONTROL - DRILLS

The following drills are conducted and recorded in the Daily Drilling Report and the Contractor's reporting system while engaged in drilling operations:

Type	Frequency	Objective	Comments
Shallow gas kick drill - drilling	Once per well with crew on tour	Response training to a shallow gas influx	To be done prior to drilling surface hole if shallow gas is noted
Kick drill - drilling	Once per week per crew	Response training to an influx while drilling (bit on bottom)	Only one kick drill per week per crew is required, alternating between drilling and tripping.
Kick drill - tripping	Once per week per crew	Response training to an influx while tripping (bit off bottom). Practice stabbing TIW valve	

1.5 WELL CONTROL – MONITORING

- Drilling operations which utilize static fluid levels in the wellbore as the active barrier element, a means of accurately monitoring fill-up and displacement volumes during trips are available to the driller and operator. A recirculating trip tank is installed and equipped with a volume indicator easily read from the driller's / operator's position. This data is recorded on a calibrated chart recorder or digitally. The actual volumes are compared to the calculated volumes.
- The On-Site Supervisor ensures hole-filling and pit monitoring procedures are established and documented for every rig operation.
- The well is kept full of fluid with a known density and monitored at all times even when out of the hole.
- Flow checks are a minimum of 15 minutes.
- A flow check is made:
 - In the event of a drilling break.
 - After indications of down hole gains or losses.
 - Prior to all trips out of the hole.
 - After pulling into the casing shoe.
 - Before the BHA enters the BOP stack.
 - If trip displacement is incorrect.

Well Control-Monitoring (Continued)

- Prior to dropping a survey instrument.
- Prior to dropping a core ball.

- After a well kill operation.
- When the mud density is reduced in the well.
- Flow checks may be made at any time at the sole discretion of the driller or his designate. The Onsite Supervisor ensures that personnel are aware of this authority and the authority to close the well in immediately without further consultation.
- Record slow circulating rates (SCR) after each crew change, bit trip, and 500' of new hole drilled and after any variance greater than 0.2 ppg in MW. Slow pump rate recordings should include return flow percent, TVD, MD & pressure. SCR's will be done on all pumps at 30, 40 & 50 SPM. Pressures will be recorded at the choke panel. SCR will be recorded in the IADC daily report and ORB Wellview daily report
- Drilling blind (i.e. without returns) is permissible only in known lithology where the absence of hydrocarbons has been predetermined and written approval of the Drilling Manager.
- All open hole logs to be run with pack-off or lubricator.
- The Drilling Contractor has a fully working pit level totalizer / monitoring system with read out for the driller and an audible alarm set to 10 BBL gain / loss volume. Systems are selectable to enable monitoring of all pits in use. Pit volumes are monitored at all times, especially when transferring fluids. Both systems data is recorded on a calibrated chart recorder or electronically.
- The Drilling Contractor has a fully working return mud flow indicator with drillers display and an audible alarm, and is adjustable to record any variance in return volumes.

1.6 WELL CONTROL – SHUT IN

- The “hard shut in” method (i.e. against a closed choke using either an annular or ram type preventer) is the Company standard.
- The HCR(s) or failsafe valves are left closed during drilling to prevent any erosion and buildup of solids. The adjustable choke should also be left closed.
- The rig specific shut in procedure, the BOP configuration along with space-out position for the tool joints is posted in the Driller's control cabin or doghouse.
- No well kill operation commences until there is a plan agreed by the Superintendent, On-Site Supervisor and the Drilling Manager.
- During a well kill by circulation, constant bottom hole pressure is maintained throughout.
- Kill sheets are maintained by the Driller and posted in the Driller's control cabin or doghouse. The sheet is updated at a minimum every 500 feet.

2. SHUT-IN PROCEDURES:

2.1 PROCEDURE WHILE DRILLING

- Sound alarm (alert crew)

- Space out drill string – Stop rotating, pick the drill string up off bottom, and space out to ensure no tool joint is located in the BOP element selected for initial closure.
- Shut down pumps (stop pumps and observe well.)
- Shut-in Well - If flow is suspected or confirmed, close uppermost applicable BOP element. (HCR and choke will already be in the closed position.)
 - **Note:** Either the uppermost pipe ram or annular preventer can be used.
- Confirm shut-in
- Notify toolpusher/company representative
- Gather all relevant data required:
 - SIDPP and SICP
 - Hole Depth and Hole TVD
 - Pit gain
 - Time
 - Kick Volume
 - Pipe depth
 - MW in, MW out
 - SPR's (Slow Pump Rate's)
- Regroup and identify forward plan (let well stabilize, update kill sheet, inventory mud additives and mud volumes on location)
- Company Representative, Drilling Superintendent, Drilling Engineer and Drilling Manager will discuss well control kill method to be utilized. A verbal Risk Assessment and preferred kill method will be finalized. Initial Risk Assessment will be finalized within 1 hour of initial shut in.
- **No well kill operation commences until there is a plan agreed by the Superintendent, On-Site Supervisor and the Drilling Contractor PIC.**
- Recheck all pressures and fluid volume on accumulator unit
- **If pressure has built or is anticipated during the kill to reach 1,000 psi or greater, the annular preventer will not be used as the primary pressure control device and operations will swap to the upper BOP pipe ram.**

2.2 PROCEDURE WHILE TRIPPING

- Sound alarm (alert crew)
- Stab full opening safety valve in the drill string and close.
- Space out drill string (ensure no tool joint is located in the BOP element selected for initial closure).
- Shut down pumps (stop pumps and observe well.)
- Shut-in Well - If flow is suspected or confirmed, close uppermost applicable BOP element. (HCR and choke will already be in the closed position.)
 - **Note:** Either the uppermost pipe ram or annular preventer can be used.
- Confirm shut-in
- Notify tool pusher/company representative
- Gather all relevant data required:
 - SIDPP and SICP
 - Hole Depth and Hole TVD
 - Pit gain

Procedure While Tripping (Continued)

- Time
- Kick Volume
- Pipe depth

- MW in, MW out
 - SPR's (Slow Pump Rate's)
- Regroup and identify forward plan (let well stabilize, update kill sheet, inventory mud additives and mud volumes on location)
- Company Representative, Drilling Superintendent, Drilling Engineer and Drilling Manager will discuss well control kill method to be utilized. A verbal Risk Assessment and preferred kill method will be finalized. Initial Risk Assessment will be finalized within 1 hour of initial shut in.
- **No well kill operation commences until there is a plan agreed by the Superintendent, On-Site Supervisor and the Drilling Contractor PIC.**
- Recheck all pressures and fluid volume on accumulator unit
- **If pressure has built or is anticipated during the kill to reach 1,000 psi or greater, the annular preventer will not be used as the primary pressure control device and operations will swap to the upper BOP pipe ram.**

2.3 PROCEDURE WHILE RUNNING CASING

- Sound alarm (alert crew)
- Stab crossover and full opening safety valve and close
- Space out casing (ensure no coupling is located in the BOP element selected for initial closure).
- Shut down pumps (stop pumps and observe well.)
- Shut-in Well - If flow is suspected or confirmed, close uppermost applicable BOP element. (HCR and choke will already be in the closed position.)
 - **Note:** Either the uppermost pipe ram or annular preventer can be used.
- Confirm shut-in
- Notify tool pusher/company representative
- Gather all relevant data required:
 - SIDPP and SICP
 - Hole Depth and Hole TVD
 - Pit gain
 - Time
 - Kick Volume
 - Pipe depth
 - MW in, MW out
 - SPR's (Slow Pump Rate's)
- Regroup and identify forward plan (let well stabilize, update kill sheet, inventory mud additives and mud volumes on location)
- Company Representative, Drilling Superintendent, Drilling Engineer and Drilling Manager will discuss well control kill method to be utilized. A verbal Risk Assessment and preferred kill method will be finalized. Initial Risk Assessment will be finalized within 1 hour of initial shut in.
- **No well kill operation commences until there is a plan agreed by the Superintendent, On-Site Supervisor and the Drilling Contractor PIC.**
- Recheck all pressures and fluid volume on accumulator unit
- **If pressure has built or is anticipated during the kill to reach 1,000 psi or greater, the annular preventer will not be used as the primary pressure control device and operations will swap to the upper BOP pipe ram.**

2.4 PROCEDURE WITH NO PIPE IN HOLE (OPEN HOLE)

- Sound alarm (alert crew)
- Shut-in with blind rams or BSR. (HCR and choke will already be in the closed position.)
- Confirm shut-in

- Notify toolpusher/company representative
- Gather all relevant data required:
 - Shut-In Pressure
 - Hole Depth and Hole TVD
 - Pit gain
 - Time
 - Kick Volume
 - MW in, MW out
 - SPR's (Slow Pump Rate's)
- Regroup and identify forward plan (let well stabilize, update kill sheet, inventory mud additives and mud volumes on location)
- Company Representative, Drilling Superintendent, Drilling Engineer and Drilling Manager will discuss well control kill method to be utilized. A verbal Risk Assessment and preferred kill method will be finalized. Initial Risk Assessment will be finalized within 1 hour of initial shut in.
- **No well kill operation commences until there is a plan agreed by the Superintendent, On-Site Supervisor and the Drilling Contractor PIC.**
- Recheck all pressures and fluid volume on accumulator unit.

2.5 PROCEDURE WHILE PULLING BHA THRU STACK

- PRIOR to pulling last joint of drill pipe thru the stack.
- Perform flow check, if flowing.
- Sound alarm (alert crew).
- Stab full opening safety valve and close
- Space out drill string with tool joint just beneath the upper pipe ram.
- Shut-in using upper pipe ram. (HCR and choke will already be in the closed position).
- Confirm shut-in.
- Notify toolpusher/company representative
- Read and record the following:
 - SIDPP and SICP
 - Pit gain
 - Time
- Regroup and identify forward plan
- **With BHA in the stack and compatible ram preventer and pipe combo immediately available.**
 - Sound alarm (alert crew)
 - Stab crossover and full opening safety valve and close
 - Space out drill string with upset just beneath the compatible pipe ram.
 - Shut-in using compatible pipe ram. (HCR and choke will already be in the closed position.)
 - Confirm shut-in
 - Notify toolpusher/company representative
 - Read and record the following:
 - SIDPP and SICP
 - Pit gain

Procedures While Pulling BHA thru Stack (Continued)

- Time
- Regroup and identify forward plan

- **With BHA in the stack and NO compatible ram preventer and pipe combo immediately available.**
 - Sound alarm (alert crew)
 - If possible to pick up high enough, pull string clear of the stack and follow "Open Hole" scenario.
 - If impossible to pick up high enough to pull the string clear of the stack:
 - Stab crossover, make up one joint/stand of drill pipe, and full opening safety valve and close
 - Space out drill string with tool joint just beneath the upper pipe ram.
 - Shut-in using upper pipe ram. (HCR and choke will already be in the closed position.)
 - Confirm shut-in
 - Notify toolpusher/company representative
 - Read and record the following:
 - SIDPP and SICP
 - Pit gain
 - Time



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

SUPO Data Report

09/12/2018

APD ID: 10400027053

Submission Date: 02/09/2018

Highlighted data
called; if not
recent changes

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

[Show Final Text](#)

Well Type: CONVENTIONAL GAS WELL

Well Work Type: Drill

Section 1 - Existing Roads

Will existing roads be used? YES

Existing Road Map:

Plat__Ballista_Federal_23_32_13_Pad__Well_Location_Plat_20180207120757.pdf

Plat__Ballista_Federal_23_32_13_Pad__Existing_Road_Map_20180712091948.pdf

Existing Road Purpose: ACCESS, FLUID TRANSPORT

Row(s) Exist? NO

ROW ID(s)

ID:

Do the existing roads need to be improved? NO

Existing Road Improvement Description:

Existing Road Improvement Attachment:

Section 2 - New or Reconstructed Access Roads

Will new roads be needed? YES

New Road Map:

Plat__Ballista_Federal_23_32_13_Pad__Proposed_Lease_Road_ATTACHMENT_20180207114121.pdf

Plat__Ballista_Federal_23_32_13_Pad__New_road_vicinity_Plat_20180712092017.pdf

New road type: LOCAL

Length: 705.53

Feet

Width (ft.): 20

Max slope (%): 1

Max grade (%): 0

Army Corp of Engineers (ACOE) permit required? NO

ACOE Permit Number(s):

New road travel width: 14

New road access erosion control: Road will be crowned to allow proper water drainage and BMP will be used to control erosion.

New road access plan or profile prepared? NO

New road access plan attachment:

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

Access road engineering design? NO

Access road engineering design attachment:

Access surfacing type: OTHER

Access topsoil source: ONSITE

Access surfacing type description: Caliche

Access onsite topsoil source depth: 6

Offsite topsoil source description:

Onsite topsoil removal process: Strip a minimum of 6" topsoil and temporarily pile while road is being constructed. After the road has been constructed, the topsoil will be spread and seeded along the road ditch in Marathon's ROW.

Access other construction information:

Access miscellaneous information:

Number of access turnouts:

Access turnout map:

Drainage Control

New road drainage crossing: OTHER

Drainage Control comments: Crowning shall be done on the access road driving surface. The road crown shall have a grade of approximately 2%. The road shall conform to cross section and plans for typical road construction found in the BLM Gold Book.

Road Drainage Control Structures (DCS) description: Road will be crowned to allow proper water drainage and ditching will be constructed on both side of the road.

Road Drainage Control Structures (DCS) attachment:

Access Additional Attachments

Additional Attachment(s):

Section 3 - Location of Existing Wells

Existing Wells Map? YES

Attach Well map:

Plat__Ballista_Federal_23_32_13_Pad__Existing_Well_Location_Map_20180809133805.pdf

Existing Wells description:

Section 4 - Location of Existing and/or Proposed Production Facilities

Submit or defer a Proposed Production Facilities plan? SUBMIT

Production Facilities description: Well Pad and Production Facilities will be located off lease in SESW of Section 13, Township 23S, Range 32E on Lease # NMNM84728. - No open top tanks will be used. - A pool commingle will be applied for

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

as needed. - Open vent exhaust stacks will be modified to prevent birds or bats from entering, discourage perching, roosting, and nesting. - The proposed Production Facilities will have a secondary containment 1.5 times the holding capacity of largest storage tank. - All above ground structures will be painted a non-reflective shale green for blending with the surrounding environment. - The proposed Production Facility will have oil and water truck hauled from the facility. - There are 6 - 750 bbl steel tanks for oil storage and 12 - 750 bbl steel tanks for water storage planned for the Production Facility. Pipelines: Flowlines will run from the well head to production facility all on the proposed pad. - All construction activity will be confined to the approved ROW. Powerlines: No powerlines, power will be provided via a natural gas generator.

Production Facilities map:

Plat__Ballista_Federal_23_32_13_Pad__Facility_Layout_20180208070255.pdf

Section 5 - Location and Types of Water Supply

Water Source Table

Water source use type: STIMULATION

Water source type: FRESH WATER LAKE

Describe type:

Source latitude: 32.3302

Source longitude: -103.68713

Source datum: NAD83

Water source permit type: PRIVATE CONTRACT

Source land ownership: PRIVATE

Water source transport method: PIPELINE

Source transportation land ownership: PRIVATE

Water source volume (barrels): 147500

Source volume (acre-feet): 19.011732

Source volume (gal): 6195000

Water source use type: STIMULATION

Water source type: FRESH WATER LAKE

Describe type:

Source latitude: 32.29495

Source longitude: -103.64632

Source datum: NAD83

Water source permit type: PRIVATE CONTRACT

Source land ownership: PRIVATE

Water source transport method: PIPELINE

Source transportation land ownership: PRIVATE

Water source volume (barrels): 147500

Source volume (acre-feet): 19.011732

Source volume (gal): 6195000

Water source use type: STIMULATION

Water source type: FRESH WATER LAKE

Describe type:

Source latitude: 32.284058

Source longitude: -103.61731

Source datum: NAD83

Water source permit type: PRIVATE CONTRACT

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

Source land ownership: PRIVATE

Water source transport method: PIPELINE

Source transportation land ownership: PRIVATE

Water source volume (barrels): 147500

Source volume (acre-feet): 19.011732

Source volume (gal): 6195000

Water source and transportation map:

SUPO_5__Ballista_Federal_23_32_13__Water__Caliche_20180710113218.jpg

Water source comments: • All Fresh water will be obtained from a private water source. • 1st proposed (Red tank pond in Section 4, T23S, R32E – LAT 32.330201 LONG -103.687131) will be utilized for fresh water. • A temporary 10" expanding pipe transfer line will run East from pond along lease rd. then turn South along proposed access road approx. 4.53 Miles. • 2nd proposed (Diamond pond in section 23 T23S R32E – LAT 32.294947 LONG -103.646318) will be utilized for fresh water. • A temporary 10" expanding pipe transfer line will run East from pond along access rd. then turn North along proposed access road approx. 1.72 miles. • 3rd proposed pond (Tres Equis in Section 19, T23S-R33E – LAT 32.284058 LONG -103.617308) will be utilized for fresh water. • A temporary 10" expanding pipe transfer line will run North from pond along access rd. then West along proposed access road approx. 2.90 Miles. • Fresh water line will run parallel to existing disturbance and will stay within 10' of access road. Proposed water suppliers Madera Travis Glenn Rockhouse
New water well? NO

New Water Well Info

Well latitude:

Well Longitude:

Well datum:

Well target aquifer:

Est. depth to top of aquifer(ft):

Est thickness of aquifer:

Aquifer comments:

Aquifer documentation:

Well depth (ft):

Well casing type:

Well casing outside diameter (in.):

Well casing inside diameter (in.):

New water well casing?

Used casing source:

Drilling method:

Drill material:

Grout material:

Grout depth:

Casing length (ft.):

Casing top depth (ft.):

Well Production type:

Completion Method:

Water well additional information:

State appropriation permit:

Additional information attachment:

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

Section 6 - Construction Materials

Construction Materials description: • Caliche will be used to construct well pad and roads. Material will be purchased from the nearest federal, state, or private permitted pit. • Source 1 - Caliche will be used to construct well pad and roads. Material will be purchased from the Mack Energy caliche pit located in Sec 32, T23S, R32E, Lea County, NM (32.256302, -103.697449). • Source 2 - Caliche will be used to construct well pad and roads. Material will be purchased from the BLM caliche pit located in Sec 11, T23, R32E, Lea County, NM(32.308154, -103.657816). • The proposed source of construction material will be located and purchased by construction contractor.

Construction Materials source location attachment:

SUPO_5__Ballista_Federal_23_32_13__Water__Caliche_20180710113740.jpg

Section 7 - Methods for Handling Waste

Waste type: DRILLING

Waste content description: All chemicals, salts, frac sand, produced oil, produced water and other waste material produced during drilling and completion operations.

Amount of waste: 5100 barrels

Waste disposal frequency : Daily

Safe containment description: Open Top Tanks

Safe containmant attachment:

Waste disposal type: HAUL TO COMMERCIAL FACILITY Disposal location ownership: PRIVATE

Disposal type description:

Disposal location description: Waste will be removed and disposed of properly at a state approved disposal facility.

Waste type: GARBAGE

Waste content description: Garbage and trash produced during drilling and completion operations

Amount of waste: 1200 pounds

Waste disposal frequency : Weekly

Safe containment description: All garbage will be stored in secure containers with lids.

Safe containmant attachment:

Waste disposal type: HAUL TO COMMERCIAL FACILITY Disposal location ownership: PRIVATE

Disposal type description:

Disposal location description: All garbage will be collected and disposed of properly at a State approved disposal facility.

Waste type: SEWAGE

Waste content description: Human waste and grey water.

Amount of waste: 600 barrels

Waste disposal frequency : Weekly

Safe containment description: Portable toilets and sewage tanks.

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

Safe containmant attachment:

Waste disposal type: HAUL TO COMMERCIAL FACILITY Disposal location ownership: PRIVATE

Disposal type description:

Disposal location description: All sewage waste will be disposed of properly at a State approved disposal facility.

Reserve Pit

Reserve Pit being used? NO

Temporary disposal of produced water into reserve pit?

Reserve pit length (ft.) Reserve pit width (ft.)

Reserve pit depth (ft.) Reserve pit volume (cu. yd.)

Is at least 50% of the reserve pit in cut?

Reserve pit liner

Reserve pit liner specifications and installation description

Cuttings Area

Cuttings Area being used? NO

Are you storing cuttings on location? YES

Description of cuttings location The well will be drilled utilizing a closed loop system. Drill cutting will be properly disposed of into steel tanks and taken to a State approved disposal facility.

Cuttings area length (ft.) Cuttings area width (ft.)

Cuttings area depth (ft.) Cuttings area volume (cu. yd.)

Is at least 50% of the cuttings area in cut?

WCuttings area liner

Cuttings area liner specifications and installation description

Section 8 - Ancillary Facilities

Are you requesting any Ancillary Facilities?: NO

Ancillary Facilities attachment:

Comments:

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

Section 9 - Well Site Layout

Well Site Layout Diagram:

Plat__Ballista_Federal_23_32_13_Pad__Well_Pad_Plat_with_Acres_20180712092310.pdf

20180726_R3818_001_BALLISTA_FEDERAL_23_32_13_REV0_CERT_CUT_AND_FILL_20180730053628.pdf

Plat__Ballista_Federal_23_32_13_Pad__Well_Pad_Plat_with_Footages_20180809133826.pdf

Comments: Exterior well pad dimensions are 400' x 540'. This pad will have 4 wells total. Interior well pad dimensions from first point of entry (well head) are: - Ballista Federal 23 32 13 WXY 3H - N-220', S-180', E-310', W-230'. - Ballista Federal 23 32 13 WA 6H - N-220', S-180', E-250', W-290'. - Ballista Federal 23 32 13 TB 7H - N-220', S-180', E-280', W-260'. - Ballista Federal 23 32 13 WXY 12H - N-220', S-180', E-220', W-320'. Pad surface area will be 5.33 acres. Disturbance needed for pad construction, including cut and fill is 6.18 acres. Topsoil will be placed on the north side of the pad (540' x 30') to accommodate interim reclamation activities. Topsoil area is 0.37 acres. Disturbance needed for road construction is 0.33.

Section 10 - Plans for Surface Reclamation

Type of disturbance: New Surface Disturbance

Multiple Well Pad Name: BALLISTA FEDERAL 23 32 13

Multiple Well Pad Number: 214-1

Recontouring attachment:

20180726_R3818_001_BALLISTA_FEDERAL_23_32_13_REV0_CERT_CUT_AND_FILL_IR_20180730053703.pdf

Drainage/Erosion control construction: During construction, BMP will be used to control erosion, runoff and siltation of surrounding area.

Drainage/Erosion control reclamation: BMP will be used to control erosion, runoff and siltation of surrounding area.

Well pad proposed disturbance (acres): 6.18	Well pad interim reclamation (acres): 2.54	Well pad long term disturbance (acres): 3.64
Road proposed disturbance (acres): 0.33	Road interim reclamation (acres): 0.09	Road long term disturbance (acres): 0.23
Powerline proposed disturbance (acres): 0	Powerline interim reclamation (acres): 0	Powerline long term disturbance (acres): 0
Pipeline proposed disturbance (acres): 0	Pipeline interim reclamation (acres): 0	Pipeline long term disturbance (acres): 0
Other proposed disturbance (acres): 0	Other interim reclamation (acres): 0	Other long term disturbance (acres): 0
Total proposed disturbance: 6.51	Total interim reclamation: 2.63	Total long term disturbance: 3.87

Disturbance Comments:

Reconstruction method: Reclamation Objectives • The objective of interim reclamation is to restore vegetative cover and a portion of the landform sufficient to maintain healthy, biologically active topsoil; control erosion; and minimize habitat and forage loss, visual impact, and weed infestation, during the life of the well or facilities. • The BLM will be notified at least 3 days prior to commencement of any reclamation procedures. • If circumstances allow, interim reclamation and/or final reclamation actions will be completed no later than 6 months from when the final well on the location has been completed or plugged. We will gain written permission from the BLM if more time is needed. • Reclamation will be performed by using the following procedures: For Interim Reclamation: • Within 6 months of first production, the well location and surrounding areas will be cleared of, and maintained free of, all materials, trash, and equipment not required for production. A plan will be submitted showing where interim reclamation will be completed in order to allow for safe operations, protection of the environment outside of drilled well, and following best management practices found in the BLM "Gold Book". • Current plans for interim reclamation include reducing the pad size to approximately 3.64 acres from the proposed size of 6.18 acres. • In areas planned for interim reclamation, all the surfacing material will be removed and returned to the original mineral pit or recycled to repair or build roads and well pads. • The areas planned for interim reclamation will then be recontoured to the original contour if feasible, or if not feasible, to an interim contour that blends with the surrounding topography as much as

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

possible. Where applicable, the fill material of the well pad will be backfilled into the cut to bring the area back to the original contour. The interim cut and fill slopes prior to re-seeding will not be steeper than a 3:1 ratio, unless the adjacent native topography is steeper. Note: Constructed slopes may be much steeper during drilling, but will be recontoured to the above ratios during interim reclamation. For Final Reclamation: • Prior to final reclamation procedures, the well pad, road, and surrounding area will be cleared of material, trash, and equipment. • All surfacing material will be removed and returned to the original mineral pit or recycled to repair or build roads and well pads. • All disturbed areas, including roads, pipelines, pads, production facilities, and interim reclaimed areas will be recontoured to the contour existing prior to initial construction or a contour that blends in distinguishably with the surrounding landscape. Topsoil that was spread over the interim reclamation areas will be stockpiled prior to recontouring. The topsoil will be redistributed evenly over the entire disturbed site to ensure successful revegetation. • After all the disturbed areas have been properly prepared; the areas will be seeded with the proper BLM LPC seed mixture free of noxious weeds. • Proper erosion control methods will be used on the entire area to control erosion, runoff and siltation of the surrounding area.

Topsoil redistribution: • Topsoil will be evenly respread and aggressively revegetated over the entire disturbed area not needed for all-weather operations including cuts & fills. To seed the area, the proper BLM LPC seed mixture free of noxious weeds, will be used. • Proper erosion control methods will be used on the area to control erosion, runoff and siltation of the surrounding area. • The interim reclamation will be monitored periodically to ensure that vegetation has reestablished.

Soil treatment: Stockpile until used for interim reclamation. Topsoil and subsoil will be piled separately.

Existing Vegetation at the well pad:

Existing Vegetation at the well pad attachment:

Existing Vegetation Community at the road:

Existing Vegetation Community at the road attachment:

Existing Vegetation Community at the pipeline:

Existing Vegetation Community at the pipeline attachment:

Existing Vegetation Community at other disturbances:

Existing Vegetation Community at other disturbances attachment:

Non native seed used? NO

Non native seed description:

Seedling transplant description:

Will seedlings be transplanted for this project? NO

Seedling transplant description attachment:

Will seed be harvested for use in site reclamation? NO

Seed harvest description:

Seed harvest description attachment:

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

Seed Management

Seed Table

Seed type: ANNUAL GRASS

Seed source: COMMERCIAL

Seed name: BLM Seed mix LPC

Source name:

Source address:

Source phone:

Seed cultivar:

Seed use location: NEW ACCESS ROAD,WELL PAD

PLS pounds per acre: 38

Proposed seeding season: AUTUMN

Seed Summary

Total pounds/Acre: 38

Seed Type	Pounds/Acre
ANNUAL GRASS	38

Seed reclamation attachment:

Operator Contact/Responsible Official Contact Info

First Name:

Last Name:

Phone:

Email:

Seedbed prep: Rip deep and leave pockets

Seed BMP: Leave rough for catching moisture and protecting young seedlings

Seed method: Broadcast

Existing invasive species? NO

Existing invasive species treatment description:

Existing invasive species treatment attachment:

Weed treatment plan description: Marathon Oil will control weeds per Federal, County and State regulations by contracting a certified third party sprayer.

Weed treatment plan attachment:

Monitoring plan description: Marathon Oil will monitor monthly during growing season for weeds through routine inspections.

Monitoring plan attachment:

Success standards: Maintain all disturbed areas as per Gold Book Standards.

Pit closure description: N/A

Pit closure attachment:

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

Section 11 - Surface Ownership

Disturbance type: WELL PAD

Describe:

Surface Owner: BUREAU OF LAND MANAGEMENT

Other surface owner description:

BIA Local Office:

BOR Local Office:

COE Local Office:

DOD Local Office:

NPS Local Office:

State Local Office:

Military Local Office:

USFWS Local Office:

Other Local Office:

USFS Region:

USFS Forest/Grassland:

USFS Ranger District:

Section 12 - Other Information

Right of Way needed? NO

Use APD as ROW?

ROW Type(s):

ROW Applications

SUPO Additional Information:

Use a previously conducted onsite? YES

Previous Onsite information: Performed 12/8/2017 Marathon Oil Attendees: Brian Hall and Harvey Waller BLM Attendee: Colleen Cepero-Rios (NRS) and Chelsie Dugan (Hydrologist)

Other SUPO Attachment

LR2000_NMNM084728_20180711110711.pdf

General_Lease_map_20180711110721.jpg

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: BALLISTA FEDERAL 23 32 13 WA

Well Number: 6H

LR2000__NMNM077062_20180711110728.pdf
