

Submit 1 Copy To Appropriate District
Office
District I
1625 N. French Dr., Hobbs, NM 88240
District II
1301 W. Grand Ave., Artesia, NM 88210
District III
1000 Rio Brazos Rd., Aztec, NM 87410
District IV
1220 S. St. Francis Dr., Santa Fe, NM
87505

State of New Mexico
Energy, Minerals and Natural Resources

Form C-103
October 13, 2009

RECEIVED

OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

AUG 27 2010

HOBBS SOGD

SUNDRIED AND REPORTS ON WELLS (DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)		WELL API NO. 30-025-03110 ✓
1. Type of Well: Oil Well <input type="checkbox"/> Gas Well <input checked="" type="checkbox"/> Other Injection <input checked="" type="checkbox"/>		5. Indicate Type of Lease STATE <input checked="" type="checkbox"/> FEE <input type="checkbox"/> ✓
2. Name of Operator ConocoPhillips Company		6. State Oil & Gas Lease No. 31158
3. Address of Operator 3300 N. "A" St., Bldg. 6 Midland, TX 79705		7. Lease Name or Unit Agreement Name Vacuum Abo Unit Tract 15 ✓
4. Well Location Unit Letter <u>B</u> : <u>330</u> feet from the <u>NORTH</u> line and <u>2310</u> feet from the <u>EAST</u> line Section <u>8</u> Township <u>18S</u> Range <u>35E</u> NMPM County <u>LEA</u> ✓		8. Well Number <u>3</u> ✓
11. Elevation (Show whether DR, RKB, RT, GR, etc.) 3958' GR		9. OGRID Number 217817 ✓
		10. Pool name or Wildcat Vacuum; Abo Reef ✓

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:

PERFORM REMEDIAL WORK ☐ PLUG AND ABANDON ☐
TEMPORARILY ABANDON ☐ CHANGE PLANS ☐
PULL OR ALTER CASING ☐ MULTIPLE COMPL ☐
DOWNHOLE COMMINGLE ☐

SUBSEQUENT REPORT OF:

REMEDIAL WORK ☐ ALTERING CASING ☐
COMMENCE DRILLING OPNS. ☐ P AND A ☐
CASING/CEMENT JOB ☐

OTHER: ☐

OTHER: Repair Downhole Failure and new MIT ☒

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

Vacuum Abo Unit #15-3 failed its annual pressure test on 2-10-2010.

Repairs were made on 7-20-2010: Ran new 2-7/8" TK-99 tubing set @ 8843'; pump 1000 gal 15% HCL mixed with 750 gal XYLENE and flush with 40 bbls water.

Return to Injection.


Successful MIT run on 8-3-2010. Chart is attached.

Spud Date:

Rig Release Date:

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE



TITLE Regulatory Specialist


DATE 08/26/2010

Type or print name Jalyn N. Fiske

E-mail address: Jalyn.Fiske@conocophillips.com PHONE: (432)688-6813

For State Use Only

APPROVED BY:



TITLE


STAFF MGR

DATE

8-31-10

Conditions of Approval (if any):

3.m.

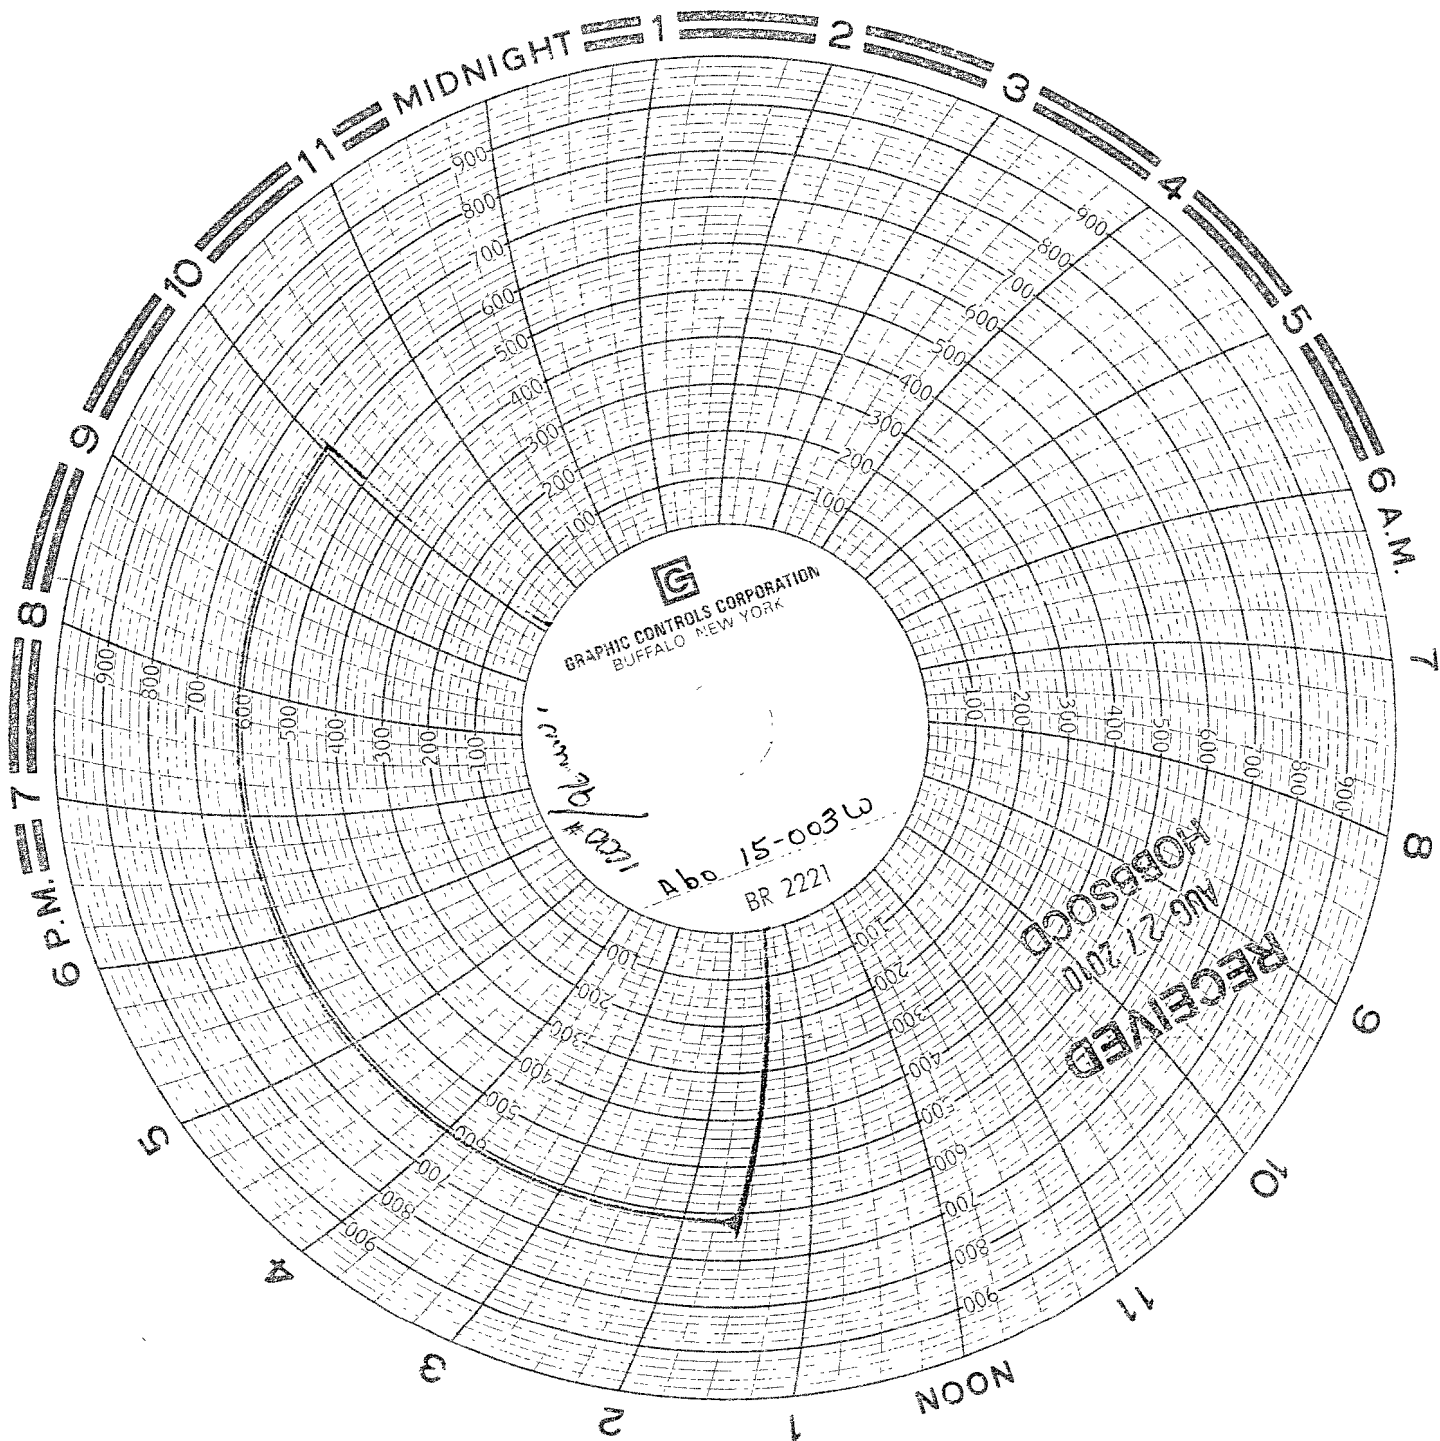

1000#
Chart
Set on 96 min.
Serial # B1235
CAL DATE, 6-17-2010

VACUUM ABO unit 015-003W
8-3-2010 3 p.m.
API # 300250311000
PKr Set at 8843.
Top Pert. 8913.

Smith Services
Michael Couger
8-3-2010
