

Conditions of Approval (if any):

Trinity Burrus Abo Unit # 16

API # 30-025-36251


(Cont.)

1/13/11: TOH laying down workstring. RU testers. PU pkr & TIH w/ tbg & pkr to set @ 8955'.

1/14/11: RU & displace hole w/200 bbls 2% KCL pkr fluid. Latch on to pkr & test casing to 600# (OK).

NDBOP, NUWH, clean location & RDMO. Notified Mr. Maxie Brown w/NMOCD of MIT test.

Original chart is attached. Please note top of perfs are at 9014'.

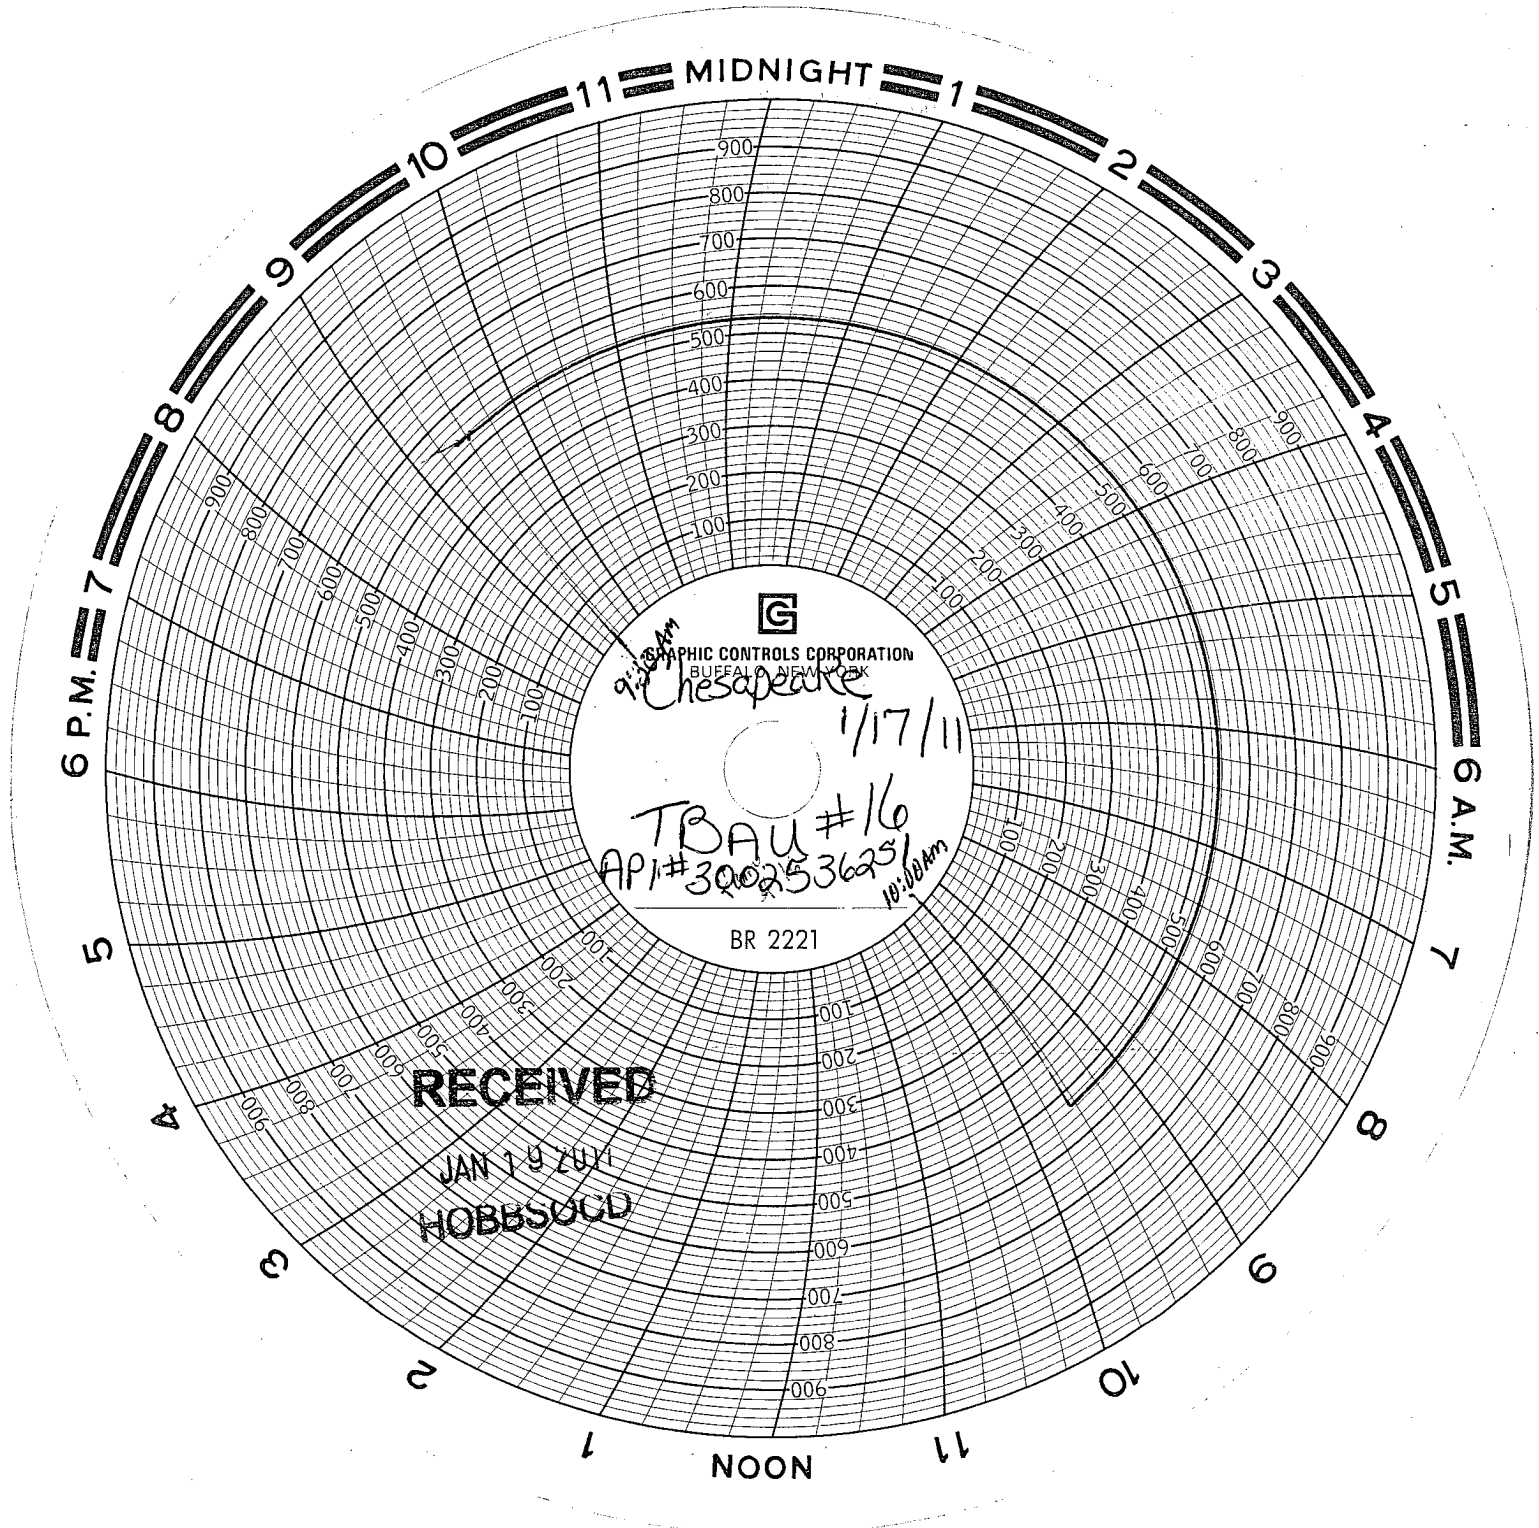

RECEIVED

JAN 19 2011
HOBBSOCD

STONE OILFIELD SERVICE
K-5 LEONEL GONZALEZ

CHESAPEAKE OPERATIONS
TRINITY BUREAU ABO UNIT NO 116

1980' FSL & 660' FWL
N/4 1/4 SW/4 SECTION 23-22S-38E
UNIT # NMNM 116169X
CEA COUNTY N.M.

January 17, 2011
