



WARD Install Com No. 2




10 SKS @ surface + marker + welded cap

PBCP Services Inc.
Pumping Services
records of Job

13 3/8 @ 350'
Spot 75 SKS @ 426' TAG plug @ 308' by wireline



cut off 8 5/8 @ 985'
SPOT 50 SKS @ 1035' TAG plug @ 937' by wireline

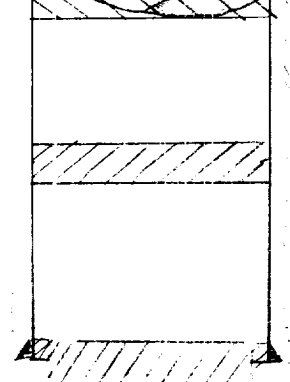


SPOT 35 SKS @ 2100' (119' by vol)

8 5/8 @ 4048'

50 SKS @ 4100' TAG PLUG @ 3973' by wireline



SPOT 50 SKS @ 5012' (1172' by vol)
tagged T.O.C. @ 4901' by wireline



cut off 5 1/2 @ 5012' (cut off 19' by vol) (1-25-79) by wireline
(called commissioning test to cut plug at 5012')

SPOT 40 SKS @ 6781 (250' plug by volume)
TAG T.O.C. @ 6378 By wireline

TOP OF 2 7/8" TUBING @ 6781 1/2
(STUCK)

Perf. 9784-9802

5 1/2 @ 9865 Com No. 260 SKS

RECEIVED
AUG 16 1983
O.C.D.
HOBBS OFFICE
