


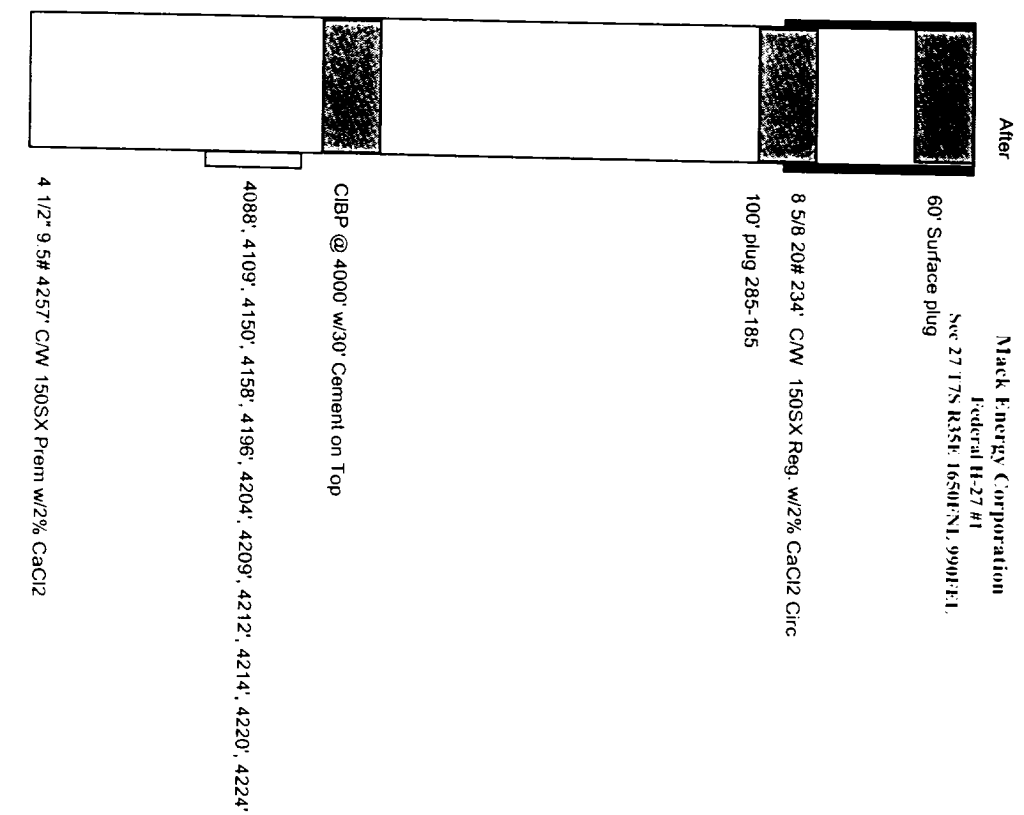

Well History	
12/07/64	Drlg. 4100'
12/14/64	TD 4260', prep to AC. Cored 4100-50', rec 50' anhy & dolo. w/scatt PPP, BO from scatt zones. Cored 4150-4; Perf @ 4088', 4109', 4150', 4158', 4196', 4204', 4209', 4212', 4214', 4220', 4224' w/1 SPI
12/21/64	TD 4260', 1stg. Ac. 2000 gals. 4088-4224' Flwd est. 4827 MCFGPD, TP 70#
01/04/65	TD 4260', PBD 4257', WO Potential.
01/11/65	TD 4260', PBD 4257', WO Potential. Flwd 10,000 MCFGPD
01/18/65	TD 4260' PBD 4257', WO Potential.
01/25/65	TD 4260', PBD. Completed. FOUR-POINT GAUGES: (GAUGES THROUGH VARIOUS CHOKES) MCFGPD- 852, TIME- 1HR, TP- 1046# MCFGPD- 1476, TIME- 1HR, TP- 1016# MCFGPD- 2169, TIME- 1HR, TP- 960# MCFGPD- 2751, TIME- 1HR, TP- 912#
COMPLETION REPORT	
07/28/94	RU, made 2 swab runs. No fluid, N/D well head, worked with tbq. could not unset packer. N/U well head, SDFI
07/29/94	Made 1 swab run, no fluid RD

4
MAY 2000
Received
Hobbs
OCD

RECEIVED
MAY 19 2000
BLM
ROSWELL NM
